

MONTHLY PROJECT OVERVIEW

I-405, South Bellevue Widening Project

August 2009


Project Location: I-405, 112th Ave SE to SE 8th St
Design-Builder: Atkinson

PIN: 840541F, 840509A, 840541G
WIN: U40541F

Design / Build Contract Summary

Contract Award: February 16, 2007
 Notice to Proceed: March 15, 2007
 Original Contract Time: 934 Calendar Days
 Original Substantial Completion: October 2009
 Original Contract Amount: \$124,000,000
 Revised Contract Amount: \$124,365,074


Project Progress to Date



Project Status as of: August 31, 2009

Contract Days Elapsed: 900 of 934 = 96.4%
 Contract Amount Earned to Date: \$121,432,321 = 98.0%
 Contract Amount Earned This Period: \$3,237,843 = 2.6%
 Current Projected Completion Date: Oct. 2009 (on schedule)

Project Cash Flow

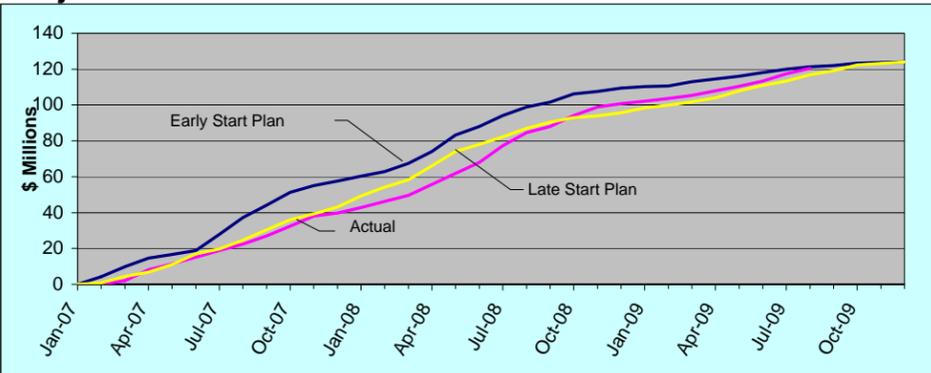

August 2009 Highlights




Design-Build Schedule Summary

Design: Original design is complete, however work is in progress on the northbound I-90 bridge restripe plan. Design team will continue to support construction to the end of the project. Design documentation package is being assembled.

Construction: Shifting the HOV lane onto the old southbound bridge. Striping the northbound lanes into final configuration per the RFP requirements. Installing quieter pavement test sections on the northbound lanes. Continuing planter wall construction at SE 8th Street. Installing amendments at the ponds throughout the project limits. Installing media filter drains north of I-90. Construction at the ecology embankment monitoring station by the Coal Creek Parkway bike path. Installing permanent signing, loops, barrier wall, and guardrail throughout project limits. Construction of the southbound Main Street bridge retrofit. Replacing the 116th outfall pipe. PCCP and HMA paving for the inside widening southbound by wall 2005. Installing luminaires on the I-90 bridge.

Summary Project Schedule

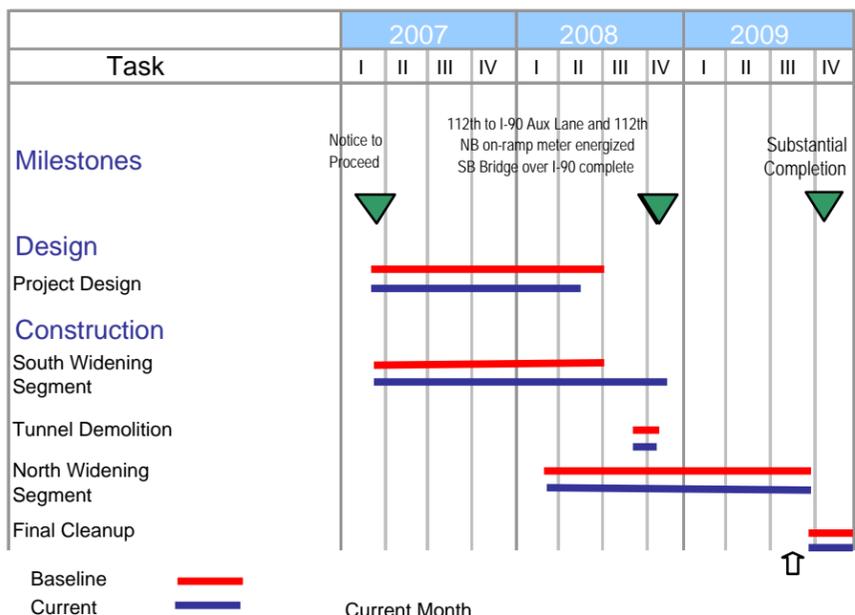

Quality Control / Quality Assurance

With the I-405, 112th Ave SE to SE 8th Widening project nearing completion, the Design Builder's quality acceptance staff is preparing for final records and the material's certification of the project.

SAMs data (the Statistical Analysis of Materials software program) is being analyzed to verify the Design Builder's testing of materials incorporated into this project. If the Design Builder's sampling and testing results are validated with the results of sampling and testing done by the WSDOT quality verification staff, the Design Builder's test results will be used for the acceptance of the materials placed.

Risks / Challenges / Issues

Minimizing traffic control with the volume of remaining work and noise impacts to the public in a busy construction season remains a challenge.

Public Information & Community Outreach

Informed the public of I-405 lane closures for placing quieter pavement. Answered comments from citizens and updated the public of the projects' progress using construction updates on WSDOT web sites and e-mail updates.

Upcoming Activities - Fall 2009

Substantial completion is anticipated the third week in September. The major work remaining is the southbound inside widening. Construction of noise wall 2000 and the I-90 restripe work with the bridge drainage retrofit work remains.

For more information, Call 425.401.4143 or 425.456.8624 or visit www.wsdot.wa.gov/Projects/i405/112thAveToSE8th/

IT'S YOUR NICKEL. WATCH IT WORK.

"Washington's Future Just Got Better"
MAKING EVERY DOLLAR COUNT.

Washington State Department of Transportation
