

MONTHLY PROJECT OVERVIEW

I-405, South Bellevue Widening Project

April 2009


Project Location: I-405, 112th Ave SE to SE 8th St
Design-Builder: Atkinson

PIN: 840541F, 840509A, 840541G
WIN: U40541F

Design / Build Contract Summary


Contract Award: February 16, 2007
 Notice to Proceed: March 15, 2007
 Original Contract Time: 934 Calendar Days
 Original Substantial Completion: October 2009
 Original Contract Amount: \$124,000,000
 Revised Contract Amount: \$124,000,000

Project Progress to Date



Project Status as of: April 30, 2009
 Contract Days Elapsed: 777 of 934 = 83.2%
 Contract Amount Earned to Date: \$108,346,223 = 87.5%
 Contract Amount Earned This Period: \$2,834,648 = 2.3%
 Current Projected Completion Date: Oct. 2009 (on schedule)

Project Cash Flow

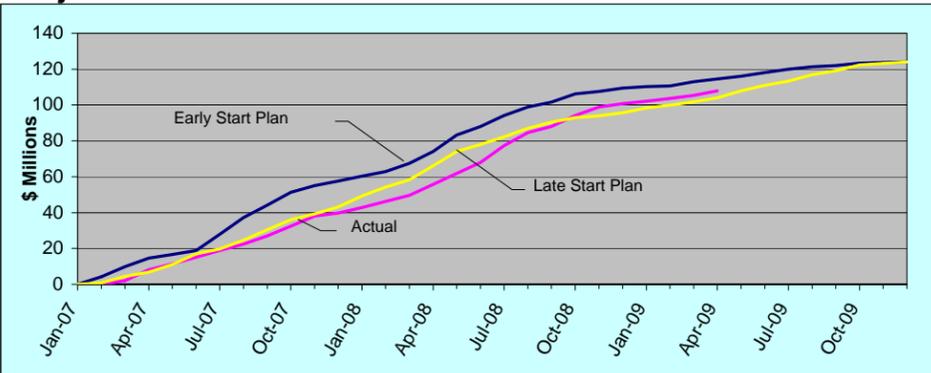

April 2009 Highlights



Beginning of bridge deck construction on SE 8th street bridge



Slip form barrier pour at wall 2080



Paving on SE 8th street off ramp



Constructing MSE wall 2025

Design-Build Schedule Summary

Design: Original design is complete. Design team will continue to support construction to the end of the project. Design documentation package is being assembled.


Construction: Opening of a new southbound lane from SE 8th to I-90. Completing the ITS switch over so the widening in the median north of I-90 could begin. Continuing work on the retaining walls at the SE 8th Street Bridge and the widening of the SE 8th Street Bridge. Planting vegetation throughout the project limits. Pressure washing existing wall, pig sealing wall, and installing underdeck lighting at the I-90 bridge. Completing a retaining wall in the median for the northbound widening. Pulling loop wire at the new data station cabinet locations from SE 8th to I-90. Starting the northbound Main Street retrofit.

Quality Control / Quality Assurance

The Design Builder Quality Assurance staff continues acceptance inspection and material testing for the project. WSDOT is providing quality verification inspection and hot mix asphalt inspection.

The Design Builder Quality Assurance staff generates NCRs (Nonconformance Reports) to document when elements of the work do not, or is believed to not have been constructed in accordance to the approved plans and specifications. Currently the project has ten open NCRs. All NCRs have resolutions and are waiting for re-work or documentation prior to final acceptance.

Summary Project Schedule

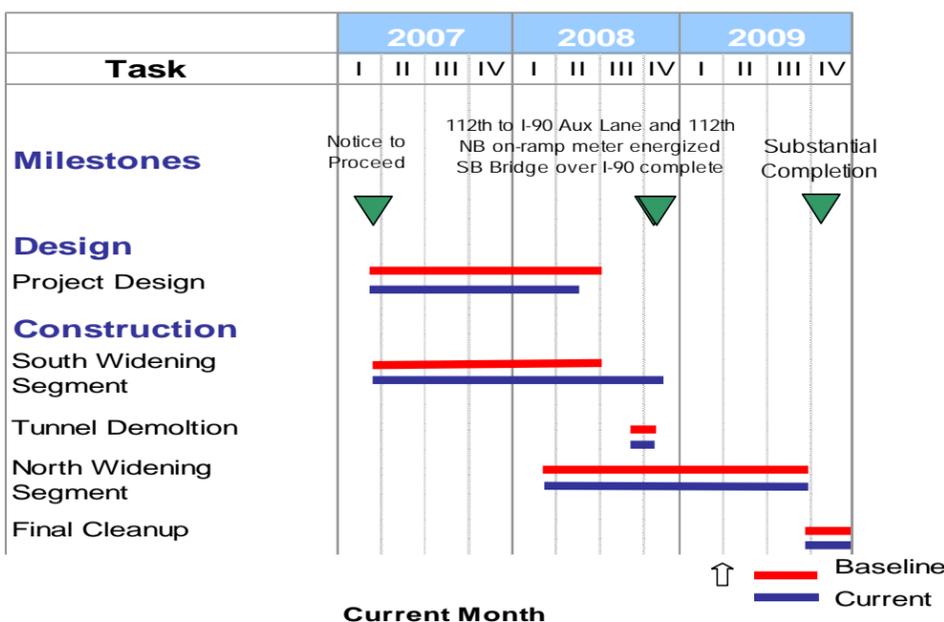

Risks / Challenges / Issues

Minimizing traffic control and noise impacts to the public in a busy construction season remains a challenge.

Public Information & Community Outreach

Informed public of closures and potential delays using construction updates on WSDOT web sites and ListServ messaging. Began working on project folio for neighboring residents outlining milestones and upcoming construction.

Upcoming Activities - Spring 2008/2009

Noise wall construction. Construction of new approaches to existing bridge over I-90 for new northbound HOV lanes. Construction of median MSE walls north of I-90. ITS installation north of I-90.

For more information, Call 425.401.4143 or 425.456.8624 or visit www.wsdot.wa.gov/Projects/i405/112thAveToSE8th/

IT'S YOUR NICKEL. WATCH IT WORK.

"Washington's Future Just Got Better"
MAKING EVERY DOLLAR COUNT.

