

MONTHLY PROJECT OVERVIEW


I-405, Bellevue Braids Design Build Project

May 2010


Project Location: I-405/NE 8th St to SR 520
Design-Builder: Guy F. Atkinson Construction, LLC.
WSDOT Project Engineer : Seema Javeri, PE.

PIN: 840551A, 840541F
WIN: U40541F
Federal Aid Project: ARRA-4053(858)

Design / Build Contract Summary
 Contract Award: November 9, 2009
 Notice to Proceed: December 7, 2009
 Original Contract Time: 929 Calendar Days
 Original Substantial Completion: June 2012
 Original Contract Amount: \$107,500,000
 Revised Contract Amount: \$107,500,000

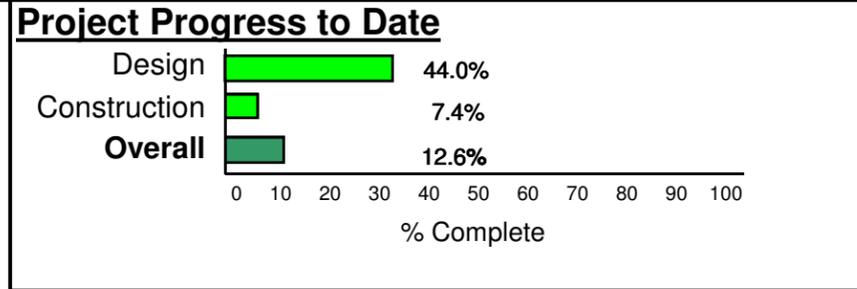

Project Status as of: May 31, 2010
 Contract Days Elapsed: 175 of 929 = 18.8%
 Contract Amount Paid to Date: \$13,559,731 = 12.6%
 Contract Amount Paid This Period: \$2,169,847 = 2.0%
 Projected Substantial Completion Date: June 2012 (on schedule)

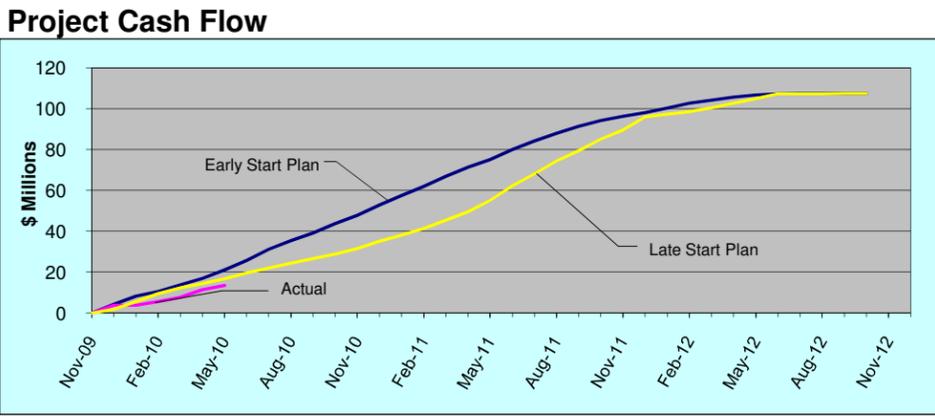

May 2010 Highlights

Drilling Pile for Shoring Wall

Demolished Noise Wall Panels

Drill shaft for Shoring Wall

Tieback Installation

Design-Build Schedule Summary
 Design: I-405 - Submittals for ITS, signing, perm. lighting, noise wall, noise wall analysis, City water and sewer, retaining walls, channelization and site preparation reviewed.
 SR 520 - Submittals for Seattle City Light Pole, alignment, right of way, and City water reviewed.
 NE 12th - Submittals for channelization, and drainage reviewed.

Quality Control / Quality Assurance
 The Design Builder continues inspection and materials testing. The Design Builder is inspecting all materials used in the construction of this project. When new materials arrive onsite, the Design Builder's Quality Assurance staff will generate a MMR (Materials Receiving Report). This report will document that the material meets the contract specifications, is properly stored and that all required testing and documentation has been completed prior to the acceptance of the material.
 WSDOT Quality Verification continues oversight inspection of the project and is performing audits on both the design and construction elements of the project.


Bridges - Preliminary submittals for NE 10th to SR 520 Ramp, Braid Ramp, BNSF and Northup Bridges reviewed. NE 12th superstructure and foundations RFC'ed.
 Drainage - Preliminary submittals for TDA's F, G, and I reviewed. NE 12th Street drainage RFC'ed.

Risks / Challenges / Issues
 Keeping the NE 12th Street design and construction on schedule, work on BNSF/ Port of Seattle ROW, and MOT are areas of concern for our project.

Construction:
 NE 12th Street bridge pier 1 & 3 foundation construction underway. City of Bellevue sanitary sewer installation on east side of I-405, under NE 12th and north. NB and SB traffic switch is complete creating a work zone in the median. NB clearing is complete. Pond G is nearly complete.

Public Information & Community Outreach
 The Public Information team is preparing for an open house in June to inform area businesses and residents about upcoming construction. This month, the team began issuing news releases and posting Website construction updates about closures.

Summary Project Schedule

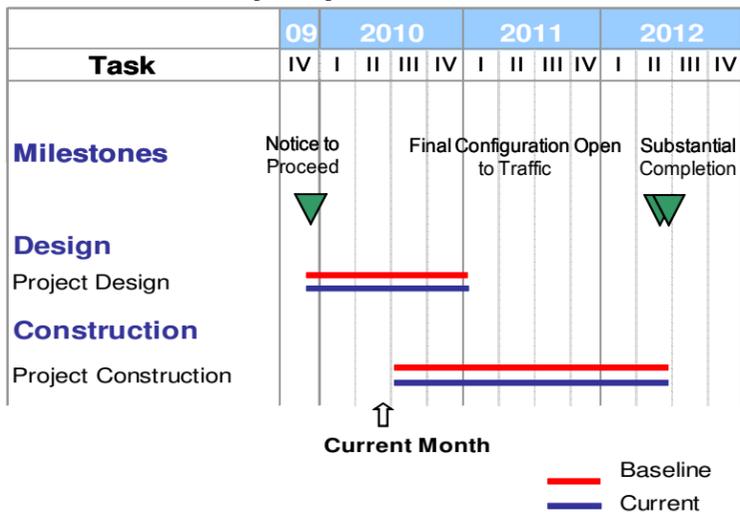

Upcoming Activities - Summer 2010
 Construction of the NE 12th Street bridge footing, columns, and caps. Working in the median for NE 12th Street pier 2 construction. Starting work on NB 405.

