

MONTHLY PROJECT OVERVIEW – April 2009

SR 532 Corridor Improvements Design-Build Project

Project Location: SR 532 from Camano Island to I-5

Design-Builder: Parsons / Kunej JV


PIN: 153203D, 153209G, 153210G, 153211G, 153212G

WIN: A53210G

Design / Build Contract Summary

Contract Award: January 29, 2009
 Notice to Proceed: February 23, 2009
 Original Contract Time: 646 Calendar Days
 Original Substantial Completion: December 1, 2010
 Original Contract Amount: \$50,415,851
 Revised Contract Amount: \$50,415,854

Project Progress to Date



Project Status as of: **April 30, 2009**

Contract Days Elapsed: 66 of 646 = 10.22%
 Contract Amount Earned to Date: \$6,112,697 = 12.12%
 Contract Amount Earned This Period: \$724,086 = 1.44%
 Current Projected Completion Date: December 1, 2010

Project Cash Flow



April 2009 Highlights



Project identification sign installation in progress



Highway Advisory Radio along eastbound SR 532 near 270th



Right-of-way survey flagging at 72nd Avenue




Installing bird netting under the General Mark Clark Bridge

Design / Build Schedule Summary

Design: The Weekly Task Force teams continue to address design and utility issues in their meetings. The focus on the General Mark Clark Bridge design is on-going. Early design for the roadway improvements such as channelization, drainage, and paving plans are also in progress. Roadway design improvements commenced for the work within Camano Island and 64th Ave. NW to I-5, and is also underway for the Stanwood area. Geotechnical investigation of the soils by the Design-Builder was completed.

Construction: Pending July 1, 2009 start date.

Summary Project Schedule

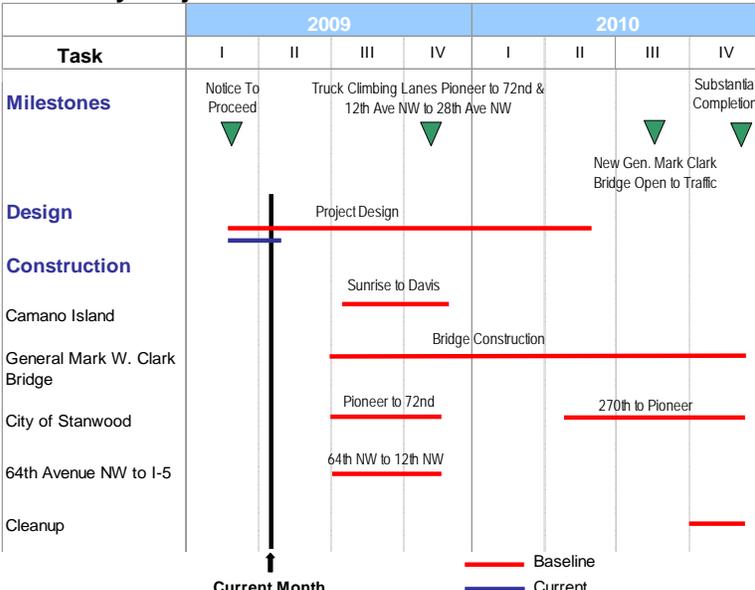

Quality Control/Quality Assurance

The Project Quality Management Plan and six appendices have been submitted. The Quality Management Plan and four of the appendices have been reviewed and approved. The Design-Builder is currently working on providing necessary documentation for use of suppliers and pit sources.

Risks / Challenges / Issues

- Acquisition of environmental permits is still on-going, and could potentially affect utility relocations and the start of construction.
- An existing breach in the dike at the northwest corner of the General Mark Clark Bridge could create some difficulties in wall construction and access to the area.
- Coordination of several contracts scheduled to begin this summer within the project limits to minimize traffic impacts to the 532 corridor.

Public Information & Community Outreach

- "Jobs Now", Highway Advisory Radio, and project hotline signs are installed
- Messages now running on Highway Advisory Radio
- Handout cards printed and distributed throughout corridor
- Launching SR 532 corridor e-mail update in May 2009

Upcoming Activities – May 2009

- A preconstruction conference with Environmental Agencies to be held on May 14, 2009
- Open house and groundbreaking in mid-June to July 2009
