

MONTHLY PROJECT OVERVIEW – February 2010

SR 532 Corridor Improvements Design-Build Project


Project Location: SR 532 from Camano Island to I-5
Design-Builder: Parsons / Kunej JV

PIN: 153203D, 153209G, 153210G, 153211G, 153212G
WIN: A53210G

Design / Build Contract Summary

Contract Award: January 29, 2009
 Notice to Proceed: February 23, 2009
 Original Contract Time: 646 Calendar Days
 Original Substantial Completion: December 1, 2010
 Original Contract Amount: \$50,415,851
 Revised Contract Amount: \$50,269,550


Project Progress to Date



Project Status as of: February 28, 2010

Contract Days Elapsed: 370 of 646 = 57.28%
 Contract Amount Earned to Date: \$34,836,081 = 69.30%
 Contract Amount Earned This Period: \$1,949,955 = 3.88%
 Current Projected Completion Date: December 1, 2010

Project Cash Flow

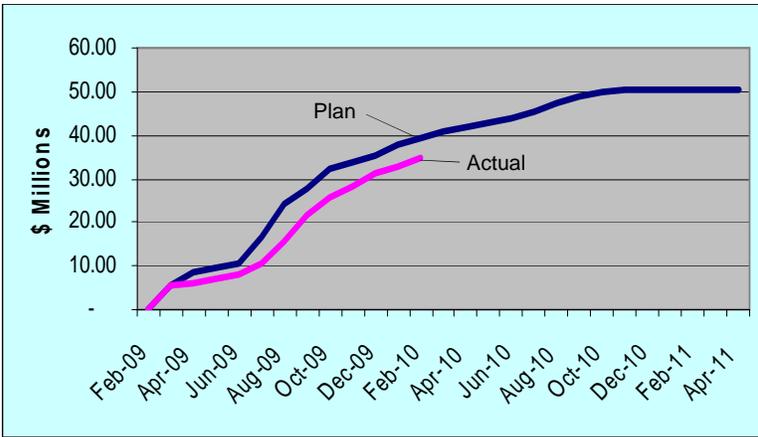

February 2010 Highlights



Crew pouring concrete on intermediate diaphragm of new bridge



Trench box in use to protect crews working on the detention pond near Pioneer Hwy.



Grading work at 270th Street in progress.




Ongoing road widening at 12th Avenue

Design / Build Schedule Summary

Design: The Stanwood segment is in the final design stage.
Construction: Placement of all 17 precast girders for the new General Mark Clark Bridge is completed. Construction of intermediate diaphragms is ongoing. Installation of chain link fence around the detention ponds at the Camano and Snohomish segments is in progress.

Summary Project Schedule

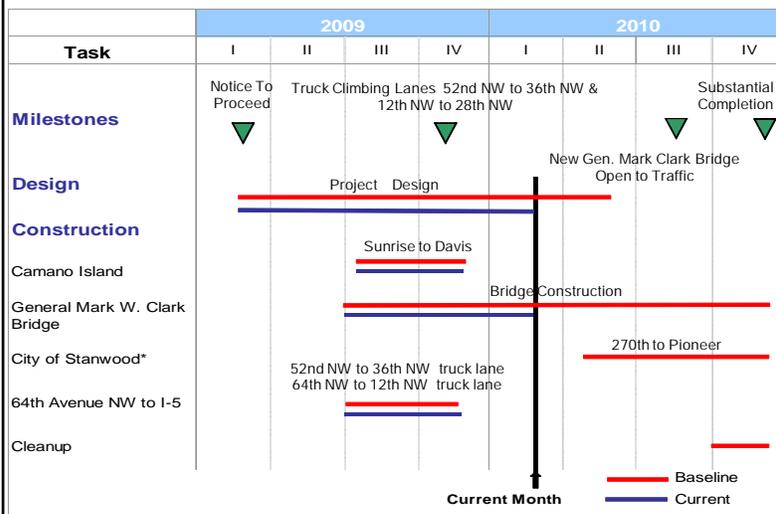

* Construction of eastbound Pioneer to 72nd truck climbing lane rescheduled to 2010

Quality Control/Quality Assurance

WSDOT's Quality verification team completed 133 audits covering 1021 separate audit items resulting in seven non-conformance incidents (NCIs) with two in resolution. QA/QV team finished materials documentation for bridge retaining walls.

Risks / Challenges / Issues

- Possible utility interferences within downtown Stanwood.
- Wet weather conditions present a challenge for environmental compliance throughout the job.

Public Information & Community Outreach

- Continued posting bridge construction photos on Flickr site
- Distributed weekly updates to media and SR532 e-mail update (857 currently subscribed)
- Distributed construction safety zone posters to Stanwood High School and noise fliers to homeowners near Pioneer Highway.
- Continue responding quickly to questions/concerns from local residents and drivers

Upcoming Activities – March 2010

- Construction of intermediate diaphragms for the new General Mark Clark Bridge.
- Construction of Mechanically Stabilized Earth (MSE) Wall on the east side of the new bridge.
