

# MONTHLY PROJECT OVERVIEW

## I-405, South Bellevue Widening Project

January 2009


**Project Location:** I-405, 112th Ave SE to SE 8th St  
**Design-Builder:** Atkinson

**PIN:** 840541F, 840509A, 840541G  
**WIN:** U40541F

### Design / Build Contract Summary


Contract Award: February 16, 2007  
 Notice to Proceed: March 15, 2007  
 Original Contract Time: 934 Calendar Days  
 Original Substantial Completion: October 2009  
 Original Contract Amount: \$124,000,000  
 Revised Contract Amount: \$124,000,000

### Project Progress to Date



Project Status as of: January 31, 2009  
 Contract Days Elapsed: 688 of 934 = 73.7%  
 Contract Amount Earned to Date: \$102,082,795 = 82.4%  
 Contract Amount Earned This Period: \$1,279,087 = 1.0%  
 Current Projected Completion Date: Oct. 2009 (on schedule)

### Project Cash Flow

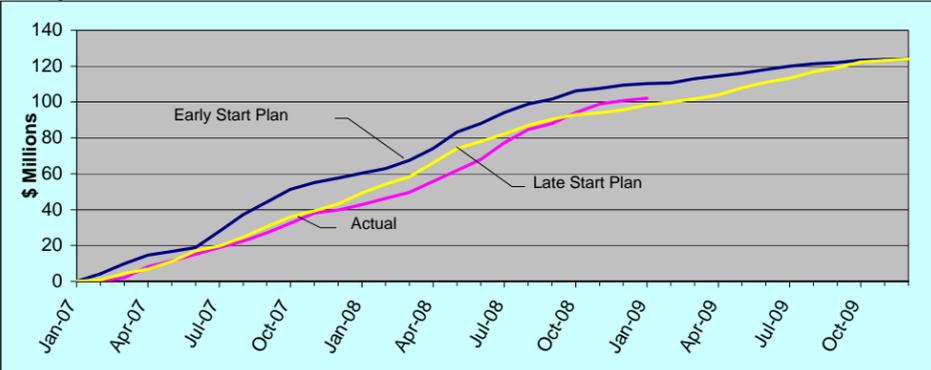

### January 2009 Highlights



### Design-Build Schedule Summary

**Design:** Original design is complete. Design team will continue to support construction to the end of the project. Design documentation package is being assembled.


**Construction:** On northbound I-405 between 112th Ave SE and I-90, the highway has been restriped and the new lane has been opened. Also, the 112th ramp meter has been activated. At Coal Creek Parkway interchange, fine grading and landscaping has begun. Cement concrete paving is complete southbound from SE 8th to I-90 and concrete barrier is being set. Started constructing the southbound I-405 widening over SE 8th street. Erected permanent sign bridges on both northbound and southbound I-405. Checked, reinforced and re-applied erosion control measures to stabilize exposed soil for the wet season.

### Quality Control / Quality Assurance

The Design Builder's Quality Assurance team continues inspection and materials testing for the project, with WSDOT providing oversight inspection and verification testing. Both teams are making good use of quality hold points. Hold points are established to identify critical components of the construction process, in which work cannot proceed until verification is performed and release is granted by the Design Builder's quality organization.

Materials test data is being entered into SAMs, the Statistical Analysis of Materials. Analyses of the test results indicate that materials incorporated into the project are meeting contract specifications.

### Summary Project Schedule

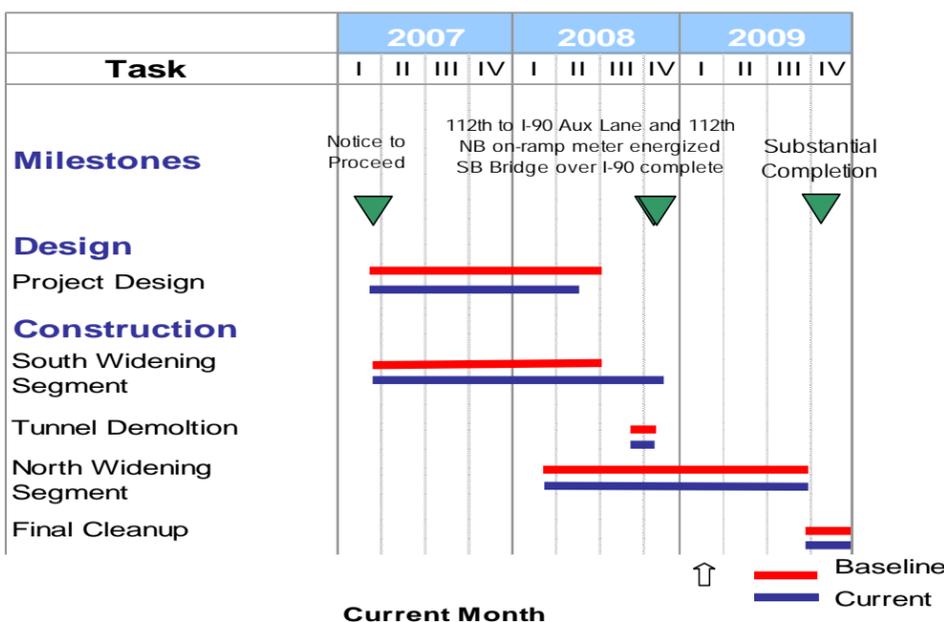

### Risks / Challenges / Issues

Winter weather is creating challenges for work progress and erosion control. Minimizing impacts to the public from construction traffic control remains a challenge. Deep excavation for northbound drainage structure.

### Public Information & Community Outreach

Informed public of closures using construction updates on WSDOT web sites. Updated project milestone map on web site to reflect accomplishments. Received several notes from drivers pleased with their reduced commute time on northbound I-405 as a result of the new lane.

### Upcoming Activities - Winter 2008/2009

Bridge and wall construction at SE 8th Street for southbound bridge widening. Weekend closure of southbound off-ramp to SE 8th Street. Construction of deep drainage structure east of northbound I-405, north of I-90.

For more information, Call 425.401.4143 or 425.456.8624 or visit [www.wsdot.wa.gov/Projects/i405/112thAveToSE8th/](http://www.wsdot.wa.gov/Projects/i405/112thAveToSE8th/)

**IT'S YOUR NICKEL. WATCH IT WORK.**

"Washington's Future Just Got Better"  
**MAKING EVERY DOLLAR COUNT.**

