

# MONTHLY PROJECT OVERVIEW

## I-405 I-5 to SR 169 Stage 1 Widening

March 2009


**Project Location:** I-405, I-5 to SR 169  
**Design-Builder:** Tri-State Construction Inc.

**PIN:** 816701B, 816719A, 840502B, 840503A  
**WIN:** U40502B

### Design / Build Contract Summary

Contract Award: June 13, 2007  
 Notice to Proceed: July 5, 2007  
 Original Contract Time: 1061 Calendar Days  
 Original Substantial Completion: June, 2010  
 Original Contract Amount: \$91,500,000  
 Revised Contract Amount: \$91,500,000


### Project Progress to Date




### Project Status as of: **March 31, 2009**

Contract Days Elapsed: 635 Days  
 Contract Amount Earned to Date: \$1,053,400.00  
 Contract Amount Earned This Period: \$73,699,900.00  
 Current Projected Completion Date: June, 2010

### Project Cash Flow



### March 2009 Highlights

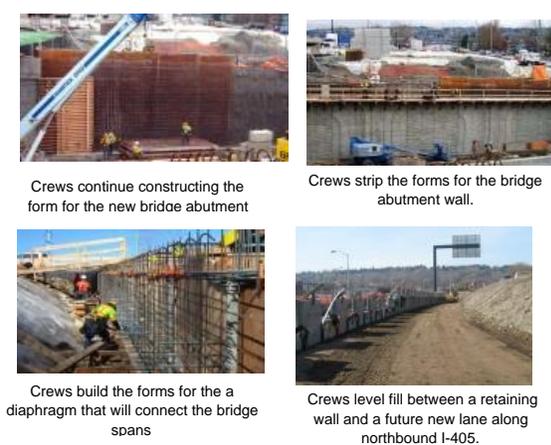

### Design-Build Schedule Summary

**Design:** Work on the completion of project deviations is continuing. Field Design Changes and Notice of Design Changes are being processed documenting revisions to the Issued for Construction plans. Videoing of existing drainage is proceeding. Closeout of the design documentation is progressing.

**Construction:** Work on wall 4010 was completed. Work is continuing on wall 4008. Deck forming and rebar placement is underway on spans 1 and 2. Precast girders were placed for span 3 of the Oakesdale structure. Illumination, permanent signing and ITS work is progressing on both I-405 and SR-167. Moment slab barrier was completed on SR-167 and precast barrier is being installed along both I-405 and SR-167.

### Quality Control / Quality Assurance

The project environmental team continues to do a great job of protecting the environment. The project inspection and materials teams thorough inspection and adherence to materials acceptance requirements are key to providing a quality project.

### Risks / Challenges / Issues

Weather continues to be the greatest challenge to progressing with the project work. Rain and snow in March have caused delays to some of the work activities. Work in Springbrook Creek to bypass the existing channel and remove the existing box culvert may begin as early as June, 2009.

### Contract Milestones

Contract Milestones	Date
Contract Time	May 31, 2010
NB I-405 Lane between I-5 and SR-167 Open to Traffic	Fall 2009
SB I-405 Lane between I-5 and SR-167 Open to Traffic	Fall 2009
Final Configuration Open to Traffic	Fall 2009
Stream Mitigation Site Complete	Fall 2009

### Public Information and Community Outreach

Released lane, ramp and road closure information to the media. WSDOT and the Design-Builder also responded to questions from citizens about the project.

### Upcoming Activities - April 2009

Work will continue on the placement of deck forming for the new Oakesdale structure. Anticipate pouring the deck for Spans 1 and 2. Work will continue on wall 4008 and will begin on walls 4006 and 4007. A 14 day closure of the Tukwila Parkway on-ramp will be implemented. Paving will occur along I-405 and SR-167.

For more information call 425-456-8585  
 visit <http://www.wsdot.wa.gov/Projects/I405/I5toSR169/>

IT'S YOUR NICKEL.  
WATCH IT WORK.

"Washington's Future Just Got Better"  
 MAKING EVERY DOLLAR COUNT.

