

# MONTHLY PROJECT OVERVIEW

## I-405, South Bellevue Widening Project

October 2009


**Project Location:** I-405, 112th Ave SE to SE 8th St  
**Design-Builder:** Atkinson

**PIN:** 840541F, 840509A, 840541G  
**WIN:** U40541F

### Design / Build Contract Summary

Contract Award: February 16, 2007  
 Notice to Proceed: March 15, 2007  
 Original Contract Time: 934 Calendar Days  
 Original Substantial Completion: October 2009  
 Original Contract Amount: \$124,000,000  
 Revised Contract Amount: \$125,525,313  
 Project Status as of: October 31, 2009  
 Contract Days Elapsed: 961  
 Contract Amount Earned to Date: \$124,950,023 = 99.5%  
 Contract Amount Earned This Period: \$1,402,856 = 1.1%  
 Current Projected Completion Date: Feb. 2010 (on schedule)  
 Achieved Substantial Completion: September 22, 2009

### Project Cash Flow

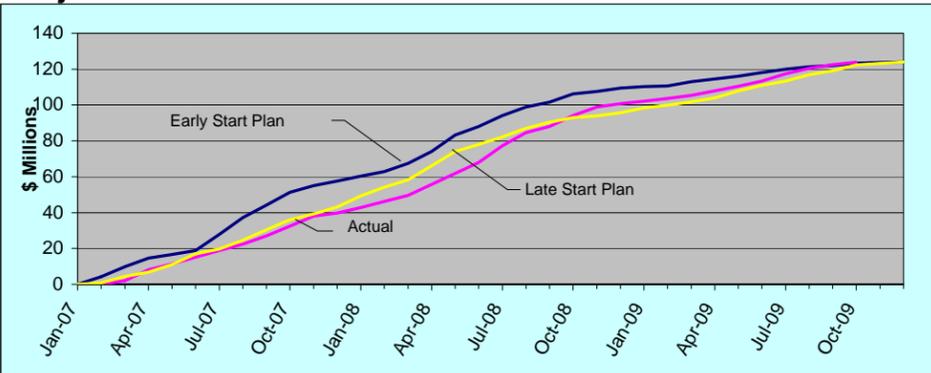


### Design-Build Schedule Summary

**Design:** Original design is complete. Design team will continue to support construction to the end of the project. Design documentation package is being assembled.

**Construction:** Construction of noise wall 2000, planting, and punch list items are currently being worked on. The contractor achieved substantial completion on September 22, 2009.

### Project Progress to Date



### October 2009 Highlights



Completion of the science experiment by the Coal Creek Parkway bike path



City of Bellevue outfall pipe near 112th street complete



All lanes are in final configuration



Super Pond is operational at the southbound Coal Creek Parkway onramp

### Quality Control / Quality Assurance

The Design Builder's quality control and quality assurance staffs are working to close-out all the remaining punch list items for final acceptance of work.

Quality assurance is assembling all project records for submittal of the final documentation package to WSDOT.

### Risks / Challenges / Issues

Minimizing traffic control and coordinating with other regional work.


### Public Information & Community Outreach

Informed the public of closures using construction updates on WSDOT web sites and ListServ messaging. We are planning a ribbon cutting for the project in late November.

### Upcoming Activities - Fall/Winter 2009

Installing plants, completing noise wall 2000, and completing the punch list items. Physical completion is on December 20, 2009 and completion is on February 17, 2010.

### Summary Project Schedule

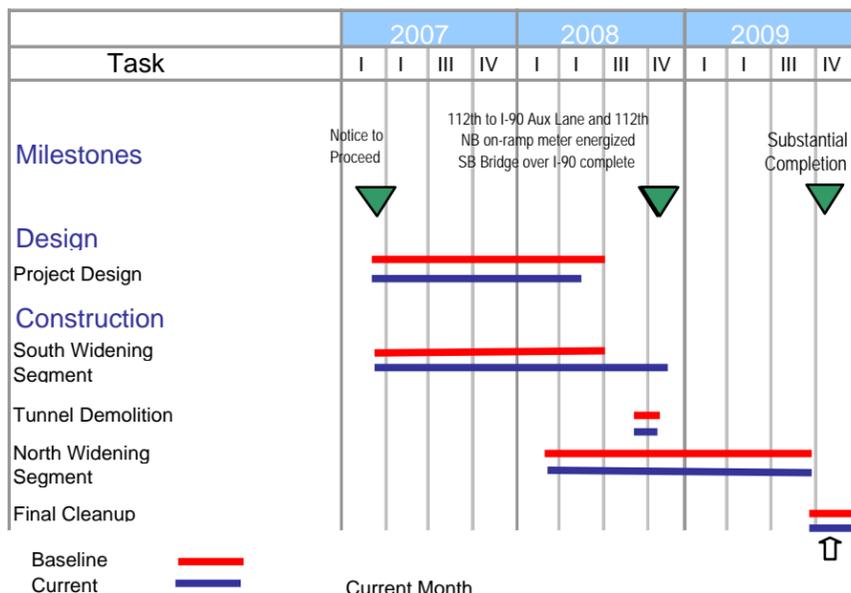

For more information, Call 425.401.4143 or 425.456.8624 or visit [www.wsdot.wa.gov/Projects/i405/112thAvetoSE8th/](http://www.wsdot.wa.gov/Projects/i405/112thAvetoSE8th/)

**IT'S YOUR NICKEL. WATCH IT WORK.**

"Washington's Future Just Got Better"  
**MAKING EVERY DOLLAR COUNT.**

**Washington State Department of Transportation**
