

MONTHLY PROJECT OVERVIEW
I-405 I-5 to SR 169 Stage 1 Widening

February 2008


Project Location: I-405, I-5 to SR 169
Design-Builder: Bilfinger/Tri-State Joint Venture

PIN: 816701B, 816719A, 840502B, 840503A, 840504A
WIN: U40502B

Design / Build Contract Summary

Contract Award: June 13, 2007
 Notice to Proceed: July 5, 2007
 Original Contract Time: 1061 Calendar Days
 Original Substantial Completion: June 2010
 Original Contract Amount: \$91,500,000
 Revised Contract Amount: \$91,500,000

Project Progress to Date



Project Status as of: **February 29, 2008**

Contract Days Elapsed: 239 Calendar Days
 Contract Amount Earned to Date: \$22,592,266.31
 Contract Amount Earned This Period: \$12,726,470.81
 Current Projected Completion Date: June, 2010

January 2008 Highlights



Crews install liner for water pipeline in Tukwila.




Crews prepare to install VMS sign on SR 167.



Crews install a gantry pole on SR 167.

Project Cash Flow

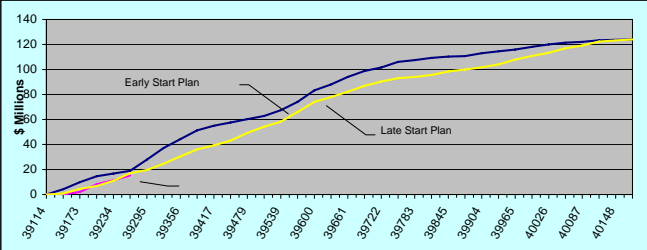

Design-Build Schedule Summary

Design: The Design-Builder is working toward submittal of the Issued For Construction plans and specifications for the SR-167 part of the project. Some of the I-405 package has been prepared for early release and the rest is continuing toward an Issued for Construction submittal. WSDOT worked with the Design-Builder during task force meetings to answer questions and provide input for their design of the project.

Construction: Work has begun on the slip-lining of the SPU waterline and is on schedule. The phase I shafts and columns for the new Springbrook Creek/Oakesdale Avenue structure are currently being constructed. The HOT lane and ITS construction is continuing on SR-167.

Quality Control / Quality Assurance

WSDOT worked with the Design-Builder to improve their Quality Management Plan. WSDOT also reviewed the installation of the High Visibility Fence in the areas at the west end of the project. Site specific inspections continue as the Design-Builder mobilizes equipment into new areas of the project.

Summary Project Schedule

Contract Milestones	Date
Contract Time	May 31, 2010
NB I-405 Lane between I-5 and SR-167 Open to Traffic	September 1, 2009
SB I-405 Lane between I-5 and SR-167 Open to Traffic	September 1, 2009
Final Configuration Open to Traffic	September 1, 2009
Stream Mitigation Site Complete	November 23, 2009

Risks / Challenges / Issues

Removal of contaminated soils from the pond S-3 site should begin soon.

Public Information & Community Outreach

Contacts have been made with business owners in the areas of work.

Upcoming Activities - February 2008

Work on the HOT lanes is continuing toward an April opening. The Seattle Public Utility work is continuing with the completion expected during the month of March. Work on the new Springbrook Creek substructure is continuing. Clearing for walls, soil stabilization and widening has begun and will continue through the month.

For more information call 425-456-8585
 visit <http://www.wsdot.wa.gov/Projects/i405/i5toSR169/>

