

# MONTHLY PROJECT REPORT

## SR 104 Hood Canal Bridge Retrofit and East Half Replacement

February 2004

**Project Location:** SR 104, Hood Canal Bridge

**PIN:** 310407B

**WIN:** C10407T

**Contractor:** Kiewit-General, A Joint Venture


### Project Cost Summary:

Category	Budget (\$M)	Expended (\$M)
Construction Contract	221.17	30.57
Engineering	15.00	2.35
Contingencies / Other	8.98	0.60
Total	245.15	33.52

### Project Schedule Status:

- Graving Dock construction is behind schedule as a result of a suspension of work due to an archaeology investigation.
- Contractor and WSDOT are evaluating the schedule at the Graving Dock to determine if plan completion date is achievable.

### Project Progress To Date: (% Based on contract \$'s)



### Project Milestones Overview:

Milestone	Plan	Current	Months Ahead
Notice to Proceed	Jul-03	Jul-03	0.0
Start Project Construction	Aug-03	Aug-03	0.0
Graving Dock Work Suspended		Aug-03	
Pontoons - 1st Concrete Placement	Jan-04	?	?
Start West Half Bridge Deck Widening	May-04	?	?
Complete Graving Dock Construction	Nov-04	?	?
Pontoons - 1st Float Out at Graving Dock	Nov-04	?	?
Complete West Bridge Approach Spans	Sep-05	?	?
Complete East Bridge Approach Spans	Oct-05	?	?
Set 1st Bridge Anchor	Jul-05	?	?
Complete Pontoon & Anchor Casting	Jul-05	?	?
Close Bridge	May-06	?	?
Open Bridge	Jun-06	?	?
Complete West Half Elect / Mech Upgrade	Aug-07	?	?
Substantial Completion	Dec-07	?	?

Hood Canal Bridge



Access Rd to Work Trestle ↑

Graving Dock PA



K-G checking Grade on a section of pipe DR1-23. ↑

[Click on an Image to enlarge](#)

### Progress Highlights for February 2004:

- Continue Drainage Work at Graving Dock Site
- Continue Erosion Control Efforts at Canal Site
- Continue Preparation for Construction at Canal Site

### Risks/Challenges/Issues:

- Resuming Graving Dock Construction
- Working within Marine Work Restrictions
- Maintain Public, Contractor and WSDOT Safety


### Activities Scheduled for March 2004:

- Continue Drainage Work at Graving Dock
- Inventory Existing RS&T Pontoons
- Preparation Activities for Canal Site Construction

### Public Information:

- Presentations to the Peninsula Regional Transportation Planning Organization and the Norwester Rotary Club of Port Angeles.
- Maintained ongoing media updates regarding graving dock status.
- Monthly flier update distributed for use by local agencies and organizations
- Web site ([www.hoodcanalbridge.com](http://www.hoodcanalbridge.com)) received 2,049 page views in January.

### Project Summary Schedule: \*Once the Graving Dock work resumes an updated schedule will be provided.

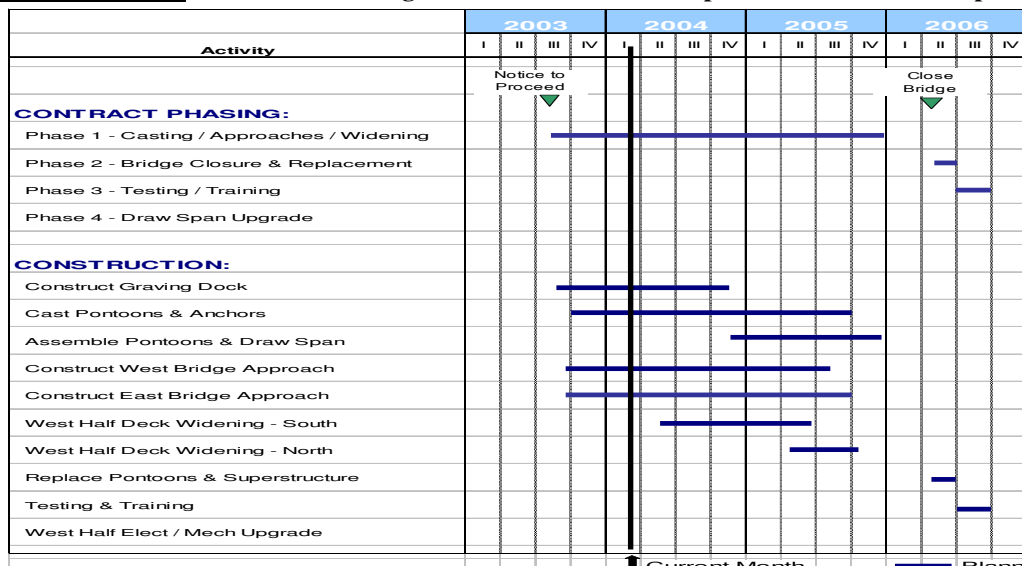

For more information, Call Ron Lewis, Project Manager at (360) 357-2614

Or visit our website: [www.hoodcanalbridge.com](http://www.hoodcanalbridge.com)
