

MONTHLY PROJECT REPORT

SR 104 Hood Canal Bridge Retrofit and East Half Replacement

January 2004

Project Location: SR 104, Hood Canal Bridge

PIN: 310407B

WIN: C10407T

Contractor: Kiewit-General, A Joint Venture

Project Cost Summary:

Category	Budget (\$M)	Expended (\$M)
Construction Contract	221.17	28.93
Engineering	15.00	2.02
Contingencies / Other	8.98	0.50
Total	245.15	31.45

Project Schedule Status:

- Graving Dock construction is behind schedule as a result of a suspension of work due to an archaeology investigation.
- Contractor and WSDOT are evaluating the schedule at the Graving Dock to determine if plan completion date is achievable.

Hood Canal Bridge



Work Trestle with Crane


Graving Dock PA



K-G checking Grade on a section of pipe DR1-23.

[Click on an Image to enlarge](#)

Project Progress To Date: (% Based on contract \$'s)



Progress Highlights for January 2004:

- Drainage Work at Graving Dock Continued
- East Approach Access Road at Bridge Site Completed
- Continue Work Trestle for East Approach at HCB

Risks/Challenges/Issues:

- Resuming Graving Dock Construction
- Working within Marine Work Restrictions
- Maintain Public, Contractor and WSDOT Safety

Project Milestones Overview:

Milestone	Plan	Current	Months Ahead
Notice to Proceed	Jul-03	Jul-03	0.0
Start Project Construction	Aug-03	Aug-03	0.0
Graving Dock Work Suspended		Aug-03	
Pontoons - 1st Concrete Placement	Jan-04	?	?
Start West Half Bridge Deck Widening	May-04	?	?
Complete Graving Dock Construction	Nov-04	?	?
Pontoons - 1st Float Out at Graving Dock	Nov-04	?	?
Complete West Bridge Approach Spans	Sep-05	?	?
Complete East Bridge Approach Spans	Oct-05	?	?
Set 1st Bridge Anchor	Jul-05	?	?
Complete Pontoon & Anchor Casting	Jul-05	?	?
Close Bridge	May-06	?	?
Open Bridge	Jun-06	?	?
Complete West Half Elect / Mech Upgrade	Aug-07	?	?
Substantial Completion	Dec-07	?	?


Activities Scheduled for February 2004:

- Continue Drainage Work at Graving Dock

Public Information:

- Presentations to Port Angeles Chamber of Commerce, Port Angeles Association of Realtors, Port Ludlow Village Council and Sequim Association of Realtors.
- Maintained ongoing media updates regarding graving dock status.
- Monthly flier update distributed for use by local agencies and organizations
- Web site (www.hoodcanalbridge.com) received 2,746 page views in January.

Project Summary Schedule: *Once the Graving Dock work resumes an updated schedule will be provided.

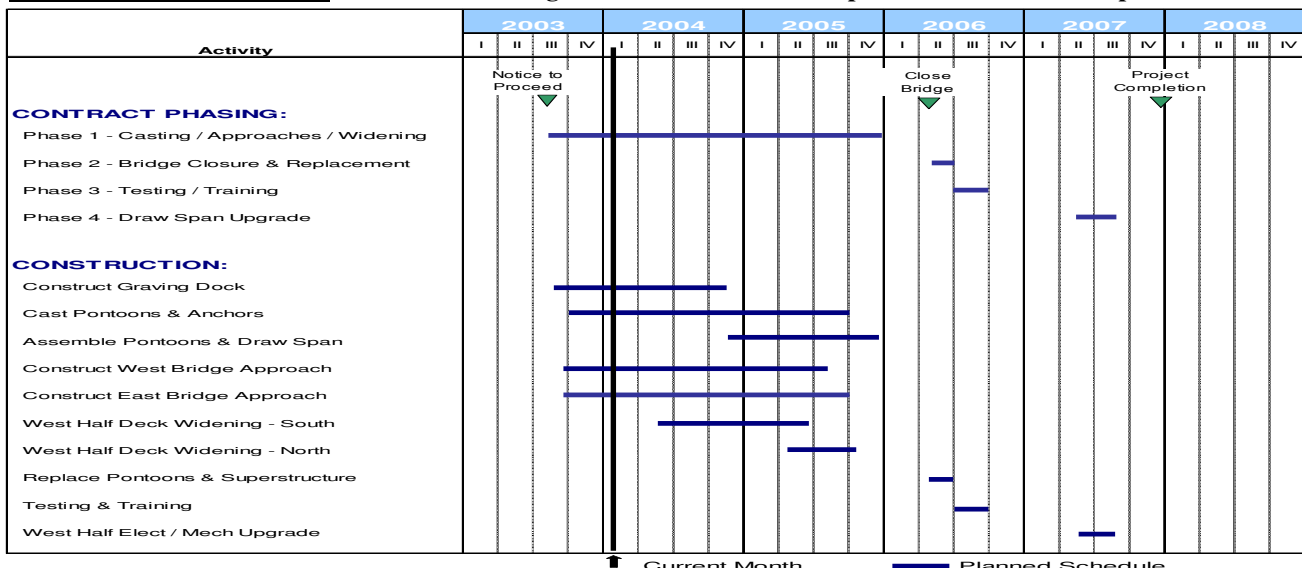

For more information, Call Ron Lewis, Project Manager at (360) 357-2614

Or visit our website: www.hoodcanalbridge.com
