

MONTHLY PROJECT REPORT

SR 104 Hood Canal Bridge Retrofit and East Half Replacement

December 2003

Project Location: SR 104, Hood Canal Bridge

PIN: 310407B

WIN: C10407T

Contractors: Kiewit-General, A Joint Venture


Project Cost Summary:

| Category | Budget (\$M) | Expended (\$M) |
|-----------------------|--------------|----------------|
| Construction Contract | 221.17 | 26.39 |
| Engineering | 15.00 | 1.75 |
| Contingencies / Other | 8.98 | 0.45 |
| Total | 245.15 | 28.59 |

Project Schedule Status:

- Graving Dock construction is behind schedule as a result of a suspension of work due to an archaeology investigation.
- Contractor and WSDOT are evaluating the schedule at the Graving Dock to determine if plan completion date is achievable.

Project Progress To Date: (% Based on contract \$'s)



Project Milestones Overview:

| Milestone | Plan | Current | Months Ahead |
|--|--------|---------|--------------|
| Notice to Proceed | Jul-03 | Jul-03 | 0.0 |
| Start Project Construction | Aug-03 | Aug-03 | 0.0 |
| Graving Dock Work Suspended | | Aug-03 | |
| Pontoons - 1st Concrete Placement | Jan-04 | ? | ? |
| Start West Half Bridge Deck Widening | May-04 | ? | ? |
| Complete Graving Dock Construction | Nov-04 | ? | ? |
| Pontoons - 1st Float Out at Graving Dock | Nov-04 | ? | ? |
| Complete West Bridge Approach Spans | Sep-05 | ? | ? |
| Complete East Bridge Approach Spans | Oct-05 | ? | ? |
| Set 1st Bridge Anchor | Jul-05 | ? | ? |
| Complete Pontoon & Anchor Casting | Jul-05 | ? | ? |
| Close Bridge | May-06 | ? | ? |
| Open Bridge | Jun-06 | ? | ? |
| Complete West Half Elect / Mech Upgrade | Aug-07 | ? | ? |
| Substantial Completion | Dec-07 | ? | ? |

Hood Canal Bridge



Work Trestle - Span 1

Graving Dock PA



Drainage Installation

[Click on an Image to enlarge](#)

Progress Highlights for December 2003:

- Drainage Work at Graving Dock
- East Approach Access Road at Bridge Site
- Prepare Work Trestle Foundation for East Approach at HCB

Risks/Challenges/Issues:

- Resuming Graving Dock Construction
- Working within Marine Work Restrictions
- Maintain Public, Contractor and WSDOT Safety


Activities Scheduled for January 2004:

- Continue Drainage Work at Graving Dock
- Installing Bridge Work Trestle for East Approach

Public Information:

- Monthly flier update distributed for use by local agencies and organizations
- Planned and scheduled public presentations for Jan/Feb 04
- Maintained ongoing media updates regarding graving dock status.
- Web site (www.hoodcanalbridge.com) received 2,342 page views in December.

Project Summary Schedule:

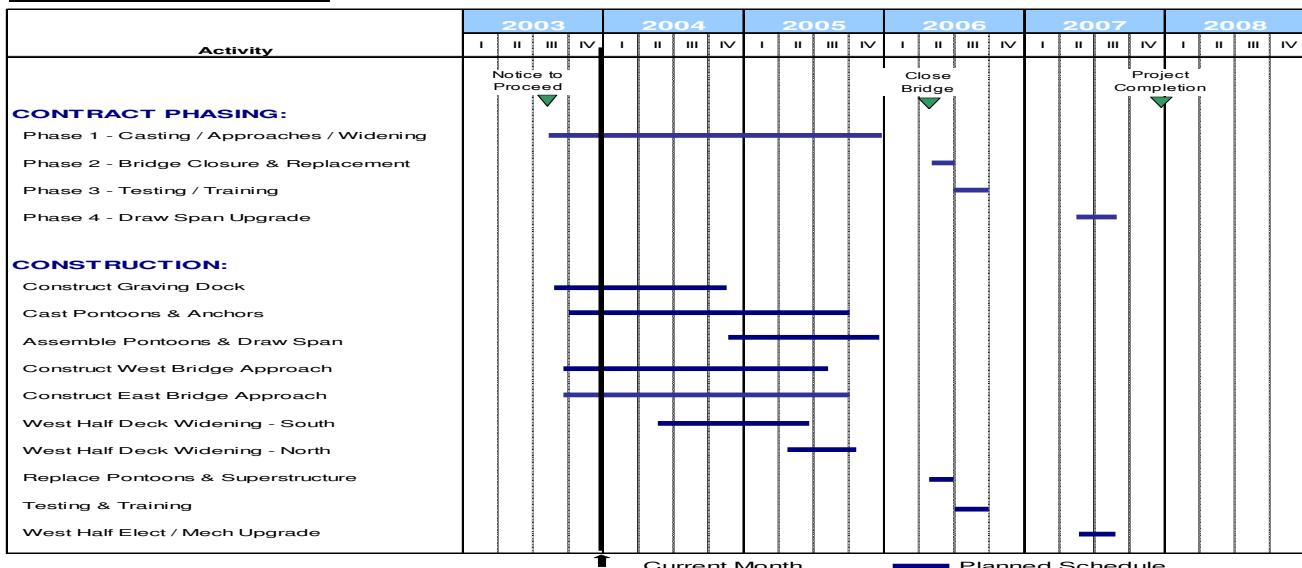

For more information, Call Ron Lewis, Project Manager at (360) 357-2614

Or visit our website: www.hoodcanalbridge.com
