

MONTHLY PROJECT REPORT

SR 104 Hood Canal Bridge Retrofit and East Half Replacement

OCTOBER 2003

Project Location: SR 104, Hood Canal Bridge

PIN: 310407B

WIN: C10407T

Contractors: Kiewit-General, A Joint Venture

Project Cost Summary:

Category	Budget (\$M)	Expended (\$M)
Construction Contract	221.17	8.30
Engineering	15.00	1.16
Contingencies / Other	8.98	0.31
Total	245.15	9.77

Project Schedule Status:

- Graving Dock construction is behind schedule as a result of a suspension of work due to an archaeology investigation.
- Contractor and WSDOT are evaluating the schedule at the Graving Dock to determine if plan completion date is achievable.

Hood Canal Bridge



Soldier Pile Installation ↑

Graving Dock PA




Cofferdam Boring ↑

[Click on an Image to enlarge](#)

Progress Highlights for October 2003:

- Complete Shoreline Restoration at Port Angeles
- Work on the East Approach Access Road at Bridge Site

Project Progress To Date: (% Based on contract \$'s)



Risks/Challenges/Issues:

- Resuming Graving Dock Construction
- Working within Marine Work Restrictions
- Maintain Public, Contractor and WSDOT Safety

Activities Scheduled for November 2003:

- Start Drainage Work at Graving Dock
- East Approach Temporary Work Trestle Fabrication at Bridge
- Continue East Approach Access Road at Bridge Site


Project Milestones Overview:

Milestone	Plan	Current	Months Ahead
Notice to Proceed	Jul-03	Jul-03	0.0
Start Project Construction	Aug-03	Aug-03	0.0
Graving Dock Work Suspended		Aug-03	
Pontoons - 1st Concrete Placement	Jan-04	?	?
Start West Half Bridge Deck Widening	Oct-03	?	?
Complete Graving Dock Construction	Nov-04	?	?
Pontoons - 1st Float Out at Graving Dock	Nov-04	?	?
Complete West Bridge Approach Spans	Dec-05	?	?
Complete East Bridge Approach Spans	Oct-05	?	?
Set 1st Bridge Anchor	Jul-05	?	?
Complete Pontoon & Anchor Casting	Jul-05	?	?
Close Bridge	May-06	?	?
Open Bridge	Jun-06	?	?
Complete West Half Elect / Mech Upgrade	Aug-07	?	?
Substantial Completion	Dec-07	?	?

Public Information:

- Presentation to the Olympic Peninsula Marketing Association, Nov. 6.
- Maintained ongoing media updates regarding graving dock status.
- Web site (www.hoodcanalbridge.com) received 2,488 page view in October, up 11 percent from September.

Project Summary Schedule:

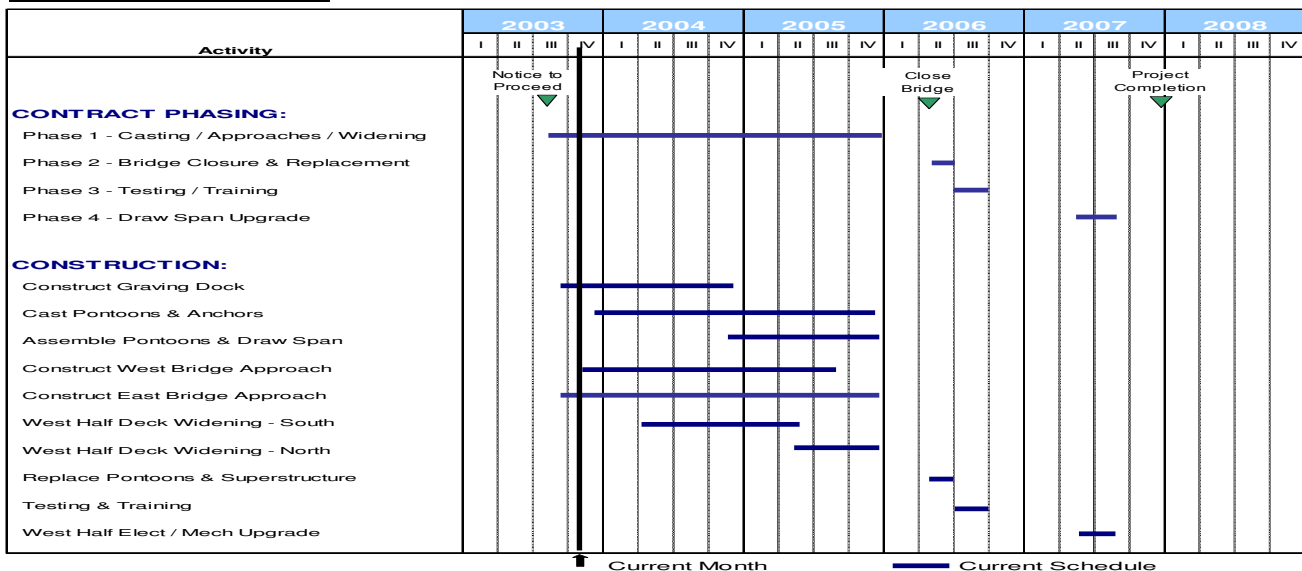

For more information, Call Ron Lewis, Project Manager at (360) 357-2614

Or visit our website: www.hoodcanalbridge.com
