

## SR 104 Hood Canal Bridge Retrofit and East Half Replacement

November 2004


**WIN:** C10407T

**Contractor:** Kiewit-General, A Joint Venture

### **Project Cost Summary:**


Sections	Dollars in Millions	Percent of Total
Preliminary Engineering	\$12,097,853	97.8%
Right-of-Way	\$6,788,623	88.4%
Construction	\$117,633,995	41.2%
Total	\$136,520,471	47.9%

**Project Cash Flow:**      **Planned vs. Actual Expenditures**  
**(Total Project Cost)**

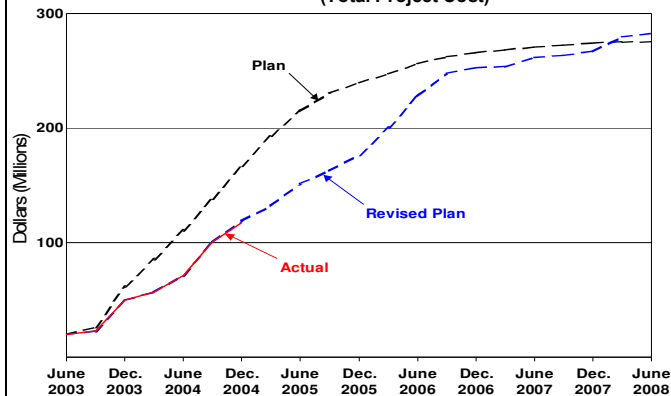


### Project Milestones Overview:

Milestone	Original	Current	Mos. Change
Notice to Proceed	Jul-03	Jul-03	0.0
Start Project Construction	Aug-03	Aug-03	0.0
Start Graving Dock Sheetpile	Sep-03	Apr-04	-7.5
Pontoons - 1st Concrete Placement	Jan-04	Nov-05	-22.0
Start West Half Bridge Deck Widening	May-04	May-04	0.0
Complete Graving Dock Construction	Nov-04	Aug-06	-21.0
Pontoons - 1st Float Out at Graving Dock	Nov-04	Nov-06	-24.0
Complete West Bridge Approach Spans	Sep-05	Sep-05	0.0
Complete East Bridge Approach Spans	Oct-05	Oct-05	0.0
Set 1st Bridge Anchor	Jul-05	Jul-07	-24.0
Complete Pontoon & Anchor Casting	Jul-05	Jul-07	-24.0
Close Bridge	May-06	May-08	-24.0
Open Bridge	Jun-06	Jun-08	-24.0
Complete West Half Elect / Mech Upgrade	Aug-07	Aug-09	-24.0
Substantial Completion	Dec-07	Dec-09	-24.0



## Lift Rebar Cage for Shafts



*Aerial Photo of Graving Dock* 

**Click on an Image to enlarge**

**Progress Highlights for November 2004:**

**Graving Dock Site:**

- Archeology; Sheet Pile Driving; Work Trestle Pile; Pontoon Mockup; Set Crane Rail; Slab Trench Concrete.

**Canal Site:**

- Trestle Construction; Shaft Installation; Ready Bridge Deck for Winter; West Approach Access; Concrete Column Placement.

**Activities Scheduled for December 2004:**

**Graving Dock Site:**

- Archeology; Sheet Pile Driving; Work Trestle; Slab Concrete Placement; Trench Drains.

**Canal Site:**

- Trestle Construction; Shaft Installation; Concrete Column Placement; West Approach Access.

**Public Information:**

- Provided presentations to North Mason Chamber of Commerce and the Peninsula Regional Transportation Planning Organization.
- Updated project web site.
- Provided project media information.
- Distributed monthly project updates via e-mail to constituent list.

**Project Summary Schedule:** (Note: Based on current information. Adjustments will be made as necessary.)

[illegible]

For more information, Call Ron Lewis, Project Manager at (360) 357-2614

Or visit our website: [www.hoodcanalbridge.com](http://www.hoodcanalbridge.com)

