

# MONTHLY PROJECT REPORT

## SR 104 Hood Canal Bridge Retrofit and East Half Replacement

October 2004

**Project Location:** SR 104, Hood Canal Bridge  
**Contractor:** Kiewit-General, A Joint Venture


**PIN:** 310407B

**WIN:** C10407T

### Project Cost Summary:

Sections	Dollars in Millions	Percent of Total
Preliminary Engineering	\$12,097,420	97.8%
Right-of-Way	\$6,769,123	88.1%
Construction	\$106,726,321	37.4%
<b>Total</b>	<b>\$125,592,864</b>	<b>44.0%</b>


### Project Cash Flow: Planned vs. Actual Expenditures (Total Project Cost)

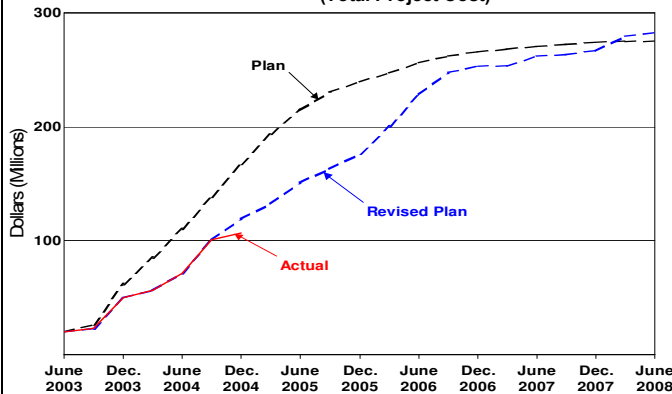

### Project Milestones Overview:

Milestone	Original	Current	Mos. Change
Notice to Proceed	Jul-03	Jul-03	0.0
Start Project Construction	Aug-03	Aug-03	0.0
Start Graving Dock Sheetpile	Sep-03	Apr-04	-7.5
Pontoons - 1st Concrete Placement	Jan-04	Nov-05	-22.0
Start West Half Bridge Deck Widening	May-04	May-04	0.0
Complete Graving Dock Construction	Nov-04	Aug-06	-21.0
Pontoons - 1st Float Out at Graving Dock	Nov-04	Nov-06	-24.0
Complete West Bridge Approach Spans	Sep-05	Sep-05	0.0
Complete East Bridge Approach Spans	Oct-05	Oct-05	0.0
Set 1st Bridge Anchor	Jul-05	Jul-07	-24.0
Complete Pontoon & Anchor Casting	Jul-05	Jul-07	-24.0
Close Bridge	May-06	May-08	-24.0
Open Bridge	Jun-06	Jun-08	-24.0
Complete West Half Elect / Mech Upgrade	Aug-07	Aug-09	-24.0
Substantial Completion	Dec-07	Dec-09	-24.0

Hood Canal Bridge



Cleaning Shaft for Concrete Placement

Graving Dock PA



Pontoon Test Section

[Click on an Image to enlarge](#)

### Progress Highlights for October 2004:

#### Graving Dock Site:

- Archeology; Sheet Pile Driving; Coffercell Backfill; Concrete Slabs; Trench Drains; Crane Footings

#### Canal Site:

- Concrete Barrier Placement; Bridge Cleanup; Trestle Construction; Phillystrand Installation; Shaft Casings

### Activities Scheduled for November 2004:

#### Graving Dock Site:

- Archeology; Sheet Pile Driving; Pontoon Mockup; Crane Rail Installation


#### Canal Site:

- Trestle Construction; Shaft Installation; West Approach Temporary Access

### Public Information:

- Provided presentation to East Bremerton Rotary
- Updated project web site
- Provided project media information
- Distributed monthly project updates via e-mail to constituent list

### Project Summary Schedule: (Note: Based on current information. Adjustments will be made as necessary.)

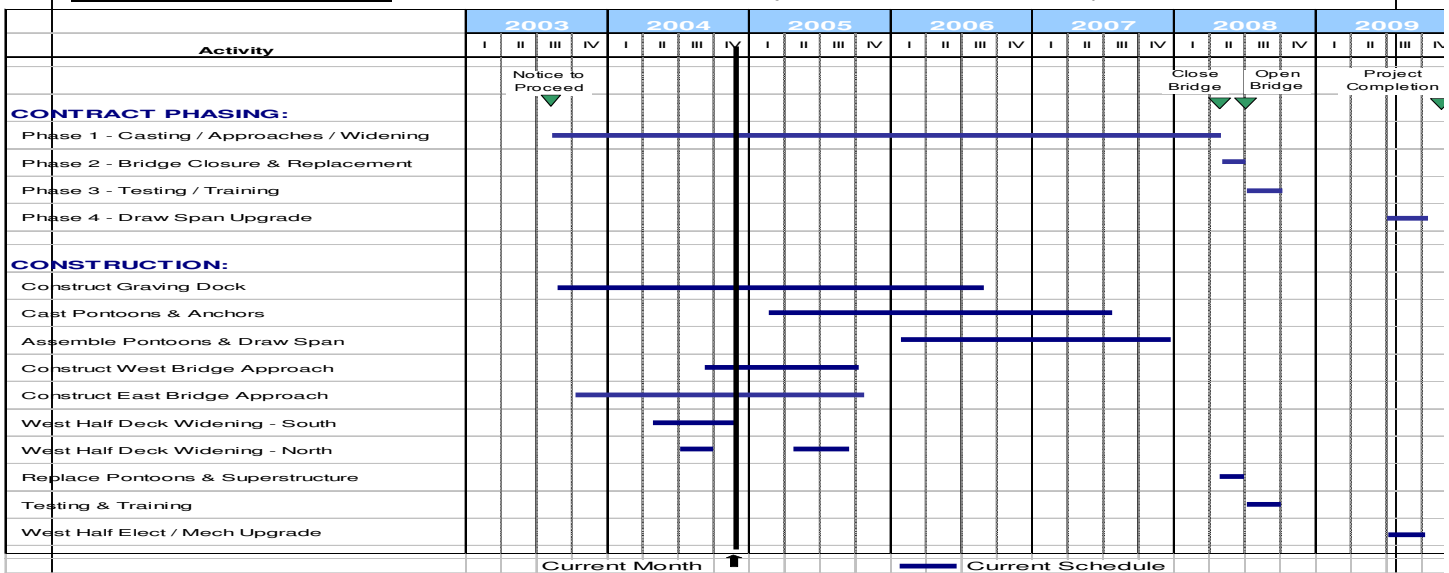

For more information, Call Ron Lewis, Project Manager at (360) 357-2614

Or visit our website: [www.hoodcanalbridge.com](http://www.hoodcanalbridge.com)
