


FREYA TO FAIRVIEW VICINITY - GRADING & STRUCTURES CONTRACT

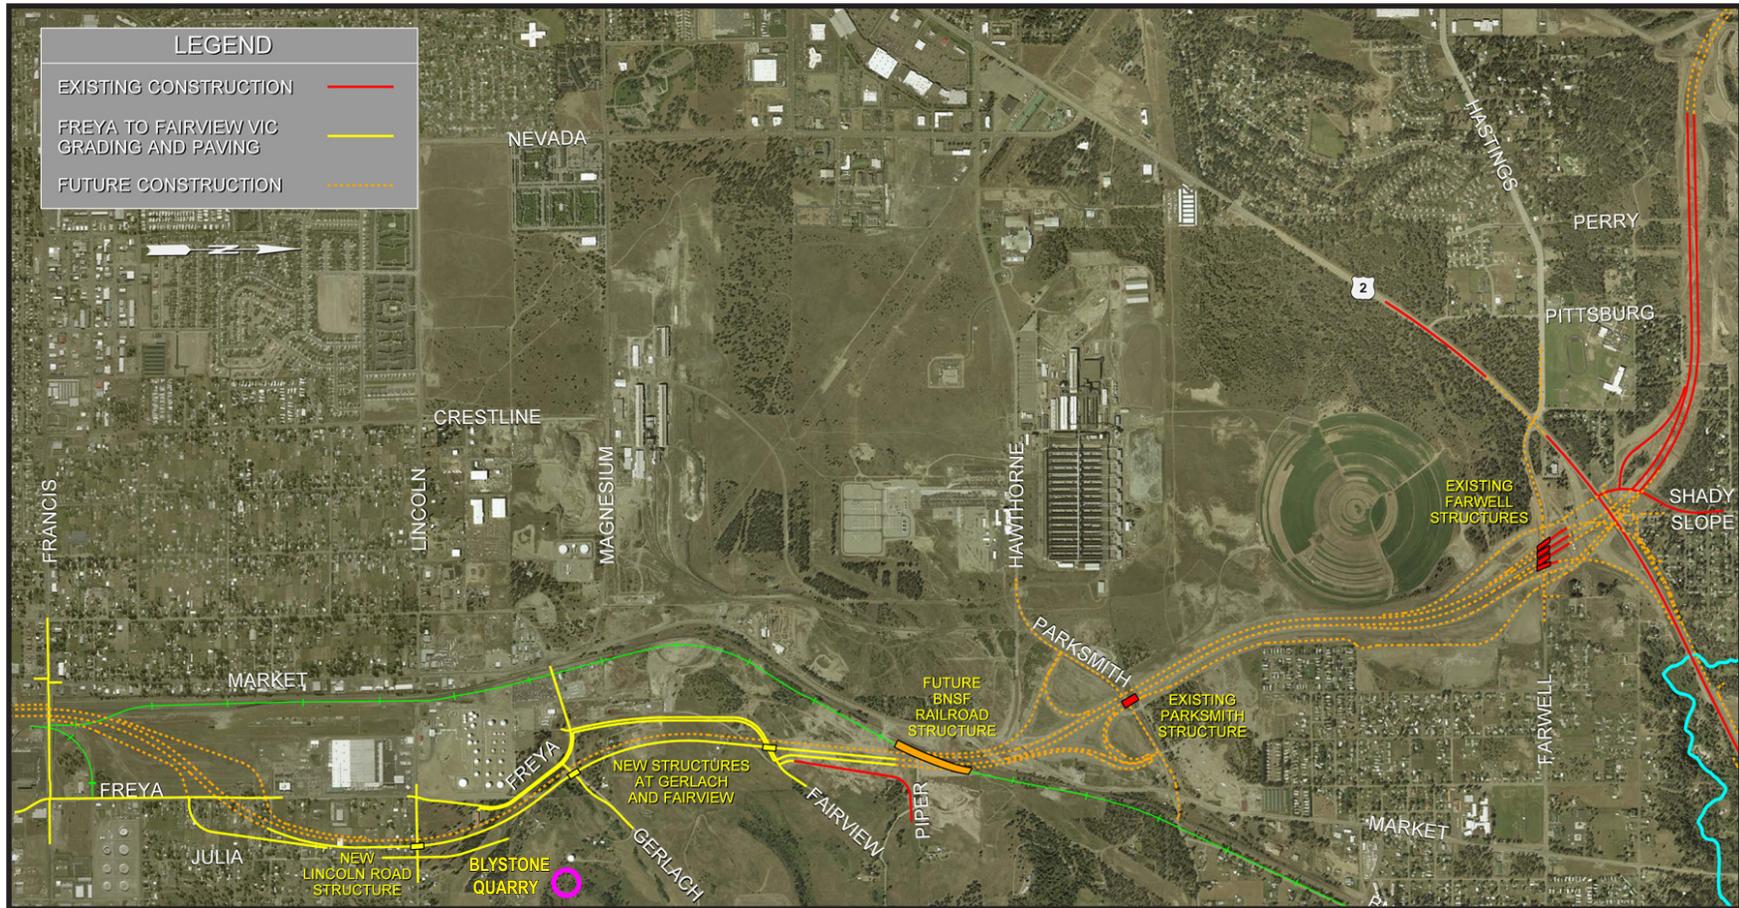

Contract Description:

This contract constructed bridges at Lincoln and Gerlach Roads, completed the earthwork between Freya Street and Fairview Road, realigned portions of Freya and Fairview Roads, improved the intersections at Francis/Freya and Francis/Market and constructed a roundabout at the Freya/NSC Intersection.

Planned Advertisement Date: January 29, 2007

Advertisement Date: January 29, 2007

Contract Award Date: April 4, 2007

Contract Funds: \$23.3 million Nickel funds

CONTRACT COMPLETE

Interesting Facts:

- This contract required nearly one million cubic yards of excavation.
- Included modifications to various utilities.
- A roundabout was constructed at the intersection of Freya Street and the NSC on/off ramp.


IT'S YOUR NICKEL.
WATCH IT WORK.

FREYA TO FAIRVIEW VICINITY - GRADING & STRUCTURES CONTRACT

Progress Planned Actual	Planned Schedule Start	Actual Start	Planned Schedule Finish	Actual Finish	Dec-03	Jan-04	Feb-04	Mar-04	Apr-04	May-04	Jun-04	Jul-04	Aug-04	Sep-04	Oct-04	Nov-04	Dec-04	Jan-05	Feb-05	Mar-05	Apr-05	May-05	Jun-05	Jul-05	Aug-05	Sep-05	Oct-05	Nov-05	Dec-05	Jan-06	Feb-06	Mar-06	Apr-06	May-06	Jun-06	Jul-06	Aug-06	Sep-06	Oct-06	Nov-06	Dec-06	Jan-07	Feb-07	Mar-07	Apr-07	May-07	Jun-07	Jul-07	Aug-07	Sep-07
					Dec-03	Jan-04	Feb-04	Mar-04	Apr-04	May-04	Jun-04	Jul-04	Aug-04	Sep-04	Oct-04	Nov-04	Dec-04	Jan-05	Feb-05	Mar-05	Apr-05	May-05	Jun-05	Jul-05	Aug-05	Sep-05	Oct-05	Nov-05	Dec-05	Jan-06	Feb-06	Mar-06	Apr-06	May-06	Jun-06	Jul-06	Aug-06	Sep-06	Oct-06	Nov-06	Dec-06	Jan-07	Feb-07	Mar-07	Apr-07	May-07	Jun-07	Jul-07	Aug-07	Sep-07
	12/29/03	12/5/03	2/29/07	2/29/07	[Green bar]																																													
	1/29/07	1/29/07	11/1/08	5/26/09	[Red bar]																																													
Construction Continued					[Green bar]																																													


Current Status:

100% Complete




Design

100% Complete



Right of Way

100% Complete



Construction

Progress:

Physical Completion was granted on May 26, 2009.



Lincoln Road Bridge looking east.

September 2009



Roundabout at the Freya/NSC Intersection, the Lincoln Road Bridge and Gerlach Road Bridge are in the background.

September 2008
