



ST3 Expert Review Panel: Overview of Project Schedules

April 12, 2016

SOUND TRANSIT

Lynnwood to Everett

Lynnwood Transit Center to 128th St SW (Mariner) LRT

	Year 1	Year 2	Year 3	Year 4	Year 5	Year 6	Year 7	Year 8	Year 9	Year 10	Year 11	Year 12	Year 13	Year 14	Year 15	Year 16	Year 17
Project Mobilization / PE Consultant Procurement <small>(jointly with 128th St SW to Everett via Southwest Everett Industrial Center)</small>	█																
Alternatives Analysis / Scoping / CE / DEIS <small>(jointly with 128th St SW to Everett via Southwest Everett Industrial Center)</small>		█	█	█													
PE / Final EIS <small>(jointly with 128th St SW to Everett via Southwest Everett Industrial Center)</small>					█	█											
Final Design Procurement							█										
Final Design							█	█	█	█							
Permitting / ROW								█	█	█	█						
Construction Procurement											█						
Construction											█	█	█	█	█	█	
Mobilization, Site Prep, Utility Relocation												█	█				
At-Grade Guideway Construction													█	█			
Aerial Guideway Construction														█	█		
Station Construction															█	█	
Trackwork																█	█
Systems																	█
Startup / Testing																	█
Project Float																	█

Lynnwood to Everett

128th St SW (Mariner) to Everett via Southwest Everett Industrial Center LRT

	Year 1	Year 2	Year 3	Year 4	Year 5	Year 6	Year 7	Year 8	Year 9	Year 10	Year 11	Year 12	Year 13	Year 14	Year 15	Year 16	Year 17	Year 18	Year 19	
Project Mobilization / PE Consultant Procurement <i>(jointly with Lynnwood TC to 128th SW)</i>	█																			
Alternatives Analysis / Scoping / CE / DEIS <i>(jointly with Lynnwood TC to 128th SW)</i>		█	█	█																
PE / Final EIS <i>(jointly with Lynnwood TC to 128th SW)</i>					█	█														
Final Design Procurement							█													
Final Design							█	█	█	█										
Permitting / ROW									█	█	█	█								
Construction Procurement												█								
Construction												█	█	█	█	█	█	█	█	█
Mobilization, Site Prep, Utility Relocation												█								
At-Grade Guideway Construction													█	█	█	█				
Aerial Guideway Construction													█	█	█	█				
Station Construction															█	█	█			
Trackwork																█	█			
Systems																	█	█		
Startup / Testing																			█	█
Project Float																				█


SR 522 & 145th St BRT: UW Bothell to 145th Light Rail Station

SR 522 & 145th St BRT: UW Bothell to 145th Light Rail Station

	Year 1	Year 2	Year 3	Year 4	Year 5	Year 6	Year 7	Year 8	Year 9
Project Mobilization / PE Consultant Procurement	█								
Alternatives Analysis / Scoping / CE / DEIS		█	█						
PE / Final EIS			█	█					
Final Design Procurement				█					
Final Design					█	█			
Permitting / ROW						█	█		
Construction Procurement							█		
Construction								█	█
Mobilization, Site Prep, Demolition, Utility Relocation								█	█
At-Grade Roadway Construction								█	█
Parking Facility Construction								█	█
BRT Station & Transit Center Construction									█
Project Float									█


West Seattle to Downtown Seattle

West Seattle to Downtown Seattle LRT

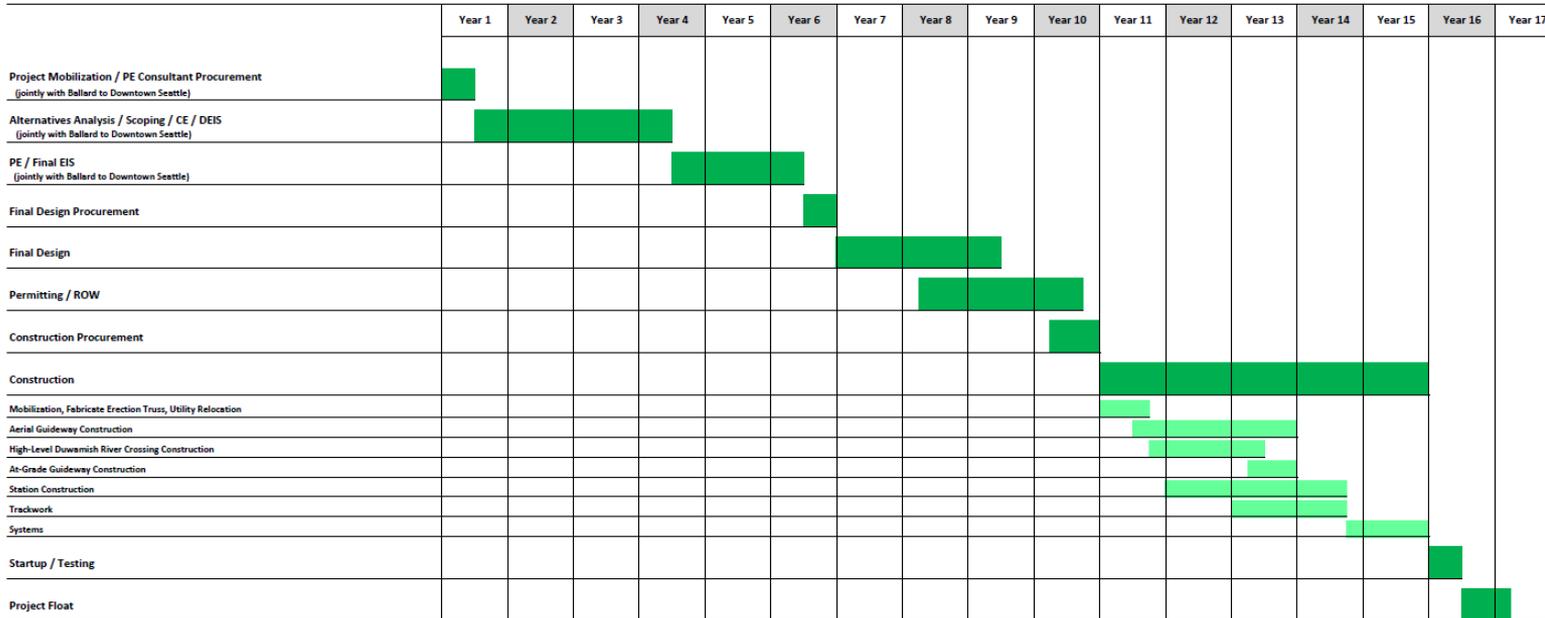

Ballard to Downtown Seattle LRT

Ballard to Downtown Seattle LRT, with new downtown rail tunnel

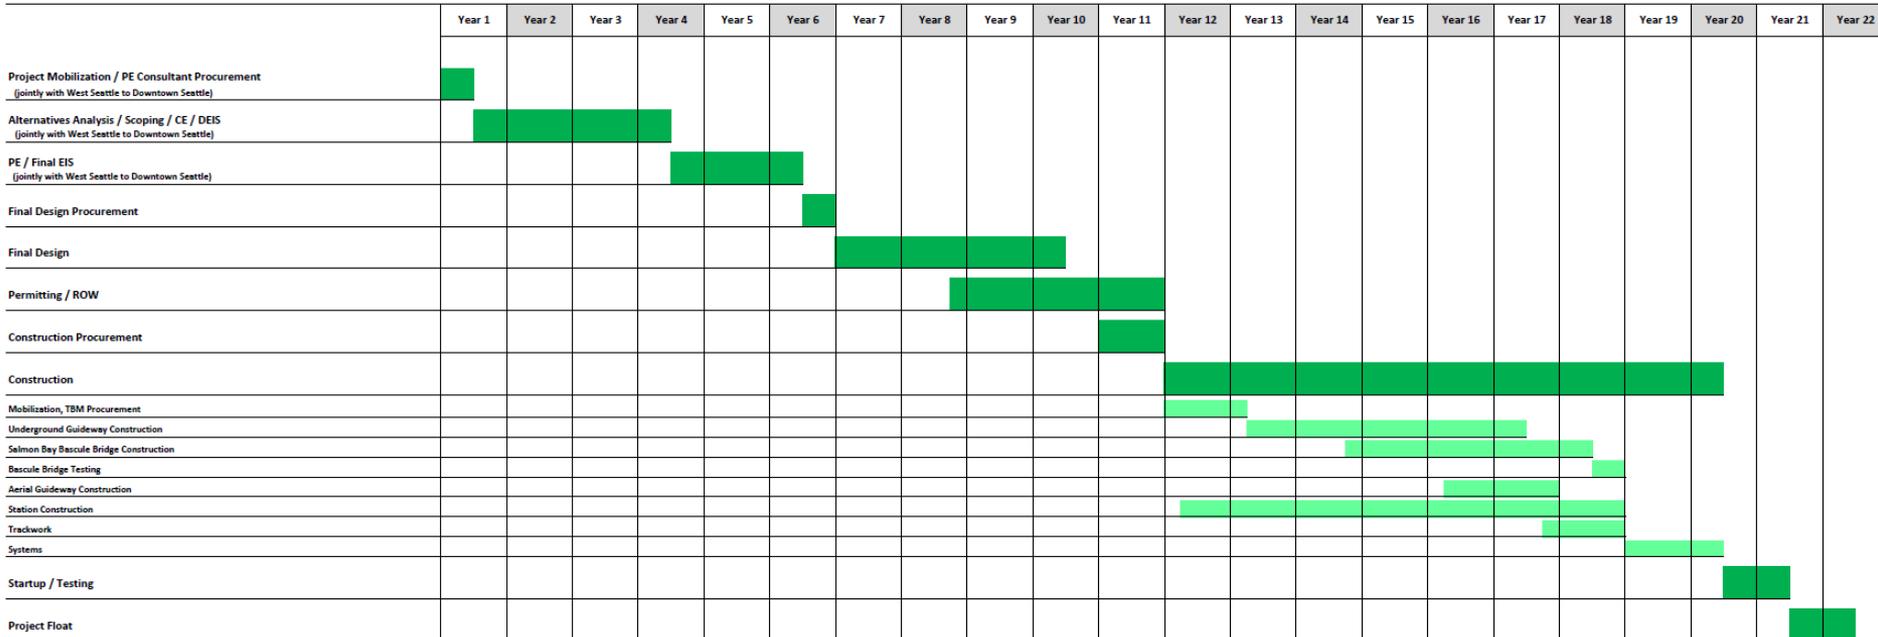

Redmond Technology Center to Downtown Redmond LRT

Redmond Technology Center to Downtown Redmond LRT

	Year 1	Year 2	Year 3	Year 4	Year 5	Year 6	Year 7	Year 8	Year 9	Year 10	Year 11	Year 12
Preliminary Engineering, including Environmental re-evaluation	█	█										
Final Design Procurement		█										
Final Design			█	█	█	█						
Permitting / ROW				█	█	█	█					
Construction Procurement						█						
Construction							█	█	█	█	█	
Mobilization, Site Prep, Utility Relocation							█					
At-Grade Guideway Construction								█	█			
Aerial Guideway Construction								█	█	█		
Station Construction									█	█		
Trackwork									█	█		
Systems										█	█	
Startup / Testing											█	█
Project Float												█

Bellevue to Issaquah LRT

Bellevue to Issaquah LRT

	Year 1	Year 2	Year 3	Year 4	Year 5	Year 6	Year 7	Year 8	Year 9	Year 10	Year 11	Year 12	Year 13	Year 14	Year 15	Year 16	Year 17
Project Mobilization / PE Consultant Procurement	█																
Alternatives Analysis / Scoping / CE / DEIS		█	█	█													
PE / Final EIS					█	█											
Final Design Procurement							█										
Final Design							█	█	█								
Permitting / ROW								█	█	█	█						
Construction Procurement											█						
Construction												█	█	█	█	█	█
Mobilization, Site Prep, Utility Relocation												█	█	█			
At-Grade Guideway Construction												█	█	█	█		
Aerial Guideway Construction													█	█	█		
Station Construction														█	█		
Trackwork															█	█	
Systems																█	█
Startup / Testing																	█
Project Float																	█

I-405 BRT: Lynnwood to Burien

I-405 BRT: Lynnwood to Burien

	Year 1	Year 2	Year 3	Year 4	Year 5	Year 6	Year 7	Year 8	Year 9
Project Mobilization / PE Consultant Procurement	█								
Alternatives Analysis / Scoping / CE / DEIS		█	█						
PE / Final EIS				█					
Final Design Procurement					█				
Final Design					█	█			
Permitting / ROW						█	█		
Construction Procurement							█		
Construction								█	█
Mobilization, Site Prep, Demolition, Utility Relocation								█	█
Roadway Construction								█	█
BRT Station Construction								█	█
Parking Facility Construction								█	█
Project Float									█


Kent / Des Moines to Federal Way LRT

Kent/Des Moines to Federal Way LRT

	Year 1	Year 2	Year 3	Year 4	Year 5	Year 6	Year 7	Year 8	Year 9	Year 10	Year 11	Year 12
Final Design Procurement	█											
Final Design		█	█	█								
Permitting / ROW			█	█	█							
Construction Procurement					█							
Construction						█	█	█	█	█	█	
Mobilization, Site Prep, Utility Relocation						█						
At-Grade Guideway Construction						█	█	█				
Aerial Guideway Construction						█	█					
Underground Guideway Construction						█	█					
Station Construction								█	█			
Trackwork									█			
Systems										█		
Startup / Testing											█	
Project Float												█

Federal Way to Tacoma Dome LRT

Federal Way to Tacoma Dome LRT

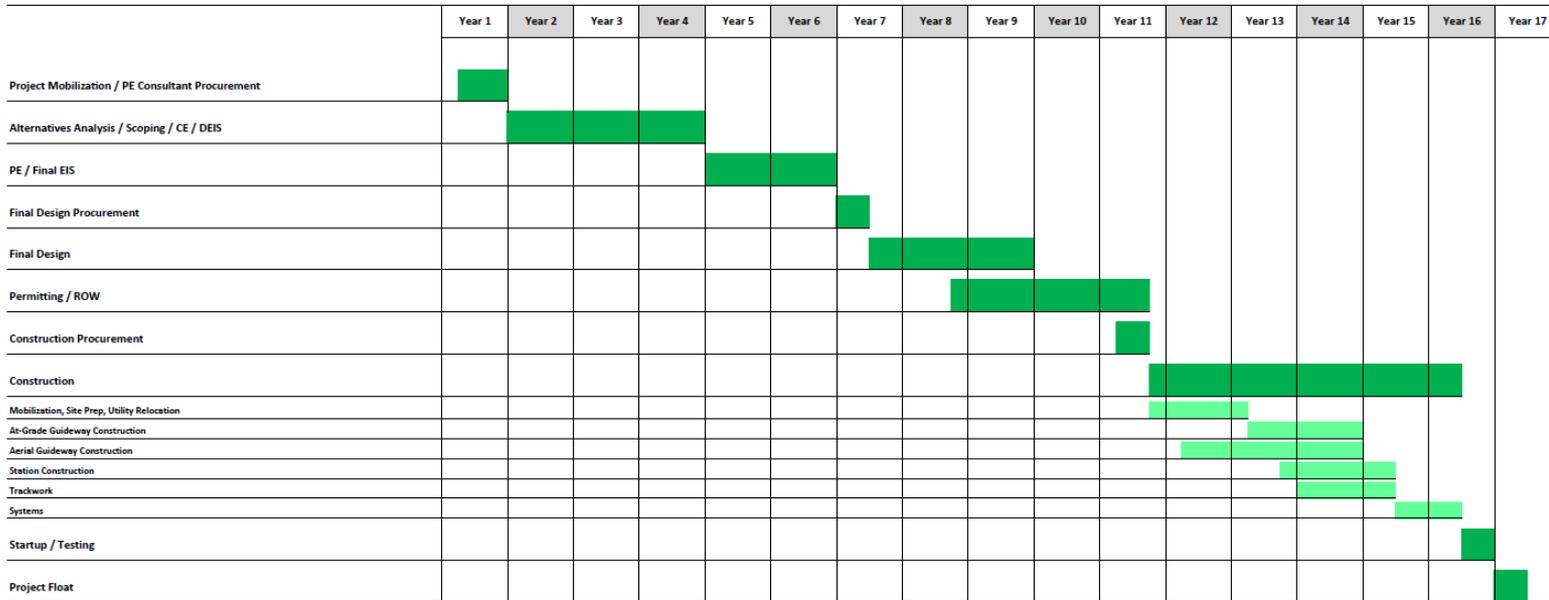

Tacoma Link Extension to Tacoma Community College

Tacoma Link Extension to Tacoma Community College

	Year 1	Year 2	Year 3	Year 4	Year 5	Year 6	Year 7	Year 8	Year 9	Year 10	Year 11	Year 12	Year 13	Year 14	Year 15	Year 16	
Project Mobilization / PE Consultant Procurement	█																
Alternatives Analysis / Scoping / CE / DEIS		█	█	█													
PE / Final EIS					█	█											
Final Design Procurement							█										
Final Design							█	█	█								
Permitting / ROW								█	█	█							
Construction Procurement											█						
Construction												█	█	█	█	█	
Mobilization, Site Prep, Utility Relocation, Street Reconstruction												█	█	█			
At-Grade Guideway Construction												█	█	█			
Aerial Guideway Construction												█	█	█			
Station Construction													█	█			
Maintenance Facility Construction													█	█			
Trackwork														█	█		
Systems															█		
Startup / Testing																█	
Project Float																	█

Lakewood to DuPont Sounder

Lakewood to DuPont Sounder

	Year 1	Year 2	Year 3	Year 4	Year 5	Year 6	Year 7	Year 8	Year 9	Year 10	Year 11
Project Mobilization / PE Consultant Procurement	█										
Alternatives Analysis / Scoping / CE / DEIS		█	█								
PE / Final EIS				█							
Final Design Procurement					█						
Final Design					█	█					
Permitting / ROW						█	█				
Construction Procurement							█				
Construction							█	█	█	█	
Mobilization, Site Prep, Demolition, Utility Relocation							█	█	█		
Trackway Construction							█	█	█	█	
Station Construction										█	
Parking Facility Construction										█	
Systems										█	█
Startup / Testing											█
Project Float											█



 **SOUND TRANSIT**
