



## Floating bridge assembly

Aug. 27, 2015

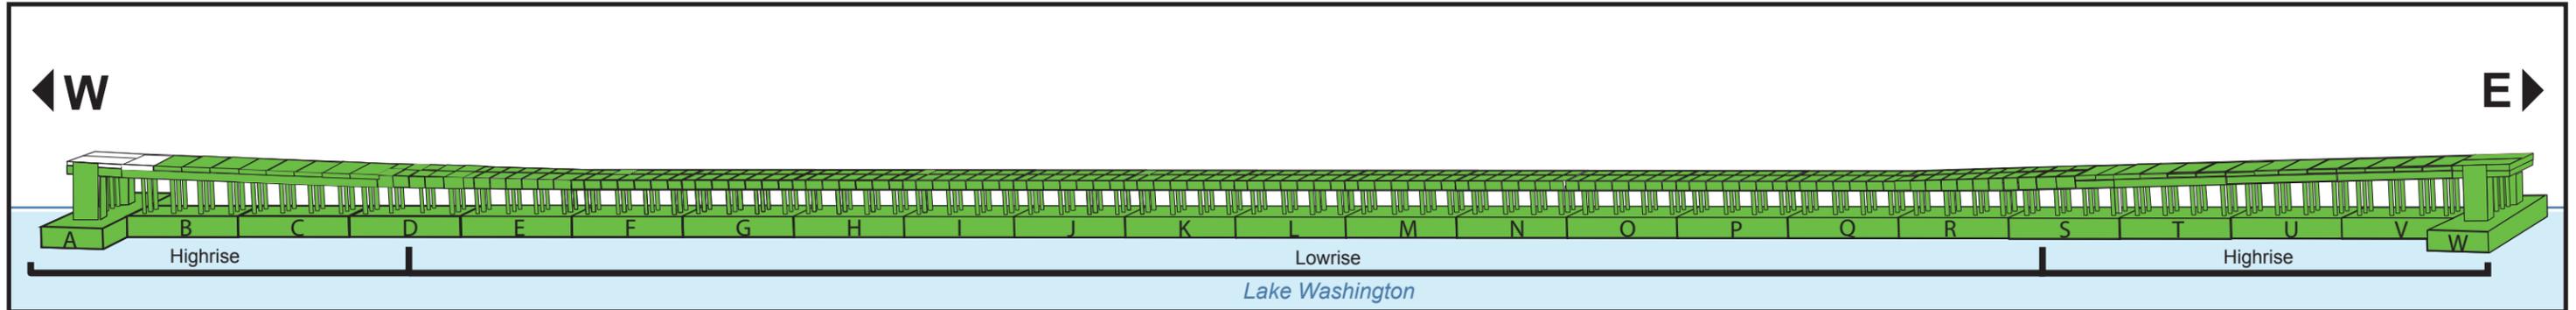

### GRAPHIC KEY AND FACTS

- 776 low-rise roadway deck sections
  - 27 high-rise roadway deck spans
  - 331 girders
  - 771 columns
  - 21 longitudinal pontoons + 2 cross pontoons
- 
- In Final Location
  - Construction Complete
  - Under Construction
  - Future Construction

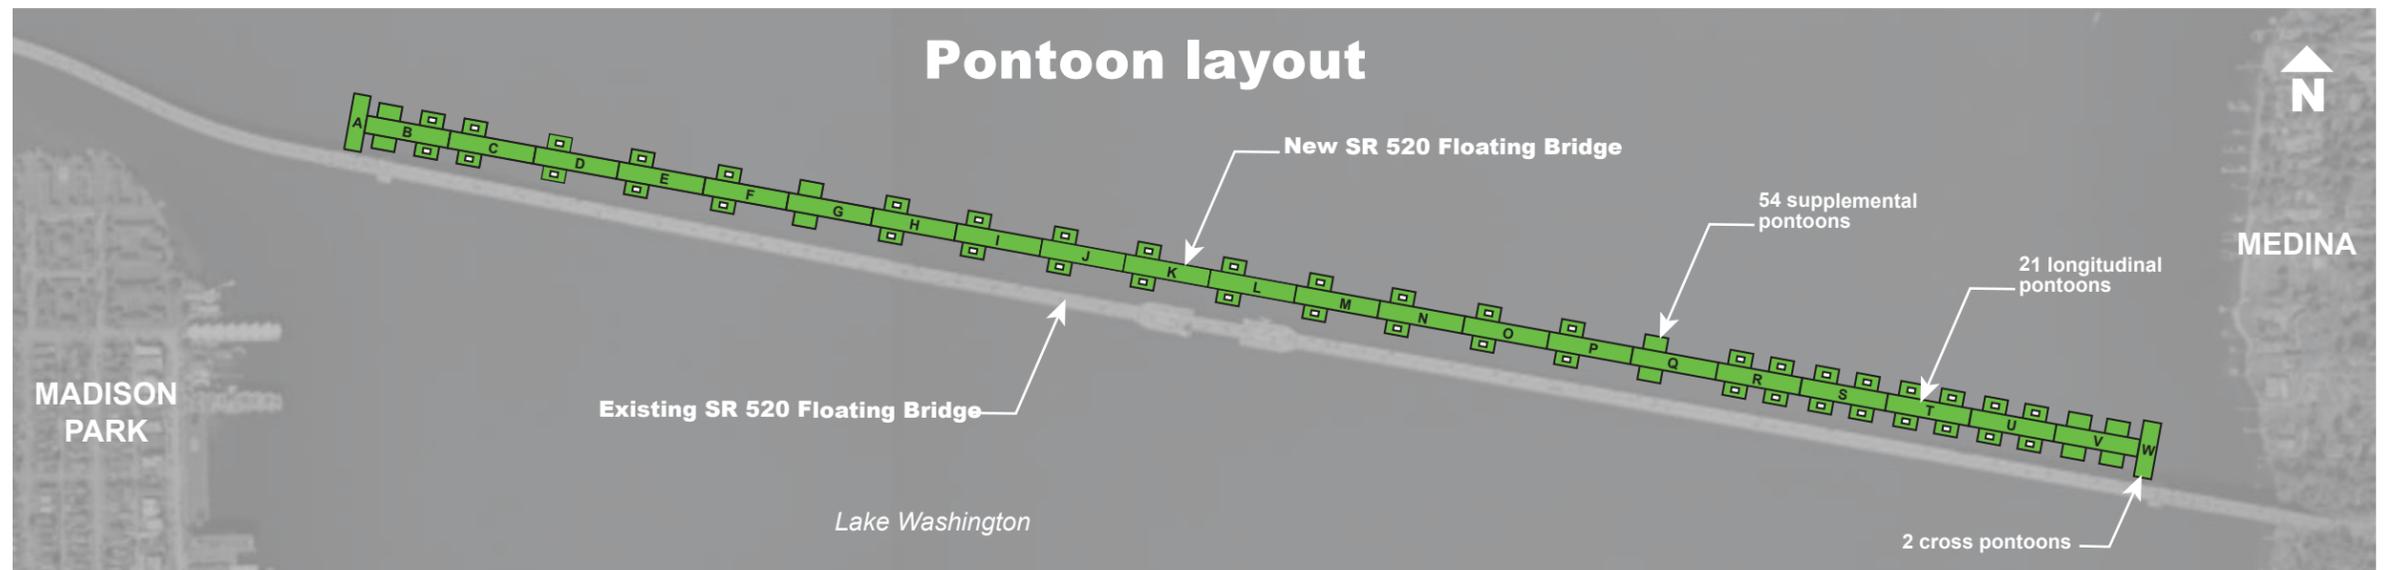

Low-rise roadway deck includes pre-cast deck panels being constructed in Kenmore.

- 776 out of 776 pre-cast deck panels have been constructed. 776 of 776 have been placed.

High-rise roadway deck includes girders and cast-in-place deck.

- 21 out of 23 cast-in-place deck spans have been constructed.
- 331 out of 331 girders have been constructed. 331 of 331 have been placed.

The number of columns shown is a representation of the total number of columns.

- 771 out of 771 columns have been installed.

- Current number of pontoons on Lake Washington: 77

- Total number of pontoons constructed to date: 77

- Pontoons currently under construction: 0

**Note:** not to scale, for illustrative purposes only
