



# Alaskan Way Viaduct Replacement Program

## SR 99 Tunnel - Project Delivery



The contract packages shown below represent the work that will be necessary to construct the SR 99 tunnel and remove the Alaskan Way Viaduct's central waterfront section. The following is preliminary schedule information that is subject to change.




**Viaduct Removal**  
**Contract type:** Design-bid-build  
**Construction duration (est.):** January 2016 - September 2016  
**Major scope items:**

- Relocate utilities attached to structure.
- Demolition.

**Battery Street Tunnel Decommissioning**  
**Contract type:** Design-bid-build  
**Construction duration (est.):** January 2016 - September 2016  
**Major scope items:**

- Remediation to remove soot and asbestos.
- Disconnect power, water and drainage lines.
- Relocate utilities that run through the tunnel.
- Fill tunnel with suitable material and seal portals.

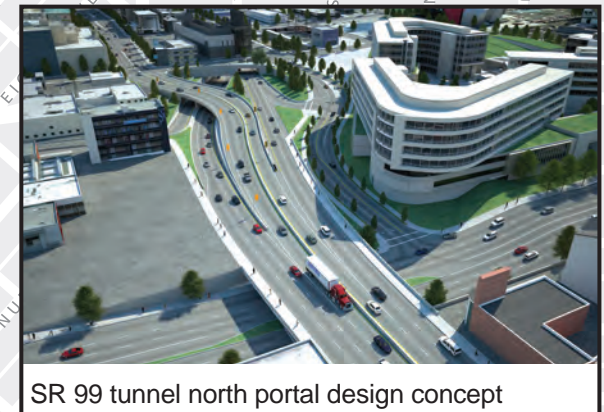

**South Access Project**  
**Contract type:** Design-bid-build  
**Contract advertisement date:** April 2014  
**Construction duration (est.):** June 2014 – January 2017  
**Major scope items:**

- Connecting the S. Holgate Street to S. King Street project with the tunnel.
- SR 99 on- and off-ramps connecting the tunnel's south portal to city streets.
- Remove SR 99 bypass.
- Surface streets between S. Atlantic Street and S. King Street.
- Landscaping, sidewalks, signage, stormwater control and roadway restoration.

**SR 99 Tunnel**  
**Contract type:** Design-build  
**Construction duration (est.):** August 2011 – December 2015  
**Contract amount:** \$1.35 billion  
**Major scope items:**

- Tunnel boring machine.
- Bored tunnel and interior stacked roadway with two lanes in each direction.
- Fire, life and safety systems.
- Tunnel operations buildings at the tunnel's north and south ends.
- Traffic management systems: Overhead signage and electronic tolling equipment.

**North Surface Street Connections**  
**Contract type:** Design-bid-build  
**Contract advertisement date:** October 2015  
**Construction duration (est.):** October 2015 – June 2017  
**Major scope items:**

- Re-building John, Thomas and Harrison streets between Dexter and Taylor avenues and re-building a small section of Denny Way and Wall Street.
- Improvements to Aurora Avenue N. between Denny Way and Harrison Street.
- Restoration work such as landscaping and sidewalks.

**North Access Project**  
**Contract type:** Design-bid-build  
**Contract advertisement date:** October 2013  
**Construction duration (est.):** January 2014 – February 2016  
**Major scope items:**

- Connection between the tunnel's north portal and Aurora Avenue N.
- SR 99 on- and off-ramps at Republican Street.
- Stormwater control, signage and roadway restoration.
- Extension of Sixth Avenue N. between Harrison and Mercer streets.
- Utility relocation.



# Alaskan Way Viaduct Replacement Program

## S. Holgate Street to S. King Street Viaduct Replacement - Project Delivery



These contract packages represent the work that will be necessary to replace the south end of the Alaskan Way Viaduct between S. Holgate Street and S. King Street.

The stages of work shown here include a temporary bypass between S. Royal Brougham Way and S. King Street that will connect the new SR 99 roadway to the existing viaduct along the waterfront. A connection between the new roadway and the SR 99 tunnel will be built as part of the tunnel's south access project.

The following schedule information is subject to change.



**Stage 1 (Utility relocation)**

**Contract type:** Design-bid-build  
**Construction duration:** July 2009 – May 2010  
**Cost:** \$13.5 million

**Major scope items:**

- Rebuild and relocate utilities.
- Prepare the area for road and bridge construction.

**Stage 2 (SR 99 road and bridge construction)**

**Contract type:** Design-bid-build  
**Construction duration:** July 2010 – mid 2013  
**Contract amount:** \$114.6 million

**Major scope items:**

- Replace SR 99 between S. Holgate and S. King streets.
- Relocate railroad track.
- Surface street improvements.
- Build new bicycle/pedestrian facilities.

**Stage 3 (S. Atlantic Street overcrossing)**

**Contract type:** Design-bid-build  
**Contract advertisement date:** April 2012  
**Construction duration:** July 2012 – early 2014

**Major scope items:**

- Build overcrossing of railroad track at S. Atlantic Street.
- Finish building the shared bicycle/pedestrian path on east side of Alaskan Way S.
- Alaskan Way S./East Marginal Way S. connection.
