

# MONTHLY PROJECT OVERVIEW

## I-405, South Bellevue Widening Project

September 2009


**Project Location:** I-405, 112th Ave SE to SE 8th St  
**Design-Builder:** Atkinson

**PIN:** 840541F, 840509A, 840541G  
**WIN:** U40541F

### Design / Build Contract Summary

Contract Award: February 16, 2007  
 Notice to Proceed: March 15, 2007  
 Original Contract Time: 934 Calendar Days  
 Original Substantial Completion: October 2009  
 Original Contract Amount: \$124,000,000  
 Revised Contract Amount: \$124,390,198  
 Project Status as of: September 30, 2009  
 Contract Days Elapsed: 930 of 934 = 99.6%  
 Contract Amount Earned to Date: \$123,547,167 = 99.6%  
 Contract Amount Earned This Period: \$2,114,845 = 1.7%  
 Current Projected Completion Date: Feb. 2010 (on schedule)  
 Achieved Substantial Completion: September 22, 2009

### Project Cash Flow

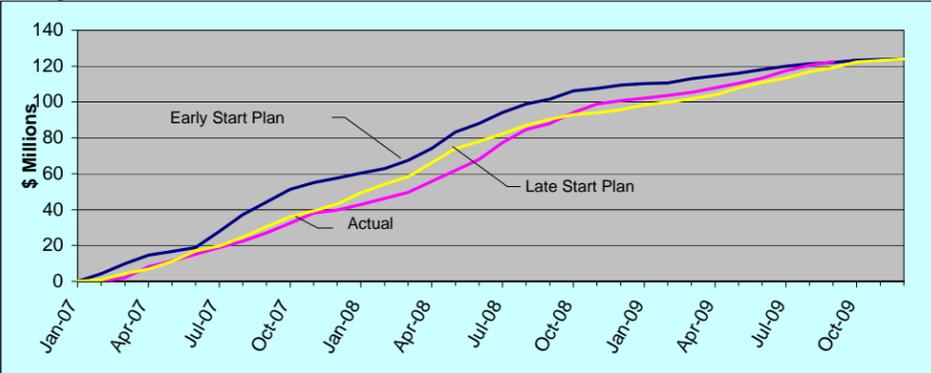


### Design-Build Schedule Summary


**Design:** Original design is complete. Design team will continue to support construction to the end of the project. Design documentation package is being assembled.

**Construction:** Completing all PCCP and asphalt paving. Opening up a new southbound lane north of I-90. Completing the planter walls at SE 8th Street. Installing final signing and removing old and temporary ITS equipment throughout project limits. Final clean up and installing amendments at ponds. Completing wall 2005. Constructing the ecology embankment monitoring facility. Installing joints on Coal Creek Parkway and BNSF bridges. Beginning construction at noise wall 2000. The contractor achieved substantial completion on September 22, 2009.

### Summary Project Schedule

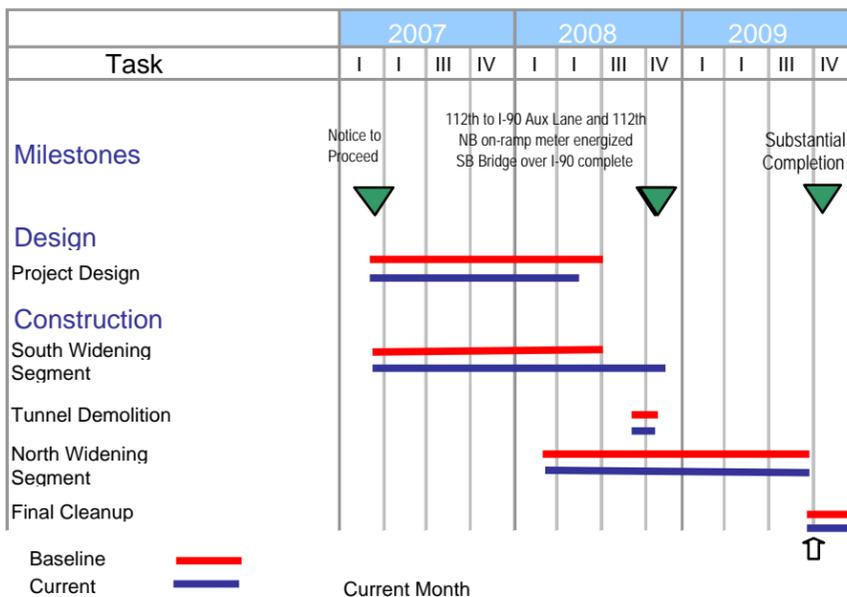

### Project Progress to Date



### September 2009 Highlights



### Quality Control / Quality Assurance

With the project achieving substantial completion, Atkinson's QA staff is busy performing final inspection of all work items. QA has generated a final punch list of work needing to be completed prior to project physical completion. Quality acceptance staff is also in the process of assembling project records for the final documentation of this project.

WSDOT QV is calculating bonus payments to the Design Builder for furnishing superior quality hot mix asphalt and concrete used in the construction this project.

### Risks / Challenges / Issues

Minimizing traffic control and coordinating with other regional work remains a challenge.

### Public Information & Community Outreach

Informed the public of I-405 lane closures. Hosted a media event on September 22 to open a new lane on southbound I-405. Answered comments from citizens and updated the public of the projects' progress using construction updates on WSDOT web sites and e-mail updates.

### Upcoming Activities - Fall 2009

Placing MMA striping, installing plants, completing noise wall 2000, and completing the punch list items.

For more information, Call 425.401.4143 or 425.456.8624 or visit [www.wsdot.wa.gov/Projects/i405/112thAveToSE8th/](http://www.wsdot.wa.gov/Projects/i405/112thAveToSE8th/)

**IT'S YOUR NICKEL. WATCH IT WORK.**

"Washington's Future Just Got Better"  
**MAKING EVERY DOLLAR COUNT.**

**Washington State Department of Transportation**
