

MONTHLY PROJECT OVERVIEW

I-405, South Bellevue Widening Project

November 2008


Project Location: I-405, 112th Ave SE to SE 8th St
Design-Builder: Atkinson

PIN: 840541F, 840509A, 840541G
WIN: U40541F

Design / Build Contract Summary


Contract Award: February 16, 2007
 Notice to Proceed: March 15, 2007
 Original Contract Time: 934 Calendar Days
 Original Substantial Completion: October 2009
 Original Contract Amount: \$124,000,000
 Revised Contract Amount: \$124,000,000

Project Progress to Date



Project Status as of: November 30, 2008
 Contract Days Elapsed: 626 of 934 = 67.0%
 Contract Amount Earned to Date: \$98,911,120 = 80%
 Contract Amount Earned This Period: \$4,792,929 = 3.8%
 Current Projected Completion Date: Oct. 2009 (on schedule)

Project Cash Flow

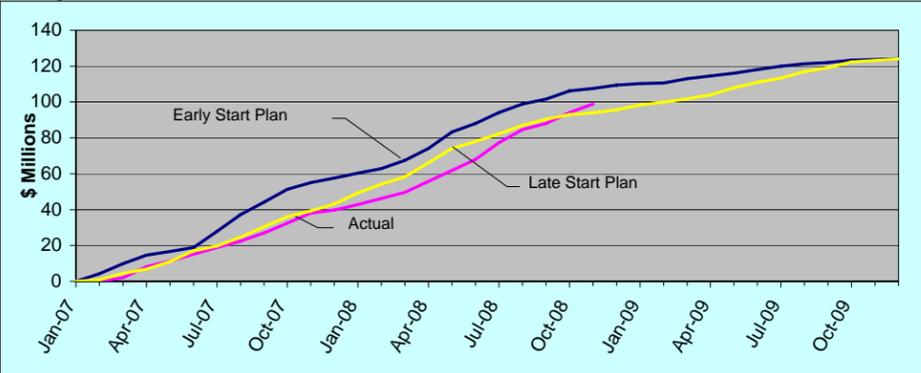

November 2008 Highlights



New Guardrail Set on Southbound I-405 Mainline.



I-90 Bridge Barrier Work in Progress.



Crane Used on SE 8th St Ramp for Setting Wall Panels.



112th to Coal Creek Parkway Coping.

Design-Build Schedule Summary

Design: Design is functionally complete. Design team will continue to support construction to the end of the project.


Construction: Between 112th and Coal Creek Parkway northbound: Retaining walls have been complete, metal beam guardrail set and some temporary barrier has been removed. Median paving is in progress between Coal Creek Parkway and I-90. Completed north and south approaches to the new bridge over I-90, started stripping the formwork from the bridge. Preparing subgrade north of the Wilburton Tunnel location. Installed illumination and traffic monitoring systems between SE 8th and I-90 southbound. Checked, reinforced and re-applied erosion control measures to stabilize exposed soil for the wetter season.

Quality Control / Quality Assurance

QA continues inspection and materials testing for the project. The Design Builder is currently completing work on northbound I-405 from 112th Street to Coal Creek Parkway. QA is generating punch lists and reviewing materials documentation to ensure all work meets contract specifications prior to opening this section of the project to the public.

Materials test data is being entered into SAMs, the Statistical Analysis of Materials. Analyses of the test results indicate that materials incorporated into the project are meeting contract specifications.

Summary Project Schedule

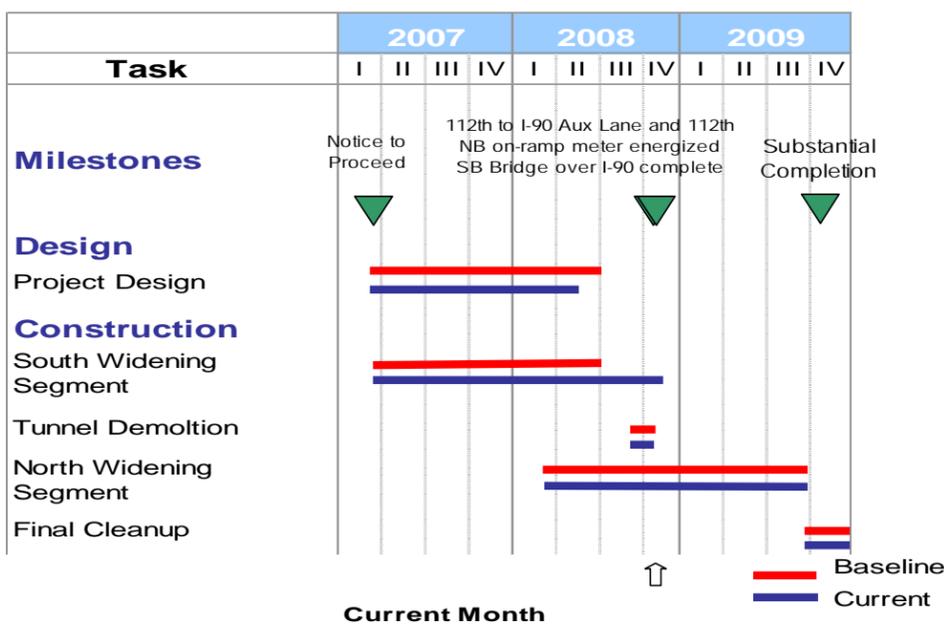

Risks / Challenges / Issues

Fall weather and shorter days are creating challenges for work progress and erosion control. Minimizing the construction traffic control impacts to the public remains a challenge.

Public Information & Community Outreach

Informed public of lane and ramp closures using daily construction updates on WSDOT web sites and weekly press releases. Added new project milestone map to web site that features current and future project milestones.

Upcoming Activities - Winter 2008

Opening northbound lanes from 112th to I-90, turning on ramp meter at 112th northbound onramp, opening the new southbound I-405 bridge at I-90, opening up lanes on Coal Creek Parkway.

For more information, Call 425.401.4143 or 425.456.8624 or visit www.wsdot.wa.gov/Projects/i405/112thAvetoSE8th/

IT'S YOUR NICKEL. WATCH IT WORK.

"Washington's Future Just Got Better"
MAKING EVERY DOLLAR COUNT.

