

Truck climbing passing lanes - I-90/Cle Elum to Vantage



Quarterly Project Report Update For Quarter Ending June 2003

Project Title & Location

I-90/Ryegrass Summit to Vantage – West of Vantage

Contractor

Superior Paving Co.

Project Description

Constructs new truck climbing/passing lane westbound on I-90 from Ryegrass Summit to Vantage. This work will consist of adding a 12 ft Asphalt Cement Pavement lane and other work associated with paving.

Recent Progress

This contract was awarded to Superior Paving Co. August 5, 2003.

Design / Construction Impacts

No impacts to the project's scope, schedule or budget are known or anticipated at this time.

Environmental Impacts / Compliance

All environmental permits for construction have been received and anticipated environmental impacts are mitigated as part of the contract.

Impacts to Traffic

Lane closures are possible Monday through Sunday except on holidays or holiday weekends.

Project Milestones	Scheduled	Attained	Milestone Outlook
Contract Advertised	Jul 03	Jun 03	Completed 1 month in advance of schedule.
Contract Awarded	Aug 03	Aug 03	Completed on time.
Groundbreaking			No issues at this time.
Open to Traffic	Summer 05		No issues at this time.

Project Cost Summary:

Preliminary Engineering

Dollars in millions

\$0.9 m

Percent of total

9.8 %

Right-Of-Way

\$0.0 m

0.1 %

Construction

\$8.4 m

90.0 %

Total Project Cost

\$9.3 m

100 %


Nickel funds included in above costs

\$8.4 m

90.0 %

The current expectation is that the project cost at completion will be within the total project cost noted above.

Actual vs. Planned Expenditures (Total Project Cost)

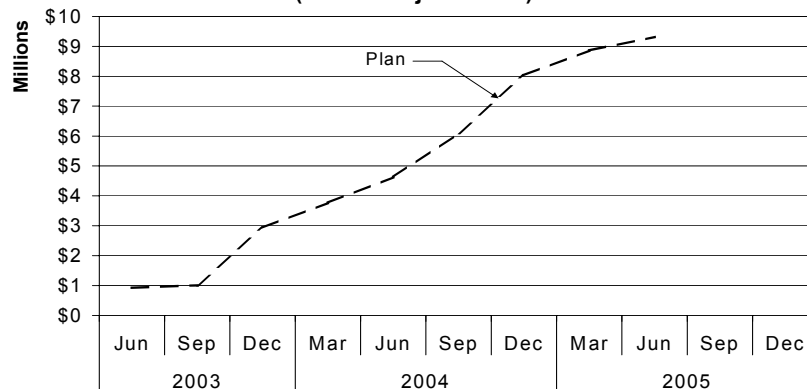

For more information, go to <http://www.wsdot.wa.gov/projects/>

Jim Dwyer, WSDOT Project Engineer @ (509) 577-1844
or E-mail: DwyerJ@wsdot.wa.gov
