


## Pontoon ballasting and inspections on Lake Washington

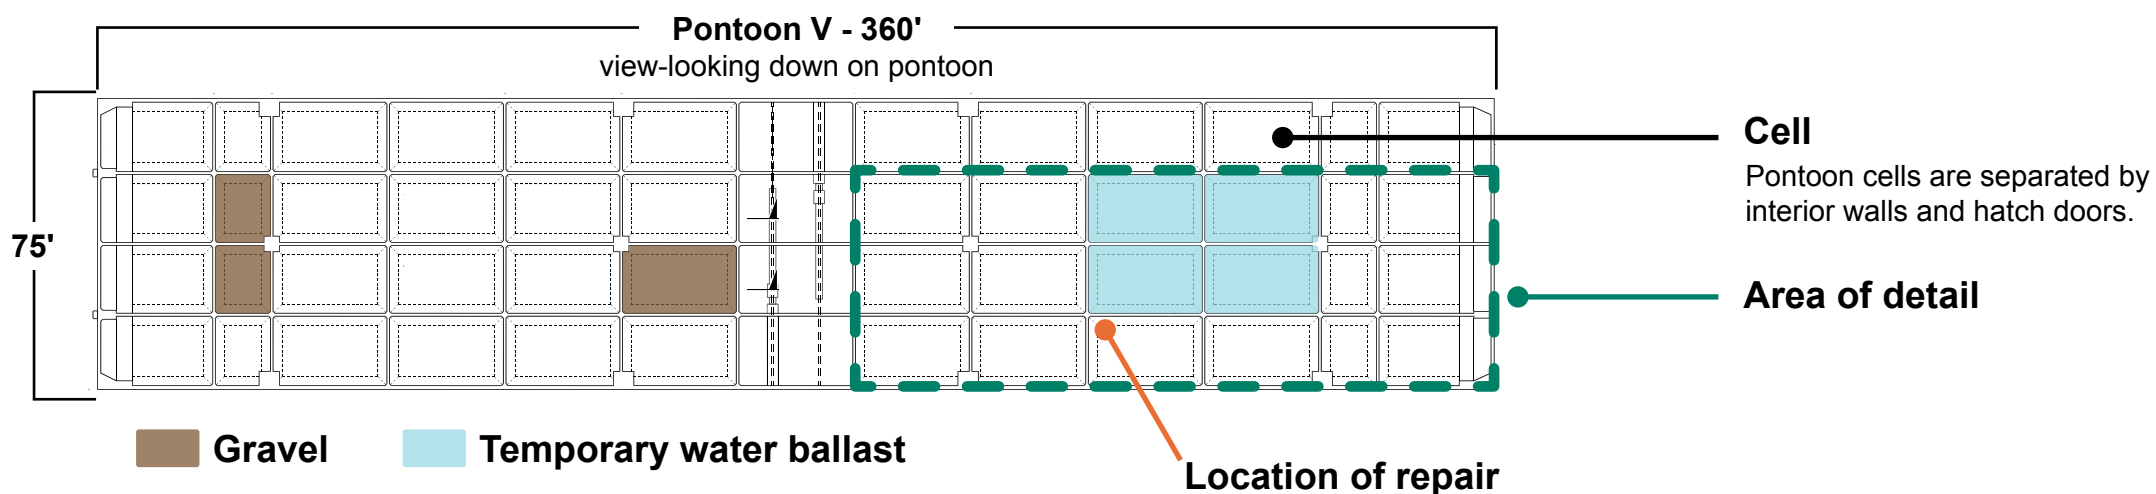


**NOTE:** pontoons are ballasted to bring them to the correct level to join to other pontoons.


Water is used as temporary ballast and will be removed prior to project completion.

Gravel will be used for permanent ballast.


**1** Water was added to internal cells as temporary ballast.

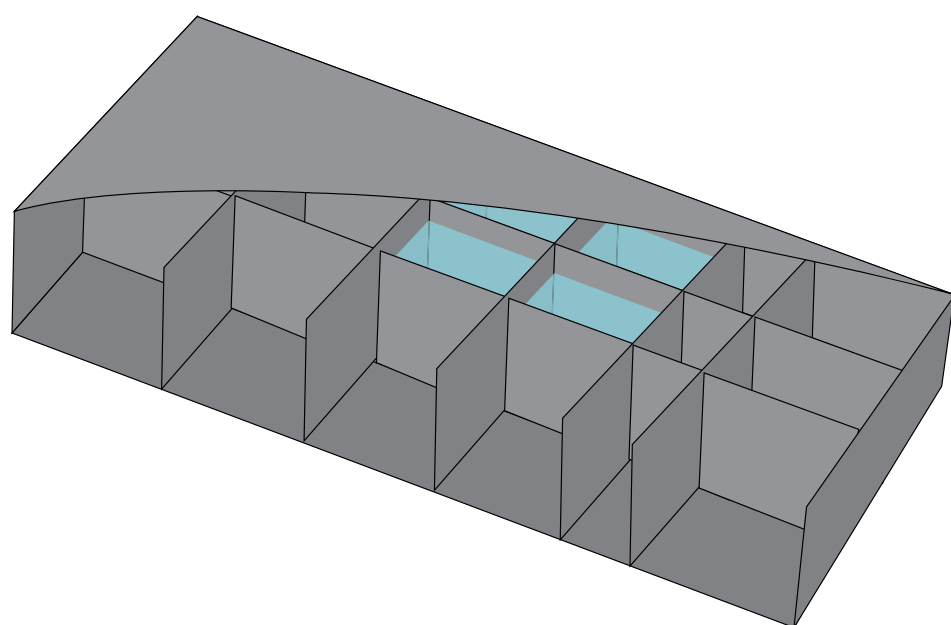

**2** A small leak occurred between two cells in pontoon V on Aug. 22.

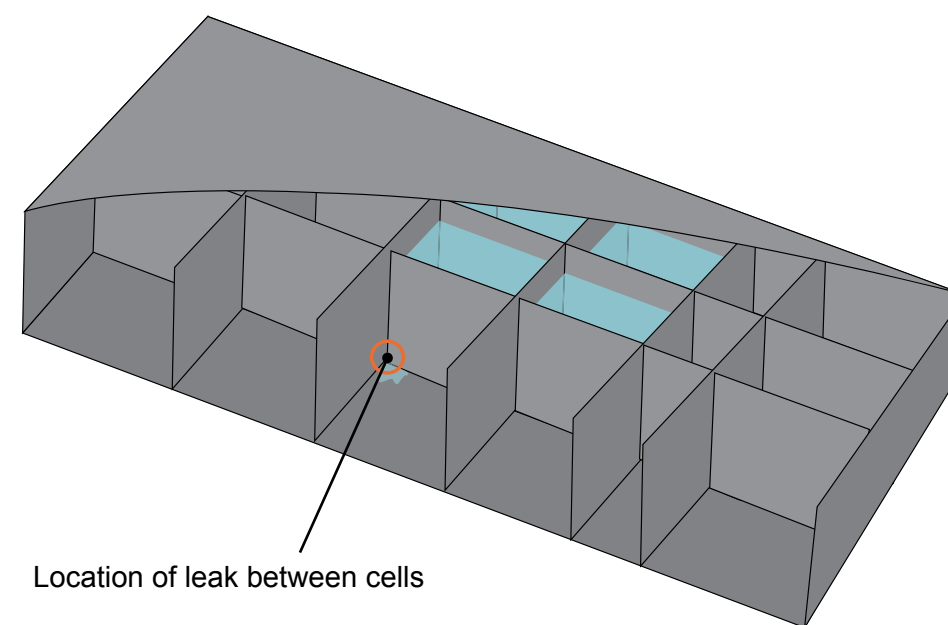

**3** The leak in pontoon V was repaired and excess water was removed on Aug. 24.

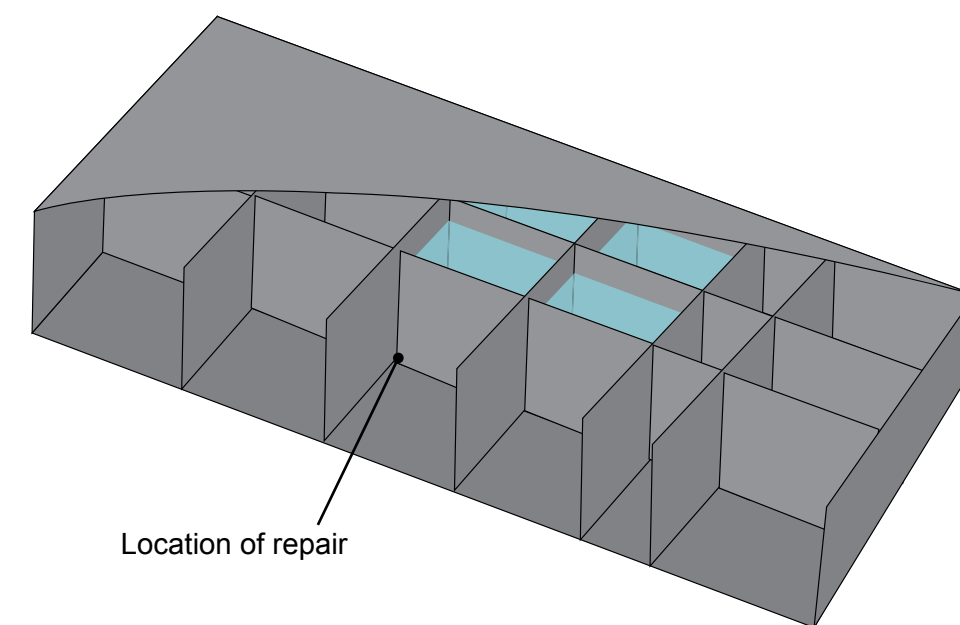

*For illustration purposes only - not to scale*
