


West Approach Bridge North - Conceptual Construction Staging

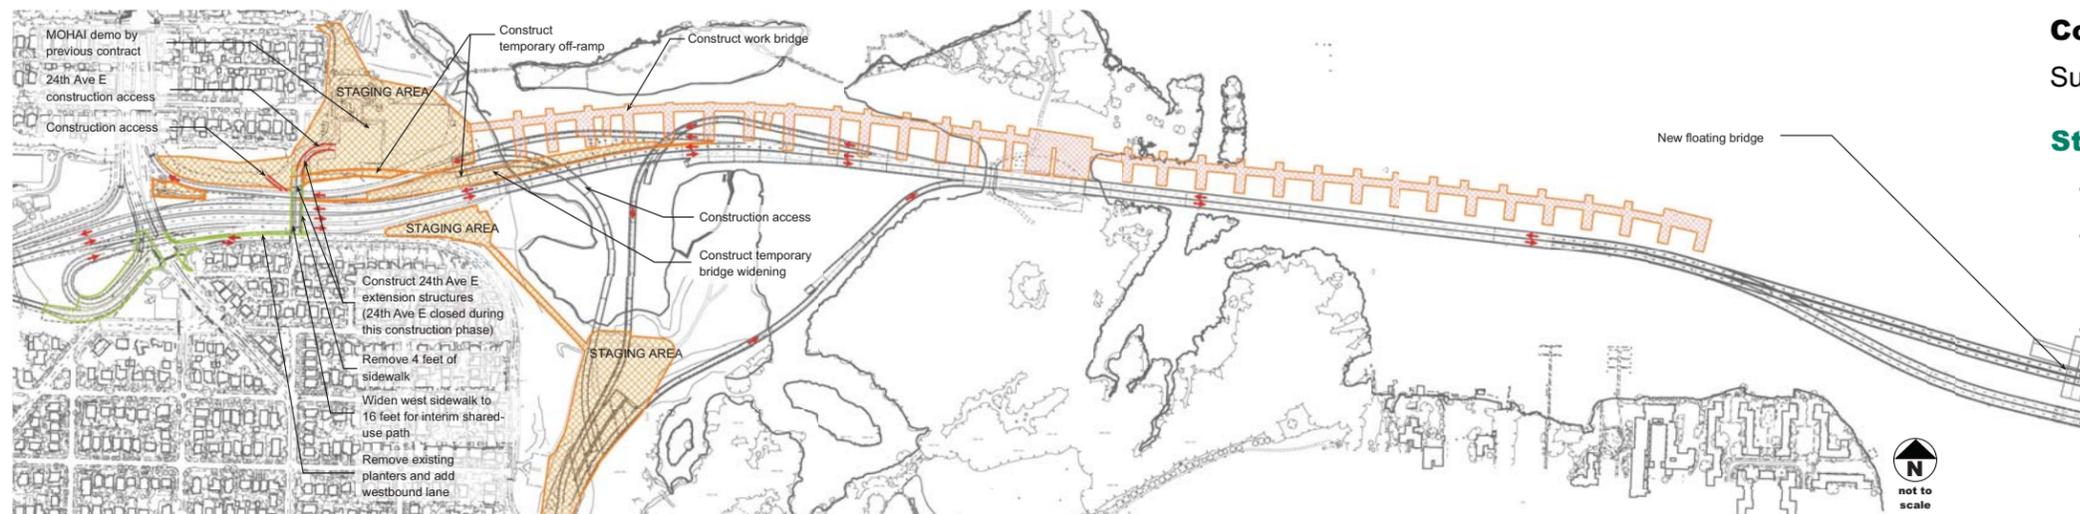

Construction Period:

Summer 2014 to Winter 2016


Stage 1 - Approximately 4-6 months duration

- Make local street improvements
- Construct temporary ramp to Montlake Boulevard East and 24th Avenue East
- Extend 24th Avenue East
- Construct work bridge
- Conduct limited lane closures



Stage 2 - Approximately 20-24 months duration

- Construct stormwater facility at old MOHAI site
- Switch traffic to temporary ramp to Montlake and 24th Avenue East
- Remove RH Thompson Expressway ramps and westbound Lake Washington off-ramp
- Continue work bridge construction
- Construct West Approach Bridge North
- Conduct limited weekend and night closures

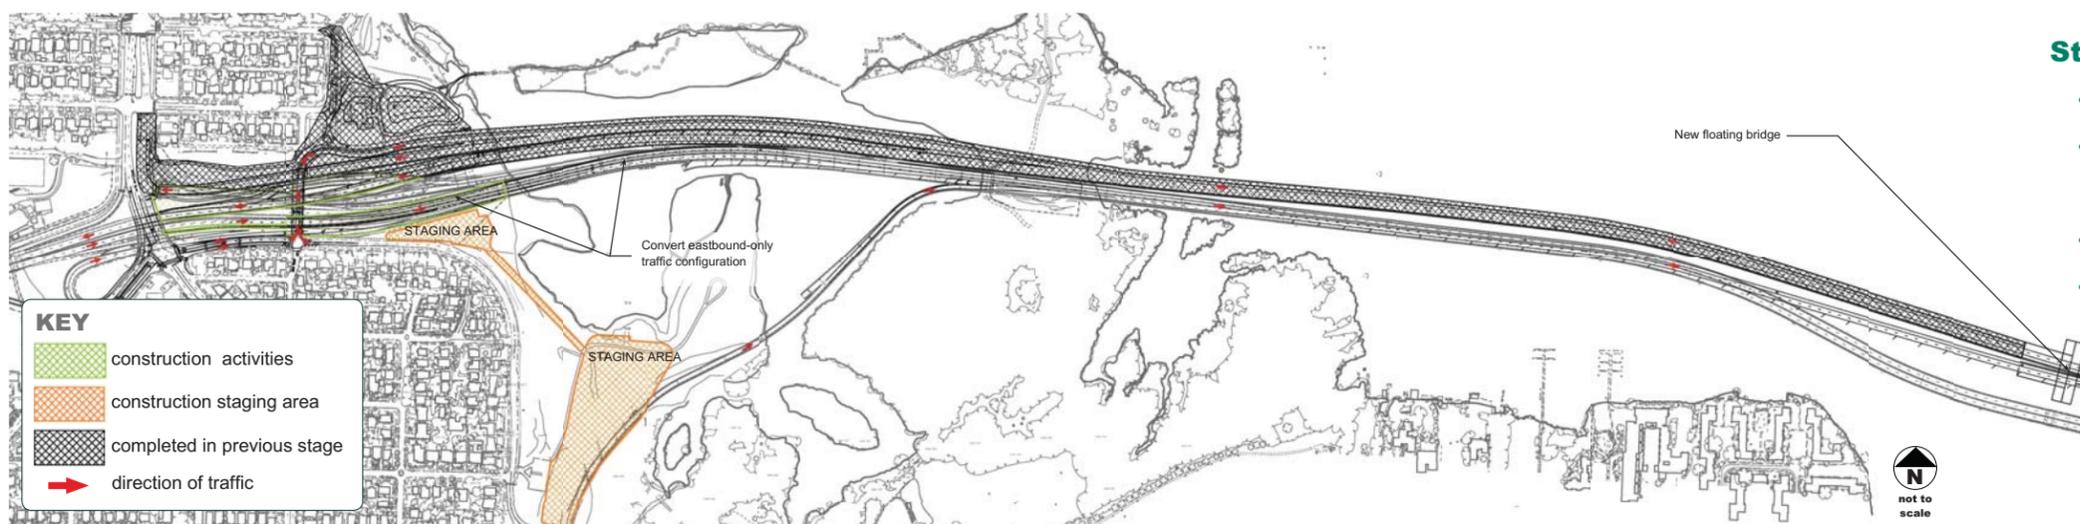

Stage 3 - Approximately 2-3 months duration

- Remove work bridge
- Conduct paving and grading work at the west end
- Reconfigure traffic to 6-lane
- Conduct limited weekend and night closures

CONCEPTUAL
DRAFT - THIS SKETCH ONLY DEPICTS THE IDEA. ENGINEERING, OPERATIONS AND ENVIRONMENTAL ANALYSIS REQUIRED.
