Floating bridge assembly

October 2015

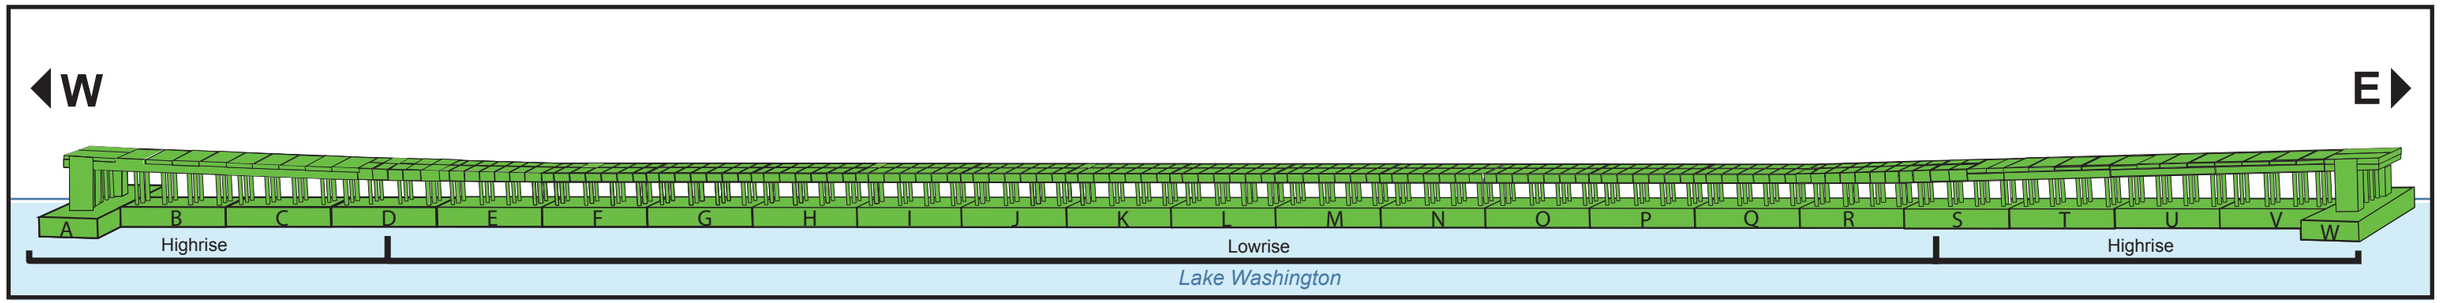

GRAPHIC KEY AND FACTS

- 776 low-rise roadway deck sections
- 27 high-rise roadway deck spans
- 331 girders
- 771 columns
- 21 longitudinal pontoons + 2 cross pontoons

- In Final Location
- Construction Complete
- Under Construction
- Future Construction

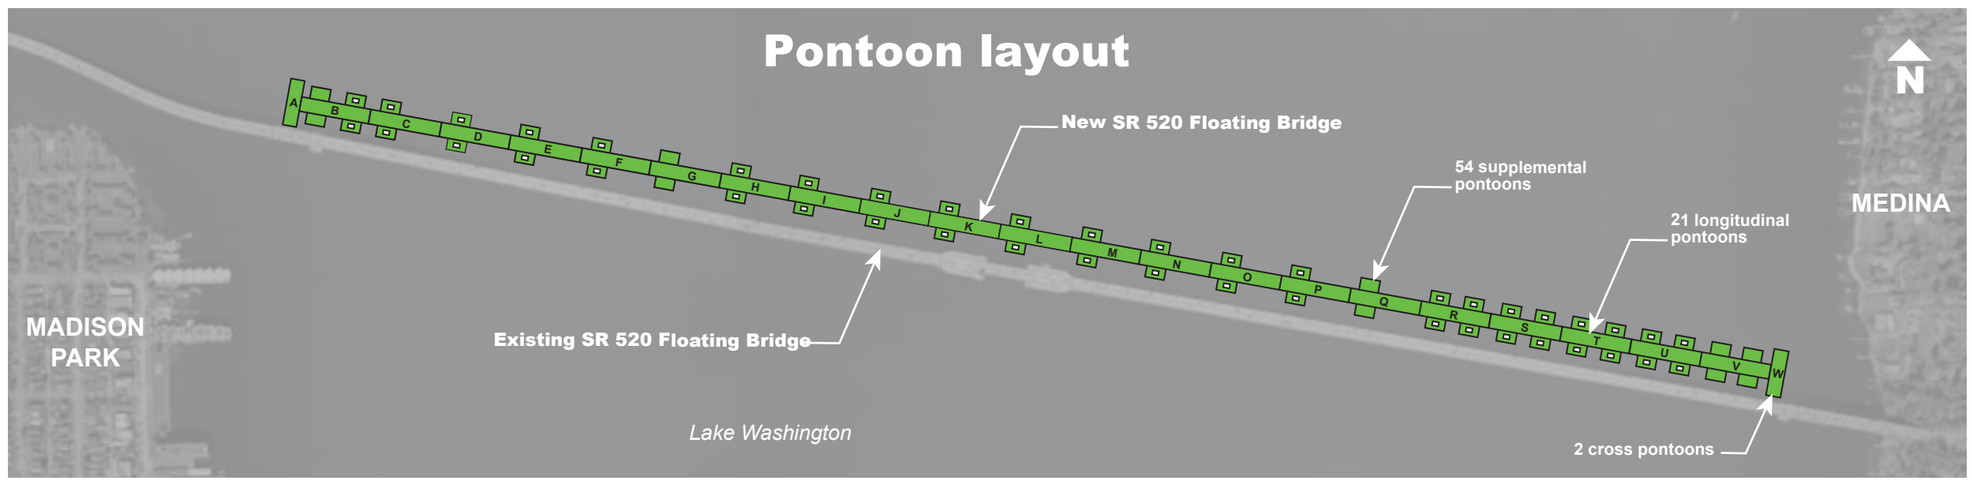

Low-rise roadway deck includes pre-cast deck panels being constructed in Kenmore.

- 776 out of 776 pre-cast deck panels have been constructed. 774 of 776 have been placed.

High-rise roadway deck includes girders and cast-in-place deck.

- 27 out of 27 cast-in-place deck spans have been constructed.
- 331 out of 331 girders have been constructed. 331 of 331 have been placed.

The number of columns shown is a representation of the total number of columns.

- 771 out of 771 columns have been installed.

- Current number of pontoons on Lake Washington: 77
- Total number of pontoons constructed to date: 77
- Pontoons currently under construction: 0

Note: not to scale, for illustrative purposes only
