Alaskan Way Viaduct
REPLACEMENT
PROGRAM

SR 99 Tunnel Project – Interior Structures Weekly Report *Dec. 23, 2016 (covers Dec. 16 to Dec. 23)*

The information in this report is based on Seattle Tunnel Partners' three-week schedule, and does not necessarily reflect progress as it relates to the overall project schedule.
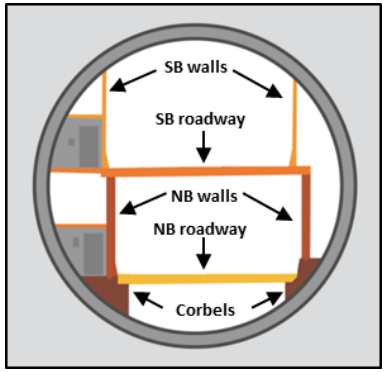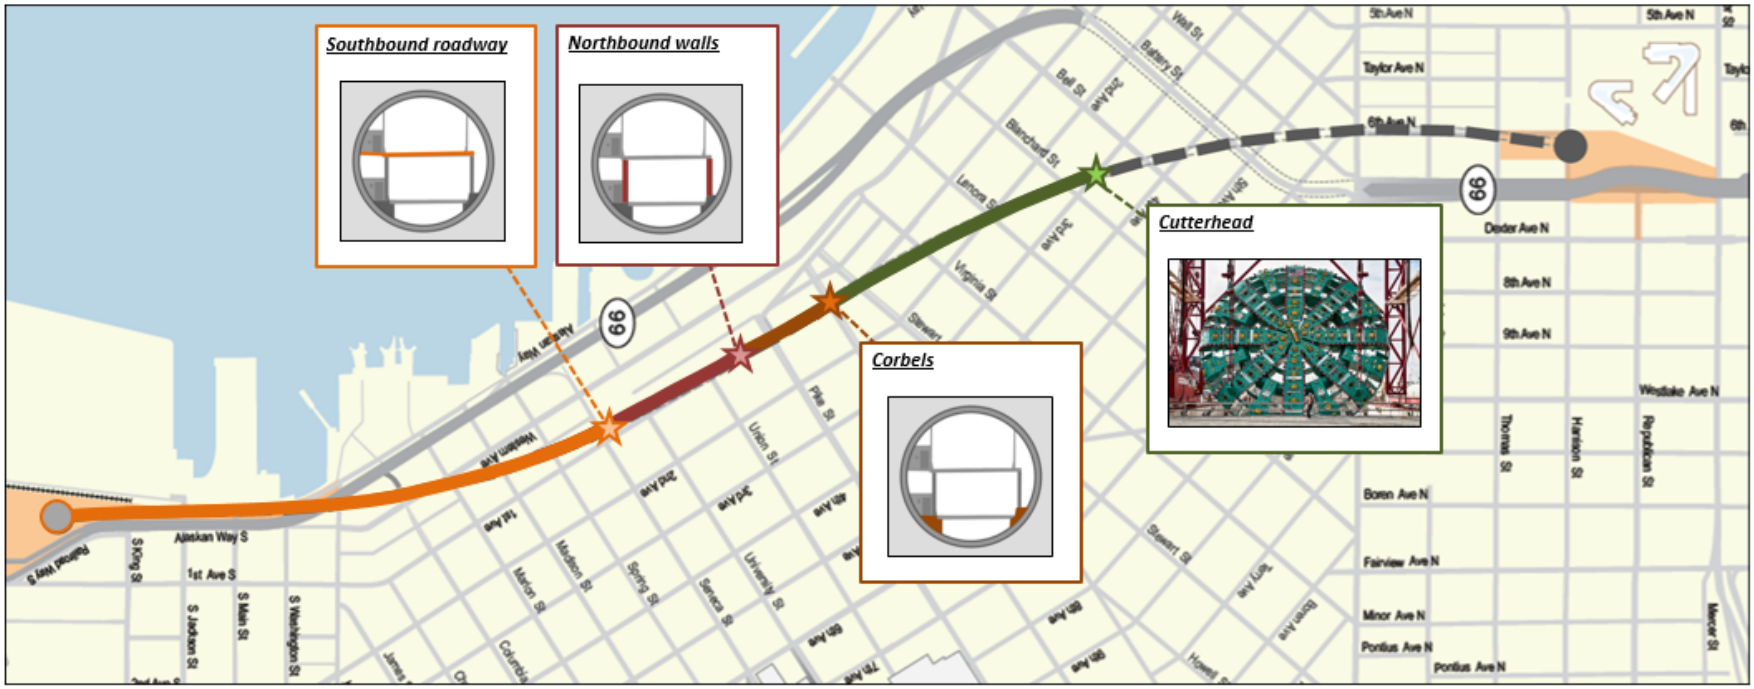
	Sections completed/planned	Distance completed (of 9,270 total feet)	Percent completed	Notes
Southbound roadway	2/2	3,202 feet	35 percent	
Northbound walls	3/3	4,224 feet	46 percent	
Corbels	3/3	4,887 feet	53 percent	
Northbound roadway	N/A	N/A	N/A	
Southbound walls	N/A	N/A	N/A
