Peak Hour Report

YEAR 2009

Washington State Department of Transportation

In cooperation with the
United States Department of Transportation
Federal Highway Administration

WASHINGTON STATE
DEPARTMENT OF TRANSPORTATION

PEAK HOUR REPORT

STRATEGIC PLANNING & PROGRAMMING

TRANSPORTATION DATA OFFICE

HIGHWAY USAGE BRANCH

CONTACT: MS:47380 PHONE: (360) 570-2392

2009

JANUARY 1 through DECEMBER 31

TABLE OF CONTENTS

Introduction……..……SECTION…..….....I

Executive Summary…….……SECTION……....…II

Site Numbers and Locations…….……..SECTION……...…..III

ADC Site Map……..SECTION……..…IV

Design Hour Factors ……...SECTION……..…...V

Factor Support Sheet…….……..SECTION…...….…VI

Peak Hour Data Summary. …….SECTION……VII

Site Data……..……..……SECTION…..……..VIII

Glossary……..……..……SECTION.……...….IX

INTRODUCTION

The Peak Hour Report is a list of Design Hour Factors (K and D) calculated from and including the highest 200 hours of hourly traffic volume collected from Automated Data Collection (ADC) sites being monitored during the previous complete year.

This years report is comparable to years past. It shows the Annual Average Daily Traffic (AADT) volumes in normal growth trends. It also shows where volumes of traffic are causing congestion within rural and urban areas around the state.

Typically each site is represented by two graphs within the site data section of this report.
The first of the two graphs--K FOR PEAK 200 HOURS of 2008--represents the top two hundred hours in descending order. (As volumes increase, the "K" value decreases.)
The second of the two graphs--D % IN THE PEAK 200 HOURS of 2008--represents the highest directional difference order.

If there is not a graph showing the "D-factor" percentage, no data was available for the opposing direction of travel at that particular site.

K Factors = A peak hour traffic volume divided by the Annual Average Daily Traffic (AADT) for each ADC location, without regard to direction, i.e.

K Factor = Highest Peak Hour-- traffic volume hour divided by the AADT.
K30 Factor = 30th Peak Hour-- traffic volume hour divided by the AADT.

D Factor = Highest directional volume percentage for the 30th peak hour.
D Factors for all other peak hours are available by request.

COMMON USES:

Peak Hour Report is used for determining traffic patterns
Peak Hour Report is used for determining projected and estimated traffic volumes
Peak Hour Report is used for project design purposes by planning and engineering offices. (State, County, City and private)

EXECUTIVE SUMMARY

The Washington State Department of Transportation is responsible for over seven thousand miles of state highways. This responsibility creates large expenditures for designing, planning, constructing and maintaining. It requires reliable data collection and reporting of vehicle volumes, classification types, speeds, travel trends and highest volume-hours throughout the state.

The Peak Hour Report is a compilation of multi-directional data containing the top volume-hours for the year at the Automated Data Collection sites around the State of Washington. The report summarizes the top two hundred **volume-hours** for the year by site and by direction on any given state highway.

The Peak Hour report is used as a tool for estimating future **design hour volume** of traffic. This information is used by traffic, design, planning and other engineers designing highway features.

Typically the K-30, K-50, K-100 and K-200, (30th, 50th, $100^{th,}$ 200th peak hour factors) are reported to engineering for highway design.

Also, included within this report is the D factor, which represents the proportion of peak hour traffic traveling in the peak direction (Please see Glossary for explanation of the different types of K-factors).

Questions or Comments regarding the Peak Hour Report; please contact the Automated Data Collection Section by Emailing ---- tdoadc@wsdot.wa.gov ---- or call 360-570-2392.

WASHINGTON STATE DEPARTMENT OF TRANSPORTATION

STRATEGIC PLANNING & PROGRAMMING

HIGHWAY USAGE BRANCH

PEAK HOUR REPORT

2009

SITE #	LEG #	STATUS OF DATA	RURAL/URBAN	EASTERN / WESTERN WASHINGTON	REGION	REC SITE	SITE LOCATION
B02	0		RURAL	WESTERN	OR		SR 012 W/O MONTE BRADY LOOP RD WYE CONN - BRADY - MP 12.30
B03	0		RURAL	EASTERN	SC		SR 395 S/O VINEYARD DR - PASCO - MP 27.20
B04	0		RURAL	EASTERN	SC	YES	SR 090 W/O CLE ELUM OFF RAMP - CLE ELLUM - MP 82.70
D1	0	No Data	URBAN	WESTERN	NW		SR 405 AT 112TH AVE SE UXING - BELLEVUE - MP 9.26
D10	0		URBAN	WESTERN	NW		SR 520 W/O 76TH AVE NE UXING - TOLL PLAZA - MP 4.00
D12	0		URBAN	WESTERN	NW		SR 018 AT 180TH AVE SE UXING - COVINGTON - MP 12.55
D13	0		URBAN	WESTERN	NW		SR 518 E/O SR 509 I/C - SEATAC - MP 0.35
D14	0		URBAN	WESTERN	NW		SR 509 N/O SR 518 I/C - BURIEN - MP 26.37
D3	0		URBAN	WESTERN	OR		SR 512 W/O SR 007 I/C - PARKLAND - MP 1.53
P01	0		RURAL	EASTERN	NC		SR 002 W/O RED APPLE RD - CASHMERE - MP 113.10
P02	0		RURAL	EASTERN	NC	YES	SR 002 E/O J SE - COULEE CITY - MP 179.10
P03	0		RURAL	EASTERN	SC		SR 097 S/O PROGRESSIVE ROAD WYE CONN - WAPATO - MP 66.30
P04	0		RURAL	WESTERN	NW		SR 005 N/O SLATER ROAD I/C - FERNDALE - MP 261.33
P05	0		RURAL	EASTERN	SC		SR 012 W/O TUCANNON RIVER BRIDGE - DAYTON - MP 376.98
P06	0		URBAN	WESTERN	SW		SR 014 E/O ALPINE RD - CAMAS - MP 11.90
P07	0		URBAN	WESTERN	SW		SR 014 E/O 32ND ST - WASHOUGAL - MP 17.70
P08	0		RURAL	EASTERN	SC		SR 082 W/O SR 22 - BUENA - MP 48.50
P09	0		RURAL	EASTERN	SC		SR 082 W/O COFFIN RD - PLYMOUTH - MP 121.20
P1	0		URBAN	WESTERN	NW		SR 005 N/O 164TH STREET SW - EVERETT - MP 184.48
P10	0		RURAL	EASTERN	ER	YES	SR 090 W/O SR 395 I/C - RITZVILLE - MP 218.83
P11	0		RURAL	EASTERN	NC		SR 097 N/O COUNTY ROAD NO 1525 - PATEROS - MP 250.35
P13	0		RURAL	EASTERN	ER		SR 195 S/O BAUER RD 9440 - UNION TOWN - MP 6.01
P14	0		RURAL	EASTERN	ER		SR 195 S/O SR 270 - PULLMAN - MP 22.20
P15	0		RURAL	EASTERN	ER		SR 195 N/O WASHINGTON RD - SPANGLE - MP 87.70
P17	0		RURAL	EASTERN	SC		SR 221 S/O SELLARDS RD - PROSSER - MP 13.10
P18	0		RURAL	WESTERN	OR	YES	SR 101 S/O EAGLE CREEK BRIDGE -LILLIWAUP - MP 324.80
P19	0		URBAN	WESTERN	NW		SR 522 W/O SR 009 I/C - WOODINVILLE - MP 13.30
P20	0		URBAN	WESTERN	NW		SR 018 E/O SR 164 I/C - AUBURN - MP 5.26
P21	0		RURAL	WESTERN	NW		SR 009 N/O HIGHLAND DRIVE - ARLINGTON - MP 28.75
P22	0		RURAL	EASTERN	NC		SR 097 S/O OLD HIGHWAY ROAD - OROVILLE - MP 335.30
P23	0		RURAL	EASTERN	NC		SR 097 S/O SR 020 - OKANOGAN - MP 286.16
P24	0		RURAL	EASTERN	ER		SR 090 W/O IDAHO ROAD I/C -STATELINE - MP 298.40
P26	0		RURAL	EASTERN	ER		SR 395 N/O COUNTY ROAD - ORIENT - MP 260.00
P27	0	No Data	RURAL	EASTERN	ER		SR 025 N/O BOSSBURG RD - BOSSBURG - MP 97.00
P28	0		RURAL	EASTERN	ER		SR 002 S/O NORWOOD RD - CHATTAROY - MP 301.40
P29	0		URBAN	EASTERN	SC		SR 082 N/O SR 24 - YAKIMA - MP 34.02
P3	0		URBAN	WESTERN	NW		SR 005 AT NE 185TH ST UXING -SEATTLE/185TH - MP 176.72
P30	0		RURAL	EASTERN	ER		SR 027 S/O GIBBS ROAD - MICA - MP 77.30
P33	0		RURAL	EASTERN	ER		SR 290 E/O NEWMAN LAKE RD - NEWMAN LAKE - MP 17.66
P4	0		URBAN	WESTERN	OR		SR 005 AT BOULEVARD RD UXING - OLYMPIA - MP 106.70
P5	5		URBAN	WESTERN	SW		SR 005 S/O SR 500/39TH ST. I/C - VANCOUVER - MP 1.98
P6	0		URBAN	WESTERN	NW		SR 167 N/O S212TH ST I/C -KENT - MP 23.70
P7C	5		RURAL	EASTERN	ER		SR 395 S/O SR 90 I/C -RITZVILLE - MP 93.01
P8	0	No Data - Const	RURAL	WESTERN	SW		SR 005 N/O KELSO WEIGH STATION - KELSO - MP 44.30
R001	5	No Data - Const	RURAL	WESTERN	NW		SR 005 S/O SR 530 I/C - MARYSVILLE - MP 207.76
R003N	1		RURAL	WESTERN	OR		SR 101 N/O SR 008 - OLYMPIA/MUD BAY NORTH - MP 361.37
R003E	3		RURAL	WESTERN	OR		SR 101 E/O SR 008 - OLYMPIA/MUD BAY EAST - MP 361.81
R003W	7		RURAL	WESTERN	OR		SR 008 AT SR 101 OXING - OLYMPIA/MUD BAY WEST - MP 20.67

LEG LEGEND
DIRECTION OF SITE

0 NO LEG ASSIGNED
1 NORTH
2 NORTHEAST
3 EAST
5 SOUTH
6 SOUTHWEST
7 WEST
8 NORTHWEST

SITE #	LEG #	STATUS OF DATA	RURAL/URBAN	EASTERN / WESTERN	REGION	REC	SITE LOCATION	LEG LEGEND
R008	3		RURAL	EASTERN	SC		SR 012 E/O SR 730 SPUR - WALLULA - MP 307.90	
R014	3		RURAL	EASTERN	ER		SR 090 E/O FISHTRAP ROAD I/C - FISHTRAP - MP 254.38	
R017	0		URBAN	WESTERN	NW		SR 090 EAST END MT BAKER TUNNEL - MT BAKER TUNNEL - MP 4.22	
R019	5		RURAL	WESTERN	OR		SR 005 S/O SR 012 I/C - GRAND MOUND - MP 86.32	
R020	5		RURAL	EASTERN	NC		SR 017 S/O LEE ROAD - OTHELLO - MP 30.37	
R021	0		URBAN	EASTERN	ER		SR 002 E/O WALTON AVENUE - SPOKANE/DIVISION - MP 289.79	
R023	5		RURAL	WESTERN	OR		SR 101 S/O ORCAS AND HOLLAND DRIVES - DISCOVERY BAY - MP 281.15	
R034	0		URBAN	WESTERN	OR		SR 005 AT 48TH ST UXING - TACOMA/48TH ST - MP 131.18	
R036	0		URBAN	EASTERN	ER		SR 090 W/O SPRAGUE AVE I/C - SPOKANE/SPRAGUE AVE - MP 285.23	
R037	0		RURAL	EASTERN	NC	YES	SR 020 W/O RADER ROAD - WINTHROP - MP 191.90	
R038	0		RURAL	WESTERN	NW	YES	SR 002 E/O NE OLD CASCADE HWY - SKYKOMISH - MP 50.12	
R039	7		RURAL	WESTERN	SC	YES	SR 090 W/O EDGEWICK ROAD I/C - NORTH BEND - MP 33.56	
R040N	1	No Data	RURAL	WESTERN	SW	YES	SR 123 N/O ENTRANCE/EXIT OHANAPECOSH CAMPGROUND - OHANAPECOSH - MP 3.88	
R040W	7		RURAL	WESTERN	SW	YES	SR 012 W/O COAL CREEK BRIDGE - PACKWOOD - MP 135.10	
R041	0		RURAL	EASTERN	SW		SR 097 N/O STATE FRONTAGE RD - GOLDENDALE - MP 13.41	
R042	0		RURAL	EASTERN	SC	YES	SR 090 E/O WB OFF RAMP TO WANAPUM ROAD - VANTAGE - MP 136.59	
R043	0		RURAL	WESTERN	OR		SR 105 AT ELK RIVER BRIDGE - WESTPORT - MP 31.92	
R044	0		URBAN	WESTERN	OR		SR 016 W/O TACOMA NARROWS BRIDGE - TACOMA/NARROWS BRIDGE - MP 8.43	
R045	0	No Data	RURAL	WESTERN	SW		SR 005 S/O SR 503 I/C - WOODLAND - MP 20.14	
R046	0	No Data	URBAN	WESTERN	NW		SR 005 N.SR 520 I/C - SEATTLE - MP 168.84	
R047E	3		RURAL	EASTERN	NC		SR 002 E/O SR 097 - DRYDEN - MP 104.84	
R047S	5		RURAL	EASTERN	NC	YES	SR 097 S/O SR 002 - BLEWETT PASS - MP 178.19	
R047W	7		RURAL	EASTERN	NC		SR 002 W/O GREEN AND SAUNDERS ROADS - PESHASTIN - MP 103.92	
R048	0		RURAL	EASTERN	SC		SR 082 E/O SELAH CR REST AREA ON RAMP - SELAH - MP 24.83	
R050	1		URBAN	WESTERN	OR		SR 003 N/O NEWBERRY HILL I/C - SILVERDALE - MP 44.33	
R051	1		URBAN	WESTERN	SW		SR 205 N/O MILL PLAIN ROAD I/C - MILL PLAIN - MP 28.84	
R052	3		URBAN	WESTERN	NW		SR 002 E/O SR 005 I/C - EVERETT/SR 2 - MP 0.26	
R053	3		URBAN	EASTERN	NC		SR 002 E/O SR 97 AR I/C (OLDS BR) - WENATCHEE - MP 119.77	
R054	5		RURAL	WESTERN	OR		SR 101 S/O HENSEL RD - HUMPTULIPS - MP 104.55	
R055	3		RURAL	EASTERN	NC	YES	SR 090 E/O SR 17 I/C - MOSES LAKE - MP 180.33	
R057	0		RURAL	EASTERN	NC	YES	SR 970 W/O TEANAWAY RD - TEANAWAY - MP 6.85	
R058	7		RURAL	EASTERN	NC	YES	SR 002 E/O NASON RIDGE ROAD - NASON CREEK - MP 80.20	
R059	0		URBAN	EASTERN	NC		SR 097 S/O ROCKY REACH DAM ROAD - ROCKY REACH - MP 201.53	
R060	5		URBAN	WESTERN	OR		SR 005 W/O SR 510 I/C - LACEY - MP 111.01	
R061	1		RURAL	EASTERN	SC		SR 395 N/O E ELM RD - ELTOPIA - MP 36.24	
R062	7		URBAN	EASTERN	SC		SR 240 W/O OLD SR 012 I/C - RICHLAND - MP 37.20	
R063	0		RURAL	EASTERN	ER		SR 395 S/O SR 292 - LOON LAKE - MP 190.29	
R064	7		RURAL	EASTERN	ER		SR 002 W/O HARMES RD - DAVENPORT - MP 250.50	
R066	3		RURAL	EASTERN	NC	YES	SR 026 E/O SR 017 I/C - OTHELLO EAST - MP 43.06	
R067	7		RURAL	EASTERN	SC		SR 012 AT PATAHA CREEK BRIDGE - DODGE JCT - MP 390.66	
R068	1		RURAL	EASTERN	NC		SR 097 N/O COPPLE RD - OMAK - MP 293.42	
R069	0		RURAL	WESTERN	OR		SR 101 AT WEIGH STATION - PORT ANGELES - MP 254.35	
R070	0		RURAL	EASTERN	ER		SR 395 E/O SR 25 - KETTLE FALLS - MP 235.60	
R073	0		RURAL	WESTERN	OR		SR 101 E/O SR 113/BURNT MOUNTAIN RD - SAPPHO - MP 203.93	
R074	1		RURAL	WESTERN	SW	YES	SR 101 N/O SR 4 - NEMAH - MP 28.95	
R075	3		RURAL	WESTERN	SW		SR 012 E/O KENNEDY ROAD - SALKUM - MP 77.78	
R076	7		RURAL	EASTERN	SW		SR 014 W/O SR 014 MARYHILL SPUR - MARYHILL - MP 100.64	
R077	7		RURAL	EASTERN	SW		SR 014 W/O MARYHILL ROAD - STONEHENGE - MP 102.27	
R078	0		URBAN	WESTERN	SW		SR 004 W/O SR 432 AND COAL CREEK ROAD - LONGVIEW/SR 4 - MP 55.05	
R081	0		URBAN	EASTERN	SC		SR 182 AT COLUMBIA RIVER BRIDGE - PASCO - MP 6.34	
R082	5	No Data - Const	URBAN	WESTERN	NW		SR 005 S/O PACIFIC AVE I/C - EVERETT/PACIFIC - MP 193.29	
R083	1		RURAL	WESTERN	NW		SR 009 N/O 269TH PLACE NE - BRYANT - MP 32.98	
R084	1		RURAL	EASTERN	NC		SR 097 N/O BRAYS ROAD - ORONDO - MP 220.55	
R085	0		RURAL	WESTERN	OR		SR 104 AT HOOD CANAL BRIDGE - HOOD CANAL BRIDGE - MP 13.92	
R086	3		RURAL	EASTERN	SC		SR 082 E/O SR 014 I/C - UMATILLA - MP 132.03	
R087	0	No Data	URBAN	EASTERN	SC		SR 395 AT COLUMBIA RIVER BRIDGE - KENNEWICK - MP 18.58	
R088	0		RURAL	WESTERN	OR		SR 016 N/O SR 302 PURDY SPUR - BURLEY - MP 18.65	
R089	5		RURAL	WESTERN	OR		SR 003 S/O LAKE FLORA RD. - BELFAIR - MP 28.68	
R090	1		URBAN	WESTERN	OR		SR 007 N/O 38TH ST I/C - TACOMA/SR 007/ 38TH ST - MP 58.20	
R091	0		URBAN	WESTERN	OR		SR 005 AT DUPONT I/C - DUPONT - MP 119.39	
R092	5	No Data	URBAN	WESTERN	OR		SR 005 S/O SR 512 I/C - LAKEWOOD/BRIDGEPROT WAY - MP 126.76	
R093	1		URBAN	WESTERN	NW		SR 005 N/O SR 536 I/C - MOUNT VERNON - MP 226.96	
R094	0		RURAL	WESTERN	NW		SR 005 AT 236TH ST NE UXING - SYLVANA - MP 210.30	
R095	0		RURAL	WESTERN	OR		SR 104 W/O OLD PORT GAMBLE RD WYE CONN - PORT GAMBLE - MP 19.48	
R096	5		RURAL	WESTERN	OR		SR 307 S/O NE GUNDERSON RD - POULSBO - MP 2.31	
R097	5		URBAN	WESTERN	OR		SR 005 S/O TUMWATER BLVD - TUMWATER - MP 100.54	

SITE #	LEG #	STATUS OF DATA	RURAL/URBAN	EASTERN / WESTERN	REGION	REC	SITE LOCATION	LEG LEGEND
R098	0		URBAN	WESTERN	OR		SR 101 OLYMPIA/COOPER POINT RD - OLYMPIA/COOPER POINT - MP 366.69	
R099	1		URBAN	WESTERN	OR		SR 005 N/O DESHUTES PRKWY OFF RMP - TUMWATER /CUSTER - MP 103.54	
R100	1		RURAL	EASTERN	NC		SR 017 N/O SR 172 - MANSFIELD/SR 017 - MANSFIELD - MP 112.25	
R101	1		URBAN	WESTERN	NW		SR 099 N/O SPOKANE ST BRIDGE - SEATTLE/ALASKAN WAY - MP 29.37	
R104	0		RURAL	WESTERN	OR		SR 005 S/O 13TH ST I/C - CHEHALIS - MP 75.35	
R17R	0		URBAN	WESTERN	NW		SR 090 ON I-90 E. END OF MT. BAKER TUNNEL MP 4.22	
R49R	0		URBAN	WESTERN	NW		SR 005 ON I-5 REVERSABLE LANES AT E. ROANOKE ST UXING - MP 168.31	
S103	0	No Data	URBAN	EASTERN	NC		SR 285 AT COLUMBIA RIVER BRIDGE - E. WENATCHEE BRIDGE - MP 0.39	
S205	0		URBAN	WESTERN	NW		SR 005 S/O I-405/SR 518 I/C - MP 152.82	
S502	0	No Data	URBAN	WESTERN	NW		SR 520 E. OF-I-5 I/C - SEATTLE - MP 0.19	
S503	0		URBAN	WESTERN	SW		SR 433 AT COLUMBIA RIVER BR - LONGVIEW - MP 0.70	
S533	0		URBAN	WESTERN	NW		SR 520 W/O 148TH AVE NE I/C - MP 7.93	
S547	0	No Data	URBAN	WESTERN	NW		SR 520 E. OF W. LAKE SAMMAMISH PKWY - MP 12.01	
S612	0		RURAL	EASTERN	SC		SR 024 AT COLUMBIA RIVER BRIDGE - VERNITA - MP 43.50	
S706	0		RURAL	WESTERN	OR		SR 020 E/O RHODODENDRON PARK DR - COUPEVILLE - MP 20.02	
S803	5		RURAL	WESTERN	NW		SR 005 S/O BIRCH BAY/LYNDEN RD I/C - CUSTER - MP 269.41	
S809	5		URBAN	WESTERN	NW		SR 005 S/O SR 516 I/C - MIDWAY - MP 148.07	
S818E	3		RURAL	EASTERN	SC	YES	SR 012 EAST OF SR 410 - NACHES - MP 185.62	
S818S	5		RURAL	EASTERN	SC	YES	SR 012 S/O SR 410 I/C - WHITE PASS - MP 185.25	
S818W	7		RURAL	EASTERN	SC	YES	SR 410 W/O SR 012 - CHINOOK PASS - MP 116.26	
S819	0		URBAN	WESTERN	SW		SR 411 ON SR 411 S/O SANDY BEND RD - LEXINGTON - MP 7.97	
S820	7		RURAL	EASTERN	ER		SR 020 W/O FAIRGROUNDS ROAD - REPUBLIC - MP 304.60	
S822	0	No Data	URBAN	WESTERN	NW		SR 405 N OF SR 908 I/C - MP 18.71	
S824	0		URBAN	WESTERN	NW		SR 405 N/O SR 527 I/C - BOTHELL - MP 28.99	
S825	0		URBAN	WESTERN	NW		SR 090 W/O SR 900 I/C - ISSAQUAH - MP 14.65	
S826	0	No Data	URBAN	WESTERN	NW		SR 090 E/O 82ND ST I/C - PRESTON - MP 23.54	
S837	0		URBAN	WESTERN	OR		SR 005 S/O SR 099 I/C - FIFE - MP 136.80	
S838	0		RURAL	WESTERN	NW		SR 018 S/O SR 090 - ECHO GLEN - MP 27.26	
S839	0		URBAN	WESTERN	NW		SR 599 E/O SR 099 I/C - TUKWILA - MP 1.15	
S840	0		RURAL	WESTERN	SW	YES	SR 504 E/O PRIVATE ROAD 1900 - KID VALLEY - MP 19.43	
S841E	2	No Data	RURAL	WESTERN	SW		SR 401 NE/O SR 101 - ASTORIA/MEGLER - MP 0.01	
S841W	8	No Data	RURAL	WESTERN	SW		SR 101 NW/O SR 401 ASTORIA/CHINOOK - MP 0.60	
S901	0		RURAL	WESTERN	SC	YES	SR 090 AT TINKHAM ROAD UXING - TINKHAM RD - MP 47.71	
S902	0		RURAL	WESTERN	SC	YES	SR 090 AT SR 906 OXING - SNOQUALMIE - MP 52.24	
S903	0	No Data	RURAL	WESTERN	SC	YES	SR 090 AT CABIN CREEK ROAD UXING - CABIN CREEK - MP 63.98	

Prepared by the
WASHINGTON STATE DEPARTMENT OF TRANSPORTATION
Strategic Planning and Programming
Transportation Data Office

In cooperation with the
U.S. DEPARTMENT OF TRANSPORTATION
Federal Highway Administration

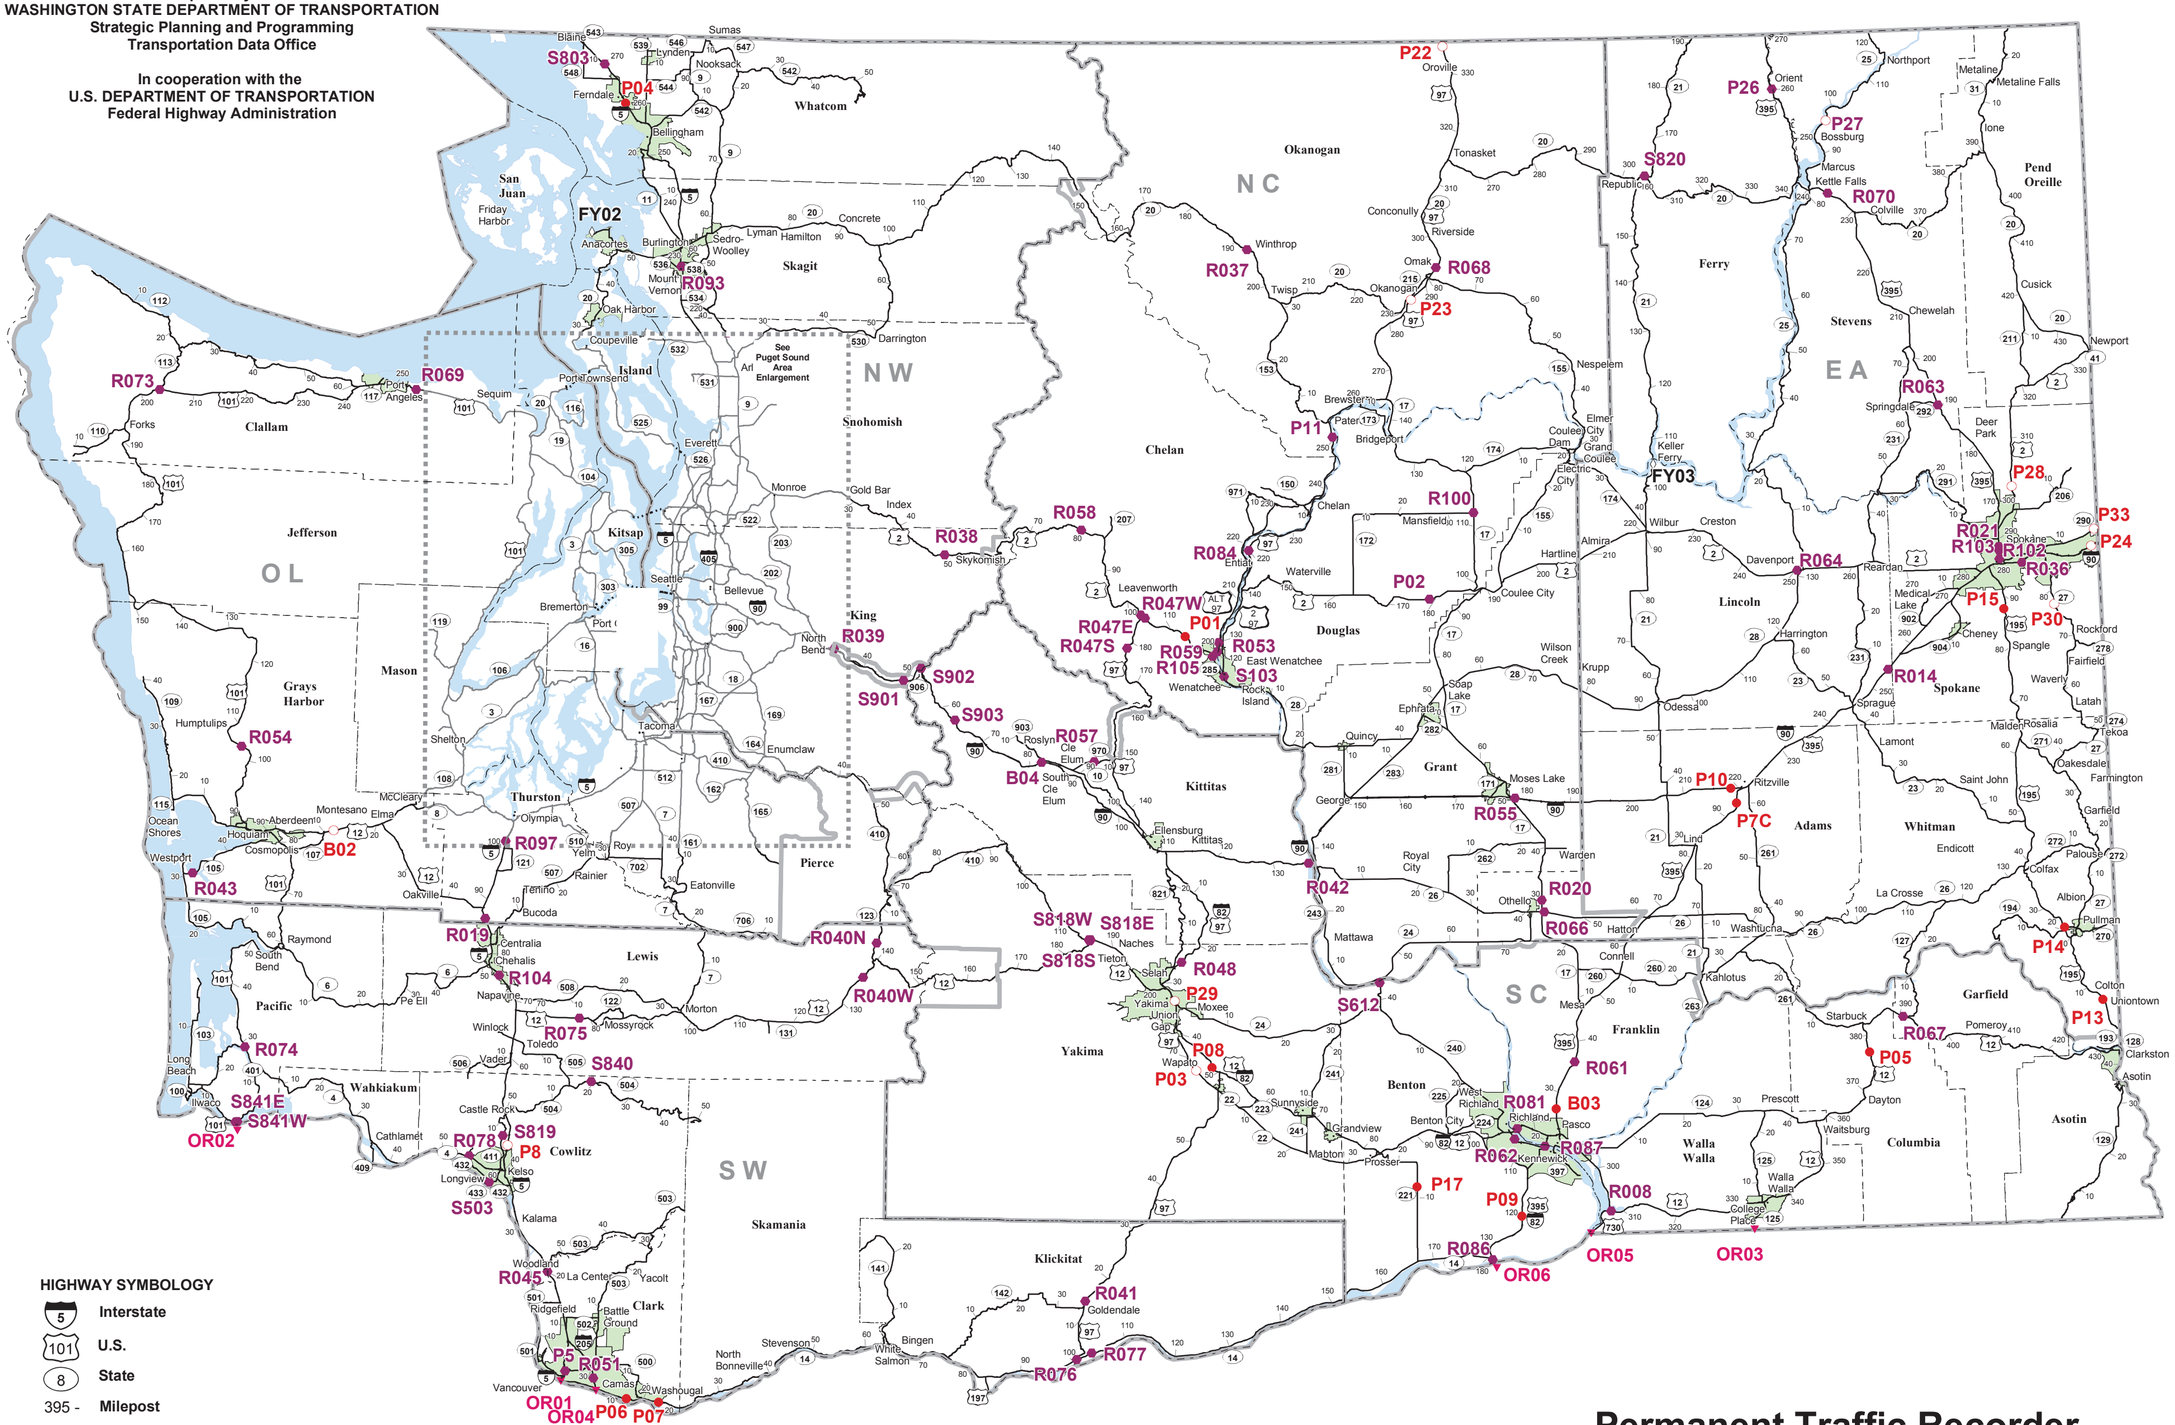

HIGHWAY SYMBOLOGY

- Interstate
- U.S.
- State
- 395 - Milepost

DATA COLLECTION TYPES

- Ferry Terminal
- Permanent Traffic Recorder (Volume, Speed, Classification)
- WIM/Vehicle Axle Classification (SHRP/LTTP Research Site)
- WIM/Vehicle Axle Classification (WIM- Weight in Motion)
- Oregon State Recorders
- Urban Area

Permanent Traffic Recorder Data Collection Sites

WASHINGTON STATE HIGHWAYS

2009

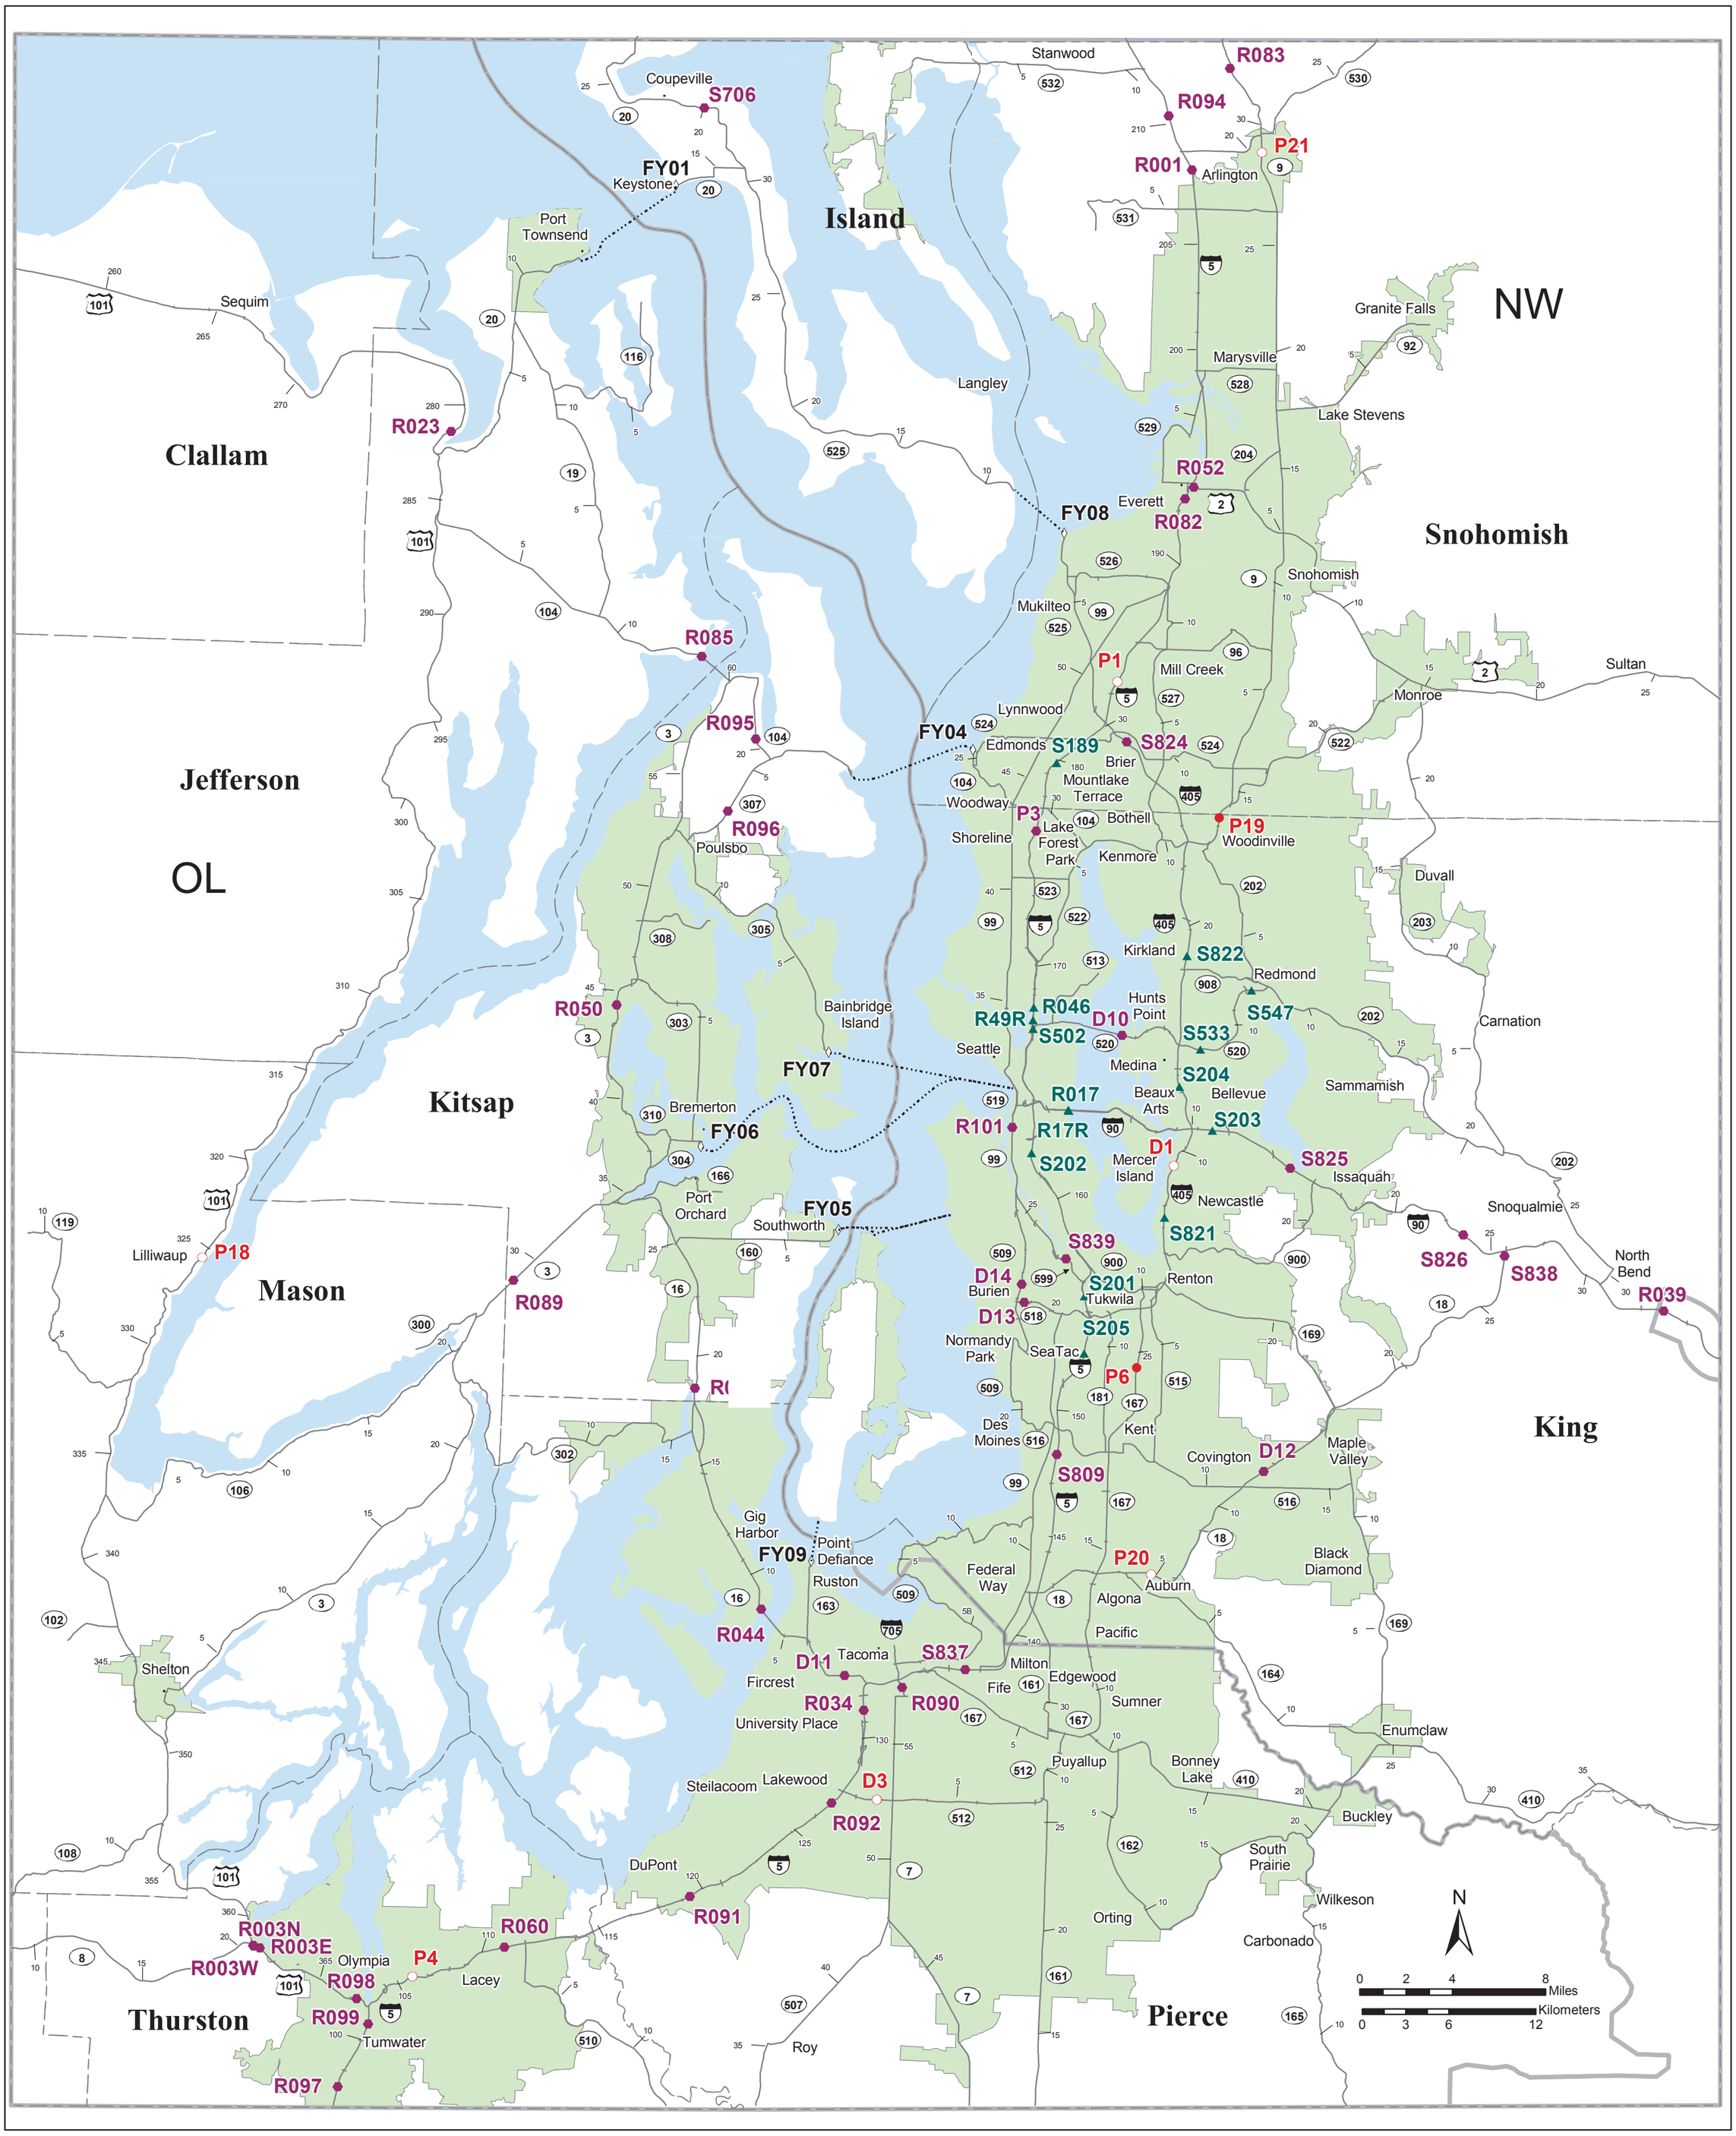

2009
Puget Sound Enlargement

Permanent Traffic Recorder Sites

- ◊ Ferry Terminal
- ▲ Northwest Region Volume Recorder
- ● Permanent Traffic Recorder (Volume, Speed, Classification)
- ● WIM/Vehicle Axle Classification (SHRP/LTTP Research Site)
- ○ WIM/Vehicle Axle Classification (WIM - Weight in Motion)
- Urban Area

2009 AVERAGE DESIGN HOUR FACTORS AS A PERCENT OF AADT

STATEWIDE AVERAGE OF 131 TOTAL LOCATIONS DESIGN FACTOR AVG 11.64 %

STATEWIDE AVERAGE OF 85 RURAL LOCATIONS DESIGN FACTOR AVG 12.75 %

STATEWIDE AVERAGE OF 46 URBAN LOCATIONS DESIGN FACTOR AVG 9.60 %

0-2,500 AADT =	15.35 %	7	RECREATIONAL	&	11	OTHER RURAL LOCATIONS			
2,500-5,000 AADT =	13.98 %	6	RECREATIONAL	&	10	OTHER RURAL	&	1	URBAN LOCATION
5,000-10,000 AADT =	11.90 %	1	RECREATIONAL	&	13	OTHER RURAL	&	2	URBAN LOCATIONS
10,000-20,000 AADT =	12.42 %	3	RECREATIONAL	&	16	OTHER RURAL	&	2	URBAN LOCATIONS
20,000-50,000 AADT =	10.53 %	4	RECREATIONAL	&	11	OTHER RURAL	&	10	URBAN LOCATIONS
50,000-100,000 AADT =	9.25 %	3	RURAL	&	15	URBAN LOCATIONS			
100,000-200,000 AADT =	8.17 %	15	URBAN LOCATIONS						
Over 200,000 AADT =	7.83 %	1	URBAN LOCATIONS						

WESTERN WASHINGTON

AVERAGE OF 72 LOCATIONS DESIGN FACTOR 10.84 %

AVERAGE OF 33 RURAL LOCATIONS DESIGN FACTOR 12.58 %

AVERAGE OF 39 URBAN LOCATIONS DESIGN FACTOR 9.36 %

EASTERN WASHINGTON

AVERAGE OF 59 LOCATIONS DESIGN FACTOR 12.63 %

AVERAGE OF 52 RURAL LOCATIONS DESIGN FACTOR 12.86 %

AVERAGE OF 7 URBAN LOCATIONS DESIGN FACTOR 10.93 %

NOTE: K 100 was used at 21 RECREATIONAL LOCATIONS AVERAGE 16.68 %

Data source: Peak Hour report from ADC sites maintained by WSDOT's Transportation Data Office

Supporting Data Sheet 2009 **Average Design Hour Factors as a Percent of AADT**

0-2500 AADT	SITE	SR	MP	AADT	K-30 FACTOR	K-100 FACTOR	DESIGN FACTOR	D-FACTOR	URBAN	RURAL	K-REC	LOCATION	
	P02-Data	002	179.10	645	20.00	16.12	16.12	58.70		R	K	EASTERN	
	P05-Data	012	376.98	1,975	13.87	12.35	13.87	55.29		R		EASTERN	
	P17-Data	221	13.10	2,037	12.57	11.34	12.57	73.08		R		EASTERN	
	P22-Data	097	335.30	1,858	13.02	12.00	13.02	54.58		R		EASTERN	
	P26-Data	395	260.00	638	18.03	13.64	11.55	57.48		R		EASTERN	
	R037-Data	020	191.9	1,759	25.18	20.01	20.01	59.49		R	K	EASTERN	
	R040W-Data	012	135.10	1,814	26.30	20.89	20.89	55.17		R	K		WESTERN
	R054-Data	101	104.55	2,153	11.66	10.13	11.66	54.66		R			WESTERN
	R067-Data	012	390.66	1,955	14.02	12.79	14.02	55.64		R		EASTERN	
	R074-Data	101	28.95	2,267	21.97	16.76	16.76	61.04		R	K		WESTERN
	R076-Data	014	100.64	2,022	15.23	12.86	15.23	54.51		R		EASTERN	
	R077-Data	014	102.27	1,951	5.13	4.31	5.13	56.25		R		EASTERN	
	R083-Data	009	32.98	1,965	15.22	13.18	15.22	59.07		R			WESTERN
	R100-Data	017	112.25	554	13.18	11.73	13.18	58.44		R		EASTERN	
	S818S-Data	012	185.25	2,121	23.39	18.01	18.01	59.29		R	K	EASTERN	
	S818W-Data	410	116.26	1,950	19.38	16.51	16.51	54.76		R	K	EASTERN	
	S820-Data	020	304.60	2,263	13.26	11.58	13.26	53.94		R		EASTERN	
	S840-Data	504	19.43	731	37.35	29.27	29.27	71.43		R	K		WESTERN
TOTALS & AVERAGES	**18**			**1,703**	**17.71**	**14.64**	**15.35**	**58.49**	**0**	**18**	**7**	**13**	**5**

Supporting Data Sheet 2009 **Average Design Hour Factors as a Percent of AADT**

2,500 - 5,000 AADT	SITE	SR	MP	AADT	K-30 FACTOR	K-100 FACTOR	DESIGN FACTOR	D-FACTOR	URBAN	RURAL	K-REC	LOCATION	
	P11-Data	097	250.35	4,213	12.63	11.54	12.63	59.69		R		EASTERN	
	P13-Data	195	6.01	4,394	10.47	9.85	10.47	60.04		R		EASTERN	
	P14-Data	195	22.2	3,136	11.13	10.01	11.13	52.94		R		EASTERN	
	P18-Data	101	324.80	3,027	22.63	17.84	17.84	57.83		R	K		WESTERN
	P23-Data	097	286.16	3,971	11.31	10.17	11.31	55.51		R		EASTERN	
	R008-Data	012	307.90	3,294	11.26	10.32	11.26	53.95		R		EASTERN	
	R038-Data	002	50.12	4,903	19.62	17.34	17.34	73.56		R	K		WESTERN
	R041-Data	097	13.41	4,769	14.59	11.87	14.59	53.74		R		EASTERN	
	R057-Data	970	6.85	4,123	20.16	16.74	16.74	67.97		R	K	EASTERN	
	R058-Data	002	80.20	4,037	22.27	19.79	19.79	70.36		R	K	EASTERN	
	R064-Data	002	250.50	2,745	12.35	11.44	12.35	55.22		R		EASTERN	
	R066-Data	026	43.06	2,576	20.42	14.44	14.44	62.65		R	K	EASTERN	
	R073-Data	101	203.93	2,578	14.20	13.03	14.20	55.56		R			WESTERN
	R084-Data	097	220.55	4,065	13.09	11.86	13.09	59.87		R		EASTERN	
	S612-Data	024	43.50	3,666	11.67	10.69	11.67	54.71		R		EASTERN	
	S818E-Data	012	185.62	4,209	20.67	17.84	17.84	56.92		R	K	EASTERN	
	S819-Data	411	7.97	3,651	10.96	10.05	10.96	62.86	U				WESTERN
TOTALS & AVERAGES	**17**			**3,727**	**15.26**	**13.22**	**13.98**	**59.61**	**1**	**16**	**6**	**13**	**4**

5,000 - 10,000 AADT	SITE	SR	MP	AADT	K-30 FACTOR	K-100 FACTOR	DESIGN FACTOR	D-FACTOR	URBAN	RURAL	K-REC	LOCATION	
	P07-Data	014	17.70	5,734	11.48	10.34	11.48	56.25		R			WESTERN
	P15-Data	195	87.7	8,211	11.08	9.84	11.08	53.78		R		EASTERN	
	P30-Data	027	77.30	6,058	10.81	9.95	10.81	56.39		R		EASTERN	
	P33-Data	290	17.66	7,156	12.12	11.32	12.12	65.38		R		EASTERN	
	P7C-Data	395	93.01	7,029	13.47	11.98	13.47	55.97		R		EASTERN	
	R020-Data	017	30.37	6,002	9.88	9.23	9.88	53.32		R		EASTERN	
	R043-Data	105	31.92	5,497	12.63	11.46	12.63	56.12		R			WESTERN
	R047S-Data	097	178.19	5,167	18.52	15.73	15.73	64.94		R	K	EASTERN	
	R059-Data	97ALT	201.53	6,870	14.43	12.94	14.43	59.35	U			EASTERN	
	R063-Data	395	190.29	8,171	10.89	9.78	10.89	56.63		R		EASTERN	
	R068-Data	097	293.42	5,316	11.00	10.03	11.00	57.27		R		EASTERN	
	R070-Data	395	235.60	7,424	10.59	10.09	10.59	53.63		R		EASTERN	
	R075-Data	012	77.78	6,541	12.70	11.34	12.70	56.87		R			WESTERN
	R078-Data	004	55.05	5,083	10.31	9.38	10.31	56.92	U				WESTERN
	R095-Data	104	19.48	5,256	12.75	11.47	12.75	55.57		R			WESTERN
	S706-Data	020	20.02	8,479	10.50	9.97	10.50	57.16		R			WESTERN
TOTALS & AVERAGES	**16**			**6,500**	**12.07**	**10.93**	**11.90**	**57.22**	**2**	**14**	**1**	**10**	**6**

Supporting Data Sheet 2009 **Average Design Hour Factors as a Percent of AADT**

10,000 - 20,000 AADT	SITE	SR	MP	AADT	K-30 FACTOR	K-100 FACTOR	DESIGN FACTOR	D-FACTOR	URBAN	RURAL	K-REC	LOCATION	
	B03-Data	395	27.20	14,597	10.82	10.06	10.82	52.38		R		EASTERN	
	P03-Data	097	66.30	12,195	10.02	9.48	10.02	52.98		R		EASTERN	
	P09-Data	082	121.20	15,982	11.28	10.29	11.28	51.96		R		EASTERN	
	P10-Data	090	218.83	10,092	16.22	14.09	14.09	55.49		R	K	EASTERN	
	P21-Data	009	28.75	11,245	10.23	9.74	10.23	58.02		R			WESTERN
	P28-Data	002	301.40	17,309	10.57	9.82	10.57	67.21		R		EASTERN	
	R003W-Data	008	20.67	17,145	10.93	9.94	10.93	63.31		R			WESTERN
	R014-Data	090	254.38	16,441	14.46	12.57	14.46	55.81		R		EASTERN	
	R023-Data	101	281.15	10,913	12.76	11.27	12.76	56.34		R			WESTERN
	R042-Data	090	136.59	14,287	17.40	15.03	15.03	60.55		R	K	EASTERN	
	R047E-Data	002	104.84	14,784	13.18	12.07	13.18	58.67		R		EASTERN	
	R047W-Data	002	103.92	12,169	12.60	11.69	12.60	53.29		R		EASTERN	
	R048-Data	082	24.83	15,896	11.87	11.03	11.87	53.48		R		EASTERN	
	R055-Data	090	180.33	10,714	14.46	12.00	12.00	53.27		R	K	EASTERN	
	R061-Data	395	36.24	13,342	10.66	9.80	10.66	52.41		R		EASTERN	
	R085-Data	104	13.92	16,011	11.67	10.52	11.67	56.80		R			WESTERN
	R086-Data	082	132.03	17,158	10.96	10.04	10.96	52.04		R		EASTERN	
	R089-Data	003	28.68	17,113	9.54	9.17	9.54	61.63		R			WESTERN
	R096-Data	307	2.31	15,393	10.02	9.53	10.02	58.12		R			WESTERN
	R17R-Data	090	4.22	11,530	27.48	24.56	27.48	50.00	U				WESTERN
	S503-Data	433	0.70	19,542	10.62	9.91	10.62	52.17	U				WESTERN
TOTALS & AVERAGES	**21**			**14,469**	**12.75**	**11.55**	**12.42**	**56.00**	**2**	**19**	**3**	**13**	**8**

Supporting Data Sheet 2009 **Average Design Hour Factors as a Percent of AADT**

20,000 - 50,000 AADT	SITE	SR	MP	AADT	K-30 FACTOR	K-100 FACTOR	DESIGN FACTOR	D-FACTOR	URBAN	RURAL	K-REC	LOCATION	
	B02-Data	012	12.30	20,042	11.73	10.49	11.73	60.47		R			WESTERN
	B04-Data	090	82.70	26,961	15.88	13.92	13.92	59.98		R	K	EASTERN	
	D12-Data	018	12.55	31,288	10.26	9.55	10.26	53.63	U				WESTERN
	P01-Data	002	113.10	20,647	11.28	10.49	11.28	54.89		R		EASTERN	
	P04-Data	005	261.33	45,544	9.54	9.15	9.54	56.10		R			WESTERN
	P06-Data	014	11.90	37,838	9.25	9.03	9.25	58.60	U				WESTERN
	P08-Data	082	48.50	24,049	10.25	9.60	10.25	53.41		R		EASTERN	
	P19-Data	522	13.30	45,644	8.45	8.24	8.45	65.85	U				WESTERN
	P24-Data	090	298.40	47,313	10.24	9.71	10.24	56.62		R		EASTERN	
	P29-Data	082	34.02	45,611	10.15	9.58	10.15	50.89	U			EASTERN	
	R003E-Data	101	361.81	47,785	9.76	9.38	9.76	61.15		R			WESTERN
	R003N-Data	101	361.37	30,635	9.65	9.37	9.65	61.69		R			WESTERN
	R021-Data	002	289.79	42,561	9.24	8.91	9.24	56.63	U			EASTERN	
	R039-Data	090	33.56	32,946	14.67	13.24	13.24	62.57		R	K		WESTERN
	R050-Data	003	44.33	42,748	9.98	9.71	9.98	51.95	U				WESTERN
	R053-Data	002	119.77	20,326	10.98	10.23	10.98	56.44	U			EASTERN	
	R069-Data	101	254.35	21,919	10.26	9.74	10.26	54.42		R			WESTERN
	R088-Data	016	18.65	42,310	8.90	8.58	8.90	53.22		R			WESTERN
	R090-Data	007	58.02	23,105	9.15	8.63	9.15	61.91	U				WESTERN
	R49R-Data	005	168.31	44,707	11.75	11.42	11.75	50.01	U				WESTERN
	S803-Data	005	269.41	27,032	9.32	8.88	9.32	55.03		R			WESTERN
	S838-Data	018	27.62	21,277	11.42	10.51	11.42	57.00		R			WESTERN
	S839-Data	599	1.15	39,926	9.77	9.57	9.77	64.11	U				WESTERN
	S901-Data	090	47.71	30,170	13.72	12.12	12.12	61.78		R	K		WESTERN
	S902-Data	090	52.24	27,535	14.12	12.61	12.61	62.16		R	K		WESTERN
TOTALS & AVERAGES	**25**			**33,597**	**10.79**	**10.11**	**10.53**	**57.62**	**10**	**15**	**4**	**7**	**18**

Supporting Data Sheet 2009 **Average Design Hour Factors as a Percent of AADT**

50,000 - 100,000 AADT	SITE	SR	MP	AADT	K-30 FACTOR	K-100 FACTOR	DESIGN FACTOR	D-FACTOR	URBAN	RURAL	K-REC	LOCATION	
	D10-Data	520	4.00	97,372	7.95	7.70	7.95	51.16	U				WESTERN
	D13-Data	518	0.35	54,561	8.13	7.92	8.13	55.44	U				WESTERN
	D14-Data	509	26.37	57,371	9.84	9.54	9.84	59.74	U				WESTERN
	D3-Data	512	1.53	88,733	8.07	7.89	8.07	59.07	U				WESTERN
	P20-Data	018	5.26	55,239	9.05	8.69	9.05	52.49	U				WESTERN
	R019-Data	005	86.32	59,609	9.76	9.33	9.76	51.94		R			WESTERN
	R044-Data	016	8.43	78,925	8.77	8.56	8.77	61.36	U				WESTERN
	R052-Data	002	0.26	71,855	8.52	8.24	8.52	64.88	U				WESTERN
	R062-Data	240	37.20	64,399	11.38	10.91	11.38	60.20	U			EASTERN	
	R081-Data	182	6.34	53,828	10.58	9.86	10.58	58.31	U			EASTERN	
	R093-Data	005	226.96	66,554	9.18	8.77	9.18	51.91	U				WESTERN
	R094-Data	005	210.30	71,695	8.93	8.37	8.93	53.71		R			WESTERN
	R097-Data	005	100.54	68,903	9.26	8.81	9.26	52.55	U				WESTERN
	R098-Data	101	366.69	96,528	9.08	8.89	9.08	52.99	U				WESTERN
	R099-Data	005	103.54	95,564	9.05	8.73	9.05	51.35	U				WESTERN
	R101-Data	099	29.37	73,176	11.07	10.75	11.07	53.84	U				WESTERN
	R104-Data	005	75.35	59,548	9.46	8.73	9.46	52.87		R			WESTERN
	S533-Data	520	7.93	97,510	8.49	8.28	8.49	55.58	U				WESTERN
TOTALS & AVERAGES	**18**			**72,854**	**9.25**	**8.89**	**9.25**	**55.52**	**15**	**3**	**0**	**2**	**16**

Supporting Data Sheet 2009 **Average Design Hour Factors as a Percent of AADT**

100,000 - 200,000 AADT	SITE	SR	MP	AADT	K-30 FACTOR	K-100 FACTOR	DESIGN FACTOR	D-FACTOR	URBAN	RURAL	K-REC	LOCATION	
	P1-Data	005	184.48/185.35	181,503	7.60	7.34	7.60	52.40	U				WESTERN
	P3-Data	005	176.72	185,290	7.59	7.45	7.59	56.27	U				WESTERN
	P4-Data	005	106.7	138,427	8.77	8.59	8.77	51.53	U				WESTERN
	P5-Data	005	1.98	123,359	8.43	8.30	8.43	60.02	U				WESTERN
	P6-Data	167	23.7	114,340	7.09	6.98	7.09	56.41	U				WESTERN
	R017-Data	090	4.22	112,454	9.67	9.43	9.67	50.76	U				WESTERN
	R034-Data	005	131.18	185,645	7.45	7.33	7.45	53.39	U				WESTERN
	R036-Data	090	285.23	107,345	9.77	9.54	9.77	55.42	U			EASTERN	
	R051-Data	205	28.84	107,856	8.18	7.86	8.18	54.39	U				WESTERN
	R060-Data	005	111.01	113,492	8.40	8.09	8.40	51.87	U				WESTERN
	R091-Data	005	119.36	118,013	8.02	7.84	8.02	54.49	U				WESTERN
	S809-Data	005	148.07	191,400	7.79	7.64	7.79	61.85	U				WESTERN
	S824-Data	405	28.99	111,033	8.46	8.32	8.46	52.09	U				WESTERN
	S825-Data	090	14.65	119,100	8.09	6.97	8.09	62.22	U				WESTERN
	S837-Data	005	136.8	182,204	7.24	7.10	7.24	53.64	U				WESTERN
TOTALS & AVERAGES	**15**			**139,431**	**8.17**	**7.92**	**8.17**	**55.12**	**15**	**0**	**0**	**1**	**14**

200,000 + AADT	SITE	SR	MP	AADT	K-30 FACTOR	K-100 FACTOR	DESIGN FACTOR	D-FACTOR	URBAN	RURAL	K-REC	LOCATION	
	S205-Data	005	152.82	207,015	7.83	7.68	7.83	58.02	U				WESTERN
TOTALS & AVERAGES	**1**			**207,015**	**7.83**	**7.68**	**7.83**	**58.02**	**1**	**0**	**0**	**0**	**1**

PEAK HOUR REPORT FOR PEAK 200 HOURS OF 2009--DATA SUMMARY

SITE	AADT	K-30 FACTOR	% OF ADT	K-50 FACTOR	% OF ADT	K-100 FACTOR	% OF ADT	K-200 FACTOR	% OF ADT	D-FACTOR	% OF ADT
B02-Data		ON SR 012 W/O MONTE BRADY RD WYE CONN - BRADY - MP 12.3									
AADT=	20,042	K 30 FACTOR=	11.73	K-50 FACTOR=	11.35	K 100 FACTOR=	10.49	K-200 FACTOR	9.86	D FACTOR=	60.47
B03-Data		ON SR 395 S/O VINEYARD DR - PASCO - MP 27.20									
AADT=	14,597	K 30 FACTOR=	10.82	K-50 FACTOR=	10.46	K 100 FACTOR=	10.06	K-200 FACTOR	9.52	D FACTOR=	52.38
B04-Data		ON SR 090 W/O CLE ELUM OFF RAMP - CLE ELLUM - MP 82.70									
AADT=	26,961	K 30 FACTOR=	15.88	K-50 FACTOR=	15.10	K 100 FACTOR=	13.92	K-200 FACTOR	12.58	D FACTOR=	59.98
D10-Data		ON SR 520 W/O 76TH AVE NE UXING - TOLL PLAZA - MP 4.00									
AADT=	97,372	K 30 FACTOR=	7.95	K-50 FACTOR=	7.86	K 100 FACTOR=	7.70	K-200 FACTOR	7.53	D FACTOR=	51.16
D12-Data		ON SR 018 AT 180TH AVE SE UXING - COVINGTON - MP 12.55									
AADT=	31,288	K 30 FACTOR=	10.26	K-50 FACTOR=	9.95	K 100 FACTOR=	9.55	K-200 FACTOR	9.01	D FACTOR=	53.63
D13-Data		ON SR 518 E/O SR 509 I/C - SEATAC - MP 0.35									
AADT=	54,561	K 30 FACTOR=	8.13	K-50 FACTOR=	8.04	K 100 FACTOR=	7.92	K-200 FACTOR	7.73	D FACTOR=	55.44
D14-Data		ON SR 509 N/O SR 518 I/C - BURIEN - MP 26.37									
AADT=	57,371	K 30 FACTOR=	9.84	K-50 FACTOR=	9.73	K 100 FACTOR=	9.54	K-200 FACTOR	9.30	D FACTOR=	59.74
D3-Data		ON SR 512 W/O SR 007 I/C - PARKLAND - MP 1.53									
AADT=	88,733	K 30 FACTOR=	8.07	K-50 FACTOR=	8.00	K 100 FACTOR=	7.89	K-200 FACTOR	7.78	D FACTOR=	59.07
P01-Data		ON SR 097 S/O PROGRESSIVE ROAD WYE CONN - WAPATO - MP 66.30									
AADT=	20,647	K 30 FACTOR=	11.28	K-50 FACTOR=	11.03	K 100 FACTOR=	10.49	K-200 FACTOR	9.80	D FACTOR=	54.89
P02-Data		ON SR 002 E/O J SE - COULEE CITY - MP 179.10									
AADT=	645	K 30 FACTOR=	20.00	K-50 FACTOR=	18.29	K 100 FACTOR=	16.12	K-200 FACTOR	13.64	D FACTOR=	58.70
P03-Data		ON SR 097 S/O PROGRESSIVE ROAD WYE CONN - WAPATO - MP 66.30									
AADT=	12,195	K 30 FACTOR=	10.02	K-50 FACTOR=	9.83	K 100 FACTOR=	9.48	K-200 FACTOR	9.09	D FACTOR=	52.98
P04-Data		ON SR 005 N/O SLATER ROAD I/C - FERNDALE - MP 261.33									
AADT=	45,544	K 30 FACTOR=	9.54	K-50 FACTOR=	9.35	K 100 FACTOR=	9.15	K-200 FACTOR	8.92	D FACTOR=	56.10
P05-Data		ON SR 012 W/O TUCANNON RIVER BR - DAYTON - MP 376.98									
AADT=	1,975	K 30 FACTOR=	13.87	K-50 FACTOR=	13.22	K 100 FACTOR=	12.35	K-200 FACTOR	11.39	D FACTOR=	55.29
P06-Data		ON SR 014 E/O ALPINE RD - CAMAS - MP 11.90									
AADT=	37,838	K 30 FACTOR=	9.25	K-50 FACTOR=	9.17	K 100 FACTOR=	9.03	K-200 FACTOR	8.84	D FACTOR=	58.60
P07-Data		ON SR 014 E/O 32ND ST - WASHOUGAL - MP 17.70									
AADT=	5,734	K 30 FACTOR=	11.48	K-50 FACTOR=	10.97	K 100 FACTOR=	10.34	K-200 FACTOR	9.75	D FACTOR=	56.25
P08-Data		ON SR 082 W/O SR 22 - ZILLAH - MP 48.50									
AADT=	24,049	K 30 FACTOR=	10.25	K-50 FACTOR=	10.03	K 100 FACTOR=	9.60	K-200 FACTOR	9.06	D FACTOR=	53.41
P09-Data		ON SR 082 W/O COFFIN RD - PLYMOUTH - MP 121.20									
AADT=	15,982	K 30 FACTOR=	11.28	K-50 FACTOR=	10.79	K 100 FACTOR=	10.29	K-200 FACTOR	9.61	D FACTOR=	51.96
P1-Data		ON SR 005 N/O 164TH STREET SW - EVERETT - MP 184.48									
AADT=	181,503	K 30 FACTOR=	7.60	K-50 FACTOR=	7.51	K 100 FACTOR=	7.34	K-200 FACTOR	7.11	D FACTOR=	52.40

PEAK HOUR REPORT FOR PEAK 200 HOURS OF 2009--DATA SUMMARY

SITE	AADT	K-30 FACTOR	% OF ADT	K-50 FACTOR	% OF ADT	K-100 FACTOR	% OF ADT	K-200 FACTOR	% OF ADT	D-FACTOR	% OF ADT
P10-Data		ON SR 090 W/O SR 395 I/C - RITZVILLE - MP 218.83									
AADT=	10,092	K 30 FACTOR=	16.22	K-50 FACTOR=	15.50	K 100 FACTOR=	14.09	K-200 FACTOR	12.57	D FACTOR=	55.49
P11-Data		ON SR 097 N/O COUNTY ROAD NO 1525 - PATEROS - MP 250.35									
AADT=	4,213	K 30 FACTOR=	12.63	K-50 FACTOR=	12.13	K 100 FACTOR=	11.54	K-200 FACTOR	10.63	D FACTOR=	59.69
P13-Data		ON SR 195 S/O BAUER RD 9440 - COLTON - MP 6.01									
AADT=	4,394	K 30 FACTOR=	10.47	K-50 FACTOR=	10.26	K 100 FACTOR=	9.85	K-200 FACTOR	9.38	D FACTOR=	60.04
P14-Data		ON SR 195 S/O SR 270 - PULLMAN - MP 22.20									
AADT=	3,136	K 30 FACTOR=	11.13	K-50 FACTOR=	10.91	K 100 FACTOR=	10.01	K-200 FACTOR	9.18	D FACTOR=	52.94
P15-Data		ON SR 195 N/O WASHINGTON RD - SPOKANE - MP 87.70									
AADT=	8,211	K 30 FACTOR=	11.08	K-50 FACTOR=	10.62	K 100 FACTOR=	9.84	K-200 FACTOR	9.15	D FACTOR=	53.78
P17-Data		ON SR 221 S/O SELLARDS RD - PROSSER - MP 13.10									
AADT=	2,037	K 30 FACTOR=	12.57	K-50 FACTOR=	12.17	K 100 FACTOR=	11.34	K-200 FACTOR	10.41	D FACTOR=	73.08
P18-Data		ON SR 195 N/O WASHINGTON RD - SPOKANE - MP 87.70									
AADT=	3,027	K 30 FACTOR=	22.63	K-50 FACTOR=	20.42	K 100 FACTOR=	17.84	K-200 FACTOR	14.83	D FACTOR=	57.83
P19-Data		ON SR 522 W/O SR 9 I/C - WOODINVILLE - MP 13.30									
AADT=	45,644	K 30 FACTOR=	8.45	K-50 FACTOR=	8.37	K 100 FACTOR=	8.24	K-200 FACTOR	8.07	D FACTOR=	65.85
P20-Data		ON SR 018 E/O SR 164 I/C - AUBURN - MP 5.26									
AADT=	55,239	K 30 FACTOR=	9.05	K-50 FACTOR=	8.93	K 100 FACTOR=	8.69	K-200 FACTOR	8.37	D FACTOR=	52.49
P21-Data		ON SR 009 N/O HIGHLAND DR - ARLINGTON - MP 28.75									
AADT=	11,245	K 30 FACTOR=	10.23	K-50 FACTOR=	10.06	K 100 FACTOR=	9.74	K-200 FACTOR	9.41	D FACTOR=	58.02
P22-Data		ON SR 097 S/O OLD HIGHWAY ROAD - OROVILLE - MP 335.30									
AADT=	1,858	K 30 FACTOR=	13.02	K-50 FACTOR=	12.59	K 100 FACTOR=	12.00	K-200 FACTOR	11.14	D FACTOR=	54.58
P23-Data		ON SR 097 S/O SR 20 - OKANOGAN - MP 286.16									
AADT=	3,971	K 30 FACTOR=	11.31	K-50 FACTOR=	10.75	K 100 FACTOR=	10.17	K-200 FACTOR	9.59	D FACTOR=	55.51
P24-Data		ON SR 090 W/O IDAHO ROAD I/C - STATELINE - MP 298.4									
AADT=	47,313	K 30 FACTOR=	10.24	K-50 FACTOR=	10.00	K 100 FACTOR=	9.71	K-200 FACTOR	9.27	D FACTOR=	56.62
P26-Data		ON SR 395 N/O COUNTY ROAD - ORIENT - MP 260.00									
AADT=	638	K 30 FACTOR=	18.03	K-50 FACTOR=	16.14	K 100 FACTOR=	13.64	K-200 FACTOR	11.76	D FACTOR=	57.48
P27-Data		ON SR 025 N/O BOSSBURG RD - BOSSBURG - MP 97.0									
AADT=	0	K 30 FACTOR=	0.00	K-50 FACTOR=	0.00	K 100 FACTOR=	0.00	K-200 FACTOR	0.00	D FACTOR=	0.00
P28-Data		ON SR 002 S/O NORWOOD RD - CHATTAROY - MP 301.40									
AADT=	17,309	K 30 FACTOR=	10.57	K-50 FACTOR=	10.23	K 100 FACTOR=	9.82	K-200 FACTOR	9.38	D FACTOR=	67.21
P29-Data		ON SR 082 W/O SR 024 I/C - YAKIMA - MP 34.02									
AADT=	45,611	K 30 FACTOR=	10.15	K-50 FACTOR=	9.91	K 100 FACTOR=	9.58	K-200 FACTOR	9.18	D FACTOR=	50.89
P3-Data		ON SR 005 AT NE 185TH ST UXING - SEATTLE/185TH - MP 176.72									
AADT=	185,290	K 30 FACTOR=	7.59	K-50 FACTOR=	7.54	K 100 FACTOR=	7.45	K-200 FACTOR	7.35	D FACTOR=	56.27

PEAK HOUR REPORT FOR PEAK 200 HOURS OF 2009--DATA SUMMARY

SITE	AADT	K-30 FACTOR	% OF ADT	K-50 FACTOR	% OF ADT	K-100 FACTOR	% OF ADT	K-200 FACTOR	% OF ADT	D-FACTOR	% OF ADT
P30-Data		ON SR 027 S/O GIBBS ROAD - MICA - MP 77.30									
AADT=	6,058	K 30 FACTOR=	10.81	K-50 FACTOR=	10.56	K 100 FACTOR=	9.95	K-200 FACTOR	9.39	D FACTOR=	56.39
P33-Data		ON SR 290 E/O NEWMAN LAKE RD - NEWMAN LAKE - MP 17.66									
AADT=	7,156	K 30 FACTOR=	12.12	K-50 FACTOR=	11.82	K 100 FACTOR=	11.32	K-200 FACTOR	10.51	D FACTOR=	65.38
P4-Data		ON SR 005 AT BOULEVARD RD UXING-OLYMPIA - MP 106.70									
AADT=	138,427	K 30 FACTOR=	8.77	K-50 FACTOR=	8.69	K 100 FACTOR=	8.59	K-200 FACTOR	8.47	D FACTOR=	51.53
P5-Data		ON SR 005 S/O SR 500/39TH ST I/C - VANCOUVER - MP 1.98									
AADT=	123,359	K 30 FACTOR=	8.43	K-50 FACTOR=	8.38	K 100 FACTOR=	8.30	K-200 FACTOR	8.16	D FACTOR=	60.02
P6-Data		ON SR 167 N/O S212TH ST I/C - KENT - MP 23.7									
AADT=	114,340	K 30 FACTOR=	7.09	K-50 FACTOR=	7.06	K 100 FACTOR=	6.98	K-200 FACTOR	6.91	D FACTOR=	56.41
P7C-Data		ON SR 395 S/O SR90 I/C- RITZVILLE - MP 93.01									
AADT=	7,029	K 30 FACTOR=	13.47	K-50 FACTOR=	12.65	K 100 FACTOR=	11.98	K-200 FACTOR	10.94	D FACTOR=	55.97
P8-Data		ON SR 005 N/O KELSO WEIGH STATION - KELSO - MP 44.30									
AADT=	0	K 30 FACTOR=	0.00	K-50 FACTOR=	0.00	K 100 FACTOR=	0.00	K-200 FACTOR	0.00	D FACTOR=	0.00
R001-Data		ON SR 005 S/O SR 530 I/C - MARYSVILLE - MP 207.76									
AADT=	0	K 30 FACTOR=	0.00	K-50 FACTOR=	0.00	K 100 FACTOR=	0.00	K-200 FACTOR	0.00	D FACTOR=	0.00
R003N-Data		ON SR 101 N/O SR 8 - OLYMPIA/MUDBAY NORTH - MP 361.37									
AADT=	30,635	K 30 FACTOR=	9.65	K-50 FACTOR=	9.54	K 100 FACTOR=	9.37	K-200 FACTOR	9.07	D FACTOR=	61.69
R003E-Data		ON SR 101 E/O SR 8 - OLYMPIA/MUDBAY EAST - MP 361.81									
AADT=	47,785	K 30 FACTOR=	9.76	K-50 FACTOR=	9.56	K 100 FACTOR=	9.38	K-200 FACTOR	9.07	D FACTOR=	61.15
R003W-Data		ON SR 008 AT SR 101 OXING - OLYMPIA/MUDBAY WEST - MP 20.67									
AADT=	17,145	K 30 FACTOR=	10.93	K 50 FACTOR=	10.58	K 100 FACTOR=	9.94	K-200 FACTOR	9.26	D FACTOR=	63.31
R008-Data		ON SR 012 E/O SR 730 SPUR - WALLULA - MP 307.90									
AADT=	3,294	K 30 FACTOR=	11.26	K-50 FACTOR=	10.87	K 100 FACTOR=	10.32	K-200 FACTOR	9.65	D FACTOR=	53.95
R014-Data		ON SR 090 E/O FISHTRAP ROAD 1/C - FISHTRAP - MP 254.23									
AADT=	16,441	K 30 FACTOR=	14.46	K-50 FACTOR=	13.72	K 100 FACTOR=	12.57	K-200 FACTOR	11.44	D FACTOR=	55.81
R017-Data		ON SR 090 E. END OF MT BAKER TUNNEL - MP 4.22									
AADT=	112,454	K 30 FACTOR=	9.67	K-50 FACTOR=	9.56	K 100 FACTOR=	9.43	K-200 FACTOR	9.28	D FACTOR=	50.76
R019-Data		ON SR 005 S/O SR 012 I/C - GRAND MOUND - MP 86.32									
AADT=	59,609	K 30 FACTOR=	9.76	K-50 FACTOR=	9.58	K 100 FACTOR=	9.33	K-200 FACTOR	8.91	D FACTOR=	51.94
R020-Data		ON SR 017 S/O LEE ROAD - OTHELLO - MP 30.37									
AADT=	6,002	K 30 FACTOR=	9.88	K-50 FACTOR=	9.65	K 100 FACTOR=	9.23	K-200 FACTOR	8.80	D FACTOR=	53.32
R021-Data		ON SR 002 E/O WALTON AVENUE - SPOKANE - MP 289.79									
AADT=	42,561	K 30 FACTOR=	9.24	K-50 FACTOR=	9.13	K 100 FACTOR=	8.91	K-200 FACTOR	56.63	D FACTOR=	56.63
R023-Data		ON SR 101 S/O ORCAS AND HOLLAND DRIVES - DISCOVERY BAY - MP 281.15									
AADT=	10,913	K 30 FACTOR=	12.76	K-50 FACTOR=	12.05	K 100 FACTOR=	11.27	K-200 FACTOR	10.45	D FACTOR=	56.34

PEAK HOUR REPORT FOR PEAK 200 HOURS OF 2009--DATA SUMMARY

SITE	AADT	K-30 FACTOR	% OF ADT	K-50 FACTOR	% OF ADT	K-100 FACTOR	% OF ADT	K-200 FACTOR	% OF ADT	D-FACTOR	% OF ADT
R034-Data		ON SR 090 W/O SPRAGUE AVE I/C - SPOKANE/SPRAGUE AVE - MP 285.23									
AADT=	185,645	K 30 FACTOR=	7.45	K-50 FACTOR=	7.42	K 100 FACTOR=	7.33	K-200 FACTOR	7.20	D FACTOR=	53.39
R036-Data		ON SR 005 N/O So 56TH ST I/C - TACOMA/48TH ST - MP 131.18									
AADT=	107,345	K 30 FACTOR=	9.77	K-50 FACTOR=	9.67	K 100 FACTOR=	9.54	K-200 FACTOR	9.31	D FACTOR=	55.42
R037-Data		ON SR 020 W/O RADER ROAD - WINTHROP - MP 191.90									
AADT=	1,759	K 30 FACTOR=	25.18	K-50 FACTOR=	22.97	K 100 FACTOR=	20.01	K-200 FACTOR	17.23	D FACTOR=	59.49
R038-Data		ON SR 002 E/O NE OLD CASCADE HWY - SKYKOMISH - MP 50.12									
AADT=	4,903	K 30 FACTOR=	19.62	K-50 FACTOR=	18.74	K 100 FACTOR=	17.34	K-200 FACTOR	15.56	D FACTOR=	73.56
R039-Data		ON SR 090 W/O EDGEWICK ROAD I/C - NORTH BEND - MP 33.56									
AADT=	32,946	K 30 FACTOR=	14.67	K-50 FACTOR=	14.31	K 100 FACTOR=	13.24	K-200 FACTOR	12.07	D FACTOR=	62.57
R040N-Data		ON SR 123 N/O ENTRANCE/EXIT OHANAPECOSH CMPGRND - OHANAPECOSH - MP 3.88									
AADT=	0	K 30 FACTOR=	0.00	K-50 FACTOR=	0.00	K 100 FACTOR=	0.00	K-200 FACTOR	0.00	D FACTOR=	0.00
R040W-Data		ON SR 012 W/O COAL CREEK BRIDGE - PACKWOOD - MP 135.10									
AADT=	1,814	K 30 FACTOR=	26.30	K-50 FACTOR=	23.81	K 100 FACTOR=	20.89	K-200 FACTOR	17.36	D FACTOR=	55.17
R041-Data		ON SR 097 N/O STATE FRONTAGE RD - GOLDENDALE - MP 13.41									
AADT=	4,769	K 30 FACTOR=	14.59	K-50 FACTOR=	13.00	K 100 FACTOR=	11.87	K-200 FACTOR	10.72	D FACTOR=	53.74
R042-Data		ON SR 090 E/O WB OFF RAMP TO WANAPUM ROAD - VANTAGE - MP 136.59									
AADT=	14,287	K 30 FACTOR=	17.40	K-50 FACTOR=	16.65	K 100 FACTOR=	15.03	K-200 FACTOR	13.50	D FACTOR=	60.55
R043-Data		ON SR 105 E/O SR 105 WYE CONN - WESTPORT - MP 30.73									
AADT=	5,497	K 30 FACTOR=	12.63	K-50 FACTOR=	12.22	K 100 FACTOR=	11.46	K-200 FACTOR	10.66	D FACTOR=	56.12
R044-Data		ON SR 016 W/O TACOMA NARROWS BRIDGE - NARROWS BRIDGE - MP 8.43									
AADT=	78,925	K 30 FACTOR=	8.77	K-50 FACTOR=	8.69	K 100 FACTOR=	8.56	K-200 FACTOR	8.40	D FACTOR=	61.36
R045-Data		ON SR 005 S/O SR 503 I/C - WOODLAND -MP 20.14									
AADT=	0	K 30 FACTOR=	0.00	K-50 FACTOR=	0.00	K 100 FACTOR=	0.00	K-200 FACTOR	0.00	D FACTOR=	0.00
R046-Data		ON SR 005 N.SR 520 I/C - MP 168.84									
AADT=	0	K 30 FACTOR=	0.00	K-50 FACTOR=	0.00	K 100 FACTOR=	0.00	K-200 FACTOR	0.00	D FACTOR=	0.00
R047E-Data		ON SR 002 E/O SR 097 - DRYDEN - MP 104.84									
AADT=	14,784	K 30 FACTOR=	13.18	K-50 FACTOR=	12.75	K 100 FACTOR=	12.07	K-200 FACTOR	11.10	D FACTOR=	58.67
R047S-Data		ON SR 097 S/O SR 2 - BLEWETT - MP 178.19									
AADT=	5,167	K 30 FACTOR=	18.52	K-50 FACTOR=	17.55	K 100 FACTOR=	15.73	K-200 FACTOR	14.21	D FACTOR=	64.94
R047W-Data		ON SR 002 W/O GREEN AND SAUNDERS ROADS - PESHASTIN - MP 103.92									
AADT=	12,169	K 30 FACTOR=	12.60	K-50 FACTOR=	12.24	K 100 FACTOR=	11.69	K-200 FACTOR	10.96	D FACTOR=	53.29
R048-Data		ON SR 082 E/O SELAH CR REST AREA ON RAMP - SELAH - MP 24.83									
AADT=	15,896	K 30 FACTOR=	11.87	K-50 FACTOR=	11.47	K 100 FACTOR=	11.03	K-200 FACTOR	10.24	D FACTOR=	53.48
R050-Data		ON SR 003 N/O NEWBERRY HILL I/C - SILVERDALE - MP 44.33									
AADT=	42,748	K 30 FACTOR=	9.98	K-50 FACTOR=	9.86	K 100 FACTOR=	9.71	K-200 FACTOR	9.46	D FACTOR=	51.95

PEAK HOUR REPORT FOR PEAK 200 HOURS OF 2009--DATA SUMMARY

SITE	AADT	K-30 FACTOR	% OF ADT	K-50 FACTOR	% OF ADT	K-100 FACTOR	% OF ADT	K-200 FACTOR	% OF ADT	D-FACTOR	% OF ADT
R051-Data		ON SR 205 N/O MILL PLAIN ROAD I/C - MILL PLAIN - MP 28.84									
AADT=	107,856	K 30 FACTOR=	8.18	K-50 FACTOR=	8.04	K 100 FACTOR=	7.86	K-200 FACTOR	7.50	D FACTOR=	54.39
R052-Data		ON SR 002 E/O SR 005 I/C - EVERETT - MP 0.26									
AADT=	71,855	K 30 FACTOR=	8.52	K-50 FACTOR=	8.42	K 100 FACTOR=	8.24	K-200 FACTOR	7.93	D FACTOR=	64.88
R053-Data		ON SR 002 E/O SR 97 AR I/C (OLDS BR) - WENATCHEE - MP 119.77									
AADT=	20,326	K 30 FACTOR=	10.98	K-50 FACTOR=	10.66	K 100 FACTOR=	10.23	K-200 FACTOR	9.79	D FACTOR=	56.44
R054-Data		ON SR 101 S/O HENSEL ROAD - HUMPTULIPS - MP 104.55									
AADT=	2,153	K 30 FACTOR=	11.66	K-50 FACTOR=	11.10	K 100 FACTOR=	10.13	K-200 FACTOR	8.50	D FACTOR=	54.66
R055-Data		ON SR 090 E/O SR 17 I/C - MOSES LAKE - MP 180.33									
AADT=	10,714	K 30 FACTOR=	14.46	K-50 FACTOR=	13.46	K 100 FACTOR=	12.00	K-200 FACTOR	10.71	D FACTOR=	53.27
R057-Data		ON SR 970 W/O TEANAWAY RD - TEANAWAY - MP 6.85									
AADT=	4,123	K 30 FACTOR=	20.16	K-50 FACTOR=	18.60	K 100 FACTOR=	16.74	K-200 FACTOR	14.70	D FACTOR=	67.97
R058-Data		ON SR 002 E/O NASON RIDGE ROAD - NASON CREEK - MP 80.20									
AADT=	4,037	K 30 FACTOR=	22.27	K-50 FACTOR=	21.35	K 100 FACTOR=	19.79	K-200 FACTOR	17.22	D FACTOR=	70.36
R059-Data		ON SR 097 S/O ROCKY REACH DAM ROAD - ROCKY REACH - MP 201.53									
AADT=	6,870	K 30 FACTOR=	14.43	K-50 FACTOR=	13.86	K 100 FACTOR=	12.94	K-200 FACTOR	11.89	D FACTOR=	59.35
R060-Data		ON SR 005 W/O SR 510 I/C - LACEY - MP 111.01									
AADT=	113,492	K 30 FACTOR=	8.40	K-50 FACTOR=	8.26	K 100 FACTOR=	8.09	K-200 FACTOR	7.87	D FACTOR=	51.87
R061-Data		ON SR 395 N/O E ELM RD - ELTOPIA - MP 36.24									
AADT=	13,342	K 30 FACTOR=	10.66	K-50 FACTOR=	10.31	K 100 FACTOR=	9.80	K-200 FACTOR	9.11	D FACTOR=	52.41
R062-Data		ON SR 240 W/O COLUMBIA PARK TRAIL - RICHLAND - MP 37.2									
AADT=	64,399	K 30 FACTOR=	11.38	K-50 FACTOR=	11.24	K 100 FACTOR=	10.91	K-200 FACTOR	10.33	D FACTOR=	60.20
R063-Data		ON SR 395 S/O SR 292 - LOON LAKE - MP 190.29									
AADT=	8,171	K 30 FACTOR=	10.89	K-50 FACTOR=	10.41	K 100 FACTOR=	9.78	K-200 FACTOR	9.06	D FACTOR=	56.63
R064-Data		ON SR 002 W/O HARMES RD - DAVENPORT - MP 250.50									
AADT=	2,745	K 30 FACTOR=	12.35	K-50 FACTOR=	12.06	K 100 FACTOR=	11.44	K-200 FACTOR	10.60	D FACTOR=	55.22
R066-Data		ON SR 026 E/O SR 017 I/C - OTHELLO EAST - MP 43.06									
AADT=	2,576	K 30 FACTOR=	20.42	K-50 FACTOR=	17.51	K 100 FACTOR=	14.44	K-200 FACTOR	12.42	D FACTOR=	62.65
R067-Data		ON SR 012 AT PATAHA CREEK BRIDGE - DODGE JCT. - MP 390.66									
AADT=	1,955	K 30 FACTOR=	14.02	K-50 FACTOR=	13.61	K 100 FACTOR=	12.79	K-200 FACTOR	11.76	D FACTOR=	55.64
R068-Data		ON SR 097 N/O COPPLE RD - OMAK - MP 293.42									
AADT=	5,316	K 30 FACTOR=	11.00	K-50 FACTOR=	10.55	K 100 FACTOR=	10.03	K-200 FACTOR	9.57	D FACTOR=	57.27
R069-Data		ON SR 101 AT WEIGH STATION-PORT ANGELES - MP 254.35									
AADT=	21,919	K 30 FACTOR=	10.26	K-50 FACTOR=	10.07	K 100 FACTOR=	9.74	K-200 FACTOR	9.28	D FACTOR=	54.42
R070-Data		ON SR 395 E/O SR 25 KETTLE FALLS - MP 234.57									
AADT=	7,424	K 30 FACTOR=	10.59	K-50 FACTOR=	10.39	K 100 FACTOR=	10.09	K-200 FACTOR	9.75	D FACTOR=	53.63

PEAK HOUR REPORT FOR PEAK 200 HOURS OF 2009--DATA SUMMARY

SITE	AADT	K-30 FACTOR	% OF ADT	K-50 FACTOR	% OF ADT	K-100 FACTOR	% OF ADT	K-200 FACTOR	% OF ADT	D-FACTOR	% OF ADT
R073-Data		ON SR 101 E/O SR 113/BURNT MTN RD - SAPPHO - MP 203.93									
AADT=	2,578	K 30 FACTOR=	14.20	K-50 FACTOR=	13.69	K 100 FACTOR=	13.03	K-200 FACTOR	12.10	D FACTOR=	55.56
R074-Data		ON SR 101 N/O SR 4 - NEMAH - MP 28.95									
AADT=	2,267	K 30 FACTOR=	21.97	K-50 FACTOR=	20.11	K 100 FACTOR=	16.76	K-200 FACTOR	14.47	D FACTOR=	61.04
R075-Data		ON SR 012 E/O KENNEDY ROAD-SALKUM - MP 77.78									
AADT=	6,541	K 30 FACTOR=	12.70	K-50 FACTOR=	12.22	K 100 FACTOR=	11.34	K-200 FACTOR	10.43	D FACTOR=	56.87
R076-Data		ON SR 014 W/O SR 014 MARYHILL SPUR - MARYHILL - MP 100.64									
AADT=	2,022	K 30 FACTOR=	15.23	K-50 FACTOR=	13.95	K 100 FACTOR=	12.86	K-200 FACTOR	11.67	D FACTOR=	54.51
R077-Data		ON SR 014 W/O MARYHILL ROAD - STONEHENGE - MP 102.27									
AADT=	1,951	K 30 FACTOR=	5.13	K-50 FACTOR=	4.87	K 100 FACTOR=	4.31	K-200 FACTOR	3.28	D FACTOR=	56.25
R078-Data		ON SR 004 W/O SR 432 & COAL CREEK RD - LONGVIEW/SR4 - MP 55.05									
AADT=	5,083	K 30 FACTOR=	10.31	K-50 FACTOR=	9.92	K 100 FACTOR=	9.38	K-200 FACTOR	8.83	D FACTOR=	56.92
R081-Data		ON SR 182 AT COLUMBIA RIVER BRIDGE - PASCO - MP 6.34									
AADT=	53,828	K 30 FACTOR=	10.58	K-50 FACTOR=	10.26	K 100 FACTOR=	9.86	K-200 FACTOR	9.13	D FACTOR=	58.31
R083-Data		SR 009 N/O 269TH PLACE NE - ARLINGTON - MP 32.98									
AADT=	1,965	K 30 FACTOR=	15.22	K-50 FACTOR=	14.45	K 100 FACTOR=	13.18	K-200 FACTOR	12.01	D FACTOR=	59.07
R084-Data		ON SR 097 N/O BRAYS ROAD - ORONDO - MP 220.55									
AADT=	4,065	K 30 FACTOR=	13.09	K-50 FACTOR=	12.62	K 100 FACTOR=	11.86	K-200 FACTOR	10.82	D FACTOR=	59.87
R085-Data		ON SR 104 AT HOOD CANAL BRIDGE - HOOD CANAL BRIDGE - MP 13.92									
AADT=	16,011	K 30 FACTOR=	11.67	K-50 FACTOR=	11.25	K 100 FACTOR=	10.52	K-200 FACTOR	9.82	D FACTOR=	56.80
R086-Data		ON SR 082 S/O SR 14 I/C - UMATILLA - MP 132.03									
AADT=	17,158	K 30 FACTOR=	10.96	K-50 FACTOR=	10.57	K 100 FACTOR=	10.04	K-200 FACTOR	9.45	D FACTOR=	52.04
R087-Data		ON SR 395 AT COLUMBIA RIVER BRIDGE - KENNEWICK - MP 18.58									
AADT=	0	K 30 FACTOR=	0.00	K-50 FACTOR=	0.00	K 100 FACTOR=	0.00	K-200 FACTOR	0.00	D FACTOR=	0.00
R088-Data		ON 016 W/O SR 302 PURDY SPUR - BURLEY - MP 18.65									
AADT=	42,310	K 30 FACTOR=	8.90	K-50 FACTOR=	8.78	K 100 FACTOR=	8.58	K-200 FACTOR	8.32	D FACTOR=	53.22
R089-Data		ON SR 003 S/O LAKE FLORA RD - BELFAIR - MP 28.68									
AADT=	17,113	K 30 FACTOR=	9.54	K-50 FACTOR=	9.43	K 100 FACTOR=	9.17	K-200 FACTOR	8.85	D FACTOR=	61.63
R090-Data		ON SR 007 N/O 38TH ST. I/C - TACOMA/SR7/38TH ST - 58.29									
AADT=	23,105	K 30 FACTOR=	9.15	K-50 FACTOR=	8.96	K 100 FACTOR=	8.63	K-200 FACTOR	8.21	D FACTOR=	61.91
R091-Data		ON SR 005 N/O DUPONT I/C - DUPONT - MP 119.31									
AADT=	118,013	K 30 FACTOR=	8.02	K-50 FACTOR=	7.96	K 100 FACTOR=	7.84	K-200 FACTOR	7.70	D FACTOR=	54.49
R092-Data		ON SR 005 S/O SR 512 I/C - LAKEWOOD/BRIDGEPORT WAY - MP 126.76									
AADT=	0	K 30 FACTOR=	0.00	K-50 FACTOR=	0.00	K 100 FACTOR=	0.00	K-200 FACTOR	0.00	D FACTOR=	0.00
R093-Data		ON SR 005 N/O SR 536 I/C - MOUNT VERNON - MP 226.96									
AADT=	66,554	K 30 FACTOR=	9.18	K-50 FACTOR=	9.04	K 100 FACTOR=	8.77	K-200 FACTOR	8.46	D FACTOR=	51.91

PEAK HOUR REPORT FOR PEAK 200 HOURS OF 2009--DATA SUMMARY

SITE	AADT	K-30 FACTOR	% OF ADT	K-50 FACTOR	% OF ADT	K-100 FACTOR	% OF ADT	K-200 FACTOR	% OF ADT	D-FACTOR	% OF ADT
R094-Data		ON SR 005 AT 236TH ST NE UXING - SYLVANNA - MP 210.30									
AADT=	71,695	K 30 FACTOR=	8.93	K-50 FACTOR=	8.72	K 100 FACTOR=	8.37	K-200 FACTOR	8.01	D FACTOR=	53.71
R095-Data		ON SR 104 W/O OLD PORT GAMBLE RD WYE CONN - PORT GAMBLE - MP 19.48									
AADT=	5,256	K 30 FACTOR=	12.75	K-50 FACTOR=	12.31	K 100 FACTOR=	11.47	K-200 FACTOR	10.73	D FACTOR=	55.57
R096-Data		ON SR 307 S/O NE GUNDERSON RD - POULSBO - MP 2.31									
AADT=	15,393	K 30 FACTOR=	10.02	K-50 FACTOR=	9.80	K 100 FACTOR=	9.53	K-200 FACTOR	9.17	D FACTOR=	58.12
R097-Data		ON SR 005 S/O TUMWATER BLVD - TUMWATER BLVD - MP 100.54									
AADT=	68,903	K 30 FACTOR=	9.26	K-50 FACTOR=	9.05	K 100 FACTOR=	8.81	K-200 FACTOR	8.51	D FACTOR=	52.55
R098-Data		ON SR 101 E/O OLYMPIA/COOPER POINT RD - OLYMPIA/COOPER POINT - MP 366.69									
AADT=	96,528	K 30 FACTOR=	9.08	K-50 FACTOR=	9.02	K 100 FACTOR=	8.89	K-200 FACTOR	8.75	D FACTOR=	52.99
R099-Data		ON SR 005 N/O DESHUTESPRKWY OFF RMP - TUMWATER/CUSTER WAY - MP 103.98									
AADT=	95,564	K 30 FACTOR=	9.05	K-50 FACTOR=	8.87	K 100 FACTOR=	8.73	K-200 FACTOR	8.58	D FACTOR=	51.35
R100-Data		ON SR 017 N/O SR 172 I/C - MANSFIELD - MP 112.25									
AADT=	554	K 30 FACTOR=	13.18	K-50 FACTOR=	12.64	K 100 FACTOR=	11.73	K-200 FACTOR	10.83	D FACTOR=	58.44
R101-Data		ON SR 099 N/O SPOKANE ST BRIDGE- SEATTLE/ALASKAN WAY - MP 29.37									
AADT=	73,176	K 30 FACTOR=	11.07	K-50 FACTOR=	11.01	K 100 FACTOR=	10.75	K-200 FACTOR	10.34	D FACTOR=	53.84
R104-Data		ON SR 005 S/O 13TH ST I/C - CHEHALIS - MP 75.35									
AADT=	59,548	K 30 FACTOR=	9.46	K-50 FACTOR=	9.14	K 100 FACTOR=	8.73	K-200 FACTOR	8.26	D FACTOR=	52.87
R17R-Data		ON SR 90 E/O MT BAKER TUNNEL - I-90 E end OF MT BAKER TUNNEL - MP 4.22									
AADT=	11,530	K 30 FACTOR=	27.48	K-50 FACTOR=	26.63	K 100 FACTOR=	24.56	K-200 FACTOR	15.87	D FACTOR=	50.00
R49R-Data		ON SR 005 AT E. ROANOKE ST UXING - MP 167.35									
AADT=	44,707	K 30 FACTOR=	11.75	K-50 FACTOR=	11.62	K 100 FACTOR=	11.42	K-200 FACTOR	11.08	D FACTOR=	50.01
S103-Data		ON SR 285 AT COLUMBIA RIVER BR -- E. WENATCHEE - BRIDGE MP 0.39									
AADT=	0	K 30 FACTOR=	0.00	K-50 FACTOR=	0.00	K 100 FACTOR=	0.00	K-200 FACTOR	0.00	D FACTOR=	0.00
S205-Data		ON I-5 S/O I-405/SR518 I/C - I-5 S/O I-405/SR518 I/C - MP 152.82									
AADT=	207,015	K 30 FACTOR=	7.83	K-50 FACTOR=	7.78	K 100 FACTOR=	7.68	K-200 FACTOR	7.54	D FACTOR=	58.02
S503-Data		ON SR 433 AT COLUMBIA RIVER BRDG - LONGVIEW BRIDGE - MP 0.70									
AADT=	19,542	K 30 FACTOR=	10.62	K-50 FACTOR=	10.36	K 100 FACTOR=	9.91	K-200 FACTOR	9.40	D FACTOR=	52.17
S533-Data		ON SR 520 W/O 148TH AVE NE I/C - SEATTLE/SR 520 E/O SR I-405 - MP 7.93									
AADT=	97,510	K 30 FACTOR=	8.49	K-50 FACTOR=	8.42	K 100 FACTOR=	8.28	K-200 FACTOR	8.06	D FACTOR=	55.58
S612-Data		ON SR 024 AT COLUMBIA RVR BRIDGE - VERNITA - MP 43.50									
AADT=	3,666	K 30 FACTOR=	11.67	K-50 FACTOR=	11.27	K 100 FACTOR=	10.69	K-200 FACTOR	9.98	D FACTOR=	54.71
S706-Data		ON SR 020 E/O RHODODENDRON PARK DR - COUPEVILLE - MP 20.02									
AADT=	8,479	K 30 FACTOR=	10.50	K-50 FACTOR=	10.33	K 100 FACTOR=	9.97	K-200 FACTOR	9.58	D FACTOR=	57.16
S803-Data		ON SR 005 S/O BIRCH BAY/LYNDEN RD I/C - CUSTER - MP 269.41									
AADT=	27,032	K 30 FACTOR=	9.32	K-50 FACTOR=	9.14	K 100 FACTOR=	8.88	K-200 FACTOR	8.56	D FACTOR=	55.03

PEAK HOUR REPORT FOR PEAK 200 HOURS OF 2009--DATA SUMMARY

SITE	AADT	K-30 FACTOR	% OF ADT	K-50 FACTOR	% OF ADT	K-100 FACTOR	% OF ADT	K-200 FACTOR	% OF ADT	D-FACTOR	% OF ADT
S809-Data		ON SR 005 S/O SR 516 I/C - MIDWAY - MP 148.07									
AADT=	191,400	K 30 FACTOR=	7.79	K-50 FACTOR=	7.74	K 100 FACTOR=	7.64	K-200 FACTOR	7.52	D FACTOR=	61.85
S818E-Data		ON SR 012 EAST OF SR 410 - NACHES - MP 185.62									
AADT=	4,209	K 30 FACTOR=	20.67	K-50 FACTOR=	19.58	K 100 FACTOR=	17.84	K-200 FACTOR	15.06	D FACTOR=	56.92
S818S-Data		ON SR 012 S/O SR 410 I/C - WHITE PASS - MP 185.25									
AADT=	2,121	K 30 FACTOR=	23.39	K-50 FACTOR=	21.07	K 100 FACTOR=	18.01	K-200 FACTOR	15.18	D FACTOR=	59.29
S818W-Data		ON SR 410 W/O SR 012 - CHINOOK PASS - MP 116.26									
AADT=	1,950	K 30 FACTOR=	19.38	K-50 FACTOR=	18.51	K 100 FACTOR=	16.51	K-200 FACTOR	13.85	D FACTOR=	54.76
S819-Data		ON SR 411 S/O SANDY BEND RD - LEXINGTON - MP 7.97									
AADT=	3,651	K 30 FACTOR=	10.96	K-50 FACTOR=	10.52	K 100 FACTOR=	10.05	K-200 FACTOR	9.61	D FACTOR=	62.86
S820-Data		ON SR 020 W/O FAIRGROUNDS ROAD-REPUBLIC - MP 304.60									
AADT=	2,263	K 30 FACTOR=	13.26	K-50 FACTOR=	12.59	K 100 FACTOR=	11.58	K-200 FACTOR	10.74	D FACTOR=	53.94
S822-Data		ON SR 405 N/O SR 908 I/C - I-405 N/O SR 908 I/C - MP 18.71									
AADT=	0	K 30 FACTOR=	0.00	K-50 FACTOR=	0.00	K 100 FACTOR=	0.00	K-200 FACTOR	0.00	D FACTOR=	0.00
S824-Data		ON SR 405 N/O SR 527 I/C - BOTHELL - 28.99									
AADT=	111,033	K 30 FACTOR=	8.46	K-50 FACTOR=	8.40	K 100 FACTOR=	8.32	K-200 FACTOR	8.17	D FACTOR=	52.09
S825-Data		ON SR 090 W/O SR 900 I/C - ISSAQUAH - MP 14.65									
AADT=	119,100	K 30 FACTOR=	8.09	K-50 FACTOR=	7.52	K 100 FACTOR=	6.97	K-200 FACTOR	6.08	D FACTOR=	62.22
S826-Data		ON SR 090 E/O 82ND ST I/C - PRESTON - MP 23.54									
AADT=	0	K 30 FACTOR=	0.00	K-50 FACTOR=	0.00	K 100 FACTOR=	0.00	K-200 FACTOR	0.00	D FACTOR=	0.00
S837-Data		ON SR 005 S/O SR 99 I/C - FIFE - MP 136.80									
AADT=	182,204	K 30 FACTOR=	7.24	K-50 FACTOR=	7.18	K 100 FACTOR=	7.10	K-200 FACTOR	7.02	D FACTOR=	53.64
S838-Data		ON SR 018 S/O SR 90 - ECHO GLEN - MP 27.62									
AADT=	21,277	K 30 FACTOR=	11.42	K-50 FACTOR=	11.13	K 100 FACTOR=	10.51	K-200 FACTOR	9.85	D FACTOR=	57.00
S839-Data		ON SR 599 E/O SR 099 I/C - TUKWILLA - MP 1.40									
AADT=	39,926	K 30 FACTOR=	9.77	K-50 FACTOR=	9.69	K 100 FACTOR=	9.57	K-200 FACTOR	9.41	D FACTOR=	64.11
S840-Data		ON SR 504 E/O PRIVATE ROAD 1900 - KID VALLEY MP 19.43									
AADT=	731	K 30 FACTOR=	37.35	K-50 FACTOR=	34.34	K 100 FACTOR=	29.27	K-200 FACTOR	24.21	D FACTOR=	71.43
S841W-Data		ON SR 101 NW/O SR 401 - ASTORIA/CHINOOK MP 0.47									
AADT=	0	K 30 FACTOR=	0.00	K-50 FACTOR=	0.00	K 100 FACTOR=	0.00	K-200 FACTOR	0.00	D FACTOR=	0.00
S901-Data		ON SR 090 AT TINKHAM ROAD UXING - TINKHAM RD - MP 47.71									
AADT=	30,170	K 30 FACTOR=	13.72	K-50 FACTOR=	13.25	K 100 FACTOR=	12.12	K-200 FACTOR	10.54	D FACTOR=	61.78
S902-Data		ON SR 090 AT SR 906 OXING - SNOQUALMIE - MP 52.24									
AADT=	27,535	K 30 FACTOR=	14.12	K-50 FACTOR=	13.75	K 100 FACTOR=	12.61	K-200 FACTOR	10.93	D FACTOR=	62.16
S903-Data		ON SR 090 AT CABIN CREEK ROAD UXING - CABIN CREEK - MP 63.98									
AADT=	0	K 30 FACTOR=	0.00	K-50 FACTOR=	0.00	K 100 FACTOR=	0.00	K-200 FACTOR	0.00	D FACTOR=	0.00

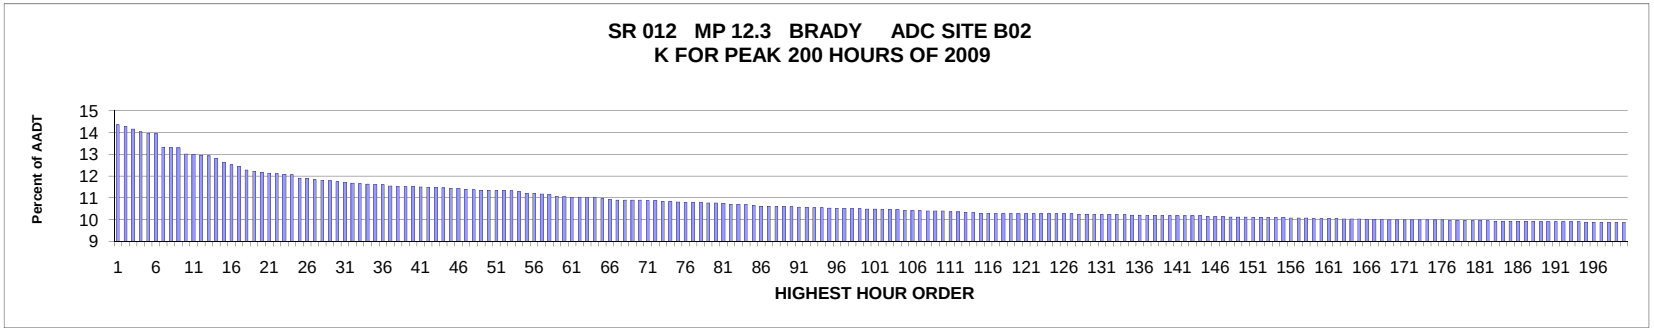

AADT= 20042 **K 30 FACTOR=** 11.73 **K 100 FACTOR=** 10.49 **K 200 FACTOR=** 9.86 **D FACTOR=** 60.47

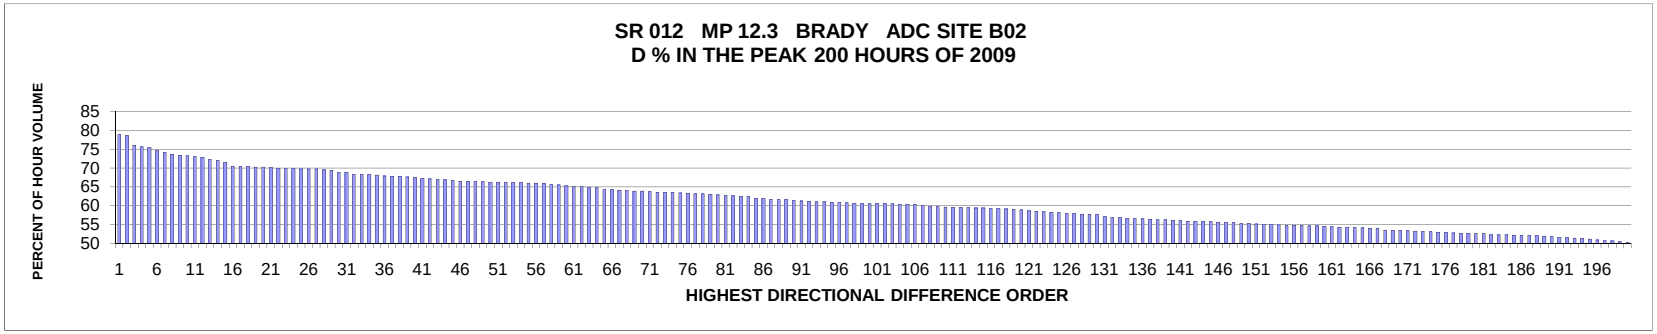

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	5	9	1	14	2876	14.35	1	20042	2105	771	73.19	26.81
7	5	9	1	15	2859	14.27	2		2120	739	74.15	25.85
7	26	9	1	14	2838	14.16	3		1734	1104	61.1	38.9
7	26	9	1	13	2809	14.02	4		1572	1237	55.96	44.04
7	5	9	1	13	2796	13.95	5		2041	755	73	27
7	5	9	1	16	2794	13.94	6		2108	686	75.45	24.55
7	3	9	6	12	2669	13.32	7		800	1869	29.97	70.03
7	3	9	6	13	2666	13.3	8		845	1821	31.7	68.3
7	3	9	6	15	2664	13.29	9		806	1858	30.26	69.74
7	26	9	1	15	2610	13.02	10		1728	882	66.21	33.79
7	26	9	1	12	2606	13	11		1437	1169	55.14	44.86
7	5	9	1	12	2596	12.95	12		1905	691	73.38	26.62
7	3	9	6	14	2592	12.93	13		857	1735	33.06	66.94
8	2	9	1	14	2566	12.8	14		1532	1034	59.7	40.3
8	2	9	1	13	2532	12.63	15		1503	1029	59.36	40.64
7	5	9	1	17	2508	12.51	16		1907	601	76.04	23.96
8	16	9	1	14	2494	12.44	17		1538	956	61.67	38.33

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	3	9	6	16	2462	12.28	18		830	1632	33.71	66.29
8	23	9	1	15	2449	12.22	19		1587	862	64.8	35.2
7	25	9	7	12	2439	12.17	20		785	1654	32.19	67.81
2	7	9	7	14	2432	12.13	21	20042	641	1791	26.36	73.64
8	16	9	1	13	2427	12.11	22		1485	942	61.19	38.81
7	26	9	1	16	2420	12.07	23		1594	826	65.87	34.13
5	25	9	2	13	2415	12.05	24		1684	731	69.73	30.27
8	23	9	1	14	2385	11.9	25		1523	862	63.86	36.14
7	19	9	1	13	2382	11.89	26		1491	891	62.59	37.41
5	25	9	2	14	2370	11.83	27		1695	675	71.52	28.48
8	7	9	6	15	2367	11.81	28		1055	1312	44.57	55.43
7	5	9	1	18	2361	11.78	29		1862	499	78.86	21.14
8	1	9	7	13	2351	11.73	30		985	1366	41.9	58.1
8	9	9	1	14	2349	11.72	31		1527	822	65.01	34.99
8	14	9	6	16	2340	11.68	32		1060	1280	45.3	54.7
7	3	9	6	11	2333	11.64	33		705	1628	30.22	69.78
7	19	9	1	14	2331	11.63	34		1488	843	63.84	36.16
7	24	9	6	16	2325	11.6	35		958	1367	41.2	58.8
7	3	9	6	17	2324	11.6	36		832	1492	35.8	64.2
8	23	9	1	13	2313	11.54	37		1460	853	63.12	36.88
7	31	9	6	15	2311	11.53	38		1062	1249	45.95	54.05
3	29	9	1	14	2309	11.52	39		1623	686	70.29	29.71
7	31	9	6	16	2309	11.52	40		1048	1261	45.39	54.61
8	9	9	1	13	2305	11.5	41	20042	1455	850	63.12	36.88
8	7	9	6	17	2302	11.49	42		1091	1211	47.39	52.61
8	2	9	1	15	2300	11.48	43		1398	902	60.78	39.22
7	26	9	1	17	2294	11.45	44		1578	716	68.79	31.21
3	29	9	1	13	2292	11.44	45		1563	729	68.19	31.81
8	28	9	6	16	2289	11.42	46		1067	1222	46.61	53.39
8	16	9	1	15	2285	11.4	47		1432	853	62.67	37.33
7	12	9	1	14	2277	11.36	48		1504	773	66.05	33.95
7	24	9	6	14	2274	11.35	49		928	1346	40.81	59.19
7	25	9	7	13	2274	11.35	50		829	1445	36.46	63.54
7	31	9	6	18	2272	11.34	51		1093	1179	48.11	51.89
8	14	9	6	15	2272	11.34	52		995	1277	43.79	56.21
7	26	9	1	18	2268	11.32	53		1593	675	70.24	29.76
8	2	9	1	12	2260	11.28	54		1256	1004	55.58	44.42
8	2	9	1	16	2245	11.2	55		1471	774	65.52	34.48
8	7	9	6	16	2245	11.2	56		940	1305	41.87	58.13
8	9	9	1	15	2241	11.18	57		1412	829	63.01	36.99
7	24	9	6	13	2232	11.14	58		980	1252	43.91	56.09
8	30	9	1	14	2219	11.07	59		1473	746	66.38	33.62
3	29	9	1	15	2213	11.04	60		1557	656	70.36	29.64
5	25	9	2	15	2210	11.03	61	20042	1648	562	74.57	25.43
8	1	9	7	12	2209	11.02	62		903	1306	40.88	59.12
8	21	9	6	17	2207	11.01	63		1017	1190	46.08	53.92
7	31	9	6	14	2206	11.01	64		1055	1151	47.82	52.18
7	24	9	6	17	2199	10.97	65		995	1204	45.25	54.75
7	17	9	6	16	2190	10.93	66		952	1238	43.47	56.53
7	2	9	5	16	2185	10.9	67		884	1301	40.46	59.54
8	2	9	1	17	2184	10.9	68		1444	740	66.12	33.88
8	8	9	7	13	2184	10.9	69		1107	1077	50.69	49.31

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	24	9	6	15	2182	10.89	70		918	1264	42.07	57.93
7	25	9	7	11	2178	10.87	71		690	1488	31.68	68.32
7	5	9	1	19	2176	10.86	72		1709	467	78.54	21.46
8	30	9	1	13	2172	10.84	73		1416	756	65.19	34.81
9	4	9	6	16	2169	10.82	74		876	1293	40.39	59.61
5	23	9	7	12	2166	10.81	75		696	1470	32.13	67.87
7	2	9	5	17	2165	10.8	76		963	1202	44.48	55.52
7	31	9	6	17	2161	10.78	77		1005	1156	46.51	53.49
7	25	9	7	18	2160	10.78	78		1384	776	64.07	35.93
7	12	9	1	13	2159	10.77	79		1460	699	67.62	32.38
8	21	9	6	16	2158	10.77	80		987	1171	45.74	54.26
8	15	9	7	12	2155	10.75	81	20042	847	1308	39.3	60.7
7	31	9	6	13	2147	10.71	82		1015	1132	47.28	52.72
5	25	9	2	12	2143	10.69	83		1432	711	66.82	33.18
7	19	9	1	16	2143	10.69	84		1361	782	63.51	36.49
7	25	9	7	16	2136	10.66	85		1114	1022	52.15	47.85
5	22	9	6	16	2129	10.62	86		869	1260	40.82	59.18
7	19	9	1	15	2129	10.62	87		1367	762	64.21	35.79
7	3	9	6	18	2125	10.6	88		829	1296	39.01	60.99
8	2	9	1	18	2124	10.6	89		1391	733	65.49	34.51
8	23	9	1	16	2121	10.58	90		1399	722	65.96	34.04
7	19	9	1	12	2118	10.57	91		1280	838	60.43	39.57
8	14	9	6	14	2117	10.56	92		974	1143	46.01	53.99
8	28	9	6	17	2115	10.55	93		1003	1112	47.42	52.58
3	29	9	1	16	2112	10.54	94		1467	645	69.46	30.54
8	23	9	1	12	2111	10.53	95		1283	828	60.78	39.22
7	17	9	6	15	2109	10.52	96		917	1192	43.48	56.52
9	12	9	7	12	2107	10.51	97		833	1274	39.53	60.47
7	18	9	7	12	2104	10.5	98		853	1251	40.54	59.46
12	31	9	5	15	2104	10.5	99		773	1331	36.74	63.26
5	22	9	6	18	2103	10.49	100		853	1250	40.56	59.44
8	30	9	1	15	2103	10.49	101	20042	1402	701	66.67	33.33
5	22	9	6	17	2098	10.47	102		830	1268	39.56	60.44
6	28	9	1	13	2098	10.47	103		1297	801	61.82	38.18
4	24	9	6	16	2094	10.45	104		800	1294	38.2	61.8
7	24	9	6	18	2088	10.42	105		922	1166	44.16	55.84
7	17	9	6	18	2087	10.41	106		997	1090	47.77	52.23
9	4	9	6	18	2086	10.41	107		827	1259	39.65	60.35
6	28	9	1	15	2083	10.39	108		1374	709	65.96	34.04
10	9	9	6	17	2083	10.39	109		936	1147	44.94	55.06
8	7	9	6	18	2082	10.39	110		1038	1044	49.86	50.14
2	7	9	7	13	2074	10.35	111		674	1400	32.5	67.5
2	7	9	7	15	2074	10.35	112		625	1449	30.14	69.86
8	16	9	1	17	2072	10.34	113		1313	759	63.37	36.63
8	16	9	1	16	2071	10.33	114		1293	778	62.43	37.57
8	28	9	6	15	2063	10.29	115		946	1117	45.86	54.14
7	2	9	5	14	2061	10.28	116		814	1247	39.5	60.5
7	2	9	5	15	2060	10.28	117		816	1244	39.61	60.39
2	6	9	6	14	2059	10.27	118		613	1446	29.77	70.23
8	21	9	6	15	2059	10.27	119		911	1148	44.24	55.76
8	21	9	6	14	2058	10.27	120		922	1136	44.8	55.2
9	4	9	6	17	2058	10.27	121	20042	818	1240	39.75	60.25

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	6	9	2	14	2057	10.26	122		1307	750	63.54	36.46
7	17	9	6	14	2057	10.26	123		940	1117	45.7	54.3
8	16	9	1	12	2057	10.26	124		1203	854	58.48	41.52
9	4	9	6	15	2057	10.26	125		843	1214	40.98	59.02
5	23	9	7	14	2056	10.26	126		694	1362	33.75	66.25
8	6	9	5	16	2056	10.26	127		1062	994	51.65	48.35
8	8	9	7	14	2055	10.25	128		1067	988	51.92	48.08
2	6	9	6	17	2054	10.25	129		1081	973	52.63	47.37
9	7	9	2	14	2053	10.24	130		1413	640	68.83	31.17
8	6	9	5	17	2052	10.24	131		1120	932	54.58	45.42
8	14	9	6	17	2051	10.23	132		908	1143	44.27	55.73
7	4	9	7	13	2050	10.23	133		694	1356	33.85	66.15
7	25	9	7	14	2048	10.22	134		864	1184	42.19	57.81
9	7	9	2	13	2047	10.21	135		1479	568	72.25	27.75
8	7	9	6	13	2046	10.21	136		1032	1014	50.44	49.56
6	26	9	6	15	2043	10.19	137		819	1224	40.09	59.91
7	26	9	1	19	2043	10.19	138		1426	617	69.8	30.2
9	11	9	6	17	2043	10.19	139		999	1044	48.9	51.1
7	30	9	5	14	2041	10.18	140		993	1048	48.65	51.35
6	28	9	1	14	2040	10.18	141	20042	1255	785	61.52	38.48
3	27	9	6	17	2039	10.17	142		861	1178	42.23	57.77
8	1	9	7	14	2039	10.17	143		861	1178	42.23	57.77
7	2	9	5	13	2038	10.17	144		783	1255	38.42	61.58
5	23	9	7	13	2033	10.14	145		684	1349	33.64	66.36
5	25	9	2	16	2031	10.13	146		1463	568	72.03	27.97
9	11	9	6	18	2031	10.13	147		1004	1027	49.43	50.57
7	5	9	1	11	2029	10.12	148		1534	495	75.6	24.4
8	21	9	6	18	2029	10.12	149		958	1071	47.22	52.78
9	11	9	6	16	2027	10.11	150		915	1112	45.14	54.86
4	26	9	1	14	2025	10.1	151		1427	598	70.47	29.53
9	13	9	1	13	2025	10.1	152		1273	752	62.86	37.14
10	16	9	6	15	2025	10.1	153		729	1296	36	64
8	9	9	1	16	2024	10.1	154		1262	762	62.35	37.65
9	12	9	7	13	2023	10.09	155		801	1222	39.59	60.41
8	23	9	1	17	2021	10.08	156		1369	652	67.74	32.26
5	24	9	1	13	2020	10.08	157		981	1039	48.56	51.44
9	13	9	1	14	2018	10.07	158		1356	662	67.2	32.8
7	2	9	5	18	2013	10.04	159		964	1049	47.89	52.11
7	10	9	6	17	2013	10.04	160		938	1075	46.6	53.4
7	4	9	7	12	2012	10.04	161	20042	641	1371	31.86	68.14
10	9	9	6	16	2012	10.04	162		905	1107	44.98	55.02
5	22	9	6	15	2010	10.03	163		833	1177	41.44	58.56
7	11	9	7	14	2010	10.03	164		947	1063	47.11	52.89
7	31	9	6	12	2010	10.03	165		980	1030	48.76	51.24
4	26	9	1	13	2009	10.02	166		1394	615	69.39	30.61
8	5	9	4	16	2006	10.01	167		1093	913	54.49	45.51
4	24	9	6	18	2004	10	168		860	1144	42.91	57.09
3	27	9	6	16	2003	9.99	169		776	1227	38.74	61.26
8	21	9	6	13	2003	9.99	170		935	1068	46.68	53.32
12	31	9	5	16	2003	9.99	171		728	1275	36.35	63.65
5	22	9	6	14	2002	9.99	172		807	1195	40.31	59.69
6	28	9	1	16	2002	9.99	173		1304	698	65.13	34.87

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	18	9	7	13	2001	9.98	174		872	1129	43.58	56.42
7	25	9	7	17	2001	9.98	175		1124	877	56.17	43.83
9	7	9	2	15	2001	9.98	176		1330	671	66.47	33.53
2	6	9	6	18	1997	9.96	177		1084	913	54.28	45.72
2	7	9	7	19	1997	9.96	178		1453	544	72.76	27.24
9	25	9	6	17	1996	9.96	179		957	1039	47.95	52.05
6	26	9	6	16	1995	9.95	180		862	1133	43.21	56.79
7	30	9	5	16	1994	9.95	181	20042	981	1013	49.2	50.8
3	29	9	1	12	1992	9.94	182		1389	603	69.73	30.27
7	29	9	4	14	1991	9.93	183		845	1146	42.44	57.56
8	14	9	6	18	1991	9.93	184		945	1046	47.46	52.54
9	4	9	6	14	1990	9.93	185		829	1161	41.66	58.34
8	14	9	6	13	1989	9.92	186		895	1094	45	55
9	18	9	6	18	1988	9.92	187		951	1037	47.84	52.16
10	16	9	6	16	1988	9.92	188		785	1203	39.49	60.51
7	6	9	2	15	1984	9.9	189		1178	806	59.38	40.63
7	19	9	1	17	1984	9.9	190		1285	699	64.77	35.23
7	10	9	6	16	1983	9.89	191		962	1021	48.51	51.49
7	17	9	6	17	1983	9.89	192		930	1053	46.9	53.1
7	17	9	6	13	1982	9.89	193		897	1085	45.26	54.74
7	30	9	5	18	1982	9.89	194		1209	773	61	39
7	10	9	6	18	1981	9.88	195		930	1051	46.95	53.05
7	18	9	7	14	1980	9.88	196		876	1104	44.24	55.76
5	23	9	7	11	1979	9.87	197		652	1327	32.95	67.05
7	24	9	6	12	1979	9.87	198		863	1116	43.61	56.39
7	30	9	5	17	1977	9.86	199		1053	924	53.26	46.74
6	26	9	6	17	1976	9.86	200		853	1123	43.17	56.83

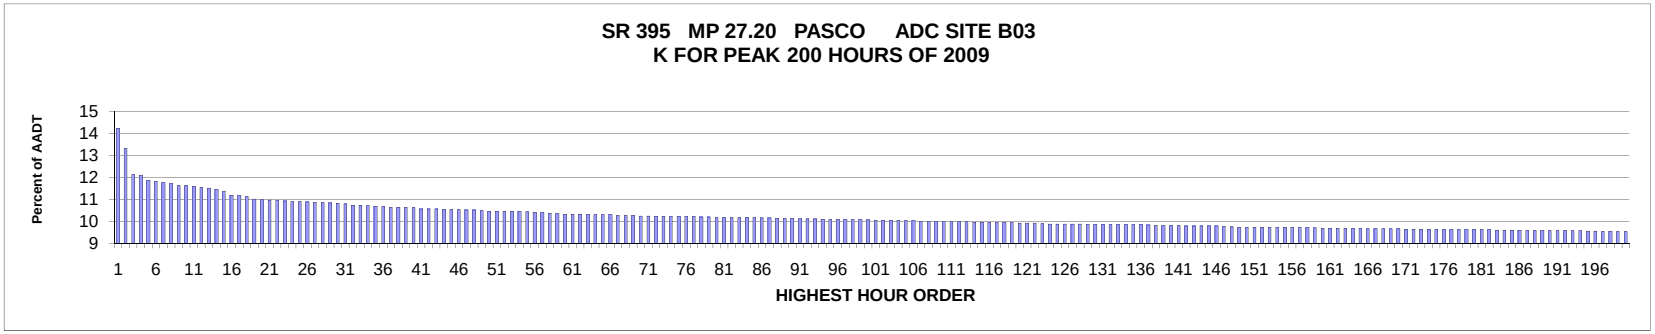

AADT= 14597 K 30 FACTOR= 10.82 K 100 FACTOR= 10.06 K 200 FACTOR= 9.52 D FACTOR= 52.38

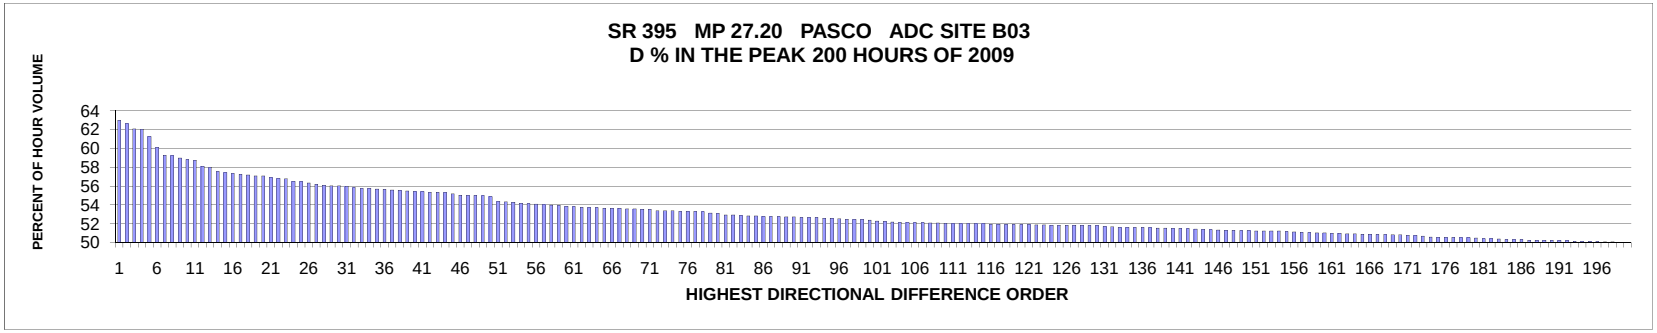

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
11	29	9	1	15	2077	14.23	1	14597	1129	948	54.36	45.64
11	29	9	1	16	1944	13.32	2		1104	840	56.79	43.21
11	25	9	4	16	1769	12.12	3		825	944	46.64	53.36
11	29	9	1	14	1768	12.11	4		917	851	51.87	48.13
8	16	9	1	17	1733	11.87	5		972	761	56.09	43.91
9	7	9	2	16	1727	11.83	6		764	963	44.24	55.76
11	25	9	4	17	1716	11.76	7		764	952	44.52	55.48
11	25	9	4	15	1710	11.71	8		869	841	50.82	49.18
8	2	9	1	17	1696	11.62	9		933	763	55.01	44.99
9	4	9	6	17	1696	11.62	10		882	814	52	48
8	9	9	1	17	1692	11.59	11		994	698	58.75	41.25
9	4	9	6	16	1684	11.54	12		905	779	53.74	46.26
11	29	9	1	17	1680	11.51	13		974	706	57.98	42.02
7	5	9	1	16	1671	11.45	14		700	971	41.89	58.11
8	9	9	1	18	1660	11.37	15		976	684	58.8	41.2
7	5	9	1	15	1634	11.19	16		652	982	39.9	60.1
11	29	9	1	13	1630	11.17	17		792	838	48.59	51.41

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	16	9	1	16	1624	11.13	18		823	801	50.68	49.32
7	24	9	6	17	1607	11.01	19		761	846	47.36	52.64
8	7	9	6	16	1603	10.98	20		805	798	50.22	49.78
9	7	9	2	15	1600	10.96	21	14597	710	890	44.38	55.63
9	4	9	6	18	1598	10.95	22		831	767	52	48
8	14	9	6	16	1596	10.93	23		806	790	50.5	49.5
7	5	9	1	14	1590	10.89	24		652	938	41.01	58.99
5	22	9	6	16	1589	10.89	25		738	851	46.44	53.56
5	15	9	6	17	1588	10.88	26		774	814	48.74	51.26
8	23	9	1	15	1585	10.86	27		779	806	49.15	50.85
6	26	9	6	17	1584	10.85	28		858	726	54.17	45.83
6	26	9	6	15	1583	10.84	29		879	704	55.53	44.47
5	22	9	6	17	1579	10.82	30		825	754	52.25	47.75
11	25	9	4	14	1575	10.79	31		818	757	51.94	48.06
7	2	9	5	17	1567	10.74	32		835	732	53.29	46.71
8	13	9	5	16	1567	10.74	33		745	822	47.54	52.46
10	9	9	6	17	1562	10.7	34		762	800	48.78	51.22
6	26	9	6	16	1560	10.69	35		805	755	51.6	48.4
9	11	9	6	17	1558	10.67	36		748	810	48.01	51.99
7	31	9	6	17	1552	10.63	37		757	795	48.78	51.22
9	7	9	2	17	1552	10.63	38		666	886	42.91	57.09
9	25	9	6	17	1552	10.63	39		739	813	47.62	52.38
7	5	9	1	17	1550	10.62	40		677	873	43.68	56.32
7	5	9	1	13	1541	10.56	41	14597	570	971	36.99	63.01
8	9	9	1	16	1541	10.56	42		772	769	50.1	49.9
10	23	9	6	17	1541	10.56	43		775	766	50.29	49.71
6	19	9	6	17	1538	10.54	44		739	799	48.05	51.95
7	24	9	6	14	1538	10.54	45		763	775	49.61	50.39
5	22	9	6	18	1537	10.53	46		769	768	50.03	49.97
6	19	9	6	15	1536	10.52	47		742	794	48.31	51.69
8	16	9	1	18	1536	10.52	48		884	652	57.55	42.45
10	16	9	6	16	1531	10.49	49		781	750	51.01	48.99
8	6	9	5	17	1527	10.46	50		681	846	44.6	55.4
8	14	9	6	17	1527	10.46	51		758	769	49.64	50.36
8	7	9	6	15	1526	10.45	52		731	795	47.9	52.1
8	9	9	1	13	1526	10.45	53		682	844	44.69	55.31
10	9	9	6	16	1524	10.44	54		805	719	52.82	47.18
7	24	9	6	16	1521	10.42	55		738	783	48.52	51.48
10	11	9	1	17	1519	10.41	56		746	773	49.11	50.89
11	25	9	4	18	1518	10.4	57		722	796	47.56	52.44
8	23	9	1	14	1513	10.37	58		647	866	42.76	57.24
8	23	9	1	16	1511	10.35	59		736	775	48.71	51.29
7	2	9	5	16	1507	10.32	60		755	752	50.1	49.9
9	18	9	6	16	1507	10.32	61	14597	781	726	51.82	48.18
6	19	9	6	16	1506	10.32	62		710	796	47.14	52.86
5	22	9	6	15	1504	10.3	63		812	692	53.99	46.01
8	9	9	1	14	1504	10.3	64		713	791	47.41	52.59
10	25	9	1	15	1504	10.3	65		737	767	49	51
9	4	9	6	15	1502	10.29	66		765	737	50.93	49.07
7	24	9	6	15	1498	10.26	67		741	757	49.47	50.53
7	31	9	6	18	1497	10.26	68		756	741	50.5	49.5
9	18	9	6	18	1497	10.26	69		745	752	49.77	50.23

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
5	8	9	6	16	1495	10.24	70		764	731	51.1	48.9
8	9	9	1	15	1495	10.24	71		709	786	47.42	52.58
7	17	9	6	15	1494	10.23	72		788	706	52.74	47.26
7	31	9	6	15	1494	10.23	73		774	720	51.81	48.19
8	7	9	6	17	1494	10.23	74		723	771	48.39	51.61
9	7	9	2	14	1494	10.23	75		608	886	40.7	59.3
8	21	9	6	17	1493	10.23	76		718	775	48.09	51.91
10	11	9	1	15	1492	10.22	77		768	724	51.47	48.53
10	11	9	1	16	1489	10.2	78		729	760	48.96	51.04
7	31	9	6	14	1488	10.19	79		798	690	53.63	46.37
6	5	9	6	17	1485	10.17	80		728	757	49.02	50.98
8	7	9	6	14	1485	10.17	81	14597	703	782	47.34	52.66
5	8	9	6	17	1484	10.17	82		708	776	47.71	52.29
6	5	9	6	18	1484	10.17	83		764	720	51.48	48.52
8	16	9	1	13	1484	10.17	84		633	851	42.65	57.35
7	12	9	1	14	1483	10.16	85		639	844	43.09	56.91
10	16	9	6	17	1482	10.15	86		695	787	46.9	53.1
8	6	9	5	16	1481	10.15	87		636	845	42.94	57.06
8	14	9	6	15	1478	10.13	88		785	693	53.11	46.89
10	18	9	1	16	1478	10.13	89		733	745	49.59	50.41
8	13	9	5	17	1477	10.12	90		685	792	46.38	53.62
3	27	9	6	17	1476	10.11	91		654	822	44.31	55.69
6	26	9	6	18	1475	10.1	92		757	718	51.32	48.68
10	16	9	6	15	1474	10.1	93		739	735	50.14	49.86
5	1	9	6	17	1473	10.09	94		716	757	48.61	51.39
8	16	9	1	15	1472	10.08	95		696	776	47.28	52.72
6	12	9	6	16	1471	10.08	96		731	740	49.69	50.31
7	31	9	6	16	1471	10.08	97		759	712	51.6	48.4
8	21	9	6	15	1470	10.07	98		794	676	54.01	45.99
9	18	9	6	17	1470	10.07	99		736	734	50.07	49.93
7	12	9	1	15	1469	10.06	100		671	798	45.68	54.32
7	10	9	6	18	1467	10.05	101	14597	732	735	49.9	50.1
8	2	9	1	18	1467	10.05	102		790	677	53.85	46.15
8	21	9	6	16	1467	10.05	103		763	704	52.01	47.99
10	2	9	6	17	1467	10.05	104		645	822	43.97	56.03
7	10	9	6	15	1465	10.04	105		763	702	52.08	47.92
7	10	9	6	17	1465	10.04	106		732	733	49.97	50.03
3	22	9	1	17	1458	9.99	107		913	545	62.62	37.38
6	21	9	1	16	1458	9.99	108		808	650	55.42	44.58
8	2	9	1	14	1458	9.99	109		651	807	44.65	55.35
4	17	9	6	17	1457	9.98	110		669	788	45.92	54.08
6	12	9	6	17	1457	9.98	111		755	702	51.82	48.18
11	25	9	4	13	1456	9.97	112		735	721	50.48	49.52
6	19	9	6	18	1455	9.97	113		700	755	48.11	51.89
7	17	9	6	16	1454	9.96	114		775	679	53.3	46.7
11	20	9	6	17	1454	9.96	115		652	802	44.84	55.16
7	3	9	6	12	1453	9.95	116		731	722	50.31	49.69
6	12	9	6	15	1452	9.95	117		748	704	51.52	48.48
10	25	9	1	16	1452	9.95	118		672	780	46.28	53.72
5	15	9	6	16	1449	9.93	119		695	754	47.96	52.04
11	6	9	6	17	1447	9.91	120		634	813	43.81	56.19
7	2	9	5	15	1446	9.91	121	14597	722	724	49.93	50.07

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	6	9	5	18	1446	9.91	122		672	774	46.47	53.53
8	13	9	5	15	1444	9.89	123		704	740	48.75	51.25
7	19	9	1	15	1442	9.88	124		724	718	50.21	49.79
7	30	9	5	17	1442	9.88	125		634	808	43.97	56.03
11	20	9	6	16	1441	9.87	126		694	747	48.16	51.84
5	29	9	6	17	1440	9.87	127		694	746	48.19	51.81
11	6	9	6	16	1440	9.87	128		767	673	53.26	46.74
7	10	9	6	16	1439	9.86	129		709	730	49.27	50.73
10	18	9	1	17	1437	9.84	130		730	707	50.8	49.2
10	23	9	6	16	1437	9.84	131		754	683	52.47	47.53
10	23	9	6	18	1437	9.84	132		745	692	51.84	48.16
10	25	9	1	17	1437	9.84	133		667	770	46.42	53.58
3	29	9	1	15	1436	9.84	134		742	694	51.67	48.33
6	5	9	6	16	1436	9.84	135		710	726	49.44	50.56
10	2	9	6	16	1436	9.84	136		665	771	46.31	53.69
8	16	9	1	14	1435	9.83	137		695	740	48.43	51.57
11	29	9	1	18	1434	9.82	138		814	620	56.76	43.24
5	25	9	2	16	1431	9.8	139		639	792	44.65	55.35
6	28	9	1	16	1430	9.8	140		718	712	50.21	49.79
10	16	9	6	18	1430	9.8	141	14597	654	776	45.73	54.27
3	22	9	1	15	1428	9.78	142		875	553	61.27	38.73
4	5	9	1	17	1428	9.78	143		820	608	57.42	42.58
4	17	9	6	16	1428	9.78	144		745	683	52.17	47.83
10	4	9	1	16	1428	9.78	145		662	766	46.36	53.64
9	18	9	6	15	1427	9.78	146		726	701	50.88	49.12
4	5	9	1	16	1426	9.77	147		795	631	55.75	44.25
11	29	9	1	12	1422	9.74	148		626	796	44.02	55.98
7	17	9	6	14	1421	9.73	149		703	718	49.47	50.53
7	17	9	6	17	1421	9.73	150		728	693	51.23	48.77
10	11	9	1	18	1421	9.73	151		694	727	48.84	51.16
6	21	9	1	17	1420	9.73	152		779	641	54.86	45.14
7	2	9	5	18	1420	9.73	153		729	691	51.34	48.66
8	14	9	6	18	1420	9.73	154		726	694	51.13	48.87
8	23	9	1	17	1420	9.73	155		736	684	51.83	48.17
9	4	9	6	14	1420	9.73	156		764	656	53.8	46.2
2	27	9	6	17	1418	9.71	157		638	780	44.99	55.01
6	26	9	6	14	1418	9.71	158		788	630	55.57	44.43
7	5	9	1	18	1416	9.7	159		694	722	49.01	50.99
3	13	9	6	17	1415	9.69	160		606	809	42.83	57.17
5	25	9	2	15	1415	9.69	161	14597	577	838	40.78	59.22
4	10	9	6	17	1413	9.68	162		660	753	46.71	53.29
8	7	9	6	13	1413	9.68	163		685	728	48.48	51.52
10	18	9	1	14	1412	9.67	164		636	776	45.04	54.96
7	2	9	5	14	1411	9.67	165		735	676	52.09	47.91
8	2	9	1	15	1410	9.66	166		634	776	44.96	55.04
8	7	9	6	18	1409	9.65	167		708	701	50.25	49.75
6	12	9	6	13	1408	9.65	168		732	676	51.99	48.01
7	30	9	5	16	1408	9.65	169		663	745	47.09	52.91
9	7	9	2	13	1408	9.65	170		534	874	37.93	62.07
3	22	9	1	16	1407	9.64	171		873	534	62.05	37.95
5	15	9	6	18	1407	9.64	172		665	742	47.26	52.74
10	25	9	1	14	1407	9.64	173		612	795	43.5	56.5

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
6	21	9	1	13	1406	9.63	174		677	729	48.15	51.85
6	21	9	1	15	1406	9.63	175		714	692	50.78	49.22
5	22	9	6	14	1405	9.63	176		750	655	53.38	46.62
7	10	9	6	14	1404	9.62	177		664	740	47.29	52.71
8	14	9	6	14	1404	9.62	178		739	665	52.64	47.36
9	25	9	6	16	1404	9.62	179		655	749	46.65	53.35
10	4	9	1	17	1404	9.62	180		720	684	51.28	48.72
10	23	9	6	15	1404	9.62	181	14597	673	731	47.93	52.07
5	15	9	6	15	1403	9.61	182		675	728	48.11	51.89
7	24	9	6	13	1402	9.6	183		660	742	47.08	52.92
5	8	9	6	18	1401	9.6	184		661	740	47.18	52.82
10	9	9	6	15	1401	9.6	185		739	662	52.75	47.25
5	1	9	6	16	1400	9.59	186		730	670	52.14	47.86
4	3	9	6	17	1399	9.58	187		692	707	49.46	50.54
8	14	9	6	12	1399	9.58	188		650	749	46.46	53.54
10	2	9	6	18	1398	9.58	189		644	754	46.07	53.93
7	19	9	1	14	1397	9.57	190		641	756	45.88	54.12
4	24	9	6	17	1396	9.56	191		686	710	49.14	50.86
8	14	9	6	13	1396	9.56	192		681	715	48.78	51.22
6	12	9	6	14	1395	9.56	193		724	671	51.9	48.1
8	21	9	6	13	1395	9.56	194		720	675	51.61	48.39
7	16	9	5	18	1394	9.55	195		616	778	44.19	55.81
8	28	9	6	15	1394	9.55	196		710	684	50.93	49.07
10	30	9	6	17	1393	9.54	197		693	700	49.75	50.25
9	25	9	6	15	1392	9.54	198		731	661	52.51	47.49
8	20	9	5	16	1391	9.53	199		666	725	47.88	52.12
7	30	9	5	18	1390	9.52	200		605	785	43.53	56.47

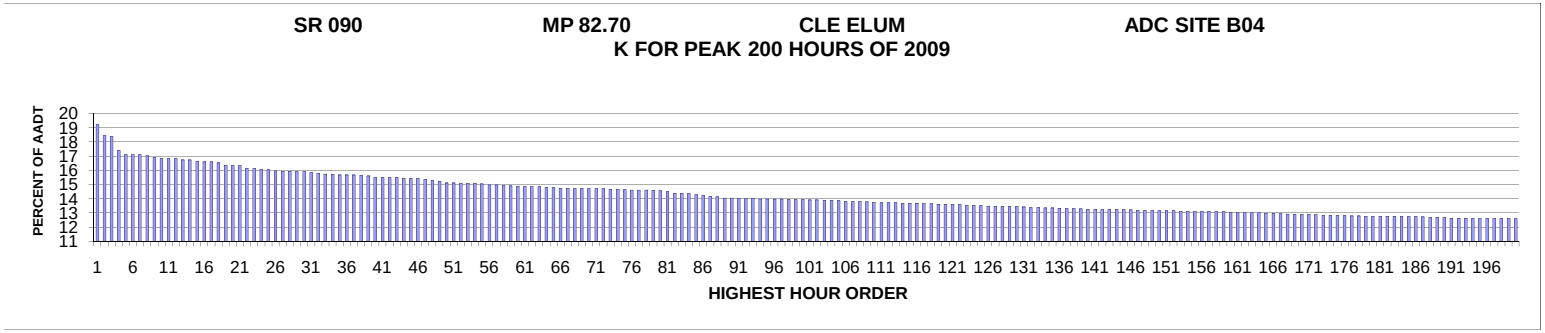

AADT= 26961 K 30 FACTOR= 15.88 K 100 FACTOR= 13.92 K 200 FACTOR= 12.58 D FACTOR= 59.98

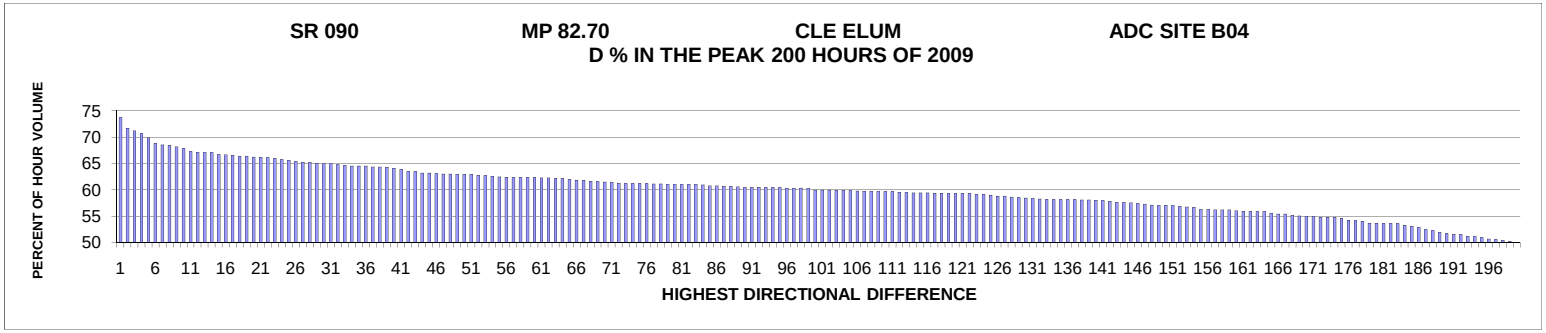

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
11	29	9	1	15	5175	19.19	1	26961	2596	2579	50.16	49.84
11	29	9	1	16	4965	18.42	2		2437	2528	49.08	50.92
11	29	9	1	14	4953	18.37	3		2532	2421	51.12	48.88
8	9	9	1	14	4682	17.37	4		1819	2863	38.85	61.15
8	9	9	1	15	4614	17.11	5		1813	2801	39.29	60.71
8	23	9	1	17	4604	17.08	6		1828	2776	39.7	60.3
8	9	9	1	13	4602	17.07	7		1854	2748	40.29	59.71
11	25	9	4	15	4585	17.01	8		2460	2125	53.65	46.35
8	16	9	1	18	4554	16.89	9		1862	2692	40.89	59.11
5	22	9	6	15	4539	16.84	10		3044	1495	67.06	32.94
8	23	9	1	15	4538	16.83	11		1781	2757	39.25	60.75
8	23	9	1	16	4529	16.8	12		1729	2800	38.18	61.82
7	26	9	1	16	4509	16.72	13		1754	2755	38.9	61.1
8	16	9	1	14	4504	16.71	14		1948	2556	43.25	56.75
11	25	9	4	16	4476	16.6	15		2601	1875	58.11	41.89
8	16	9	1	16	4470	16.58	16		1821	2649	40.74	59.26
7	5	9	1	14	4469	16.58	17		1645	2824	36.81	63.19

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	5	9	1	15	4451	16.51	18		1685	2766	37.86	62.14
11	29	9	1	13	4408	16.35	19		2386	2022	54.13	45.87
7	12	9	1	15	4401	16.32	20		1609	2792	36.56	63.44
8	16	9	1	17	4396	16.31	21	26961	1789	2607	40.7	59.3
6	28	9	1	15	4348	16.13	22		1480	2868	34.04	65.96
8	23	9	1	14	4345	16.12	23		1764	2581	40.6	59.4
7	26	9	1	15	4325	16.04	24		1707	2618	39.47	60.53
8	7	9	6	15	4322	16.03	25		2529	1793	58.51	41.49
8	9	9	1	17	4304	15.96	26		1661	2643	38.59	61.41
7	12	9	1	14	4294	15.93	27		1592	2702	37.07	62.93
6	28	9	1	16	4292	15.92	28		1412	2880	32.9	67.1
8	16	9	1	13	4285	15.89	29		1893	2392	44.18	55.82
7	12	9	1	16	4281	15.88	30		1586	2695	37.05	62.95
5	22	9	6	14	4263	15.81	31		2760	1503	64.74	35.26
7	19	9	1	15	4255	15.78	32		1578	2677	37.09	62.91
8	7	9	6	14	4240	15.73	33		2386	1854	56.27	43.73
8	16	9	1	19	4236	15.71	34		1696	2540	40.04	59.96
7	5	9	1	13	4226	15.67	35		1641	2585	38.83	61.17
7	5	9	1	16	4222	15.66	36		1614	2608	38.23	61.77
6	28	9	1	17	4219	15.65	37		1411	2808	33.44	66.56
5	10	9	1	17	4217	15.64	38		1472	2745	34.91	65.09
7	12	9	1	17	4207	15.6	39		1488	2719	35.37	64.63
11	29	9	1	17	4177	15.49	40		2018	2159	48.31	51.69
7	19	9	1	14	4176	15.49	41	26961	1546	2630	37.02	62.98
8	14	9	6	15	4172	15.47	42		2205	1967	52.85	47.15
11	25	9	4	17	4172	15.47	43		2489	1683	59.66	40.34
8	9	9	1	16	4164	15.44	44		1602	2562	38.47	61.53
7	3	9	6	14	4160	15.43	45		2589	1571	62.24	37.76
7	26	9	1	17	4156	15.41	46		1531	2625	36.84	63.16
11	25	9	4	14	4139	15.35	47		2114	2025	51.08	48.92
6	28	9	1	18	4122	15.29	48		1299	2823	31.51	68.49
8	7	9	6	16	4102	15.21	49		2392	1710	58.31	41.69
8	7	9	6	13	4072	15.1	50		2366	1706	58.1	41.9
7	3	9	6	15	4070	15.1	51		2482	1588	60.98	39.02
8	30	9	1	15	4066	15.08	52		1578	2488	38.81	61.19
5	23	9	7	11	4065	15.08	53		2755	1310	67.77	32.23
5	10	9	1	16	4063	15.07	54		1353	2710	33.3	66.7
8	16	9	1	12	4053	15.03	55		1893	2160	46.71	53.29
6	28	9	1	14	4037	14.97	56		1520	2517	37.65	62.35
8	9	9	1	12	4034	14.96	57		1733	2301	42.96	57.04
8	14	9	6	14	4019	14.91	58		2152	1867	53.55	46.45
5	10	9	1	18	4018	14.9	59		1485	2533	36.96	63.04
7	12	9	1	13	4011	14.88	60		1584	2427	39.49	60.51
7	26	9	1	18	4001	14.84	61	26961	1509	2492	37.72	62.28
7	5	9	1	17	4000	14.84	62		1578	2422	39.45	60.55
6	26	9	6	15	3998	14.83	63		2443	1555	61.11	38.89
5	17	9	1	15	3978	14.75	64		1382	2596	34.74	65.26
8	30	9	1	14	3978	14.75	65		1496	2482	37.61	62.39
8	14	9	6	16	3973	14.74	66		2176	1797	54.77	45.23
7	26	9	1	14	3972	14.73	67		1685	2287	42.42	57.58
6	26	9	6	14	3969	14.72	68		2431	1538	61.25	38.75
8	14	9	6	17	3965	14.71	69		2264	1701	57.1	42.9

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
5	25	9	2	13	3964	14.7	70		1373	2591	34.64	65.36
5	23	9	7	12	3963	14.7	71		2601	1362	65.63	34.37
8	7	9	6	17	3963	14.7	72		2355	1608	59.42	40.58
7	26	9	1	13	3953	14.66	73		1764	2189	44.62	55.38
5	23	9	7	14	3947	14.64	74		2705	1242	68.53	31.47
6	26	9	6	16	3944	14.63	75		2444	1500	61.97	38.03
8	2	9	1	15	3939	14.61	76		1529	2410	38.82	61.18
7	3	9	6	13	3937	14.6	77		2400	1537	60.96	39.04
5	25	9	2	11	3936	14.6	78		1133	2803	28.79	71.21
8	23	9	1	13	3931	14.58	79		1826	2105	46.45	53.55
7	19	9	1	13	3926	14.56	80		1618	2308	41.21	58.79
8	16	9	1	15	3908	14.5	81	26961	1894	2014	48.46	51.54
8	14	9	6	13	3878	14.38	82		2130	1748	54.93	45.07
5	22	9	6	13	3874	14.37	83		2499	1375	64.51	35.49
7	24	9	6	15	3871	14.36	84		2073	1798	53.55	46.45
7	12	9	1	18	3848	14.27	85		1528	2320	39.71	60.29
8	21	9	6	15	3835	14.22	86		2058	1777	53.66	46.34
8	2	9	1	14	3814	14.15	87		1551	2263	40.67	59.33
5	17	9	1	17	3811	14.14	88		1378	2433	36.16	63.84
7	17	9	6	15	3783	14.03	89		2078	1705	54.93	45.07
8	15	9	7	11	3783	14.03	90		2287	1496	60.45	39.55
5	23	9	7	13	3780	14.02	91		2536	1244	67.09	32.91
8	21	9	6	16	3780	14.02	92		2198	1582	58.15	41.85
5	3	9	1	17	3776	14.01	93		1280	2496	33.9	66.1
6	26	9	6	17	3768	13.98	94		2272	1496	60.3	39.7
5	22	9	6	20	3766	13.97	95		2591	1175	68.8	31.2
5	17	9	1	18	3764	13.96	96		1446	2318	38.42	61.58
6	28	9	1	13	3763	13.96	97		1648	2115	43.79	56.21
8	7	9	6	12	3760	13.95	98		2144	1616	57.02	42.98
8	2	9	1	17	3755	13.93	99		1516	2239	40.37	59.63
5	25	9	2	14	3753	13.92	100		1415	2338	37.7	62.3
7	24	9	6	16	3751	13.91	101	26961	2093	1658	55.8	44.2
8	9	9	1	18	3748	13.9	102		1654	2094	44.13	55.87
7	19	9	1	17	3744	13.89	103		1580	2164	42.2	57.8
5	17	9	1	16	3740	13.87	104		1440	2300	38.5	61.5
7	5	9	1	12	3738	13.86	105		1458	2280	39	61
4	26	9	1	17	3718	13.79	106		1327	2391	35.69	64.31
7	17	9	6	16	3718	13.79	107		2092	1626	56.27	43.73
7	24	9	6	17	3718	13.79	108		2226	1492	59.87	40.13
7	10	9	6	15	3711	13.76	109		2004	1707	54	46
5	22	9	6	19	3704	13.74	110		2434	1270	65.71	34.29
5	25	9	2	12	3696	13.71	111		1351	2345	36.55	63.45
11	29	9	1	12	3695	13.7	112		2094	1601	56.67	43.33
5	17	9	1	14	3694	13.7	113		1317	2377	35.65	64.35
8	15	9	7	12	3689	13.68	114		2231	1458	60.48	39.52
6	26	9	6	13	3685	13.67	115		2248	1437	61	39
8	7	9	6	18	3685	13.67	116		2199	1486	59.67	40.33
8	8	9	7	12	3679	13.65	117		2202	1477	59.85	40.15
4	26	9	1	16	3675	13.63	118		1391	2284	37.85	62.15
5	8	9	6	17	3672	13.62	119		2199	1473	59.89	40.11
5	22	9	6	12	3667	13.6	120		2500	1167	68.18	31.82
7	19	9	1	19	3666	13.6	121	26961	1239	2427	33.8	66.2

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	2	9	1	16	3665	13.59	122		1438	2227	39.24	60.76
7	12	9	1	12	3644	13.52	123		1469	2175	40.31	59.69
6	7	9	1	16	3643	13.51	124		1194	2449	32.78	67.22
8	30	9	1	13	3639	13.5	125		1372	2267	37.7	62.3
5	10	9	1	19	3635	13.48	126		1290	2345	35.49	64.51
4	3	9	6	16	3629	13.46	127		2410	1219	66.41	33.59
7	17	9	6	14	3629	13.46	128		1903	1726	52.44	47.56
6	26	9	6	12	3627	13.45	129		2365	1262	65.21	34.79
8	14	9	6	18	3627	13.45	130		2192	1435	60.44	39.56
8	21	9	6	17	3612	13.4	131		2104	1508	58.25	41.75
6	7	9	1	17	3606	13.37	132		1295	2311	35.91	64.09
7	10	9	6	16	3601	13.36	133		1994	1607	55.37	44.63
5	22	9	6	21	3595	13.33	134		2650	945	73.71	26.29
7	10	9	6	14	3593	13.33	135		1819	1774	50.63	49.37
4	19	9	1	17	3591	13.32	136		1422	2169	39.6	60.4
5	23	9	7	10	3585	13.3	137		2570	1015	71.69	28.31
7	2	9	5	16	3585	13.3	138		2239	1346	62.45	37.55
7	2	9	5	18	3580	13.28	139		2246	1334	62.74	37.26
8	2	9	1	13	3573	13.25	140		1617	1956	45.26	54.74
7	24	9	6	14	3572	13.25	141	26961	1842	1730	51.57	48.43
7	5	9	1	18	3568	13.23	142		1443	2125	40.44	59.56
8	15	9	7	13	3567	13.23	143		2052	1515	57.53	42.47
7	2	9	5	15	3564	13.22	144		2107	1457	59.12	40.88
12	27	9	1	15	3563	13.22	145		1404	2159	39.4	60.6
4	12	9	1	18	3558	13.2	146		1411	2147	39.66	60.34
4	5	9	1	15	3549	13.16	147		1554	1995	43.79	56.21
5	22	9	6	17	3547	13.16	148		2063	1484	58.16	41.84
7	24	9	6	13	3546	13.15	149		1882	1664	53.07	46.93
6	7	9	1	15	3543	13.14	150		1243	2300	35.08	64.92
7	17	9	6	17	3539	13.13	151		2075	1464	58.63	41.37
8	14	9	6	12	3539	13.13	152		2067	1472	58.41	41.59
7	19	9	1	20	3537	13.12	153		1188	2349	33.59	66.41
8	28	9	6	16	3534	13.11	154		2013	1521	56.96	43.04
7	3	9	6	16	3533	13.1	155		2119	1414	59.98	40.02
8	23	9	1	20	3532	13.1	156		1064	2468	30.12	69.88
7	2	9	5	17	3529	13.09	157		2207	1322	62.54	37.46
8	8	9	7	13	3521	13.06	158		2017	1504	57.28	42.72
11	25	9	4	13	3521	13.06	159		1762	1759	50.04	49.96
5	25	9	2	18	3514	13.03	160		1255	2259	35.71	64.29
8	21	9	6	14	3512	13.03	161	26961	2066	1446	58.83	41.17
7	31	9	6	17	3510	13.02	162		2085	1425	59.4	40.6
6	26	9	6	18	3507	13.01	163		2198	1309	62.67	37.33
4	12	9	1	17	3506	13	164		1439	2067	41.04	58.96
6	28	9	1	19	3502	12.99	165		1168	2334	33.35	66.65
7	12	9	1	19	3491	12.95	166		1462	2029	41.88	58.12
7	31	9	6	16	3485	12.93	167		1889	1596	54.2	45.8
7	2	9	5	19	3483	12.92	168		2171	1312	62.33	37.67
5	3	9	1	16	3479	12.9	169		1235	2244	35.5	64.5
8	2	9	1	18	3479	12.9	170		1417	2062	40.73	59.27
5	10	9	1	15	3474	12.89	171		1176	2298	33.85	66.15
8	28	9	6	17	3468	12.86	172		1990	1478	57.38	42.62
7	19	9	1	12	3458	12.83	173		1450	2008	41.93	58.07

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	23	9	1	12	3457	12.82	174		1711	1746	49.49	50.51
5	17	9	1	13	3454	12.81	175		1349	2105	39.06	60.94
7	19	9	1	18	3449	12.79	176		1387	2062	40.21	59.79
5	8	9	6	15	3445	12.78	177		1997	1448	57.97	42.03
7	24	9	6	18	3442	12.77	178		2000	1442	58.11	41.89
4	3	9	6	14	3441	12.76	179		2168	1273	63	37
7	10	9	6	13	3441	12.76	180		1897	1544	55.13	44.87
7	17	9	6	13	3440	12.76	181	26961	1878	1562	54.59	45.41
8	6	9	5	16	3440	12.76	182		2099	1341	61.02	38.98
8	30	9	1	16	3439	12.76	183		1706	1733	49.61	50.39
8	16	9	1	11	3438	12.75	184		1530	1908	44.5	55.5
3	29	9	1	16	3432	12.73	185		1543	1889	44.96	55.04
7	19	9	1	16	3432	12.73	186		1639	1793	47.76	52.24
5	25	9	2	19	3423	12.7	187		1004	2419	29.33	70.67
8	1	9	7	12	3421	12.69	188		1875	1546	54.81	45.19
12	27	9	1	14	3421	12.69	189		1505	1916	43.99	56.01
4	19	9	1	18	3412	12.66	190		1433	1979	42	58
5	15	9	6	16	3403	12.62	191		1934	1469	56.83	43.17
6	5	9	6	18	3403	12.62	192		2210	1193	64.94	35.06
7	26	9	1	12	3401	12.61	193		1635	1766	48.07	51.93
7	17	9	6	18	3397	12.6	194		2016	1381	59.35	40.65
7	24	9	6	12	3397	12.6	195		1900	1497	55.93	44.07
8	21	9	6	18	3397	12.6	196		2037	1360	59.96	40.04
7	25	9	7	12	3396	12.6	197		1955	1441	57.57	42.43
8	28	9	6	15	3396	12.6	198		1908	1488	56.18	43.82
5	25	9	2	15	3395	12.59	199		1376	2019	40.53	59.47
8	16	9	1	20	3393	12.58	200		1381	2012	40.7	59.3

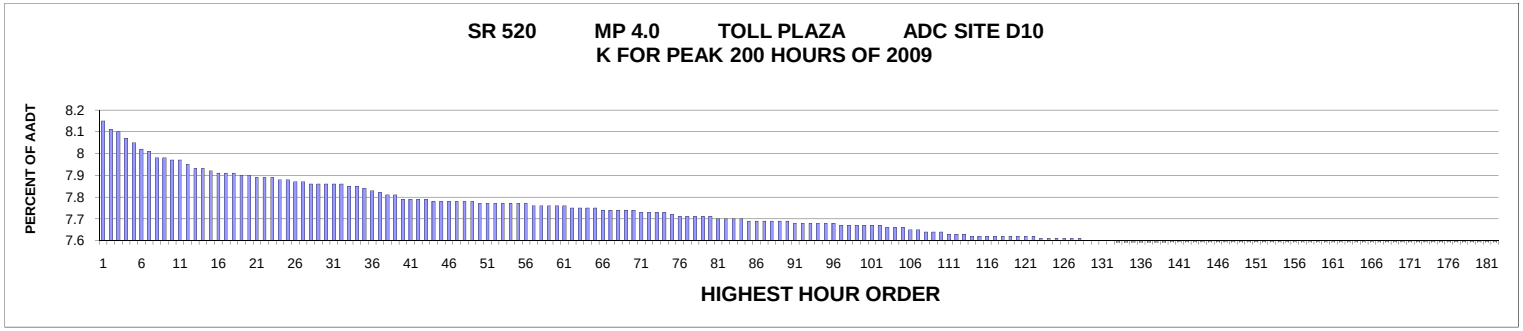

AADT= 97372 **K 30 FACTOR=** 7.95 **K 100 FACTOR=** 7.7 **K 200 FACTOR=** 7.53 **D FACTOR=** 51.16

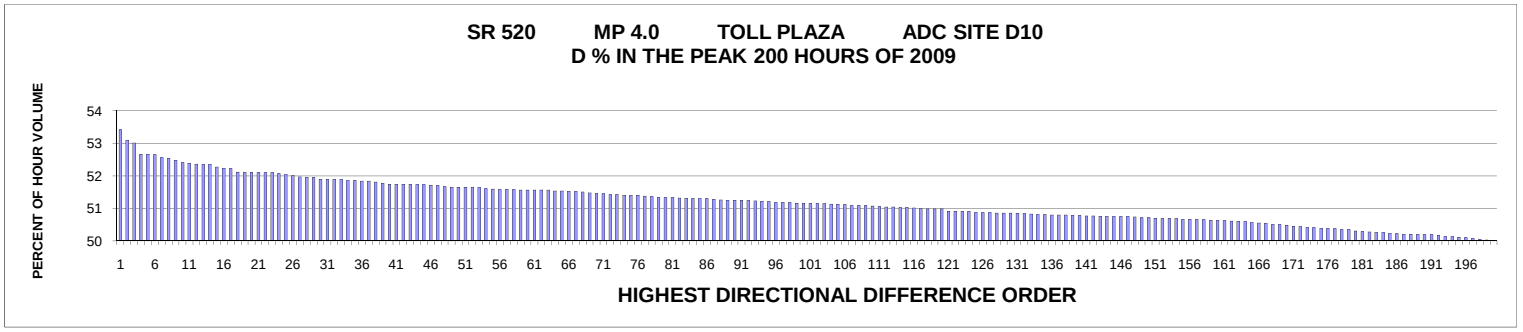

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
5	7	9	5	8	7931	8.15	1	97372	3983	3948	50.22	49.78
5	20	9	4	8	7899	8.11	2		4022	3877	50.92	49.08
5	12	9	3	8	7883	8.1	3		3935	3948	49.92	50.08
5	27	9	4	8	7861	8.07	4		3996	3865	50.83	49.17
4	30	9	5	8	7834	8.05	5		3976	3858	50.75	49.25
4	29	9	4	8	7810	8.02	6		4041	3769	51.74	48.26
4	28	9	3	9	7802	8.01	7		4011	3791	51.41	48.59
5	11	9	2	8	7771	7.98	8		3907	3864	50.28	49.72
4	28	9	3	8	7767	7.98	9		3971	3796	51.13	48.87
7	9	9	5	8	7758	7.97	10		3934	3824	50.71	49.29
5	13	9	4	8	7756	7.97	11		3975	3781	51.25	48.75
5	19	9	3	8	7741	7.95	12		3971	3770	51.3	48.7
5	7	9	5	9	7723	7.93	13		3963	3760	51.31	48.69
5	18	9	2	8	7717	7.93	14		3920	3797	50.8	49.2
7	8	9	4	8	7713	7.92	15		3838	3875	49.76	50.24
4	27	9	2	8	7704	7.91	16		3961	3743	51.41	48.59
2	5	9	5	8	7702	7.91	17		3913	3789	50.8	49.2

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
4	15	9	4	8	7700	7.91	18		4047	3653	52.56	47.44
1	22	9	5	8	7696	7.9	19		3975	3721	51.65	48.35
5	11	9	2	9	7693	7.9	20		3895	3798	50.63	49.37
2	5	9	5	9	7681	7.89	21	97372	3806	3875	49.55	50.45
6	5	9	6	8	7680	7.89	22		3893	3787	50.69	49.31
10	7	9	4	8	7680	7.89	23		3926	3754	51.12	48.88
1	15	9	5	8	7673	7.88	24		3886	3787	50.65	49.35
4	16	9	5	8	7670	7.88	25		3944	3726	51.42	48.58
5	20	9	4	9	7666	7.87	26		3984	3682	51.97	48.03
5	13	9	4	9	7663	7.87	27		3882	3781	50.66	49.34
3	31	9	3	8	7657	7.86	28		3990	3667	52.11	47.89
6	16	9	3	8	7657	7.86	29		3999	3658	52.23	47.77
5	15	9	6	8	7654	7.86	30		3881	3773	50.71	49.29
3	18	9	4	8	7651	7.86	31		3918	3733	51.21	48.79
10	13	9	3	9	7651	7.86	32		3871	3780	50.59	49.41
5	21	9	5	8	7642	7.85	33		3887	3755	50.86	49.14
11	4	9	4	8	7642	7.85	34		3881	3761	50.79	49.21
4	22	9	4	9	7638	7.84	35		3839	3799	50.26	49.74
4	15	9	4	9	7629	7.83	36		3917	3712	51.34	48.66
6	2	9	3	8	7611	7.82	37		3921	3690	51.52	48.48
10	2	9	6	8	7605	7.81	38		3884	3721	51.07	48.93
7	9	9	5	9	7601	7.81	39		3867	3734	50.87	49.13
3	24	9	3	8	7590	7.79	40		3929	3661	51.77	48.23
5	19	9	3	9	7588	7.79	41	97372	3955	3633	52.12	47.88
4	29	9	4	9	7587	7.79	42		3915	3672	51.6	48.4
4	16	9	5	9	7584	7.79	43		3910	3674	51.56	48.44
12	17	9	5	9	7580	7.78	44		3898	3682	51.42	48.58
4	8	9	4	8	7578	7.78	45		3968	3610	52.36	47.64
1	28	9	4	9	7576	7.78	46		3874	3702	51.14	48.86
5	12	9	3	9	7574	7.78	47		3955	3619	52.22	47.78
6	10	9	4	8	7573	7.78	48		3885	3688	51.3	48.7
7	13	9	2	8	7571	7.78	49		3760	3811	49.66	50.34
6	8	9	2	8	7567	7.77	50		3893	3674	51.45	48.55
3	27	9	6	8	7566	7.77	51		3931	3635	51.96	48.04
3	4	9	4	9	7564	7.77	52		3926	3638	51.9	48.1
6	18	9	5	8	7563	7.77	53		3969	3594	52.48	47.52
11	30	9	2	8	7562	7.77	54		3850	3712	50.91	49.09
10	1	9	5	9	7561	7.77	55		3905	3656	51.65	48.35
10	13	9	3	8	7561	7.77	56		3900	3661	51.58	48.42
6	17	9	4	8	7558	7.76	57		3922	3636	51.89	48.11
11	2	9	2	8	7555	7.76	58		3785	3770	50.1	49.9
1	13	9	3	8	7553	7.76	59		3924	3629	51.95	48.05
4	22	9	4	18	7553	7.76	60		3676	3877	48.67	51.33
5	12	9	3	17	7553	7.76	61	97372	3731	3822	49.4	50.6
6	12	9	6	8	7547	7.75	62		3925	3622	52.01	47.99
7	7	9	3	9	7547	7.75	63		3802	3745	50.38	49.62
1	16	9	6	8	7545	7.75	64		3822	3723	50.66	49.34
10	28	9	4	8	7544	7.75	65		3818	3726	50.61	49.39
5	26	9	3	8	7534	7.74	66		3891	3643	51.65	48.35
5	26	9	3	9	7534	7.74	67		3926	3608	52.11	47.89
1	29	9	5	8	7533	7.74	68		3884	3649	51.56	48.44
7	8	9	4	9	7533	7.74	69		3776	3757	50.13	49.87

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
2	4	9	4	8	7532	7.74	70		3780	3752	50.19	49.81
4	7	9	3	9	7530	7.73	71		3865	3665	51.33	48.67
3	23	9	2	8	7529	7.73	72		3843	3686	51.04	48.96
7	15	9	4	8	7527	7.73	73		3690	3837	49.02	50.98
1	22	9	5	9	7522	7.73	74		3917	3605	52.07	47.93
6	24	9	4	8	7521	7.72	75		3937	3584	52.35	47.65
10	15	9	5	9	7511	7.71	76		3816	3695	50.81	49.19
3	30	9	2	8	7510	7.71	77		3886	3624	51.74	48.26
10	7	9	4	9	7507	7.71	78		3839	3668	51.14	48.86
5	15	9	6	9	7505	7.71	79		3765	3740	50.17	49.83
6	4	9	5	8	7505	7.71	80		3808	3697	50.74	49.26
5	4	9	2	8	7501	7.7	81	97372	3839	3662	51.18	48.82
6	9	9	3	8	7496	7.7	82		3804	3692	50.75	49.25
5	27	9	4	9	7495	7.7	83		3841	3654	51.25	48.75
1	21	9	4	9	7494	7.7	84		3799	3695	50.69	49.31
2	17	9	3	8	7492	7.69	85		3833	3659	51.16	48.84
4	13	9	2	8	7491	7.69	86		3849	3642	51.38	48.62
1	8	9	5	9	7487	7.69	87		3854	3633	51.48	48.52
2	2	9	2	8	7486	7.69	88		3707	3779	49.52	50.48
5	8	9	6	8	7486	7.69	89		3747	3739	50.05	49.95
3	31	9	3	9	7484	7.69	90		3912	3572	52.27	47.73
10	28	9	4	9	7481	7.68	91		3790	3691	50.66	49.34
3	17	9	3	8	7477	7.68	92		3840	3637	51.36	48.64
6	1	9	2	9	7475	7.68	93		3795	3680	50.77	49.23
7	13	9	2	9	7475	7.68	94		3753	3722	50.21	49.79
5	8	9	6	9	7474	7.68	95		3836	3638	51.32	48.68
7	9	9	5	10	7474	7.68	96		3769	3705	50.43	49.57
3	4	9	4	8	7473	7.67	97		3778	3695	50.56	49.44
3	18	9	4	9	7473	7.67	98		3936	3537	52.67	47.33
3	18	9	4	17	7468	7.67	99		3582	3886	47.96	52.04
6	3	9	4	8	7467	7.67	100		3790	3677	50.76	49.24
4	28	9	3	17	7466	7.67	101	97372	3604	3862	48.27	51.73
10	22	9	5	9	7464	7.67	102		3731	3733	49.99	50.01
4	16	9	5	18	7463	7.66	103		3575	3888	47.9	52.1
7	22	9	4	8	7461	7.66	104		3813	3648	51.11	48.89
11	3	9	3	8	7459	7.66	105		3810	3649	51.08	48.92
5	21	9	5	9	7453	7.65	106		3757	3696	50.41	49.59
6	5	9	6	9	7453	7.65	107		3742	3711	50.21	49.79
1	15	9	5	9	7442	7.64	108		3816	3626	51.28	48.72
3	26	9	5	18	7440	7.64	109		3615	3825	48.59	51.41
1	28	9	4	8	7439	7.64	110		3833	3606	51.53	48.47
7	6	9	2	8	7434	7.63	111		3637	3797	48.92	51.08
2	12	9	5	9	7429	7.63	112		3772	3657	50.77	49.23
11	24	9	3	8	7428	7.63	113		3807	3621	51.25	48.75
6	4	9	5	9	7424	7.62	114		3714	3710	50.03	49.97
4	14	9	3	9	7421	7.62	115		3825	3596	51.54	48.46
4	9	9	5	9	7420	7.62	116		3940	3480	53.1	46.9
3	25	9	4	18	7419	7.62	117		3622	3797	48.82	51.18
4	13	9	2	9	7419	7.62	118		3933	3486	53.01	46.99
6	24	9	4	9	7419	7.62	119		3801	3618	51.23	48.77
7	16	9	5	8	7417	7.62	120		3694	3723	49.8	50.2
4	8	9	4	9	7415	7.62	121	97372	3904	3511	52.65	47.35

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
6	9	9	3	9	7415	7.62	122		3798	3617	51.22	48.78
12	1	9	3	9	7412	7.61	123		3781	3631	51.01	48.99
12	16	9	4	9	7410	7.61	124		3822	3588	51.58	48.42
1	23	9	6	8	7407	7.61	125		3819	3588	51.56	48.44
6	25	9	5	8	7407	7.61	126		3901	3506	52.67	47.33
3	5	9	5	9	7406	7.61	127		3796	3610	51.26	48.74
10	22	9	5	8	7406	7.61	128		3755	3651	50.7	49.3
6	3	9	4	9	7405	7.6	129		3758	3647	50.75	49.25
5	4	9	2	9	7403	7.6	130		3787	3616	51.15	48.85
10	15	9	5	8	7402	7.6	131		3726	3676	50.34	49.66
4	20	9	2	8	7398	7.6	132		3758	3640	50.8	49.2
4	28	9	3	18	7395	7.59	133		3606	3789	48.76	51.24
5	29	9	6	8	7394	7.59	134		3831	3563	51.81	48.19
7	22	9	4	9	7393	7.59	135		3836	3557	51.89	48.11
3	26	9	5	16	7392	7.59	136		3508	3884	47.46	52.54
11	2	9	2	9	7391	7.59	137		3824	3567	51.74	48.26
12	3	9	5	9	7391	7.59	138		3717	3674	50.29	49.71
7	1	9	4	8	7388	7.59	139		3817	3571	51.66	48.34
2	4	9	4	9	7384	7.58	140		3706	3678	50.19	49.81
2	18	9	4	9	7383	7.58	141	97372	3799	3584	51.46	48.54
4	14	9	3	8	7382	7.58	142		3943	3439	53.41	46.59
5	18	9	2	9	7378	7.58	143		3844	3534	52.1	47.9
7	7	9	3	10	7378	7.58	144		3697	3681	50.11	49.89
3	25	9	4	17	7376	7.58	145		3511	3865	47.6	52.4
1	29	9	5	9	7375	7.57	146		3747	3628	50.81	49.19
6	23	9	3	8	7371	7.57	147		3763	3608	51.05	48.95
3	24	9	3	9	7370	7.57	148		3772	3598	51.18	48.82
3	18	9	4	18	7369	7.57	149		3571	3798	48.46	51.54
10	20	9	3	8	7369	7.57	150		3805	3564	51.64	48.36
5	22	9	6	8	7368	7.57	151		3730	3638	50.62	49.38
7	7	9	3	8	7368	7.57	152		3707	3661	50.31	49.69
4	21	9	3	9	7366	7.56	153		3758	3608	51.02	48.98
4	29	9	4	17	7365	7.56	154		3663	3702	49.74	50.26
5	14	9	5	17	7365	7.56	155		3636	3729	49.37	50.63
1	14	9	4	8	7364	7.56	156		3645	3719	49.5	50.5
3	3	9	3	9	7363	7.56	157		3807	3556	51.7	48.3
4	28	9	3	16	7362	7.56	158		3606	3756	48.98	51.02
3	2	9	2	8	7361	7.56	159		3753	3608	50.98	49.02
5	14	9	5	10	7360	7.56	160		3708	3652	50.38	49.62
5	6	9	4	8	7357	7.56	161	97372	3669	3688	49.87	50.13
5	8	9	6	15	7357	7.56	162		3638	3719	49.45	50.55
3	17	9	3	18	7355	7.55	163		3552	3803	48.29	51.71
4	22	9	4	17	7354	7.55	164		3550	3804	48.27	51.73
6	25	9	5	9	7354	7.55	165		3745	3609	50.92	49.08
2	13	9	6	8	7353	7.55	166		3772	3581	51.3	48.7
2	18	9	4	8	7353	7.55	167		3744	3609	50.92	49.08
5	20	9	4	17	7352	7.55	168		3565	3787	48.49	51.51
11	23	9	2	9	7352	7.55	169		3852	3500	52.39	47.61
2	25	9	4	9	7345	7.54	170		3787	3558	51.56	48.44
4	16	9	5	17	7345	7.54	171		3518	3827	47.9	52.1
2	19	9	5	8	7344	7.54	172		3645	3699	49.63	50.37
7	10	9	6	8	7344	7.54	173		3537	3807	48.16	51.84

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
3	16	9	2	8	7341	7.54	174		3787	3554	51.59	48.41
4	7	9	3	8	7341	7.54	175		3700	3641	50.4	49.6
4	20	9	2	9	7341	7.54	176		3806	3535	51.85	48.15
2	2	9	2	9	7340	7.54	177		3732	3608	50.84	49.16
6	12	9	6	9	7339	7.54	178		3797	3542	51.74	48.26
1	20	9	3	8	7338	7.54	179		3742	3596	50.99	49.01
10	8	9	5	8	7338	7.54	180		3584	3754	48.84	51.16
1	16	9	6	9	7335	7.53	181	97372	3807	3528	51.9	48.1
3	3	9	3	8	7335	7.53	182		3732	3603	50.88	49.12
6	23	9	3	9	7335	7.53	183		3744	3591	51.04	48.96
7	14	9	3	10	7335	7.53	184		3730	3605	50.85	49.15
5	20	9	4	18	7334	7.53	185		3495	3839	47.65	52.35
5	12	9	3	10	7333	7.53	186		3738	3595	50.98	49.02
12	1	9	3	8	7332	7.53	187		3703	3629	50.5	49.5
3	24	9	3	17	7331	7.53	188		3545	3786	48.36	51.64
1	9	9	6	8	7329	7.53	189		3744	3585	51.08	48.92
3	13	9	6	16	7329	7.53	190		3530	3799	48.16	51.84
7	21	9	3	8	7325	7.52	191		3702	3623	50.54	49.46

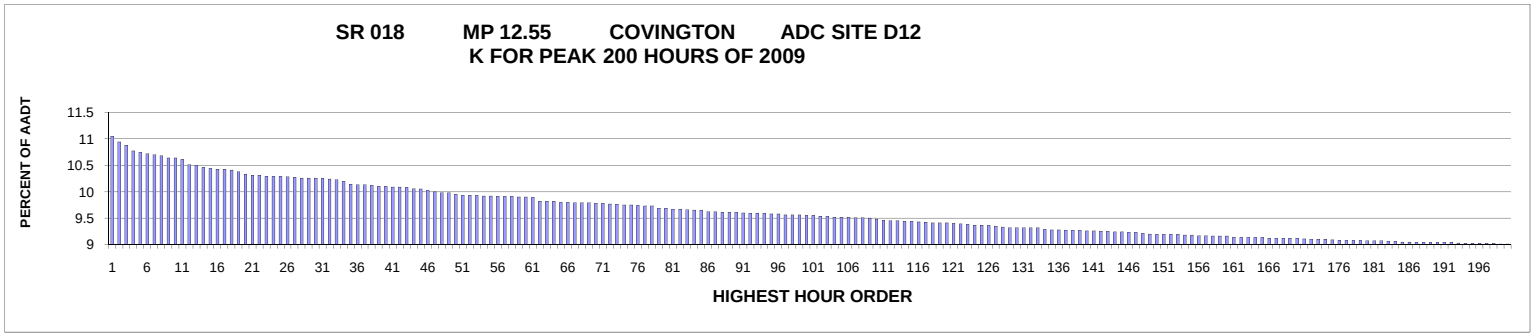

AADT= 31288 K 30 FACTOR= 10.26 K 100 FACTOR= 9.55 K 200 FACTOR= 9.01 D FACTOR= 53.63

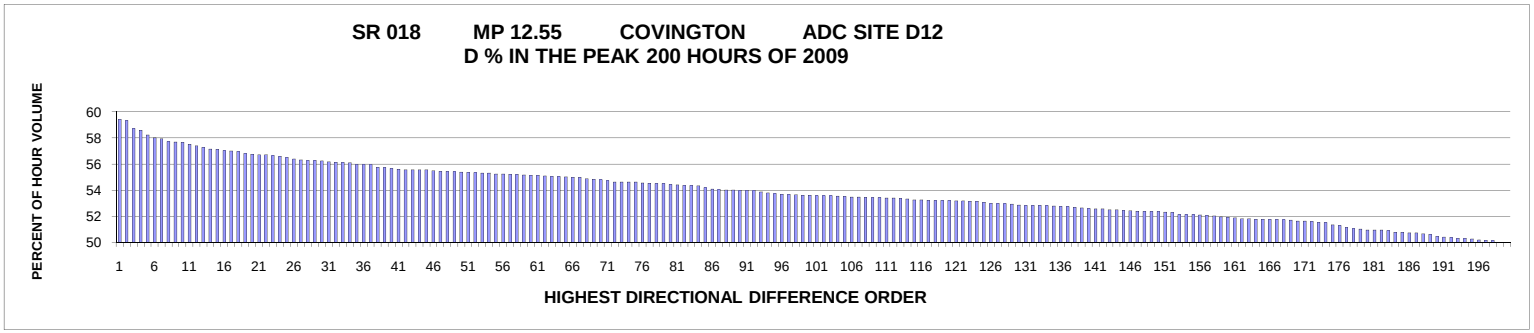

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	24	9	6	16	3458	11.05	1	31288	1667	1791	48.21	51.79
6	12	9	6	17	3424	10.94	2		1602	1822	46.79	53.21
7	10	9	6	16	3403	10.88	3		1538	1865	45.2	54.8
8	7	9	6	17	3371	10.77	4		1569	1802	46.54	53.46
5	22	9	6	17	3361	10.74	5		1741	1620	51.8	48.2
5	22	9	6	16	3354	10.72	6		1755	1599	52.33	47.67
8	14	9	6	17	3348	10.7	7		1554	1794	46.42	53.58
11	25	9	4	16	3343	10.68	8		1610	1733	48.16	51.84
7	2	9	5	17	3329	10.64	9		1593	1736	47.85	52.15
5	15	9	6	17	3328	10.64	10		1553	1775	46.66	53.34
7	24	9	6	17	3319	10.61	11		1546	1773	46.58	53.42
7	17	9	6	16	3287	10.51	12		1466	1821	44.6	55.4
5	8	9	6	17	3284	10.5	13		1545	1739	47.05	52.95
9	4	9	6	17	3272	10.46	14		1661	1611	50.76	49.24
7	17	9	6	17	3267	10.44	15		1482	1785	45.36	54.64
6	19	9	6	17	3264	10.43	16		1562	1702	47.86	52.14
7	10	9	6	17	3263	10.43	17		1473	1790	45.14	54.86

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
6	12	9	6	18	3256	10.41	18		1548	1708	47.54	52.46
7	17	9	6	18	3247	10.38	19		1592	1655	49.03	50.97
11	25	9	4	17	3231	10.33	20		1519	1712	47.01	52.99
6	5	9	6	17	3227	10.31	21	31288	1498	1729	46.42	53.58
6	12	9	6	16	3227	10.31	22		1521	1706	47.13	52.87
11	25	9	4	15	3221	10.29	23		1586	1635	49.24	50.76
7	31	9	6	18	3220	10.29	24		1518	1702	47.14	52.86
6	26	9	6	17	3219	10.29	25		1449	1770	45.01	54.99
8	21	9	6	17	3217	10.28	26		1480	1737	46.01	53.99
4	24	9	6	17	3214	10.27	27		1517	1697	47.2	52.8
9	11	9	6	17	3210	10.26	28		1460	1750	45.48	54.52
5	15	9	6	18	3209	10.26	29		1528	1681	47.62	52.38
8	7	9	6	16	3209	10.26	30		1424	1785	44.38	55.62
7	10	9	6	18	3208	10.25	31		1485	1723	46.29	53.71
7	31	9	6	17	3205	10.24	32		1489	1716	46.46	53.54
6	26	9	6	16	3200	10.23	33		1512	1688	47.25	52.75
8	21	9	6	16	3192	10.2	34		1540	1652	48.25	51.75
9	4	9	6	16	3173	10.14	35		1602	1571	50.49	49.51
8	14	9	6	16	3170	10.13	36		1469	1701	46.34	53.66
5	1	9	6	17	3168	10.13	37		1483	1685	46.81	53.19
6	19	9	6	16	3166	10.12	38		1550	1616	48.96	51.04
7	31	9	6	16	3161	10.1	39		1434	1727	45.37	54.63
8	28	9	6	17	3160	10.1	40		1477	1683	46.74	53.26
7	2	9	5	18	3158	10.09	41	31288	1566	1592	49.59	50.41
9	25	9	6	18	3157	10.09	42		1588	1569	50.3	49.7
7	2	9	5	16	3153	10.08	43		1449	1704	45.96	54.04
5	22	9	6	15	3149	10.06	44		1641	1508	52.11	47.89
4	17	9	6	17	3145	10.05	45		1415	1730	44.99	55.01
9	18	9	6	17	3135	10.02	46		1467	1668	46.79	53.21
2	13	9	6	17	3128	10	47		1360	1768	43.48	56.52
7	16	9	5	17	3122	9.98	48		1390	1732	44.52	55.48
7	24	9	6	18	3121	9.98	49		1436	1685	46.01	53.99
10	9	9	6	17	3113	9.95	50		1482	1631	47.61	52.39
5	29	9	6	17	3108	9.93	51		1436	1672	46.2	53.8
10	16	9	6	17	3107	9.93	52		1534	1573	49.37	50.63
5	8	9	6	16	3106	9.93	53		1481	1625	47.68	52.32
5	1	9	6	16	3105	9.92	54		1363	1742	43.9	56.1
9	11	9	6	16	3103	9.92	55		1379	1724	44.44	55.56
6	5	9	6	16	3102	9.91	56		1446	1656	46.62	53.38
5	21	9	5	17	3100	9.91	57		1392	1708	44.9	55.1
6	26	9	6	18	3100	9.91	58		1485	1615	47.9	52.1
8	28	9	6	16	3099	9.9	59		1457	1642	47.02	52.98
8	14	9	6	18	3097	9.9	60		1448	1649	46.75	53.25
5	15	9	6	16	3094	9.89	61	31288	1385	1709	44.76	55.24
6	25	9	5	17	3074	9.82	62		1331	1743	43.3	56.7
7	17	9	6	15	3074	9.82	63		1379	1695	44.86	55.14
3	20	9	6	17	3073	9.82	64		1398	1675	45.49	54.51
9	18	9	6	18	3067	9.8	65		1523	1544	49.66	50.34
9	11	9	6	18	3065	9.8	66		1428	1637	46.59	53.41
11	25	9	4	14	3064	9.79	67		1562	1502	50.98	49.02
2	13	9	6	16	3063	9.79	68		1398	1665	45.64	54.36
9	25	9	6	17	3062	9.79	69		1408	1654	45.98	54.02

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
3	27	9	6	17	3060	9.78	70		1457	1603	47.61	52.39
5	29	9	6	16	3059	9.78	71		1396	1663	45.64	54.36
7	31	9	6	15	3058	9.77	72		1414	1644	46.24	53.76
6	19	9	6	18	3055	9.76	73		1517	1538	49.66	50.34
5	8	9	6	18	3051	9.75	74		1421	1630	46.57	53.43
6	18	9	5	17	3050	9.75	75		1319	1731	43.25	56.75
3	13	9	6	17	3046	9.74	76		1348	1698	44.25	55.75
2	27	9	6	17	3045	9.73	77		1364	1681	44.79	55.21
9	18	9	6	16	3044	9.73	78		1435	1609	47.14	52.86
7	2	9	5	15	3033	9.69	79		1481	1552	48.83	51.17
6	5	9	6	18	3031	9.69	80		1483	1548	48.93	51.07
5	22	9	6	18	3026	9.67	81	31288	1653	1373	54.63	45.37
10	23	9	6	17	3026	9.67	82		1422	1604	46.99	53.01
3	13	9	6	18	3023	9.66	83		1355	1668	44.82	55.18
5	1	9	6	18	3020	9.65	84		1458	1562	48.28	51.72
8	16	9	1	13	3019	9.65	85		1504	1515	49.82	50.18
10	2	9	6	17	3010	9.62	86		1427	1583	47.41	52.59
10	9	9	6	16	3010	9.62	87		1429	1581	47.48	52.52
7	16	9	5	18	3008	9.61	88		1352	1656	44.95	55.05
8	28	9	6	18	3007	9.61	89		1474	1533	49.02	50.98
2	13	9	6	18	3006	9.61	90		1423	1583	47.34	52.66
11	6	9	6	17	3005	9.6	91		1398	1607	46.52	53.48
6	12	9	6	15	3001	9.59	92		1441	1560	48.02	51.98
8	21	9	6	18	3001	9.59	93		1451	1550	48.35	51.65
2	20	9	6	17	2999	9.59	94		1336	1663	44.55	55.45
1	30	9	6	17	2998	9.58	95		1339	1659	44.66	55.34
7	23	9	5	17	2996	9.58	96		1341	1655	44.76	55.24
10	30	9	6	17	2992	9.56	97		1386	1606	46.32	53.68
4	3	9	6	16	2991	9.56	98		1399	1592	46.77	53.23
3	27	9	6	16	2990	9.56	99		1410	1580	47.16	52.84
6	26	9	6	15	2989	9.55	100		1493	1496	49.95	50.05
8	5	9	4	17	2988	9.55	101	31288	1284	1704	42.97	57.03
5	29	9	6	18	2984	9.54	102		1431	1553	47.96	52.04
8	14	9	6	15	2981	9.53	103		1416	1565	47.5	52.5
8	13	9	5	17	2980	9.52	104		1352	1628	45.37	54.63
4	24	9	6	16	2979	9.52	105		1395	1584	46.83	53.17
9	4	9	6	18	2979	9.52	106		1544	1435	51.83	48.17
7	16	9	5	16	2977	9.51	107		1265	1712	42.49	57.51
8	27	9	5	17	2975	9.51	108		1326	1649	44.57	55.43
8	16	9	1	14	2973	9.5	109		1540	1433	51.8	48.2
7	7	9	3	17	2965	9.48	110		1254	1711	42.29	57.71
8	7	9	6	18	2961	9.46	111		1398	1563	47.21	52.79
1	16	9	6	17	2956	9.45	112		1326	1630	44.86	55.14
9	3	9	5	17	2956	9.45	113		1401	1555	47.4	52.6
6	11	9	5	17	2954	9.44	114		1234	1720	41.77	58.23
8	20	9	5	18	2953	9.44	115		1322	1631	44.77	55.23
10	8	9	5	17	2950	9.43	116		1358	1592	46.03	53.97
8	16	9	1	17	2946	9.42	117		1449	1497	49.19	50.81
3	6	9	6	17	2944	9.41	118		1305	1639	44.33	55.67
1	23	9	6	17	2943	9.41	119		1353	1590	45.97	54.03
11	20	9	6	17	2943	9.41	120		1308	1635	44.44	55.56
5	21	9	5	18	2942	9.4	121	31288	1395	1547	47.42	52.58

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
9	17	9	5	17	2937	9.39	122		1325	1612	45.11	54.89
8	19	9	4	17	2935	9.38	123		1243	1692	42.35	57.65
4	3	9	6	17	2932	9.37	124		1364	1568	46.52	53.48
3	20	9	6	16	2931	9.37	125		1269	1662	43.3	56.7
7	9	9	5	17	2930	9.36	126		1280	1650	43.69	56.31
4	24	9	6	18	2926	9.35	127		1457	1469	49.79	50.21
11	25	9	4	18	2919	9.33	128		1340	1579	45.91	54.09
7	15	9	4	17	2917	9.32	129		1276	1641	43.74	56.26
6	11	9	5	18	2916	9.32	130		1227	1689	42.08	57.92
7	23	9	5	18	2916	9.32	131		1266	1650	43.42	56.58
8	7	9	6	15	2916	9.32	132		1459	1457	50.03	49.97
9	25	9	6	16	2916	9.32	133		1284	1632	44.03	55.97
6	21	9	1	15	2906	9.29	134		1353	1553	46.56	53.44
8	20	9	5	17	2904	9.28	135		1315	1589	45.28	54.72
3	6	9	6	16	2902	9.28	136		1323	1579	45.59	54.41
7	22	9	4	17	2901	9.27	137		1265	1636	43.61	56.39
8	23	9	1	16	2901	9.27	138		1295	1606	44.64	55.36
9	24	9	5	17	2899	9.27	139		1328	1571	45.81	54.19
8	16	9	1	15	2898	9.26	140		1379	1519	47.58	52.42
10	16	9	6	18	2897	9.26	141	31288	1392	1505	48.05	51.95
7	10	9	6	15	2894	9.25	142		1343	1551	46.41	53.59
7	30	9	5	16	2894	9.25	143		1240	1654	42.85	57.15
6	18	9	5	18	2890	9.24	144		1300	1590	44.98	55.02
7	6	9	2	17	2890	9.24	145		1173	1717	40.59	59.41
8	16	9	1	16	2889	9.23	146		1450	1439	50.19	49.81
10	9	9	6	18	2888	9.23	147		1467	1421	50.8	49.2
8	26	9	4	17	2882	9.21	148		1264	1618	43.86	56.14
3	26	9	5	17	2880	9.2	149		1231	1649	42.74	57.26
2	6	9	6	17	2876	9.19	150		1278	1598	44.44	55.56
6	10	9	4	17	2876	9.19	151		1238	1638	43.05	56.95
3	6	9	6	18	2874	9.19	152		1284	1590	44.68	55.32
4	17	9	6	16	2874	9.19	153		1348	1526	46.9	53.1
3	13	9	6	16	2873	9.18	154		1272	1601	44.27	55.73
4	17	9	6	18	2873	9.18	155		1359	1514	47.3	52.7
10	30	9	6	18	2870	9.17	156		1396	1474	48.64	51.36
8	31	9	2	17	2869	9.17	157		1188	1681	41.41	58.59
8	28	9	6	15	2866	9.16	158		1389	1477	48.46	51.54
9	3	9	5	18	2866	9.16	159		1388	1478	48.43	51.57
9	4	9	6	15	2866	9.16	160		1524	1342	53.18	46.82
10	8	9	5	18	2860	9.14	161	31288	1360	1500	47.55	52.45
6	4	9	5	17	2858	9.13	162		1229	1629	43	57
9	17	9	5	18	2858	9.13	163		1270	1588	44.44	55.56
5	22	9	6	14	2857	9.13	164		1607	1250	56.25	43.75
10	16	9	6	16	2857	9.13	165		1455	1402	50.93	49.07
10	2	9	6	16	2855	9.12	166		1390	1465	48.69	51.31
2	16	9	2	16	2854	9.12	167		1252	1602	43.87	56.13
7	19	9	1	17	2854	9.12	168		1376	1478	48.21	51.79
10	23	9	6	16	2854	9.12	169		1446	1408	50.67	49.33
8	16	9	1	18	2853	9.12	170		1323	1530	46.37	53.63
7	1	9	4	18	2849	9.11	171		1255	1594	44.05	55.95
7	1	9	4	17	2847	9.1	172		1245	1602	43.73	56.27
7	9	9	5	18	2847	9.1	173		1248	1599	43.84	56.16

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
11	20	9	6	16	2846	9.1	174		1272	1574	44.69	55.31
7	30	9	5	17	2845	9.09	175		1319	1526	46.36	53.64
1	16	9	6	16	2842	9.08	176		1267	1575	44.58	55.42
4	10	9	6	17	2842	9.08	177		1367	1475	48.1	51.9
11	29	9	1	15	2842	9.08	178		1468	1374	51.65	48.35
8	12	9	4	17	2840	9.08	179		1297	1543	45.67	54.33
2	16	9	2	17	2838	9.07	180		1201	1637	42.32	57.68
6	18	9	5	16	2838	9.07	181	31288	1293	1545	45.56	54.44
8	13	9	5	16	2837	9.07	182		1326	1511	46.74	53.26
7	23	9	5	16	2834	9.06	183		1248	1586	44.04	55.96
11	29	9	1	14	2834	9.06	184		1610	1224	56.81	43.19
6	17	9	4	17	2833	9.05	185		1273	1560	44.93	55.07
10	14	9	4	18	2832	9.05	186		1477	1355	52.15	47.85
7	15	9	4	16	2829	9.04	187		1151	1678	40.69	59.31
7	17	9	6	14	2829	9.04	188		1368	1461	48.36	51.64
8	27	9	5	16	2828	9.04	189		1286	1542	45.47	54.53
7	19	9	1	14	2827	9.04	190		1333	1494	47.15	52.85
10	29	9	5	17	2827	9.04	191		1226	1601	43.37	56.63
11	24	9	3	17	2827	9.04	192		1212	1615	42.87	57.13
8	23	9	1	15	2824	9.03	193		1322	1502	46.81	53.19
11	12	9	5	18	2823	9.02	194		1311	1512	46.44	53.56
8	19	9	4	18	2822	9.02	195		1282	1540	45.43	54.57
8	24	9	2	17	2822	9.02	196		1185	1637	41.99	58.01
7	13	9	2	17	2821	9.02	197		1165	1656	41.3	58.7
8	2	9	1	15	2821	9.02	198		1301	1520	46.12	53.88
8	17	9	2	17	2820	9.01	199		1202	1618	42.62	57.38
5	15	9	6	15	2819	9.01	200		1397	1422	49.56	50.44

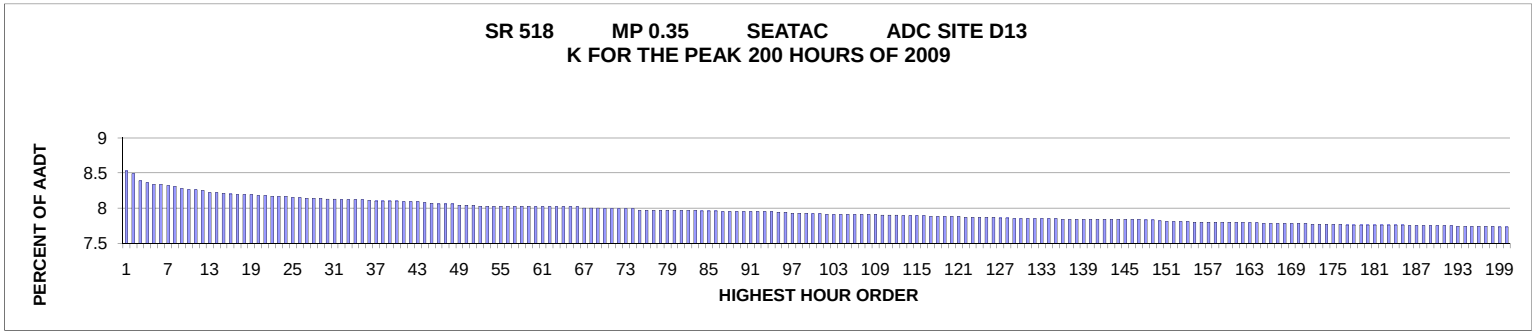

AADT= 54561 K 30 FACTOR= 8.13 K 100 FACTOR= 7.92 K 200 FACTOR= 7.73 D FACTOR= 55.44

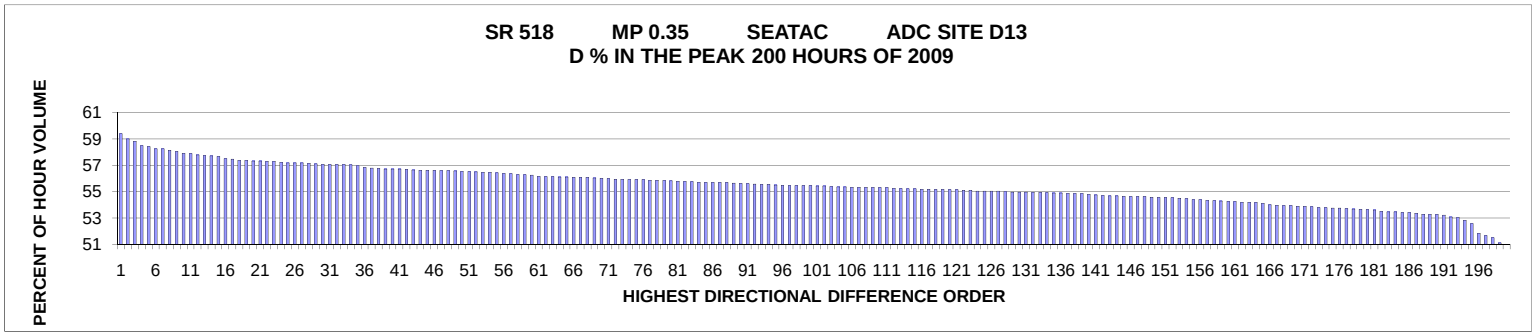

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
12	23	9	4	17	4654	8.53	1	54561	2153	2501	46.26	53.74
12	18	9	6	17	4630	8.49	2		1957	2673	42.27	57.73
2	13	9	6	17	4579	8.39	3		2046	2533	44.68	55.32
6	16	9	3	18	4563	8.36	4		1871	2692	41	59
12	23	9	4	16	4551	8.34	5		2126	2425	46.72	53.28
1	30	9	6	16	4550	8.34	6		1974	2576	43.38	56.62
12	18	9	6	18	4538	8.32	7		2037	2501	44.89	55.11
12	22	9	3	17	4533	8.31	8		2086	2447	46.02	53.98
5	21	9	5	18	4517	8.28	9		1879	2638	41.6	58.4
5	15	9	6	16	4508	8.26	10		2053	2455	45.54	54.46
10	9	9	6	18	4507	8.26	11		2043	2464	45.33	54.67
6	19	9	6	17	4504	8.25	12		2033	2471	45.14	54.86
12	17	9	5	18	4487	8.22	13		1953	2534	43.53	56.47
12	18	9	6	16	4484	8.22	14		2023	2461	45.12	54.88
7	23	9	5	18	4477	8.21	15		1964	2513	43.87	56.13
8	20	9	5	18	4473	8.2	16		1950	2523	43.59	56.41
11	25	9	4	16	4469	8.19	17		2015	2454	45.09	54.91

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
6	17	9	4	18	4466	8.19	18		1982	2484	44.38	55.62
7	10	9	6	17	4466	8.19	19		1906	2560	42.68	57.32
12	23	9	4	14	4465	8.18	20		2166	2299	48.51	51.49
12	11	9	6	17	4463	8.18	21	54561	1978	2485	44.32	55.68
1	16	9	6	17	4458	8.17	22		1957	2501	43.9	56.1
12	4	9	6	17	4458	8.17	23		2034	2424	45.63	54.37
7	23	9	5	17	4455	8.17	24		1914	2541	42.96	57.04
6	5	9	6	18	4446	8.15	25		2034	2412	45.75	54.25
2	27	9	6	17	4445	8.15	26		1986	2459	44.68	55.32
1	16	9	6	18	4443	8.14	27		1894	2549	42.63	57.37
5	1	9	6	17	4442	8.14	28		1959	2483	44.1	55.9
7	10	9	6	18	4440	8.14	29		1917	2523	43.18	56.82
6	5	9	6	17	4435	8.13	30		1947	2488	43.9	56.1
8	21	9	6	18	4435	8.13	31		2028	2407	45.73	54.27
6	19	9	6	18	4433	8.12	32		2010	2423	45.34	54.66
7	8	9	4	17	4433	8.12	33		1925	2508	43.42	56.58
7	30	9	5	17	4433	8.12	34		1900	2533	42.86	57.14
2	13	9	6	16	4431	8.12	35		1989	2442	44.89	55.11
8	7	9	6	17	4423	8.11	36		1888	2535	42.69	57.31
10	16	9	6	18	4422	8.1	37		2077	2345	46.97	53.03
6	12	9	6	18	4419	8.1	38		1969	2450	44.56	55.44
11	20	9	6	18	4419	8.1	39		1987	2432	44.96	55.04
8	6	9	5	18	4417	8.1	40		1897	2520	42.95	57.05
1	30	9	6	17	4415	8.09	41	54561	1889	2526	42.79	57.21
11	6	9	6	17	4415	8.09	42		2066	2349	46.8	53.2
10	2	9	6	18	4413	8.09	43		2035	2378	46.11	53.89
6	11	9	5	17	4407	8.08	44		1912	2495	43.39	56.61
4	9	9	5	18	4404	8.07	45		1932	2472	43.87	56.13
7	15	9	4	18	4400	8.06	46		1861	2539	42.3	57.7
6	4	9	5	18	4398	8.06	47		1837	2561	41.77	58.23
5	8	9	6	17	4395	8.06	48		2014	2381	45.82	54.18
11	20	9	6	17	4388	8.04	49		2045	2343	46.6	53.4
7	16	9	5	18	4387	8.04	50		1847	2540	42.1	57.9
5	7	9	5	18	4386	8.04	51		1966	2420	44.82	55.18
6	26	9	6	18	4383	8.03	52		1989	2394	45.38	54.62
12	11	9	6	18	4383	8.03	53		1877	2506	42.82	57.18
12	23	9	4	15	4383	8.03	54		2048	2335	46.73	53.27
5	22	9	6	17	4382	8.03	55		2040	2342	46.55	53.45
6	12	9	6	17	4382	8.03	56		1907	2475	43.52	56.48
4	24	9	6	18	4381	8.03	57		1985	2396	45.31	54.69
6	25	9	5	18	4380	8.03	58		1937	2443	44.22	55.78
10	23	9	6	18	4379	8.03	59		2021	2358	46.15	53.85
8	13	9	5	18	4378	8.02	60		1832	2546	41.85	58.15
7	16	9	5	17	4377	8.02	61	54561	1869	2508	42.7	57.3
2	6	9	6	17	4376	8.02	62		1901	2475	43.44	56.56
5	15	9	6	18	4376	8.02	63		1913	2463	43.72	56.28
2	20	9	6	17	4375	8.02	64		1939	2436	44.32	55.68
7	2	9	5	17	4375	8.02	65		2023	2352	46.24	53.76
5	8	9	6	16	4374	8.02	66		2076	2298	47.46	52.54
5	20	9	4	18	4365	8	67		1888	2477	43.25	56.75
7	9	9	5	17	4363	8	68		1869	2494	42.84	57.16
8	14	9	6	16	4363	8	69		2010	2353	46.07	53.93

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
5	20	9	4	17	4362	7.99	70		1923	2439	44.09	55.91
7	8	9	4	18	4361	7.99	71		1877	2484	43.04	56.96
7	15	9	4	17	4360	7.99	72		1874	2486	42.98	57.02
7	24	9	6	17	4360	7.99	73		1921	2439	44.06	55.94
9	25	9	6	18	4359	7.99	74		1989	2370	45.63	54.37
7	17	9	6	17	4351	7.97	75		1911	2440	43.92	56.08
5	22	9	6	16	4350	7.97	76		2025	2325	46.55	53.45
7	31	9	6	17	4350	7.97	77		1928	2422	44.32	55.68
8	14	9	6	17	4349	7.97	78		1943	2406	44.68	55.32
12	23	9	4	18	4349	7.97	79		1987	2362	45.69	54.31
6	11	9	5	18	4347	7.97	80		1916	2431	44.08	55.92
12	17	9	5	17	4347	7.97	81	54561	1950	2397	44.86	55.14
5	15	9	6	17	4346	7.97	82		1886	2460	43.4	56.6
8	28	9	6	17	4346	7.97	83		1912	2434	43.99	56.01
8	14	9	6	18	4344	7.96	84		1930	2414	44.43	55.57
8	28	9	6	18	4344	7.96	85		1988	2356	45.76	54.24
7	31	9	6	15	4342	7.96	86		1974	2368	45.46	54.54
2	13	9	6	18	4340	7.95	87		1939	2401	44.68	55.32
6	26	9	6	17	4340	7.95	88		1930	2410	44.47	55.53
12	22	9	3	16	4339	7.95	89		2012	2327	46.37	53.63
4	17	9	6	17	4338	7.95	90		1916	2422	44.17	55.83
5	1	9	6	18	4337	7.95	91		1920	2417	44.27	55.73
8	21	9	6	17	4337	7.95	92		1954	2383	45.05	54.95
6	15	9	2	18	4336	7.95	93		1971	2365	45.46	54.54
12	22	9	3	18	4336	7.95	94		1973	2363	45.5	54.5
8	5	9	4	18	4332	7.94	95		1825	2507	42.13	57.87
10	22	9	5	18	4332	7.94	96		1931	2401	44.58	55.42
7	30	9	5	18	4328	7.93	97		1901	2427	43.92	56.08
12	3	9	5	17	4325	7.93	98		1949	2376	45.06	54.94
12	11	9	6	16	4325	7.93	99		1994	2331	46.1	53.9
6	16	9	3	17	4320	7.92	100		1779	2541	41.18	58.82
7	7	9	3	17	4319	7.92	101	54561	1880	2439	43.53	56.47
6	24	9	4	18	4317	7.91	102		1944	2373	45.03	54.97
7	9	9	5	18	4317	7.91	103		1822	2495	42.21	57.79
8	7	9	6	18	4317	7.91	104		1934	2383	44.8	55.2
10	9	9	6	17	4317	7.91	105		1944	2373	45.03	54.97
6	18	9	5	18	4316	7.91	106		1909	2407	44.23	55.77
4	3	9	6	18	4315	7.91	107		1932	2383	44.77	55.23
12	10	9	5	17	4315	7.91	108		1868	2447	43.29	56.71
6	5	9	6	16	4314	7.91	109		1977	2337	45.83	54.17
5	8	9	6	18	4310	7.9	110		2000	2310	46.4	53.6
2	6	9	6	18	4308	7.9	111		1865	2443	43.29	56.71
11	25	9	4	17	4308	7.9	112		2007	2301	46.59	53.41
5	14	9	5	18	4307	7.89	113		1954	2353	45.37	54.63
9	4	9	6	17	4307	7.89	114		2032	2275	47.18	52.82
6	25	9	5	17	4305	7.89	115		1931	2374	44.85	55.15
12	22	9	3	15	4304	7.89	116		2020	2284	46.93	53.07
8	12	9	4	17	4300	7.88	117		1934	2366	44.98	55.02
7	1	9	4	17	4299	7.88	118		1951	2348	45.38	54.62
10	15	9	5	18	4299	7.88	119		1907	2392	44.36	55.64
4	24	9	6	17	4298	7.88	120		1940	2358	45.14	54.86
6	26	9	6	16	4297	7.88	121	54561	1979	2318	46.06	53.94

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
6	24	9	4	17	4296	7.87	122		1887	2409	43.92	56.08
3	6	9	6	17	4294	7.87	123		1937	2357	45.11	54.89
1	23	9	6	17	4292	7.87	124		1861	2431	43.36	56.64
7	24	9	6	18	4292	7.87	125		1859	2433	43.31	56.69
7	31	9	6	18	4292	7.87	126		1947	2345	45.36	54.64
11	13	9	6	18	4290	7.86	127		1987	2303	46.32	53.68
9	18	9	6	17	4288	7.86	128		1928	2360	44.96	55.04
3	20	9	6	18	4285	7.85	129		1892	2393	44.15	55.85
7	10	9	6	16	4285	7.85	130		1937	2348	45.2	54.8
10	30	9	6	17	4285	7.85	131		1967	2318	45.9	54.1
12	4	9	6	16	4284	7.85	132		1948	2336	45.47	54.53
2	21	9	7	17	4283	7.85	133		1778	2505	41.51	58.49
3	6	9	6	16	4283	7.85	134		1998	2285	46.65	53.35
12	18	9	6	15	4282	7.85	135		2094	2188	48.9	51.1
2	27	9	6	18	4280	7.84	136		1937	2343	45.26	54.74
7	14	9	3	17	4280	7.84	137		1738	2542	40.61	59.39
1	9	9	6	17	4279	7.84	138		1908	2371	44.59	55.41
9	16	9	4	18	4279	7.84	139		1852	2427	43.28	56.72
12	21	9	2	17	4279	7.84	140		1904	2375	44.5	55.5
8	7	9	6	16	4278	7.84	141	54561	1989	2289	46.49	53.51
12	16	9	4	17	4278	7.84	142		1787	2491	41.77	58.23
7	1	9	4	18	4277	7.84	143		1857	2420	43.42	56.58
7	24	9	6	16	4277	7.84	144		1978	2299	46.25	53.75
8	20	9	5	17	4277	7.84	145		1894	2383	44.28	55.72
12	24	9	5	15	4276	7.84	146		2060	2216	48.18	51.82
4	23	9	5	18	4275	7.84	147		1836	2439	42.95	57.05
6	18	9	5	17	4274	7.83	148		1917	2357	44.85	55.15
10	29	9	5	17	4272	7.83	149		1846	2426	43.21	56.79
5	29	9	6	17	4266	7.82	150		1905	2361	44.66	55.34
12	10	9	5	16	4263	7.81	151		1899	2364	44.55	55.45
7	22	9	4	17	4262	7.81	152		1859	2403	43.62	56.38
12	9	9	4	18	4261	7.81	153		1788	2473	41.96	58.04
8	12	9	4	18	4259	7.81	154		1852	2407	43.48	56.52
2	27	9	6	16	4258	7.8	155		1990	2268	46.74	53.26
9	18	9	6	18	4258	7.8	156		1887	2371	44.32	55.68
12	16	9	4	18	4257	7.8	157		1881	2376	44.19	55.81
4	10	9	6	17	4256	7.8	158		1918	2338	45.07	54.93
3	27	9	6	18	4254	7.8	159		1913	2341	44.97	55.03
7	17	9	6	16	4254	7.8	160		1933	2321	45.44	54.56
9	3	9	5	18	4254	7.8	161	54561	1825	2429	42.9	57.1
11	20	9	6	16	4254	7.8	162		1959	2295	46.05	53.95
7	13	9	2	18	4251	7.79	163		1876	2375	44.13	55.87
3	18	9	4	18	4248	7.79	164		1917	2331	45.13	54.87
9	4	9	6	18	4247	7.78	165		1969	2278	46.36	53.64
12	9	9	4	17	4247	7.78	166		1899	2348	44.71	55.29
7	31	9	6	16	4246	7.78	167		1805	2441	42.51	57.49
8	6	9	5	17	4245	7.78	168		1872	2373	44.1	55.9
2	12	9	5	17	4244	7.78	169		1818	2426	42.84	57.16
5	21	9	5	17	4244	7.78	170		1853	2391	43.66	56.34
4	3	9	6	17	4243	7.78	171		1868	2375	44.03	55.97
10	28	9	4	18	4241	7.77	172		1898	2343	44.75	55.25
2	21	9	7	13	4240	7.77	173		1963	2277	46.3	53.7

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
1	30	9	6	18	4239	7.77	174		1902	2337	44.87	55.13
9	11	9	6	18	4239	7.77	175		1887	2352	44.52	55.48
12	30	9	4	16	4238	7.77	176		2049	2189	48.35	51.65
12	21	9	2	18	4236	7.76	177		1941	2295	45.82	54.18
6	30	9	3	18	4235	7.76	178		1793	2442	42.34	57.66
7	7	9	3	18	4235	7.76	179		1801	2434	42.53	57.47
7	17	9	6	18	4235	7.76	180		1893	2342	44.7	55.3
12	4	9	6	18	4235	7.76	181	54561	1887	2348	44.56	55.44
6	8	9	2	17	4234	7.76	182		1853	2381	43.76	56.24
10	9	9	6	16	4234	7.76	183		1934	2300	45.68	54.32
11	24	9	3	17	4234	7.76	184		1906	2328	45.02	54.98
5	14	9	5	17	4233	7.76	185		1890	2343	44.65	55.35
12	24	9	5	14	4231	7.75	186		2156	2075	50.96	49.04
8	4	9	3	18	4230	7.75	187		1860	2370	43.97	56.03
3	11	9	4	18	4229	7.75	188		1896	2333	44.83	55.17
3	27	9	6	17	4229	7.75	189		1888	2341	44.64	55.36
2	20	9	6	16	4227	7.75	190		1954	2273	46.23	53.77
6	17	9	4	17	4226	7.75	191		1848	2378	43.73	56.27
12	3	9	5	18	4226	7.75	192		1814	2412	42.92	57.08
10	8	9	5	18	4225	7.74	193		1878	2347	44.45	55.55
12	2	9	4	18	4225	7.74	194		1801	2424	42.63	57.37
8	13	9	5	17	4224	7.74	195		1892	2332	44.79	55.21
12	2	9	4	17	4222	7.74	196		1803	2419	42.7	57.3
6	22	9	2	18	4221	7.74	197		1881	2340	44.56	55.44
12	10	9	5	18	4221	7.74	198		1874	2347	44.4	55.6
8	10	9	2	17	4220	7.73	199		1834	2386	43.46	56.54
1	23	9	6	18	4219	7.73	200		1850	2369	43.85	56.15

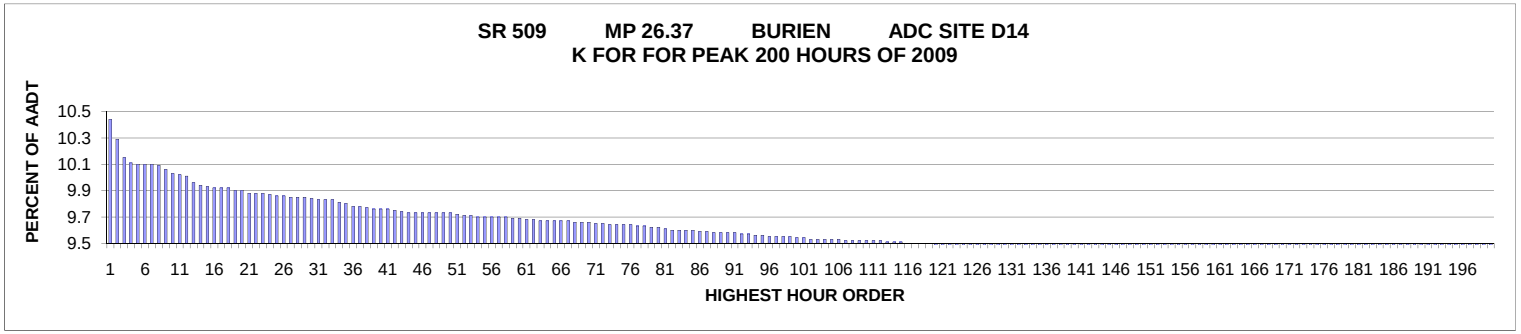

AADT= 57371 **K 30 FACTOR=** 9.84 **K 100 FACTOR=** 9.54 **K 200 FACTOR=** 9.3 **D FACTOR=** 59.74

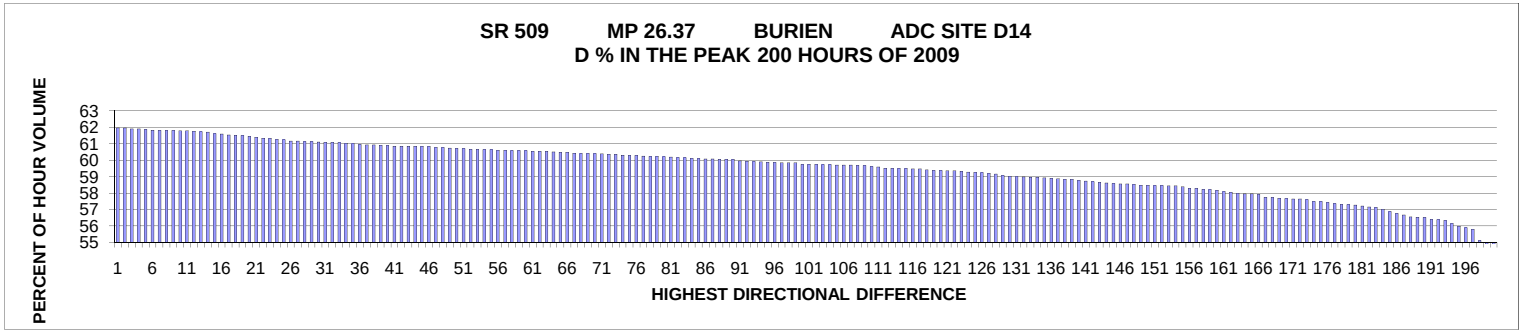

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
5	15	9	6	17	5988	10.44	1	57371	2531	3457	42.27	57.73
6	16	9	3	18	5904	10.29	2		2686	3218	45.49	54.51
5	21	9	5	17	5822	10.15	3		2405	3417	41.31	58.69
5	1	9	6	17	5801	10.11	4		2386	3415	41.13	58.87
6	5	9	6	17	5794	10.1	5		2335	3459	40.3	59.7
6	24	9	4	17	5793	10.1	6		2269	3524	39.17	60.83
6	19	9	6	17	5792	10.1	7		2416	3376	41.71	58.29
5	13	9	4	17	5787	10.09	8		2291	3496	39.59	60.41
2	27	9	6	17	5769	10.06	9		2304	3465	39.94	60.06
6	11	9	5	17	5756	10.03	10		2286	3470	39.72	60.28
6	10	9	4	17	5748	10.02	11		2317	3431	40.31	59.69
7	30	9	5	17	5740	10.01	12		2311	3429	40.26	59.74
1	23	9	6	17	5716	9.96	13		2228	3488	38.98	61.02
6	17	9	4	18	5703	9.94	14		2460	3243	43.14	56.86
4	21	9	3	17	5695	9.93	15		2234	3461	39.23	60.77
6	17	9	4	17	5694	9.92	16		2364	3330	41.52	58.48
5	15	9	6	18	5693	9.92	17		2555	3138	44.88	55.12

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	23	9	5	17	5689	9.92	18		2334	3355	41.03	58.97
3	19	9	5	17	5681	9.9	19		2391	3290	42.09	57.91
12	10	9	5	17	5677	9.9	20		2299	3378	40.5	59.5
5	20	9	4	17	5671	9.88	21	57371	2321	3350	40.93	59.07
6	16	9	3	17	5671	9.88	22		2426	3245	42.78	57.22
9	24	9	5	17	5671	9.88	23		2177	3494	38.39	61.61
5	14	9	5	17	5664	9.87	24		2232	3432	39.41	60.59
9	10	9	5	18	5659	9.86	25		2161	3498	38.19	61.81
2	13	9	6	17	5655	9.86	26		2175	3480	38.46	61.54
5	7	9	5	18	5653	9.85	27		2377	3276	42.05	57.95
6	18	9	5	18	5653	9.85	28		2415	3238	42.72	57.28
12	3	9	5	17	5652	9.85	29		2243	3409	39.69	60.31
5	28	9	5	17	5643	9.84	30		2287	3356	40.53	59.47
1	30	9	6	17	5642	9.83	31		2254	3388	39.95	60.05
4	17	9	6	17	5640	9.83	32		2291	3349	40.62	59.38
1	16	9	6	17	5639	9.83	33		2166	3473	38.41	61.59
3	6	9	6	17	5630	9.81	34		2147	3483	38.13	61.87
7	29	9	4	17	5621	9.8	35		2286	3335	40.67	59.33
10	15	9	5	17	5613	9.78	36		2212	3401	39.41	60.59
12	9	9	4	17	5612	9.78	37		2182	3430	38.88	61.12
1	9	9	6	17	5603	9.77	38		2166	3437	38.66	61.34
1	15	9	5	17	5601	9.76	39		2192	3409	39.14	60.86
5	21	9	5	18	5600	9.76	40		2551	3049	45.55	54.45
2	20	9	6	17	5597	9.76	41	57371	2138	3459	38.2	61.8
2	12	9	5	17	5594	9.75	42		2208	3386	39.47	60.53
4	30	9	5	17	5586	9.74	43		2289	3297	40.98	59.02
5	29	9	6	17	5585	9.73	44		2251	3334	40.3	59.7
3	13	9	6	17	5584	9.73	45		2159	3425	38.66	61.34
6	11	9	5	18	5584	9.73	46		2374	3210	42.51	57.49
12	4	9	6	17	5583	9.73	47		2209	3374	39.57	60.43
6	24	9	4	18	5581	9.73	48		2363	3218	42.34	57.66
11	12	9	5	17	5581	9.73	49		2126	3455	38.09	61.91
4	9	9	5	17	5580	9.73	50		2137	3443	38.3	61.7
5	7	9	5	17	5579	9.72	51		2226	3353	39.9	60.1
4	16	9	5	17	5568	9.71	52		2242	3326	40.27	59.73
12	2	9	4	17	5568	9.71	53		2219	3349	39.85	60.15
6	3	9	4	17	5567	9.7	54		2218	3349	39.84	60.16
2	25	9	4	17	5564	9.7	55		2157	3407	38.77	61.23
6	12	9	6	18	5564	9.7	56		2294	3270	41.23	58.77
4	24	9	6	17	5563	9.7	57		2187	3376	39.31	60.69
5	20	9	4	18	5563	9.7	58		2448	3115	44.01	55.99
6	18	9	5	17	5561	9.69	59		2284	3277	41.07	58.93
5	13	9	4	18	5558	9.69	60		2219	3339	39.92	60.08
3	11	9	4	17	5554	9.68	61	57371	2174	3380	39.14	60.86
6	12	9	6	17	5552	9.68	62		2257	3295	40.65	59.35
1	15	9	5	18	5550	9.67	63		2297	3253	41.39	58.61
5	27	9	4	17	5550	9.67	64		2224	3326	40.07	59.93
11	6	9	6	17	5546	9.67	65		2171	3375	39.15	60.85
5	8	9	6	17	5545	9.67	66		2177	3368	39.26	60.74
10	16	9	6	18	5545	9.67	67		2215	3330	39.95	60.05
7	16	9	5	17	5543	9.66	68		2246	3297	40.52	59.48
3	12	9	5	17	5542	9.66	69		2117	3425	38.2	61.8

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
10	16	9	6	17	5542	9.66	70		2169	3373	39.14	60.86
11	5	9	5	17	5538	9.65	71		2245	3293	40.54	59.46
4	15	9	4	17	5535	9.65	72		2204	3331	39.82	60.18
8	20	9	5	17	5532	9.64	73		2177	3355	39.35	60.65
3	27	9	6	17	5529	9.64	74		2151	3378	38.9	61.1
4	23	9	5	17	5529	9.64	75		2162	3367	39.1	60.9
12	1	9	3	18	5529	9.64	76		2214	3315	40.04	59.96
7	23	9	5	18	5527	9.63	77		2292	3235	41.47	58.53
1	22	9	5	17	5526	9.63	78		2109	3417	38.17	61.83
7	10	9	6	17	5519	9.62	79		2366	3153	42.87	57.13
3	26	9	5	17	5518	9.62	80		2130	3388	38.6	61.4
10	1	9	5	17	5512	9.61	81	57371	2189	3323	39.71	60.29
11	19	9	5	17	5510	9.6	82		2172	3338	39.42	60.58
6	4	9	5	18	5509	9.6	83		2395	3114	43.47	56.53
6	23	9	3	17	5508	9.6	84		2182	3326	39.62	60.38
6	25	9	5	17	5507	9.6	85		2212	3295	40.17	59.83
7	9	9	5	17	5503	9.59	86		2265	3238	41.16	58.84
9	17	9	5	18	5503	9.59	87		2236	3267	40.63	59.37
7	1	9	4	17	5499	9.58	88		2144	3355	38.99	61.01
6	19	9	6	18	5495	9.58	89		2397	3098	43.62	56.38
6	26	9	6	17	5495	9.58	90		2194	3301	39.93	60.07
5	15	9	6	16	5494	9.58	91		2305	3189	41.95	58.05
8	19	9	4	17	5493	9.57	92		2102	3391	38.27	61.73
2	12	9	5	18	5492	9.57	93		2266	3226	41.26	58.74
12	8	9	3	17	5485	9.56	94		2146	3339	39.12	60.88
8	6	9	5	18	5483	9.56	95		2357	3126	42.99	57.01
3	18	9	4	18	5481	9.55	96		2277	3204	41.54	58.46
3	18	9	4	17	5479	9.55	97		2169	3310	39.59	60.41
8	6	9	5	17	5479	9.55	98		2207	3272	40.28	59.72
6	2	9	3	17	5477	9.55	99		2264	3213	41.34	58.66
1	14	9	4	17	5473	9.54	100		2208	3265	40.34	59.66
7	1	9	4	18	5471	9.54	101	57371	2268	3203	41.45	58.55
5	14	9	5	18	5470	9.53	102		2298	3172	42.01	57.99
8	20	9	5	18	5467	9.53	103		2384	3083	43.61	56.39
3	24	9	3	17	5466	9.53	104		2194	3272	40.14	59.86
3	12	9	5	18	5465	9.53	105		2180	3285	39.89	60.11
12	11	9	6	17	5465	9.53	106		2274	3191	41.61	58.39
7	2	9	5	17	5464	9.52	107		2127	3337	38.93	61.07
8	12	9	4	17	5464	9.52	108		2151	3313	39.37	60.63
1	21	9	4	17	5460	9.52	109		2105	3355	38.55	61.45
11	20	9	6	17	5460	9.52	110		2219	3241	40.64	59.36
3	5	9	5	17	5459	9.52	111		2170	3289	39.75	60.25
7	22	9	4	17	5459	9.52	112		2198	3261	40.26	59.74
3	3	9	3	17	5458	9.51	113		2172	3286	39.79	60.21
6	30	9	3	17	5455	9.51	114		2222	3233	40.73	59.27
6	26	9	6	18	5454	9.51	115		2326	3128	42.65	57.35
4	10	9	6	17	5452	9.5	116		2129	3323	39.05	60.95
5	19	9	3	17	5452	9.5	117		2197	3255	40.3	59.7
5	22	9	6	17	5452	9.5	118		2278	3174	41.78	58.22
4	1	9	4	18	5449	9.5	119		2308	3141	42.36	57.64
5	28	9	5	18	5440	9.48	120		2366	3074	43.49	56.51
6	15	9	2	18	5440	9.48	121	57371	2254	3186	41.43	58.57

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	13	9	5	17	5440	9.48	122		2216	3224	40.74	59.26
9	25	9	6	18	5440	9.48	123		2302	3138	42.32	57.68
2	3	9	3	17	5439	9.48	124		2144	3295	39.42	60.58
7	24	9	6	17	5432	9.47	125		2235	3197	41.15	58.85
12	1	9	3	17	5432	9.47	126		2112	3320	38.88	61.12
6	25	9	5	18	5431	9.47	127		2348	3083	43.23	56.77
5	12	9	3	17	5430	9.46	128		2177	3253	40.09	59.91
8	5	9	4	18	5430	9.46	129		2395	3035	44.11	55.89
2	19	9	5	17	5428	9.46	130		2121	3307	39.08	60.92
9	17	9	5	17	5428	9.46	131		2151	3277	39.63	60.37
9	16	9	4	18	5427	9.46	132		2230	3197	41.09	58.91
6	10	9	4	18	5422	9.45	133		2356	3066	43.45	56.55
6	23	9	3	18	5420	9.45	134		2267	3153	41.83	58.17
7	15	9	4	18	5419	9.45	135		2307	3112	42.57	57.43
9	18	9	6	17	5418	9.44	136		2211	3207	40.81	59.19
2	5	9	5	17	5416	9.44	137		2120	3296	39.14	60.86
8	14	9	6	17	5415	9.44	138		2188	3227	40.41	59.59
10	28	9	4	17	5415	9.44	139		2172	3243	40.11	59.89
10	22	9	5	17	5413	9.44	140		2153	3260	39.77	60.23
4	23	9	5	18	5411	9.43	141	57371	2310	3101	42.69	57.31
6	9	9	3	17	5410	9.43	142		2133	3277	39.43	60.57
12	2	9	4	18	5410	9.43	143		2300	3110	42.51	57.49
10	21	9	4	17	5409	9.43	144		2096	3313	38.75	61.25
4	9	9	5	18	5408	9.43	145		2219	3189	41.03	58.97
6	15	9	2	17	5405	9.42	146		2065	3340	38.21	61.79
3	20	9	6	18	5404	9.42	147		2203	3201	40.77	59.23
9	11	9	6	17	5403	9.42	148		2127	3276	39.37	60.63
2	4	9	4	17	5402	9.42	149		2188	3214	40.5	59.5
9	15	9	3	18	5402	9.42	150		2314	3088	42.84	57.16
1	16	9	6	18	5399	9.41	151		2270	3129	42.04	57.96
8	27	9	5	17	5399	9.41	152		2187	3212	40.51	59.49
10	29	9	5	18	5398	9.41	153		2305	3093	42.7	57.3
7	15	9	4	17	5397	9.41	154		2262	3135	41.91	58.09
5	19	9	3	18	5394	9.4	155		2366	3028	43.86	56.14
7	22	9	4	18	5394	9.4	156		2285	3109	42.36	57.64
10	8	9	5	18	5390	9.39	157		2240	3150	41.56	58.44
9	16	9	4	17	5389	9.39	158		2075	3314	38.5	61.5
1	28	9	4	17	5384	9.38	159		2048	3336	38.04	61.96
4	8	9	4	17	5384	9.38	160		2104	3280	39.08	60.92
6	8	9	2	17	5382	9.38	161	57371	2094	3288	38.91	61.09
9	15	9	3	17	5382	9.38	162		2126	3256	39.5	60.5
10	27	9	3	17	5381	9.38	163		2094	3287	38.91	61.09
5	27	9	4	18	5376	9.37	164		2330	3046	43.34	56.66
7	16	9	5	18	5376	9.37	165		2279	3097	42.39	57.61
5	26	9	3	18	5375	9.37	166		2164	3211	40.26	59.74
11	3	9	3	17	5375	9.37	167		2124	3251	39.52	60.48
11	12	9	5	18	5375	9.37	168		2181	3194	40.58	59.42
4	22	9	4	17	5373	9.37	169		2231	3142	41.52	58.48
11	18	9	4	17	5373	9.37	170		2087	3286	38.84	61.16
4	29	9	4	17	5366	9.35	171		2120	3246	39.51	60.49
1	8	9	5	17	5365	9.35	172		2117	3248	39.46	60.54
3	10	9	3	18	5365	9.35	173		2199	3166	40.99	59.01

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	19	9	4	18	5365	9.35	174		2223	3142	41.44	58.56
9	25	9	6	17	5365	9.35	175		2083	3282	38.83	61.17
11	24	9	3	17	5364	9.35	176		2041	3323	38.05	61.95
7	9	9	5	18	5363	9.35	177		2342	3021	43.67	56.33
10	6	9	3	17	5363	9.35	178		2049	3314	38.21	61.79
1	30	9	6	16	5360	9.34	179		2227	3133	41.55	58.45
2	6	9	6	17	5359	9.34	180		2152	3207	40.16	59.84
3	10	9	3	17	5359	9.34	181	57371	2041	3318	38.09	61.91
3	25	9	4	17	5359	9.34	182		2115	3244	39.47	60.53
4	13	9	2	17	5359	9.34	183		2049	3310	38.23	61.77
5	22	9	6	16	5359	9.34	184		2165	3194	40.4	59.6
7	7	9	3	17	5357	9.34	185		2121	3236	39.59	60.41
2	24	9	3	17	5352	9.33	186		2102	3250	39.28	60.72
9	2	9	4	18	5352	9.33	187		2150	3202	40.17	59.83
6	30	9	3	18	5350	9.33	188		2232	3118	41.72	58.28
7	8	9	4	18	5349	9.32	189		2236	3113	41.8	58.2
10	23	9	6	17	5348	9.32	190		2194	3154	41.02	58.98
6	3	9	4	18	5347	9.32	191		2364	2983	44.21	55.79
1	7	9	4	17	5346	9.32	192		2057	3289	38.48	61.52
7	8	9	4	17	5346	9.32	193		2260	3086	42.27	57.73
7	31	9	6	17	5345	9.32	194		2126	3219	39.78	60.22
6	22	9	2	17	5344	9.31	195		2144	3200	40.12	59.88
11	17	9	3	17	5344	9.31	196		2118	3226	39.63	60.37
3	4	9	4	17	5343	9.31	197		2102	3241	39.34	60.66
4	24	9	6	18	5342	9.31	198		2220	3122	41.56	58.44
10	19	9	2	17	5341	9.31	199		2095	3246	39.22	60.78
9	3	9	5	17	5338	9.3	200		2180	3158	40.84	59.16

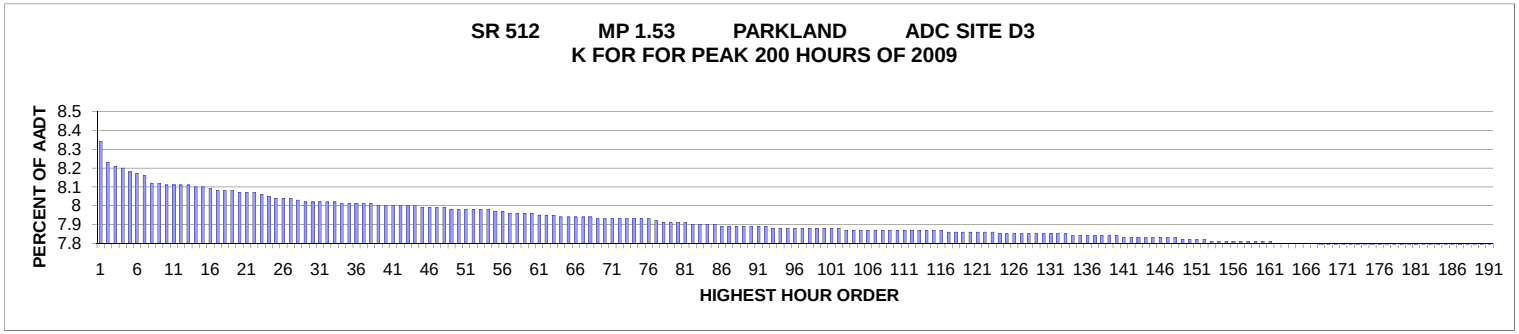

AADT= 88733 **K 30 FACTOR=** 8.07 **K 100 FACTOR=** 7.89 **K 200 FACTOR=** 7.78 **D FACTOR=** 59.07

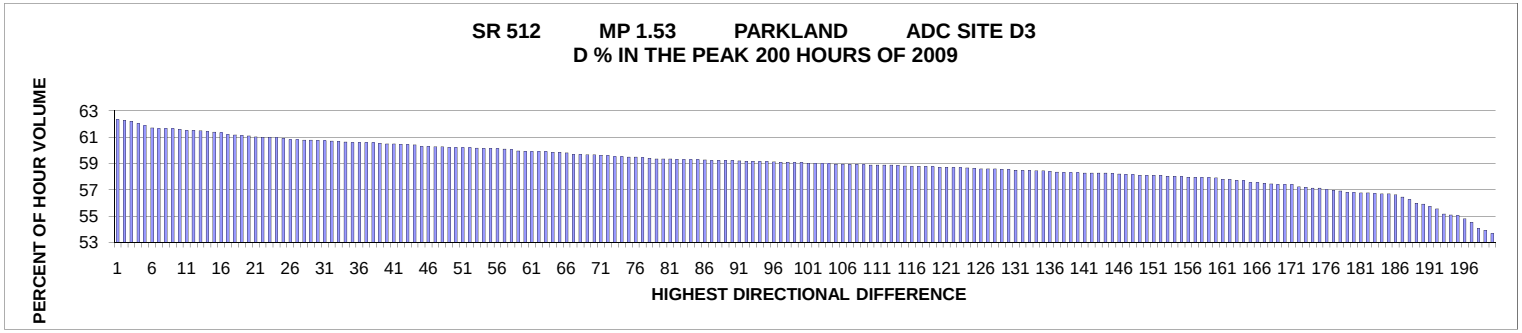

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
2	27	9	6	16	7401	8.34	1	88733	4125	3276	55.74	44.26
1	23	9	6	16	7304	8.23	2		4243	3061	58.09	41.91
10	9	9	6	16	7284	8.21	3		4218	3066	57.91	42.09
2	13	9	6	16	7276	8.2	4		4144	3132	56.95	43.05
1	16	9	6	16	7261	8.18	5		4121	3140	56.76	43.24
3	13	9	6	16	7250	8.17	6		4112	3138	56.72	43.28
3	6	9	6	16	7245	8.16	7		4056	3189	55.98	44.02
5	8	9	6	16	7206	8.12	8		4086	3120	56.7	43.3
4	15	9	4	17	7202	8.12	9		4310	2892	59.84	40.16
4	8	9	4	17	7199	8.11	10		4370	2829	60.7	39.3
2	27	9	6	17	7197	8.11	11		4160	3037	57.8	42.2
4	30	9	5	16	7192	8.11	12		4166	3026	57.93	42.07
5	12	9	3	17	7192	8.11	13		4369	2823	60.75	39.25
4	22	9	4	17	7187	8.1	14		4287	2900	59.65	40.35
3	11	9	4	17	7186	8.1	15		4389	2797	61.08	38.92
4	7	9	3	17	7180	8.09	16		4321	2859	60.18	39.82
9	18	9	6	16	7174	8.08	17		4140	3034	57.71	42.29

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
4	24	9	6	16	7169	8.08	18		4009	3160	55.92	44.08
5	5	9	3	17	7169	8.08	19		4357	2812	60.78	39.22
4	3	9	6	16	7164	8.07	20		4100	3064	57.23	42.77
3	27	9	6	16	7162	8.07	21	88733	4131	3031	57.68	42.32
10	30	9	6	16	7157	8.07	22		4207	2950	58.78	41.22
2	20	9	6	16	7151	8.06	23		4145	3006	57.96	42.04
9	14	9	2	16	7140	8.05	24		4159	2981	58.25	41.75
5	20	9	4	17	7133	8.04	25		4236	2897	59.39	40.61
9	30	9	4	16	7133	8.04	26		4257	2876	59.68	40.32
1	30	9	6	16	7130	8.04	27		4187	2943	58.72	41.28
6	23	9	3	17	7127	8.03	28		4287	2840	60.15	39.85
5	7	9	5	16	7120	8.02	29		4206	2914	59.07	40.93
5	7	9	5	17	7116	8.02	30		4290	2826	60.29	39.71
3	18	9	4	17	7112	8.02	31		4309	2803	60.59	39.41
10	2	9	6	16	7112	8.02	32		4181	2931	58.79	41.21
11	2	9	2	17	7112	8.02	33		4309	2803	60.59	39.41
6	24	9	4	17	7110	8.01	34		4387	2723	61.7	38.3
4	17	9	6	16	7109	8.01	35		4052	3057	57	43
6	5	9	6	16	7108	8.01	36		4087	3021	57.5	42.5
11	3	9	3	17	7107	8.01	37		4293	2814	60.41	39.59
2	12	9	5	17	7104	8.01	38		4237	2867	59.64	40.36
5	1	9	6	16	7103	8	39		3946	3157	55.55	44.45
1	22	9	5	17	7101	8	40		4202	2899	59.17	40.83
10	22	9	5	17	7101	8	41	88733	4367	2734	61.5	38.5
10	8	9	5	16	7099	8	42		4204	2895	59.22	40.78
10	9	9	6	15	7096	8	43		3914	3182	55.16	44.84
4	28	9	3	17	7095	8	44		4320	2775	60.89	39.11
4	16	9	5	17	7093	7.99	45		4142	2951	58.4	41.6
2	3	9	3	17	7091	7.99	46		4306	2785	60.72	39.28
10	20	9	3	17	7090	7.99	47		4370	2720	61.64	38.36
12	3	9	5	16	7086	7.99	48		4097	2989	57.82	42.18
7	1	9	4	16	7085	7.98	49		4066	3019	57.39	42.61
10	28	9	4	17	7085	7.98	50		4345	2740	61.33	38.67
4	15	9	4	16	7082	7.98	51		4173	2909	58.92	41.08
4	23	9	5	17	7081	7.98	52		4202	2879	59.34	40.66
6	23	9	3	16	7080	7.98	53		4125	2955	58.26	41.74
10	5	9	2	17	7077	7.98	54		4280	2797	60.48	39.52
3	26	9	5	17	7070	7.97	55		4205	2865	59.48	40.52
1	15	9	5	17	7069	7.97	56		4254	2815	60.18	39.82
6	25	9	5	16	7065	7.96	57		4151	2914	58.75	41.25
6	3	9	4	16	7063	7.96	58		4166	2897	58.98	41.02
4	29	9	4	17	7061	7.96	59		4252	2809	60.22	39.78
2	19	9	5	17	7059	7.96	60		4188	2871	59.33	40.67
1	15	9	5	16	7053	7.95	61	88733	4169	2884	59.11	40.89
10	7	9	4	16	7053	7.95	62		4175	2878	59.19	40.81
3	27	9	6	17	7050	7.95	63		4152	2898	58.89	41.11
1	21	9	4	16	7047	7.94	64		4179	2868	59.3	40.7
6	25	9	5	17	7047	7.94	65		4238	2809	60.14	39.86
12	18	9	6	16	7047	7.94	66		4153	2894	58.93	41.07
1	9	9	6	16	7042	7.94	67		4145	2897	58.86	41.14
11	4	9	4	16	7042	7.94	68		4241	2801	60.22	39.78
4	8	9	4	16	7040	7.93	69		4115	2925	58.45	41.55

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
9	9	9	4	17	7040	7.93	70		4281	2759	60.81	39.19
9	28	9	2	17	7038	7.93	71		4291	2747	60.97	39.03
2	26	9	5	16	7036	7.93	72		4038	2998	57.39	42.61
6	2	9	3	16	7035	7.93	73		4157	2878	59.09	40.91
6	12	9	6	16	7035	7.93	74		3971	3064	56.45	43.55
9	3	9	5	16	7035	7.93	75		4094	2941	58.19	41.81
6	16	9	3	17	7034	7.93	76		4292	2742	61.02	38.98
10	29	9	5	17	7025	7.92	77		4331	2694	61.65	38.35
9	28	9	2	16	7022	7.91	78		4220	2802	60.1	39.9
2	26	9	5	17	7020	7.91	79		4140	2880	58.97	41.03
4	6	9	2	17	7020	7.91	80		4246	2774	60.48	39.52
6	11	9	5	17	7019	7.91	81	88733	4138	2881	58.95	41.05
8	11	9	3	17	7010	7.9	82		4369	2641	62.33	37.67
4	21	9	3	16	7008	7.9	83		4126	2882	58.88	41.12
4	7	9	3	16	7007	7.9	84		4144	2863	59.14	40.86
10	1	9	5	17	7007	7.9	85		4284	2723	61.14	38.86
2	17	9	3	17	7005	7.89	86		4315	2690	61.6	38.4
11	2	9	2	16	7003	7.89	87		4069	2934	58.1	41.9
9	24	9	5	16	7002	7.89	88		4194	2808	59.9	40.1
11	12	9	5	17	7000	7.89	89		4145	2855	59.21	40.79
11	12	9	5	16	6999	7.89	90		4100	2899	58.58	41.42
5	27	9	4	16	6998	7.89	91		4094	2904	58.5	41.5
3	4	9	4	17	6997	7.89	92		4160	2837	59.45	40.55
3	13	9	6	17	6996	7.88	93		4070	2926	58.18	41.82
1	30	9	6	17	6993	7.88	94		4088	2905	58.46	41.54
12	2	9	4	17	6993	7.88	95		4265	2728	60.99	39.01
4	30	9	5	17	6992	7.88	96		4182	2810	59.81	40.19
2	19	9	5	16	6989	7.88	97		4146	2843	59.32	40.68
2	4	9	4	17	6988	7.88	98		4347	2641	62.21	37.79
5	29	9	6	15	6988	7.88	99		3850	3138	55.09	44.91
6	5	9	6	17	6988	7.88	100		4071	2917	58.26	41.74
9	23	9	4	16	6988	7.88	101	88733	4020	2968	57.53	42.47
12	1	9	3	16	6988	7.88	102		4135	2853	59.17	40.83
10	19	9	2	16	6987	7.87	103		4138	2849	59.22	40.78
10	21	9	4	16	6987	7.87	104		4108	2879	58.79	41.21
6	8	9	2	16	6986	7.87	105		4070	2916	58.26	41.74
1	21	9	4	17	6984	7.87	106		4231	2753	60.58	39.42
10	5	9	2	16	6984	7.87	107		4141	2843	59.29	40.71
11	5	9	5	16	6984	7.87	108		4107	2877	58.81	41.19
2	2	9	2	17	6983	7.87	109		4304	2679	61.64	38.36
11	3	9	3	16	6983	7.87	110		4096	2887	58.66	41.34
11	19	9	5	17	6983	7.87	111		4208	2775	60.26	39.74
3	10	9	3	17	6981	7.87	112		4121	2860	59.03	40.97
4	10	9	6	16	6981	7.87	113		3966	3015	56.81	43.19
4	8	9	4	18	6980	7.87	114		4257	2723	60.99	39.01
4	16	9	5	16	6979	7.87	115		4055	2924	58.1	41.9
10	6	9	3	17	6979	7.87	116		4224	2755	60.52	39.48
8	25	9	3	17	6978	7.86	117		4292	2686	61.51	38.49
12	4	9	6	16	6978	7.86	118		4008	2970	57.44	42.56
5	18	9	2	17	6976	7.86	119		4345	2631	62.28	37.72
5	26	9	3	16	6975	7.86	120		4078	2897	58.47	41.53
9	25	9	6	15	6975	7.86	121	88733	3950	3025	56.63	43.37

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
12	17	9	5	16	6975	7.86	122		4057	2918	58.16	41.84
10	13	9	3	17	6970	7.86	123		4324	2646	62.04	37.96
3	11	9	4	16	6967	7.85	124		4103	2864	58.89	41.11
10	6	9	3	16	6967	7.85	125		4129	2838	59.27	40.73
10	29	9	5	16	6967	7.85	126		4107	2860	58.95	41.05
1	13	9	3	17	6966	7.85	127		4188	2778	60.12	39.88
5	11	9	2	16	6966	7.85	128		4175	2791	59.93	40.07
1	29	9	5	17	6964	7.85	129		4156	2808	59.68	40.32
9	30	9	4	17	6964	7.85	130		4235	2729	60.81	39.19
2	27	9	6	15	6963	7.85	131		3815	3148	54.79	45.21
10	8	9	5	17	6963	7.85	132		4113	2850	59.07	40.93
10	27	9	3	17	6963	7.85	133		4309	2654	61.88	38.12
3	10	9	3	16	6961	7.84	134		4033	2928	57.94	42.06
2	6	9	6	16	6960	7.84	135		3952	3008	56.78	43.22
7	15	9	4	16	6960	7.84	136		4033	2927	57.95	42.05
6	29	9	2	17	6959	7.84	137		4230	2729	60.78	39.22
10	15	9	5	17	6959	7.84	138		4272	2687	61.39	38.61
5	29	9	6	16	6958	7.84	139		3960	2998	56.91	43.09
2	13	9	6	17	6957	7.84	140		3975	2982	57.14	42.86
4	9	9	5	16	6950	7.83	141	88733	4071	2879	58.58	41.42
11	13	9	6	16	6950	7.83	142		4069	2881	58.55	41.45
11	20	9	6	16	6949	7.83	143		4110	2839	59.15	40.85
3	20	9	6	16	6948	7.83	144		3909	3039	56.26	43.74
4	1	9	4	17	6948	7.83	145		4187	2761	60.26	39.74
4	24	9	6	15	6948	7.83	146		3757	3191	54.07	45.93
3	26	9	5	16	6945	7.83	147		4122	2823	59.35	40.65
10	20	9	3	16	6945	7.83	148		4077	2868	58.7	41.3
3	25	9	4	17	6943	7.82	149		4213	2730	60.68	39.32
1	14	9	4	16	6940	7.82	150		4140	2800	59.65	40.35
9	3	9	5	17	6940	7.82	151		4128	2812	59.48	40.52
1	16	9	6	17	6938	7.82	152		4072	2866	58.69	41.31
4	27	9	2	16	6933	7.81	153		4024	2909	58.04	41.96
5	18	9	2	16	6933	7.81	154		4041	2892	58.29	41.71
6	3	9	4	17	6933	7.81	155		4090	2843	58.99	41.01
2	11	9	4	16	6930	7.81	156		4042	2888	58.33	41.67
6	17	9	4	16	6930	7.81	157		4039	2891	58.28	41.72
5	1	9	6	15	6928	7.81	158		3777	3151	54.52	45.48
11	18	9	4	16	6928	7.81	159		4160	2768	60.05	39.95
6	30	9	3	16	6927	7.81	160		4057	2870	58.57	41.43
6	4	9	5	16	6926	7.81	161	88733	4019	2907	58.03	41.97
2	12	9	5	16	6925	7.8	162		4128	2797	59.61	40.39
6	29	9	2	16	6925	7.8	163		4101	2824	59.22	40.78
9	11	9	6	16	6925	7.8	164		3974	2951	57.39	42.61
10	1	9	5	16	6925	7.8	165		4046	2879	58.43	41.57
12	7	9	2	17	6923	7.8	166		4257	2666	61.49	38.51
4	6	9	2	16	6922	7.8	167		4059	2863	58.64	41.36
2	11	9	4	17	6916	7.79	168		4194	2722	60.64	39.36
7	14	9	3	17	6916	7.79	169		4142	2774	59.89	40.11
7	23	9	5	16	6916	7.79	170		4115	2801	59.5	40.5
1	13	9	3	16	6915	7.79	171		4073	2842	58.9	41.1
6	24	9	4	16	6915	7.79	172		4011	2904	58	42
4	3	9	6	17	6914	7.79	173		4031	2883	58.3	41.7

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
4	29	9	4	16	6914	7.79	174		4070	2844	58.87	41.13
8	5	9	4	17	6914	7.79	175		4180	2734	60.46	39.54
10	22	9	5	16	6914	7.79	176		4051	2863	58.59	41.41
4	22	9	4	18	6913	7.79	177		4231	2682	61.2	38.8
6	8	9	2	17	6913	7.79	178		4188	2725	60.58	39.42
4	2	9	5	17	6911	7.79	179		4177	2734	60.44	39.56
12	9	9	4	16	6910	7.79	180		4084	2826	59.1	40.9
6	5	9	6	15	6909	7.79	181	88733	3802	3107	55.03	44.97
6	12	9	6	15	6906	7.78	182		3707	3199	53.68	46.32
6	1	9	2	17	6905	7.78	183		4224	2681	61.17	38.83
7	1	9	4	17	6905	7.78	184		4094	2811	59.29	40.71
7	23	9	5	17	6905	7.78	185		4154	2751	60.16	39.84
12	1	9	3	17	6905	7.78	186		4136	2769	59.9	40.1
5	1	9	6	17	6904	7.78	187		3944	2960	57.13	42.87
11	13	9	6	17	6904	7.78	188		4109	2795	59.52	40.48
5	21	9	5	16	6903	7.78	189		3918	2985	56.76	43.24
6	18	9	5	16	6902	7.78	190		3948	2954	57.2	42.8
3	13	9	6	15	6900	7.78	191		3721	3179	53.93	46.07
10	28	9	4	16	6900	7.78	192		4008	2892	58.09	41.91

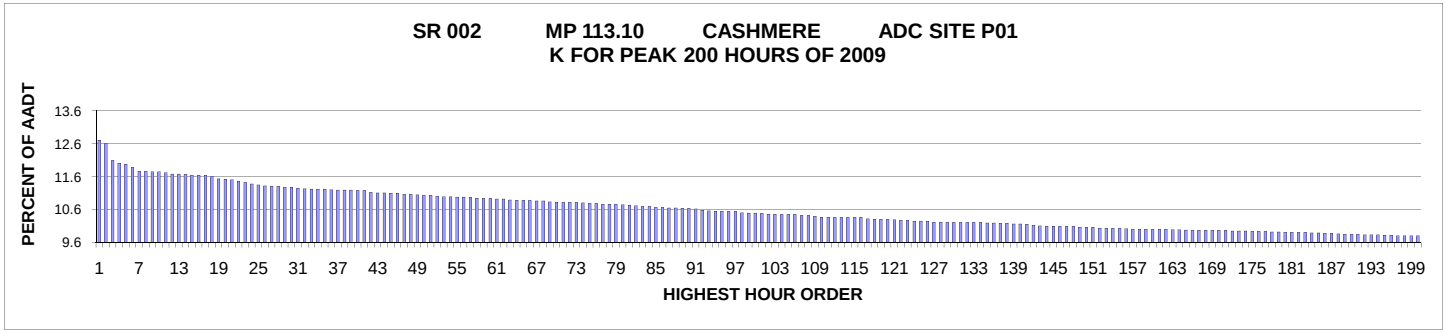

AADT= 20647 **K 30 FACTOR=** 11.28 **K 100 FACTOR=** 10.49 **K 200 FACTOR=** 9.8 **D FACTOR=** 54.89

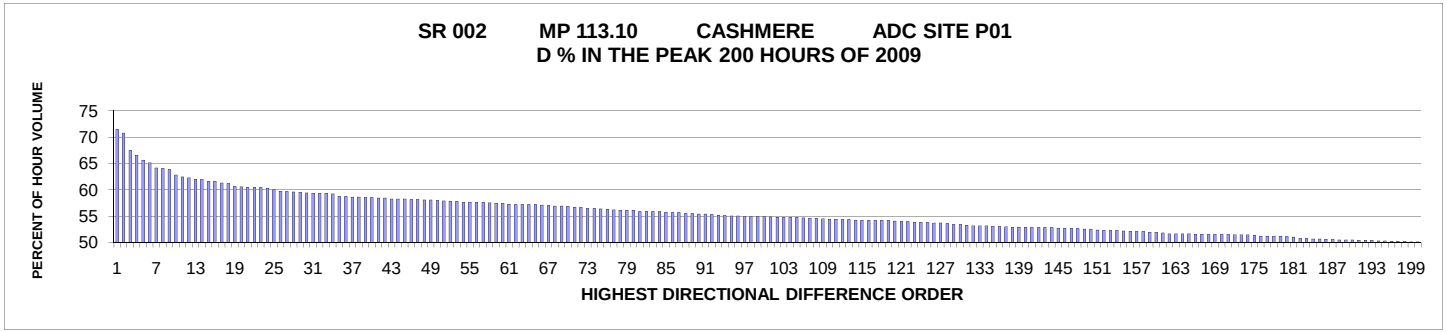

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
5	22	9	6	16	2625	12.71	1	20647	1649	976	62.82	37.18
5	22	9	6	17	2603	12.61	2		1513	1090	58.13	41.87
9	4	9	6	17	2497	12.09	3		1445	1052	57.87	42.13
9	18	9	6	16	2479	12.01	4		1437	1042	57.97	42.03
8	7	9	6	16	2474	11.98	5		1421	1053	57.44	42.56
9	4	9	6	16	2452	11.88	6		1519	933	61.95	38.05
6	21	9	1	13	2431	11.77	7		1043	1388	42.9	57.1
8	14	9	6	16	2428	11.76	8		1280	1148	52.72	47.28
9	11	9	6	18	2426	11.75	9		1173	1253	48.35	51.65
8	21	9	6	16	2425	11.75	10		1369	1056	56.45	43.55
5	25	9	2	13	2420	11.72	11		786	1634	32.48	67.52
8	9	9	1	14	2412	11.68	12		998	1414	41.38	58.62
9	11	9	6	16	2411	11.68	13		1324	1087	54.91	45.09
9	18	9	6	17	2408	11.66	14		1274	1134	52.91	47.09
5	22	9	6	18	2404	11.64	15		1401	1003	58.28	41.72
6	19	9	6	17	2403	11.64	16		1356	1047	56.43	43.57
9	11	9	6	17	2403	11.64	17		1205	1198	50.15	49.85

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	7	9	6	17	2396	11.6	18		1267	1129	52.88	47.12
8	9	9	1	13	2381	11.53	19		983	1398	41.29	58.71
9	4	9	6	18	2378	11.52	20		1311	1067	55.13	44.87
7	10	9	6	17	2375	11.5	21	20647	1197	1178	50.4	49.6
8	28	9	6	16	2368	11.47	22		1376	992	58.11	41.89
7	19	9	1	13	2358	11.42	23		1041	1317	44.15	55.85
5	25	9	2	12	2349	11.38	24		686	1663	29.2	70.8
7	10	9	6	16	2344	11.35	25		1260	1084	53.75	46.25
7	24	9	6	17	2337	11.32	26		1288	1049	55.11	44.89
9	25	9	6	16	2335	11.31	27		1278	1057	54.73	45.27
7	5	9	1	13	2334	11.3	28		844	1490	36.16	63.84
6	19	9	6	16	2329	11.28	29		1287	1042	55.26	44.74
6	19	9	6	18	2329	11.28	30		1192	1137	51.18	48.82
7	2	9	5	17	2320	11.24	31		1295	1025	55.82	44.18
7	2	9	5	16	2319	11.23	32		1384	935	59.68	40.32
7	2	9	5	18	2317	11.22	33		1223	1094	52.78	47.22
7	17	9	6	16	2316	11.22	34		1289	1027	55.66	44.34
10	2	9	6	17	2316	11.22	35		1207	1109	52.12	47.88
10	16	9	6	17	2313	11.2	36		1184	1129	51.19	48.81
7	17	9	6	17	2311	11.19	37		1282	1029	55.47	44.53
5	22	9	6	15	2310	11.19	38		1399	911	60.56	39.44
8	28	9	6	17	2310	11.19	39		1262	1048	54.63	45.37
6	26	9	6	17	2307	11.17	40		1241	1066	53.79	46.21
8	14	9	6	17	2306	11.17	41	20647	1190	1116	51.6	48.4
8	21	9	6	18	2295	11.12	42		1185	1110	51.63	48.37
8	23	9	1	14	2294	11.11	43		927	1367	40.41	59.59
6	26	9	6	16	2293	11.11	44		1291	1002	56.3	43.7
7	31	9	6	16	2292	11.1	45		1248	1044	54.45	45.55
8	7	9	6	18	2292	11.1	46		1216	1076	53.05	46.95
10	2	9	6	16	2286	11.07	47		1233	1053	53.94	46.06
9	25	9	6	17	2283	11.06	48		1131	1152	49.54	50.46
7	12	9	1	13	2282	11.05	49		983	1299	43.08	56.92
7	24	9	6	18	2278	11.03	50		1211	1067	53.16	46.84
8	28	9	6	18	2277	11.03	51		1183	1094	51.95	48.05
7	3	9	6	15	2272	11	52		1348	924	59.33	40.67
7	10	9	6	18	2270	10.99	53		1184	1086	52.16	47.84
7	31	9	6	17	2269	10.99	54		1227	1042	54.08	45.92
10	16	9	6	16	2268	10.98	55		1257	1011	55.42	44.58
7	19	9	1	14	2267	10.98	56		871	1396	38.42	61.58
8	8	9	7	13	2264	10.97	57		1102	1162	48.67	51.33
8	7	9	6	15	2259	10.94	58		1240	1019	54.89	45.11
6	5	9	6	16	2258	10.94	59		1312	946	58.1	41.9
8	2	9	1	13	2257	10.93	60		1021	1236	45.24	54.76
7	3	9	6	17	2255	10.92	61	20647	1379	876	61.15	38.85
8	21	9	6	17	2255	10.92	62		1199	1056	53.17	46.83
10	2	9	6	18	2249	10.89	63		1134	1115	50.42	49.58
7	26	9	1	13	2246	10.88	64		962	1284	42.83	57.17
8	14	9	6	15	2244	10.87	65		1173	1071	52.27	47.73
11	25	9	4	16	2244	10.87	66		1230	1014	54.81	45.19
6	28	9	1	15	2243	10.86	67		936	1307	41.73	58.27
8	23	9	1	13	2242	10.86	68		995	1247	44.38	55.62
6	5	9	6	17	2237	10.83	69		1249	988	55.83	44.17

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
9	25	9	6	18	2233	10.82	70		1152	1081	51.59	48.41
7	3	9	6	16	2232	10.81	71		1375	857	61.6	38.4
8	16	9	1	15	2232	10.81	72		926	1306	41.49	58.51
8	23	9	1	16	2232	10.81	73		947	1285	42.43	57.57
7	19	9	1	15	2230	10.8	74		955	1275	42.83	57.17
8	9	9	1	15	2226	10.78	75		919	1307	41.28	58.72
8	16	9	1	14	2225	10.78	76		960	1265	43.15	56.85
6	28	9	1	14	2222	10.76	77		838	1384	37.71	62.29
7	17	9	6	15	2221	10.76	78		1200	1021	54.03	45.97
7	31	9	6	15	2221	10.76	79		1173	1048	52.81	47.19
6	28	9	1	13	2219	10.75	80		902	1317	40.65	59.35
9	13	9	1	13	2217	10.74	81	20647	937	1280	42.26	57.74
5	15	9	6	18	2214	10.72	82		1166	1048	52.66	47.34
9	18	9	6	18	2207	10.69	83		1183	1024	53.6	46.4
10	16	9	6	18	2207	10.69	84		1114	1093	50.48	49.52
7	26	9	1	14	2201	10.66	85		873	1328	39.66	60.34
10	23	9	6	17	2201	10.66	86		1078	1123	48.98	51.02
8	16	9	1	13	2199	10.65	87		1002	1197	45.57	54.43
9	10	9	5	17	2198	10.65	88		1086	1112	49.41	50.59
8	23	9	1	15	2196	10.64	89		931	1265	42.4	57.6
7	5	9	1	14	2194	10.63	90		787	1407	35.87	64.13
5	25	9	2	14	2193	10.62	91		765	1428	34.88	65.12
9	11	9	6	15	2184	10.58	92		1219	965	55.82	44.18
8	9	9	1	17	2181	10.56	93		903	1278	41.4	58.6
8	14	9	6	18	2178	10.55	94		1146	1032	52.62	47.38
9	7	9	2	13	2177	10.54	95		728	1449	33.44	66.56
7	31	9	6	14	2176	10.54	96		1082	1094	49.72	50.28
8	16	9	1	16	2176	10.54	97		924	1252	42.46	57.54
8	14	9	6	14	2167	10.5	98		1086	1081	50.12	49.88
7	12	9	1	14	2166	10.49	99		838	1328	38.69	61.31
7	17	9	6	14	2165	10.49	100		1191	974	55.01	44.99
7	5	9	1	15	2163	10.48	101	20647	872	1291	40.31	59.69
8	13	9	5	16	2158	10.45	102		1121	1037	51.95	48.05
8	21	9	6	15	2157	10.45	103		1123	1034	52.06	47.94
6	21	9	1	15	2156	10.44	104		875	1281	40.58	59.42
7	17	9	6	18	2155	10.44	105		1132	1023	52.53	47.47
7	24	9	6	16	2155	10.44	106		1210	945	56.15	43.85
6	21	9	1	14	2152	10.42	107		808	1344	37.55	62.45
6	26	9	6	18	2151	10.42	108		1089	1062	50.63	49.37
6	5	9	6	18	2147	10.4	109		1049	1098	48.86	51.14
8	28	9	6	15	2141	10.37	110		1125	1016	52.55	47.45
9	10	9	5	18	2141	10.37	111		921	1220	43.02	56.98
5	22	9	6	14	2140	10.36	112		1327	813	62.01	37.99
6	21	9	1	16	2140	10.36	113		870	1270	40.65	59.35
8	6	9	5	17	2140	10.36	114		1149	991	53.69	46.31
8	6	9	5	18	2140	10.36	115		1026	1114	47.94	52.06
7	10	9	6	15	2139	10.36	116		1132	1007	52.92	47.08
8	21	9	6	14	2131	10.32	117		1116	1015	52.37	47.63
8	9	9	1	16	2129	10.31	118		909	1220	42.7	57.3
7	24	9	6	15	2126	10.3	119		1154	972	54.28	45.72
9	4	9	6	15	2126	10.3	120		1210	916	56.91	43.09
8	2	9	1	14	2125	10.29	121	20647	922	1203	43.39	56.61

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	30	9	1	14	2121	10.27	122		839	1282	39.56	60.44
7	19	9	1	16	2120	10.27	123		879	1241	41.46	58.54
7	3	9	6	12	2117	10.25	124		1230	887	58.1	41.9
9	5	9	7	13	2117	10.25	125		1271	846	60.04	39.96
5	15	9	6	16	2116	10.25	126		1210	906	57.18	42.82
8	9	9	1	12	2108	10.21	127		876	1232	41.56	58.44
9	17	9	5	16	2108	10.21	128		1142	966	54.17	45.83
6	28	9	1	16	2107	10.2	129		829	1278	39.35	60.65
7	31	9	6	18	2107	10.2	130		1092	1015	51.83	48.17
8	14	9	6	13	2106	10.2	131		991	1115	47.06	52.94
9	3	9	5	18	2106	10.2	132		988	1118	46.91	53.09
9	13	9	1	14	2106	10.2	133		892	1214	42.36	57.64
5	25	9	2	11	2105	10.2	134		601	1504	28.55	71.45
8	27	9	5	16	2104	10.19	135		1166	938	55.42	44.58
8	7	9	6	14	2103	10.19	136		1107	996	52.64	47.36
7	31	9	6	13	2102	10.18	137		1020	1082	48.53	51.47
5	29	9	6	16	2101	10.18	138		1139	962	54.21	45.79
8	7	9	6	19	2098	10.16	139		1178	920	56.15	43.85
8	30	9	1	13	2097	10.16	140		849	1248	40.49	59.51
6	26	9	6	15	2095	10.15	141	20647	1187	908	56.66	43.34
4	24	9	6	18	2089	10.12	142		1111	978	53.18	46.82
9	12	9	7	14	2086	10.1	143		1120	966	53.69	46.31
9	9	9	4	16	2084	10.09	144		1051	1033	50.43	49.57
9	7	9	2	12	2083	10.09	145		716	1367	34.37	65.63
7	6	9	2	15	2081	10.08	146		922	1159	44.31	55.69
8	21	9	6	13	2081	10.08	147		1051	1030	50.5	49.5
10	9	9	6	17	2081	10.08	148		1070	1011	51.42	48.58
6	25	9	5	17	2079	10.07	149		1035	1044	49.78	50.22
6	26	9	6	14	2077	10.06	150		1109	968	53.39	46.61
9	10	9	5	16	2077	10.06	151		1129	948	54.36	45.64
11	6	9	6	17	2072	10.04	152		1067	1005	51.5	48.5
9	20	9	1	14	2071	10.03	153		873	1198	42.15	57.85
11	25	9	4	17	2071	10.03	154		1162	909	56.11	43.89
7	3	9	6	14	2070	10.03	155		1210	860	58.45	41.55
5	1	9	6	17	2068	10.02	156		1122	946	54.26	45.74
7	6	9	2	16	2066	10.01	157		954	1112	46.18	53.82
10	9	9	6	16	2066	10.01	158		1046	1020	50.63	49.37
6	26	9	6	13	2065	10	159		1130	935	54.72	45.28
7	12	9	1	15	2065	10	160		884	1181	42.81	57.19
7	26	9	1	16	2065	10	161	20647	875	1190	42.37	57.63
7	26	9	1	17	2064	10	162		932	1132	45.16	54.84
7	10	9	6	14	2062	9.99	163		1028	1034	49.85	50.15
9	25	9	6	15	2062	9.99	164		1099	963	53.3	46.7
7	6	9	2	17	2061	9.98	165		938	1123	45.51	54.49
5	8	9	6	18	2059	9.97	166		1024	1035	49.73	50.27
6	28	9	1	17	2059	9.97	167		840	1219	40.8	59.2
7	26	9	1	15	2059	9.97	168		928	1131	45.07	54.93
5	29	9	6	17	2058	9.97	169		1041	1017	50.58	49.42
9	6	9	1	15	2058	9.97	170		933	1125	45.34	54.66
9	18	9	6	15	2058	9.97	171		1088	970	52.87	47.13
5	1	9	6	16	2055	9.95	172		1131	924	55.04	44.96
6	5	9	6	15	2055	9.95	173		1154	901	56.16	43.84

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
9	17	9	5	17	2054	9.95	174		981	1073	47.76	52.24
6	19	9	6	15	2052	9.94	175		1112	940	54.19	45.81
8	26	9	4	16	2051	9.93	176		1056	995	51.49	48.51
9	20	9	1	13	2050	9.93	177		939	1111	45.8	54.2
7	30	9	5	16	2049	9.92	178		1022	1027	49.88	50.12
8	8	9	7	14	2048	9.92	179		1054	994	51.46	48.54
7	9	9	5	18	2047	9.91	180		930	1117	45.43	54.57
8	6	9	5	16	2047	9.91	181	20647	1046	1001	51.1	48.9
7	19	9	1	17	2044	9.9	182		936	1108	45.79	54.21
8	2	9	1	15	2044	9.9	183		853	1191	41.73	58.27
9	8	9	3	17	2043	9.89	184		869	1174	42.54	57.46
10	8	9	5	17	2043	9.89	185		990	1053	48.46	51.54
5	15	9	6	17	2039	9.88	186		988	1051	48.46	51.54
8	16	9	1	17	2037	9.87	187		907	1130	44.53	55.47
9	8	9	3	16	2036	9.86	188		1034	1002	50.79	49.21
8	13	9	5	18	2033	9.85	189		948	1085	46.63	53.37
5	8	9	6	17	2032	9.84	190		1061	971	52.21	47.79
9	3	9	5	16	2031	9.84	191		1072	959	52.78	47.22
7	6	9	2	18	2030	9.83	192		803	1227	39.56	60.44
6	21	9	1	12	2029	9.83	193		804	1225	39.63	60.37
9	7	9	2	14	2029	9.83	194		730	1299	35.98	64.02
9	12	9	7	13	2028	9.82	195		1038	990	51.18	48.82
4	17	9	6	18	2027	9.82	196		999	1028	49.28	50.72
7	12	9	1	17	2024	9.8	197		912	1112	45.06	54.94
8	31	9	2	16	2024	9.8	198		1045	979	51.63	48.37
8	7	9	6	13	2023	9.8	199		1044	979	51.61	48.39
9	13	9	1	15	2023	9.8	200		882	1141	43.6	56.4

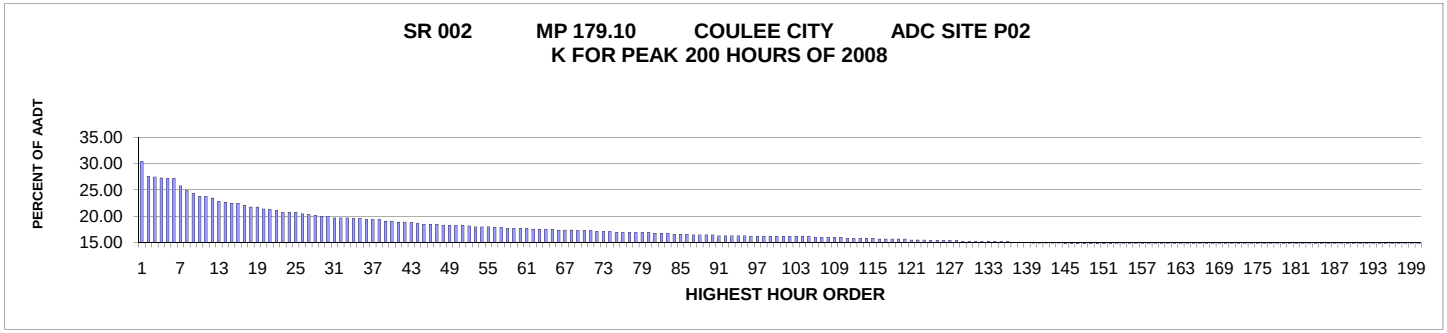

AADT= 645 **K 30 FACTOR=** 20 **K 100 FACTOR=** 16.12 **K 200 FACTOR=** 13.64 **D FACTOR=** 58.7

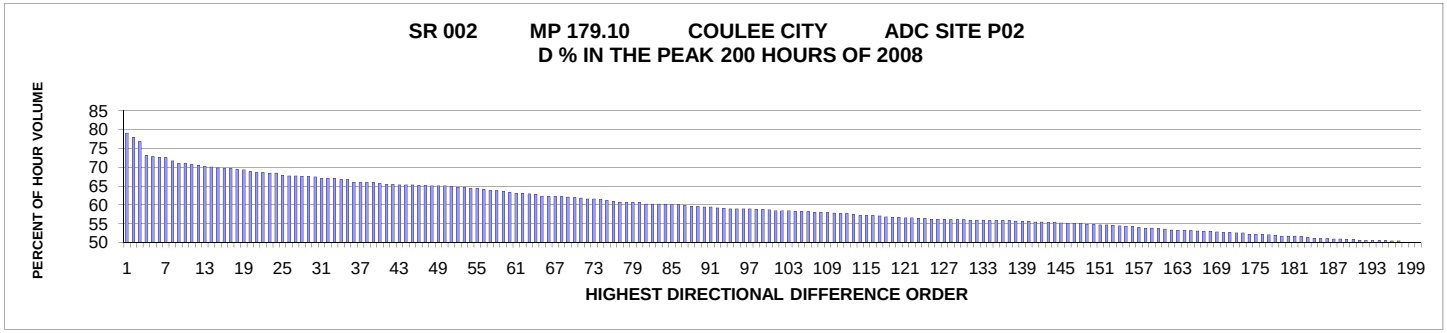

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
10	4	9	1	16	196	30.39	1	645	68	128	34.69	65.31
8	2	9	1	13	178	27.60	2		86	92	48.31	51.69
10	4	9	1	17	177	27.44	3		67	110	37.85	62.15
5	25	9	2	13	176	27.29	4		61	115	34.66	65.34
5	25	9	2	14	175	27.13	5		71	104	40.57	59.43
10	4	9	1	15	175	27.13	6		77	98	44.00	56.00
10	4	9	1	18	166	25.74	7		65	101	39.16	60.84
5	25	9	2	12	160	24.81	8		49	111	30.63	69.38
5	25	9	2	16	157	24.34	9		68	89	43.31	56.69
5	25	9	2	11	153	23.72	10		32	121	20.92	79.08
8	2	9	1	12	153	23.72	11		42	111	27.45	72.55
9	7	9	2	14	151	23.41	12		55	96	36.42	63.58
5	22	9	6	18	147	22.79	13		104	43	70.75	29.25
6	28	9	1	15	146	22.64	14		55	91	37.67	62.33
5	22	9	6	15	145	22.48	15		98	47	67.59	32.41
9	7	9	2	12	145	22.48	16		32	113	22.07	77.93
6	28	9	1	14	142	22.02	17		58	84	40.85	59.15

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
5	25	9	2	15	140	21.71	18		53	87	37.86	62.14
8	2	9	1	14	140	21.71	19		61	79	43.57	56.43
5	22	9	6	17	138	21.40	20		81	57	58.70	41.30
5	22	9	6	19	137	21.24	21	645	89	48	64.96	35.04
10	4	9	1	13	136	21.09	22		56	80	41.18	58.82
6	28	9	1	16	134	20.78	23		59	75	44.03	55.97
8	8	9	7	14	134	20.78	24		63	71	47.01	52.99
8	30	9	1	15	134	20.78	25		51	83	38.06	61.94
8	30	9	1	13	132	20.47	26		50	82	37.88	62.12
5	22	9	6	14	131	20.31	27		93	38	70.99	29.01
8	2	9	1	15	130	20.16	28		64	66	49.23	50.77
6	28	9	1	12	129	20.00	29		44	85	34.11	65.89
8	30	9	1	18	129	20.00	30		74	55	57.36	42.64
5	25	9	2	10	127	19.69	31		36	91	28.35	71.65
8	1	9	7	11	127	19.69	32		59	68	46.46	53.54
10	4	9	1	14	127	19.69	33		41	86	32.28	67.72
8	30	9	1	12	126	19.53	34		45	81	35.71	64.29
8	30	9	1	14	126	19.53	35		44	82	34.92	65.08
5	24	9	1	14	125	19.38	36		63	62	50.40	49.60
9	7	9	2	13	125	19.38	37		38	87	30.40	69.60
10	4	9	1	12	125	19.38	38		48	77	38.40	61.60
6	28	9	1	13	123	19.07	39		43	80	34.96	65.04
9	7	9	2	11	123	19.07	40		40	83	32.52	67.48
5	25	9	2	17	122	18.91	41	645	36	86	29.51	70.49
8	8	9	7	15	122	18.91	42		53	69	43.44	56.56
8	1	9	7	13	121	18.76	43		58	63	47.93	52.07
8	7	9	6	16	120	18.60	44		64	56	53.33	46.67
8	2	9	1	17	119	18.45	45		51	68	42.86	57.14
8	8	9	7	13	119	18.45	46		57	62	47.90	52.10
8	30	9	1	17	119	18.45	47		55	64	46.22	53.78
5	17	9	1	13	118	18.29	48		60	58	50.85	49.15
8	2	9	1	16	118	18.29	49		50	68	42.37	57.63
8	28	9	6	14	118	18.29	50		57	61	48.31	51.69
9	6	9	1	14	118	18.29	51		51	67	43.22	56.78
8	7	9	6	15	117	18.14	52		59	58	50.43	49.57
5	24	9	1	13	116	17.98	53		47	69	40.52	59.48
9	7	9	2	15	116	17.98	54		44	72	37.93	62.07
9	13	9	1	14	116	17.98	55		52	64	44.83	55.17
8	1	9	7	15	115	17.83	56		63	52	54.78	45.22
8	29	9	7	15	115	17.83	57		59	56	51.30	48.70
5	22	9	6	16	114	17.67	58		79	35	69.30	30.70
8	6	9	5	13	114	17.67	59		48	66	42.11	57.89
9	20	9	1	13	114	17.67	60		38	76	33.33	66.67
9	20	9	1	14	114	17.67	61	645	41	73	35.96	64.04
5	23	9	7	11	113	17.52	62		68	45	60.18	39.82
5	25	9	2	18	113	17.52	63		45	68	39.82	60.18
6	28	9	1	18	113	17.52	64		47	66	41.59	58.41
9	18	9	6	15	113	17.52	65		50	63	44.25	55.75
6	7	9	1	15	112	17.36	66		46	66	41.07	58.93
8	7	9	6	14	112	17.36	67		56	56	50.00	50.00
10	4	9	1	19	112	17.36	68		55	57	49.11	50.89
6	7	9	1	14	111	17.21	69		35	76	31.53	68.47

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	29	9	7	13	111	17.21	70		41	70	36.94	63.06
9	4	9	6	16	111	17.21	71		70	41	63.06	36.94
8	28	9	6	15	110	17.05	72		62	48	56.36	43.64
9	7	9	2	16	110	17.05	73		42	68	38.18	61.82
9	20	9	1	17	110	17.05	74		45	65	40.91	59.09
5	23	9	7	13	109	16.90	75		61	48	55.96	44.04
8	8	9	7	12	109	16.90	76		36	73	33.03	66.97
8	28	9	6	16	109	16.90	77		67	42	61.47	38.53
9	20	9	1	16	109	16.90	78		36	73	33.03	66.97
9	25	9	6	15	109	16.90	79		45	64	41.28	58.72
9	27	9	1	13	109	16.90	80		35	74	32.11	67.89
5	24	9	1	15	108	16.74	81	645	49	59	45.37	54.63
8	1	9	7	12	108	16.74	82		48	60	44.44	55.56
9	18	9	6	13	108	16.74	83		42	66	38.89	61.11
4	26	9	1	13	107	16.59	84		37	70	34.58	65.42
8	27	9	5	14	107	16.59	85		61	46	57.01	42.99
9	11	9	6	17	107	16.59	86		60	47	56.07	43.93
8	29	9	7	12	106	16.43	87		54	52	50.94	49.06
8	30	9	1	11	106	16.43	88		32	74	30.19	69.81
9	6	9	1	12	106	16.43	89		37	69	34.91	65.09
9	18	9	6	18	106	16.43	90		77	29	72.64	27.36
6	7	9	1	13	105	16.28	91		46	59	43.81	56.19
8	7	9	6	12	105	16.28	92		35	70	33.33	66.67
8	7	9	6	17	105	16.28	93		66	39	62.86	37.14
8	27	9	5	17	105	16.28	94		63	42	60.00	40.00
9	5	9	7	12	105	16.28	95		59	46	56.19	43.81
5	23	9	7	14	104	16.12	96		57	47	54.81	45.19
5	24	9	1	17	104	16.12	97		36	68	34.62	65.38
5	24	9	1	18	104	16.12	98		28	76	26.92	73.08
8	2	9	1	11	104	16.12	99		31	73	29.81	70.19
8	3	9	2	14	104	16.12	100		46	58	44.23	55.77
8	5	9	4	14	104	16.12	101	645	58	46	55.77	44.23
8	28	9	6	18	104	16.12	102		44	60	42.31	57.69
9	13	9	1	15	104	16.12	103		50	54	48.08	51.92
9	18	9	6	16	104	16.12	104		64	40	61.54	38.46
9	27	9	1	14	104	16.12	105		41	63	39.42	60.58
5	17	9	1	15	103	15.97	106		46	57	44.66	55.34
5	24	9	1	16	103	15.97	107		36	67	34.95	65.05
6	12	9	6	17	103	15.97	108		62	41	60.19	39.81
8	7	9	6	18	103	15.97	109		60	43	58.25	41.75
9	27	9	1	12	103	15.97	110		34	69	33.01	66.99
4	26	9	1	15	102	15.81	111		36	66	35.29	64.71
5	23	9	7	15	102	15.81	112		54	48	52.94	47.06
8	28	9	6	13	102	15.81	113		37	65	36.27	63.73
8	28	9	6	17	102	15.81	114		50	52	49.02	50.98
8	29	9	7	14	102	15.81	115		37	65	36.27	63.73
8	7	9	6	11	101	15.66	116		42	59	41.58	58.42
8	7	9	6	13	101	15.66	117		51	50	50.50	49.50
8	28	9	6	19	101	15.66	118		60	41	59.41	40.59
9	4	9	6	18	101	15.66	119		65	36	64.36	35.64
9	13	9	1	13	101	15.66	120		45	56	44.55	55.45
5	15	9	6	17	100	15.50	121	645	58	42	58.00	42.00

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	8	9	7	11	100	15.50	122		42	58	42.00	58.00
9	4	9	6	17	100	15.50	123		71	29	71.00	29.00
5	17	9	1	17	99	15.35	124		43	56	43.43	56.57
8	3	9	2	15	99	15.35	125		39	60	39.39	60.61
8	29	9	7	16	99	15.35	126		45	54	45.45	54.55
9	5	9	7	17	99	15.35	127		47	52	47.47	52.53
9	20	9	1	11	99	15.35	128		23	76	23.23	76.77
5	15	9	6	15	98	15.19	129		59	39	60.20	39.80
5	17	9	1	16	98	15.19	130		36	62	36.73	63.27
5	22	9	6	13	98	15.19	131		57	41	58.16	41.84
6	7	9	1	16	98	15.19	132		42	56	42.86	57.14
8	2	9	1	18	98	15.19	133		48	50	48.98	51.02
8	30	9	1	16	98	15.19	134		44	54	44.90	55.10
9	20	9	1	12	98	15.19	135		34	64	34.69	65.31
9	25	9	6	13	98	15.19	136		46	52	46.94	53.06
8	5	9	4	12	97	15.04	137		44	53	45.36	54.64
9	8	9	3	13	97	15.04	138		29	68	29.90	70.10
10	2	9	6	16	97	15.04	139		46	51	47.42	52.58
5	22	9	6	20	96	14.88	140		65	31	67.71	32.29
5	23	9	7	16	96	14.88	141	645	45	51	46.88	53.13
5	24	9	1	11	96	14.88	142		33	63	34.38	65.63
8	1	9	7	14	96	14.88	143		50	46	52.08	47.92
8	4	9	3	12	96	14.88	144		34	62	35.42	64.58
4	26	9	1	12	95	14.73	145		42	53	44.21	55.79
5	25	9	2	19	95	14.73	146		47	48	49.47	50.53
6	7	9	1	12	95	14.73	147		45	50	47.37	52.63
6	12	9	6	12	95	14.73	148		47	48	49.47	50.53
6	12	9	6	14	95	14.73	149		50	45	52.63	47.37
8	6	9	5	14	95	14.73	150		56	39	58.95	41.05
8	27	9	5	12	95	14.73	151		51	44	53.68	46.32
9	11	9	6	16	95	14.73	152		46	49	48.42	51.58
5	1	9	6	15	94	14.57	153		62	32	65.96	34.04
5	18	9	2	13	94	14.57	154		37	57	39.36	60.64
8	6	9	5	16	94	14.57	155		51	43	54.26	45.74
8	28	9	6	12	94	14.57	156		42	52	44.68	55.32
9	18	9	6	17	94	14.57	157		56	38	59.57	40.43
9	20	9	1	15	94	14.57	158		47	47	50.00	50.00
5	17	9	1	14	93	14.42	159		29	64	31.18	68.82
5	31	9	1	13	93	14.42	160		41	52	44.09	55.91
8	27	9	5	15	93	14.42	161	645	46	47	49.46	50.54
4	19	9	1	14	92	14.26	162		42	50	45.65	54.35
5	17	9	1	12	92	14.26	163		49	43	53.26	46.74
5	22	9	6	12	92	14.26	164		63	29	68.48	31.52
6	5	9	6	18	92	14.26	165		51	41	55.43	44.57
8	8	9	7	16	92	14.26	166		47	45	51.09	48.91
9	4	9	6	15	92	14.26	167		55	37	59.78	40.22
9	6	9	1	15	92	14.26	168		25	67	27.17	72.83
9	11	9	6	13	92	14.26	169		43	49	46.74	53.26
10	25	9	1	15	92	14.26	170		44	48	47.83	52.17
4	26	9	1	16	91	14.11	171		31	60	34.07	65.93
5	1	9	6	13	91	14.11	172		53	38	58.24	41.76
8	6	9	5	11	91	14.11	173		42	49	46.15	53.85

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	8	9	7	17	91	14.11	174		51	40	56.04	43.96
9	25	9	6	17	91	14.11	175		45	46	49.45	50.55
9	27	9	1	15	91	14.11	176		31	60	34.07	65.93
10	2	9	6	13	91	14.11	177		39	52	42.86	57.14
4	24	9	6	16	90	13.95	178		49	41	54.44	45.56
5	3	9	1	15	90	13.95	179		40	50	44.44	55.56
5	23	9	7	18	90	13.95	180		39	51	43.33	56.67
6	28	9	1	11	90	13.95	181	645	38	52	42.22	57.78
8	3	9	2	13	90	13.95	182		37	53	41.11	58.89
8	3	9	2	17	90	13.95	183		53	37	58.89	41.11
9	18	9	6	19	90	13.95	184		54	36	60.00	40.00
9	27	9	1	16	90	13.95	185		45	45	50.00	50.00
4	26	9	1	17	89	13.80	186		31	58	34.83	65.17
6	5	9	6	16	89	13.80	187		41	48	46.07	53.93
6	7	9	1	11	89	13.80	188		28	61	31.46	68.54
6	7	9	1	17	89	13.80	189		43	46	48.31	51.69
6	28	9	1	17	89	13.80	190		27	62	30.34	69.66
8	5	9	4	11	89	13.80	191		56	33	62.92	37.08
8	31	9	2	12	89	13.80	192		28	61	31.46	68.54
8	31	9	2	14	89	13.80	193		39	50	43.82	56.18
9	4	9	6	14	89	13.80	194		47	42	52.81	47.19
9	6	9	1	13	89	13.80	195		29	60	32.58	67.42
9	6	9	1	16	89	13.80	196		37	52	41.57	58.43
9	7	9	2	17	89	13.80	197		35	54	39.33	60.67
9	13	9	1	12	89	13.80	198		40	49	44.94	55.06
9	26	9	7	12	89	13.80	199		40	49	44.94	55.06
4	26	9	1	14	88	13.64	200		39	49	44.32	55.68

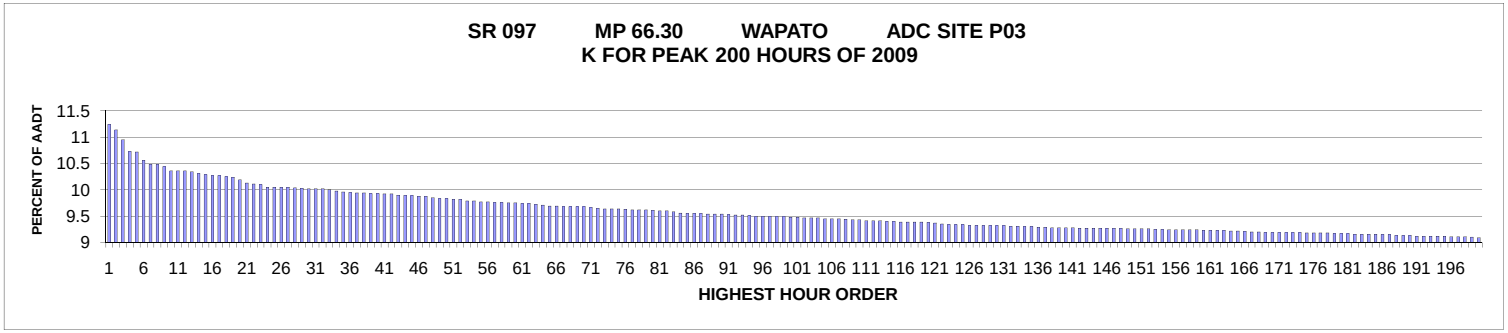

AADT= 12195 **K 30 FACTOR=** 10.02 **K 100 FACTOR=** 9.48 **K 200 FACTOR=** 9.09 **D FACTOR=** 52.98

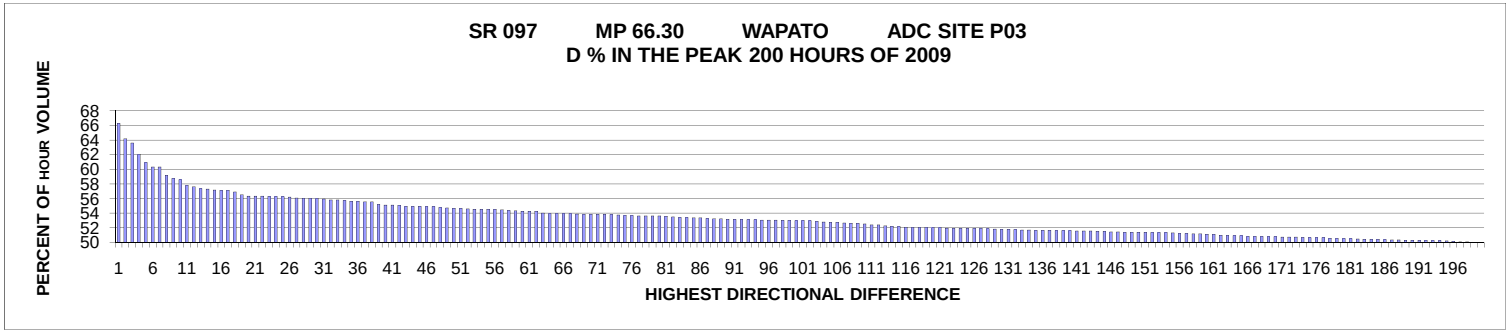

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
9	4	9	6	16	1371	11.24	1	12195	764	607	55.73	44.27
8	7	9	6	18	1359	11.14	2		843	516	62.03	37.97
10	30	9	6	17	1335	10.95	3		720	615	53.93	46.07
8	7	9	6	16	1309	10.73	4		695	614	53.09	46.91
11	25	9	4	16	1307	10.72	5		720	587	55.09	44.91
8	7	9	6	17	1288	10.56	6		710	578	55.12	44.88
1	9	9	6	16	1278	10.48	7		681	597	53.29	46.71
9	4	9	6	17	1278	10.48	8		682	596	53.36	46.64
10	2	9	6	16	1273	10.44	9		655	618	51.45	48.55
5	15	9	6	17	1263	10.36	10		711	552	56.29	43.71
9	18	9	6	16	1263	10.36	11		622	641	49.25	50.75
10	26	9	2	16	1263	10.36	12		628	635	49.72	50.28
5	15	9	6	16	1261	10.34	13		680	581	53.93	46.07
1	9	9	6	17	1257	10.31	14		668	589	53.14	46.86
12	4	9	6	16	1255	10.29	15		689	566	54.9	45.1
5	22	9	6	16	1252	10.27	16		674	578	53.83	46.17
11	13	9	6	16	1252	10.27	17		661	591	52.8	47.2

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
2	6	9	6	16	1250	10.25	18		686	564	54.88	45.12
10	16	9	6	18	1249	10.24	19		665	584	53.24	46.76
8	21	9	6	16	1243	10.19	20		657	586	52.86	47.14
8	21	9	6	18	1235	10.13	21	12195	608	627	49.23	50.77
5	1	9	6	16	1233	10.11	22		617	616	50.04	49.96
10	16	9	6	16	1232	10.1	23		624	608	50.65	49.35
5	8	9	6	17	1226	10.05	24		627	599	51.14	48.86
10	23	9	6	16	1226	10.05	25		637	589	51.96	48.04
6	5	9	6	16	1225	10.05	26		667	558	54.45	45.55
8	7	9	6	15	1225	10.05	27		649	576	52.98	47.02
3	27	9	6	16	1224	10.04	28		621	603	50.74	49.26
9	21	9	2	16	1223	10.03	29		630	593	51.51	48.49
5	15	9	6	18	1222	10.02	30		698	524	57.12	42.88
10	30	9	6	16	1222	10.02	31		623	599	50.98	49.02
11	25	9	4	15	1222	10.02	32		632	590	51.72	48.28
10	9	9	6	16	1219	10	33		613	606	50.29	49.71
8	21	9	6	17	1217	9.98	34		603	614	49.55	50.45
6	22	9	2	16	1215	9.96	35		654	561	53.83	46.17
10	2	9	6	17	1214	9.95	36		602	612	49.59	50.41
5	8	9	6	16	1212	9.94	37		600	612	49.5	50.5
8	21	9	6	15	1212	9.94	38		587	625	48.43	51.57
7	31	9	6	16	1211	9.93	39		597	614	49.3	50.7
10	9	9	6	17	1211	9.93	40		600	611	49.55	50.45
1	9	9	6	18	1210	9.92	41	12195	641	569	52.98	47.02
7	10	9	6	18	1210	9.92	42		660	550	54.55	45.45
8	9	9	1	14	1207	9.9	43		479	728	39.69	60.31
8	14	9	6	17	1206	9.89	44		588	618	48.76	51.24
9	4	9	6	15	1206	9.89	45		671	535	55.64	44.36
8	24	9	2	17	1205	9.88	46		664	541	55.1	44.9
10	12	9	2	17	1205	9.88	47		691	514	57.34	42.66
8	14	9	6	16	1201	9.85	48		641	560	53.37	46.63
8	10	9	2	16	1199	9.83	49		588	611	49.04	50.96
10	2	9	6	18	1199	9.83	50		667	532	55.63	44.37
5	22	9	6	17	1198	9.82	51		619	579	51.67	48.33
4	3	9	6	16	1197	9.82	52		604	593	50.46	49.54
5	4	9	2	16	1194	9.79	53		620	574	51.93	48.07
6	19	9	6	16	1194	9.79	54		599	595	50.17	49.83
6	19	9	6	17	1192	9.77	55		572	620	47.99	52.01
9	4	9	6	18	1191	9.77	56		639	552	53.65	46.35
9	7	9	2	15	1190	9.76	57		598	592	50.25	49.75
10	13	9	3	16	1190	9.76	58		699	491	58.74	41.26
7	13	9	2	17	1189	9.75	59		687	502	57.78	42.22
9	8	9	3	17	1189	9.75	60		650	539	54.67	45.33
5	4	9	2	17	1188	9.74	61	12195	660	528	55.56	44.44
6	19	9	6	15	1188	9.74	62		558	630	46.97	53.03
7	10	9	6	15	1187	9.73	63		616	571	51.9	48.1
10	26	9	2	17	1184	9.71	64		669	515	56.5	43.5
6	5	9	6	15	1182	9.69	65		662	520	56.01	43.99
10	23	9	6	17	1182	9.69	66		594	588	50.25	49.75
6	22	9	2	15	1181	9.68	67		615	566	52.07	47.93
7	31	9	6	17	1181	9.68	68		635	546	53.77	46.23
2	20	9	6	17	1180	9.68	69		641	539	54.32	45.68

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	2	9	5	16	1180	9.68	70		646	534	54.75	45.25
5	17	9	1	15	1179	9.67	71		515	664	43.68	56.32
8	7	9	6	14	1177	9.65	72		626	551	53.19	46.81
6	26	9	6	17	1176	9.64	73		614	562	52.21	47.79
7	17	9	6	16	1175	9.64	74		602	573	51.23	48.77
11	2	9	2	17	1175	9.64	75		662	513	56.34	43.66
8	9	9	1	15	1174	9.63	76		517	657	44.04	55.96
10	2	9	6	15	1173	9.62	77		589	584	50.21	49.79
10	26	9	2	18	1173	9.62	78		687	486	58.57	41.43
11	5	9	5	16	1173	9.62	79		609	564	51.92	48.08
7	10	9	6	16	1172	9.61	80		610	562	52.05	47.95
4	10	9	6	16	1171	9.6	81	12195	582	589	49.7	50.3
9	11	9	6	17	1171	9.6	82		575	596	49.1	50.9
4	20	9	2	16	1168	9.58	83		639	529	54.71	45.29
11	6	9	6	16	1166	9.56	84		614	552	52.66	47.34
9	11	9	6	18	1165	9.55	85		589	576	50.56	49.44
10	13	9	3	17	1165	9.55	86		625	540	53.65	46.35
10	16	9	6	17	1165	9.55	87		574	591	49.27	50.73
3	6	9	6	16	1164	9.54	88		610	554	52.41	47.59
6	5	9	6	17	1164	9.54	89		617	547	53.01	46.99
5	8	9	6	18	1163	9.54	90		628	535	54	46
5	17	9	1	14	1162	9.53	91		454	708	39.07	60.93
8	10	9	2	17	1161	9.52	92		648	513	55.81	44.19
8	10	9	2	18	1161	9.52	93		645	516	55.56	44.44
6	12	9	6	18	1160	9.51	94		584	576	50.34	49.66
6	12	9	6	16	1158	9.5	95		570	588	49.22	50.78
6	22	9	2	17	1158	9.5	96		597	561	51.55	48.45
9	21	9	2	17	1158	9.5	97		636	522	54.92	45.08
6	30	9	3	17	1157	9.49	98		597	560	51.6	48.4
11	3	9	3	17	1157	9.49	99		628	529	54.28	45.72
2	3	9	3	17	1156	9.48	100		594	562	51.38	48.62
5	18	9	2	16	1156	9.48	101	12195	606	550	52.42	47.58
5	1	9	6	18	1155	9.47	102		627	528	54.29	45.71
6	26	9	6	16	1155	9.47	103		604	551	52.29	47.71
8	10	9	2	14	1155	9.47	104		561	594	48.57	51.43
6	8	9	2	16	1153	9.45	105		608	545	52.73	47.27
7	10	9	6	17	1153	9.45	106		584	569	50.65	49.35
3	20	9	6	16	1152	9.45	107		582	570	50.52	49.48
8	9	9	1	13	1151	9.44	108		388	763	33.71	66.29
10	30	9	6	18	1150	9.43	109		619	531	53.83	46.17
11	23	9	2	17	1150	9.43	110		659	491	57.3	42.7
9	3	9	5	16	1147	9.41	111		587	560	51.18	48.82
11	3	9	3	16	1147	9.41	112		609	538	53.1	46.9
11	9	9	2	16	1147	9.41	113		630	517	54.93	45.07
8	28	9	6	17	1146	9.4	114		609	537	53.14	46.86
10	5	9	2	16	1146	9.4	115		554	592	48.34	51.66
5	1	9	6	17	1145	9.39	116		557	588	48.65	51.35
7	24	9	6	16	1145	9.39	117		592	553	51.7	48.3
8	6	9	5	17	1145	9.39	118		617	528	53.89	46.11
9	4	9	6	14	1145	9.39	119		614	531	53.62	46.38
7	27	9	2	15	1144	9.38	120		568	576	49.65	50.35
9	8	9	3	16	1143	9.37	121	12195	640	503	55.99	44.01

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
9	22	9	3	16	1140	9.35	122		605	535	53.07	46.93
4	24	9	6	17	1139	9.34	123		619	520	54.35	45.65
6	26	9	6	15	1139	9.34	124		563	576	49.43	50.57
10	8	9	5	16	1139	9.34	125		560	579	49.17	50.83
3	27	9	6	17	1137	9.32	126		568	569	49.96	50.04
8	6	9	5	16	1137	9.32	127		587	550	51.63	48.37
8	21	9	6	14	1137	9.32	128		559	578	49.16	50.84
10	1	9	5	16	1137	9.32	129		553	584	48.64	51.36
2	13	9	6	17	1136	9.32	130		553	583	48.68	51.32
6	25	9	5	17	1136	9.32	131		567	569	49.91	50.09
2	3	9	3	18	1135	9.31	132		606	529	53.39	46.61
10	13	9	3	18	1135	9.31	133		619	516	54.54	45.46
3	26	9	5	16	1134	9.3	134		592	542	52.2	47.8
9	25	9	6	16	1134	9.3	135		585	549	51.59	48.41
10	15	9	5	18	1133	9.29	136		585	548	51.63	48.37
10	22	9	5	17	1133	9.29	137		618	515	54.55	45.45
2	20	9	6	16	1132	9.28	138		565	567	49.91	50.09
5	1	9	6	15	1132	9.28	139		625	507	55.21	44.79
5	22	9	6	15	1132	9.28	140		551	581	48.67	51.33
9	3	9	5	18	1132	9.28	141	12195	632	500	55.83	44.17
5	22	9	6	18	1131	9.27	142		636	495	56.23	43.77
9	1	9	3	16	1131	9.27	143		600	531	53.05	46.95
9	17	9	5	16	1131	9.27	144		599	532	52.96	47.04
9	25	9	6	18	1131	9.27	145		595	536	52.61	47.39
2	17	9	3	16	1130	9.27	146		617	513	54.6	45.4
3	26	9	5	18	1130	9.27	147		635	495	56.19	43.81
6	4	9	5	16	1130	9.27	148		585	545	51.77	48.23
2	6	9	6	17	1129	9.26	149		609	520	53.94	46.06
6	26	9	6	18	1129	9.26	150		633	496	56.07	43.93
9	10	9	5	17	1129	9.26	151		616	513	54.56	45.44
10	1	9	5	18	1129	9.26	152		636	493	56.33	43.67
6	22	9	2	18	1128	9.25	153		650	478	57.62	42.38
7	24	9	6	18	1128	9.25	154		605	523	53.63	46.37
2	20	9	6	18	1127	9.24	155		600	527	53.24	46.76
4	17	9	6	17	1127	9.24	156		560	567	49.69	50.31
9	3	9	5	17	1127	9.24	157		603	524	53.5	46.5
10	8	9	5	17	1127	9.24	158		616	511	54.66	45.34
11	24	9	3	16	1127	9.24	159		604	523	53.59	46.41
8	28	9	6	16	1125	9.23	160		567	558	50.4	49.6
10	9	9	6	15	1125	9.23	161	12195	578	547	51.38	48.62
11	13	9	6	15	1125	9.23	162		578	547	51.38	48.62
11	20	9	6	16	1125	9.23	163		605	520	53.78	46.22
2	9	9	2	17	1124	9.22	164		632	492	56.23	43.77
7	31	9	6	18	1124	9.22	165		593	531	52.76	47.24
8	10	9	2	15	1123	9.21	166		551	572	49.07	50.93
7	24	9	6	17	1122	9.2	167		581	541	51.78	48.22
8	24	9	2	16	1122	9.2	168		584	538	52.05	47.95
1	16	9	6	16	1121	9.19	169		583	538	52.01	47.99
9	11	9	6	16	1121	9.19	170		579	542	51.65	48.35
9	25	9	6	15	1121	9.19	171		601	520	53.61	46.39
10	9	9	6	18	1121	9.19	172		576	545	51.38	48.62
10	29	9	5	16	1121	9.19	173		582	539	51.92	48.08

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
12	7	9	2	16	1121	9.19	174		590	531	52.63	47.37
12	4	9	6	18	1120	9.18	175		640	480	57.14	42.86
2	5	9	5	16	1119	9.18	176		581	538	51.92	48.08
4	21	9	3	16	1119	9.18	177		600	519	53.62	46.38
4	24	9	6	16	1119	9.18	178		552	567	49.33	50.67
1	23	9	6	17	1118	9.17	179		572	546	51.16	48.84
4	14	9	3	16	1118	9.17	180		597	521	53.4	46.6
11	6	9	6	18	1118	9.17	181	12195	607	511	54.29	45.71
3	20	9	6	17	1117	9.16	182		587	530	52.55	47.45
8	9	9	1	12	1117	9.16	183		400	717	35.81	64.19
9	7	9	2	14	1117	9.16	184		443	674	39.66	60.34
10	20	9	3	16	1117	9.16	185		582	535	52.1	47.9
7	6	9	2	17	1116	9.15	186		567	549	50.81	49.19
10	5	9	2	17	1116	9.15	187		638	478	57.17	42.83
10	12	9	2	16	1114	9.13	188		591	523	53.05	46.95
3	13	9	6	16	1113	9.13	189		569	544	51.12	48.88
5	17	9	1	13	1113	9.13	190		405	708	36.39	63.61
7	7	9	3	16	1112	9.12	191		577	535	51.89	48.11
9	17	9	5	17	1112	9.12	192		611	501	54.95	45.05
9	21	9	2	18	1112	9.12	193		633	479	56.92	43.08
11	13	9	6	17	1112	9.12	194		623	489	56.03	43.97
12	3	9	5	16	1112	9.12	195		573	539	51.53	48.47
3	20	9	6	18	1111	9.11	196		575	536	51.76	48.24
9	29	9	3	16	1111	9.11	197		599	512	53.92	46.08
10	1	9	5	17	1111	9.11	198		576	535	51.85	48.15
5	18	9	2	18	1110	9.1	199		657	453	59.19	40.81
1	16	9	6	17	1109	9.09	200		597	512	53.83	46.17

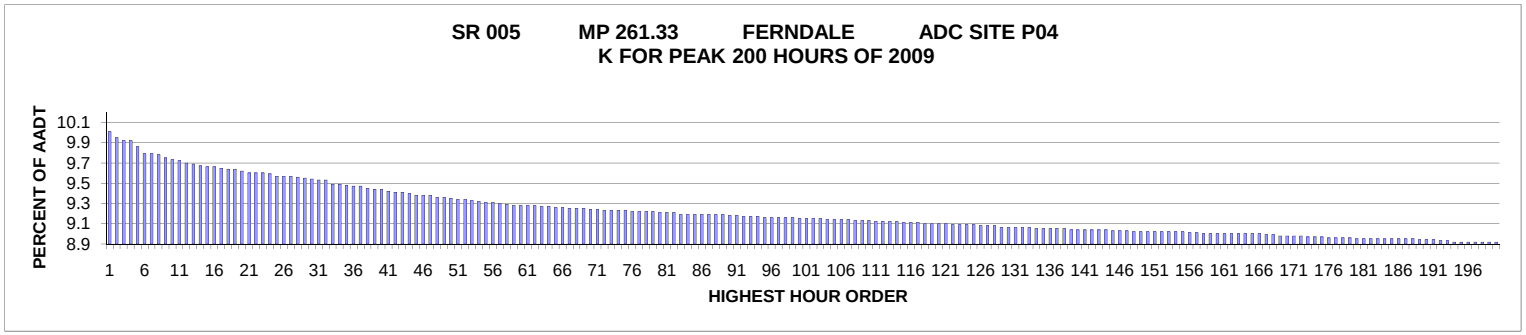

AADT= 45544 **K 30 FACTOR=** 9.54 **K 100 FACTOR=** 9.15 **K 200 FACTOR=** 8.92 **D FACTOR=** 56.1

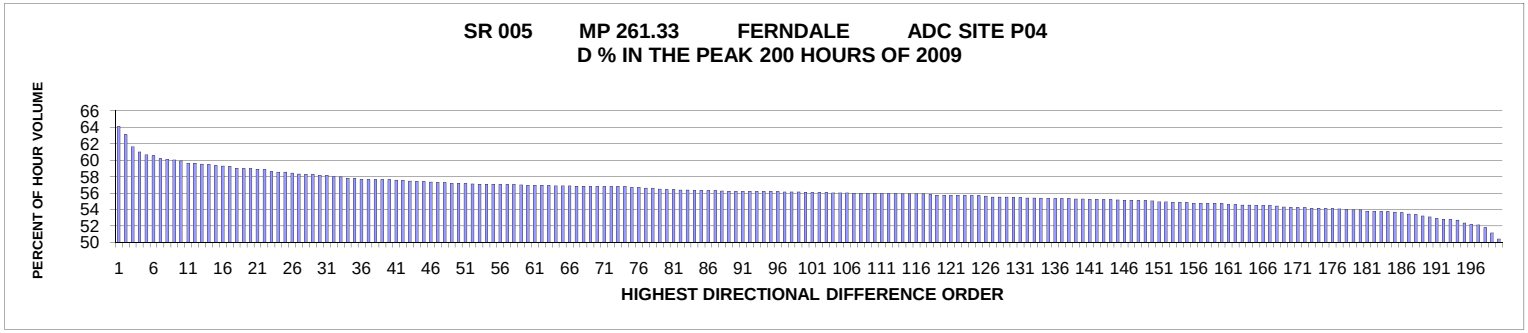

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	31	9	2	18	4557	10.01	1	45544	2561	1996	56.2	43.8
5	15	9	6	17	4530	9.95	2		2284	2246	50.42	49.58
5	1	9	6	18	4519	9.92	3		2478	2041	54.84	45.16
5	18	9	2	18	4516	9.92	4		2850	1666	63.11	36.89
5	1	9	6	17	4492	9.86	5		2416	2076	53.78	46.22
10	12	9	2	17	4459	9.79	6		2720	1739	61	39
7	24	9	6	17	4458	9.79	7		2394	2064	53.7	46.3
8	3	9	2	17	4452	9.78	8		2700	1752	60.65	39.35
5	18	9	2	17	4439	9.75	9		2665	1774	60.04	39.96
4	24	9	6	18	4430	9.73	10		2480	1950	55.98	44.02
9	4	9	6	17	4425	9.72	11		2440	1985	55.14	44.86
9	3	9	5	17	4420	9.7	12		2335	2085	52.83	47.17
8	6	9	5	18	4413	9.69	13		2450	1963	55.52	44.48
11	12	9	5	17	4404	9.67	14		2513	1891	57.06	42.94
5	8	9	6	17	4399	9.66	15		2295	2104	52.17	47.83
8	14	9	6	17	4398	9.66	16		2489	1909	56.59	43.41
8	13	9	5	18	4395	9.65	17		2471	1924	56.22	43.78

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
4	30	9	5	18	4392	9.64	18		2548	1844	58.01	41.99
5	15	9	6	18	4389	9.64	19		2318	2071	52.81	47.19
4	24	9	6	17	4382	9.62	20		2428	1954	55.41	44.59
8	26	9	4	18	4374	9.6	21	45544	2452	1922	56.06	43.94
9	1	9	3	18	4372	9.6	22		2464	1908	56.36	43.64
1	9	9	6	17	4371	9.6	23		2459	1912	56.26	43.74
5	8	9	6	18	4366	9.59	24		2418	1948	55.38	44.62
4	13	9	2	18	4360	9.57	25		2600	1760	59.63	40.37
4	27	9	2	18	4358	9.57	26		2620	1738	60.12	39.88
4	29	9	4	18	4357	9.57	27		2584	1773	59.31	40.69
5	22	9	6	17	4356	9.56	28		2281	2075	52.36	47.64
8	3	9	2	18	4349	9.55	29		2680	1669	61.62	38.38
5	7	9	5	18	4345	9.54	30		2479	1866	57.05	42.95
4	22	9	4	18	4342	9.53	31		2537	1805	58.43	41.57
8	12	9	4	18	4340	9.53	32		2440	1900	56.22	43.78
12	29	9	3	17	4322	9.49	33		2418	1904	55.95	44.05
11	20	9	6	17	4321	9.49	34		2429	1892	56.21	43.79
8	5	9	4	17	4316	9.48	35		2388	1928	55.33	44.67
4	23	9	5	18	4314	9.47	36		2467	1847	57.19	42.81
10	9	9	6	17	4313	9.47	37		2369	1944	54.93	45.07
9	25	9	6	17	4302	9.45	38		2399	1903	55.76	44.24
3	13	9	6	18	4301	9.44	39		2398	1903	55.75	44.25
4	28	9	3	18	4299	9.44	40		2587	1712	60.18	39.82
7	27	9	2	17	4289	9.42	41	45544	2339	1950	54.53	45.47
5	19	9	3	18	4287	9.41	42		2552	1735	59.53	40.47
5	22	9	6	18	4284	9.41	43		2303	1981	53.76	46.24
8	28	9	6	17	4282	9.4	44		2377	1905	55.51	44.49
7	24	9	6	18	4273	9.38	45		2311	1962	54.08	45.92
8	27	9	5	18	4273	9.38	46		2392	1881	55.98	44.02
8	25	9	3	18	4271	9.38	47		2396	1875	56.1	43.9
9	1	9	3	17	4264	9.36	48		2313	1951	54.24	45.76
9	2	9	4	17	4261	9.36	49		2263	1998	53.11	46.89
8	26	9	4	17	4258	9.35	50		2364	1894	55.52	44.48
8	5	9	4	18	4255	9.34	51		2430	1825	57.11	42.89
6	30	9	3	18	4252	9.34	52		2352	1900	55.32	44.68
9	3	9	5	18	4251	9.33	53		2415	1836	56.81	43.19
4	15	9	4	18	4243	9.32	54		2453	1790	57.81	42.19
8	13	9	5	17	4241	9.31	55		2390	1851	56.35	43.65
8	6	9	5	17	4238	9.31	56		2319	1919	54.72	45.28
5	21	9	5	18	4237	9.3	57		2427	1810	57.28	42.72
12	4	9	6	17	4229	9.29	58		2275	1954	53.8	46.2
7	16	9	5	18	4228	9.28	59		2308	1920	54.59	45.41
10	23	9	6	17	4228	9.28	60		2339	1889	55.32	44.68
7	10	9	6	17	4226	9.28	61	45544	2313	1913	54.73	45.27
1	8	9	5	17	4225	9.28	62		2435	1790	57.63	42.37
9	11	9	6	17	4224	9.27	63		2318	1906	54.88	45.12
10	12	9	2	18	4220	9.27	64		2706	1514	64.12	35.88
4	15	9	4	17	4218	9.26	65		2277	1941	53.98	46.02
7	30	9	5	18	4216	9.26	66		2301	1915	54.58	45.42
9	2	9	4	18	4214	9.25	67		2378	1836	56.43	43.57
4	17	9	6	18	4211	9.25	68		2355	1856	55.92	44.08
7	23	9	5	18	4211	9.25	69		2333	1878	55.4	44.6

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	4	9	3	17	4210	9.24	70		2354	1856	55.91	44.09
8	14	9	6	18	4207	9.24	71		2400	1807	57.05	42.95
8	17	9	2	18	4205	9.23	72		2325	1880	55.29	44.71
4	16	9	5	18	4204	9.23	73		2339	1865	55.64	44.36
8	31	9	2	17	4204	9.23	74		2247	1957	53.45	46.55
10	2	9	6	17	4203	9.23	75		2224	1979	52.91	47.09
8	28	9	6	16	4201	9.22	76		2290	1911	54.51	45.49
8	28	9	6	18	4201	9.22	77		2323	1878	55.3	44.7
4	30	9	5	17	4199	9.22	78		2280	1919	54.3	45.7
1	9	9	6	18	4197	9.22	79		2387	1810	56.87	43.13
10	9	9	6	18	4196	9.21	80		2327	1869	55.46	44.54
1	7	9	4	17	4195	9.21	81	45544	2406	1789	57.35	42.65
7	27	9	2	18	4193	9.21	82		2336	1857	55.71	44.29
3	18	9	4	18	4187	9.19	83		2370	1817	56.6	43.4
8	4	9	3	18	4187	9.19	84		2404	1783	57.42	42.58
8	20	9	5	17	4187	9.19	85		2291	1896	54.72	45.28
4	9	9	5	18	4186	9.19	86		2206	1980	52.7	47.3
12	22	9	3	17	4186	9.19	87		2373	1813	56.69	43.31
9	18	9	6	17	4185	9.19	88		2266	1919	54.15	45.85
12	28	9	2	17	4184	9.19	89		2356	1828	56.31	43.69
8	21	9	6	18	4183	9.18	90		2344	1839	56.04	43.96
2	13	9	6	18	4179	9.18	91		2461	1718	58.89	41.11
6	19	9	6	17	4177	9.17	92		2261	1916	54.13	45.87
7	9	9	5	18	4177	9.17	93		2367	1810	56.67	43.33
4	14	9	3	18	4176	9.17	94		2445	1731	58.55	41.45
8	24	9	2	18	4174	9.16	95		2433	1741	58.29	41.71
4	3	9	6	18	4172	9.16	96		2332	1840	55.9	44.1
8	27	9	5	17	4171	9.16	97		2270	1901	54.42	45.58
5	14	9	5	18	4170	9.16	98		2404	1766	57.65	42.35
11	13	9	6	17	4170	9.16	99		2341	1829	56.14	43.86
8	12	9	4	17	4166	9.15	100		2366	1800	56.79	43.21
4	13	9	2	17	4165	9.15	101	45544	2521	1644	60.53	39.47
5	7	9	5	17	4165	9.15	102		2342	1823	56.23	43.77
7	14	9	3	18	4165	9.15	103		2394	1771	57.48	42.52
7	28	9	3	17	4164	9.14	104		2281	1883	54.78	45.22
7	23	9	5	17	4163	9.14	105		2236	1927	53.71	46.29
7	31	9	6	17	4162	9.14	106		2296	1866	55.17	44.83
8	19	9	4	18	4162	9.14	107		2364	1798	56.8	43.2
7	15	9	4	18	4159	9.13	108		2329	1830	56	44
4	22	9	4	17	4157	9.13	109		2318	1839	55.76	44.24
9	17	9	5	18	4157	9.13	110		2254	1903	54.22	45.78
2	13	9	6	17	4155	9.12	111		2417	1738	58.17	41.83
12	3	9	5	17	4155	9.12	112		2267	1888	54.56	45.44
7	1	9	4	17	4153	9.12	113		2445	1708	58.87	41.13
5	22	9	6	16	4152	9.12	114		2248	1904	54.14	45.86
6	16	9	3	18	4151	9.11	115		2365	1786	56.97	43.03
9	25	9	6	18	4149	9.11	116		2362	1787	56.93	43.07
7	30	9	5	17	4148	9.11	117		2319	1829	55.91	44.09
10	8	9	5	18	4145	9.1	118		2370	1775	57.18	42.82
5	14	9	5	17	4144	9.1	119		2309	1835	55.72	44.28
5	29	9	6	17	4144	9.1	120		2240	1904	54.05	45.95
8	14	9	6	16	4143	9.1	121	45544	2211	1932	53.37	46.63

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	7	9	3	18	4142	9.09	122		2401	1741	57.97	42.03
1	16	9	6	18	4138	9.09	123		2391	1747	57.78	42.22
2	20	9	6	18	4138	9.09	124		2382	1756	57.56	42.44
7	2	9	5	17	4138	9.09	125		2279	1859	55.07	44.93
4	17	9	6	17	4137	9.08	126		2269	1868	54.85	45.15
4	20	9	2	18	4134	9.08	127		2449	1685	59.24	40.76
12	18	9	6	17	4134	9.08	128		2288	1846	55.35	44.65
7	1	9	4	18	4128	9.06	129		2455	1673	59.47	40.53
3	19	9	5	18	4127	9.06	130		2312	1815	56.02	43.98
4	24	9	6	16	4127	9.06	131		2249	1878	54.49	45.51
4	10	9	6	17	4126	9.06	132		2319	1807	56.2	43.8
5	1	9	6	16	4126	9.06	133		2279	1847	55.24	44.76
8	18	9	3	18	4124	9.05	134		2315	1809	56.13	43.87
5	12	9	3	18	4123	9.05	135		2459	1664	59.64	40.36
4	21	9	3	18	4122	9.05	136		2433	1689	59.02	40.98
10	2	9	6	18	4122	9.05	137		2310	1812	56.04	43.96
8	7	9	6	18	4121	9.05	138		2401	1720	58.26	41.74
7	10	9	6	18	4119	9.04	139		2222	1897	53.95	46.05
8	17	9	2	17	4119	9.04	140		2318	1801	56.28	43.72
3	16	9	2	18	4118	9.04	141	45544	2321	1797	56.36	43.64
8	25	9	3	17	4118	9.04	142		2353	1765	57.14	42.86
4	29	9	4	17	4115	9.04	143		2362	1753	57.4	42.6
10	23	9	6	16	4115	9.04	144		2146	1969	52.15	47.85
7	17	9	6	17	4114	9.03	145		2338	1776	56.83	43.17
12	30	9	4	17	4113	9.03	146		2426	1687	58.98	41.02
7	21	9	3	18	4111	9.03	147		2338	1773	56.87	43.13
2	12	9	5	18	4110	9.02	148		2368	1742	57.62	42.38
7	31	9	6	18	4110	9.02	149		2321	1789	56.47	43.53
3	6	9	6	17	4109	9.02	150		2300	1809	55.97	44.03
5	4	9	2	17	4108	9.02	151		2306	1802	56.13	43.87
6	26	9	6	18	4108	9.02	152		2303	1805	56.06	43.94
9	4	9	6	18	4108	9.02	153		2344	1764	57.06	42.94
9	8	9	3	17	4108	9.02	154		2299	1809	55.96	44.04
8	19	9	4	17	4107	9.02	155		2269	1838	55.25	44.75
6	12	9	6	17	4102	9.01	156		2183	1919	53.22	46.78
11	11	9	4	17	4102	9.01	157		2458	1644	59.92	40.08
2	20	9	6	17	4101	9	158		2257	1844	55.04	44.96
6	5	9	6	17	4101	9	159		2236	1865	54.52	45.48
6	30	9	3	17	4101	9	160		2253	1848	54.94	45.06
8	11	9	3	18	4101	9	161	45544	2336	1765	56.96	43.04
5	15	9	6	16	4100	9	162		2097	2003	51.15	48.85
5	4	9	2	18	4099	9	163		2385	1714	58.18	41.82
7	29	9	4	17	4098	9	164		2298	1800	56.08	43.92
12	11	9	6	17	4098	9	165		2224	1874	54.27	45.73
12	21	9	2	17	4098	9	166		2308	1790	56.32	43.68
4	27	9	2	17	4094	8.99	167		2270	1824	55.45	44.55
6	25	9	5	17	4093	8.99	168		2254	1839	55.07	44.93
4	3	9	6	17	4092	8.98	169		2215	1877	54.13	45.87
4	23	9	5	17	4090	8.98	170		2324	1766	56.82	43.18
7	31	9	6	16	4089	8.98	171		2192	1897	53.61	46.39
4	28	9	3	17	4088	8.98	172		2307	1781	56.43	43.57
7	2	9	5	18	4087	8.97	173		2322	1765	56.81	43.19

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	10	9	2	18	4085	8.97	174		2350	1735	57.53	42.47
7	20	9	2	18	4084	8.97	175		2331	1753	57.08	42.92
5	20	9	4	18	4083	8.96	176		2381	1702	58.31	41.69
9	10	9	5	18	4080	8.96	177		2324	1756	56.96	43.04
5	5	9	3	18	4079	8.96	178		2388	1691	58.54	41.46
5	29	9	6	18	4079	8.96	179		2338	1741	57.32	42.68
9	4	9	6	16	4078	8.95	180		2248	1830	55.13	44.87
8	20	9	5	18	4077	8.95	181	45544	2316	1761	56.81	43.19
9	21	9	2	17	4076	8.95	182		2272	1804	55.74	44.26
11	20	9	6	18	4076	8.95	183		2290	1786	56.18	43.82
5	28	9	5	18	4075	8.95	184		2350	1725	57.67	42.33
7	24	9	6	16	4075	8.95	185		2110	1965	51.78	48.22
7	29	9	4	18	4075	8.95	186		2250	1825	55.21	44.79
8	18	9	3	17	4075	8.95	187		2269	1806	55.68	44.32
10	15	9	5	18	4074	8.95	188		2324	1750	57.04	42.96
10	28	9	4	18	4071	8.94	189		2386	1685	58.61	41.39
9	8	9	3	18	4070	8.94	190		2315	1755	56.88	43.12
12	3	9	5	18	4070	8.94	191		2312	1758	56.81	43.19
7	28	9	3	18	4069	8.93	192		2345	1724	57.63	42.37
11	6	9	6	17	4067	8.93	193		2227	1840	54.76	45.24
1	16	9	6	17	4064	8.92	194		2274	1790	55.95	44.05
5	11	9	2	18	4064	8.92	195		2409	1655	59.28	40.72
6	11	9	5	18	4064	8.92	196		2285	1779	56.23	43.77
9	28	9	2	18	4064	8.92	197		2317	1747	57.01	42.99
10	30	9	6	17	4064	8.92	198		2244	1820	55.22	44.78
12	22	9	3	18	4064	8.92	199		2397	1667	58.98	41.02
3	6	9	6	18	4063	8.92	200		2268	1795	55.82	44.18

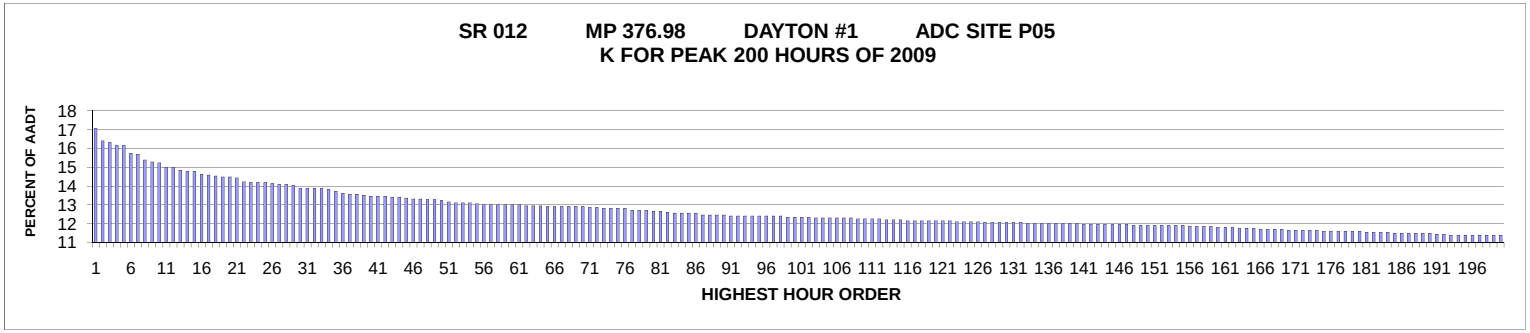

AADT= 1975 **K 30 FACTOR=** 13.87 **K 100 FACTOR=** 12.35 **K 200 FACTOR=** 11.39 **D FACTOR=** 55.29

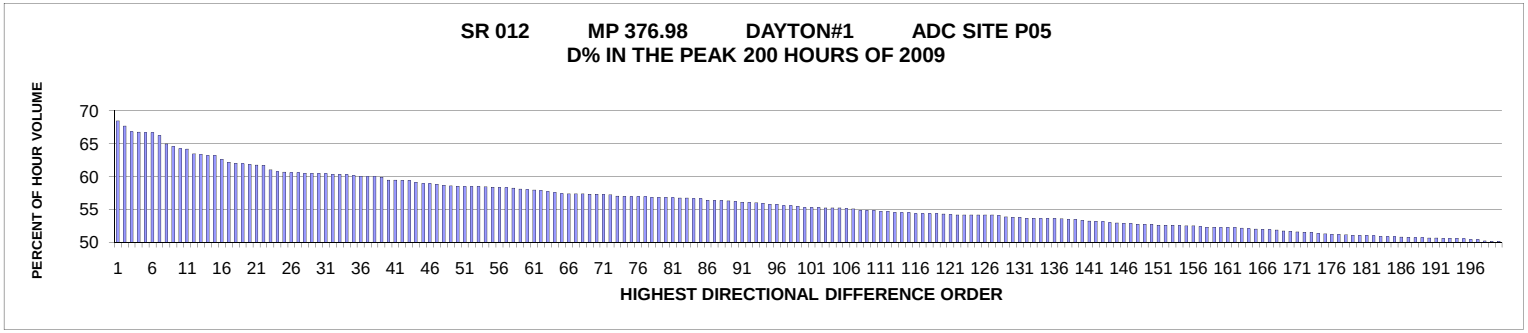

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
5	25	9	2	13	337	17.06	1	1975	118	219	35.01	64.99
11	29	9	1	16	324	16.41	2		153	171	47.22	52.78
5	25	9	2	12	322	16.3	3		104	218	32.3	67.7
5	22	9	6	16	319	16.15	4		187	132	58.62	41.38
5	22	9	6	18	319	16.15	5		178	141	55.8	44.2
5	25	9	2	14	311	15.75	6		105	206	33.76	66.24
5	25	9	2	15	310	15.7	7		114	196	36.77	63.23
11	29	9	1	15	304	15.39	8		158	146	51.97	48.03
7	5	9	1	14	302	15.29	9		121	181	40.07	59.93
7	5	9	1	13	301	15.24	10		100	201	33.22	66.78
5	25	9	2	16	296	14.99	11		130	166	43.92	56.08
7	5	9	1	17	296	14.99	12		128	168	43.24	56.76
10	16	9	6	16	293	14.84	13		172	121	58.7	41.3
5	22	9	6	17	292	14.78	14		166	126	56.85	43.15
6	21	9	1	13	292	14.78	15		141	151	48.29	51.71
7	3	9	6	12	289	14.63	16		157	132	54.33	45.67
9	4	9	6	16	288	14.58	17		164	124	56.94	43.06

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
9	4	9	6	17	287	14.53	18		151	136	52.61	47.39
11	25	9	4	15	286	14.48	19		154	132	53.85	46.15
11	25	9	4	16	286	14.48	20		154	132	53.85	46.15
7	5	9	1	15	285	14.43	21	1975	117	168	41.05	58.95
9	7	9	2	14	281	14.23	22		112	169	39.86	60.14
5	9	9	7	11	280	14.18	23		177	103	63.21	36.79
6	21	9	1	14	280	14.18	24		130	150	46.43	53.57
10	16	9	6	17	280	14.18	25		164	116	58.57	41.43
10	16	9	6	15	279	14.13	26		142	137	50.9	49.1
5	23	9	7	12	278	14.08	27		141	137	50.72	49.28
9	7	9	2	17	278	14.08	28		120	158	43.17	56.83
8	16	9	1	16	277	14.03	29		125	152	45.13	54.87
6	28	9	1	15	274	13.87	30		120	154	43.8	56.2
8	16	9	1	15	274	13.87	31		129	145	47.08	52.92
9	7	9	2	16	274	13.87	32		134	140	48.91	51.09
11	25	9	4	17	274	13.87	33		139	135	50.73	49.27
9	7	9	2	15	273	13.82	34		109	164	39.93	60.07
9	18	9	6	16	271	13.72	35		147	124	54.24	45.76
5	23	9	7	10	269	13.62	36		157	112	58.36	41.64
6	28	9	1	16	268	13.57	37		121	147	45.15	54.85
9	7	9	2	13	268	13.57	38		119	149	44.4	55.6
6	28	9	1	13	267	13.52	39		105	162	39.33	60.67
5	10	9	1	17	266	13.47	40		127	139	47.74	52.26
8	9	9	1	19	266	13.47	41	1975	149	117	56.02	43.98
8	21	9	6	16	266	13.47	42		140	126	52.63	47.37
6	19	9	6	14	265	13.42	43		145	120	54.72	45.28
11	29	9	1	13	265	13.42	44		127	138	47.92	52.08
5	22	9	6	19	264	13.37	45		152	112	57.58	42.42
6	19	9	6	15	263	13.32	46		145	118	55.13	44.87
7	5	9	1	18	263	13.32	47		108	155	41.06	58.94
2	27	9	6	18	262	13.27	48		96	166	36.64	63.36
5	25	9	2	17	262	13.27	49		104	158	39.69	60.31
8	9	9	1	18	261	13.22	50		140	121	53.64	46.36
3	21	9	7	17	260	13.16	51		107	153	41.15	58.85
5	25	9	2	11	259	13.11	52		109	150	42.08	57.92
9	4	9	6	18	259	13.11	53		139	120	53.67	46.33
11	29	9	1	17	259	13.11	54		146	113	56.37	43.63
9	20	9	1	15	258	13.06	55		131	127	50.78	49.22
5	1	9	6	17	257	13.01	56		142	115	55.25	44.75
7	5	9	1	16	257	13.01	57		81	176	31.52	68.48
9	5	9	7	12	257	13.01	58		159	98	61.87	38.13
9	18	9	6	18	257	13.01	59		142	115	55.25	44.75
9	20	9	1	16	257	13.01	60		135	122	52.53	47.47
9	25	9	6	17	257	13.01	61	1975	161	96	62.65	37.35
6	28	9	1	18	256	12.96	62		122	134	47.66	52.34
8	9	9	1	16	256	12.96	63		125	131	48.83	51.17
8	23	9	1	15	256	12.96	64		110	146	42.97	57.03
6	12	9	6	14	255	12.91	65		139	116	54.51	45.49
6	19	9	6	17	255	12.91	66		132	123	51.76	48.24
8	9	9	1	17	255	12.91	67		114	141	44.71	55.29
8	16	9	1	14	255	12.91	68		126	129	49.41	50.59
9	7	9	2	12	255	12.91	69		97	158	38.04	61.96

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
9	18	9	6	17	255	12.91	70		149	106	58.43	41.57
4	10	9	6	17	254	12.86	71		151	103	59.45	40.55
7	5	9	1	12	254	12.86	72		90	164	35.43	64.57
7	10	9	6	15	253	12.81	73		129	124	50.99	49.01
8	21	9	6	13	253	12.81	74		153	100	60.47	39.53
8	21	9	6	14	253	12.81	75		142	111	56.13	43.87
9	11	9	6	14	253	12.81	76		138	115	54.55	45.45
5	22	9	6	15	251	12.71	77		144	107	57.37	42.63
9	4	9	6	14	251	12.71	78		133	118	52.99	47.01
9	13	9	1	16	251	12.71	79		115	136	45.82	54.18
6	5	9	6	14	250	12.66	80		129	121	51.6	48.4
8	23	9	1	16	250	12.66	81	1975	111	139	44.4	55.6
6	26	9	6	16	249	12.61	82		143	106	57.43	42.57
7	3	9	6	13	248	12.56	83		141	107	56.85	43.15
8	14	9	6	15	248	12.56	84		137	111	55.24	44.76
9	4	9	6	15	248	12.56	85		142	106	57.26	42.74
9	11	9	6	16	248	12.56	86		119	129	47.98	52.02
4	19	9	1	17	246	12.46	87		126	120	51.22	48.78
6	28	9	1	12	246	12.46	88		93	153	37.8	62.2
7	3	9	6	15	246	12.46	89		136	110	55.28	44.72
9	20	9	1	18	246	12.46	90		103	143	41.87	58.13
6	12	9	6	15	245	12.41	91		124	121	50.61	49.39
6	19	9	6	16	245	12.41	92		136	109	55.51	44.49
6	21	9	1	12	245	12.41	93		107	138	43.67	56.33
6	28	9	1	17	245	12.41	94		114	131	46.53	53.47
7	10	9	6	14	245	12.41	95		131	114	53.47	46.53
8	7	9	6	14	245	12.41	96		121	124	49.39	50.61
9	20	9	1	14	245	12.41	97		122	123	49.8	50.2
9	25	9	6	15	245	12.41	98		132	113	53.88	46.12
6	5	9	6	15	244	12.35	99		131	113	53.69	46.31
6	28	9	1	11	244	12.35	100		104	140	42.62	57.38
8	7	9	6	17	244	12.35	101	1975	133	111	54.51	45.49
11	25	9	4	14	244	12.35	102		139	105	56.97	43.03
4	5	9	1	18	243	12.3	103		141	102	58.02	41.98
8	2	9	1	14	243	12.3	104		116	127	47.74	52.26
10	2	9	6	15	243	12.3	105		133	110	54.73	45.27
10	18	9	1	15	243	12.3	106		106	137	43.62	56.38
10	23	9	6	16	243	12.3	107		116	127	47.74	52.26
10	23	9	6	17	243	12.3	108		136	107	55.97	44.03
5	15	9	6	17	242	12.25	109		135	107	55.79	44.21
5	22	9	6	14	242	12.25	110		146	96	60.33	39.67
6	12	9	6	17	242	12.25	111		124	118	51.24	48.76
7	3	9	6	14	242	12.25	112		147	95	60.74	39.26
8	9	9	1	12	241	12.2	113		100	141	41.49	58.51
8	9	9	1	15	241	12.2	114		100	141	41.49	58.51
9	25	9	6	16	241	12.2	115		131	110	54.36	45.64
4	24	9	6	16	240	12.15	116		136	104	56.67	43.33
6	7	9	1	16	240	12.15	117		119	121	49.58	50.42
8	2	9	1	15	240	12.15	118		110	130	45.83	54.17
8	16	9	1	17	240	12.15	119		110	130	45.83	54.17
8	23	9	1	14	240	12.15	120		104	136	43.33	56.67
10	9	9	6	17	240	12.15	121	1975	144	96	60	40

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
10	9	9	6	18	240	12.15	122		122	118	50.83	49.17
6	28	9	1	14	239	12.1	123		101	138	42.26	57.74
8	6	9	5	15	239	12.1	124		122	117	51.05	48.95
8	16	9	1	18	239	12.1	125		97	142	40.59	59.41
10	9	9	6	15	239	12.1	126		112	127	46.86	53.14
4	3	9	6	17	238	12.05	127		144	94	60.5	39.5
8	6	9	5	16	238	12.05	128		100	138	42.02	57.98
8	14	9	6	14	238	12.05	129		144	94	60.5	39.5
9	20	9	1	17	238	12.05	130		120	118	50.42	49.58
9	25	9	6	18	238	12.05	131		139	99	58.4	41.6
10	9	9	6	19	238	12.05	132		126	112	52.94	47.06
4	5	9	1	17	237	12	133		119	118	50.21	49.79
4	26	9	1	17	237	12	134		102	135	43.04	56.96
5	8	9	6	15	237	12	135		125	112	52.74	47.26
8	14	9	6	17	237	12	136		136	101	57.38	42.62
9	5	9	7	13	237	12	137		131	106	55.27	44.73
9	7	9	2	11	237	12	138		90	147	37.97	62.03
9	27	9	1	17	237	12	139		102	135	43.04	56.96
10	18	9	1	16	237	12	140		114	123	48.1	51.9
5	10	9	1	15	236	11.95	141	1975	106	130	44.92	55.08
6	14	9	1	15	236	11.95	142		112	124	47.46	52.54
8	23	9	1	13	236	11.95	143		93	143	39.41	60.59
9	7	9	2	18	236	11.95	144		116	120	49.15	50.85
9	19	9	7	11	236	11.95	145		143	93	60.59	39.41
10	4	9	1	15	236	11.95	146		92	144	38.98	61.02
10	23	9	6	18	236	11.95	147		134	102	56.78	43.22
5	8	9	6	18	235	11.9	148		123	112	52.34	47.66
6	21	9	1	16	235	11.9	149		109	126	46.38	53.62
6	26	9	6	12	235	11.9	150		120	115	51.06	48.94
7	2	9	5	16	235	11.9	151		151	84	64.26	35.74
7	5	9	1	11	235	11.9	152		90	145	38.3	61.7
8	21	9	6	15	235	11.9	153		142	93	60.43	39.57
10	18	9	1	14	235	11.9	154		98	137	41.7	58.3
11	25	9	4	13	235	11.9	155		124	111	52.77	47.23
5	8	9	6	17	234	11.85	156		139	95	59.4	40.6
5	17	9	1	17	234	11.85	157		78	156	33.33	66.67
6	20	9	7	16	234	11.85	158		123	111	52.56	47.44
8	7	9	6	15	234	11.85	159		132	102	56.41	43.59
4	19	9	1	16	233	11.8	160		109	124	46.78	53.22
6	21	9	1	17	233	11.8	161	1975	118	115	50.64	49.36
6	25	9	5	11	233	11.8	162		125	108	53.65	46.35
8	9	9	1	14	232	11.75	163		94	138	40.52	59.48
9	27	9	1	16	232	11.75	164		99	133	42.67	57.33
10	25	9	1	15	232	11.75	165		92	140	39.66	60.34
4	5	9	1	16	231	11.7	166		108	123	46.75	53.25
5	23	9	7	13	231	11.7	167		111	120	48.05	51.95
6	26	9	6	14	231	11.7	168		125	106	54.11	45.89
7	2	9	5	18	231	11.7	169		154	77	66.67	33.33
6	14	9	1	13	230	11.65	170		112	118	48.7	51.3
6	20	9	7	14	230	11.65	171		110	120	47.83	52.17
8	2	9	1	16	230	11.65	172		96	134	41.74	58.26
10	16	9	6	18	230	11.65	173		138	92	60	40

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
11	25	9	4	18	230	11.65	174		125	105	54.35	45.65
3	22	9	1	17	229	11.59	175		147	82	64.19	35.81
5	25	9	2	18	229	11.59	176		76	153	33.19	66.81
6	7	9	1	15	229	11.59	177		105	124	45.85	54.15
6	7	9	1	17	229	11.59	178		114	115	49.78	50.22
6	20	9	7	12	229	11.59	179		95	134	41.48	58.52
9	11	9	6	18	229	11.59	180		130	99	56.77	43.23
7	10	9	6	12	228	11.54	181	1975	112	116	49.12	50.88
8	14	9	6	18	228	11.54	182		124	104	54.39	45.61
9	20	9	1	11	228	11.54	183		124	104	54.39	45.61
11	6	9	6	17	228	11.54	184		120	108	52.63	47.37
5	22	9	6	13	227	11.49	185		144	83	63.44	36.56
5	24	9	1	12	227	11.49	186		104	123	45.81	54.19
7	2	9	5	19	227	11.49	187		130	97	57.27	42.73
8	7	9	6	16	227	11.49	188		110	117	48.46	51.54
9	13	9	1	18	227	11.49	189		112	115	49.34	50.66
9	20	9	1	12	227	11.49	190		123	104	54.19	45.81
6	26	9	6	17	226	11.44	191		124	102	54.87	45.13
10	4	9	1	17	226	11.44	192		110	116	48.67	51.33
3	22	9	1	15	225	11.39	193		139	86	61.78	38.22
6	19	9	6	11	225	11.39	194		116	109	51.56	48.44
7	3	9	6	17	225	11.39	195		133	92	59.11	40.89
7	11	9	7	12	225	11.39	196		106	119	47.11	52.89
8	14	9	6	12	225	11.39	197		105	120	46.67	53.33
8	30	9	1	17	225	11.39	198		114	111	50.67	49.33
10	9	9	6	16	225	11.39	199		129	96	57.33	42.67
10	11	9	1	16	225	11.39	200		107	118	47.56	52.44

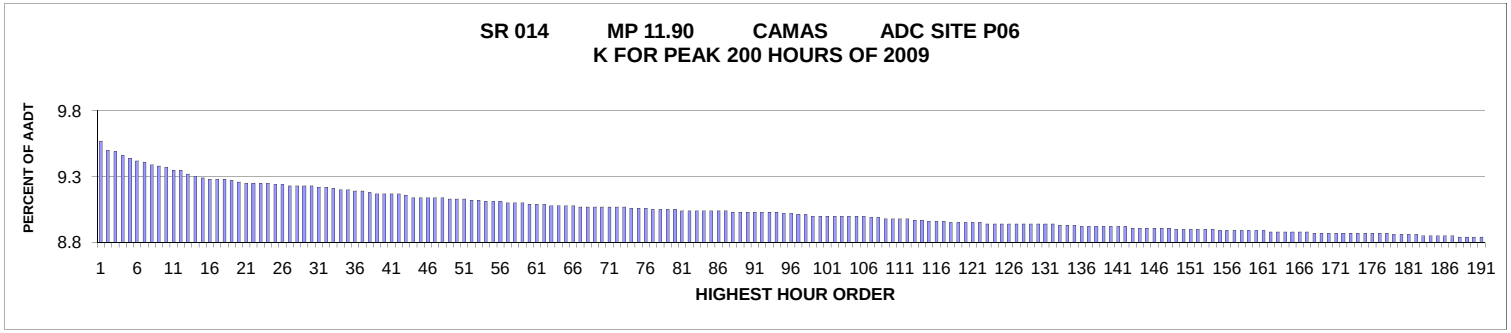

AADT= 37838 **K 30 FACTOR=** 9.25 **K 100 FACTOR=** 9.03 **K 200 FACTOR=** 8.84 **D FACTOR=** 58.6

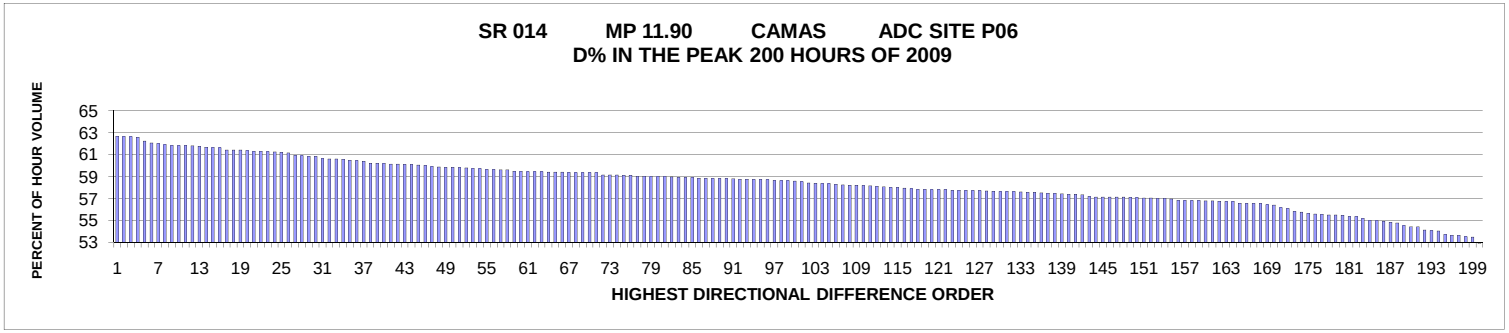

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
5	29	9	6	17	3622	9.57	1	37838	2080	1542	57.43	42.57
6	18	9	5	17	3595	9.5	2		2078	1517	57.8	42.2
12	4	9	6	17	3590	9.49	3		2083	1507	58.02	41.98
4	7	9	3	17	3578	9.46	4		2078	1500	58.08	41.92
5	8	9	6	17	3571	9.44	5		1987	1584	55.64	44.36
12	18	9	6	17	3563	9.42	6		2026	1537	56.86	43.14
5	1	9	6	18	3562	9.41	7		2054	1508	57.66	42.34
6	18	9	5	18	3552	9.39	8		2054	1498	57.83	42.17
5	22	9	6	16	3550	9.38	9		1970	1580	55.49	44.51
5	21	9	5	17	3544	9.37	10		1976	1568	55.76	44.24
3	13	9	6	18	3538	9.35	11		2080	1458	58.79	41.21
5	15	9	6	17	3538	9.35	12		2010	1528	56.81	43.19
4	24	9	6	17	3525	9.32	13		1993	1532	56.54	43.46
5	1	9	6	17	3518	9.3	14		2027	1491	57.62	42.38
6	5	9	6	17	3514	9.29	15		1945	1569	55.35	44.65
10	28	9	4	17	3512	9.28	16		2076	1436	59.11	40.89
5	28	9	5	17	3510	9.28	17		2006	1504	57.15	42.85

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
11	6	9	6	17	3510	9.28	18		2001	1509	57.01	42.99
6	9	9	3	17	3506	9.27	19		2025	1481	57.76	42.24
8	26	9	4	17	3503	9.26	20		2059	1444	58.78	41.22
5	28	9	5	18	3500	9.25	21	37838	2129	1371	60.83	39.17
6	10	9	4	17	3500	9.25	22		2026	1474	57.89	42.11
10	30	9	6	17	3500	9.25	23		2052	1448	58.63	41.37
4	21	9	3	18	3499	9.25	24		2070	1429	59.16	40.84
8	27	9	5	17	3497	9.24	25		1974	1523	56.45	43.55
6	11	9	5	17	3495	9.24	26		2012	1483	57.57	42.43
6	1	9	2	17	3492	9.23	27		2055	1437	58.85	41.15
9	18	9	6	17	3492	9.23	28		1959	1533	56.1	43.9
6	12	9	6	17	3491	9.23	29		1969	1522	56.4	43.6
9	9	9	4	18	3491	9.23	30		2152	1339	61.64	38.36
6	15	9	2	18	3488	9.22	31		2110	1378	60.49	39.51
6	16	9	3	18	3488	9.22	32		2136	1352	61.24	38.76
5	14	9	5	17	3486	9.21	33		1991	1495	57.11	42.89
2	12	9	5	18	3481	9.2	34		2069	1412	59.44	40.56
5	1	9	6	16	3480	9.2	35		1931	1549	55.49	44.51
10	6	9	3	17	3477	9.19	36		2049	1428	58.93	41.07
6	5	9	6	18	3476	9.19	37		1995	1481	57.39	42.61
6	10	9	4	18	3473	9.18	38		2098	1375	60.41	39.59
6	26	9	6	18	3471	9.17	39		2018	1453	58.14	41.86
9	23	9	4	18	3470	9.17	40		2090	1380	60.23	39.77
5	29	9	6	18	3469	9.17	41	37838	2061	1408	59.41	40.59
6	17	9	4	18	3468	9.17	42		2073	1395	59.78	40.22
4	21	9	3	17	3467	9.16	43		1994	1473	57.51	42.49
5	7	9	5	18	3459	9.14	44		2145	1314	62.01	37.99
9	10	9	5	17	3459	9.14	45		1956	1503	56.55	43.45
6	17	9	4	17	3458	9.14	46		1974	1484	57.09	42.91
9	11	9	6	18	3458	9.14	47		1964	1494	56.8	43.2
10	15	9	5	17	3457	9.14	48		2070	1387	59.88	40.12
2	27	9	6	17	3456	9.13	49		1961	1495	56.74	43.26
5	26	9	3	17	3455	9.13	50		2039	1416	59.02	40.98
10	1	9	5	17	3453	9.13	51		2021	1432	58.53	41.47
9	2	9	4	18	3452	9.12	52		2134	1318	61.82	38.18
9	25	9	6	17	3450	9.12	53		1965	1485	56.96	43.04
5	20	9	4	17	3447	9.11	54		2020	1427	58.6	41.4
8	18	9	3	18	3447	9.11	55		1994	1453	57.85	42.15
4	16	9	5	17	3446	9.11	56		1989	1457	57.72	42.28
6	5	9	6	16	3445	9.1	57		1823	1622	52.92	47.08
6	11	9	5	18	3443	9.1	58		2115	1328	61.43	38.57
9	11	9	6	17	3443	9.1	59		1934	1509	56.17	43.83
8	26	9	4	18	3441	9.09	60		2042	1399	59.34	40.66
10	20	9	3	17	3441	9.09	61	37838	1996	1445	58.01	41.99
2	20	9	6	16	3438	9.09	62		1845	1593	53.66	46.34
6	12	9	6	18	3437	9.08	63		1976	1461	57.49	42.51
12	3	9	5	17	3436	9.08	64		2001	1435	58.24	41.76
6	4	9	5	17	3435	9.08	65		1986	1449	57.82	42.18
10	8	9	5	18	3434	9.08	66		2026	1408	59	41
3	13	9	6	17	3433	9.07	67		2006	1427	58.43	41.57
4	22	9	4	17	3433	9.07	68		2038	1395	59.36	40.64
11	4	9	4	17	3433	9.07	69		2047	1386	59.63	40.37

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
4	28	9	3	17	3432	9.07	70		2030	1402	59.15	40.85
5	29	9	6	16	3432	9.07	71		1868	1564	54.43	45.57
6	3	9	4	18	3432	9.07	72		2088	1344	60.84	39.16
9	28	9	2	17	3432	9.07	73		2063	1369	60.11	39.89
1	23	9	6	17	3429	9.06	74		1956	1473	57.04	42.96
9	23	9	4	17	3429	9.06	75		1994	1435	58.15	41.85
6	2	9	3	17	3427	9.06	76		1967	1460	57.4	42.6
2	6	9	6	17	3424	9.05	77		1956	1468	57.13	42.87
4	23	9	5	17	3424	9.05	78		2061	1363	60.19	39.81
9	30	9	4	18	3423	9.05	79		2142	1281	62.58	37.42
11	3	9	3	17	3423	9.05	80		2020	1403	59.01	40.99
10	22	9	5	17	3422	9.04	81	37838	2024	1398	59.15	40.85
8	27	9	5	18	3421	9.04	82		1971	1450	57.61	42.39
9	4	9	6	17	3421	9.04	83		1975	1446	57.73	42.27
4	10	9	6	16	3420	9.04	84		1848	1572	54.04	45.96
9	17	9	5	17	3420	9.04	85		2043	1377	59.74	40.26
4	16	9	5	18	3419	9.04	86		2029	1390	59.34	40.66
10	2	9	6	17	3419	9.04	87		1972	1447	57.68	42.32
4	15	9	4	18	3418	9.03	88		2083	1335	60.94	39.06
5	20	9	4	18	3418	9.03	89		2127	1291	62.23	37.77
8	19	9	4	18	3418	9.03	90		1976	1442	57.81	42.19
9	10	9	5	18	3418	9.03	91		2032	1386	59.45	40.55
4	7	9	3	18	3416	9.03	92		2069	1347	60.57	39.43
4	22	9	4	18	3416	9.03	93		2054	1362	60.13	39.87
12	11	9	6	17	3415	9.03	94		1968	1447	57.63	42.37
4	10	9	6	17	3412	9.02	95		1877	1535	55.01	44.99
9	30	9	4	17	3412	9.02	96		2035	1377	59.64	40.36
3	27	9	6	17	3411	9.01	97		1936	1475	56.76	43.24
5	27	9	4	17	3411	9.01	98		2028	1383	59.45	40.55
6	16	9	3	17	3407	9	99		1954	1453	57.35	42.65
4	24	9	6	18	3406	9	100		2009	1397	58.98	41.02
9	17	9	5	18	3406	9	101	37838	2022	1384	59.37	40.63
4	24	9	6	16	3405	9	102		1867	1538	54.83	45.17
4	30	9	5	18	3405	9	103		2040	1365	59.91	40.09
9	8	9	3	17	3405	9	104		2064	1341	60.62	39.38
6	9	9	3	18	3404	9	105		2058	1346	60.46	39.54
9	1	9	3	17	3404	9	106		1957	1447	57.49	42.51
10	13	9	3	17	3400	8.99	107		2071	1329	60.91	39.09
12	4	9	6	18	3400	8.99	108		2101	1299	61.79	38.21
4	17	9	6	17	3398	8.98	109		1889	1509	55.59	44.41
1	9	9	6	17	3397	8.98	110		1956	1441	57.58	42.42
4	23	9	5	18	3397	8.98	111		2059	1338	60.61	39.39
10	1	9	5	18	3397	8.98	112		1992	1405	58.64	41.36
6	26	9	6	17	3395	8.97	113		1928	1467	56.79	43.21
10	15	9	5	18	3395	8.97	114		2078	1317	61.21	38.79
10	6	9	3	18	3391	8.96	115		1979	1412	58.36	41.64
4	9	9	5	18	3390	8.96	116		2099	1291	61.92	38.08
7	9	9	5	18	3389	8.96	117		1939	1450	57.21	42.79
4	30	9	5	17	3388	8.95	118		1933	1455	57.05	42.95
5	22	9	6	17	3388	8.95	119		1834	1554	54.13	45.87
9	2	9	4	17	3387	8.95	120		1990	1397	58.75	41.25
9	28	9	2	18	3386	8.95	121	37838	2093	1293	61.81	38.19

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
10	2	9	6	18	3386	8.95	122		1992	1394	58.83	41.17
7	16	9	5	18	3384	8.94	123		2010	1374	59.4	40.6
10	9	9	6	18	3384	8.94	124		1961	1423	57.95	42.05
5	7	9	5	17	3383	8.94	125		1922	1461	56.81	43.19
9	3	9	5	18	3383	8.94	126		2035	1348	60.15	39.85
11	18	9	4	17	3383	8.94	127		2069	1314	61.16	38.84
10	30	9	6	16	3382	8.94	128		1857	1525	54.91	45.09
4	30	9	5	16	3381	8.94	129		1815	1566	53.68	46.32
5	8	9	6	18	3381	8.94	130		1973	1408	58.36	41.64
5	27	9	4	18	3381	8.94	131		2099	1282	62.08	37.92
6	12	9	6	16	3381	8.94	132		1840	1541	54.42	45.58
5	8	9	6	16	3380	8.93	133		1843	1537	54.53	45.47
12	4	9	6	16	3379	8.93	134		1865	1514	55.19	44.81
6	3	9	4	17	3378	8.93	135		1966	1412	58.2	41.8
5	12	9	3	17	3377	8.92	136		1969	1408	58.31	41.69
5	19	9	3	17	3377	8.92	137		1983	1394	58.72	41.28
9	24	9	5	16	3377	8.92	138		1876	1501	55.55	44.45
4	14	9	3	17	3376	8.92	139		1987	1389	58.86	41.14
7	10	9	6	17	3375	8.92	140		1884	1491	55.82	44.18
10	30	9	6	18	3375	8.92	141	37838	2026	1349	60.03	39.97
3	6	9	6	17	3374	8.92	142		1948	1426	57.74	42.26
7	1	9	4	17	3373	8.91	143		1908	1465	56.57	43.43
4	15	9	4	17	3372	8.91	144		2001	1371	59.34	40.66
10	23	9	6	17	3372	8.91	145		1963	1409	58.21	41.79
10	28	9	4	18	3372	8.91	146		1987	1385	58.93	41.07
11	12	9	5	17	3371	8.91	147		2018	1353	59.86	40.14
12	3	9	5	18	3370	8.91	148		2066	1304	61.31	38.69
11	10	9	3	17	3369	8.9	149		2043	1326	60.64	39.36
10	27	9	3	17	3368	8.9	150		2078	1290	61.7	38.3
5	15	9	6	16	3367	8.9	151		1821	1546	54.08	45.92
6	8	9	2	18	3367	8.9	152		2015	1352	59.85	40.15
6	23	9	3	18	3367	8.9	153		2024	1343	60.11	39.89
5	11	9	2	18	3366	8.9	154		2068	1298	61.44	38.56
11	5	9	5	18	3365	8.89	155		1999	1366	59.41	40.59
4	17	9	6	18	3363	8.89	156		1981	1382	58.91	41.09
4	20	9	2	17	3363	8.89	157		1985	1378	59.02	40.98
6	1	9	2	18	3363	8.89	158		2107	1256	62.65	37.35
9	25	9	6	16	3363	8.89	159		1842	1521	54.77	45.23
11	13	9	6	18	3363	8.89	160		2000	1363	59.47	40.53
9	4	9	6	16	3362	8.89	161	37838	1865	1497	55.47	44.53
12	23	9	4	17	3361	8.88	162		1977	1384	58.82	41.18
3	26	9	5	17	3360	8.88	163		1970	1390	58.63	41.37
6	8	9	2	17	3360	8.88	164		1974	1386	58.75	41.25
10	20	9	3	18	3360	8.88	165		2024	1336	60.24	39.76
12	18	9	6	16	3360	8.88	166		1805	1555	53.72	46.28
4	8	9	4	18	3359	8.88	167		2104	1255	62.64	37.36
6	24	9	4	18	3358	8.87	168		2006	1352	59.74	40.26
7	15	9	4	18	3358	8.87	169		2002	1356	59.62	40.38
10	9	9	6	17	3358	8.87	170		1905	1453	56.73	43.27
2	3	9	3	18	3357	8.87	171		2070	1287	61.66	38.34
11	20	9	6	17	3357	8.87	172		1960	1397	58.39	41.61
9	25	9	6	18	3356	8.87	173		1918	1438	57.15	42.85

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
11	9	9	2	17	3356	8.87	174		2075	1281	61.83	38.17
4	28	9	3	18	3355	8.87	175		2074	1281	61.82	38.18
9	3	9	5	17	3355	8.87	176		1996	1359	59.49	40.51
10	21	9	4	17	3355	8.87	177		2057	1298	61.31	38.69
11	17	9	3	17	3355	8.87	178		2007	1348	59.82	40.18
8	28	9	6	16	3354	8.86	179		1794	1560	53.49	46.51
12	2	9	4	18	3352	8.86	180		2057	1295	61.37	38.63
4	6	9	2	18	3351	8.86	181	37838	1999	1352	59.65	40.35
11	12	9	5	18	3351	8.86	182		2053	1298	61.27	38.73
2	4	9	4	18	3350	8.85	183		2100	1250	62.69	37.31
5	18	9	2	17	3350	8.85	184		1976	1374	58.99	41.01
9	18	9	6	16	3348	8.85	185		1841	1507	54.99	45.01
9	24	9	5	18	3348	8.85	186		1970	1378	58.84	41.16
11	25	9	4	16	3348	8.85	187		1792	1556	53.52	46.48
5	6	9	4	18	3346	8.84	188		2055	1291	61.42	38.58
7	16	9	5	17	3346	8.84	189		1912	1434	57.14	42.86
10	22	9	5	18	3346	8.84	190		1948	1398	58.22	41.78
3	26	9	5	18	3345	8.84	191		2009	1336	60.06	39.94
9	10	9	5	16	3345	8.84	192		1787	1558	53.42	46.58
12	2	9	4	17	3345	8.84	193		2002	1343	59.85	40.15
9	22	9	3	18	3344	8.84	194		1977	1367	59.12	40.88
9	1	9	3	18	3343	8.84	195		1998	1345	59.77	40.23
7	1	9	4	18	3342	8.83	196		1974	1368	59.07	40.93
4	9	9	5	17	3341	8.83	197		1947	1394	58.28	41.72
4	29	9	4	18	3341	8.83	198		1995	1346	59.71	40.29
11	17	9	3	18	3341	8.83	199		2087	1254	62.47	37.53
11	30	9	2	17	3341	8.83	200		1998	1343	59.8	40.2

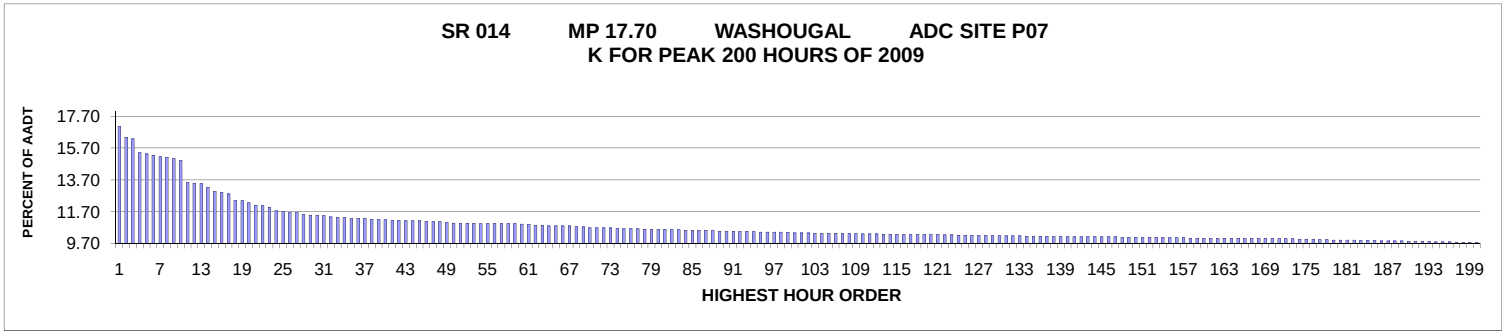

AADT= 5734 **K 30 FACTOR=** 11.48 **K 100 FACTOR=** 10.34 **K 200 FACTOR=** 9.75 **D FACTOR=** 56.25

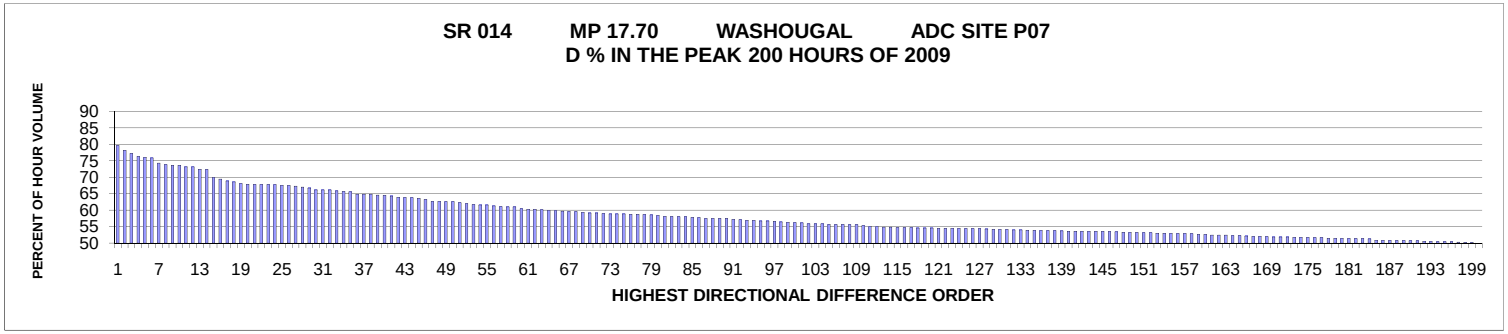

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	8	9	4	14	978	17.06	1	5734	779	199	79.65	20.35
7	8	9	4	16	939	16.38	2		687	252	73.16	26.84
7	8	9	4	10	933	16.27	3		708	225	75.88	24.12
7	8	9	4	13	883	15.40	4		650	233	73.61	26.39
7	8	9	4	12	879	15.33	5		687	192	78.16	21.84
7	8	9	4	17	874	15.24	6		645	229	73.80	26.20
7	8	9	4	9	868	15.14	7		670	198	77.19	22.81
7	8	9	4	15	867	15.12	8		659	208	76.01	23.99
7	8	9	4	11	861	15.02	9		657	204	76.31	23.69
7	8	9	4	18	856	14.93	10		571	285	66.71	33.29
5	25	9	2	15	775	13.52	11		285	490	36.77	63.23
5	25	9	2	14	774	13.50	12		324	450	41.86	58.14
4	19	9	1	16	771	13.45	13		279	492	36.19	63.81
5	25	9	2	16	758	13.22	14		195	563	25.73	74.27
5	25	9	2	13	743	12.96	15		370	373	49.80	50.20
7	8	9	4	8	740	12.91	16		489	251	66.08	33.92
7	8	9	4	19	734	12.80	17		531	203	72.34	27.66

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
4	5	9	1	16	710	12.38	18		290	420	40.85	59.15
4	19	9	1	17	710	12.38	19		223	487	31.41	68.59
7	11	9	7	16	701	12.23	20		265	436	37.80	62.20
12	13	9	1	13	694	12.10	21	5734	299	395	43.08	56.92
5	25	9	2	17	692	12.07	22		208	484	30.06	69.94
4	5	9	1	17	687	11.98	23		227	460	33.04	66.96
8	16	9	1	17	673	11.74	24		228	445	33.88	66.12
4	19	9	1	15	672	11.72	25		297	375	44.20	55.80
7	26	9	1	13	667	11.63	26		308	359	46.18	53.82
8	16	9	1	16	667	11.63	27		249	418	37.33	62.67
4	19	9	1	13	659	11.49	28		379	280	57.51	42.49
4	19	9	1	14	658	11.48	29		338	320	51.37	48.63
7	11	9	7	15	658	11.48	30		265	393	40.27	59.73
8	16	9	1	18	656	11.44	31		222	434	33.84	66.16
4	5	9	1	15	651	11.35	32		274	377	42.09	57.91
6	18	9	5	18	650	11.34	33		273	377	42.00	58.00
5	24	9	1	17	649	11.32	34		171	478	26.35	73.65
7	10	9	6	17	647	11.28	35		291	356	44.98	55.02
5	25	9	2	12	646	11.27	36		346	300	53.56	46.44
8	23	9	1	16	646	11.27	37		252	394	39.01	60.99
8	15	9	7	16	643	11.21	38		324	319	50.39	49.61
7	24	9	6	17	642	11.20	39		302	340	47.04	52.96
5	24	9	1	15	640	11.16	40		280	360	43.75	56.25
7	18	9	7	14	638	11.13	41	5734	331	307	51.88	48.12
8	16	9	1	14	638	11.13	42		315	323	49.37	50.63
5	16	9	7	16	637	11.11	43		263	374	41.29	58.71
5	22	9	6	17	637	11.11	44		310	327	48.67	51.33
7	19	9	1	16	637	11.11	45		238	399	37.36	62.64
5	9	9	7	13	635	11.07	46		361	274	56.85	43.15
7	19	9	1	14	635	11.07	47		293	342	46.14	53.86
8	9	9	1	17	635	11.07	48		244	391	38.43	61.57
8	14	9	6	17	631	11.00	49		310	321	49.13	50.87
8	16	9	1	15	629	10.97	50		303	326	48.17	51.83
5	10	9	1	15	628	10.95	51		260	368	41.40	58.60
7	26	9	1	14	628	10.95	52		279	349	44.43	55.57
12	13	9	1	12	628	10.95	53		325	303	51.75	48.25
4	19	9	1	18	627	10.93	54		173	454	27.59	72.41
7	3	9	6	14	627	10.93	55		332	295	52.95	47.05
7	5	9	1	14	627	10.93	56		286	341	45.61	54.39
5	10	9	1	14	626	10.92	57		325	301	51.92	48.08
5	16	9	7	17	626	10.92	58		257	369	41.05	58.95
5	24	9	1	14	626	10.92	59		368	258	58.79	41.21
7	18	9	7	15	625	10.90	60		345	280	55.20	44.80
8	23	9	1	14	624	10.88	61	5734	307	317	49.20	50.80
5	10	9	1	16	621	10.83	62		214	407	34.46	65.54
10	9	9	6	16	621	10.83	63		283	338	45.57	54.43
5	25	9	2	18	618	10.78	64		166	452	26.86	73.14
7	5	9	1	15	618	10.78	65		259	359	41.91	58.09
8	15	9	7	14	618	10.78	66		330	288	53.40	46.60
9	18	9	6	18	618	10.78	67		282	336	45.63	54.37
9	18	9	6	17	616	10.74	68		285	331	46.27	53.73
7	10	9	6	16	615	10.73	69		315	300	51.22	48.78

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
4	5	9	1	14	612	10.67	70		328	284	53.59	46.41
10	9	9	6	17	612	10.67	71		287	325	46.90	53.10
8	15	9	7	15	611	10.66	72		288	323	47.14	52.86
9	7	9	2	15	611	10.66	73		238	373	38.95	61.05
8	2	9	1	17	609	10.62	74		228	381	37.44	62.56
5	9	9	7	16	608	10.60	75		251	357	41.28	58.72
5	10	9	1	17	608	10.60	76		196	412	32.24	67.76
8	9	9	1	16	608	10.60	77		261	347	42.93	57.07
9	11	9	6	17	607	10.59	78		276	331	45.47	54.53
6	14	9	1	16	606	10.57	79		213	393	35.15	64.85
9	25	9	6	17	606	10.57	80		268	338	44.22	55.78
11	6	9	6	17	606	10.57	81	5734	303	303	50.00	50.00
6	19	9	6	17	605	10.55	82		328	277	54.21	45.79
8	21	9	6	17	605	10.55	83		294	311	48.60	51.40
9	27	9	1	15	604	10.53	84		273	331	45.20	54.80
5	24	9	1	13	603	10.52	85		361	242	59.87	40.13
9	13	9	1	17	603	10.52	86		212	391	35.16	64.84
10	10	9	7	16	603	10.52	87		261	342	43.28	56.72
5	30	9	7	15	602	10.50	88		245	357	40.70	59.30
4	18	9	7	15	600	10.46	89		303	297	50.50	49.50
5	10	9	1	13	600	10.46	90		340	260	56.67	43.33
7	19	9	1	15	600	10.46	91		273	327	45.50	54.50
8	23	9	1	17	599	10.45	92		196	403	32.72	67.28
9	7	9	2	17	599	10.45	93		191	408	31.89	68.11
8	15	9	7	17	598	10.43	94		242	356	40.47	59.53
5	16	9	7	15	597	10.41	95		290	307	48.58	51.42
8	23	9	1	15	597	10.41	96		264	333	44.22	55.78
8	30	9	1	16	597	10.41	97		246	351	41.21	58.79
9	4	9	6	17	597	10.41	98		311	286	52.09	47.91
9	27	9	1	14	595	10.38	99		287	308	48.24	51.76
5	16	9	7	14	593	10.34	100		270	323	45.53	54.47
8	2	9	1	15	593	10.34	101	5734	264	329	44.52	55.48
8	23	9	1	18	593	10.34	102		193	400	32.55	67.45
5	23	9	7	13	592	10.32	103		361	231	60.98	39.02
5	24	9	1	16	592	10.32	104		210	382	35.47	64.53
8	30	9	1	15	592	10.32	105		291	301	49.16	50.84
9	7	9	2	16	592	10.32	106		214	378	36.15	63.85
5	30	9	7	13	591	10.31	107		298	293	50.42	49.58
7	9	9	5	18	591	10.31	108		272	319	46.02	53.98
9	12	9	7	16	591	10.31	109		275	316	46.53	53.47
5	23	9	7	16	590	10.29	110		227	363	38.47	61.53
8	9	9	1	15	590	10.29	111		234	356	39.66	60.34
9	13	9	1	14	590	10.29	112		282	308	47.80	52.20
4	18	9	7	17	589	10.27	113		180	409	30.56	69.44
5	28	9	5	17	589	10.27	114		267	322	45.33	54.67
5	31	9	1	15	589	10.27	115		228	361	38.71	61.29
4	4	9	7	16	588	10.25	116		250	338	42.52	57.48
4	5	9	1	13	588	10.25	117		350	238	59.52	40.48
9	4	9	6	18	588	10.25	118		313	275	53.23	46.77
10	24	9	7	16	588	10.25	119		252	336	42.86	57.14
9	20	9	1	18	587	10.24	120		183	404	31.18	68.82
10	2	9	6	17	587	10.24	121	5734	309	278	52.64	47.36

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	5	9	1	13	586	10.22	122		279	307	47.61	52.39
8	6	9	5	18	586	10.22	123		289	297	49.32	50.68
7	17	9	6	17	585	10.20	124		302	283	51.62	48.38
7	19	9	1	18	585	10.20	125		189	396	32.31	67.69
7	24	9	6	18	585	10.20	126		289	296	49.40	50.60
7	3	9	6	13	584	10.18	127		273	311	46.75	53.25
8	22	9	7	16	584	10.18	128		302	282	51.71	48.29
8	23	9	1	12	584	10.18	129		310	274	53.08	46.92
6	18	9	5	17	583	10.17	130		265	318	45.45	54.55
7	19	9	1	17	583	10.17	131		207	376	35.51	64.49
9	25	9	6	18	583	10.17	132		274	309	47.00	53.00
10	24	9	7	17	583	10.17	133		208	375	35.68	64.32
5	9	9	7	17	582	10.15	134		211	371	36.25	63.75
9	12	9	7	15	582	10.15	135		290	292	49.83	50.17
10	9	9	6	18	582	10.15	136		264	318	45.36	54.64
7	3	9	6	12	581	10.13	137		299	282	51.46	48.54
8	9	9	1	18	580	10.12	138		187	393	32.24	67.76
9	11	9	6	18	580	10.12	139		269	311	46.38	53.62
5	24	9	1	12	579	10.10	140		349	230	60.28	39.72
5	29	9	6	18	579	10.10	141	5734	318	261	54.92	45.08
5	31	9	1	16	579	10.10	142		246	333	42.49	57.51
7	11	9	7	13	579	10.10	143		333	246	57.51	42.49
7	19	9	1	13	579	10.10	144		271	308	46.80	53.20
8	22	9	7	17	579	10.10	145		245	334	42.31	57.69
9	4	9	6	16	579	10.10	146		306	273	52.85	47.15
9	12	9	7	14	579	10.10	147		301	278	51.99	48.01
4	19	9	1	12	578	10.08	148		375	203	64.88	35.12
5	16	9	7	13	578	10.08	149		315	263	54.50	45.50
7	3	9	6	16	578	10.08	150		238	340	41.18	58.82
6	7	9	1	16	577	10.06	151		197	380	34.14	65.86
6	14	9	1	15	577	10.06	152		236	341	40.90	59.10
8	30	9	1	13	577	10.06	153		277	300	48.01	51.99
9	20	9	1	17	577	10.06	154		186	391	32.24	67.76
5	30	9	7	14	576	10.05	155		286	290	49.65	50.35
10	18	9	1	16	576	10.05	156		230	346	39.93	60.07
7	2	9	5	17	575	10.03	157		266	309	46.26	53.74
5	9	9	7	18	574	10.01	158		209	365	36.41	63.59
5	23	9	7	15	574	10.01	159		314	260	54.70	45.30
7	10	9	6	18	574	10.01	160		266	308	46.34	53.66
8	9	9	1	14	574	10.01	161	5734	295	279	51.39	48.61
8	15	9	7	12	574	10.01	162		354	220	61.67	38.33
9	7	9	2	14	574	10.01	163		250	324	43.55	56.45
9	20	9	1	14	574	10.01	164		273	301	47.56	52.44
9	20	9	1	16	574	10.01	165		215	359	37.46	62.54
9	27	9	1	17	574	10.01	166		186	388	32.40	67.60
10	24	9	7	14	574	10.01	167		311	263	54.18	45.82
7	11	9	7	14	573	9.99	168		282	291	49.21	50.79
8	30	9	1	14	573	9.99	169		254	319	44.33	55.67
9	13	9	1	16	573	9.99	170		227	346	39.62	60.38
7	9	9	5	17	572	9.98	171		248	324	43.36	56.64
7	26	9	1	16	572	9.98	172		237	335	41.43	58.57
8	15	9	7	13	572	9.98	173		318	254	55.59	44.41

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
9	17	9	5	18	571	9.96	174		265	306	46.41	53.59
9	24	9	5	17	571	9.96	175		273	298	47.81	52.19
10	23	9	6	17	571	9.96	176		306	265	53.59	46.41
8	22	9	7	15	569	9.92	177		289	280	50.79	49.21
10	16	9	6	16	568	9.91	178		298	270	52.46	47.54
4	5	9	1	18	567	9.89	179		182	385	32.10	67.90
7	16	9	5	17	567	9.89	180		273	294	48.15	51.85
7	26	9	1	15	567	9.89	181	5734	261	306	46.03	53.97
8	21	9	6	16	567	9.89	182		263	304	46.38	53.62
5	16	9	7	12	566	9.87	183		305	261	53.89	46.11
8	2	9	1	14	566	9.87	184		257	309	45.41	54.59
5	9	9	7	12	565	9.85	185		314	251	55.58	44.42
5	22	9	6	18	564	9.84	186		305	259	54.08	45.92
8	2	9	1	16	564	9.84	187		235	329	41.67	58.33
8	8	9	7	12	564	9.84	188		306	258	54.26	45.74
8	30	9	1	17	564	9.84	189		194	370	34.40	65.60
5	9	9	7	15	563	9.82	190		257	306	45.65	54.35
9	27	9	1	16	563	9.82	191		214	349	38.01	61.99
10	16	9	6	17	563	9.82	192		309	254	54.88	45.12
5	31	9	1	14	562	9.80	193		272	290	48.40	51.60
6	14	9	1	14	561	9.78	194		245	316	43.67	56.33
8	29	9	7	14	561	9.78	195		315	246	56.15	43.85
8	8	9	7	17	560	9.77	196		225	335	40.18	59.82
5	21	9	5	17	559	9.75	197		265	294	47.41	52.59
8	23	9	1	13	559	9.75	198		236	323	42.22	57.78
9	26	9	7	15	559	9.75	199		296	263	52.95	47.05
10	24	9	7	13	559	9.75	200		281	278	50.27	49.73

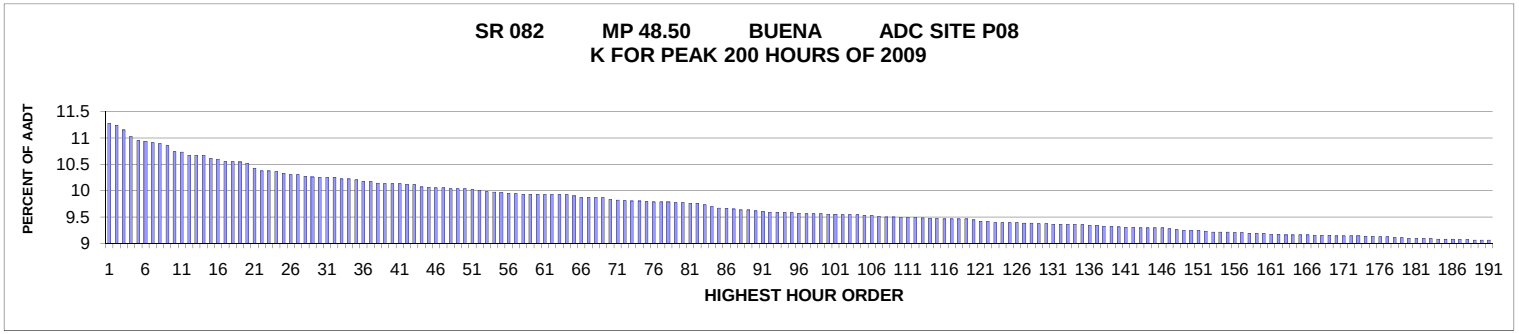

AADT= 24049 **K 30 FACTOR=** 10.25 **K 100 FACTOR=** 9.6 **K 200 FACTOR=** 9.06 **D FACTOR=** 53.41

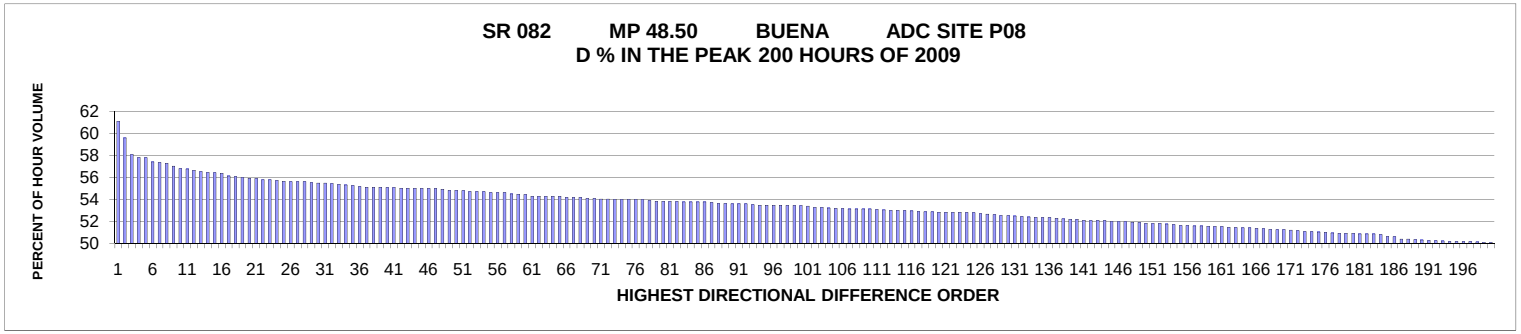

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
9	4	9	6	17	2712	11.28	1	24049	1325	1387	48.86	51.14
6	19	9	6	17	2702	11.24	2		1610	1092	59.59	40.41
9	4	9	6	16	2682	11.15	3		1368	1314	51.01	48.99
9	18	9	6	17	2651	11.02	4		1405	1246	53	47
5	22	9	6	17	2634	10.95	5		1333	1301	50.61	49.39
10	2	9	6	18	2632	10.94	6		1326	1306	50.38	49.62
11	25	9	4	17	2624	10.91	7		1524	1100	58.08	41.92
10	2	9	6	17	2620	10.89	8		1316	1304	50.23	49.77
9	4	9	6	18	2610	10.85	9		1297	1313	49.69	50.31
10	9	9	6	18	2582	10.74	10		1492	1090	57.78	42.22
9	25	9	6	18	2580	10.73	11		1413	1167	54.77	45.23
5	22	9	6	16	2565	10.67	12		1336	1229	52.09	47.91
6	19	9	6	18	2565	10.67	13		1403	1162	54.7	45.3
11	25	9	4	16	2565	10.67	14		1424	1141	55.52	44.48
10	16	9	6	17	2551	10.61	15		1442	1109	56.53	43.47
9	25	9	6	17	2550	10.6	16		1398	1152	54.82	45.18
11	25	9	4	15	2537	10.55	17		1318	1219	51.95	48.05

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	7	9	6	17	2536	10.55	18		1300	1236	51.26	48.74
8	14	9	6	18	2535	10.54	19		1359	1176	53.61	46.39
6	26	9	6	17	2530	10.52	20		1411	1119	55.77	44.23
8	14	9	6	17	2505	10.42	21	24049	1345	1160	53.69	46.31
7	10	9	6	16	2495	10.37	22		1246	1249	49.94	50.06
9	18	9	6	16	2494	10.37	23		1249	1245	50.08	49.92
4	24	9	6	18	2491	10.36	24		1356	1135	54.44	45.56
10	9	9	6	17	2484	10.33	25		1326	1158	53.38	46.62
5	8	9	6	18	2476	10.3	26		1377	1099	55.61	44.39
6	26	9	6	16	2476	10.3	27		1294	1182	52.26	47.74
5	22	9	6	18	2470	10.27	28		1181	1289	47.81	52.19
7	2	9	5	18	2467	10.26	29		1339	1128	54.28	45.72
5	15	9	6	17	2466	10.25	30		1266	1200	51.34	48.66
6	5	9	6	17	2464	10.25	31		1316	1148	53.41	46.59
10	9	9	6	16	2464	10.25	32		1302	1162	52.84	47.16
6	12	9	6	17	2458	10.22	33		1364	1094	55.49	44.51
10	2	9	6	16	2458	10.22	34		1287	1171	52.36	47.64
10	16	9	6	18	2454	10.2	35		1393	1061	56.76	43.24
8	7	9	6	18	2446	10.17	36		1255	1191	51.31	48.69
4	17	9	6	18	2445	10.17	37		1315	1130	53.78	46.22
6	12	9	6	16	2439	10.14	38		1283	1156	52.6	47.4
6	26	9	6	18	2437	10.13	39		1315	1122	53.96	46.04
8	14	9	6	16	2437	10.13	40		1269	1168	52.07	47.93
5	8	9	6	17	2435	10.13	41	24049	1302	1133	53.47	46.53
7	10	9	6	18	2431	10.11	42		1259	1172	51.79	48.21
8	21	9	6	16	2431	10.11	43		1291	1140	53.11	46.89
2	13	9	6	17	2421	10.07	44		1355	1066	55.97	44.03
6	19	9	6	16	2420	10.06	45		1283	1137	53.02	46.98
4	3	9	6	18	2418	10.05	46		1364	1054	56.41	43.59
9	18	9	6	18	2416	10.05	47		1277	1139	52.86	47.14
5	1	9	6	17	2412	10.03	48		1273	1139	52.78	47.22
10	23	9	6	18	2412	10.03	49		1309	1103	54.27	45.73
8	28	9	6	18	2411	10.03	50		1281	1130	53.13	46.87
7	24	9	6	18	2410	10.02	51		1328	1082	55.1	44.9
7	2	9	5	16	2408	10.01	52		1300	1108	53.99	46.01
5	8	9	6	16	2399	9.98	53		1334	1065	55.61	44.39
5	22	9	6	15	2397	9.97	54		1290	1107	53.82	46.18
6	5	9	6	18	2396	9.96	55		1318	1078	55.01	44.99
7	24	9	6	17	2393	9.95	56		1282	1111	53.57	46.43
6	26	9	6	15	2390	9.94	57		1192	1198	49.87	50.13
5	15	9	6	18	2388	9.93	58		1253	1135	52.47	47.53
9	25	9	6	16	2388	9.93	59		1251	1137	52.39	47.61
10	23	9	6	17	2387	9.93	60		1276	1111	53.46	46.54
7	2	9	5	17	2386	9.92	61	24049	1290	1096	54.07	45.93
7	24	9	6	16	2386	9.92	62		1253	1133	52.51	47.49
5	29	9	6	18	2385	9.92	63		1260	1125	52.83	47.17
7	17	9	6	18	2385	9.92	64		1242	1143	52.08	47.92
7	10	9	6	17	2380	9.9	65		1296	1084	54.45	45.55
4	3	9	6	17	2374	9.87	66		1360	1014	57.29	42.71
8	14	9	6	15	2374	9.87	67		1142	1232	48.1	51.9
11	6	9	6	17	2373	9.87	68		1253	1120	52.8	47.2
8	7	9	6	16	2372	9.86	69		1157	1215	48.78	51.22

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
6	18	9	5	18	2364	9.83	70		1322	1042	55.92	44.08
4	24	9	6	17	2362	9.82	71		1249	1113	52.88	47.12
8	28	9	6	17	2359	9.81	72		1216	1143	51.55	48.45
8	21	9	6	17	2358	9.8	73		1307	1051	55.43	44.57
11	25	9	4	18	2358	9.8	74		1441	917	61.11	38.89
3	27	9	6	18	2354	9.79	75		1293	1061	54.93	45.07
7	9	9	5	18	2351	9.78	76		1246	1105	53	47
8	21	9	6	18	2351	9.78	77		1300	1051	55.3	44.7
9	4	9	6	15	2351	9.78	78		1182	1169	50.28	49.72
7	17	9	6	16	2349	9.77	79		1210	1139	51.51	48.49
7	31	9	6	18	2349	9.77	80		1285	1064	54.7	45.3
3	13	9	6	17	2347	9.76	81	24049	1316	1031	56.07	43.93
8	28	9	6	16	2347	9.76	82		1155	1192	49.21	50.79
4	17	9	6	17	2339	9.73	83		1254	1085	53.61	46.39
6	12	9	6	18	2331	9.69	84		1282	1049	55	45
8	7	9	6	15	2325	9.67	85		1101	1224	47.35	52.65
6	25	9	5	18	2324	9.66	86		1269	1055	54.6	45.4
11	6	9	6	16	2321	9.65	87		1272	1049	54.8	45.2
2	27	9	6	18	2317	9.63	88		1300	1017	56.11	43.89
6	25	9	5	17	2316	9.63	89		1262	1054	54.49	45.51
10	1	9	5	17	2310	9.61	90		1187	1123	51.39	48.61
2	20	9	6	17	2308	9.6	91		1187	1121	51.43	48.57
7	1	9	4	18	2307	9.59	92		1269	1038	55.01	44.99
7	17	9	6	17	2306	9.59	93		1174	1132	50.91	49.09
6	30	9	3	18	2305	9.58	94		1309	996	56.79	43.21
11	6	9	6	18	2304	9.58	95		1269	1035	55.08	44.92
4	24	9	6	16	2301	9.57	96		1171	1130	50.89	49.11
8	6	9	5	18	2300	9.56	97		1303	997	56.65	43.35
11	25	9	4	14	2299	9.56	98		1145	1154	49.8	50.2
8	6	9	5	17	2298	9.56	99		1222	1076	53.18	46.82
5	29	9	6	17	2297	9.55	100		1170	1127	50.94	49.06
5	15	9	6	16	2296	9.55	101	24049	1169	1127	50.91	49.09
10	15	9	5	18	2295	9.54	102		1253	1042	54.6	45.4
5	1	9	6	18	2294	9.54	103		1227	1067	53.49	46.51
10	16	9	6	16	2294	9.54	104		1239	1055	54.01	45.99
2	27	9	6	17	2292	9.53	105		1260	1032	54.97	45.03
3	27	9	6	17	2292	9.53	106		1232	1060	53.75	46.25
6	19	9	6	15	2286	9.51	107		1222	1064	53.46	46.54
3	6	9	6	18	2284	9.5	108		1203	1081	52.67	47.33
5	1	9	6	16	2284	9.5	109		1195	1089	52.32	47.68
3	20	9	6	16	2283	9.49	110		1213	1070	53.13	46.87
10	30	9	6	17	2283	9.49	111		1206	1077	52.83	47.17
7	16	9	5	18	2282	9.49	112		1232	1050	53.99	46.01
3	20	9	6	17	2279	9.48	113		1259	1020	55.24	44.76
4	10	9	6	17	2278	9.47	114		1273	1005	55.88	44.12
4	10	9	6	18	2277	9.47	115		1267	1010	55.64	44.36
3	12	9	5	17	2276	9.46	116		1298	978	57.03	42.97
7	23	9	5	18	2276	9.46	117		1229	1047	54	46
8	21	9	6	15	2276	9.46	118		1151	1125	50.57	49.43
10	23	9	6	16	2274	9.46	119		1210	1064	53.21	46.79
3	20	9	6	18	2270	9.44	120		1312	958	57.8	42.2
7	17	9	6	15	2265	9.42	121	24049	1156	1109	51.04	48.96

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
6	21	9	1	15	2263	9.41	122		1058	1205	46.75	53.25
5	21	9	5	18	2259	9.39	123		1245	1014	55.11	44.89
7	10	9	6	15	2259	9.39	124		1135	1124	50.24	49.76
7	8	9	4	18	2257	9.39	125		1216	1041	53.88	46.12
7	24	9	6	15	2257	9.39	126		1168	1089	51.75	48.25
2	13	9	6	18	2256	9.38	127		1213	1043	53.77	46.23
8	13	9	5	17	2256	9.38	128		1213	1043	53.77	46.23
7	31	9	6	17	2254	9.37	129		1165	1089	51.69	48.31
6	18	9	5	17	2253	9.37	130		1190	1063	52.82	47.18
6	5	9	6	16	2252	9.36	131		1153	1099	51.2	48.8
3	13	9	6	18	2251	9.36	132		1269	982	56.37	43.63
7	1	9	4	17	2251	9.36	133		1222	1029	54.29	45.71
10	30	9	6	18	2251	9.36	134		1216	1035	54.02	45.98
6	11	9	5	17	2249	9.35	135		1171	1078	52.07	47.93
6	28	9	1	14	2247	9.34	136		1030	1217	45.84	54.16
3	6	9	6	17	2245	9.34	137		1196	1049	53.27	46.73
6	19	9	6	14	2241	9.32	138		1139	1102	50.83	49.17
10	1	9	5	16	2241	9.32	139		1170	1071	52.21	47.79
7	6	9	2	18	2238	9.31	140		1146	1092	51.21	48.79
7	31	9	6	15	2237	9.3	141	24049	1074	1163	48.01	51.99
10	8	9	5	17	2236	9.3	142		1262	974	56.44	43.56
9	3	9	5	17	2235	9.29	143		1109	1126	49.62	50.38
2	20	9	6	18	2234	9.29	144		1148	1086	51.39	48.61
10	1	9	5	18	2234	9.29	145		1157	1077	51.79	48.21
10	8	9	5	18	2234	9.29	146		1220	1014	54.61	45.39
9	10	9	5	17	2230	9.27	147		1118	1112	50.13	49.87
7	9	9	5	17	2227	9.26	148		1149	1078	51.59	48.41
6	11	9	5	18	2223	9.24	149		1222	1001	54.97	45.03
10	2	9	6	15	2222	9.24	150		1077	1145	48.47	51.53
9	3	9	5	18	2221	9.24	151		1187	1034	53.44	46.56
11	13	9	6	17	2219	9.23	152		1165	1054	52.5	47.5
7	7	9	3	18	2216	9.21	153		1151	1065	51.94	48.06
9	24	9	5	17	2215	9.21	154		1170	1045	52.82	47.18
11	20	9	6	18	2215	9.21	155		1229	986	55.49	44.51
12	11	9	6	17	2213	9.2	156		1190	1023	53.77	46.23
4	17	9	6	16	2212	9.2	157		1171	1041	52.94	47.06
8	23	9	1	16	2211	9.19	158		1140	1071	51.56	48.44
6	4	9	5	18	2209	9.19	159		1158	1051	52.42	47.58
9	24	9	5	18	2209	9.19	160		1208	1001	54.69	45.31
9	8	9	3	18	2206	9.17	161	24049	1230	976	55.76	44.24
5	29	9	6	16	2205	9.17	162		1068	1137	48.44	51.56
9	25	9	6	15	2204	9.16	163		1099	1105	49.86	50.14
1	23	9	6	17	2203	9.16	164		1213	990	55.06	44.94
2	27	9	6	16	2202	9.16	165		1069	1133	48.55	51.45
9	17	9	5	17	2202	9.16	166		1180	1022	53.59	46.41
8	14	9	6	14	2201	9.15	167		1103	1098	50.11	49.89
8	26	9	4	18	2201	9.15	168		1190	1011	54.07	45.93
9	30	9	4	18	2201	9.15	169		1214	987	55.16	44.84
7	31	9	6	16	2199	9.14	170		1135	1064	51.61	48.39
9	9	9	4	18	2198	9.14	171		1217	981	55.37	44.63
2	20	9	6	16	2197	9.14	172		1080	1117	49.16	50.84
6	28	9	1	15	2197	9.14	173		1007	1190	45.84	54.16

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
4	10	9	6	16	2196	9.13	174		1149	1047	52.32	47.68
5	22	9	6	14	2196	9.13	175		1174	1022	53.46	46.54
8	13	9	5	18	2194	9.12	176		1191	1003	54.28	45.72
9	17	9	5	16	2194	9.12	177		1145	1049	52.19	47.81
7	23	9	5	17	2190	9.11	178		1162	1028	53.06	46.94
6	26	9	6	14	2188	9.1	179		1117	1071	51.05	48.95
9	4	9	6	19	2187	9.09	180		1177	1010	53.82	46.18
3	27	9	6	16	2186	9.09	181	24049	1162	1024	53.16	46.84
6	12	9	6	15	2185	9.09	182		1114	1071	50.98	49.02
8	11	9	3	18	2185	9.09	183		1254	931	57.39	42.61
9	28	9	2	17	2184	9.08	184		1134	1050	51.92	48.08
12	4	9	6	17	2184	9.08	185		1157	1027	52.98	47.02
12	23	9	4	17	2183	9.08	186		1252	931	57.35	42.65
7	6	9	2	16	2182	9.07	187		1130	1052	51.79	48.21
8	27	9	5	18	2181	9.07	188		1215	966	55.71	44.29
8	6	9	5	16	2180	9.06	189		1108	1072	50.83	49.17
8	17	9	2	18	2180	9.06	190		1181	999	54.17	45.83
10	30	9	6	16	2180	9.06	191		1165	1015	53.44	46.56
8	23	9	1	14	2179	9.06	192		1054	1125	48.37	51.63
8	12	9	4	18	2178	9.06	193		1201	977	55.14	44.86
4	26	9	1	16	2175	9.04	194		1084	1091	49.84	50.16
5	28	9	5	16	2175	9.04	195		1015	1160	46.67	53.33
7	6	9	2	17	2173	9.04	196		1152	1021	53.01	46.99
7	24	9	6	14	2172	9.03	197		1095	1077	50.41	49.59
10	15	9	5	17	2172	9.03	198		1187	985	54.65	45.35
10	22	9	5	18	2171	9.03	199		1161	1010	53.48	46.52
6	25	9	5	16	2170	9.02	200		1110	1060	51.15	48.85

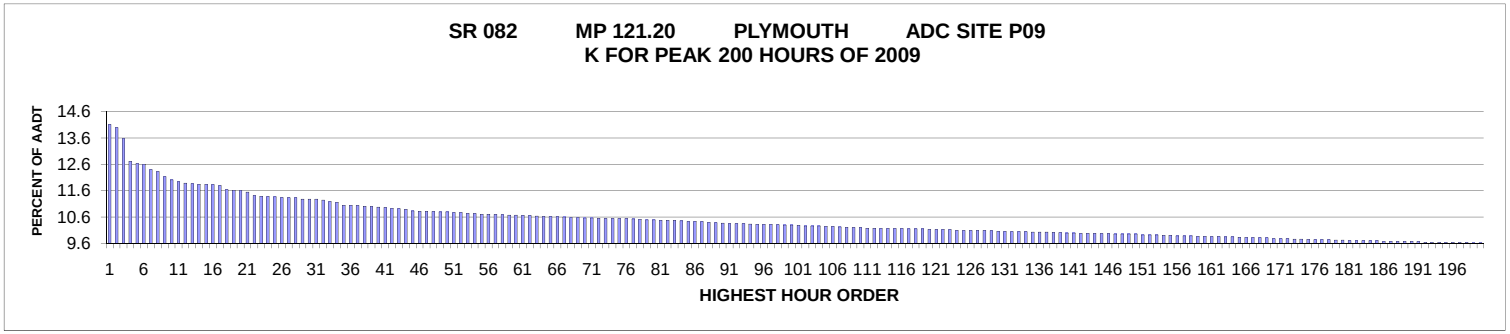

AADT= 15982 **K 30 FACTOR=** 11.28 **K 100 FACTOR=** 10.29 **K 200 FACTOR=** 9.61 **D FACTOR=** 51.96

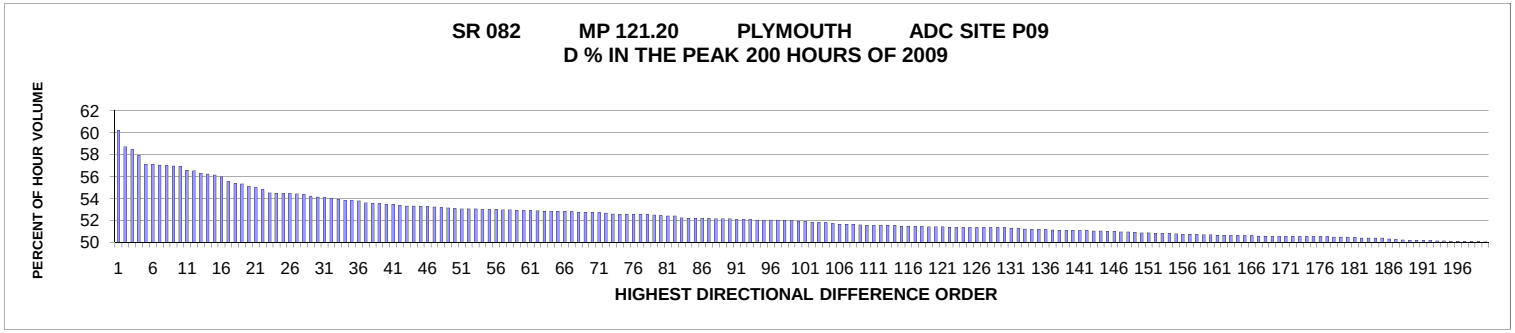

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
11	29	9	1	15	2255	14.11	1	15982	1046	1209	46.39	53.61
11	29	9	1	16	2234	13.98	2		962	1272	43.06	56.94
11	29	9	1	14	2169	13.57	3		999	1170	46.06	53.94
11	29	9	1	13	2032	12.71	4		986	1046	48.52	51.48
11	25	9	4	16	2019	12.63	5		996	1023	49.33	50.67
7	5	9	1	15	2013	12.6	6		1057	956	52.51	47.49
7	5	9	1	17	1980	12.39	7		982	998	49.6	50.4
9	7	9	2	16	1969	12.32	8		944	1025	47.94	52.06
7	5	9	1	16	1939	12.13	9		991	948	51.11	48.89
8	16	9	1	17	1918	12	10		991	927	51.67	48.33
11	25	9	4	17	1906	11.93	11		912	994	47.85	52.15
8	9	9	1	17	1899	11.88	12		945	954	49.76	50.24
8	16	9	1	16	1895	11.86	13		937	958	49.45	50.55
8	9	9	1	15	1893	11.84	14		861	1032	45.48	54.52
9	4	9	6	16	1892	11.84	15		943	949	49.84	50.16
9	7	9	2	15	1889	11.82	16		928	961	49.13	50.87
8	9	9	1	14	1883	11.78	17		971	912	51.57	48.43

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	9	9	1	16	1859	11.63	18		865	994	46.53	53.47
8	14	9	6	17	1855	11.61	19		924	931	49.81	50.19
11	29	9	1	17	1854	11.6	20		797	1057	42.99	57.01
9	4	9	6	17	1845	11.54	21	15982	900	945	48.78	51.22
8	16	9	1	15	1823	11.41	22		852	971	46.74	53.26
8	23	9	1	15	1821	11.39	23		853	968	46.84	53.16
11	25	9	4	18	1817	11.37	24		905	912	49.81	50.19
7	2	9	5	17	1815	11.36	25		861	954	47.44	52.56
9	7	9	2	14	1813	11.34	26		899	914	49.59	50.41
11	25	9	4	14	1810	11.33	27		943	867	52.1	47.9
6	26	9	6	17	1809	11.32	28		864	945	47.76	52.24
5	22	9	6	17	1802	11.28	29		894	908	49.61	50.39
7	5	9	1	14	1802	11.28	30		960	842	53.27	46.73
11	25	9	4	15	1801	11.27	31		951	850	52.8	47.2
8	7	9	6	16	1796	11.24	32		917	879	51.06	48.94
8	7	9	6	17	1787	11.18	33		884	903	49.47	50.53
9	7	9	2	17	1782	11.15	34		796	986	44.67	55.33
7	3	9	6	13	1764	11.04	35		825	939	46.77	53.23
8	16	9	1	14	1764	11.04	36		858	906	48.64	51.36
6	28	9	1	15	1763	11.03	37		871	892	49.4	50.6
8	6	9	5	18	1759	11.01	38		801	958	45.54	54.46
11	25	9	4	13	1757	10.99	39		973	784	55.38	44.62
4	5	9	1	16	1753	10.97	40		792	961	45.18	54.82
8	9	9	1	13	1752	10.96	41	15982	874	878	49.89	50.11
7	10	9	6	17	1746	10.92	42		891	855	51.03	48.97
9	4	9	6	18	1743	10.91	43		903	840	51.81	48.19
8	9	9	1	18	1741	10.89	44		832	909	47.79	52.21
8	23	9	1	14	1729	10.82	45		794	935	45.92	54.08
6	19	9	6	16	1728	10.81	46		873	855	50.52	49.48
8	21	9	6	17	1727	10.81	47		855	872	49.51	50.49
5	22	9	6	18	1726	10.8	48		819	907	47.45	52.55
7	17	9	6	15	1725	10.79	49		920	805	53.33	46.67
9	4	9	6	15	1724	10.79	50		846	878	49.07	50.93
8	13	9	5	17	1722	10.77	51		824	898	47.85	52.15
8	23	9	1	16	1720	10.76	52		807	913	46.92	53.08
4	5	9	1	17	1716	10.74	53		820	896	47.79	52.21
7	24	9	6	16	1715	10.73	54		867	848	50.55	49.45
7	2	9	5	16	1712	10.71	55		837	875	48.89	51.11
6	19	9	6	17	1711	10.71	56		853	858	49.85	50.15
11	29	9	1	12	1709	10.69	57		853	856	49.91	50.09
7	26	9	1	16	1707	10.68	58		831	876	48.68	51.32
7	19	9	1	15	1706	10.67	59		860	846	50.41	49.59
5	25	9	2	16	1705	10.67	60		782	923	45.87	54.13
5	22	9	6	16	1703	10.66	61	15982	863	840	50.68	49.32
7	3	9	6	14	1703	10.66	62		817	886	47.97	52.03
3	27	9	6	17	1699	10.63	63		971	728	57.15	42.85
8	14	9	6	15	1697	10.62	64		879	818	51.8	48.2
5	25	9	2	15	1696	10.61	65		794	902	46.82	53.18
7	17	9	6	17	1695	10.61	66		896	799	52.86	47.14
7	31	9	6	16	1693	10.59	67		830	863	49.03	50.97
7	12	9	1	17	1690	10.57	68		725	965	42.9	57.1
4	3	9	6	17	1689	10.57	69		697	992	41.27	58.73

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	19	9	1	16	1688	10.56	70		743	945	44.02	55.98
8	14	9	6	16	1687	10.56	71		830	857	49.2	50.8
7	17	9	6	16	1686	10.55	72		871	815	51.66	48.34
7	2	9	5	18	1685	10.54	73		833	852	49.44	50.56
7	17	9	6	14	1685	10.54	74		893	792	53	47
7	26	9	1	15	1683	10.53	75		807	876	47.95	52.05
8	16	9	1	13	1683	10.53	76		799	884	47.47	52.53
8	7	9	6	15	1682	10.52	77		865	817	51.43	48.57
7	31	9	6	17	1679	10.51	78		874	805	52.05	47.95
5	25	9	2	17	1677	10.49	79		728	949	43.41	56.59
8	7	9	6	18	1675	10.48	80		842	833	50.27	49.73
6	21	9	1	16	1674	10.47	81	15982	813	861	48.57	51.43
7	10	9	6	16	1674	10.47	82		821	853	49.04	50.96
7	12	9	1	15	1673	10.47	83		835	838	49.91	50.09
7	5	9	1	13	1670	10.45	84		853	817	51.08	48.92
6	21	9	1	17	1665	10.42	85		763	902	45.83	54.17
7	24	9	6	14	1665	10.42	86		809	856	48.59	51.41
7	31	9	6	14	1665	10.42	87		840	825	50.45	49.55
8	14	9	6	14	1661	10.39	88		853	808	51.35	48.65
5	25	9	2	14	1657	10.37	89		809	848	48.82	51.18
8	2	9	1	17	1655	10.36	90		780	875	47.13	52.87
7	24	9	6	15	1653	10.34	91		885	768	53.54	46.46
8	21	9	6	15	1653	10.34	92		893	760	54.02	45.98
8	16	9	1	18	1652	10.34	93		941	711	56.96	43.04
7	2	9	5	15	1651	10.33	94		801	850	48.52	51.48
6	14	9	1	16	1650	10.32	95		743	907	45.03	54.97
7	24	9	6	17	1648	10.31	96		791	857	48	52
3	29	9	1	15	1647	10.31	97		870	777	52.82	47.18
8	2	9	1	14	1646	10.3	98		813	833	49.39	50.61
7	19	9	1	17	1645	10.29	99		760	885	46.2	53.8
8	30	9	1	15	1645	10.29	100		799	846	48.57	51.43
8	2	9	1	16	1643	10.28	101	15982	813	830	49.48	50.52
8	21	9	6	16	1640	10.26	102		799	841	48.72	51.28
7	31	9	6	18	1639	10.26	103		810	829	49.42	50.58
8	21	9	6	14	1638	10.25	104		863	775	52.69	47.31
7	5	9	1	18	1636	10.24	105		796	840	48.66	51.34
7	24	9	6	18	1636	10.24	106		792	844	48.41	51.59
6	19	9	6	18	1633	10.22	107		865	768	52.97	47.03
7	12	9	1	16	1632	10.21	108		781	851	47.86	52.14
3	29	9	1	16	1628	10.19	109		836	792	51.35	48.65
6	26	9	6	18	1628	10.19	110		773	855	47.48	52.52
8	2	9	1	15	1626	10.17	111		837	789	51.48	48.52
7	10	9	6	14	1625	10.17	112		854	771	52.55	47.45
7	17	9	6	18	1624	10.16	113		834	790	51.35	48.65
7	26	9	1	17	1624	10.16	114		800	824	49.26	50.74
6	19	9	6	15	1623	10.16	115		837	786	51.57	48.43
8	6	9	5	16	1623	10.16	116		710	913	43.75	56.25
8	6	9	5	17	1622	10.15	117		705	917	43.46	56.54
8	30	9	1	16	1622	10.15	118		825	797	50.86	49.14
7	3	9	6	15	1620	10.14	119		771	849	47.59	52.41
6	25	9	5	18	1618	10.12	120		707	911	43.7	56.3
12	23	9	4	16	1618	10.12	121	15982	752	866	46.48	53.52

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	28	9	6	17	1617	10.12	122		787	830	48.67	51.33
11	25	9	4	12	1617	10.12	123		879	738	54.36	45.64
6	28	9	1	17	1613	10.09	124		745	868	46.19	53.81
6	12	9	6	16	1612	10.09	125		779	833	48.33	51.67
8	30	9	1	14	1612	10.09	126		787	825	48.82	51.18
11	28	9	7	14	1612	10.09	127		814	798	50.5	49.5
7	10	9	6	15	1611	10.08	128		780	831	48.42	51.58
8	7	9	6	13	1610	10.07	129		788	822	48.94	51.06
8	14	9	6	18	1606	10.05	130		828	778	51.56	48.44
8	23	9	1	17	1606	10.05	131		755	851	47.01	52.99
7	3	9	6	16	1605	10.04	132		759	846	47.29	52.71
8	14	9	6	13	1604	10.04	133		811	793	50.56	49.44
7	31	9	6	15	1603	10.03	134		762	841	47.54	52.46
7	12	9	1	14	1602	10.02	135		790	812	49.31	50.69
7	26	9	1	14	1602	10.02	136		799	803	49.88	50.12
8	7	9	6	14	1602	10.02	137		855	747	53.37	46.63
9	7	9	2	13	1600	10.01	138		789	811	49.31	50.69
6	26	9	6	16	1598	10	139		752	846	47.06	52.94
6	28	9	1	16	1597	9.99	140		763	834	47.78	52.22
6	26	9	6	15	1596	9.99	141	15982	815	781	51.07	48.93
6	21	9	1	15	1594	9.97	142		774	820	48.56	51.44
8	30	9	1	17	1594	9.97	143		753	841	47.24	52.76
7	2	9	5	14	1593	9.97	144		763	830	47.9	52.1
7	3	9	6	12	1592	9.96	145		780	812	48.99	51.01
9	7	9	2	18	1592	9.96	146		698	894	43.84	56.16
8	21	9	6	18	1591	9.95	147		752	839	47.27	52.73
8	8	9	7	14	1590	9.95	148		766	824	48.18	51.82
8	13	9	5	16	1590	9.95	149		714	876	44.91	55.09
11	28	9	7	15	1590	9.95	150		785	805	49.37	50.63
5	22	9	6	14	1586	9.92	151		828	758	52.21	47.79
7	6	9	2	17	1586	9.92	152		722	864	45.52	54.48
7	19	9	1	14	1584	9.91	153		783	801	49.43	50.57
6	19	9	6	14	1582	9.9	154		812	770	51.33	48.67
8	13	9	5	18	1582	9.9	155		721	861	45.58	54.42
7	2	9	5	13	1579	9.88	156		776	803	49.15	50.85
8	13	9	5	15	1579	9.88	157		737	842	46.68	53.32
8	14	9	6	12	1579	9.88	158		877	702	55.54	44.46
9	4	9	6	14	1577	9.87	159		777	800	49.27	50.73
7	6	9	2	15	1576	9.86	160		745	831	47.27	52.73
4	5	9	1	18	1574	9.85	161	15982	741	833	47.08	52.92
8	8	9	7	12	1574	9.85	162		749	825	47.59	52.41
5	8	9	6	17	1572	9.84	163		778	794	49.49	50.51
6	21	9	1	14	1572	9.84	164		774	798	49.24	50.76
8	10	9	2	15	1571	9.83	165		803	768	51.11	48.89
6	14	9	1	15	1570	9.82	166		758	812	48.28	51.72
12	27	9	1	15	1569	9.82	167		738	831	47.04	52.96
7	10	9	6	13	1568	9.81	168		831	737	53	47
8	2	9	1	13	1568	9.81	169		786	782	50.13	49.87
7	9	9	5	18	1562	9.77	170		727	835	46.54	53.46
8	10	9	2	17	1562	9.77	171		737	825	47.18	52.82
10	9	9	6	16	1561	9.77	172		779	782	49.9	50.1
9	27	9	1	16	1560	9.76	173		812	748	52.05	47.95

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
11	28	9	7	16	1560	9.76	174		759	801	48.65	51.35
9	11	9	6	17	1558	9.75	175		778	780	49.94	50.06
5	22	9	6	15	1555	9.73	176		809	746	52.03	47.97
7	6	9	2	16	1555	9.73	177		730	825	46.95	53.05
10	9	9	6	17	1555	9.73	178		808	747	51.96	48.04
9	4	9	6	13	1554	9.72	179		747	807	48.07	51.93
11	29	9	1	18	1553	9.72	180		618	935	39.79	60.21
7	23	9	5	17	1551	9.7	181	15982	728	823	46.94	53.06
6	12	9	6	17	1550	9.7	182		763	787	49.23	50.77
7	31	9	6	13	1549	9.69	183		727	822	46.93	53.07
8	28	9	6	18	1549	9.69	184		705	844	45.51	54.49
8	23	9	1	18	1548	9.69	185		715	833	46.19	53.81
7	24	9	6	13	1546	9.67	186		781	765	50.52	49.48
8	17	9	2	18	1546	9.67	187		642	904	41.53	58.47
9	18	9	6	16	1546	9.67	188		733	813	47.41	52.59
5	15	9	6	17	1545	9.67	189		763	782	49.39	50.61
8	17	9	2	15	1545	9.67	190		765	780	49.51	50.49
12	27	9	1	14	1544	9.66	191		759	785	49.16	50.84
3	29	9	1	17	1541	9.64	192		788	753	51.14	48.86
4	26	9	1	18	1541	9.64	193		662	879	42.96	57.04
6	26	9	6	14	1541	9.64	194		768	773	49.84	50.16
5	15	9	6	18	1540	9.64	195		725	815	47.08	52.92
8	21	9	6	13	1540	9.64	196		752	788	48.83	51.17
7	6	9	2	18	1539	9.63	197		648	891	42.11	57.89
8	15	9	7	15	1537	9.62	198		792	745	51.53	48.47
7	23	9	5	16	1536	9.61	199		724	812	47.14	52.86
7	31	9	6	12	1536	9.61	200		763	773	49.67	50.33

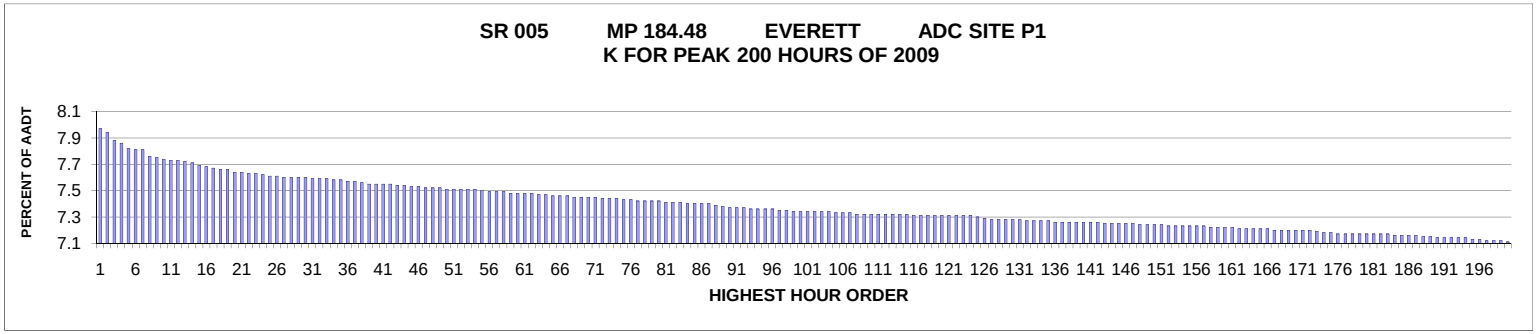

AADT= 181503 **K 30 FACTOR=** 7.6 **K 100 FACTOR=** 7.34 **K 200 FACTOR=** 7.11 **D FACTOR=** 52.4

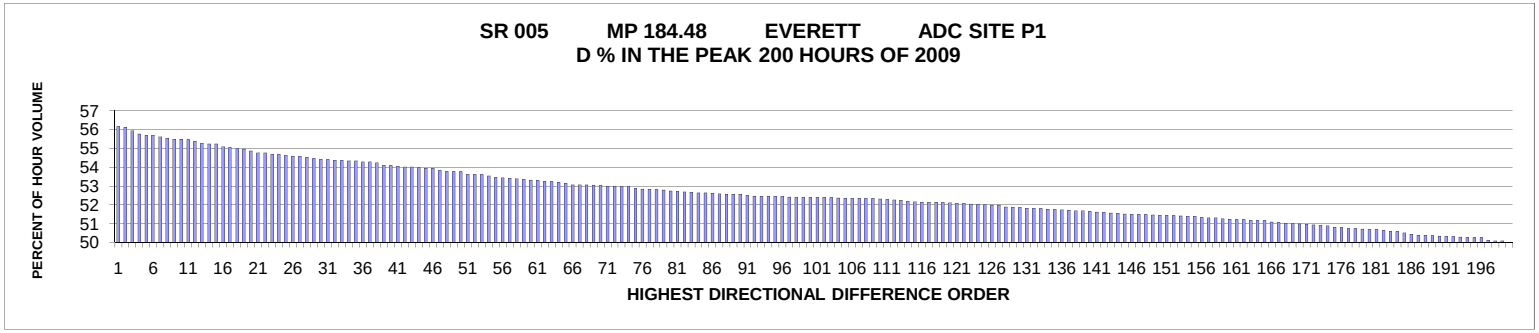

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
2	16	9	2	17	14464	7.97	1	181503	7458	7006	51.56	48.44
11	25	9	4	15	14407	7.94	2		7372	7035	51.17	48.83
3	27	9	6	16	14301	7.88	3		7667	6634	53.61	46.39
3	13	9	6	17	14270	7.86	4		7315	6955	51.26	48.74
2	13	9	6	16	14197	7.82	5		7462	6735	52.56	47.44
11	25	9	4	14	14176	7.81	6		7258	6918	51.2	48.8
3	27	9	6	15	14168	7.81	7		7462	6706	52.67	47.33
2	13	9	6	15	14081	7.76	8		7303	6778	51.86	48.14
1	30	9	6	16	14058	7.75	9		7604	6454	54.09	45.91
2	6	9	6	17	14055	7.74	10		7274	6781	51.75	48.25
2	13	9	6	17	14029	7.73	11		7163	6866	51.06	48.94
3	19	9	5	17	14024	7.73	12		7196	6828	51.31	48.69
3	13	9	6	16	14013	7.72	13		7399	6614	52.8	47.2
2	20	9	6	17	14002	7.71	14		7359	6643	52.56	47.44
2	6	9	6	16	13954	7.69	15		7546	6408	54.08	45.92
11	6	9	6	16	13937	7.68	16		7296	6641	52.35	47.65
2	20	9	6	16	13929	7.67	17		7248	6681	52.04	47.96

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
10	9	9	6	17	13908	7.66	18		6853	7055	49.27	50.73
12	18	9	6	16	13907	7.66	19		7213	6694	51.87	48.13
11	20	9	6	17	13871	7.64	20		7138	6733	51.46	48.54
1	16	9	6	16	13866	7.64	21	181503	7411	6455	53.45	46.55
3	20	9	6	17	13854	7.63	22		7304	6550	52.72	47.28
1	30	9	6	17	13846	7.63	23		7279	6567	52.57	47.43
11	13	9	6	16	13835	7.62	24		7337	6498	53.03	46.97
12	4	9	6	17	13821	7.61	25		6858	6963	49.62	50.38
3	18	9	4	17	13804	7.61	26		7343	6461	53.19	46.81
10	9	9	6	16	13801	7.6	27		7128	6673	51.65	48.35
1	28	9	4	17	13800	7.6	28		7524	6276	54.52	45.48
1	23	9	6	17	13799	7.6	29		7102	6697	51.47	48.53
12	18	9	6	15	13788	7.6	30		7205	6583	52.26	47.74
12	23	9	4	15	13783	7.59	31		7183	6600	52.11	47.89
10	30	9	6	16	13776	7.59	32		7297	6479	52.97	47.03
10	9	9	6	18	13768	7.59	33		7042	6726	51.15	48.85
11	20	9	6	16	13762	7.58	34		7131	6631	51.82	48.18
3	20	9	6	18	13756	7.58	35		6786	6970	49.33	50.67
11	11	9	4	17	13744	7.57	36		7207	6537	52.44	47.56
3	18	9	4	16	13733	7.57	37		7522	6211	54.77	45.23
12	18	9	6	17	13730	7.56	38		7143	6587	52.02	47.98
12	22	9	3	16	13712	7.55	39		7230	6482	52.73	47.27
3	13	9	6	15	13703	7.55	40		7209	6494	52.61	47.39
12	11	9	6	17	13703	7.55	41	181503	7032	6671	51.32	48.68
3	17	9	3	16	13697	7.55	42		7489	6208	54.68	45.32
1	19	9	2	17	13688	7.54	43		7179	6509	52.45	47.55
10	28	9	4	17	13686	7.54	44		7049	6637	51.51	48.49
3	19	9	5	18	13672	7.53	45		7070	6602	51.71	48.29
3	19	9	5	16	13665	7.53	46		7125	6540	52.14	47.86
12	22	9	3	17	13655	7.52	47		7086	6569	51.89	48.11
3	13	9	6	18	13645	7.52	48		6932	6713	50.8	49.2
2	5	9	5	17	13640	7.52	49		7211	6429	52.87	47.13
10	20	9	3	17	13638	7.51	50		7012	6626	51.42	48.58
2	19	9	5	17	13630	7.51	51		7201	6429	52.83	47.17
3	17	9	3	17	13628	7.51	52		7231	6397	53.06	46.94
10	12	9	2	17	13626	7.51	53		7149	6477	52.47	47.53
2	17	9	3	17	13623	7.51	54		7227	6396	53.05	46.95
2	19	9	5	16	13612	7.5	55		7443	6169	54.68	45.32
3	11	9	4	17	13600	7.49	56		7117	6483	52.33	47.67
10	9	9	6	15	13591	7.49	57		6933	6658	51.01	48.99
3	27	9	6	17	13586	7.49	58		6912	6674	50.88	49.12
11	6	9	6	17	13578	7.48	59		6922	6656	50.98	49.02
1	16	9	6	17	13576	7.48	60		6946	6630	51.16	48.84
2	20	9	6	18	13575	7.48	61	181503	6964	6611	51.3	48.7
3	30	9	2	17	13569	7.48	62		7275	6294	53.61	46.39
10	22	9	5	17	13562	7.47	63		7050	6512	51.98	48.02
10	29	9	5	17	13560	7.47	64		6745	6815	49.74	50.26
10	23	9	6	16	13549	7.46	65		7069	6480	52.17	47.83
12	4	9	6	16	13547	7.46	66		6843	6704	50.51	49.49
11	3	9	3	17	13537	7.46	67		6959	6578	51.41	48.59
12	23	9	4	16	13523	7.45	68		7186	6337	53.14	46.86
3	24	9	3	16	13520	7.45	69		7431	6089	54.96	45.04

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
1	23	9	6	16	13518	7.45	70		7172	6346	53.06	46.94
3	4	9	4	17	13513	7.45	71		6945	6568	51.39	48.61
1	28	9	4	16	13507	7.44	72		7580	5927	56.12	43.88
1	14	9	4	17	13502	7.44	73		7106	6396	52.63	47.37
10	30	9	6	17	13502	7.44	74		7135	6367	52.84	47.16
2	25	9	4	17	13488	7.43	75		7081	6407	52.5	47.5
11	24	9	3	17	13479	7.43	76		6783	6696	50.32	49.68
12	17	9	5	16	13472	7.42	77		7051	6421	52.34	47.66
1	29	9	5	17	13463	7.42	78		7054	6409	52.4	47.6
12	11	9	6	16	13461	7.42	79		7191	6270	53.42	46.58
3	20	9	6	15	13460	7.42	80		6964	6496	51.74	48.26
3	18	9	4	18	13446	7.41	81	181503	6965	6481	51.8	48.2
10	15	9	5	16	13446	7.41	82		7122	6324	52.97	47.03
12	30	9	4	17	13441	7.41	83		7319	6122	54.45	45.55
1	16	9	6	15	13437	7.4	84		7333	6104	54.57	45.43
1	30	9	6	15	13431	7.4	85		7165	6266	53.35	46.65
12	1	9	3	17	13431	7.4	86		6930	6501	51.6	48.4
11	6	9	6	15	13424	7.4	87		7114	6310	52.99	47.01
11	13	9	6	15	13411	7.39	88		7078	6333	52.78	47.22
10	15	9	5	17	13392	7.38	89		6734	6658	50.28	49.72
2	17	9	3	16	13384	7.37	90		7344	6040	54.87	45.13
12	11	9	6	18	13382	7.37	91		6775	6607	50.63	49.37
3	30	9	2	16	13376	7.37	92		7511	5865	56.15	43.85
2	5	9	5	16	13365	7.36	93		7383	5982	55.24	44.76
12	11	9	6	15	13355	7.36	94		6920	6435	51.82	48.18
11	11	9	4	16	13351	7.36	95		7216	6135	54.05	45.95
2	20	9	6	15	13350	7.36	96		7109	6241	53.25	46.75
10	30	9	6	15	13349	7.35	97		6961	6388	52.15	47.85
11	20	9	6	18	13340	7.35	98		6670	6670	50	50
12	29	9	3	17	13329	7.34	99		7276	6053	54.59	45.41
1	28	9	4	18	13324	7.34	100		7298	6026	54.77	45.23
11	2	9	2	17	13321	7.34	101	181503	6959	6362	52.24	47.76
3	25	9	4	16	13318	7.34	102		7324	5994	54.99	45.01
12	2	9	4	17	13318	7.34	103		6674	6644	50.11	49.89
10	22	9	5	16	13317	7.34	104		7192	6125	54.01	45.99
11	4	9	4	17	13306	7.33	105		6773	6533	50.9	49.1
2	16	9	2	16	13305	7.33	106		6978	6327	52.45	47.55
11	24	9	3	16	13299	7.33	107		6926	6373	52.08	47.92
11	4	9	4	18	13291	7.32	108		6741	6550	50.72	49.28
1	19	9	2	16	13285	7.32	109		6998	6287	52.68	47.32
12	17	9	5	17	13282	7.32	110		6699	6583	50.44	49.56
10	27	9	3	17	13281	7.32	111		7038	6243	52.99	47.01
10	23	9	6	15	13278	7.32	112		6782	6496	51.08	48.92
11	20	9	6	15	13278	7.32	113		6854	6424	51.62	48.38
1	23	9	6	18	13277	7.32	114		6873	6404	51.77	48.23
12	28	9	2	17	13277	7.32	115		7225	6052	54.42	45.58
3	2	9	2	17	13276	7.31	116		7093	6183	53.43	46.57
10	19	9	2	17	13275	7.31	117		7146	6129	53.83	46.17
10	12	9	2	16	13274	7.31	118		7251	6023	54.63	45.37
1	22	9	5	16	13273	7.31	119		7372	5901	55.54	44.46
12	28	9	2	16	13270	7.31	120		7334	5936	55.27	44.73
12	4	9	6	15	13266	7.31	121	181503	6684	6582	50.38	49.62

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
12	24	9	5	15	13265	7.31	122		7362	5903	55.5	44.5
10	13	9	3	17	13262	7.31	123		7155	6107	53.95	46.05
10	13	9	3	18	13259	7.31	124		6720	6539	50.68	49.32
3	3	9	3	17	13254	7.3	125		6944	6310	52.39	47.61
12	23	9	4	17	13237	7.29	126		7115	6122	53.75	46.25
10	15	9	5	18	13222	7.28	127		6690	6532	50.6	49.4
11	5	9	5	17	13222	7.28	128		6814	6408	51.54	48.46
10	28	9	4	16	13215	7.28	129		7175	6040	54.29	45.71
3	20	9	6	16	13210	7.28	130		7039	6171	53.29	46.71
10	10	9	7	17	13210	7.28	131		5884	7326	44.54	55.46
10	12	9	2	18	13201	7.27	132		6902	6299	52.28	47.72
10	24	9	7	17	13199	7.27	133		6696	6503	50.73	49.27
2	6	9	6	18	13195	7.27	134		6821	6374	51.69	48.31
3	24	9	3	17	13189	7.27	135		6911	6278	52.4	47.6
12	8	9	3	17	13186	7.26	136		6909	6277	52.4	47.6
1	22	9	5	17	13178	7.26	137		6902	6276	52.38	47.62
1	15	9	5	16	13176	7.26	138		7338	5838	55.69	44.31
10	14	9	4	17	13176	7.26	139		6849	6327	51.98	48.02
10	22	9	5	18	13175	7.26	140		6710	6465	50.93	49.07
12	3	9	5	16	13172	7.26	141	181503	6907	6265	52.44	47.56
12	9	9	4	17	13170	7.26	142		6539	6631	49.65	50.35
12	3	9	5	17	13163	7.25	143		6803	6360	51.68	48.32
12	30	9	4	16	13160	7.25	144		7318	5842	55.61	44.39
11	9	9	2	17	13154	7.25	145		7055	6099	53.63	46.37
12	24	9	5	14	13150	7.25	146		7334	5816	55.77	44.23
12	29	9	3	16	13150	7.25	147		7324	5826	55.7	44.3
2	25	9	4	16	13148	7.24	148		7297	5851	55.5	44.5
2	24	9	3	16	13147	7.24	149		7243	5904	55.09	44.91
10	16	9	6	17	13137	7.24	150		6603	6534	50.26	49.74
1	23	9	6	15	13132	7.24	151		7094	6038	54.02	45.98
1	14	9	4	16	13129	7.23	152		7136	5993	54.35	45.65
12	7	9	2	17	13125	7.23	153		6834	6291	52.07	47.93
12	10	9	5	17	13123	7.23	154		6825	6298	52.01	47.99
2	24	9	3	17	13120	7.23	155		6878	6242	52.42	47.58
3	4	9	4	16	13116	7.23	156		7245	5871	55.24	44.76
10	28	9	4	18	13114	7.23	157		6688	6426	51	49
11	10	9	3	17	13105	7.22	158		6657	6448	50.8	49.2
1	15	9	5	17	13101	7.22	159		6974	6127	53.23	46.77
3	10	9	3	17	13100	7.22	160		6863	6237	52.39	47.61
3	23	9	2	17	13098	7.22	161	181503	7042	6056	53.76	46.24
1	2	9	6	16	13090	7.21	162		7061	6029	53.94	46.06
12	10	9	5	18	13086	7.21	163		6554	6532	50.08	49.92
12	22	9	3	15	13085	7.21	164		6882	6203	52.59	47.41
10	10	9	7	15	13082	7.21	165		6346	6736	48.51	51.49
1	30	9	6	18	13079	7.21	166		6584	6495	50.34	49.66
11	11	9	4	18	13075	7.2	167		6817	6258	52.14	47.86
11	25	9	4	16	13072	7.2	168		6694	6378	51.21	48.79
10	20	9	3	18	13065	7.2	169		6727	6338	51.49	48.51
1	13	9	3	17	13063	7.2	170		6809	6254	52.12	47.88
12	18	9	6	18	13062	7.2	171		6497	6565	49.74	50.26
3	4	9	4	18	13060	7.2	172		6809	6251	52.14	47.86
11	3	9	3	16	13050	7.19	173		6924	6126	53.06	46.94

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
1	29	9	5	16	13037	7.18	174		7174	5863	55.03	44.97
3	19	9	5	15	13031	7.18	175		6642	6389	50.97	49.03
10	21	9	4	16	13018	7.17	176		6999	6019	53.76	46.24
12	30	9	4	15	13016	7.17	177		7058	5958	54.23	45.77
10	13	9	3	16	13012	7.17	178		6965	6047	53.53	46.47
2	13	9	6	14	13011	7.17	179		6812	6199	52.36	47.64
10	30	9	6	18	13011	7.17	180		6430	6581	49.42	50.58
3	11	9	4	18	13008	7.17	181	181503	6665	6343	51.24	48.76
12	16	9	4	17	13007	7.17	182		6805	6202	52.32	47.68
12	24	9	5	16	13006	7.17	183		7072	5934	54.37	45.63
10	10	9	7	14	13000	7.16	184		6318	6682	48.6	51.4
11	23	9	2	17	12997	7.16	185		6929	6068	53.31	46.69
1	2	9	6	15	12994	7.16	186		6800	6194	52.33	47.67
12	8	9	3	18	12987	7.16	187		6681	6306	51.44	48.56
12	3	9	5	18	12984	7.15	188		6531	6453	50.3	49.7
10	21	9	4	17	12977	7.15	189		6677	6300	51.45	48.55
1	9	9	6	15	12966	7.14	190		7046	5920	54.34	45.66
1	26	9	2	17	12966	7.14	191		7053	5913	54.4	45.6
2	6	9	6	15	12963	7.14	192		6920	6043	53.38	46.62
2	2	9	2	17	12952	7.14	193		6992	5960	53.98	46.02
10	10	9	7	16	12952	7.14	194		6134	6818	47.36	52.64
3	3	9	3	16	12949	7.13	195		7171	5778	55.38	44.62
10	26	9	2	17	12937	7.13	196		7022	5915	54.28	45.72
3	2	9	2	16	12931	7.12	197		7234	5697	55.94	44.06
12	4	9	6	18	12924	7.12	198		6450	6474	49.91	50.09
10	20	9	3	16	12920	7.12	199		7019	5901	54.33	45.67
1	16	9	6	18	12906	7.11	200		6756	6150	52.35	47.65

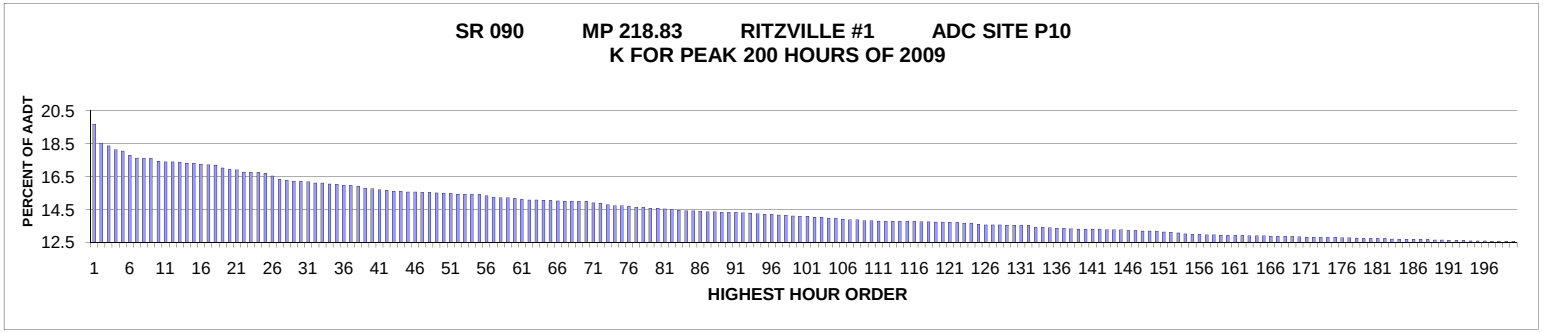

AADT= 10092 **K 30 FACTOR=** 16.22 **K 100 FACTOR=** 14.09 **K 200 FACTOR=** 12.57 **D FACTOR=** 55.49

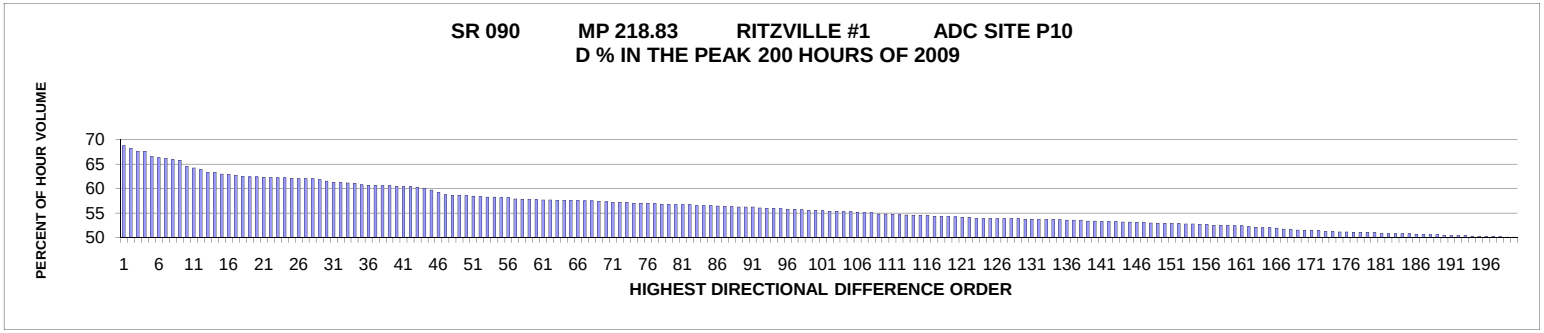

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
11	29	9	1	15	1988	19.7	1	10092	1052	936	52.92	47.08
11	29	9	1	14	1869	18.52	2		899	970	48.1	51.9
11	29	9	1	16	1854	18.37	3		1034	820	55.77	44.23
6	28	9	1	17	1830	18.13	4		661	1169	36.12	63.88
6	28	9	1	16	1823	18.06	5		693	1130	38.01	61.99
8	9	9	1	15	1797	17.81	6		847	950	47.13	52.87
6	28	9	1	18	1780	17.64	7		609	1171	34.21	65.79
6	26	9	6	15	1777	17.61	8		1073	704	60.38	39.62
6	28	9	1	15	1775	17.59	9		689	1086	38.82	61.18
7	5	9	1	15	1759	17.43	10		709	1050	40.31	59.69
8	9	9	1	16	1756	17.4	11		853	903	48.58	51.42
8	16	9	1	16	1755	17.39	12		867	888	49.4	50.6
8	9	9	1	14	1753	17.37	13		763	990	43.53	56.47
7	26	9	1	15	1747	17.31	14		768	979	43.96	56.04
8	16	9	1	15	1747	17.31	15		782	965	44.76	55.24
8	16	9	1	14	1742	17.26	16		735	1007	42.19	57.81
6	26	9	6	16	1738	17.22	17		1194	544	68.7	31.3

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	5	9	1	16	1736	17.2	18		736	1000	42.4	57.6
8	23	9	1	15	1718	17.02	19		760	958	44.24	55.76
8	16	9	1	17	1710	16.94	20		858	852	50.18	49.82
8	23	9	1	16	1707	16.91	21	10092	820	887	48.04	51.96
7	12	9	1	15	1693	16.78	22		707	986	41.76	58.24
11	25	9	4	16	1693	16.78	23		935	758	55.23	44.77
8	9	9	1	13	1691	16.76	24		732	959	43.29	56.71
11	25	9	4	17	1685	16.7	25		1045	640	62.02	37.98
11	29	9	1	13	1669	16.54	26		634	1035	37.99	62.01
11	25	9	4	18	1647	16.32	27		1037	610	62.96	37.04
11	25	9	4	15	1642	16.27	28		866	776	52.74	47.26
11	29	9	1	17	1638	16.23	29		1017	621	62.09	37.91
7	26	9	1	16	1637	16.22	30		773	864	47.22	52.78
7	26	9	1	14	1635	16.2	31		700	935	42.81	57.19
6	28	9	1	14	1626	16.11	32		610	1016	37.52	62.48
7	19	9	1	15	1626	16.11	33		700	926	43.05	56.95
7	5	9	1	14	1620	16.05	34		642	978	39.63	60.37
6	26	9	6	17	1618	16.03	35		1094	524	67.61	32.39
5	22	9	6	17	1611	15.96	36		788	823	48.91	51.09
8	2	9	1	15	1610	15.95	37		690	920	42.86	57.14
9	7	9	2	16	1606	15.91	38		760	846	47.32	52.68
8	23	9	1	17	1596	15.81	39		772	824	48.37	51.63
7	5	9	1	13	1592	15.77	40		543	1049	34.11	65.89
8	2	9	1	14	1584	15.7	41	10092	672	912	42.42	57.58
5	17	9	1	16	1581	15.67	42		901	680	56.99	43.01
8	23	9	1	14	1574	15.6	43		667	907	42.38	57.62
9	7	9	2	15	1574	15.6	44		722	852	45.87	54.13
7	12	9	1	16	1570	15.56	45		701	869	44.65	55.35
9	4	9	6	17	1570	15.56	46		803	767	51.15	48.85
8	9	9	1	12	1568	15.54	47		684	884	43.62	56.38
8	7	9	6	15	1567	15.53	48		767	800	48.95	51.05
5	22	9	6	15	1565	15.51	49		835	730	53.35	46.65
7	26	9	1	13	1564	15.5	50		666	898	42.58	57.42
8	2	9	1	16	1562	15.48	51		661	901	42.32	57.68
6	26	9	6	14	1558	15.44	52		872	686	55.97	44.03
8	9	9	1	17	1557	15.43	53		784	773	50.35	49.65
5	22	9	6	16	1555	15.41	54		823	732	52.93	47.07
9	7	9	2	14	1555	15.41	55		664	891	42.7	57.3
8	16	9	1	13	1547	15.33	56		670	877	43.31	56.69
7	19	9	1	16	1539	15.25	57		655	884	42.56	57.44
7	5	9	1	17	1536	15.22	58		702	834	45.7	54.3
7	19	9	1	14	1536	15.22	59		580	956	37.76	62.24
7	26	9	1	17	1530	15.16	60		718	812	46.93	53.07
8	30	9	1	16	1524	15.1	61	10092	697	827	45.73	54.27
7	12	9	1	14	1523	15.09	62		592	931	38.87	61.13
6	28	9	1	13	1522	15.08	63		590	932	38.76	61.24
8	7	9	6	16	1521	15.07	64		798	723	52.47	47.53
8	2	9	1	17	1519	15.05	65		676	843	44.5	55.5
8	14	9	6	16	1517	15.03	66		812	705	53.53	46.47
8	14	9	6	14	1515	15.01	67		763	752	50.36	49.64
8	14	9	6	15	1515	15.01	68		814	701	53.73	46.27
9	7	9	2	17	1515	15.01	69		725	790	47.85	52.15

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	7	9	6	14	1512	14.98	70		692	820	45.77	54.23
9	4	9	6	16	1505	14.91	71		761	744	50.56	49.44
8	16	9	1	18	1502	14.88	72		801	701	53.33	46.67
9	4	9	6	15	1493	14.79	73		751	742	50.3	49.7
6	26	9	6	18	1488	14.74	74		1006	482	67.61	32.39
9	7	9	2	13	1487	14.73	75		648	839	43.58	56.42
8	30	9	1	15	1486	14.72	76		627	859	42.19	57.81
7	19	9	1	13	1477	14.64	77		587	890	39.74	60.26
7	24	9	6	16	1477	14.64	78		781	696	52.88	47.12
7	31	9	6	15	1471	14.58	79		851	620	57.85	42.15
11	25	9	4	14	1470	14.57	80		688	782	46.8	53.2
6	14	9	1	15	1466	14.53	81	10092	667	799	45.5	54.5
7	6	9	2	14	1463	14.5	82		607	856	41.49	58.51
11	29	9	1	12	1460	14.47	83		494	966	33.84	66.16
5	25	9	2	15	1456	14.43	84		669	787	45.95	54.05
7	12	9	1	17	1456	14.43	85		674	782	46.29	53.71
7	3	9	6	12	1454	14.41	86		752	702	51.72	48.28
7	24	9	6	15	1450	14.37	87		780	670	53.79	46.21
8	23	9	1	18	1450	14.37	88		726	724	50.07	49.93
5	22	9	6	18	1445	14.32	89		653	792	45.19	54.81
6	14	9	1	16	1445	14.32	90		728	717	50.38	49.62
9	4	9	6	18	1445	14.32	91		727	718	50.31	49.69
8	16	9	1	12	1443	14.3	92		610	833	42.27	57.73
5	3	9	1	17	1442	14.29	93		516	926	35.78	64.22
7	19	9	1	17	1438	14.25	94		650	788	45.2	54.8
8	30	9	1	14	1434	14.21	95		617	817	43.03	56.97
5	25	9	2	16	1433	14.2	96		695	738	48.5	51.5
7	12	9	1	13	1430	14.17	97		563	867	39.37	60.63
5	25	9	2	14	1428	14.15	98		618	810	43.28	56.72
5	3	9	1	16	1424	14.11	99		477	947	33.5	66.5
7	2	9	5	17	1422	14.09	100		884	538	62.17	37.83
8	30	9	1	13	1422	14.09	101	10092	588	834	41.35	58.65
7	5	9	1	18	1416	14.03	102		641	775	45.27	54.73
7	10	9	6	15	1416	14.03	103		771	645	54.45	45.55
7	26	9	1	18	1408	13.95	104		781	627	55.47	44.53
8	14	9	6	17	1408	13.95	105		739	669	52.49	47.51
6	21	9	1	14	1404	13.91	106		594	810	42.31	57.69
6	21	9	1	16	1400	13.87	107		685	715	48.93	51.07
7	17	9	6	16	1400	13.87	108		744	656	53.14	46.86
7	24	9	6	14	1394	13.81	109		687	707	49.28	50.72
8	7	9	6	17	1394	13.81	110		760	634	54.52	45.48
7	17	9	6	14	1393	13.8	111		704	689	50.54	49.46
7	31	9	6	16	1392	13.79	112		783	609	56.25	43.75
7	17	9	6	15	1391	13.78	113		759	632	54.57	45.43
8	2	9	1	12	1391	13.78	114		575	816	41.34	58.66
8	9	9	1	18	1391	13.78	115		682	709	49.03	50.97
9	7	9	2	12	1391	13.78	116		635	756	45.65	54.35
6	21	9	1	15	1390	13.77	117		649	741	46.69	53.31
8	7	9	6	13	1389	13.76	118		613	776	44.13	55.87
7	31	9	6	14	1388	13.75	119		721	667	51.95	48.05
8	2	9	1	13	1387	13.74	120		522	865	37.64	62.36
8	30	9	1	12	1386	13.73	121	10092	658	728	47.47	52.53

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	21	9	6	15	1383	13.7	122		734	649	53.07	46.93
5	22	9	6	14	1379	13.66	123		726	653	52.65	47.35
7	12	9	1	12	1379	13.66	124		520	859	37.71	62.29
7	5	9	1	12	1374	13.61	125		437	937	31.8	68.2
7	26	9	1	12	1369	13.57	126		598	771	43.68	56.32
8	14	9	6	12	1369	13.57	127		559	810	40.83	59.17
5	25	9	2	17	1368	13.56	128		668	700	48.83	51.17
6	28	9	1	19	1366	13.54	129		501	865	36.68	63.32
7	2	9	5	16	1366	13.54	130		827	539	60.54	39.46
7	10	9	6	14	1365	13.53	131		673	692	49.3	50.7
8	28	9	6	15	1365	13.53	132		731	634	53.55	46.45
6	14	9	1	14	1354	13.42	133		527	827	38.92	61.08
8	30	9	1	17	1353	13.41	134		584	769	43.16	56.84
9	4	9	6	19	1351	13.39	135		718	633	53.15	46.85
8	7	9	6	12	1349	13.37	136		530	819	39.29	60.71
6	12	9	6	15	1348	13.36	137		758	590	56.23	43.77
5	3	9	1	15	1345	13.33	138		453	892	33.68	66.32
9	18	9	6	17	1344	13.32	139		756	588	56.25	43.75
7	2	9	5	18	1343	13.31	140		866	477	64.48	35.52
8	14	9	6	13	1343	13.31	141	10092	622	721	46.31	53.69
12	27	9	1	14	1343	13.31	142		560	783	41.7	58.3
3	29	9	1	16	1340	13.28	143		669	671	49.93	50.07
6	21	9	1	17	1340	13.28	144		674	666	50.3	49.7
8	15	9	7	12	1340	13.28	145		618	722	46.12	53.88
9	4	9	6	14	1334	13.22	146		658	676	49.33	50.67
7	10	9	6	16	1333	13.21	147		709	624	53.19	46.81
6	26	9	6	13	1332	13.2	148		685	647	51.43	48.57
7	12	9	1	18	1331	13.19	149		634	697	47.63	52.37
7	2	9	5	15	1330	13.18	150		808	522	60.75	39.25
8	29	9	7	14	1326	13.14	151		507	819	38.24	61.76
11	29	9	1	18	1323	13.11	152		801	522	60.54	39.46
6	12	9	6	16	1320	13.08	153		767	553	58.11	41.89
8	14	9	6	18	1314	13.02	154		672	642	51.14	48.86
6	12	9	6	18	1311	12.99	155		766	545	58.43	41.57
7	19	9	1	12	1311	12.99	156		493	818	37.6	62.4
11	25	9	4	19	1309	12.97	157		823	486	62.87	37.13
7	31	9	6	13	1308	12.96	158		670	638	51.22	48.78
7	6	9	2	15	1307	12.95	159		547	760	41.85	58.15
7	31	9	6	12	1305	12.93	160		651	654	49.89	50.11
6	12	9	6	17	1304	12.92	161	10092	737	567	56.52	43.48
9	13	9	1	16	1304	12.92	162		698	606	53.53	46.47
7	3	9	6	13	1303	12.91	163		723	580	55.49	44.51
8	21	9	6	17	1303	12.91	164		736	567	56.49	43.51
7	31	9	6	18	1302	12.9	165		749	553	57.53	42.47
8	23	9	1	13	1300	12.88	166		477	823	36.69	63.31
6	12	9	6	14	1299	12.87	167		686	613	52.81	47.19
7	6	9	2	16	1298	12.86	168		600	698	46.22	53.78
9	7	9	2	18	1298	12.86	169		652	646	50.23	49.77
6	19	9	6	17	1296	12.84	170		675	621	52.08	47.92
8	15	9	7	11	1295	12.83	171		551	744	42.55	57.45
7	17	9	6	17	1294	12.82	172		696	598	53.79	46.21
4	5	9	1	16	1293	12.81	173		656	637	50.73	49.27

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
6	14	9	1	17	1292	12.8	174		656	636	50.77	49.23
8	21	9	6	16	1292	12.8	175		732	560	56.66	43.34
4	5	9	1	15	1290	12.78	176		663	627	51.4	48.6
8	14	9	6	11	1290	12.78	177		538	752	41.71	58.29
7	2	9	5	19	1288	12.76	178		778	510	60.4	39.6
7	3	9	6	11	1286	12.74	179		692	594	53.81	46.19
7	17	9	6	12	1286	12.74	180		578	708	44.95	55.05
7	24	9	6	17	1286	12.74	181	10092	710	576	55.21	44.79
5	15	9	6	17	1285	12.73	182		612	673	47.63	52.37
9	11	9	6	16	1284	12.72	183		707	577	55.06	44.94
6	7	9	1	17	1282	12.7	184		591	691	46.1	53.9
5	10	9	1	17	1281	12.69	185		478	803	37.31	62.69
8	1	9	7	12	1281	12.69	186		700	581	54.64	45.36
8	29	9	7	15	1281	12.69	187		511	770	39.89	60.11
6	19	9	6	18	1279	12.67	188		795	484	62.16	37.84
7	10	9	6	12	1277	12.65	189		549	728	42.99	57.01
9	20	9	1	16	1277	12.65	190		570	707	44.64	55.36
4	5	9	1	17	1274	12.62	191		748	526	58.71	41.29
9	5	9	7	11	1274	12.62	192		713	561	55.97	44.03
11	25	9	4	13	1274	12.62	193		545	729	42.78	57.22
7	2	9	5	14	1272	12.6	194		708	564	55.66	44.34
7	31	9	6	17	1272	12.6	195		682	590	53.62	46.38
3	29	9	1	17	1271	12.59	196		682	589	53.66	46.34
5	25	9	2	18	1270	12.58	197		644	626	50.71	49.29
8	23	9	1	12	1270	12.58	198		489	781	38.5	61.5
3	29	9	1	15	1269	12.57	199		588	681	46.34	53.66
6	19	9	6	15	1269	12.57	200		684	585	53.9	46.1

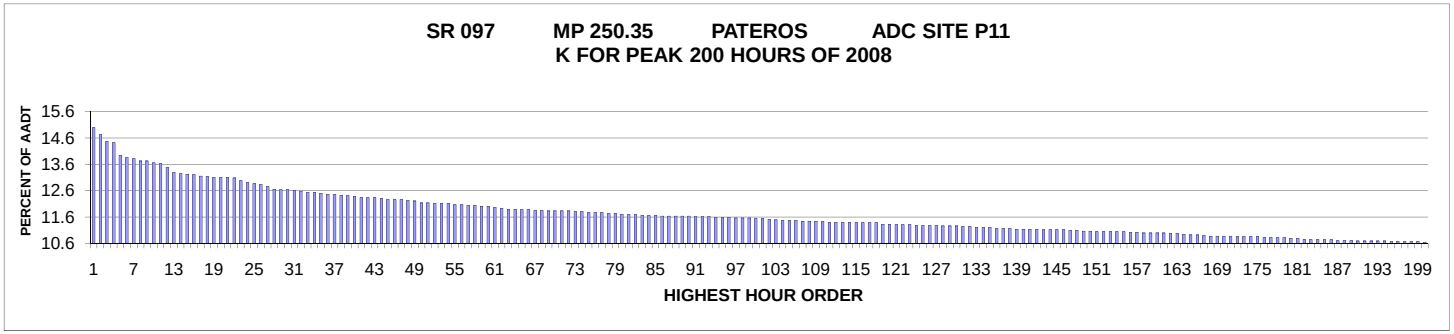

AADT= 4213 **K 30 FACTOR=** 12.63 **K 100 FACTOR=** 11.54 **K 200 FACTOR=** 10.63 **D FACTOR=** 59.69

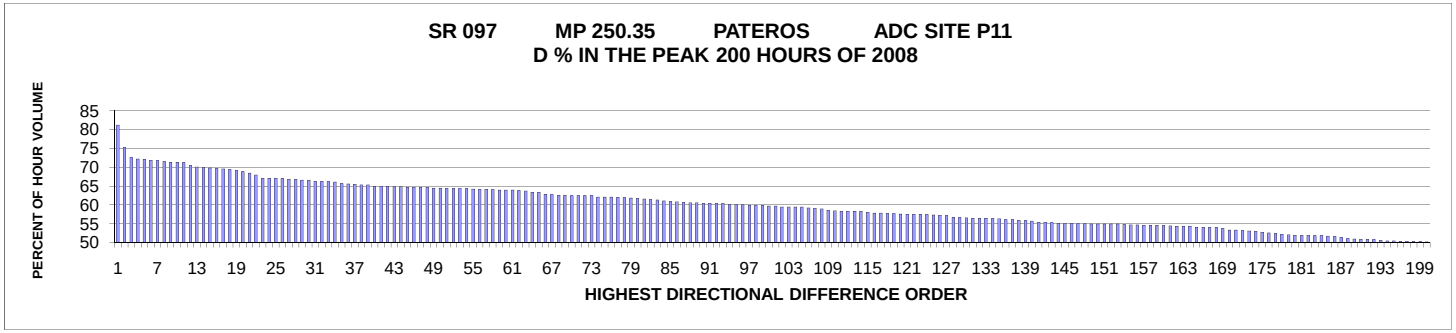

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	9	9	1	15	631	14.98	1	4213	237	394	37.56	62.44
8	9	9	1	14	620	14.72	2		245	375	39.52	60.48
7	5	9	1	12	609	14.46	3		175	434	28.74	71.26
8	9	9	1	13	607	14.41	4		215	392	35.42	64.58
5	22	9	6	16	587	13.93	5		394	193	67.12	32.88
5	22	9	6	17	583	13.84	6		376	207	64.49	35.51
10	16	9	6	14	582	13.81	7		416	166	71.48	28.52
5	22	9	6	18	578	13.72	8		386	192	66.78	33.22
10	16	9	6	16	578	13.72	9		372	206	64.36	35.64
10	16	9	6	17	575	13.65	10		417	158	72.52	27.48
5	25	9	2	12	574	13.62	11		162	412	28.22	71.78
8	7	9	6	17	568	13.48	12		378	190	66.55	33.45
7	5	9	1	14	560	13.29	13		173	387	30.89	69.11
5	25	9	2	13	558	13.24	14		174	384	31.18	68.82
10	16	9	6	13	557	13.22	15		369	188	66.25	33.75
8	7	9	6	15	556	13.2	16		337	219	60.61	39.39
5	22	9	6	15	554	13.15	17		354	200	63.9	36.1

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	19	9	1	15	553	13.13	18		222	331	40.14	59.86
7	3	9	6	12	552	13.1	19		298	254	53.99	46.01
8	9	9	1	12	552	13.1	20		174	378	31.52	68.48
10	16	9	6	15	552	13.1	21	4213	362	190	65.58	34.42
8	23	9	1	13	551	13.08	22		158	393	28.68	71.32
7	19	9	1	12	547	12.98	23		196	351	35.83	64.17
8	9	9	1	16	544	12.91	24		187	357	34.38	65.63
10	9	9	6	17	542	12.86	25		347	195	64.02	35.98
7	17	9	6	16	540	12.82	26		312	228	57.78	42.22
8	2	9	1	13	537	12.75	27		234	303	43.58	56.42
8	7	9	6	16	533	12.65	28		319	214	59.85	40.15
8	16	9	1	14	532	12.63	29		202	330	37.97	62.03
9	4	9	6	16	532	12.63	30		289	243	54.32	45.68
8	23	9	1	12	531	12.6	31		159	372	29.94	70.06
7	19	9	1	14	530	12.58	32		175	355	33.02	66.98
7	17	9	6	15	528	12.53	33		289	239	54.73	45.27
8	16	9	1	13	528	12.53	34		179	349	33.9	66.1
8	7	9	6	13	526	12.49	35		289	237	54.94	45.06
8	6	9	5	15	525	12.46	36		312	213	59.43	40.57
7	19	9	1	13	524	12.44	37		168	356	32.06	67.94
7	5	9	1	13	523	12.41	38		175	348	33.46	66.54
8	23	9	1	14	523	12.41	39		190	333	36.33	63.67
7	12	9	1	13	522	12.39	40		206	316	39.46	60.54
10	16	9	6	18	520	12.34	41	4213	366	154	70.38	29.62
7	5	9	1	15	519	12.32	42		180	339	34.68	65.32
8	7	9	6	18	519	12.32	43		336	183	64.74	35.26
9	4	9	6	18	518	12.3	44		296	222	57.14	42.86
7	31	9	6	13	516	12.25	45		274	242	53.1	46.9
8	2	9	1	12	516	12.25	46		170	346	32.95	67.05
8	14	9	6	17	516	12.25	47		327	189	63.37	36.63
8	23	9	1	15	515	12.22	48		198	317	38.45	61.55
6	21	9	1	14	514	12.2	49		180	334	35.02	64.98
5	25	9	2	11	511	12.13	50		144	367	28.18	71.82
10	9	9	6	16	511	12.13	51		312	199	61.06	38.94
5	25	9	2	14	510	12.11	52		156	354	30.59	69.41
8	22	9	7	12	510	12.11	53		207	303	40.59	59.41
10	2	9	6	17	510	12.11	54		289	221	56.67	43.33
7	6	9	2	15	508	12.06	55		232	276	45.67	54.33
9	25	9	6	16	508	12.06	56		261	247	51.38	48.62
5	22	9	6	14	507	12.03	57		329	178	64.89	35.11
7	3	9	6	14	507	12.03	58		280	227	55.23	44.77
7	2	9	5	15	506	12.01	59		285	221	56.32	43.68
7	31	9	6	15	506	12.01	60		263	243	51.98	48.02
8	22	9	7	13	504	11.96	61	4213	233	271	46.23	53.77
8	2	9	1	14	502	11.92	62		224	278	44.62	55.38
7	24	9	6	16	501	11.89	63		274	227	54.69	45.31
8	14	9	6	16	501	11.89	64		280	221	55.89	44.11
7	2	9	5	16	500	11.87	65		307	193	61.4	38.6
7	17	9	6	17	500	11.87	66		297	203	59.4	40.6
5	25	9	2	15	499	11.84	67		150	349	30.06	69.94
7	3	9	6	16	499	11.84	68		291	208	58.32	41.68
6	21	9	1	12	498	11.82	69		139	359	27.91	72.09

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	10	9	6	16	498	11.82	70		281	217	56.43	43.57
8	16	9	1	12	498	11.82	71		178	320	35.74	64.26
8	30	9	1	13	498	11.82	72		187	311	37.55	62.45
4	24	9	6	17	497	11.8	73		322	175	64.79	35.21
10	11	9	1	16	497	11.8	74		168	329	33.8	66.2
5	23	9	7	12	496	11.77	75		317	179	63.91	36.09
7	12	9	1	14	496	11.77	76		211	285	42.54	57.46
8	7	9	6	14	496	11.77	77		310	186	62.5	37.5
8	8	9	7	14	494	11.73	78		288	206	58.3	41.7
9	11	9	6	16	494	11.73	79		251	243	50.81	49.19
8	21	9	6	15	493	11.7	80		271	222	54.97	45.03
5	23	9	7	13	492	11.68	81	4213	290	202	58.94	41.06
8	1	9	7	12	492	11.68	82		270	222	54.88	45.12
8	14	9	6	18	491	11.65	83		319	172	64.97	35.03
8	28	9	6	15	491	11.65	84		260	231	52.95	47.05
10	9	9	6	18	491	11.65	85		311	180	63.34	36.66
7	5	9	1	16	490	11.63	86		184	306	37.55	62.45
7	18	9	7	15	490	11.63	87		225	265	45.92	54.08
8	8	9	7	12	490	11.63	88		254	236	51.84	48.16
8	8	9	7	16	490	11.63	89		261	229	53.27	46.73
8	28	9	6	16	490	11.63	90		284	206	57.96	42.04
7	3	9	6	17	489	11.61	91		281	208	57.46	42.54
10	16	9	6	11	489	11.61	92		320	169	65.44	34.56
11	25	9	4	15	489	11.61	93		257	232	52.56	47.44
7	17	9	6	14	488	11.58	94		260	228	53.28	46.72
7	18	9	7	13	488	11.58	95		243	245	49.8	50.2
10	9	9	6	15	488	11.58	96		282	206	57.79	42.21
7	3	9	6	18	487	11.56	97		312	175	64.07	35.93
8	8	9	7	15	487	11.56	98		266	221	54.62	45.38
8	14	9	6	12	487	11.56	99		221	266	45.38	54.62
8	9	9	1	18	486	11.54	100		202	284	41.56	58.44
8	21	9	6	16	486	11.54	101	4213	291	195	59.88	40.12
8	16	9	1	15	485	11.51	102		205	280	42.27	57.73
7	2	9	5	17	484	11.49	103		312	172	64.46	35.54
7	26	9	1	16	483	11.46	104		196	287	40.58	59.42
8	20	9	5	16	483	11.46	105		264	219	54.66	45.34
10	11	9	1	15	483	11.46	106		159	324	32.92	67.08
7	26	9	1	17	482	11.44	107		220	262	45.64	54.36
8	9	9	1	17	482	11.44	108		183	299	37.97	62.03
9	4	9	6	17	482	11.44	109		263	219	54.56	45.44
10	16	9	6	12	481	11.42	110		335	146	69.65	30.35
5	16	9	7	11	480	11.39	111		281	199	58.54	41.46
6	19	9	6	17	480	11.39	112		290	190	60.42	39.58
7	10	9	6	15	480	11.39	113		261	219	54.38	45.63
7	26	9	1	14	480	11.39	114		204	276	42.5	57.5
7	3	9	6	15	479	11.37	115		263	216	54.91	45.09
7	31	9	6	14	479	11.37	116		235	244	49.06	50.94
8	30	9	1	12	479	11.37	117		182	297	38	62
9	7	9	2	12	479	11.37	118		166	313	34.66	65.34
7	26	9	1	15	477	11.32	119		195	282	40.88	59.12
8	23	9	1	17	477	11.32	120		235	242	49.27	50.73
6	21	9	1	13	476	11.3	121	4213	161	315	33.82	66.18

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	12	9	1	15	476	11.3	122		182	294	38.24	61.76
10	11	9	1	14	476	11.3	123		145	331	30.46	69.54
7	17	9	6	12	475	11.27	124		246	229	51.79	48.21
7	24	9	6	17	475	11.27	125		269	206	56.63	43.37
8	8	9	7	13	475	11.27	126		257	218	54.11	45.89
9	18	9	6	17	475	11.27	127		263	212	55.37	44.63
6	28	9	1	15	474	11.25	128		181	293	38.19	61.81
7	3	9	6	13	474	11.25	129		276	198	58.23	41.77
7	10	9	6	18	474	11.25	130		303	171	63.92	36.08
7	18	9	7	12	473	11.23	131		228	245	48.2	51.8
8	23	9	1	16	473	11.23	132		193	280	40.8	59.2
4	24	9	6	16	472	11.2	133		271	201	57.42	42.58
7	17	9	6	18	472	11.2	134		292	180	61.86	38.14
7	18	9	7	14	472	11.2	135		212	260	44.92	55.08
7	16	9	5	17	470	11.16	136		294	176	62.55	37.45
8	21	9	6	13	470	11.16	137		224	246	47.66	52.34
8	31	9	2	16	470	11.16	138		214	256	45.53	54.47
6	19	9	6	16	469	11.13	139		291	178	62.05	37.95
6	26	9	6	16	469	11.13	140		284	185	60.55	39.45
7	30	9	5	16	469	11.13	141	4213	270	199	57.57	42.43
10	23	9	6	16	469	11.13	142		245	224	52.24	47.76
7	31	9	6	17	468	11.11	143		285	183	60.9	39.1
8	3	9	2	13	468	11.11	144		238	230	50.85	49.15
8	6	9	5	16	468	11.11	145		273	195	58.33	41.67
8	15	9	7	12	468	11.11	146		187	281	39.96	60.04
6	28	9	1	13	467	11.08	147		169	298	36.19	63.81
8	14	9	6	15	467	11.08	148		225	242	48.18	51.82
6	28	9	1	16	466	11.06	149		185	281	39.7	60.3
7	10	9	6	14	466	11.06	150		235	231	50.43	49.57
6	28	9	1	14	465	11.04	151		173	292	37.2	62.8
7	11	9	7	16	465	11.04	152		206	259	44.3	55.7
7	17	9	6	13	465	11.04	153		235	230	50.54	49.46
7	24	9	6	18	465	11.04	154		251	214	53.98	46.02
8	30	9	1	14	465	11.04	155		180	285	38.71	61.29
5	24	9	1	13	464	11.01	156		164	300	35.34	64.66
8	2	9	1	16	464	11.01	157		209	255	45.04	54.96
6	21	9	1	15	463	10.99	158		174	289	37.58	62.42
7	16	9	5	16	463	10.99	159		265	198	57.24	42.76
7	24	9	6	14	463	10.99	160		230	233	49.68	50.32
7	30	9	5	14	463	10.99	161	4213	239	224	51.62	48.38
7	31	9	6	16	462	10.97	162		254	208	54.98	45.02
11	29	9	1	13	462	10.97	163		87	375	18.83	81.17
6	19	9	6	15	461	10.94	164		254	207	55.1	44.9
5	23	9	7	16	460	10.92	165		296	164	64.35	35.65
9	7	9	2	13	460	10.92	166		139	321	30.22	69.78
7	23	9	5	16	459	10.89	167		257	202	55.99	44.01
9	25	9	6	17	458	10.87	168		243	215	53.06	46.94
5	23	9	7	17	457	10.85	169		255	202	55.8	44.2
6	7	9	1	13	457	10.85	170		160	297	35.01	64.99
7	3	9	6	11	457	10.85	171		262	195	57.33	42.67
7	30	9	5	15	457	10.85	172		227	230	49.67	50.33
8	7	9	6	19	457	10.85	173		326	131	71.33	28.67

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
9	11	9	6	17	457	10.85	174		224	233	49.02	50.98
10	23	9	6	15	457	10.85	175		216	241	47.26	52.74
8	10	9	2	15	456	10.82	176		263	193	57.68	42.32
8	30	9	1	16	456	10.82	177		184	272	40.35	59.65
5	25	9	2	16	455	10.8	178		151	304	33.19	66.81
7	31	9	6	12	455	10.8	179		235	220	51.65	48.35
8	14	9	6	14	454	10.78	180		228	226	50.22	49.78
9	18	9	6	19	454	10.78	181	4213	273	181	60.13	39.87
8	23	9	1	11	453	10.75	182		126	327	27.81	72.19
7	6	9	2	16	452	10.73	183		225	227	49.78	50.22
7	23	9	5	17	452	10.73	184		273	179	60.4	39.6
7	24	9	6	15	452	10.73	185		235	217	51.99	48.01
7	26	9	1	12	452	10.73	186		160	292	35.4	64.6
2	13	9	6	16	451	10.7	187		290	161	64.3	35.7
8	8	9	7	17	451	10.7	188		255	196	56.54	43.46
8	21	9	6	17	451	10.7	189		283	168	62.75	37.25
5	15	9	6	16	450	10.68	190		252	198	56	44
5	29	9	6	16	450	10.68	191		248	202	55.11	44.89
7	10	9	6	17	450	10.68	192		247	203	54.89	45.11
7	18	9	7	16	450	10.68	193		223	227	49.56	50.44
8	14	9	6	11	450	10.68	194		180	270	40	60
5	24	9	1	15	449	10.66	195		181	268	40.31	59.69
7	2	9	5	18	449	10.66	196		288	161	64.14	35.86
7	5	9	1	11	449	10.66	197		111	338	24.72	75.28
7	12	9	1	12	449	10.66	198		176	273	39.2	60.8
7	24	9	6	13	449	10.66	199		196	253	43.65	56.35
6	5	9	6	16	448	10.63	200		253	195	56.47	43.53

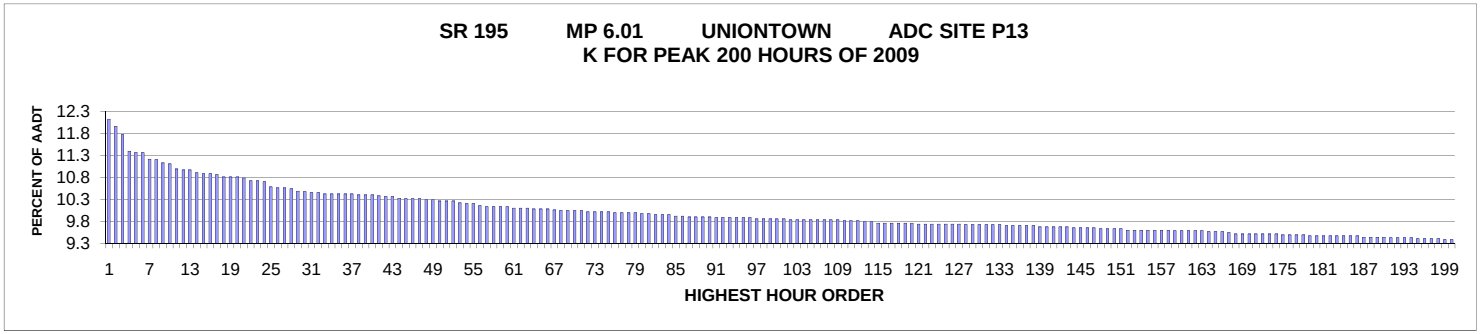

AADT= 4394 **K 30 FACTOR=** 10.47 **K 100 FACTOR=** 9.85 **K 200 FACTOR=** 9.38 **D FACTOR=** 60.04

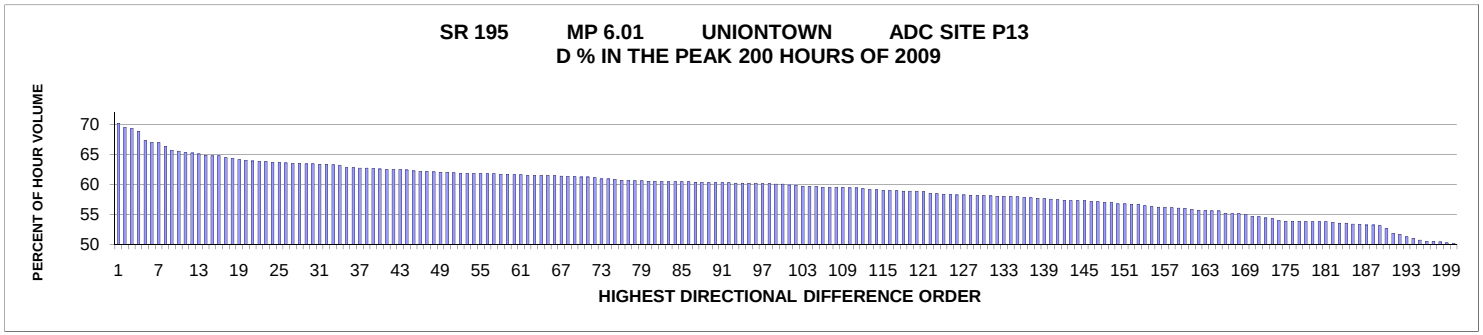

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
9	4	9	6	18	533	12.13	1	4394	203	330	38.09	61.91
9	4	9	6	17	526	11.97	2		237	289	45.06	54.94
4	24	9	6	18	517	11.77	3		186	331	35.98	64.02
9	4	9	6	16	501	11.4	4		174	327	34.73	65.27
5	8	9	6	17	499	11.36	5		218	281	43.69	56.31
8	14	9	6	15	499	11.36	6		232	267	46.49	53.51
9	18	9	6	18	493	11.22	7		195	298	39.55	60.45
9	25	9	6	16	492	11.2	8		213	279	43.29	56.71
8	14	9	6	17	489	11.13	9		189	300	38.65	61.35
9	25	9	6	17	488	11.11	10		192	296	39.34	60.66
4	3	9	6	17	483	10.99	11		195	288	40.37	59.63
5	22	9	6	16	482	10.97	12		202	280	41.91	58.09
6	26	9	6	17	482	10.97	13		212	270	43.98	56.02
5	8	9	6	16	479	10.9	14		195	284	40.71	59.29
4	3	9	6	18	478	10.88	15		183	295	38.28	61.72
5	8	9	6	18	478	10.88	16		179	299	37.45	62.55
5	22	9	6	17	477	10.86	17		180	297	37.74	62.26

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
6	25	9	5	17	475	10.81	18		183	292	38.53	61.47
6	26	9	6	16	475	10.81	19		220	255	46.32	53.68
9	25	9	6	18	475	10.81	20		188	287	39.58	60.42
11	25	9	4	17	474	10.79	21	4394	195	279	41.14	58.86
4	17	9	6	16	471	10.72	22		199	272	42.25	57.75
6	5	9	6	16	471	10.72	23		191	280	40.55	59.45
5	22	9	6	18	470	10.7	24		172	298	36.6	63.4
5	21	9	5	17	465	10.58	25		164	301	35.27	64.73
5	29	9	6	17	464	10.56	26		201	263	43.32	56.68
8	17	9	2	18	464	10.56	27		179	285	38.58	61.42
4	24	9	6	17	463	10.54	28		198	265	42.76	57.24
6	26	9	6	15	461	10.49	29		248	213	53.8	46.2
5	15	9	6	16	460	10.47	30		172	288	37.39	62.61
7	17	9	6	17	459	10.45	31		201	258	43.79	56.21
9	18	9	6	16	459	10.45	32		193	266	42.05	57.95
4	10	9	6	16	458	10.42	33		197	261	43.01	56.99
8	13	9	5	18	458	10.42	34		186	272	40.61	59.39
8	14	9	6	18	458	10.42	35		172	286	37.55	62.45
8	21	9	6	16	458	10.42	36		183	275	39.96	60.04
8	21	9	6	18	458	10.42	37		182	276	39.74	60.26
3	13	9	6	16	457	10.4	38		211	246	46.17	53.83
5	20	9	4	18	457	10.4	39		192	265	42.01	57.99
9	18	9	6	17	457	10.4	40		191	266	41.79	58.21
3	21	9	7	17	456	10.38	41	4394	317	139	69.52	30.48
2	27	9	6	17	455	10.36	42		186	269	40.88	59.12
7	2	9	5	15	455	10.36	43		202	253	44.4	55.6
9	3	9	5	18	454	10.33	44		160	294	35.24	64.76
7	10	9	6	17	453	10.31	45		194	259	42.83	57.17
8	20	9	5	18	453	10.31	46		170	283	37.53	62.47
9	11	9	6	17	453	10.31	47		135	318	29.8	70.2
5	7	9	5	16	452	10.29	48		205	247	45.35	54.65
5	14	9	5	16	452	10.29	49		186	266	41.15	58.85
8	12	9	4	17	451	10.26	50		175	276	38.8	61.2
8	18	9	3	17	451	10.26	51		185	266	41.02	58.98
8	19	9	4	17	451	10.26	52		180	271	39.91	60.09
9	17	9	5	18	449	10.22	53		172	277	38.31	61.69
8	15	9	7	11	448	10.2	54		232	216	51.79	48.21
11	13	9	6	18	448	10.2	55		221	227	49.33	50.67
1	16	9	6	17	446	10.15	56		197	249	44.17	55.83
1	22	9	5	18	445	10.13	57		217	228	48.76	51.24
3	27	9	6	16	445	10.13	58		194	251	43.6	56.4
5	15	9	6	17	445	10.13	59		173	272	38.88	61.12
9	11	9	6	18	445	10.13	60		170	275	38.2	61.8
5	9	9	7	16	444	10.1	61	4394	162	282	36.49	63.51
5	28	9	5	17	444	10.1	62		183	261	41.22	58.78
8	31	9	2	18	444	10.1	63		155	289	34.91	65.09
4	10	9	6	17	443	10.08	64		185	258	41.76	58.24
6	5	9	6	17	443	10.08	65		202	241	45.6	54.4
8	17	9	2	17	443	10.08	66		189	254	42.66	57.34
8	7	9	6	17	442	10.06	67		186	256	42.08	57.92
3	27	9	6	18	441	10.04	68		152	289	34.47	65.53
4	17	9	6	17	441	10.04	69		204	237	46.26	53.74

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	28	9	6	17	441	10.04	70		187	254	42.4	57.6
11	25	9	4	16	441	10.04	71		174	267	39.46	60.54
4	16	9	5	17	440	10.01	72		160	280	36.36	63.64
7	9	9	5	18	440	10.01	73		168	272	38.18	61.82
7	17	9	6	16	440	10.01	74		206	234	46.82	53.18
7	17	9	6	18	440	10.01	75		188	252	42.73	57.27
6	12	9	6	17	439	9.99	76		177	262	40.32	59.68
8	15	9	7	12	439	9.99	77		218	221	49.66	50.34
8	20	9	5	17	439	9.99	78		174	265	39.64	60.36
11	14	9	7	12	439	9.99	79		249	190	56.72	43.28
6	24	9	4	17	438	9.97	80		166	272	37.9	62.1
7	15	9	4	18	438	9.97	81	4394	174	264	39.73	60.27
2	27	9	6	18	437	9.95	82		156	281	35.7	64.3
6	12	9	6	18	437	9.95	83		174	263	39.82	60.18
8	27	9	5	18	437	9.95	84		174	263	39.82	60.18
4	10	9	6	18	436	9.92	85		168	268	38.53	61.47
11	13	9	6	16	436	9.92	86		204	232	46.79	53.21
7	17	9	6	15	435	9.9	87		218	217	50.11	49.89
8	5	9	4	18	435	9.9	88		191	244	43.91	56.09
8	6	9	5	17	435	9.9	89		170	265	39.08	60.92
8	21	9	6	15	435	9.9	90		203	232	46.67	53.33
5	9	9	7	10	434	9.88	91		277	157	63.82	36.18
5	21	9	5	18	434	9.88	92		135	299	31.11	68.89
6	25	9	5	18	434	9.88	93		166	268	38.25	61.75
6	26	9	6	18	434	9.88	94		193	241	44.47	55.53
7	31	9	6	16	434	9.88	95		174	260	40.09	59.91
9	3	9	5	17	434	9.88	96		172	262	39.63	60.37
3	27	9	6	17	433	9.85	97		194	239	44.8	55.2
7	9	9	5	17	433	9.85	98		164	269	37.88	62.12
7	10	9	6	18	433	9.85	99		178	255	41.11	58.89
8	13	9	5	16	433	9.85	100		192	241	44.34	55.66
8	26	9	4	18	433	9.85	101	4394	172	261	39.72	60.28
3	6	9	6	16	432	9.83	102		194	238	44.91	55.09
3	13	9	6	17	432	9.83	103		214	218	49.54	50.46
5	21	9	5	16	432	9.83	104		165	267	38.19	61.81
5	29	9	6	16	432	9.83	105		166	266	38.43	61.57
6	5	9	6	18	432	9.83	106		172	260	39.81	60.19
7	14	9	3	18	432	9.83	107		161	271	37.27	62.73
8	20	9	5	16	432	9.83	108		181	251	41.9	58.1
8	28	9	6	18	432	9.83	109		175	257	40.51	59.49
6	9	9	3	17	431	9.81	110		142	289	32.95	67.05
7	22	9	4	17	431	9.81	111		158	273	36.66	63.34
8	24	9	2	18	431	9.81	112		166	265	38.52	61.48
9	10	9	5	17	430	9.79	113		160	270	37.21	62.79
11	13	9	6	17	430	9.79	114		232	198	53.95	46.05
5	7	9	5	17	429	9.76	115		168	261	39.16	60.84
7	2	9	5	18	429	9.76	116		160	269	37.3	62.7
8	17	9	2	16	429	9.76	117		178	251	41.49	58.51
8	28	9	6	16	429	9.76	118		181	248	42.19	57.81
9	24	9	5	17	429	9.76	119		174	255	40.56	59.44
11	6	9	6	18	429	9.76	120		176	253	41.03	58.97
1	22	9	5	17	428	9.74	121	4394	215	213	50.23	49.77

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
2	26	9	5	16	428	9.74	122		199	229	46.5	53.5
6	10	9	4	18	428	9.74	123		181	247	42.29	57.71
6	11	9	5	17	428	9.74	124		183	245	42.76	57.24
7	23	9	5	18	428	9.74	125		169	259	39.49	60.51
9	15	9	3	18	428	9.74	126		172	256	40.19	59.81
11	19	9	5	18	428	9.74	127		166	262	38.79	61.21
4	3	9	6	16	427	9.72	128		194	233	45.43	54.57
5	19	9	3	17	427	9.72	129		169	258	39.58	60.42
6	16	9	3	17	427	9.72	130		163	264	38.17	61.83
7	10	9	6	16	427	9.72	131		170	257	39.81	60.19
7	24	9	6	17	427	9.72	132		159	268	37.24	62.76
8	19	9	4	18	427	9.72	133		169	258	39.58	60.42
5	15	9	6	18	426	9.7	134		168	258	39.44	60.56
6	4	9	5	18	426	9.7	135		163	263	38.26	61.74
6	30	9	3	17	426	9.7	136		172	254	40.38	59.62
9	23	9	4	18	426	9.7	137		170	256	39.91	60.09
11	20	9	6	17	426	9.7	138		197	229	46.24	53.76
5	29	9	6	18	425	9.67	139		143	282	33.65	66.35
7	1	9	4	17	425	9.67	140		155	270	36.47	63.53
7	10	9	6	15	425	9.67	141	4394	189	236	44.47	55.53
8	13	9	5	17	425	9.67	142		177	248	41.65	58.35
8	23	9	1	13	425	9.67	143		264	161	62.12	37.88
6	4	9	5	16	424	9.65	144		161	263	37.97	62.03
8	15	9	7	13	424	9.65	145		201	223	47.41	52.59
9	2	9	4	18	424	9.65	146		178	246	41.98	58.02
9	26	9	7	12	424	9.65	147		155	269	36.56	63.44
2	27	9	6	16	423	9.63	148		190	233	44.92	55.08
3	26	9	5	16	423	9.63	149		163	260	38.53	61.47
6	11	9	5	18	423	9.63	150		169	254	39.95	60.05
7	13	9	2	18	423	9.63	151		153	270	36.17	63.83
5	9	9	7	11	422	9.6	152		246	176	58.29	41.71
5	10	9	1	17	422	9.6	153		229	193	54.27	45.73
6	4	9	5	17	422	9.6	154		167	255	39.57	60.43
6	6	9	7	11	422	9.6	155		259	163	61.37	38.63
8	26	9	4	17	422	9.6	156		155	267	36.73	63.27
9	5	9	7	14	422	9.6	157		260	162	61.61	38.39
9	10	9	5	18	422	9.6	158		150	272	35.55	64.45
1	30	9	6	16	421	9.58	159		176	245	41.81	58.19
5	8	9	6	19	421	9.58	160		129	292	30.64	69.36
7	7	9	3	18	421	9.58	161	4394	171	250	40.62	59.38
8	21	9	6	17	421	9.58	162		148	273	35.15	64.85
9	24	9	5	18	421	9.58	163		151	270	35.87	64.13
4	9	9	5	18	420	9.56	164		153	267	36.43	63.57
5	20	9	4	17	420	9.56	165		167	253	39.76	60.24
8	14	9	6	16	420	9.56	166		182	238	43.33	56.67
4	17	9	6	18	419	9.54	167		178	241	42.48	57.52
2	26	9	5	17	418	9.51	168		222	196	53.11	46.89
4	24	9	6	16	418	9.51	169		175	243	41.87	58.13
7	16	9	5	18	418	9.51	170		157	261	37.56	62.44
9	4	9	6	14	418	9.51	171		216	202	51.67	48.33
9	19	9	7	12	418	9.51	172		234	184	55.98	44.02
11	25	9	4	15	418	9.51	173		180	238	43.06	56.94

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
12	11	9	6	18	418	9.51	174		154	264	36.84	63.16
5	20	9	4	16	417	9.49	175		164	253	39.33	60.67
7	2	9	5	16	417	9.49	176		145	272	34.77	65.23
8	27	9	5	17	417	9.49	177		163	254	39.09	60.91
11	6	9	6	17	417	9.49	178		169	248	40.53	59.47
4	4	9	7	11	416	9.47	179		224	192	53.85	46.15
6	15	9	2	17	416	9.47	180		161	255	38.7	61.3
7	2	9	5	17	416	9.47	181	4394	136	280	32.69	67.31
7	31	9	6	17	416	9.47	182		158	258	37.98	62.02
8	15	9	7	14	416	9.47	183		210	206	50.48	49.52
9	11	9	6	16	416	9.47	184		164	252	39.42	60.58
12	18	9	6	17	416	9.47	185		194	222	46.63	53.37
12	18	9	6	18	416	9.47	186		177	239	42.55	57.45
4	14	9	3	18	415	9.44	187		156	259	37.59	62.41
7	1	9	4	18	415	9.44	188		152	263	36.63	63.37
9	22	9	3	16	415	9.44	189		178	237	42.89	57.11
11	25	9	4	14	415	9.44	190		192	223	46.27	53.73
4	25	9	7	13	414	9.42	191		170	244	41.06	58.94
8	4	9	3	18	414	9.42	192		142	272	34.3	65.7
9	18	9	6	19	414	9.42	193		172	242	41.55	58.45
12	11	9	6	17	414	9.42	194		191	223	46.14	53.86
3	6	9	6	17	413	9.4	195		181	232	43.83	56.17
6	24	9	4	18	413	9.4	196		149	264	36.08	63.92
7	24	9	6	18	413	9.4	197		150	263	36.32	63.68
12	4	9	6	17	413	9.4	198		169	244	40.92	59.08
6	5	9	6	15	412	9.38	199		210	202	50.97	49.03
6	29	9	2	17	412	9.38	200		136	276	33.01	66.99

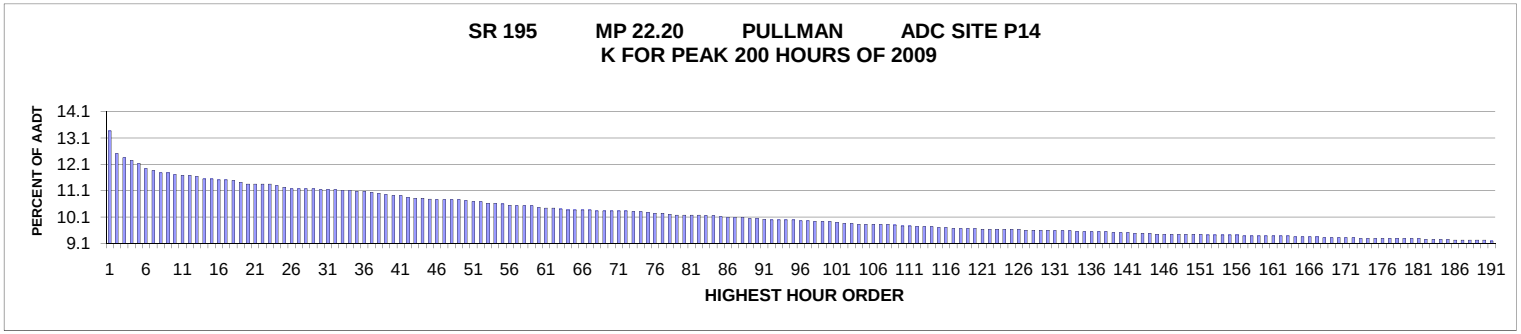

AADT= 3136 **K 30 FACTOR=** 11.13 **K 100 FACTOR=** 10.01 **K 200 FACTOR=** 9.18 **D FACTOR=** 52.94

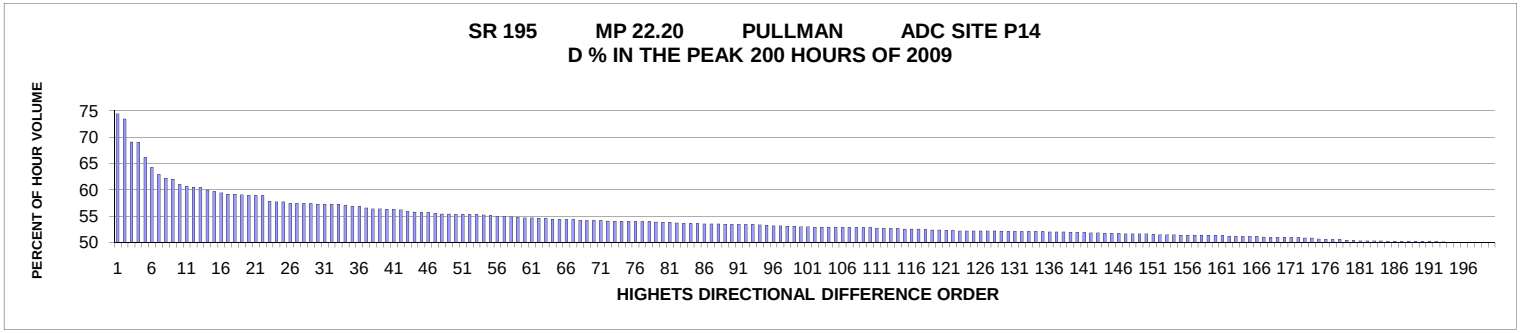

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
5	8	9	6	17	419	13.36	1	3136	210	209	50.12	49.88
9	4	9	6	18	392	12.5	2		207	185	52.81	47.19
10	10	9	7	13	387	12.34	3		158	229	40.83	59.17
9	4	9	6	17	384	12.24	4		220	164	57.29	42.71
3	13	9	6	16	380	12.12	5		244	136	64.21	35.79
4	3	9	6	18	374	11.93	6		168	206	44.92	55.08
9	4	9	6	16	372	11.86	7		196	176	52.69	47.31
5	8	9	6	18	369	11.77	8		183	186	49.59	50.41
6	26	9	6	16	369	11.77	9		199	170	53.93	46.07
8	21	9	6	16	367	11.7	10		171	196	46.59	53.41
5	22	9	6	17	366	11.67	11		166	200	45.36	54.64
9	25	9	6	16	366	11.67	12		207	159	56.56	43.44
10	9	9	6	18	365	11.64	13		199	166	54.52	45.48
9	25	9	6	18	362	11.54	14		191	171	52.76	47.24
10	16	9	6	17	362	11.54	15		195	167	53.87	46.13
5	29	9	6	17	361	11.51	16		188	173	52.08	47.92
10	2	9	6	18	361	11.51	17		174	187	48.2	51.8

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
9	25	9	6	17	360	11.48	18		180	180	50	50
10	10	9	7	12	358	11.42	19		147	211	41.06	58.94
4	24	9	6	18	356	11.35	20		188	168	52.81	47.19
5	8	9	6	16	356	11.35	21	3136	171	185	48.03	51.97
8	28	9	6	18	356	11.35	22		190	166	53.37	46.63
10	2	9	6	17	356	11.35	23		178	178	50	50
9	11	9	6	17	354	11.29	24		163	191	46.05	53.95
4	3	9	6	17	352	11.22	25		177	175	50.28	49.72
4	10	9	6	18	350	11.16	26		160	190	45.71	54.29
5	22	9	6	16	350	11.16	27		185	165	52.86	47.14
8	7	9	6	18	350	11.16	28		184	166	52.57	47.43
8	22	9	7	12	350	11.16	29		206	144	58.86	41.14
6	26	9	6	15	349	11.13	30		200	149	57.31	42.69
10	9	9	6	17	349	11.13	31		187	162	53.58	46.42
10	10	9	7	18	349	11.13	32		241	108	69.05	30.95
10	9	9	6	16	348	11.1	33		170	178	48.85	51.15
10	16	9	6	16	348	11.1	34		188	160	54.02	45.98
5	22	9	6	18	347	11.07	35		154	193	44.38	55.62
9	4	9	6	15	347	11.07	36		170	177	48.99	51.01
9	18	9	6	18	346	11.03	37		162	184	46.82	53.18
2	20	9	6	17	345	11	38		214	131	62.03	37.97
9	11	9	6	18	343	10.94	39		171	172	49.85	50.15
8	21	9	6	18	342	10.91	40		172	170	50.29	49.71
10	9	9	6	15	342	10.91	41	3136	158	184	46.2	53.8
3	13	9	6	17	340	10.84	42		225	115	66.18	33.82
4	24	9	6	17	339	10.81	43		158	181	46.61	53.39
8	21	9	6	14	339	10.81	44		179	160	52.8	47.2
9	11	9	6	16	338	10.78	45		183	155	54.14	45.86
3	27	9	6	17	337	10.75	46		185	152	54.9	45.1
3	27	9	6	18	337	10.75	47		138	199	40.95	59.05
5	15	9	6	17	337	10.75	48		169	168	50.15	49.85
10	30	9	6	18	337	10.75	49		181	156	53.71	46.29
4	3	9	6	16	336	10.71	50		152	184	45.24	54.76
6	26	9	6	17	335	10.68	51		199	136	59.4	40.6
7	17	9	6	16	335	10.68	52		173	162	51.64	48.36
2	13	9	6	17	333	10.62	53		173	160	51.95	48.05
6	5	9	6	16	333	10.62	54		184	149	55.26	44.74
9	18	9	6	16	332	10.59	55		170	162	51.2	48.8
3	27	9	6	16	331	10.55	56		191	140	57.7	42.3
2	27	9	6	18	330	10.52	57		165	165	50	50
5	15	9	6	16	330	10.52	58		160	170	48.48	51.52
7	2	9	5	18	330	10.52	59		153	177	46.36	53.64
7	10	9	6	17	328	10.46	60		155	173	47.26	52.74
6	5	9	6	18	327	10.43	61	3136	159	168	48.62	51.38
9	5	9	7	13	327	10.43	62		132	195	40.37	59.63
5	1	9	6	17	326	10.4	63		180	146	55.21	44.79
6	19	9	6	17	325	10.36	64		149	176	45.85	54.15
7	31	9	6	16	325	10.36	65		162	163	49.85	50.15
7	31	9	6	17	325	10.36	66		144	181	44.31	55.69
10	10	9	7	11	325	10.36	67		142	183	43.69	56.31
6	5	9	6	17	324	10.33	68		169	155	52.16	47.84
7	2	9	5	16	324	10.33	69		161	163	49.69	50.31

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	14	9	6	17	324	10.33	70		152	172	46.91	53.09
8	22	9	7	13	324	10.33	71		179	145	55.25	44.75
10	23	9	6	16	324	10.33	72		159	165	49.07	50.93
2	13	9	6	16	323	10.3	73		195	128	60.37	39.63
4	3	9	6	15	323	10.3	74		171	152	52.94	47.06
6	12	9	6	16	322	10.27	75		158	164	49.07	50.93
6	26	9	6	18	321	10.24	76		176	145	54.83	45.17
6	28	9	1	17	321	10.24	77		131	190	40.81	59.19
10	23	9	6	18	320	10.2	78		153	167	47.81	52.19
3	6	9	6	16	319	10.17	79		183	136	57.37	42.63
5	8	9	6	15	319	10.17	80		183	136	57.37	42.63
5	29	9	6	18	319	10.17	81	3136	155	164	48.59	51.41
10	23	9	6	17	319	10.17	82		152	167	47.65	52.35
6	12	9	6	13	318	10.14	83		159	159	50	50
8	21	9	6	17	318	10.14	84		147	171	46.23	53.77
10	8	9	5	18	317	10.11	85		167	150	52.68	47.32
5	14	9	5	16	316	10.08	86		175	141	55.38	44.62
9	7	9	2	16	316	10.08	87		166	150	52.53	47.47
9	18	9	6	17	316	10.08	88		161	155	50.95	49.05
9	7	9	2	15	315	10.04	89		173	142	54.92	45.08
10	16	9	6	15	315	10.04	90		162	153	51.43	48.57
3	6	9	6	17	314	10.01	91		174	140	55.41	44.59
6	19	9	6	16	313	9.98	92		142	171	45.37	54.63
6	26	9	6	14	313	9.98	93		162	151	51.76	48.24
8	28	9	6	17	313	9.98	94		163	150	52.08	47.92
10	30	9	6	17	313	9.98	95		161	152	51.44	48.56
2	27	9	6	17	312	9.95	96		159	153	50.96	49.04
7	17	9	6	15	312	9.95	97		169	143	54.17	45.83
3	13	9	6	18	311	9.92	98		178	133	57.23	42.77
4	17	9	6	18	311	9.92	99		162	149	52.09	47.91
5	21	9	5	16	311	9.92	100		152	159	48.87	51.13
10	2	9	6	16	310	9.89	101	3136	162	148	52.26	47.74
9	19	9	7	12	309	9.85	102		122	187	39.48	60.52
10	16	9	6	18	309	9.85	103		159	150	51.46	48.54
3	20	9	6	17	308	9.82	104		173	135	56.17	43.83
4	10	9	6	16	308	9.82	105		159	149	51.62	48.38
5	9	9	7	15	308	9.82	106		171	137	55.52	44.48
8	7	9	6	16	308	9.82	107		156	152	50.65	49.35
8	14	9	6	18	308	9.82	108		149	159	48.38	51.62
6	5	9	6	14	307	9.79	109		173	134	56.35	43.65
5	22	9	6	15	306	9.76	110		145	161	47.39	52.61
5	29	9	6	16	306	9.76	111		132	174	43.14	56.86
2	20	9	6	18	305	9.73	112		186	119	60.98	39.02
9	18	9	6	15	305	9.73	113		158	147	51.8	48.2
12	18	9	6	16	305	9.73	114		185	120	60.66	39.34
5	1	9	6	18	304	9.69	115		164	140	53.95	46.05
8	7	9	6	13	304	9.69	116		146	158	48.03	51.97
7	10	9	6	18	303	9.66	117		148	155	48.84	51.16
8	7	9	6	17	303	9.66	118		152	151	50.17	49.83
9	3	9	5	17	303	9.66	119		158	145	52.15	47.85
9	18	9	6	14	303	9.66	120		162	141	53.47	46.53
2	16	9	2	17	302	9.63	121	3136	164	138	54.3	45.7

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
6	19	9	6	13	302	9.63	122		151	151	50	50
7	2	9	5	17	302	9.63	123		144	158	47.68	52.32
7	31	9	6	15	302	9.63	124		156	146	51.66	48.34
8	20	9	5	18	302	9.63	125		148	154	49.01	50.99
9	5	9	7	12	302	9.63	126		132	170	43.71	56.29
4	10	9	6	17	301	9.6	127		161	140	53.49	46.51
4	17	9	6	16	301	9.6	128		163	138	54.15	45.85
7	31	9	6	12	301	9.6	129		161	140	53.49	46.51
9	19	9	7	19	301	9.6	130		221	80	73.42	26.58
6	19	9	6	14	300	9.57	131		155	145	51.67	48.33
7	30	9	5	15	300	9.57	132		162	138	54	46
8	22	9	7	11	300	9.57	133		160	140	53.33	46.67
5	9	9	7	13	299	9.53	134		150	149	50.17	49.83
5	22	9	6	13	299	9.53	135		150	149	50.17	49.83
8	13	9	5	18	299	9.53	136		160	139	53.51	46.49
8	20	9	5	15	299	9.53	137		146	153	48.83	51.17
8	20	9	5	17	299	9.53	138		156	143	52.17	47.83
8	21	9	6	11	298	9.5	139		153	145	51.34	48.66
8	21	9	6	13	298	9.5	140		155	143	52.01	47.99
8	22	9	7	14	298	9.5	141	3136	163	135	54.7	45.3
4	26	9	1	16	297	9.47	142		187	110	62.96	37.04
7	5	9	1	13	297	9.47	143		205	92	69.02	30.98
9	5	9	7	19	297	9.47	144		221	76	74.41	25.59
2	6	9	6	17	296	9.44	145		171	125	57.77	42.23
4	17	9	6	17	296	9.44	146		165	131	55.74	44.26
5	9	9	7	12	296	9.44	147		154	142	52.03	47.97
5	9	9	7	16	296	9.44	148		170	126	57.43	42.57
6	12	9	6	17	296	9.44	149		155	141	52.36	47.64
7	17	9	6	13	296	9.44	150		152	144	51.35	48.65
8	14	9	6	16	296	9.44	151		148	148	50	50
7	17	9	6	14	295	9.41	152		156	139	52.88	47.12
8	14	9	6	15	295	9.41	153		154	141	52.2	47.8
8	18	9	3	18	295	9.41	154		154	141	52.2	47.8
9	25	9	6	12	295	9.41	155		139	156	47.12	52.88
10	9	9	6	14	295	9.41	156		156	139	52.88	47.12
2	27	9	6	16	294	9.38	157		157	137	53.4	46.6
7	10	9	6	16	294	9.38	158		159	135	54.08	45.92
8	7	9	6	12	294	9.38	159		153	141	52.04	47.96
8	21	9	6	15	294	9.38	160		151	143	51.36	48.64
9	25	9	6	15	294	9.38	161	3136	151	143	51.36	48.64
10	2	9	6	15	294	9.38	162		167	127	56.8	43.2
10	30	9	6	16	294	9.38	163		138	156	46.94	53.06
2	20	9	6	16	293	9.34	164		168	125	57.34	42.66
6	12	9	6	14	293	9.34	165		147	146	50.17	49.83
6	19	9	6	15	293	9.34	166		148	145	50.51	49.49
9	24	9	5	17	293	9.34	167		146	147	49.83	50.17
5	8	9	6	19	292	9.31	168		117	175	40.07	59.93
5	15	9	6	18	292	9.31	169		159	133	54.45	45.55
6	18	9	5	16	292	9.31	170		150	142	51.37	48.63
7	3	9	6	12	292	9.31	171		147	145	50.34	49.66
7	24	9	6	15	292	9.31	172		153	139	52.4	47.6
1	22	9	5	17	291	9.28	173		148	143	50.86	49.14

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
1	30	9	6	17	291	9.28	174		181	110	62.2	37.8
5	1	9	6	16	291	9.28	175		168	123	57.73	42.27
6	11	9	5	17	291	9.28	176		151	140	51.89	48.11
7	2	9	5	14	291	9.28	177		161	130	55.33	44.67
7	17	9	6	18	291	9.28	178		166	125	57.04	42.96
8	28	9	6	16	291	9.28	179		144	147	49.48	50.52
9	7	9	2	17	291	9.28	180		164	127	56.36	43.64
10	23	9	6	15	291	9.28	181	3136	155	136	53.26	46.74
6	21	9	1	17	290	9.25	182		151	139	52.07	47.93
7	31	9	6	18	290	9.25	183		150	140	51.72	48.28
8	14	9	6	13	290	9.25	184		151	139	52.07	47.93
9	11	9	6	13	290	9.25	185		162	128	55.86	44.14
6	19	9	6	18	289	9.22	186		136	153	47.06	52.94
7	2	9	5	15	289	9.22	187		150	139	51.9	48.1
7	24	9	6	18	289	9.22	188		143	146	49.48	50.52
7	31	9	6	11	289	9.22	189		160	129	55.36	44.64
8	19	9	4	17	289	9.22	190		142	147	49.13	50.87
7	16	9	5	18	288	9.18	191		153	135	53.13	46.88
8	23	9	1	13	288	9.18	192		183	105	63.54	36.46

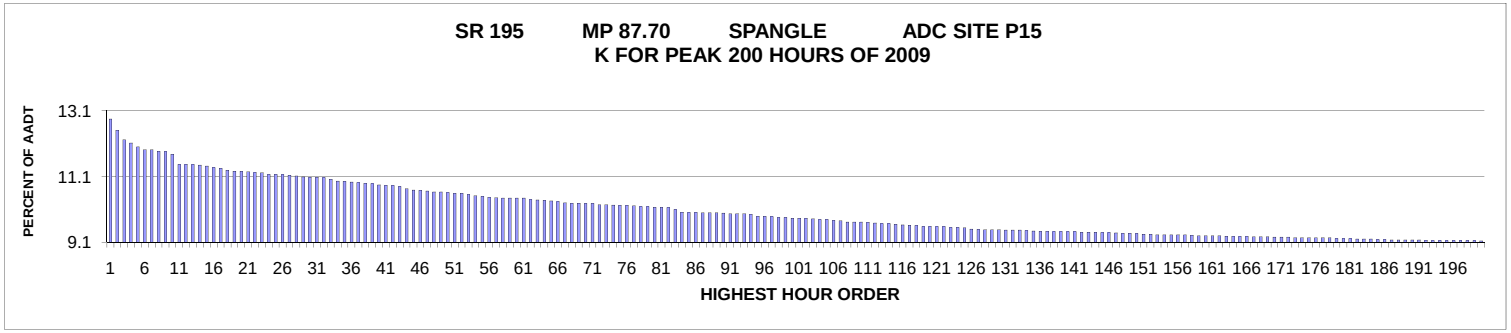

AADT= 8211 **K 30 FACTOR=** 11.08 **K 100 FACTOR=** 9.84 **K 200 FACTOR=** 9.15 **D FACTOR=** 53.78

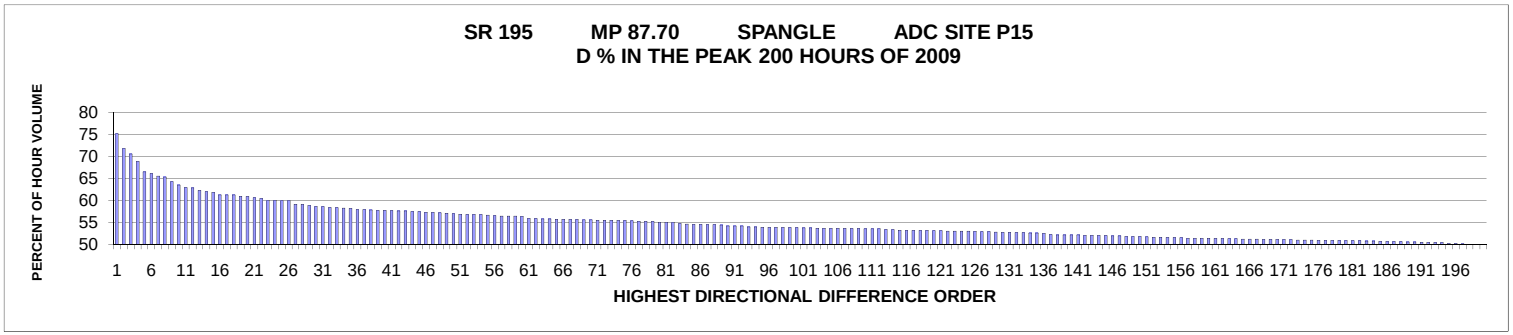

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
3	13	9	6	18	1055	12.85	1	8211	594	461	56.3	43.7
10	10	9	7	12	1027	12.51	2		382	645	37.2	62.8
5	8	9	6	18	1003	12.22	3		476	527	47.46	52.54
2	13	9	6	17	995	12.12	4		508	487	51.06	48.94
9	5	9	7	12	986	12.01	5		386	600	39.15	60.85
9	19	9	7	12	979	11.92	6		370	609	37.79	62.21
10	16	9	6	18	979	11.92	7		415	564	42.39	57.61
10	10	9	7	11	975	11.87	8		338	637	34.67	65.33
10	9	9	6	17	974	11.86	9		425	549	43.63	56.37
10	9	9	6	18	967	11.78	10		418	549	43.23	56.77
5	8	9	6	17	942	11.47	11		443	499	47.03	52.97
9	4	9	6	17	942	11.47	12		470	472	49.89	50.11
9	4	9	6	18	942	11.47	13		471	471	50	50
10	23	9	6	17	940	11.45	14		437	503	46.49	53.51
10	2	9	6	17	938	11.42	15		450	488	47.97	52.03
4	10	9	6	17	934	11.37	16		476	458	50.96	49.04
4	24	9	6	17	932	11.35	17		424	508	45.49	54.51

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
10	2	9	6	18	928	11.3	18		413	515	44.5	55.5
3	13	9	6	17	925	11.27	19		482	443	52.11	47.89
9	18	9	6	18	925	11.27	20		386	539	41.73	58.27
9	25	9	6	18	924	11.25	21	8211	469	455	50.76	49.24
4	3	9	6	16	922	11.23	22		452	470	49.02	50.98
3	6	9	6	18	921	11.22	23		456	465	49.51	50.49
5	15	9	6	18	917	11.17	24		400	517	43.62	56.38
9	19	9	7	11	917	11.17	25		350	567	38.17	61.83
11	21	9	7	11	916	11.16	26		511	405	55.79	44.21
9	18	9	6	17	915	11.14	27		410	505	44.81	55.19
11	6	9	6	18	913	11.12	28		421	492	46.11	53.89
10	10	9	7	19	911	11.09	29		643	268	70.58	29.42
4	24	9	6	18	910	11.08	30		442	468	48.57	51.43
9	5	9	7	13	910	11.08	31		365	545	40.11	59.89
3	6	9	6	17	909	11.07	32		405	504	44.55	55.45
10	16	9	6	17	905	11.02	33		429	476	47.4	52.6
9	19	9	7	20	901	10.97	34		647	254	71.81	28.19
3	27	9	6	18	900	10.96	35		454	446	50.44	49.56
9	25	9	6	17	898	10.94	36		443	455	49.33	50.67
9	5	9	7	20	897	10.92	37		674	223	75.14	24.86
4	3	9	6	17	895	10.9	38		398	497	44.47	55.53
5	22	9	6	17	894	10.89	39		410	484	45.86	54.14
11	14	9	7	11	891	10.85	40		339	552	38.05	61.95
2	13	9	6	18	890	10.84	41	8211	445	445	50	50
9	4	9	6	16	889	10.83	42		477	412	53.66	46.34
11	13	9	6	16	887	10.8	43		369	518	41.6	58.4
4	3	9	6	18	881	10.73	44		391	490	44.38	55.62
11	21	9	7	12	878	10.69	45		427	451	48.63	51.37
9	11	9	6	18	877	10.68	46		409	468	46.64	53.36
6	5	9	6	17	875	10.66	47		407	468	46.51	53.49
5	15	9	6	17	873	10.63	48		391	482	44.79	55.21
9	11	9	6	16	873	10.63	49		429	444	49.14	50.86
5	8	9	6	16	872	10.62	50		431	441	49.43	50.57
4	18	9	7	18	870	10.6	51		497	373	57.13	42.87
10	30	9	6	18	870	10.6	52		323	547	37.13	62.87
4	17	9	6	17	867	10.56	53		400	467	46.14	53.86
4	10	9	6	18	864	10.52	54		405	459	46.88	53.13
2	20	9	6	18	862	10.5	55		418	444	48.49	51.51
12	18	9	6	17	860	10.47	56		423	437	49.19	50.81
10	30	9	6	17	859	10.46	57		380	479	44.24	55.76
2	27	9	6	17	858	10.45	58		386	472	44.99	55.01
6	26	9	6	18	858	10.45	59		444	414	51.75	48.25
11	6	9	6	17	858	10.45	60		396	462	46.15	53.85
11	14	9	7	12	858	10.45	61	8211	333	525	38.81	61.19
10	9	9	6	16	854	10.4	62		427	427	50	50
3	13	9	6	16	853	10.39	63		493	360	57.8	42.2
5	1	9	6	18	852	10.38	64		408	444	47.89	52.11
3	27	9	6	17	851	10.36	65		385	466	45.24	54.76
6	19	9	6	18	849	10.34	66		360	489	42.4	57.6
10	10	9	7	20	846	10.3	67		583	263	68.91	31.09
8	28	9	6	18	845	10.29	68		361	484	42.72	57.28
10	30	9	6	16	845	10.29	69		409	436	48.4	51.6

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
6	26	9	6	17	844	10.28	70		419	425	49.64	50.36
10	16	9	6	16	844	10.28	71		432	412	51.18	48.82
2	13	9	6	16	842	10.25	72		404	438	47.98	52.02
6	5	9	6	18	842	10.25	73		357	485	42.4	57.6
9	11	9	6	17	841	10.24	74		410	431	48.75	51.25
2	20	9	6	17	840	10.23	75		441	399	52.5	47.5
2	27	9	6	18	840	10.23	76		407	433	48.45	51.55
4	17	9	6	18	839	10.22	77		381	458	45.41	54.59
2	26	9	5	17	837	10.19	78		369	468	44.09	55.91
10	23	9	6	16	837	10.19	79		391	446	46.71	53.29
5	1	9	6	17	835	10.17	80		414	421	49.58	50.42
11	13	9	6	17	835	10.17	81	8211	305	530	36.53	63.47
2	6	9	6	17	834	10.16	82		387	447	46.4	53.6
1	23	9	6	17	829	10.1	83		339	490	40.89	59.11
11	14	9	7	19	823	10.02	84		544	279	66.1	33.9
9	25	9	6	16	822	10.01	85		445	377	54.14	45.86
11	6	9	6	16	822	10.01	86		401	421	48.78	51.22
7	2	9	5	18	821	10	87		378	443	46.04	53.96
9	3	9	5	18	821	10	88		356	465	43.36	56.64
11	13	9	6	18	821	10	89		338	483	41.17	58.83
6	12	9	6	17	820	9.99	90		366	454	44.63	55.37
8	14	9	6	17	819	9.97	91		354	465	43.22	56.78
10	2	9	6	16	819	9.97	92		416	403	50.79	49.21
11	25	9	4	16	819	9.97	93		384	435	46.89	53.11
5	22	9	6	18	817	9.95	94		391	426	47.86	52.14
5	9	9	7	14	813	9.9	95		432	381	53.14	46.86
10	23	9	6	18	813	9.9	96		362	451	44.53	55.47
6	5	9	6	16	812	9.89	97		381	431	46.92	53.08
8	28	9	6	17	810	9.86	98		376	434	46.42	53.58
9	4	9	6	19	810	9.86	99		441	369	54.44	45.56
5	1	9	6	16	808	9.84	100		410	398	50.74	49.26
6	26	9	6	16	808	9.84	101	8211	425	383	52.6	47.4
7	17	9	6	18	808	9.84	102		352	456	43.56	56.44
1	16	9	6	17	806	9.82	103		380	426	47.15	52.85
4	24	9	6	16	805	9.8	104		382	423	47.45	52.55
9	18	9	6	16	805	9.8	105		393	412	48.82	51.18
5	29	9	6	18	802	9.77	106		396	406	49.38	50.62
10	9	9	6	19	801	9.76	107		355	446	44.32	55.68
5	8	9	6	15	798	9.72	108		370	428	46.37	53.63
10	8	9	5	18	798	9.72	109		336	462	42.11	57.89
11	21	9	7	19	798	9.72	110		523	275	65.54	34.46
5	22	9	6	16	797	9.71	111		390	407	48.93	51.07
4	10	9	6	16	796	9.69	112		414	382	52.01	47.99
4	17	9	6	16	794	9.67	113		408	386	51.39	48.61
6	11	9	5	18	794	9.67	114		367	427	46.22	53.78
5	29	9	6	17	792	9.65	115		407	385	51.39	48.61
9	19	9	7	13	791	9.63	116		373	418	47.16	52.84
10	10	9	7	13	790	9.62	117		352	438	44.56	55.44
5	9	9	7	10	789	9.61	118		365	424	46.26	53.74
5	7	9	5	18	787	9.58	119		326	461	41.42	58.58
8	13	9	5	18	787	9.58	120		365	422	46.38	53.62
9	9	9	4	18	787	9.58	121	8211	305	482	38.75	61.25

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
11	25	9	4	15	787	9.58	122		393	394	49.94	50.06
5	14	9	5	17	785	9.56	123		387	398	49.3	50.7
10	1	9	5	18	785	9.56	124		332	453	42.29	57.71
6	6	9	7	13	784	9.55	125		445	339	56.76	43.24
12	11	9	6	17	781	9.51	126		340	441	43.53	56.47
5	9	9	7	13	780	9.5	127		429	351	55	45
3	27	9	6	16	779	9.49	128		360	419	46.21	53.79
4	5	9	1	17	779	9.49	129		368	411	47.24	52.76
8	7	9	6	18	779	9.49	130		333	446	42.75	57.25
1	30	9	6	18	778	9.48	131		345	433	44.34	55.66
5	9	9	7	16	778	9.48	132		412	366	52.96	47.04
10	16	9	6	15	778	9.48	133		385	393	49.49	50.51
6	12	9	6	16	777	9.46	134		380	397	48.91	51.09
6	19	9	6	17	776	9.45	135		335	441	43.17	56.83
4	5	9	1	15	775	9.44	136		418	357	53.94	46.06
12	12	9	7	16	775	9.44	137		307	468	39.61	60.39
5	9	9	7	11	774	9.43	138		404	370	52.2	47.8
5	9	9	7	17	774	9.43	139		447	327	57.75	42.25
7	31	9	6	16	774	9.43	140		400	374	51.68	48.32
12	18	9	6	18	774	9.43	141	8211	380	394	49.1	50.9
3	6	9	6	16	773	9.41	142		400	373	51.75	48.25
5	8	9	6	19	773	9.41	143		393	380	50.84	49.16
9	18	9	6	15	773	9.41	144		388	385	50.19	49.81
4	3	9	6	15	772	9.4	145		354	418	45.85	54.15
5	9	9	7	12	772	9.4	146		376	396	48.7	51.3
9	5	9	7	11	771	9.39	147		345	426	44.75	55.25
6	12	9	6	18	770	9.38	148		308	462	40	60
8	7	9	6	17	770	9.38	149		328	442	42.6	57.4
5	7	9	5	17	769	9.37	150		378	391	49.15	50.85
2	13	9	6	15	768	9.35	151		391	377	50.91	49.09
4	12	9	1	18	768	9.35	152		372	396	48.44	51.56
4	16	9	5	18	766	9.33	153		360	406	47	53
4	28	9	3	17	766	9.33	154		313	453	40.86	59.14
8	29	9	7	18	766	9.33	155		459	307	59.92	40.08
10	22	9	5	17	766	9.33	156		349	417	45.56	54.44
12	4	9	6	16	766	9.33	157		367	399	47.91	52.09
2	12	9	5	17	765	9.32	158		299	466	39.08	60.92
3	13	9	6	19	764	9.3	159		445	319	58.25	41.75
3	20	9	6	17	764	9.3	160		317	447	41.49	58.51
5	21	9	5	17	764	9.3	161	8211	359	405	46.99	53.01
8	13	9	5	17	764	9.3	162		374	390	48.95	51.05
12	18	9	6	16	763	9.29	163		392	371	51.38	48.62
1	23	9	6	16	762	9.28	164		359	403	47.11	52.89
6	28	9	1	16	762	9.28	165		327	435	42.91	57.09
7	2	9	5	17	762	9.28	166		358	404	46.98	53.02
2	16	9	2	17	761	9.27	167		295	466	38.76	61.24
3	12	9	5	18	761	9.27	168		356	405	46.78	53.22
12	4	9	6	17	761	9.27	169		354	407	46.52	53.48
5	13	9	4	18	760	9.26	170		318	442	41.84	58.16
6	3	9	4	18	760	9.26	171		300	460	39.47	60.53
10	15	9	5	18	760	9.26	172		353	407	46.45	53.55
2	6	9	6	18	759	9.24	173		384	375	50.59	49.41

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	17	9	2	18	759	9.24	174		304	455	40.05	59.95
8	19	9	4	18	759	9.24	175		320	439	42.16	57.84
9	3	9	5	17	759	9.24	176		350	409	46.11	53.89
9	18	9	6	19	759	9.24	177		359	400	47.3	52.7
10	15	9	5	17	759	9.24	178		352	407	46.38	53.62
5	10	9	1	14	757	9.22	179		416	341	54.95	45.05
11	12	9	5	17	757	9.22	180		337	420	44.52	55.48
11	21	9	7	13	757	9.22	181	8211	402	355	53.1	46.9
8	6	9	5	17	756	9.21	182		365	391	48.28	51.72
8	28	9	6	16	756	9.21	183		363	393	48.02	51.98
12	11	9	6	16	756	9.21	184		368	388	48.68	51.32
6	28	9	1	17	755	9.19	185		253	502	33.51	66.49
8	14	9	6	16	755	9.19	186		381	374	50.46	49.54
1	22	9	5	17	754	9.18	187		270	484	35.81	64.19
5	9	9	7	15	754	9.18	188		420	334	55.7	44.3
11	4	9	4	18	754	9.18	189		343	411	45.49	54.51
11	13	9	6	15	754	9.18	190		337	417	44.69	55.31
11	25	9	4	14	754	9.18	191		410	344	54.38	45.62
12	11	9	6	18	753	9.17	192		356	397	47.28	52.72
1	16	9	6	16	752	9.16	193		362	390	48.14	51.86
3	4	9	4	17	752	9.16	194		369	383	49.07	50.93
5	2	9	7	17	752	9.16	195		428	324	56.91	43.09
5	28	9	5	17	752	9.16	196		390	362	51.86	48.14
7	9	9	5	18	752	9.16	197		333	419	44.28	55.72
10	25	9	1	17	752	9.16	198		348	404	46.28	53.72
12	10	9	5	18	752	9.16	199		320	432	42.55	57.45
2	26	9	5	18	751	9.15	200		384	367	51.13	48.87

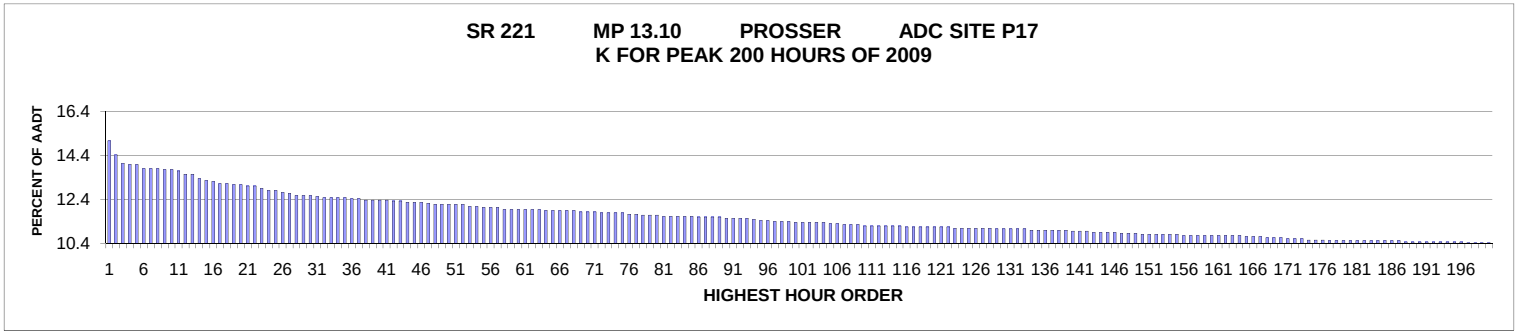

AADT= 2037 **K 30 FACTOR=** 12.57 **K 100 FACTOR=** 11.34 **K 200 FACTOR=** 10.41 **D FACTOR=** 73.08

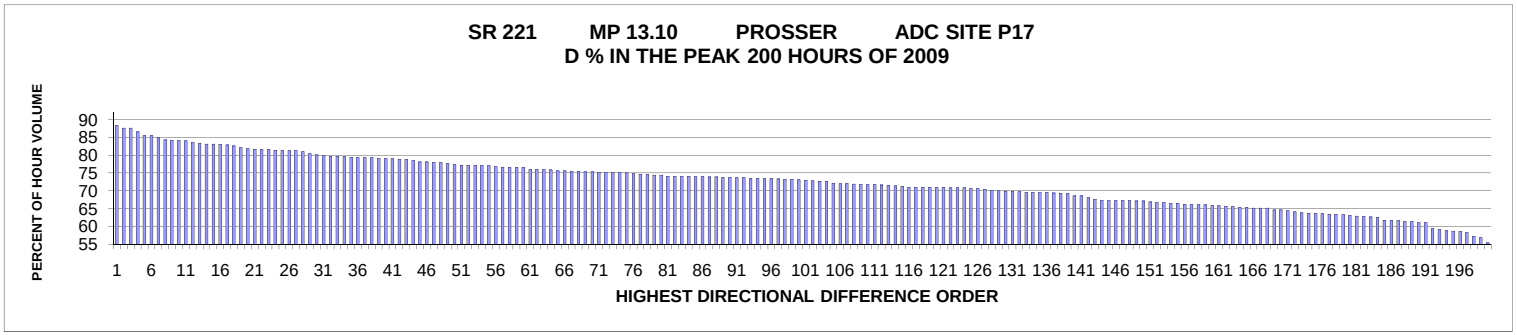

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	13	9	2	17	307	15.07	1	2037	227	80	73.94	26.06
10	21	9	4	7	294	14.43	2		67	227	22.79	77.21
10	15	9	5	7	286	14.04	3		77	209	26.92	73.08
5	28	9	5	17	285	13.99	4		211	74	74.04	25.96
10	8	9	5	7	285	13.99	5		73	212	25.61	74.39
9	24	9	5	7	281	13.79	6		82	199	29.18	70.82
9	24	9	5	18	281	13.79	7		186	95	66.19	33.81
10	22	9	5	7	281	13.79	8		73	208	25.98	74.02
10	19	9	2	7	280	13.75	9		57	223	20.36	79.64
11	3	9	3	7	280	13.75	10		52	228	18.57	81.43
9	17	9	5	18	279	13.7	11		177	102	63.44	36.56
10	7	9	4	7	276	13.55	12		63	213	22.83	77.17
10	13	9	3	7	276	13.55	13		72	204	26.09	73.91
10	9	9	6	7	272	13.35	14		79	193	29.04	70.96
9	23	9	4	7	270	13.25	15		67	203	24.81	75.19
10	16	9	6	18	269	13.21	16		171	98	63.57	36.43
9	16	9	4	7	267	13.11	17		61	206	22.85	77.15

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
10	20	9	3	7	267	13.11	18		64	203	23.97	76.03
10	14	9	4	7	266	13.06	19		66	200	24.81	75.19
10	20	9	3	18	266	13.06	20		163	103	61.28	38.72
9	17	9	5	7	265	13.01	21	2037	66	199	24.91	75.09
10	1	9	5	18	265	13.01	22		169	96	63.77	36.23
9	30	9	4	7	263	12.91	23		65	198	24.71	75.29
9	28	9	2	7	261	12.81	24		64	197	24.52	75.48
10	12	9	2	7	261	12.81	25		53	208	20.31	79.69
9	10	9	5	7	259	12.71	26		59	200	22.78	77.22
11	11	9	4	17	258	12.67	27		199	59	77.13	22.87
10	1	9	5	7	256	12.57	28		72	184	28.13	71.88
10	16	9	6	7	256	12.57	29		68	188	26.56	73.44
10	28	9	4	17	256	12.57	30		203	53	79.3	20.7
10	12	9	2	18	255	12.52	31		170	85	66.67	33.33
9	16	9	4	18	254	12.47	32		167	87	65.75	34.25
10	1	9	5	17	254	12.47	33		164	90	64.57	35.43
10	28	9	4	7	254	12.47	34		62	192	24.41	75.59
11	4	9	4	18	254	12.47	35		192	62	75.59	24.41
9	29	9	3	7	253	12.42	36		62	191	24.51	75.49
11	16	9	2	17	253	12.42	37		184	69	72.73	27.27
7	30	9	5	6	252	12.37	38		34	218	13.49	86.51
10	2	9	6	7	252	12.37	39		66	186	26.19	73.81
10	5	9	2	7	252	12.37	40		59	193	23.41	76.59
10	27	9	3	17	252	12.37	41	2037	181	71	71.83	28.17
7	29	9	4	17	251	12.32	42		185	66	73.71	26.29
11	3	9	3	18	251	12.32	43		178	73	70.92	29.08
6	4	9	5	17	250	12.27	44		173	77	69.2	30.8
9	15	9	3	7	250	12.27	45		53	197	21.2	78.8
9	22	9	3	7	250	12.27	46		67	183	26.8	73.2
10	8	9	5	18	249	12.22	47		146	103	58.63	41.37
6	11	9	5	17	248	12.17	48		170	78	68.55	31.45
9	29	9	3	18	248	12.17	49		155	93	62.5	37.5
10	15	9	5	17	248	12.17	50		158	90	63.71	36.29
10	29	9	5	7	248	12.17	51		62	186	25	75
11	23	9	2	17	248	12.17	52		182	66	73.39	26.61
7	14	9	3	17	246	12.08	53		177	69	71.95	28.05
9	21	9	2	7	246	12.08	54		54	192	21.95	78.05
9	22	9	3	18	245	12.03	55		157	88	64.08	35.92
9	28	9	2	18	245	12.03	56		162	83	66.12	33.88
11	4	9	4	7	245	12.03	57		46	199	18.78	81.22
6	18	9	5	17	243	11.93	58		178	65	73.25	26.75
9	8	9	3	7	243	11.93	59		69	174	28.4	71.6
9	9	9	4	7	243	11.93	60		60	183	24.69	75.31
9	23	9	4	18	243	11.93	61	2037	154	89	63.37	36.63
10	20	9	3	17	243	11.93	62		169	74	69.55	30.45
11	10	9	3	7	243	11.93	63		51	192	20.99	79.01
5	28	9	5	6	242	11.88	64		42	200	17.36	82.64
6	22	9	2	17	242	11.88	65		171	71	70.66	29.34
9	30	9	4	18	242	11.88	66		161	81	66.53	33.47
11	3	9	3	17	242	11.88	67		189	53	78.1	21.9
11	9	9	2	7	242	11.88	68		46	196	19.01	80.99
9	10	9	5	18	241	11.83	69		147	94	61	39

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
10	7	9	4	18	241	11.83	70		148	93	61.41	38.59
10	23	9	6	7	241	11.83	71		64	177	26.56	73.44
7	10	9	6	16	240	11.78	72		177	63	73.75	26.25
9	25	9	6	18	240	11.78	73		148	92	61.67	38.33
10	29	9	5	17	240	11.78	74		169	71	70.42	29.58
11	18	9	4	7	240	11.78	75		36	204	15	85
7	14	9	3	16	239	11.73	76		177	62	74.06	25.94
11	19	9	5	17	239	11.73	77		183	56	76.57	23.43
5	27	9	4	17	238	11.68	78		177	61	74.37	25.63
7	27	9	2	17	238	11.68	79		169	69	71.01	28.99
9	30	9	4	17	238	11.68	80		161	77	67.65	32.35
6	25	9	5	17	237	11.63	81	2037	168	69	70.89	29.11
9	25	9	6	7	237	11.63	82		49	188	20.68	79.32
10	6	9	3	7	237	11.63	83		53	184	22.36	77.64
10	19	9	2	18	237	11.63	84		150	87	63.29	36.71
10	27	9	3	18	237	11.63	85		170	67	71.73	28.27
9	14	9	2	7	236	11.59	86		57	179	24.15	75.85
10	15	9	5	18	236	11.59	87		144	92	61.02	38.98
11	2	9	2	7	236	11.59	88		40	196	16.95	83.05
11	5	9	5	7	236	11.59	89		47	189	19.92	80.08
10	5	9	2	18	235	11.54	90		139	96	59.15	40.85
10	19	9	2	17	235	11.54	91		158	77	67.23	32.77
10	21	9	4	18	235	11.54	92		158	77	67.23	32.77
11	11	9	4	7	235	11.54	93		37	198	15.74	84.26
11	4	9	4	17	234	11.49	94		178	56	76.07	23.93
9	23	9	4	17	233	11.44	95		162	71	69.53	30.47
11	16	9	2	7	233	11.44	96		40	193	17.17	82.83
9	9	9	4	17	232	11.39	97		156	76	67.24	32.76
9	11	9	6	7	232	11.39	98		65	167	28.02	71.98
10	12	9	2	17	232	11.39	99		156	76	67.24	32.76
7	9	9	5	17	231	11.34	100		168	63	72.73	27.27
9	17	9	5	17	231	11.34	101	2037	147	84	63.64	36.36
10	22	9	5	18	231	11.34	102		155	76	67.1	32.9
11	17	9	3	17	231	11.34	103		180	51	77.92	22.08
11	30	9	2	17	231	11.34	104		182	49	78.79	21.21
1	12	9	2	17	230	11.29	105		172	58	74.78	25.22
9	1	9	3	7	230	11.29	106		67	163	29.13	70.87
7	31	9	6	6	229	11.24	107		38	191	16.59	83.41
9	2	9	4	7	229	11.24	108		58	171	25.33	74.67
10	2	9	6	17	229	11.24	109		130	99	56.77	43.23
6	16	9	3	17	228	11.19	110		166	62	72.81	27.19
7	6	9	2	17	228	11.19	111		159	69	69.74	30.26
7	23	9	5	17	228	11.19	112		175	53	76.75	23.25
9	3	9	5	17	228	11.19	113		149	79	65.35	34.65
9	9	9	4	18	228	11.19	114		147	81	64.47	35.53
12	2	9	4	17	228	11.19	115		178	50	78.07	21.93
4	21	9	3	17	227	11.14	116		185	42	81.5	18.5
6	3	9	4	17	227	11.14	117		158	69	69.6	30.4
7	29	9	4	6	227	11.14	118		28	199	12.33	87.67
10	19	9	2	19	227	11.14	119		174	53	76.65	23.35
10	22	9	5	17	227	11.14	120		150	77	66.08	33.92
10	28	9	4	18	227	11.14	121	2037	158	69	69.6	30.4

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
12	1	9	3	17	227	11.14	122		180	47	79.3	20.7
7	9	9	5	16	226	11.09	123		165	61	73.01	26.99
7	16	9	5	15	226	11.09	124		158	68	69.91	30.09
7	30	9	5	17	226	11.09	125		158	68	69.91	30.09
9	8	9	3	18	226	11.09	126		125	101	55.31	44.69
10	5	9	2	17	226	11.09	127		142	84	62.83	37.17
10	26	9	2	17	226	11.09	128		160	66	70.8	29.2
9	1	9	3	17	225	11.05	129		156	69	69.33	30.67
10	2	9	6	18	225	11.05	130		131	94	58.22	41.78
10	30	9	6	7	225	11.05	131		41	184	18.22	81.78
11	24	9	3	7	225	11.05	132		42	183	18.67	81.33
12	2	9	4	7	225	11.05	133		37	188	16.44	83.56
4	9	9	5	7	224	11	134		47	177	20.98	79.02
7	7	9	3	17	224	11	135		159	65	70.98	29.02
7	30	9	5	13	224	11	136		146	78	65.18	34.82
9	11	9	6	18	224	11	137		133	91	59.38	40.63
10	27	9	3	7	224	11	138		40	184	17.86	82.14
11	25	9	4	16	224	11	139		148	76	66.07	33.93
9	2	9	4	18	223	10.95	140		131	92	58.74	41.26
11	17	9	3	7	223	10.95	141	2037	35	188	15.7	84.3
11	18	9	4	17	223	10.95	142		175	48	78.48	21.52
5	21	9	5	17	222	10.9	143		176	46	79.28	20.72
7	23	9	5	18	222	10.9	144		130	92	58.56	41.44
9	22	9	3	17	222	10.9	145		164	58	73.87	26.13
10	6	9	3	18	222	10.9	146		137	85	61.71	38.29
7	10	9	6	17	221	10.85	147		144	77	65.16	34.84
9	3	9	5	18	221	10.85	148		139	82	62.9	37.1
11	19	9	5	7	221	10.85	149		35	186	15.84	84.16
1	21	9	4	17	220	10.8	150		177	43	80.45	19.55
2	19	9	5	17	220	10.8	151		163	57	74.09	25.91
2	23	9	2	17	220	10.8	152		167	53	75.91	24.09
4	14	9	3	7	220	10.8	153		46	174	20.91	79.09
9	18	9	6	7	220	10.8	154		73	147	33.18	66.82
11	24	9	3	17	220	10.8	155		157	63	71.36	28.64
6	12	9	6	17	219	10.75	156		143	76	65.3	34.7
6	17	9	4	17	219	10.75	157		158	61	72.15	27.85
6	24	9	4	17	219	10.75	158		161	58	73.52	26.48
7	8	9	4	17	219	10.75	159		152	67	69.41	30.59
7	13	9	2	16	219	10.75	160		144	75	65.75	34.25
7	16	9	5	6	219	10.75	161	2037	37	182	16.89	83.11
10	7	9	4	17	219	10.75	162		149	70	68.04	31.96
10	26	9	2	7	219	10.75	163		44	175	20.09	79.91
11	13	9	6	7	219	10.75	164		40	179	18.26	81.74
5	27	9	4	6	218	10.7	165		27	191	12.39	87.61
6	23	9	3	17	218	10.7	166		153	65	70.18	29.82
9	21	9	2	18	218	10.7	167		142	76	65.14	34.86
7	28	9	3	6	217	10.65	168		40	177	18.43	81.57
7	28	9	3	13	217	10.65	169		168	49	77.42	22.58
10	30	9	6	17	217	10.65	170		152	65	70.05	29.95
7	17	9	6	15	216	10.6	171		145	71	67.13	32.87
7	24	9	6	16	216	10.6	172		153	63	70.83	29.17
11	2	9	2	18	216	10.6	173		154	62	71.3	28.7

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
3	16	9	2	17	215	10.55	174		159	56	73.95	26.05
5	15	9	6	16	215	10.55	175		141	74	65.58	34.42
10	1	9	5	16	215	10.55	176		139	76	64.65	35.35
7	14	9	3	6	214	10.51	177		25	189	11.68	88.32
7	23	9	5	16	214	10.51	178		153	61	71.5	28.5
9	9	9	4	6	214	10.51	179		36	178	16.82	83.18
9	11	9	6	17	214	10.51	180		151	63	70.56	29.44
9	29	9	3	16	214	10.51	181	2037	135	79	63.08	36.92
10	8	9	5	17	214	10.51	182		132	82	61.68	38.32
10	23	9	6	17	214	10.51	183		134	80	62.62	37.38
11	6	9	6	17	214	10.51	184		157	57	73.36	26.64
11	10	9	3	17	214	10.51	185		161	53	75.23	24.77
11	23	9	2	7	214	10.51	186		31	183	14.49	85.51
11	25	9	4	17	214	10.51	187		144	70	67.29	32.71
4	6	9	2	7	213	10.46	188		31	182	14.55	85.45
6	2	9	3	17	213	10.46	189		163	50	76.53	23.47
6	15	9	2	17	213	10.46	190		146	67	68.54	31.46
9	4	9	6	6	213	10.46	191		40	173	18.78	81.22
10	9	9	6	18	213	10.46	192		122	91	57.28	42.72
10	15	9	5	16	213	10.46	193		142	71	66.67	33.33
10	21	9	4	17	213	10.46	194		157	56	73.71	26.29
11	6	9	6	7	213	10.46	195		34	179	15.96	84.04
11	12	9	5	17	213	10.46	196		159	54	74.65	25.35
3	5	9	5	17	212	10.41	197		169	43	79.72	20.28
6	10	9	4	17	212	10.41	198		152	60	71.7	28.3
9	10	9	5	17	212	10.41	199		141	71	66.51	33.49
10	26	9	2	18	212	10.41	200		139	73	65.57	34.43

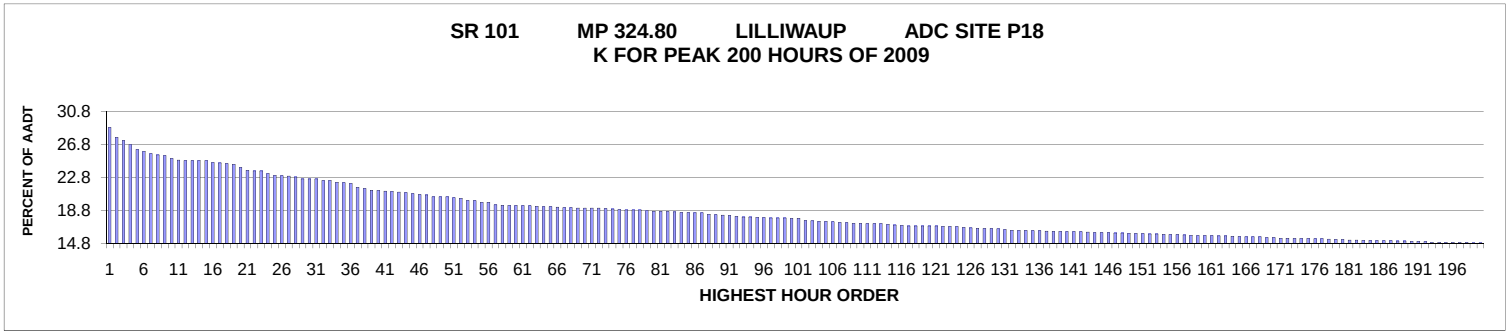

AADT= 3027 **K 30 FACTOR=** 22.63 **K 100 FACTOR=** 17.84 **K 200 FACTOR=** 14.83 **D FACTOR=** 57.83

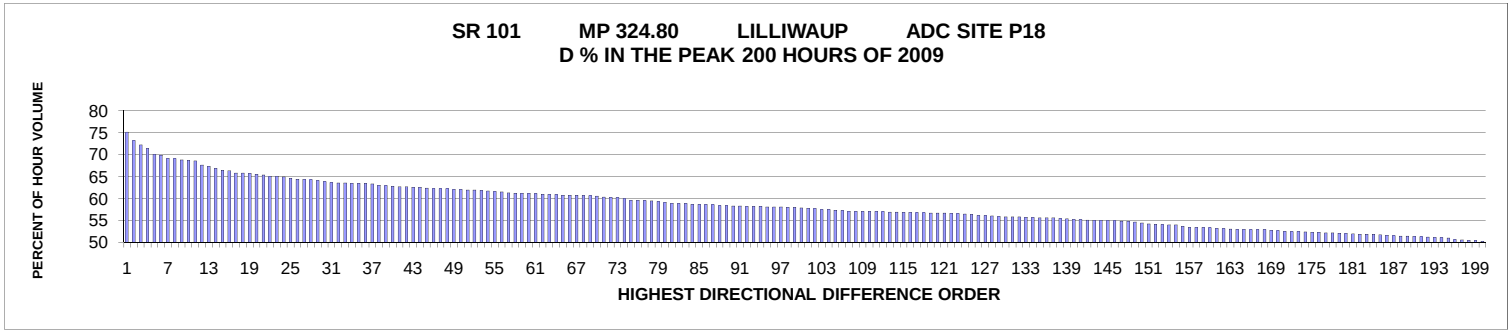

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
5	24	9	1	16	874	28.87	1	3027	384	490	43.94	56.06
5	22	9	6	17	838	27.68	2		542	296	64.68	35.32
5	24	9	1	15	826	27.29	3		389	437	47.09	52.91
5	23	9	7	11	810	26.76	4		560	250	69.14	30.86
5	22	9	6	18	793	26.2	5		548	245	69.1	30.9
5	17	9	1	15	786	25.97	6		271	515	34.48	65.52
5	22	9	6	19	778	25.7	7		500	278	64.27	35.73
5	22	9	6	16	773	25.54	8		508	265	65.72	34.28
5	23	9	7	12	771	25.47	9		490	281	63.55	36.45
5	24	9	1	14	760	25.11	10		391	369	51.45	48.55
5	23	9	7	15	754	24.91	11		457	297	60.61	39.39
5	17	9	1	18	752	24.84	12		257	495	34.18	65.82
5	24	9	1	17	752	24.84	13		284	468	37.77	62.23
5	17	9	1	14	751	24.81	14		308	443	41.01	58.99
5	22	9	6	15	751	24.81	15		460	291	61.25	38.75
5	23	9	7	17	744	24.58	16		456	288	61.29	38.71
5	23	9	7	16	743	24.55	17		486	257	65.41	34.59

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
5	22	9	6	14	741	24.48	18		471	270	63.56	36.44
5	22	9	6	20	739	24.41	19		541	198	73.21	26.79
5	15	9	6	15	727	24.02	20		386	341	53.09	46.91
5	17	9	1	16	716	23.65	21	3027	259	457	36.17	63.83
5	10	9	1	17	714	23.59	22		264	450	36.97	63.03
5	23	9	7	18	714	23.59	23		491	223	68.77	31.23
5	24	9	1	12	704	23.26	24		381	323	54.12	45.88
5	24	9	1	13	697	23.03	25		401	296	57.53	42.47
5	22	9	6	13	696	22.99	26		420	276	60.34	39.66
5	22	9	6	12	695	22.96	27		435	260	62.59	37.41
5	23	9	7	13	692	22.86	28		444	248	64.16	35.84
5	9	9	7	15	685	22.63	29		303	382	44.23	55.77
5	23	9	7	10	685	22.63	30		479	206	69.93	30.07
5	24	9	1	18	684	22.6	31		240	444	35.09	64.91
5	23	9	7	14	679	22.43	32		418	261	61.56	38.44
5	24	9	1	19	679	22.43	33		194	485	28.57	71.43
5	17	9	1	17	673	22.23	34		261	412	38.78	61.22
5	17	9	1	13	670	22.13	35		263	407	39.25	60.75
5	10	9	1	16	668	22.07	36		257	411	38.47	61.53
5	10	9	1	14	654	21.61	37		247	407	37.77	62.23
5	16	9	7	12	649	21.44	38		394	255	60.71	39.29
5	10	9	1	15	643	21.24	39		245	398	38.1	61.9
5	31	9	1	15	642	21.21	40		299	343	46.57	53.43
5	22	9	6	21	640	21.14	41	3027	481	159	75.16	24.84
5	8	9	6	16	638	21.08	42		370	268	57.99	42.01
5	24	9	1	11	636	21.01	43		369	267	58.02	41.98
7	5	9	1	14	634	20.94	44		199	435	31.39	68.61
5	22	9	6	11	630	20.81	45		356	274	56.51	43.49
5	10	9	1	12	627	20.71	46		269	358	42.9	57.1
5	3	9	1	16	626	20.68	47		244	382	38.98	61.02
5	10	9	1	13	619	20.45	48		242	377	39.1	60.9
5	10	9	1	18	619	20.45	49		226	393	36.51	63.49
5	3	9	1	17	618	20.42	50		235	383	38.03	61.97
5	29	9	6	15	615	20.32	51		301	314	48.94	51.06
5	15	9	6	16	614	20.28	52		349	265	56.84	43.16
5	9	9	7	12	605	19.99	53		353	252	58.35	41.65
5	17	9	1	19	604	19.95	54		237	367	39.24	60.76
5	9	9	7	16	599	19.79	55		266	333	44.41	55.59
5	3	9	1	15	598	19.76	56		226	372	37.79	62.21
7	26	9	1	16	589	19.46	57		210	379	35.65	64.35
5	16	9	7	15	588	19.43	58		311	277	52.89	47.11
5	1	9	6	18	587	19.39	59		335	252	57.07	42.93
5	23	9	7	19	587	19.39	60		323	264	55.03	44.97
5	1	9	6	15	585	19.33	61	3027	334	251	57.09	42.91
5	31	9	1	14	585	19.33	62		261	324	44.62	55.38
7	5	9	1	15	584	19.29	63		162	422	27.74	72.26
5	9	9	7	11	582	19.23	64		349	233	59.97	40.03
5	16	9	7	14	582	19.23	65		338	244	58.08	41.92
5	24	9	1	20	581	19.19	66		174	407	29.95	70.05
5	17	9	1	12	579	19.13	67		227	352	39.21	60.79
5	29	9	6	16	579	19.13	68		320	259	55.27	44.73
5	8	9	6	18	577	19.06	69		331	246	57.37	42.63

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
5	9	9	7	14	577	19.06	70		312	265	54.07	45.93
5	15	9	6	19	577	19.06	71		295	282	51.13	48.87
5	29	9	6	17	577	19.06	72		302	275	52.34	47.66
5	15	9	6	17	575	19	73		321	254	55.83	44.17
5	15	9	6	18	574	18.96	74		342	232	59.58	40.42
5	9	9	7	17	571	18.86	75		244	327	42.73	57.27
5	1	9	6	16	570	18.83	76		331	239	58.07	41.93
5	8	9	6	14	570	18.83	77		317	253	55.61	44.39
5	29	9	6	14	570	18.83	78		318	252	55.79	44.21
5	21	9	5	16	568	18.76	79		302	266	53.17	46.83
5	10	9	1	19	566	18.7	80		234	332	41.34	58.66
5	31	9	1	16	565	18.67	81	3027	240	325	42.48	57.52
5	15	9	6	13	564	18.63	82		311	253	55.14	44.86
5	8	9	6	17	563	18.6	83		341	222	60.57	39.43
5	16	9	7	11	561	18.53	84		365	196	65.06	34.94
5	16	9	7	13	561	18.53	85		329	232	58.65	41.35
5	8	9	6	15	560	18.5	86		299	261	53.39	46.61
5	16	9	7	16	559	18.47	87		271	288	48.48	51.52
5	29	9	6	19	555	18.33	88		293	262	52.79	47.21
5	10	9	1	11	552	18.24	89		264	288	47.83	52.17
5	30	9	7	12	551	18.2	90		340	211	61.71	38.29
5	15	9	6	14	550	18.17	91		335	215	60.91	39.09
5	15	9	6	12	547	18.07	92		284	263	51.92	48.08
5	3	9	1	14	544	17.97	93		203	341	37.32	62.68
7	5	9	1	13	544	17.97	94		170	374	31.25	68.75
8	16	9	1	15	543	17.94	95		308	235	56.72	43.28
5	29	9	6	13	542	17.91	96		281	261	51.85	48.15
5	3	9	1	13	541	17.87	97		201	340	37.15	62.85
5	31	9	1	13	541	17.87	98		240	301	44.36	55.64
7	26	9	1	15	541	17.87	99		234	307	43.25	56.75
5	1	9	6	17	540	17.84	100		302	238	55.93	44.07
5	31	9	1	17	540	17.84	101	3027	259	281	47.96	52.04
5	30	9	7	16	531	17.54	102		289	242	54.43	45.57
5	9	9	7	18	530	17.51	103		218	312	41.13	58.87
5	30	9	7	14	529	17.48	104		319	210	60.3	39.7
5	30	9	7	13	528	17.44	105		335	193	63.45	36.55
5	2	9	7	15	527	17.41	106		238	289	45.16	54.84
5	8	9	6	20	524	17.31	107		353	171	67.37	32.63
5	22	9	6	10	523	17.28	108		288	235	55.07	44.93
5	26	9	3	12	521	17.21	109		211	310	40.5	59.5
8	2	9	1	15	521	17.21	110		308	213	59.12	40.88
5	3	9	1	12	520	17.18	111		220	300	42.31	57.69
5	3	9	1	18	520	17.18	112		189	331	36.35	63.65
5	16	9	7	17	519	17.15	113		244	275	47.01	52.99
5	21	9	5	15	517	17.08	114		250	267	48.36	51.64
7	26	9	1	14	515	17.01	115		260	255	50.49	49.51
5	31	9	1	19	514	16.98	116		195	319	37.94	62.06
5	2	9	7	14	511	16.88	117		243	268	47.55	52.45
5	13	9	4	15	511	16.88	118		230	281	45.01	54.99
5	29	9	6	12	511	16.88	119		268	243	52.45	47.55
5	31	9	1	18	511	16.88	120		221	290	43.25	56.75
7	5	9	1	16	511	16.88	121	3027	169	342	33.07	66.93

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
5	15	9	6	11	510	16.85	122		268	242	52.55	47.45
5	31	9	1	12	510	16.85	123		219	291	42.94	57.06
8	2	9	1	14	509	16.82	124		279	230	54.81	45.19
5	8	9	6	13	507	16.75	125		275	232	54.24	45.76
5	26	9	3	14	505	16.68	126		239	266	47.33	52.67
6	1	9	2	15	503	16.62	127		242	261	48.11	51.89
5	9	9	7	13	502	16.58	128		286	216	56.97	43.03
5	30	9	7	15	502	16.58	129		246	256	49	51
5	16	9	7	10	501	16.55	130		285	216	56.89	43.11
8	23	9	1	15	499	16.48	131		316	183	63.33	36.67
5	17	9	1	11	496	16.39	132		207	289	41.73	58.27
5	9	9	7	10	495	16.35	133		319	176	64.44	35.56
7	26	9	1	13	495	16.35	134		241	254	48.69	51.31
5	8	9	6	12	494	16.32	135		232	262	46.96	53.04
5	18	9	2	14	494	16.32	136		244	250	49.39	50.61
5	8	9	6	19	493	16.29	137		313	180	63.49	36.51
5	1	9	6	14	492	16.25	138		301	191	61.18	38.82
8	16	9	1	13	491	16.22	139		257	234	52.34	47.66
5	2	9	7	18	490	16.19	140		217	273	44.29	55.71
5	8	9	6	11	490	16.19	141	3027	247	243	50.41	49.59
5	26	9	3	16	490	16.19	142		213	277	43.47	56.53
5	29	9	6	18	489	16.15	143		259	230	52.97	47.03
5	15	9	6	20	487	16.09	144		317	170	65.09	34.91
7	3	9	6	13	487	16.09	145		304	183	62.42	37.58
5	30	9	7	11	486	16.06	146		274	212	56.38	43.62
5	1	9	6	19	485	16.02	147		328	157	67.63	32.37
5	16	9	7	18	485	16.02	148		241	244	49.69	50.31
5	14	9	5	15	484	15.99	149		214	270	44.21	55.79
5	26	9	3	10	484	15.99	150		209	275	43.18	56.82
8	16	9	1	14	483	15.96	151		232	251	48.03	51.97
5	2	9	7	12	482	15.92	152		275	207	57.05	42.95
5	18	9	2	15	482	15.92	153		234	248	48.55	51.45
5	21	9	5	14	481	15.89	154		280	201	58.21	41.79
5	13	9	4	14	480	15.86	155		200	280	41.67	58.33
5	24	9	1	10	480	15.86	156		298	182	62.08	37.92
5	21	9	5	17	478	15.79	157		253	225	52.93	47.07
7	3	9	6	14	477	15.76	158		317	160	66.46	33.54
5	26	9	3	13	476	15.73	159		222	254	46.64	53.36
5	26	9	3	15	476	15.73	160		212	264	44.54	55.46
7	19	9	1	15	476	15.73	161	3027	209	267	43.91	56.09
5	21	9	5	19	475	15.69	162		261	214	54.95	45.05
5	27	9	4	11	475	15.69	163		231	244	48.63	51.37
7	26	9	1	17	474	15.66	164		177	297	37.34	62.66
5	6	9	4	15	473	15.63	165		197	276	41.65	58.35
5	14	9	5	16	472	15.59	166		252	220	53.39	46.61
5	1	9	6	12	471	15.56	167		268	203	56.9	43.1
5	18	9	2	11	471	15.56	168		218	253	46.28	53.72
5	1	9	6	20	469	15.49	169		276	193	58.85	41.15
7	3	9	6	15	469	15.49	170		273	196	58.21	41.79
5	26	9	3	11	467	15.43	171		205	262	43.9	56.1
7	18	9	7	12	467	15.43	172		286	181	61.24	38.76
5	11	9	2	15	465	15.36	173		211	254	45.38	54.62

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
5	11	9	2	16	465	15.36	174		214	251	46.02	53.98
5	23	9	7	9	465	15.36	175		306	159	65.81	34.19
5	30	9	7	10	464	15.33	176		263	201	56.68	43.32
7	19	9	1	13	464	15.33	177		201	263	43.32	56.68
5	28	9	5	16	463	15.3	178		234	229	50.54	49.46
5	10	9	1	20	462	15.26	179		171	291	37.01	62.99
8	2	9	1	16	462	15.26	180		271	191	58.66	41.34
5	21	9	5	12	460	15.2	181	3027	241	219	52.39	47.61
5	29	9	6	11	460	15.2	182		266	194	57.83	42.17
5	14	9	5	11	459	15.16	183		211	248	45.97	54.03
7	19	9	1	14	458	15.13	184		219	239	47.82	52.18
5	20	9	4	15	457	15.1	185		238	219	52.08	47.92
5	29	9	6	20	457	15.1	186		266	191	58.21	41.79
7	3	9	6	12	457	15.1	187		272	185	59.52	40.48
5	2	9	7	17	456	15.06	188		184	272	40.35	59.65
5	21	9	5	13	456	15.06	189		236	220	51.75	48.25
5	16	9	7	19	455	15.03	190		170	285	37.36	62.64
8	9	9	1	15	455	15.03	191		274	181	60.22	39.78
5	1	9	6	13	453	14.97	192		263	190	58.06	41.94
5	13	9	4	16	452	14.93	193		187	265	41.37	58.63
7	4	9	7	13	452	14.93	194		268	184	59.29	40.71
8	16	9	1	16	452	14.93	195		256	196	56.64	43.36
5	26	9	3	17	451	14.9	196		220	231	48.78	51.22
7	5	9	1	12	451	14.9	197		152	299	33.7	66.3
5	28	9	5	15	450	14.87	198		190	260	42.22	57.78
5	7	9	5	15	449	14.83	199		202	247	44.99	55.01
5	9	9	7	9	449	14.83	200		278	171	61.92	38.08

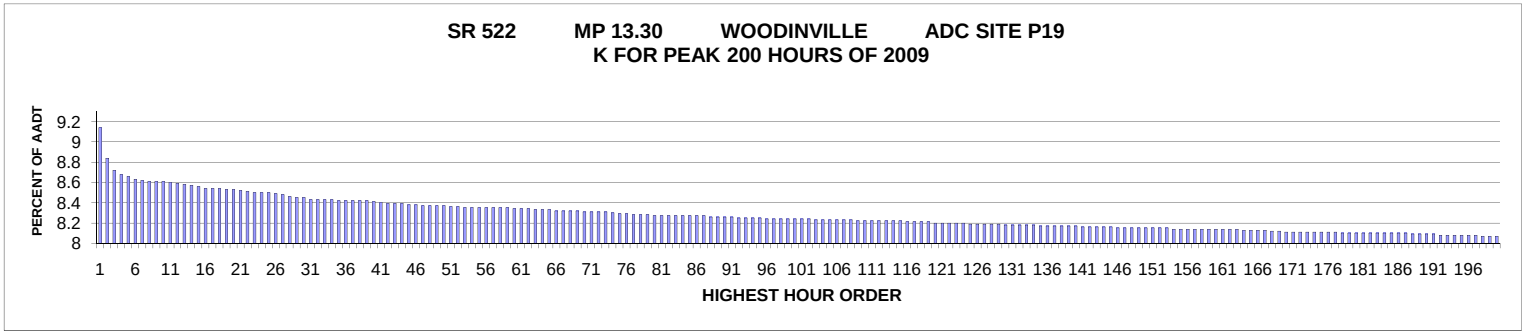

AADT= 45644 **K 30 FACTOR=** 8.45 **K 100 FACTOR=** 8.24 **K 200 FACTOR=** 8.07 **D FACTOR=** 65.85

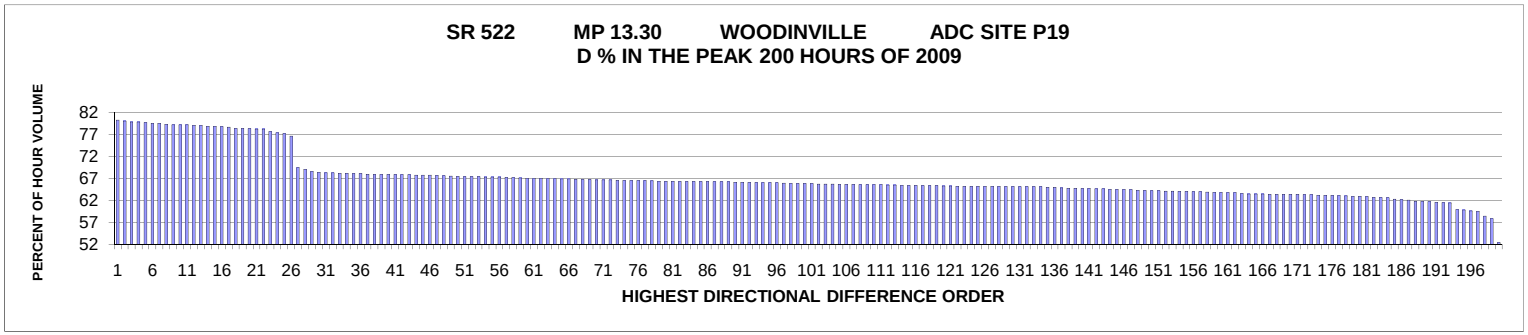

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	28	9	6	16	4172	9.14	1	45644	2481	1691	59.47	40.53
8	27	9	5	17	4037	8.84	2		2591	1446	64.18	35.82
8	28	9	6	17	3981	8.72	3		2520	1461	63.3	36.7
8	14	9	6	16	3963	8.68	4		2520	1443	63.59	36.41
9	25	9	6	16	3953	8.66	5		2496	1457	63.14	36.86
8	13	9	5	17	3938	8.63	6		2565	1373	65.13	34.87
8	14	9	6	17	3936	8.62	7		2587	1349	65.73	34.27
9	18	9	6	16	3932	8.61	8		2465	1467	62.69	37.31
9	3	9	5	17	3929	8.61	9		2508	1421	63.83	36.17
12	18	9	6	16	3929	8.61	10		2471	1458	62.89	37.11
9	22	9	3	8	3925	8.6	11		838	3087	21.35	78.65
9	1	9	3	17	3921	8.59	12		2590	1331	66.05	33.95
9	10	9	5	16	3917	8.58	13		2479	1438	63.29	36.71
10	2	9	6	17	3910	8.57	14		2597	1313	66.42	33.58
12	23	9	4	16	3906	8.56	15		2432	1474	62.26	37.74
10	30	9	6	16	3900	8.54	16		2504	1396	64.21	35.79
10	9	9	6	17	3899	8.54	17		2550	1349	65.4	34.6

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
9	11	9	6	16	3898	8.54	18		2523	1375	64.73	35.27
12	23	9	4	17	3894	8.53	19		2466	1428	63.33	36.67
1	16	9	6	16	3893	8.53	20		2535	1358	65.12	34.88
9	17	9	5	17	3890	8.52	21	45644	2592	1298	66.63	33.37
1	30	9	6	16	3883	8.51	22		2531	1352	65.18	34.82
10	9	9	6	16	3881	8.5	23		2486	1395	64.06	35.94
8	27	9	5	16	3880	8.5	24		2462	1418	63.45	36.55
12	22	9	3	17	3880	8.5	25		2458	1422	63.35	36.65
9	1	9	3	16	3874	8.49	26		2427	1447	62.65	37.35
10	2	9	6	16	3871	8.48	27		2473	1398	63.89	36.11
9	4	9	6	16	3860	8.46	28		2517	1343	65.21	34.79
1	15	9	5	17	3857	8.45	29		2590	1267	67.15	32.85
8	7	9	6	16	3857	8.45	30		2467	1390	63.96	36.04
5	15	9	6	16	3850	8.43	31		2467	1383	64.08	35.92
9	11	9	6	17	3849	8.43	32		2482	1367	64.48	35.52
9	14	9	2	17	3848	8.43	33		2588	1260	67.26	32.74
8	28	9	6	15	3846	8.43	34		2301	1545	59.83	40.17
8	26	9	4	17	3844	8.42	35		2549	1295	66.31	33.69
10	8	9	5	17	3844	8.42	36		2549	1295	66.31	33.69
9	24	9	5	8	3843	8.42	37		810	3033	21.08	78.92
2	5	9	5	16	3842	8.42	38		2540	1302	66.11	33.89
9	2	9	4	17	3842	8.42	39		2566	1276	66.79	33.21
9	17	9	5	8	3838	8.41	40		802	3036	20.9	79.1
10	1	9	5	16	3834	8.4	41	45644	2512	1322	65.52	34.48
8	7	9	6	17	3831	8.39	42		2510	1321	65.52	34.48
9	28	9	2	17	3830	8.39	43		2577	1253	67.28	32.72
9	30	9	4	17	3828	8.39	44		2586	1242	67.55	32.45
7	2	9	5	17	3827	8.38	45		2561	1266	66.92	33.08
9	23	9	4	17	3825	8.38	46		2538	1287	66.35	33.65
6	5	9	6	17	3821	8.37	47		2541	1280	66.5	33.5
10	7	9	4	8	3820	8.37	48		809	3011	21.18	78.82
7	24	9	6	17	3819	8.37	49		2545	1274	66.64	33.36
8	13	9	5	16	3819	8.37	50		2347	1472	61.46	38.54
8	6	9	5	17	3814	8.36	51		2551	1263	66.89	33.11
9	4	9	6	17	3814	8.36	52		2537	1277	66.52	33.48
5	21	9	5	17	3813	8.35	53		2556	1257	67.03	32.97
3	18	9	4	17	3811	8.35	54		2498	1313	65.55	34.45
9	29	9	3	8	3810	8.35	55		792	3018	20.79	79.21
7	23	9	5	17	3809	8.35	56		2512	1297	65.95	34.05
9	9	9	4	17	3809	8.35	57		2458	1351	64.53	35.47
9	16	9	4	8	3809	8.35	58		823	2986	21.61	78.39
10	5	9	2	16	3809	8.35	59		2482	1327	65.16	34.84
2	27	9	6	16	3808	8.34	60		2415	1393	63.42	36.58
9	15	9	3	8	3808	8.34	61	45644	826	2982	21.69	78.31
9	18	9	6	17	3807	8.34	62		2454	1353	64.46	35.54
9	16	9	4	17	3802	8.33	63		2547	1255	66.99	33.01
3	26	9	5	17	3801	8.33	64		2470	1331	64.98	35.02
9	10	9	5	17	3800	8.33	65		2484	1316	65.37	34.63
9	3	9	5	16	3798	8.32	66		2421	1377	63.74	36.26
12	21	9	2	17	3797	8.32	67		2559	1238	67.4	32.6
9	2	9	4	16	3796	8.32	68		2476	1320	65.23	34.77
10	8	9	5	16	3796	8.32	69		2404	1392	63.33	36.67

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	9	9	5	17	3793	8.31	70		2543	1250	67.04	32.96
10	6	9	3	16	3793	8.31	71		2496	1297	65.81	34.19
9	15	9	3	17	3791	8.31	72		2472	1319	65.21	34.79
10	22	9	5	17	3791	8.31	73		2503	1288	66.02	33.98
8	12	9	4	17	3790	8.3	74		2530	1260	66.75	33.25
9	21	9	2	17	3785	8.29	75		2584	1201	68.27	31.73
10	28	9	4	16	3784	8.29	76		2473	1311	65.35	34.65
8	21	9	6	16	3779	8.28	77		2409	1370	63.75	36.25
12	2	9	4	17	3779	8.28	78		2482	1297	65.68	34.32
7	24	9	6	16	3778	8.28	79		2447	1331	64.77	35.23
9	23	9	4	8	3777	8.27	80		786	2991	20.81	79.19
9	8	9	3	17	3775	8.27	81	45644	2560	1215	67.81	32.19
9	10	9	5	8	3775	8.27	82		844	2931	22.36	77.64
10	20	9	3	8	3775	8.27	83		785	2990	20.79	79.21
2	12	9	5	16	3774	8.27	84		2461	1313	65.21	34.79
11	3	9	3	8	3774	8.27	85		771	3003	20.43	79.57
11	4	9	4	8	3774	8.27	86		743	3031	19.69	80.31
12	4	9	6	17	3773	8.27	87		2475	1298	65.6	34.4
1	20	9	3	17	3772	8.26	88		2560	1212	67.87	32.13
8	31	9	2	17	3769	8.26	89		2376	1393	63.04	36.96
9	24	9	5	17	3769	8.26	90		2486	1283	65.96	34.04
6	2	9	3	16	3768	8.26	91		2433	1335	64.57	35.43
12	11	9	6	17	3767	8.25	92		2417	1350	64.16	35.84
2	20	9	6	16	3766	8.25	93		2436	1330	64.68	35.32
5	18	9	2	16	3766	8.25	94		2377	1389	63.12	36.88
9	23	9	4	16	3764	8.25	95		2371	1393	62.99	37.01
7	22	9	4	17	3762	8.24	96		2503	1259	66.53	33.47
8	19	9	4	17	3761	8.24	97		2507	1254	66.66	33.34
10	7	9	4	17	3761	8.24	98		2534	1227	67.38	32.62
9	30	9	4	16	3760	8.24	99		2407	1353	64.02	35.98
6	9	9	3	17	3759	8.24	100		2541	1218	67.6	32.4
10	7	9	4	16	3759	8.24	101	45644	2386	1373	63.47	36.53
10	22	9	5	16	3759	8.24	102		2365	1394	62.92	37.08
10	20	9	3	17	3758	8.23	103		2562	1196	68.17	31.83
5	20	9	4	16	3757	8.23	104		2445	1312	65.08	34.92
9	8	9	3	16	3756	8.23	105		2396	1360	63.79	36.21
10	5	9	2	17	3756	8.23	106		2502	1254	66.61	33.39
5	29	9	6	16	3755	8.23	107		2446	1309	65.14	34.86
9	30	9	4	8	3755	8.23	108		757	2998	20.16	79.84
5	26	9	3	16	3754	8.22	109		2424	1330	64.57	35.43
2	13	9	6	17	3752	8.22	110		2541	1211	67.72	32.28
3	13	9	6	17	3751	8.22	111		2478	1273	66.06	33.94
5	22	9	6	15	3751	8.22	112		2304	1447	61.42	38.58
10	15	9	5	16	3751	8.22	113		2376	1375	63.34	36.66
7	21	9	3	17	3750	8.22	114		2547	1203	67.92	32.08
9	15	9	3	16	3750	8.22	115		2399	1351	63.97	36.03
3	27	9	6	16	3748	8.21	116		2415	1333	64.43	35.57
9	22	9	3	18	3747	8.21	117		2483	1264	66.27	33.73
7	17	9	6	17	3746	8.21	118		2483	1263	66.28	33.72
9	25	9	6	17	3746	8.21	119		2506	1240	66.9	33.1
9	8	9	3	18	3745	8.2	120		2599	1146	69.4	30.6
5	20	9	4	17	3744	8.2	121	45644	2506	1238	66.93	33.07

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
6	29	9	2	17	3744	8.2	122		2480	1264	66.24	33.76
1	16	9	6	17	3743	8.2	123		2478	1265	66.2	33.8
10	12	9	2	17	3742	8.2	124		2518	1224	67.29	32.71
6	1	9	2	16	3739	8.19	125		2438	1301	65.2	34.8
9	11	9	6	8	3739	8.19	126		873	2866	23.35	76.65
6	1	9	2	17	3737	8.19	127		2535	1202	67.84	32.16
6	10	9	4	16	3736	8.19	128		2460	1276	65.85	34.15
6	25	9	5	17	3736	8.19	129		2531	1205	67.75	32.25
6	9	9	3	16	3734	8.18	130		2444	1290	65.45	34.55
7	17	9	6	16	3734	8.18	131		2478	1256	66.36	33.64
11	12	9	5	8	3734	8.18	132		752	2982	20.14	79.86
1	22	9	5	17	3733	8.18	133		2525	1208	67.64	32.36
11	13	9	6	17	3732	8.18	134		2482	1250	66.51	33.49
6	26	9	6	17	3731	8.17	135		2514	1217	67.38	32.62
8	5	9	4	17	3731	8.17	136		2502	1229	67.06	32.94
1	23	9	6	16	3730	8.17	137		2441	1289	65.44	34.56
5	18	9	2	17	3730	8.17	138		2545	1185	68.23	31.77
5	14	9	5	16	3729	8.17	139		2412	1317	64.68	35.32
12	17	9	5	16	3727	8.17	140		2299	1428	61.69	38.31
7	16	9	5	17	3725	8.16	141	45644	2445	1280	65.64	34.36
10	6	9	3	17	3725	8.16	142		2459	1266	66.01	33.99
3	6	9	6	16	3724	8.16	143		2329	1395	62.54	37.46
8	24	9	2	17	3724	8.16	144		2513	1211	67.48	32.52
12	22	9	3	16	3724	8.16	145		2218	1506	59.56	40.44
8	27	9	5	18	3722	8.15	146		2423	1299	65.1	34.9
12	1	9	3	17	3722	8.15	147		2443	1279	65.64	34.36
12	17	9	5	17	3722	8.15	148		2419	1303	64.99	35.01
6	3	9	4	17	3720	8.15	149		2529	1191	67.98	32.02
8	25	9	3	17	3720	8.15	150		2533	1187	68.09	31.91
9	17	9	5	16	3720	8.15	151		2350	1370	63.17	36.83
1	30	9	6	17	3719	8.15	152		2428	1291	65.29	34.71
12	22	9	3	18	3719	8.15	153		2449	1270	65.85	34.15
1	15	9	5	16	3717	8.14	154		2442	1275	65.7	34.3
3	26	9	5	16	3717	8.14	155		2339	1378	62.93	37.07
6	9	9	3	8	3717	8.14	156		760	2957	20.45	79.55
10	10	9	7	13	3716	8.14	157		1946	1770	52.37	47.63
11	5	9	5	8	3716	8.14	158		742	2974	19.97	80.03
2	27	9	6	17	3715	8.14	159		2378	1337	64.01	35.99
5	15	9	6	15	3715	8.14	160		2222	1493	59.81	40.19
9	28	9	2	8	3715	8.14	161	45644	777	2938	20.92	79.08
10	8	9	5	8	3715	8.14	162		808	2907	21.75	78.25
1	14	9	4	16	3714	8.14	163		2408	1306	64.84	35.16
8	14	9	6	15	3713	8.13	164		2170	1543	58.44	41.56
12	11	9	6	16	3713	8.13	165		2292	1421	61.73	38.27
9	21	9	2	18	3712	8.13	166		2546	1166	68.59	31.41
9	2	9	4	8	3709	8.13	167		782	2927	21.08	78.92
11	3	9	3	17	3707	8.12	168		2516	1191	67.87	32.13
8	4	9	3	17	3706	8.12	169		2510	1196	67.73	32.27
10	13	9	3	8	3704	8.11	170		751	2953	20.28	79.72
12	30	9	4	17	3703	8.11	171		2278	1425	61.52	38.48
6	8	9	2	17	3701	8.11	172		2531	1170	68.39	31.61
6	30	9	3	17	3701	8.11	173		2457	1244	66.39	33.61

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
9	9	9	4	8	3701	8.11	174		838	2863	22.64	77.36
2	19	9	5	16	3700	8.11	175		2469	1231	66.73	33.27
9	18	9	6	15	3700	8.11	176		2139	1561	57.81	42.19
11	4	9	4	17	3700	8.11	177		2453	1247	66.3	33.7
10	12	9	2	16	3699	8.1	178		2295	1404	62.04	37.96
2	3	9	3	16	3698	8.1	179		2447	1251	66.17	33.83
6	8	9	2	16	3698	8.1	180		2420	1278	65.44	34.56
7	29	9	4	8	3698	8.1	181	45644	804	2894	21.74	78.26
10	1	9	5	17	3698	8.1	182		2448	1250	66.2	33.8
6	11	9	5	17	3697	8.1	183		2517	1180	68.08	31.92
9	1	9	3	18	3696	8.1	184		2434	1262	65.85	34.15
1	29	9	5	16	3695	8.1	185		2423	1272	65.58	34.42
7	22	9	4	16	3695	8.1	186		2340	1355	63.33	36.67
8	11	9	3	18	3695	8.1	187		2518	1177	68.15	31.85
3	26	9	5	18	3694	8.09	188		2407	1287	65.16	34.84
11	12	9	5	17	3694	8.09	189		2413	1281	65.32	34.68
2	2	9	2	16	3693	8.09	190		2417	1276	65.45	34.55
5	28	9	5	8	3691	8.09	191		797	2894	21.59	78.41
3	4	9	4	17	3689	8.08	192		2547	1142	69.04	30.96
11	13	9	6	16	3689	8.08	193		2278	1411	61.75	38.25
9	25	9	6	8	3688	8.08	194		840	2848	22.78	77.22
3	27	9	6	17	3687	8.08	195		2401	1286	65.12	34.88
8	11	9	3	17	3687	8.08	196		2504	1183	67.91	32.09
10	6	9	3	8	3687	8.08	197		761	2926	20.64	79.36
6	5	9	6	16	3685	8.07	198		2369	1316	64.29	35.71
11	23	9	2	16	3685	8.07	199		2288	1397	62.09	37.91
8	21	9	6	17	3684	8.07	200		2479	1205	67.29	32.71

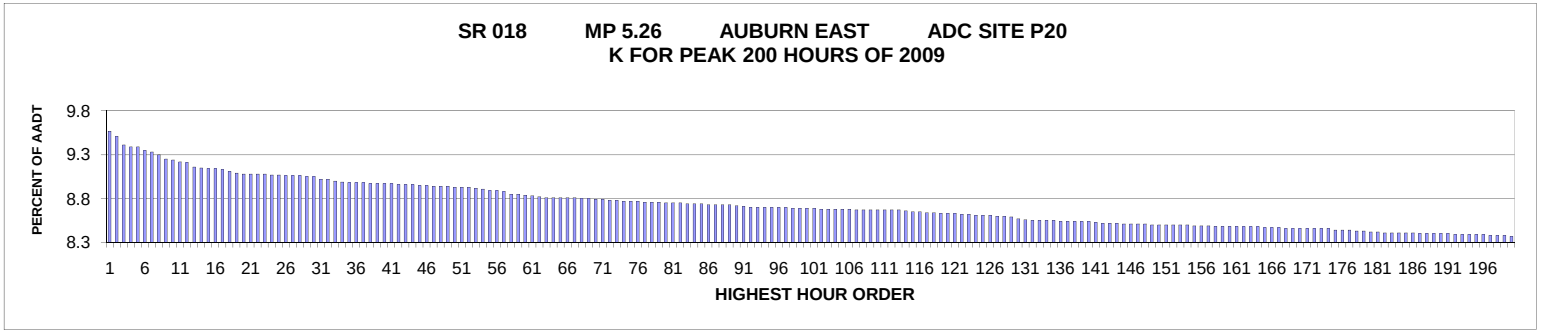

AADT= 55239 **K 30 FACTOR=** 9.05 **K 100 FACTOR=** 8.69 **K 200 FACTOR=** 8.37 **D FACTOR=** 52.49

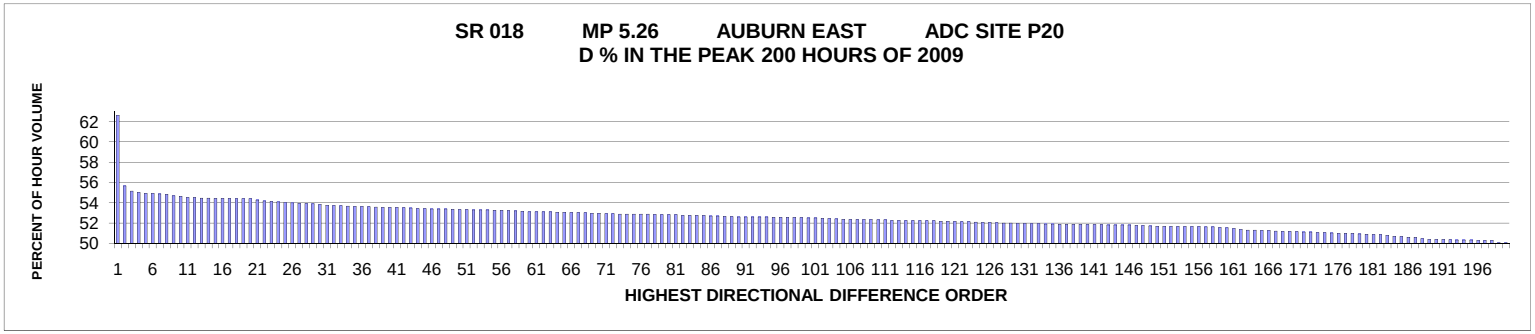

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
5	15	9	6	17	5287	9.57	1	55239	2697	2590	51.01	48.99
5	15	9	6	18	5251	9.51	2		2762	2489	52.6	47.4
6	12	9	6	17	5197	9.41	3		2630	2567	50.61	49.39
7	17	9	6	18	5189	9.39	4		2553	2636	49.2	50.8
5	29	9	6	17	5188	9.39	5		2694	2494	51.93	48.07
8	14	9	6	17	5166	9.35	6		2655	2511	51.39	48.61
7	24	9	6	17	5152	9.33	7		2744	2408	53.26	46.74
6	12	9	6	18	5139	9.3	8		2717	2422	52.87	47.13
8	7	9	6	17	5108	9.25	9		2649	2459	51.86	48.14
6	12	9	6	16	5104	9.24	10		2707	2397	53.04	46.96
10	9	9	6	17	5095	9.22	11		2583	2512	50.7	49.3
6	19	9	6	17	5086	9.21	12		2740	2346	53.87	46.13
6	5	9	6	17	5058	9.16	13		2588	2470	51.17	48.83
5	8	9	6	17	5056	9.15	14		2650	2406	52.41	47.59
4	24	9	6	17	5049	9.14	15		2589	2460	51.28	48.72
9	11	9	6	17	5047	9.14	16		2572	2475	50.96	49.04
7	10	9	6	17	5045	9.13	17		2629	2416	52.11	47.89

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
5	1	9	6	17	5032	9.11	18		2650	2382	52.66	47.34
5	22	9	6	17	5019	9.09	19		2687	2332	53.54	46.46
7	2	9	5	17	5018	9.08	20		2634	2384	52.49	47.51
5	1	9	6	16	5017	9.08	21	55239	2652	2365	52.86	47.14
9	25	9	6	17	5014	9.08	22		2564	2450	51.14	48.86
5	8	9	6	18	5013	9.08	23		2622	2391	52.3	47.7
12	18	9	6	17	5011	9.07	24		2507	2504	50.03	49.97
7	17	9	6	16	5008	9.07	25		2563	2445	51.18	48.82
5	8	9	6	16	5005	9.06	26		2682	2323	53.59	46.41
7	16	9	5	17	5004	9.06	27		2630	2374	52.56	47.44
7	17	9	6	17	5004	9.06	28		2562	2442	51.2	48.8
5	15	9	6	16	5000	9.05	29		2629	2371	52.58	47.42
7	24	9	6	16	4999	9.05	30		2662	2337	53.25	46.75
8	6	9	5	17	4985	9.02	31		2506	2479	50.27	49.73
8	14	9	6	18	4981	9.02	32		2588	2393	51.96	48.04
4	17	9	6	17	4972	9	33		2540	2432	51.09	48.91
2	13	9	6	17	4967	8.99	34		2461	2506	49.55	50.45
6	11	9	5	17	4962	8.98	35		2497	2465	50.32	49.68
8	14	9	6	16	4961	8.98	36		2563	2398	51.66	48.34
9	18	9	6	17	4958	8.98	37		2570	2388	51.84	48.16
5	1	9	6	18	4957	8.97	38		2646	2311	53.38	46.62
10	30	9	6	17	4957	8.97	39		2615	2342	52.75	47.25
9	18	9	6	16	4956	8.97	40		2619	2337	52.85	47.15
10	8	9	5	17	4954	8.97	41	55239	2613	2341	52.75	47.25
6	5	9	6	18	4952	8.96	42		2643	2309	53.37	46.63
4	3	9	6	17	4949	8.96	43		2556	2393	51.65	48.35
6	26	9	6	16	4947	8.96	44		2583	2364	52.21	47.79
5	22	9	6	16	4946	8.95	45		2652	2294	53.62	46.38
7	31	9	6	17	4945	8.95	46		2625	2320	53.08	46.92
3	13	9	6	17	4941	8.94	47		2551	2390	51.63	48.37
9	25	9	6	18	4938	8.94	48		2689	2249	54.46	45.54
9	17	9	5	17	4936	8.94	49		2578	2358	52.23	47.77
6	5	9	6	16	4935	8.93	50		2510	2425	50.86	49.14
9	11	9	6	16	4935	8.93	51		2576	2359	52.2	47.8
6	19	9	6	18	4931	8.93	52		2683	2248	54.41	45.59
3	27	9	6	17	4926	8.92	53		2636	2290	53.51	46.49
7	24	9	6	18	4923	8.91	54		2701	2222	54.86	45.14
7	10	9	6	16	4912	8.89	55		2470	2442	50.29	49.71
6	26	9	6	18	4909	8.89	56		2544	2365	51.82	48.18
6	19	9	6	16	4907	8.88	57		2611	2296	53.21	46.79
6	18	9	5	17	4889	8.85	58		2496	2393	51.05	48.95
6	4	9	5	17	4886	8.85	59		2564	2322	52.48	47.52
6	11	9	5	18	4882	8.84	60		2549	2333	52.21	47.79
8	21	9	6	17	4875	8.83	61	55239	2525	2350	51.79	48.21
6	18	9	5	18	4871	8.82	62		2544	2327	52.23	47.77
5	21	9	5	17	4868	8.81	63		2479	2389	50.92	49.08
8	7	9	6	16	4868	8.81	64		2518	2350	51.73	48.27
5	29	9	6	16	4866	8.81	65		2551	2315	52.42	47.58
6	26	9	6	17	4866	8.81	66		2503	2363	51.44	48.56
7	31	9	6	16	4866	8.81	67		2448	2418	50.31	49.69
8	21	9	6	16	4862	8.8	68		2557	2305	52.59	47.41
10	2	9	6	17	4862	8.8	69		2571	2291	52.88	47.12

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	10	9	6	18	4857	8.79	70		2614	2243	53.82	46.18
3	20	9	6	17	4853	8.79	71		2586	2267	53.29	46.71
8	13	9	5	17	4850	8.78	72		2620	2230	54.02	45.98
10	9	9	6	16	4849	8.78	73		2572	2277	53.04	46.96
4	24	9	6	16	4847	8.77	74		2410	2437	49.72	50.28
9	11	9	6	18	4844	8.77	75		2590	2254	53.47	46.53
10	1	9	5	17	4843	8.77	76		2502	2341	51.66	48.34
7	23	9	5	17	4841	8.76	77		2570	2271	53.09	46.91
4	24	9	6	18	4840	8.76	78		2545	2295	52.58	47.42
2	27	9	6	17	4837	8.76	79		2466	2371	50.98	49.02
7	2	9	5	18	4834	8.75	80		2660	2174	55.03	44.97
8	19	9	4	18	4831	8.75	81	55239	2593	2238	53.67	46.33
9	4	9	6	17	4831	8.75	82		2627	2204	54.38	45.62
9	3	9	5	17	4829	8.74	83		2566	2263	53.14	46.86
8	27	9	5	17	4828	8.74	84		2520	2308	52.2	47.8
2	6	9	6	17	4826	8.74	85		2503	2323	51.86	48.14
7	9	9	5	17	4824	8.73	86		2511	2313	52.05	47.95
7	16	9	5	18	4823	8.73	87		2624	2199	54.41	45.59
4	3	9	6	16	4822	8.73	88		2565	2257	53.19	46.81
3	6	9	6	17	4820	8.73	89		2472	2348	51.29	48.71
8	19	9	4	17	4818	8.72	90		2498	2320	51.85	48.15
5	21	9	5	18	4813	8.71	91		2538	2275	52.73	47.27
8	21	9	6	18	4808	8.7	92		2546	2262	52.95	47.05
3	13	9	6	18	4806	8.7	93		2402	2404	49.98	50.02
4	16	9	5	17	4806	8.7	94		2481	2325	51.62	48.38
5	29	9	6	18	4806	8.7	95		2560	2246	53.27	46.73
7	7	9	3	17	4804	8.7	96		2474	2330	51.5	48.5
7	31	9	6	18	4804	8.7	97		2526	2278	52.58	47.42
10	16	9	6	17	4799	8.69	98		2560	2239	53.34	46.66
1	23	9	6	17	4798	8.69	99		2485	2313	51.79	48.21
8	20	9	5	17	4798	8.69	100		2487	2311	51.83	48.17
10	7	9	4	17	4798	8.69	101	55239	2536	2262	52.86	47.14
7	2	9	5	16	4796	8.68	102		2459	2337	51.27	48.73
1	16	9	6	17	4794	8.68	103		2429	2365	50.67	49.33
7	15	9	4	17	4792	8.68	104		2492	2300	52	48
8	28	9	6	18	4792	8.68	105		2594	2198	54.13	45.87
10	15	9	5	17	4792	8.68	106		2554	2238	53.3	46.7
4	10	9	6	17	4791	8.67	107		2590	2201	54.06	45.94
10	22	9	5	17	4791	8.67	108		2535	2256	52.91	47.09
8	5	9	4	17	4790	8.67	109		2507	2283	52.34	47.66
8	28	9	6	16	4790	8.67	110		2480	2310	51.77	48.23
9	18	9	6	18	4788	8.67	111		2536	2252	52.97	47.03
10	2	9	6	16	4788	8.67	112		2585	2203	53.99	46.01
8	6	9	5	18	4787	8.67	113		2597	2190	54.25	45.75
1	30	9	6	17	4781	8.66	114		2512	2269	52.54	47.46
8	28	9	6	17	4780	8.65	115		2480	2300	51.88	48.12
2	13	9	6	18	4779	8.65	116		2487	2292	52.04	47.96
3	27	9	6	16	4771	8.64	117		2507	2264	52.55	47.45
7	29	9	4	17	4771	8.64	118		2559	2212	53.64	46.36
6	10	9	4	17	4769	8.63	119		2471	2298	51.81	48.19
7	16	9	5	16	4769	8.63	120		2471	2298	51.81	48.19
9	4	9	6	16	4766	8.63	121	55239	2598	2168	54.51	45.49

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	30	9	5	17	4763	8.62	122		2612	2151	54.84	45.16
7	17	9	6	15	4759	8.62	123		2491	2268	52.34	47.66
5	28	9	5	17	4758	8.61	124		2470	2288	51.91	48.09
8	31	9	2	17	4757	8.61	125		2469	2288	51.9	48.1
10	23	9	6	17	4755	8.61	126		2476	2279	52.07	47.93
9	24	9	5	18	4751	8.6	127		2506	2245	52.75	47.25
9	24	9	5	17	4749	8.6	128		2502	2247	52.68	47.32
6	25	9	5	17	4747	8.59	129		2462	2285	51.86	48.14
9	21	9	2	17	4733	8.57	130		2446	2287	51.68	48.32
5	20	9	4	17	4727	8.56	131		2480	2247	52.46	47.54
9	16	9	4	18	4725	8.55	132		2411	2314	51.03	48.97
4	17	9	6	18	4723	8.55	133		2442	2281	51.7	48.3
10	6	9	3	17	4722	8.55	134		2460	2262	52.1	47.9
8	20	9	5	18	4721	8.55	135		2506	2215	53.08	46.92
8	5	9	4	18	4719	8.54	136		2566	2153	54.38	45.62
10	2	9	6	18	4719	8.54	137		2566	2153	54.38	45.62
8	12	9	4	17	4717	8.54	138		2519	2198	53.4	46.6
5	28	9	5	18	4716	8.54	139		2491	2225	52.82	47.18
6	25	9	5	18	4716	8.54	140		2524	2192	53.52	46.48
8	26	9	4	17	4711	8.53	141	55239	2510	2201	53.28	46.72
5	27	9	4	17	4708	8.52	142		2446	2262	51.95	48.05
2	13	9	6	16	4707	8.52	143		2399	2308	50.97	49.03
12	11	9	6	17	4705	8.52	144		2429	2276	51.63	48.37
7	14	9	3	17	4703	8.51	145		2484	2219	52.82	47.18
8	14	9	6	15	4703	8.51	146		2427	2276	51.61	48.39
9	25	9	6	16	4703	8.51	147		2312	2391	49.16	50.84
10	9	9	6	18	4699	8.51	148		2592	2107	55.16	44.84
3	26	9	5	17	4698	8.5	149		2444	2254	52.02	47.98
7	23	9	5	18	4698	8.5	150		2535	2163	53.96	46.04
5	7	9	5	17	4697	8.5	151		2514	2183	53.52	46.48
7	1	9	4	18	4697	8.5	152		2484	2213	52.88	47.12
7	18	9	7	18	4694	8.5	153		1754	2940	37.37	62.63
9	15	9	3	17	4694	8.5	154		2457	2237	52.34	47.66
2	20	9	6	17	4691	8.49	155		2468	2223	52.61	47.39
6	10	9	4	18	4689	8.49	156		2363	2326	50.39	49.61
7	22	9	4	17	4689	8.49	157		2488	2201	53.06	46.94
7	1	9	4	17	4687	8.48	158		2480	2207	52.91	47.09
4	17	9	6	16	4686	8.48	159		2445	2241	52.18	47.82
5	22	9	6	15	4686	8.48	160		2445	2241	52.18	47.82
9	23	9	4	17	4685	8.48	161	55239	2414	2271	51.53	48.47
6	17	9	4	18	4684	8.48	162		2606	2078	55.64	44.36
7	31	9	6	15	4684	8.48	163		2360	2324	50.38	49.62
7	15	9	4	18	4682	8.48	164		2501	2181	53.42	46.58
9	17	9	5	18	4681	8.47	165		2484	2197	53.07	46.93
7	22	9	4	18	4678	8.47	166		2570	2108	54.94	45.06
9	30	9	4	17	4678	8.47	167		2443	2235	52.22	47.78
5	22	9	6	18	4675	8.46	168		2567	2108	54.91	45.09
6	21	9	1	14	4675	8.46	169		2229	2446	47.68	52.32
4	30	9	5	17	4674	8.46	170		2509	2165	53.68	46.32
6	9	9	3	17	4673	8.46	171		2468	2205	52.81	47.19
7	7	9	3	18	4673	8.46	172		2481	2192	53.09	46.91
9	22	9	3	17	4672	8.46	173		2353	2319	50.36	49.64

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
6	24	9	4	17	4671	8.46	174		2446	2225	52.37	47.63
10	30	9	6	18	4664	8.44	175		2550	2114	54.67	45.33
8	7	9	6	18	4662	8.44	176		2456	2206	52.68	47.32
9	16	9	4	17	4662	8.44	177		2346	2316	50.32	49.68
4	15	9	4	17	4659	8.43	178		2381	2278	51.11	48.89
6	3	9	4	17	4655	8.43	179		2501	2154	53.73	46.27
7	9	9	5	18	4651	8.42	180		2519	2132	54.16	45.84
8	20	9	5	16	4651	8.42	181	55239	2341	2310	50.33	49.67
9	2	9	4	17	4648	8.41	182		2490	2158	53.57	46.43
9	3	9	5	18	4648	8.41	183		2531	2117	54.45	45.55
9	1	9	3	17	4647	8.41	184		2477	2170	53.3	46.7
6	8	9	2	17	4646	8.41	185		2505	2141	53.92	46.08
12	23	9	4	17	4646	8.41	186		2430	2216	52.3	47.7
10	8	9	5	18	4642	8.4	187		2526	2116	54.42	45.58
6	9	9	3	18	4641	8.4	188		2530	2111	54.51	45.49
6	11	9	5	16	4641	8.4	189		2348	2293	50.59	49.41
4	23	9	5	17	4640	8.4	190		2413	2227	52	48
3	6	9	6	18	4638	8.4	191		2377	2261	51.25	48.75
10	23	9	6	18	4637	8.39	192		2533	2104	54.63	45.37
8	26	9	4	18	4636	8.39	193		2475	2161	53.39	46.61
3	6	9	6	16	4634	8.39	194		2436	2198	52.57	47.43
6	2	9	3	17	4632	8.39	195		2415	2217	52.14	47.86
12	17	9	5	17	4632	8.39	196		2357	2275	50.89	49.11
6	17	9	4	17	4629	8.38	197		2431	2198	52.52	47.48
12	11	9	6	16	4628	8.38	198		2453	2175	53	47
12	18	9	6	16	4627	8.38	199		2487	2140	53.75	46.25
10	29	9	5	17	4625	8.37	200		2388	2237	51.63	48.37

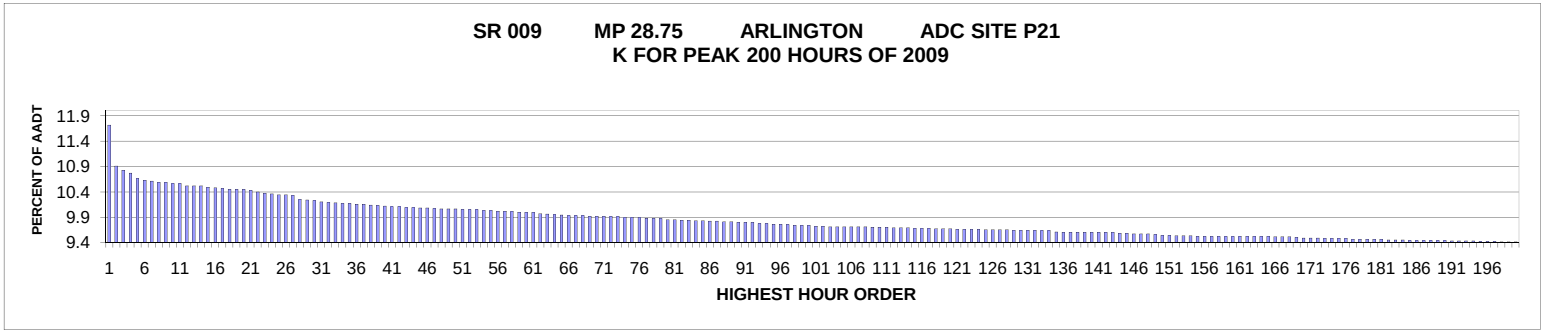

AADT= 11245 **K 30 FACTOR=** 10.23 **K 100 FACTOR=** 9.74 **K 200 FACTOR=** 9.41 **D FACTOR=** 58.02

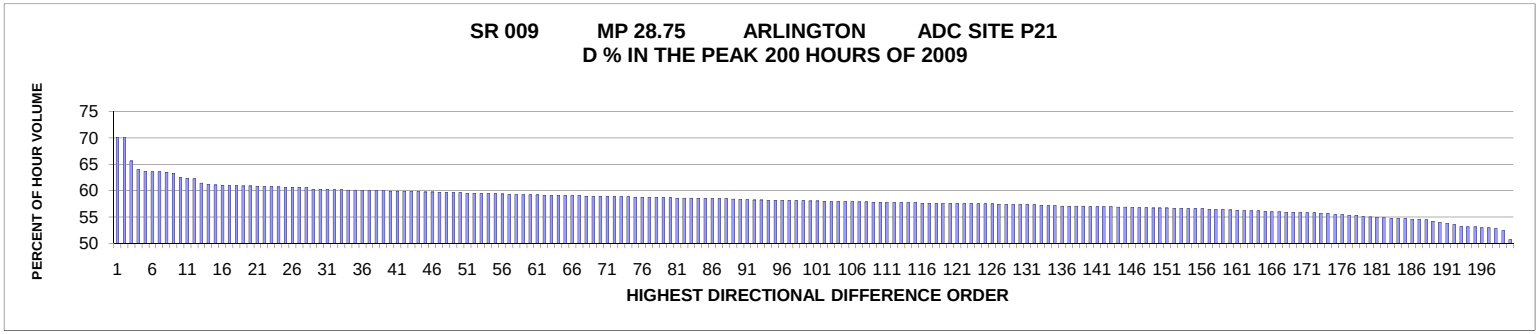

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
9	18	9	6	17	1318	11.72	1	11245	786	532	59.64	40.36
6	10	9	4	17	1227	10.91	2		714	513	58.19	41.81
9	25	9	6	17	1218	10.83	3		738	480	60.59	39.41
5	1	9	6	17	1211	10.77	4		683	528	56.4	43.6
6	12	9	6	17	1199	10.66	5		664	535	55.38	44.62
7	10	9	6	17	1195	10.63	6		702	493	58.74	41.26
6	3	9	4	18	1193	10.61	7		696	497	58.34	41.66
3	6	9	6	17	1191	10.59	8		683	508	57.35	42.65
9	11	9	6	17	1191	10.59	9		722	469	60.62	39.38
5	1	9	6	18	1187	10.56	10		682	505	57.46	42.54
6	5	9	6	17	1187	10.56	11		701	486	59.06	40.94
4	15	9	4	17	1183	10.52	12		629	554	53.17	46.83
4	21	9	3	17	1183	10.52	13		636	547	53.76	46.24
9	16	9	4	17	1183	10.52	14		699	484	59.09	40.91
4	29	9	4	17	1180	10.49	15		622	558	52.71	47.29
10	15	9	5	17	1178	10.48	16		677	501	57.47	42.53
10	30	9	6	17	1177	10.47	17		674	503	57.26	42.74

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
4	7	9	3	17	1175	10.45	18		674	501	57.36	42.64
5	22	9	6	16	1175	10.45	19		731	444	62.21	37.79
5	29	9	6	18	1175	10.45	20		676	499	57.53	42.47
7	31	9	6	17	1173	10.43	21	11245	750	423	63.94	36.06
6	3	9	4	17	1169	10.4	22		655	514	56.03	43.97
9	14	9	2	17	1166	10.37	23		656	510	56.26	43.74
5	1	9	6	16	1165	10.36	24		660	505	56.65	43.35
6	4	9	5	17	1163	10.34	25		671	492	57.7	42.3
11	27	9	6	15	1163	10.34	26		763	400	65.61	34.39
10	7	9	4	17	1162	10.33	27		698	464	60.07	39.93
9	25	9	6	18	1153	10.25	28		669	484	58.02	41.98
6	12	9	6	18	1151	10.24	29		653	498	56.73	43.27
5	29	9	6	16	1150	10.23	30		697	453	60.61	39.39
6	11	9	5	17	1147	10.2	31		649	498	56.58	43.42
4	16	9	5	17	1146	10.19	32		666	480	58.12	41.88
6	15	9	2	17	1145	10.18	33		666	479	58.17	41.83
4	8	9	4	17	1144	10.17	34		647	497	56.56	43.44
7	31	9	6	18	1144	10.17	35		695	449	60.75	39.25
4	24	9	6	17	1143	10.16	36		632	511	55.29	44.71
5	22	9	6	17	1142	10.16	37		726	416	63.57	36.43
6	2	9	3	17	1140	10.14	38		638	502	55.96	44.04
7	24	9	6	18	1139	10.13	39		697	442	61.19	38.81
4	6	9	2	17	1138	10.12	40		621	517	54.57	45.43
5	29	9	6	17	1137	10.11	41	11245	654	483	57.52	42.48
10	2	9	6	17	1137	10.11	42		670	467	58.93	41.07
5	28	9	5	18	1135	10.09	43		659	476	58.06	41.94
9	2	9	4	17	1135	10.09	44		679	456	59.82	40.18
6	12	9	6	16	1133	10.08	45		683	450	60.28	39.72
9	24	9	5	17	1133	10.08	46		660	473	58.25	41.75
7	10	9	6	18	1132	10.07	47		689	443	60.87	39.13
4	20	9	2	17	1131	10.06	48		618	513	54.64	45.36
10	8	9	5	17	1131	10.06	49		675	456	59.68	40.32
10	9	9	6	17	1131	10.06	50		666	465	58.89	41.11
7	3	9	6	14	1130	10.05	51		715	415	63.27	36.73
9	10	9	5	17	1130	10.05	52		650	480	57.52	42.48
10	5	9	2	17	1130	10.05	53		690	440	61.06	38.94
4	21	9	3	16	1128	10.03	54		677	451	60.02	39.98
4	23	9	5	17	1128	10.03	55		614	514	54.43	45.57
4	10	9	6	17	1127	10.02	56		633	494	56.17	43.83
4	29	9	4	16	1127	10.02	57		608	519	53.95	46.05
5	19	9	3	17	1126	10.01	58		642	484	57.02	42.98
3	17	9	3	17	1125	10	59		669	456	59.47	40.53
4	24	9	6	16	1123	9.99	60		659	464	58.68	41.32
10	16	9	6	18	1123	9.99	61	11245	596	527	53.07	46.93
5	14	9	5	17	1121	9.97	62		643	478	57.36	42.64
5	22	9	6	18	1120	9.96	63		665	455	59.38	40.63
4	22	9	4	17	1119	9.95	64		592	527	52.9	47.1
5	15	9	6	17	1118	9.94	65		671	447	60.02	39.98
3	12	9	5	18	1117	9.93	66		636	481	56.94	43.06
10	1	9	5	17	1117	9.93	67		656	461	58.73	41.27
10	28	9	4	17	1117	9.93	68		630	487	56.4	43.6
5	15	9	6	16	1116	9.92	69		642	474	57.53	42.47

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
9	9	9	4	17	1115	9.92	70		668	447	59.91	40.09
9	15	9	3	17	1115	9.92	71		626	489	56.14	43.86
6	5	9	6	16	1114	9.91	72		662	452	59.43	40.57
9	30	9	4	17	1114	9.91	73		665	449	59.69	40.31
3	6	9	6	18	1112	9.89	74		651	461	58.54	41.46
4	10	9	6	16	1112	9.89	75		638	474	57.37	42.63
7	3	9	6	17	1112	9.89	76		707	405	63.58	36.42
10	21	9	4	17	1111	9.88	77		652	459	58.69	41.31
11	5	9	5	17	1110	9.87	78		648	462	58.38	41.62
12	2	9	4	17	1110	9.87	79		663	447	59.73	40.27
3	20	9	6	17	1108	9.85	80		656	452	59.21	40.79
4	27	9	2	17	1108	9.85	81	11245	628	480	56.68	43.32
10	2	9	6	18	1107	9.84	82		607	500	54.83	45.17
6	18	9	5	17	1106	9.84	83		599	507	54.16	45.84
5	21	9	5	17	1105	9.83	84		636	469	57.56	42.44
10	14	9	4	17	1105	9.83	85		653	452	59.1	40.9
1	15	9	5	17	1104	9.82	86		614	490	55.62	44.38
4	24	9	6	18	1104	9.82	87		639	465	57.88	42.12
6	2	9	3	18	1103	9.81	88		641	462	58.11	41.89
9	15	9	3	18	1103	9.81	89		637	466	57.75	42.25
5	27	9	4	16	1102	9.8	90		638	464	57.89	42.11
6	5	9	6	18	1102	9.8	91		645	457	58.53	41.47
7	30	9	5	17	1102	9.8	92		651	451	59.07	40.93
4	14	9	3	17	1099	9.77	93		629	470	57.23	42.77
9	17	9	5	18	1099	9.77	94		614	485	55.87	44.13
1	30	9	6	17	1097	9.76	95		643	454	58.61	41.39
7	17	9	6	17	1097	9.76	96		656	441	59.8	40.2
4	30	9	5	17	1096	9.75	97		602	494	54.93	45.07
9	2	9	4	18	1095	9.74	98		642	453	58.63	41.37
9	29	9	3	17	1095	9.74	99		644	451	58.81	41.19
11	26	9	5	14	1095	9.74	100		767	328	70.05	29.95
3	3	9	3	17	1093	9.72	101	11245	631	462	57.73	42.27
6	10	9	4	16	1093	9.72	102		646	447	59.1	40.9
4	7	9	3	18	1092	9.71	103		605	487	55.4	44.6
5	12	9	3	17	1092	9.71	104		613	479	56.14	43.86
6	11	9	5	16	1092	9.71	105		630	462	57.69	42.31
10	12	9	2	17	1092	9.71	106		646	446	59.16	40.84
10	30	9	6	18	1092	9.71	107		553	539	50.64	49.36
11	13	9	6	17	1092	9.71	108		639	453	58.52	41.48
1	23	9	6	16	1091	9.7	109		642	449	58.85	41.15
6	1	9	2	17	1091	9.7	110		628	463	57.56	42.44
10	7	9	4	18	1091	9.7	111		638	453	58.48	41.52
1	23	9	6	17	1090	9.69	112		647	443	59.36	40.64
5	5	9	3	17	1090	9.69	113		645	445	59.17	40.83
7	24	9	6	17	1090	9.69	114		645	445	59.17	40.83
4	21	9	3	18	1089	9.68	115		619	470	56.84	43.16
6	3	9	4	16	1089	9.68	116		631	458	57.94	42.06
7	30	9	5	18	1088	9.68	117		625	463	57.44	42.56
4	17	9	6	16	1087	9.67	118		660	427	60.72	39.28
5	6	9	4	17	1087	9.67	119		640	447	58.88	41.12
10	9	9	6	18	1087	9.67	120		662	425	60.9	39.1
4	17	9	6	18	1086	9.66	121	11245	635	451	58.47	41.53

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
5	27	9	4	18	1086	9.66	122		594	492	54.7	45.3
6	9	9	3	17	1086	9.66	123		597	489	54.97	45.03
10	20	9	3	17	1086	9.66	124		625	461	57.55	42.45
4	17	9	6	17	1085	9.65	125		611	474	56.31	43.69
4	30	9	5	18	1085	9.65	126		626	459	57.7	42.3
5	26	9	3	18	1085	9.65	127		662	423	61.01	38.99
9	23	9	4	17	1085	9.65	128		605	480	55.76	44.24
1	16	9	6	17	1084	9.64	129		617	467	56.92	43.08
5	27	9	4	17	1084	9.64	130		606	478	55.9	44.1
9	4	9	6	17	1084	9.64	131		666	418	61.44	38.56
9	22	9	3	17	1084	9.64	132		626	458	57.75	42.25
6	12	9	6	19	1083	9.63	133		516	567	47.65	52.35
9	11	9	6	16	1083	9.63	134		651	432	60.11	39.89
9	17	9	5	17	1081	9.61	135		644	437	59.57	40.43
3	19	9	5	17	1080	9.6	136		602	478	55.74	44.26
5	15	9	6	18	1080	9.6	137		638	442	59.07	40.93
6	16	9	3	18	1080	9.6	138		627	453	58.06	41.94
7	28	9	3	17	1080	9.6	139		642	438	59.44	40.56
10	27	9	3	17	1080	9.6	140		650	430	60.19	39.81
4	9	9	5	17	1079	9.6	141	11245	632	447	58.57	41.43
5	28	9	5	16	1079	9.6	142		613	466	56.81	43.19
10	2	9	6	16	1079	9.6	143		650	429	60.24	39.76
10	6	9	3	18	1077	9.58	144		609	468	56.55	43.45
11	26	9	5	13	1077	9.58	145		755	322	70.1	29.9
5	20	9	4	17	1076	9.57	146		609	467	56.6	43.4
9	8	9	3	17	1076	9.57	147		569	507	52.88	47.12
10	21	9	4	16	1076	9.57	148		683	393	63.48	36.52
9	21	9	2	16	1075	9.56	149		611	464	56.84	43.16
3	24	9	3	17	1073	9.54	150		611	462	56.94	43.06
10	6	9	3	17	1073	9.54	151		621	452	57.88	42.12
3	10	9	3	17	1072	9.53	152		610	462	56.9	43.1
5	28	9	5	17	1072	9.53	153		612	460	57.09	42.91
10	8	9	5	18	1072	9.53	154		597	475	55.69	44.31
4	9	9	5	18	1071	9.52	155		607	464	56.68	43.32
5	11	9	2	17	1071	9.52	156		620	451	57.89	42.11
7	10	9	6	16	1071	9.52	157		651	420	60.78	39.22
7	29	9	4	17	1071	9.52	158		611	460	57.05	42.95
4	22	9	4	16	1070	9.52	159		568	502	53.08	46.92
7	3	9	6	13	1070	9.52	160		630	440	58.88	41.12
7	3	9	6	16	1070	9.52	161	11245	680	390	63.55	36.45
7	31	9	6	16	1070	9.52	162		643	427	60.09	39.91
9	18	9	6	16	1070	9.52	163		619	451	57.85	42.15
10	22	9	5	17	1070	9.52	164		619	451	57.85	42.15
12	10	9	5	17	1070	9.52	165		651	419	60.84	39.16
5	8	9	6	17	1069	9.51	166		597	472	55.85	44.15
10	15	9	5	18	1069	9.51	167		626	443	58.56	41.44
11	6	9	6	17	1069	9.51	168		666	403	62.3	37.7
11	3	9	3	18	1068	9.5	169		584	484	54.68	45.32
5	14	9	5	16	1067	9.49	170		666	401	62.42	37.58
5	14	9	5	18	1067	9.49	171		597	470	55.95	44.05
7	1	9	4	17	1067	9.49	172		619	448	58.01	41.99
6	4	9	5	16	1066	9.48	173		623	443	58.44	41.56

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
9	30	9	4	18	1066	9.48	174		640	426	60.04	39.96
11	10	9	3	17	1066	9.48	175		635	431	59.57	40.43
11	18	9	4	17	1066	9.48	176		619	447	58.07	41.93
3	4	9	4	17	1064	9.46	177		614	450	57.71	42.29
3	4	9	4	18	1064	9.46	178		638	426	59.96	40.04
6	19	9	6	16	1064	9.46	179		633	431	59.49	40.51
9	10	9	5	16	1064	9.46	180		646	418	60.71	39.29
10	23	9	6	17	1064	9.46	181	11245	645	419	60.62	39.38
6	30	9	3	17	1063	9.45	182		569	494	53.53	46.47
11	4	9	4	17	1063	9.45	183		603	460	56.73	43.27
11	20	9	6	17	1063	9.45	184		585	478	55.03	44.97
6	1	9	2	16	1062	9.44	185		636	426	59.89	40.11
9	23	9	4	18	1062	9.44	186		606	456	57.06	42.94
1	28	9	4	17	1061	9.44	187		609	452	57.4	42.6
6	19	9	6	17	1061	9.44	188		605	456	57.02	42.98
9	1	9	3	17	1061	9.44	189		599	462	56.46	43.54
12	1	9	3	17	1061	9.44	190		624	437	58.81	41.19
1	14	9	4	17	1060	9.43	191		600	460	56.6	43.4
4	7	9	3	16	1060	9.43	192		578	482	54.53	45.47
6	9	9	3	18	1060	9.43	193		634	426	59.81	40.19
7	22	9	4	18	1060	9.43	194		616	444	58.11	41.89
1	22	9	5	17	1059	9.42	195		645	414	60.91	39.09
6	2	9	3	16	1059	9.42	196		627	432	59.21	40.79
9	9	9	4	18	1059	9.42	197		609	450	57.51	42.49
1	20	9	3	17	1058	9.41	198		636	422	60.11	39.89
6	16	9	3	17	1058	9.41	199		604	454	57.09	42.91
6	25	9	5	17	1058	9.41	200		585	473	55.29	44.71

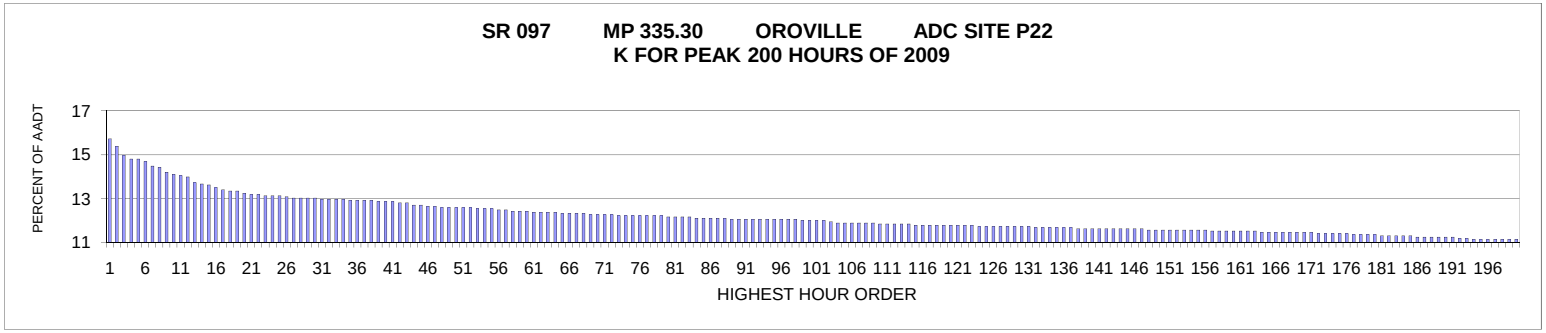

AADT= 1858 **K 30 FACTOR=** 13.02 **K 100 FACTOR=** 12 **K 200 FACTOR=** 11.14 **D FACTOR=** 54.58

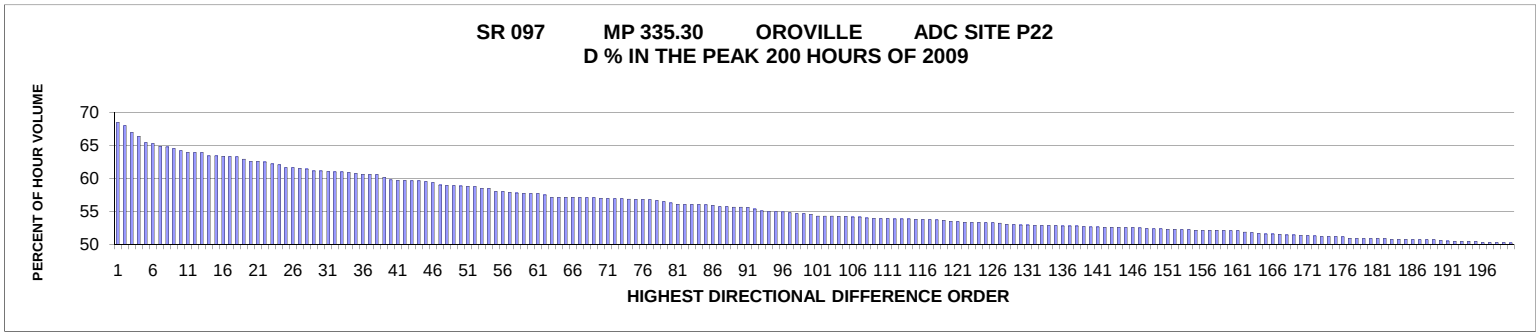

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	14	9	6	16	292	15.72	1	1858	148	144	50.68	49.32
7	3	9	6	12	286	15.39	2		123	163	43.01	56.99
8	15	9	7	13	278	14.96	3		104	174	37.41	62.59
8	14	9	6	13	275	14.8	4		102	173	37.09	62.91
8	31	9	2	12	275	14.8	5		88	187	32	68
8	14	9	6	15	273	14.69	6		149	124	54.58	45.42
7	3	9	6	13	269	14.48	7		138	131	51.3	48.7
9	4	9	6	16	268	14.42	8		124	144	46.27	53.73
7	5	9	1	12	264	14.21	9		117	147	44.32	55.68
7	6	9	2	13	262	14.1	10		96	166	36.64	63.36
9	4	9	6	12	261	14.05	11		115	146	44.06	55.94
8	22	9	7	12	260	13.99	12		90	170	34.62	65.38
11	21	9	7	14	255	13.72	13		121	134	47.45	52.55
8	21	9	6	12	254	13.67	14		93	161	36.61	63.39
8	23	9	1	14	253	13.62	15		125	128	49.41	50.59
8	31	9	2	13	251	13.51	16		79	172	31.47	68.53
7	3	9	6	11	249	13.4	17		113	136	45.38	54.62

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	2	9	5	13	248	13.35	18		108	140	43.55	56.45
9	1	9	3	14	248	13.35	19		97	151	39.11	60.89
5	18	9	2	13	246	13.24	20		147	99	59.76	40.24
8	13	9	5	12	245	13.19	21	1858	105	140	42.86	57.14
8	28	9	6	16	245	13.19	22		113	132	46.12	53.88
6	26	9	6	13	244	13.13	23		117	127	47.95	52.05
8	16	9	1	15	244	13.13	24		130	114	53.28	46.72
8	19	9	4	13	244	13.13	25		115	129	47.13	52.87
7	8	9	4	13	243	13.08	26		102	141	41.98	58.02
6	26	9	6	12	242	13.02	27		104	138	42.98	57.02
7	5	9	1	15	242	13.02	28		118	124	48.76	51.24
8	16	9	1	14	242	13.02	29		138	104	57.02	42.98
8	27	9	5	11	242	13.02	30		111	131	45.87	54.13
7	2	9	5	14	241	12.97	31		107	134	44.4	55.6
7	5	9	1	13	241	12.97	32		121	120	50.21	49.79
8	14	9	6	12	241	12.97	33		100	141	41.49	58.51
8	20	9	5	12	241	12.97	34		96	145	39.83	60.17
6	26	9	6	15	240	12.92	35		121	119	50.42	49.58
7	1	9	4	14	240	12.92	36		113	127	47.08	52.92
7	6	9	2	14	240	12.92	37		114	126	47.5	52.5
8	20	9	5	14	240	12.92	38		111	129	46.25	53.75
6	29	9	2	14	239	12.86	39		106	133	44.35	55.65
9	3	9	5	12	239	12.86	40		92	147	38.49	61.51
11	21	9	7	13	239	12.86	41	1858	106	133	44.35	55.65
7	12	9	1	14	238	12.81	42		126	112	52.94	47.06
8	22	9	7	14	238	12.81	43		120	118	50.42	49.58
5	15	9	6	13	236	12.7	44		92	144	38.98	61.02
8	31	9	2	14	236	12.7	45		78	158	33.05	66.95
8	27	9	5	12	235	12.65	46		110	125	46.81	53.19
8	28	9	6	13	235	12.65	47		114	121	48.51	51.49
6	30	9	3	13	234	12.59	48		101	133	43.16	56.84
7	4	9	7	12	234	12.59	49		91	143	38.89	61.11
8	13	9	5	15	234	12.59	50		124	110	52.99	47.01
8	14	9	6	14	234	12.59	51		111	123	47.44	52.56
8	16	9	1	13	234	12.59	52		99	135	42.31	57.69
7	12	9	1	13	233	12.54	53		105	128	45.06	54.94
8	27	9	5	16	233	12.54	54		149	84	63.95	36.05
9	4	9	6	14	233	12.54	55		92	141	39.48	60.52
7	2	9	5	15	232	12.49	56		118	114	50.86	49.14
9	4	9	6	15	232	12.49	57		102	130	43.97	56.03
5	15	9	6	15	231	12.43	58		91	140	39.39	60.61
7	10	9	6	14	231	12.43	59		97	134	41.99	58.01
7	13	9	2	12	231	12.43	60		99	132	42.86	57.14
6	19	9	6	13	230	12.38	61	1858	113	117	49.13	50.87
6	29	9	2	12	230	12.38	62		106	124	46.09	53.91
7	5	9	1	14	230	12.38	63		131	99	56.96	43.04
8	28	9	6	12	230	12.38	64		110	120	47.83	52.17
3	27	9	6	13	229	12.33	65		116	113	50.66	49.34
8	13	9	5	13	229	12.33	66		107	122	46.72	53.28
8	28	9	6	17	229	12.33	67		126	103	55.02	44.98
9	4	9	6	11	229	12.33	68		82	147	35.81	64.19
5	15	9	6	17	228	12.27	69		89	139	39.04	60.96

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	22	9	7	15	228	12.27	70		118	110	51.75	48.25
8	25	9	3	12	228	12.27	71		96	132	42.11	57.89
9	3	9	5	14	228	12.27	72		92	136	40.35	59.65
4	9	9	5	13	227	12.22	73		100	127	44.05	55.95
6	26	9	6	14	227	12.22	74		116	111	51.1	48.9
7	1	9	4	15	227	12.22	75		117	110	51.54	48.46
8	17	9	2	13	227	12.22	76		92	135	40.53	59.47
8	19	9	4	12	227	12.22	77		103	124	45.37	54.63
8	22	9	7	13	227	12.22	78		120	107	52.86	47.14
8	31	9	2	15	227	12.22	79		80	147	35.24	64.76
7	3	9	6	14	226	12.16	80		115	111	50.88	49.12
8	14	9	6	17	226	12.16	81	1858	137	89	60.62	39.38
9	2	9	4	15	226	12.16	82		111	115	49.12	50.88
9	7	9	2	13	226	12.16	83		143	83	63.27	36.73
5	15	9	6	12	225	12.11	84		95	130	42.22	57.78
7	2	9	5	11	225	12.11	85		106	119	47.11	52.89
7	7	9	3	12	225	12.11	86		97	128	43.11	56.89
8	31	9	2	11	225	12.11	87		79	146	35.11	64.89
9	18	9	6	12	225	12.11	88		103	122	45.78	54.22
4	10	9	6	13	224	12.06	89		85	139	37.95	62.05
5	15	9	6	16	224	12.06	90		96	128	42.86	57.14
6	12	9	6	12	224	12.06	91		84	140	37.5	62.5
7	6	9	2	12	224	12.06	92		100	124	44.64	55.36
7	6	9	2	16	224	12.06	93		138	86	61.61	38.39
7	11	9	7	12	224	12.06	94		86	138	38.39	61.61
7	12	9	1	12	224	12.06	95		114	110	50.89	49.11
8	19	9	4	16	224	12.06	96		126	98	56.25	43.75
8	27	9	5	13	224	12.06	97		111	113	49.55	50.45
10	8	9	5	12	224	12.06	98		96	128	42.86	57.14
5	22	9	6	15	223	12	99		103	120	46.19	53.81
6	28	9	1	13	223	12	100		98	125	43.95	56.05
8	13	9	5	14	223	12	101	1858	108	115	48.43	51.57
8	31	9	2	16	223	12	102		87	136	39.01	60.99
4	10	9	6	12	222	11.95	103		91	131	40.99	59.01
5	22	9	6	12	221	11.89	104		89	132	40.27	59.73
6	26	9	6	16	221	11.89	105		111	110	50.23	49.77
7	10	9	6	12	221	11.89	106		100	121	45.25	54.75
8	23	9	1	12	221	11.89	107		105	116	47.51	52.49
9	4	9	6	17	221	11.89	108		98	123	44.34	55.66
9	11	9	6	12	221	11.89	109		91	130	41.18	58.82
8	28	9	6	11	220	11.84	110		95	125	43.18	56.82
9	5	9	7	12	220	11.84	111		93	127	42.27	57.73
9	11	9	6	14	220	11.84	112		107	113	48.64	51.36
9	11	9	6	16	220	11.84	113		111	109	50.45	49.55
9	18	9	6	16	220	11.84	114		118	102	53.64	46.36
6	12	9	6	14	219	11.79	115		108	111	49.32	50.68
6	22	9	2	12	219	11.79	116		86	133	39.27	60.73
7	10	9	6	17	219	11.79	117		117	102	53.42	46.58
7	16	9	5	14	219	11.79	118		108	111	49.32	50.68
8	18	9	3	12	219	11.79	119		90	129	41.1	58.9
8	27	9	5	14	219	11.79	120		118	101	53.88	46.12
9	7	9	2	14	219	11.79	121	1858	125	94	57.08	42.92

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
9	25	9	6	13	219	11.79	122		91	128	41.55	58.45
9	25	9	6	15	219	11.79	123		105	114	47.95	52.05
7	6	9	2	11	218	11.73	124		88	130	40.37	59.63
7	7	9	3	13	218	11.73	125		114	104	52.29	47.71
7	8	9	4	12	218	11.73	126		105	113	48.17	51.83
7	10	9	6	15	218	11.73	127		115	103	52.75	47.25
8	25	9	3	13	218	11.73	128		94	124	43.12	56.88
8	26	9	4	13	218	11.73	129		103	115	47.25	52.75
9	9	9	4	11	218	11.73	130		90	128	41.28	58.72
10	17	9	7	14	218	11.73	131		114	104	52.29	47.71
5	17	9	1	12	217	11.68	132		77	140	35.48	64.52
6	26	9	6	17	217	11.68	133		113	104	52.07	47.93
7	7	9	3	15	217	11.68	134		103	114	47.47	52.53
8	28	9	6	15	217	11.68	135		111	106	51.15	48.85
8	29	9	7	13	217	11.68	136		82	135	37.79	62.21
11	21	9	7	11	217	11.68	137		73	144	33.64	66.36
6	25	9	5	12	216	11.63	138		100	116	46.3	53.7
7	3	9	6	15	216	11.63	139		106	110	49.07	50.93
7	12	9	1	16	216	11.63	140		127	89	58.8	41.2
8	12	9	4	12	216	11.63	141	1858	101	115	46.76	53.24
8	15	9	7	11	216	11.63	142		78	138	36.11	63.89
9	1	9	3	12	216	11.63	143		79	137	36.57	63.43
9	10	9	5	11	216	11.63	144		78	138	36.11	63.89
9	10	9	5	12	216	11.63	145		101	115	46.76	53.24
9	18	9	6	15	216	11.63	146		114	102	52.78	47.22
10	9	9	6	15	216	11.63	147		105	111	48.61	51.39
5	15	9	6	11	215	11.57	148		83	132	38.6	61.4
6	26	9	6	11	215	11.57	149		91	124	42.33	57.67
8	17	9	2	16	215	11.57	150		118	97	54.88	45.12
8	19	9	4	14	215	11.57	151		100	115	46.51	53.49
8	24	9	2	17	215	11.57	152		110	105	51.16	48.84
9	5	9	7	14	215	11.57	153		108	107	50.23	49.77
9	11	9	6	15	215	11.57	154		106	109	49.3	50.7
10	17	9	7	13	215	11.57	155		105	110	48.84	51.16
10	17	9	7	15	215	11.57	156		109	106	50.7	49.3
6	19	9	6	15	214	11.52	157		110	104	51.4	48.6
6	19	9	6	16	214	11.52	158		112	102	52.34	47.66
6	29	9	2	15	214	11.52	159		101	113	47.2	52.8
8	20	9	5	15	214	11.52	160		116	98	54.21	45.79
8	24	9	2	14	214	11.52	161	1858	108	106	50.47	49.53
9	18	9	6	14	214	11.52	162		91	123	42.52	57.48
10	7	9	4	12	214	11.52	163		102	112	47.66	52.34
5	8	9	6	14	213	11.46	164		102	111	47.89	52.11
7	8	9	4	14	213	11.46	165		112	101	52.58	47.42
8	14	9	6	11	213	11.46	166		74	139	34.74	65.26
8	18	9	3	16	213	11.46	167		106	107	49.77	50.23
8	21	9	6	13	213	11.46	168		102	111	47.89	52.11
8	24	9	2	12	213	11.46	169		86	127	40.38	59.62
9	4	9	6	13	213	11.46	170		98	115	46.01	53.99
9	6	9	1	12	213	11.46	171		92	121	43.19	56.81
6	30	9	3	15	212	11.41	172		98	114	46.23	53.77
7	6	9	2	15	212	11.41	173		111	101	52.36	47.64

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	13	9	2	14	212	11.41	174		92	120	43.4	56.6
7	15	9	4	13	212	11.41	175		115	97	54.25	45.75
8	19	9	4	15	212	11.41	176		115	97	54.25	45.75
4	9	9	5	14	211	11.36	177		111	100	52.61	47.39
5	18	9	2	14	211	11.36	178		132	79	62.56	37.44
8	12	9	4	11	211	11.36	179		82	129	38.86	61.14
10	9	9	6	18	211	11.36	180		101	110	47.87	52.13
7	1	9	4	13	210	11.3	181	1858	97	113	46.19	53.81
7	2	9	5	18	210	11.3	182		112	98	53.33	46.67
9	6	9	1	14	210	11.3	183		111	99	52.86	47.14
9	29	9	3	16	210	11.3	184		114	96	54.29	45.71
11	21	9	7	15	210	11.3	185		133	77	63.33	36.67
6	28	9	1	14	209	11.25	186		105	104	50.24	49.76
7	3	9	6	18	209	11.25	187		106	103	50.72	49.28
9	17	9	5	12	209	11.25	188		85	124	40.67	59.33
9	19	9	7	14	209	11.25	189		109	100	52.15	47.85
10	9	9	6	17	209	11.25	190		101	108	48.33	51.67
10	12	9	2	12	209	11.25	191		110	99	52.63	47.37
6	19	9	6	12	208	11.19	192		96	112	46.15	53.85
8	12	9	4	13	208	11.19	193		90	118	43.27	56.73
6	11	9	5	13	207	11.14	194		91	116	43.96	56.04
7	3	9	6	16	207	11.14	195		93	114	44.93	55.07
7	10	9	6	13	207	11.14	196		116	91	56.04	43.96
7	16	9	5	15	207	11.14	197		99	108	47.83	52.17
8	21	9	6	16	207	11.14	198		109	98	52.66	47.34
9	1	9	3	13	207	11.14	199		95	112	45.89	54.11
10	16	9	6	12	207	11.14	200		85	122	41.06	58.94

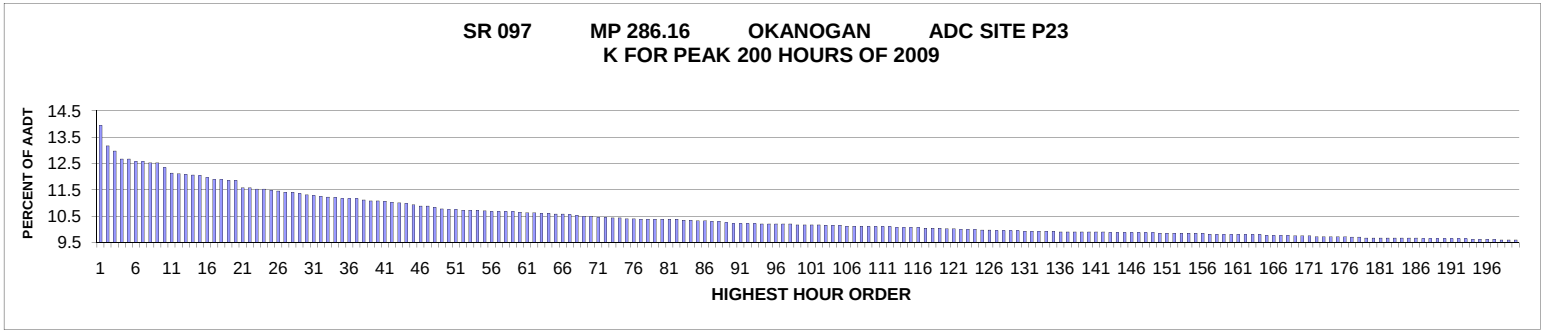

AADT= 3971 **K 30 FACTOR=** 11.31 **K 100 FACTOR=** 10.17 **K 200 FACTOR=** 9.59 **D FACTOR=** 55.51

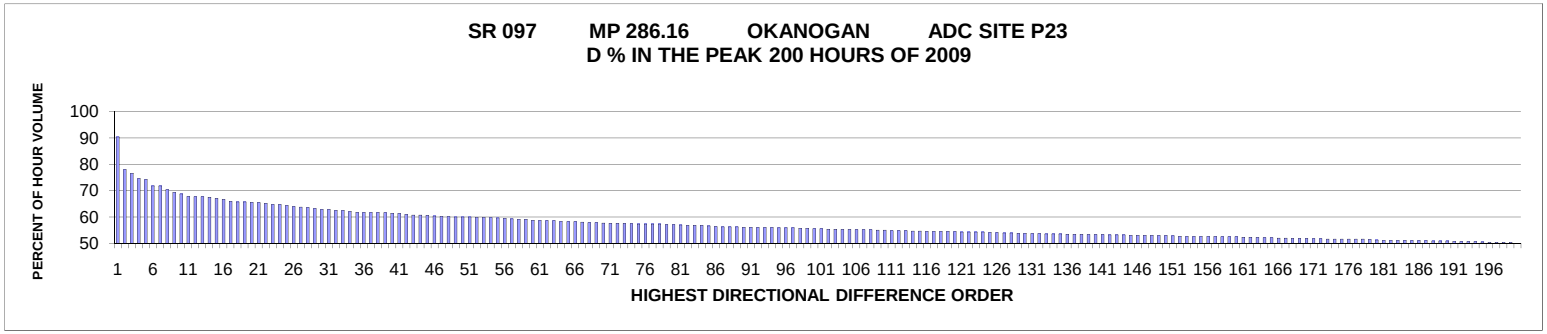

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
5	16	9	7	13	554	13.95	1	3971	413	141	74.55	25.45
10	16	9	6	18	523	13.17	2		343	180	65.58	34.42
8	9	9	1	18	515	12.97	3		158	357	30.68	69.32
5	22	9	6	16	503	12.67	4		301	202	59.84	40.16
10	16	9	6	15	503	12.67	5		310	193	61.63	38.37
8	9	9	1	13	499	12.57	6		189	310	37.88	62.12
10	9	9	6	17	499	12.57	7		323	176	64.73	35.27
8	7	9	6	18	497	12.52	8		333	164	67	33
10	9	9	6	18	497	12.52	9		297	200	59.76	40.24
8	7	9	6	17	490	12.34	10		331	159	67.55	32.45
8	7	9	6	16	482	12.14	11		305	177	63.28	36.72
9	4	9	6	18	481	12.11	12		267	214	55.51	44.49
8	9	9	1	15	480	12.09	13		175	305	36.46	63.54
9	4	9	6	17	479	12.06	14		265	214	55.32	44.68
8	9	9	1	14	478	12.04	15		204	274	42.68	57.32
10	9	9	6	16	475	11.96	16		283	192	59.58	40.42
10	16	9	6	16	472	11.89	17		302	170	63.98	36.02

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
10	16	9	6	17	472	11.89	18		310	162	65.68	34.32
8	8	9	7	19	471	11.86	19		361	110	76.65	23.35
10	11	9	1	16	471	11.86	20		191	280	40.55	59.45
10	11	9	1	15	460	11.58	21	3971	137	323	29.78	70.22
10	23	9	6	18	460	11.58	22		254	206	55.22	44.78
8	22	9	7	15	458	11.53	23		225	233	49.13	50.87
10	16	9	6	14	458	11.53	24		296	162	64.63	35.37
5	22	9	6	17	456	11.48	25		267	189	58.55	41.45
10	11	9	1	14	455	11.46	26		152	303	33.41	66.59
5	22	9	6	18	453	11.41	27		271	182	59.82	40.18
8	8	9	7	18	453	11.41	28		325	128	71.74	28.26
8	14	9	6	14	451	11.36	29		228	223	50.55	49.45
8	8	9	7	16	449	11.31	30		270	179	60.13	39.87
11	25	9	4	15	448	11.28	31		245	203	54.69	45.31
8	7	9	6	15	447	11.26	32		276	171	61.74	38.26
10	11	9	1	17	446	11.23	33		154	292	34.53	65.47
10	16	9	6	12	445	11.21	34		290	155	65.17	34.83
8	8	9	7	13	443	11.16	35		267	176	60.27	39.73
8	22	9	7	12	443	11.16	36		239	204	53.95	46.05
9	25	9	6	17	443	11.16	37		240	203	54.18	45.82
10	2	9	6	17	441	11.11	38		243	198	55.1	44.9
6	5	9	6	17	440	11.08	39		242	198	55	45
6	19	9	6	18	440	11.08	40		258	182	58.64	41.36
10	23	9	6	15	439	11.06	41	3971	203	236	46.24	53.76
8	8	9	7	17	438	11.03	42		296	142	67.58	32.42
8	7	9	6	14	437	11	43		244	193	55.84	44.16
8	6	9	5	18	436	10.98	44		269	167	61.7	38.3
8	8	9	7	24	434	10.93	45		42	392	9.68	90.32
8	6	9	5	17	432	10.88	46		259	173	59.95	40.05
8	9	9	1	17	432	10.88	47		157	275	36.34	63.66
8	8	9	7	20	430	10.83	48		319	111	74.19	25.81
8	7	9	6	19	428	10.78	49		307	121	71.73	28.27
6	26	9	6	14	427	10.75	50		233	194	54.57	45.43
9	25	9	6	18	427	10.75	51		224	203	52.46	47.54
8	22	9	7	14	426	10.73	52		223	203	52.35	47.65
10	2	9	6	18	426	10.73	53		226	200	53.05	46.95
10	16	9	6	13	426	10.73	54		258	168	60.56	39.44
8	9	9	1	12	425	10.7	55		181	244	42.59	57.41
8	8	9	7	14	424	10.68	56		255	169	60.14	39.86
8	14	9	6	13	424	10.68	57		230	194	54.25	45.75
8	14	9	6	17	424	10.68	58		216	208	50.94	49.06
8	23	9	1	15	424	10.68	59		208	216	49.06	50.94
8	24	9	2	16	423	10.65	60		226	197	53.43	46.57
8	20	9	5	17	422	10.63	61	3971	232	190	54.98	45.02
8	22	9	7	16	422	10.63	62		244	178	57.82	42.18
9	3	9	5	16	421	10.6	63		227	194	53.92	46.08
9	4	9	6	16	421	10.6	64		220	201	52.26	47.74
8	9	9	1	16	420	10.58	65		164	256	39.05	60.95
10	15	9	5	18	420	10.58	66		248	172	59.05	40.95
6	26	9	6	16	419	10.55	67		214	205	51.07	48.93
10	1	9	5	17	418	10.53	68		222	196	53.11	46.89
8	14	9	6	15	417	10.5	69		204	213	48.92	51.08

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
10	2	9	6	16	417	10.5	70		220	197	52.76	47.24
8	21	9	6	15	415	10.45	71		212	203	51.08	48.92
10	11	9	1	13	415	10.45	72		154	261	37.11	62.89
8	21	9	6	16	414	10.43	73		233	181	56.28	43.72
9	4	9	6	14	414	10.43	74		220	194	53.14	46.86
10	14	9	4	16	413	10.4	75		200	213	48.43	51.57
10	23	9	6	17	413	10.4	76		210	203	50.85	49.15
5	22	9	6	13	412	10.38	77		237	175	57.52	42.48
8	24	9	2	15	412	10.38	78		213	199	51.7	48.3
9	5	9	7	13	412	10.38	79		209	203	50.73	49.27
9	5	9	7	15	412	10.38	80		220	192	53.4	46.6
10	9	9	6	15	412	10.38	81	3971	236	176	57.28	42.72
10	23	9	6	16	412	10.38	82		231	181	56.07	43.93
7	2	9	5	16	411	10.35	83		239	172	58.15	41.85
8	22	9	7	11	411	10.35	84		181	230	44.04	55.96
5	22	9	6	15	410	10.32	85		246	164	60	40
7	31	9	6	15	410	10.32	86		207	203	50.49	49.51
8	6	9	5	16	409	10.3	87		242	167	59.17	40.83
10	23	9	6	14	409	10.3	88		180	229	44.01	55.99
7	5	9	1	14	407	10.25	89		139	268	34.15	65.85
5	25	9	2	13	406	10.22	90		131	275	32.27	67.73
7	31	9	6	14	406	10.22	91		186	220	45.81	54.19
9	2	9	4	18	406	10.22	92		222	184	54.68	45.32
9	3	9	5	18	406	10.22	93		226	180	55.67	44.33
5	29	9	6	16	405	10.2	94		209	196	51.6	48.4
7	10	9	6	17	405	10.2	95		231	174	57.04	42.96
9	27	9	1	14	405	10.2	96		181	224	44.69	55.31
10	23	9	6	12	405	10.2	97		179	226	44.2	55.8
11	25	9	4	14	405	10.2	98		178	227	43.95	56.05
7	24	9	6	17	404	10.17	99		215	189	53.22	46.78
7	25	9	7	14	404	10.17	100		198	206	49.01	50.99
8	5	9	4	18	404	10.17	101	3971	220	184	54.46	45.54
8	14	9	6	16	404	10.17	102		220	184	54.46	45.54
5	26	9	3	13	403	10.15	103		194	209	48.14	51.86
7	31	9	6	12	403	10.15	104		188	215	46.65	53.35
8	23	9	1	12	403	10.15	105		170	233	42.18	57.82
5	29	9	6	18	402	10.12	106		214	188	53.23	46.77
7	17	9	6	15	402	10.12	107		211	191	52.49	47.51
8	23	9	1	14	402	10.12	108		191	211	47.51	52.49
8	23	9	1	16	401	10.1	109		191	210	47.63	52.37
10	8	9	5	17	401	10.1	110		207	194	51.62	48.38
10	9	9	6	14	401	10.1	111		218	183	54.36	45.64
10	21	9	4	13	401	10.1	112		194	207	48.38	51.62
6	26	9	6	17	400	10.07	113		240	160	60	40
7	31	9	6	16	400	10.07	114		212	188	53	47
9	1	9	3	14	400	10.07	115		185	215	46.25	53.75
9	2	9	4	17	400	10.07	116		214	186	53.5	46.5
7	31	9	6	17	399	10.05	117		223	176	55.89	44.11
8	14	9	6	12	399	10.05	118		192	207	48.12	51.88
10	16	9	6	11	399	10.05	119		262	137	65.66	34.34
7	19	9	1	13	398	10.02	120		169	229	42.46	57.54
8	17	9	2	18	398	10.02	121	3971	213	185	53.52	46.48

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	18	9	3	17	397	10	122		205	192	51.64	48.36
10	9	9	6	19	397	10	123		268	129	67.51	32.49
10	11	9	1	12	397	10	124		156	241	39.29	60.71
7	31	9	6	13	396	9.97	125		184	212	46.46	53.54
8	14	9	6	18	396	9.97	126		225	171	56.82	43.18
6	12	9	6	17	395	9.95	127		214	181	54.18	45.82
7	2	9	5	17	395	9.95	128		243	152	61.52	38.48
10	15	9	5	17	395	9.95	129		222	173	56.2	43.8
11	25	9	4	18	395	9.95	130		232	163	58.73	41.27
5	22	9	6	14	394	9.92	131		246	148	62.44	37.56
7	5	9	1	15	394	9.92	132		148	246	37.56	62.44
7	23	9	5	18	394	9.92	133		201	193	51.02	48.98
8	13	9	5	18	394	9.92	134		217	177	55.08	44.92
8	23	9	1	13	394	9.92	135		190	204	48.22	51.78
7	17	9	6	17	393	9.9	136		214	179	54.45	45.55
8	14	9	6	11	393	9.9	137		193	200	49.11	50.89
8	21	9	6	18	393	9.9	138		229	164	58.27	41.73
8	22	9	7	13	393	9.9	139		198	195	50.38	49.62
8	22	9	7	17	393	9.9	140		223	170	56.74	43.26
8	22	9	7	18	393	9.9	141	3971	241	152	61.32	38.68
10	30	9	6	18	393	9.9	142		185	208	47.07	52.93
7	10	9	6	16	392	9.87	143		206	186	52.55	47.45
7	16	9	5	18	392	9.87	144		226	166	57.65	42.35
8	13	9	5	17	392	9.87	145		208	184	53.06	46.94
8	16	9	1	13	392	9.87	146		169	223	43.11	56.89
8	23	9	1	17	392	9.87	147		220	172	56.12	43.88
8	28	9	6	17	392	9.87	148		228	164	58.16	41.84
11	25	9	4	16	392	9.87	149		190	202	48.47	51.53
6	11	9	5	17	391	9.85	150		193	198	49.36	50.64
7	5	9	1	12	391	9.85	151		167	224	42.71	57.29
7	6	9	2	13	391	9.85	152		160	231	40.92	59.08
7	24	9	6	16	391	9.85	153		194	197	49.62	50.38
8	21	9	6	17	391	9.85	154		216	175	55.24	44.76
10	20	9	3	14	391	9.85	155		173	218	44.25	55.75
11	25	9	4	17	391	9.85	156		208	183	53.2	46.8
10	14	9	4	15	390	9.82	157		202	188	51.79	48.21
7	1	9	4	15	389	9.8	158		197	192	50.64	49.36
7	10	9	6	15	389	9.8	159		200	189	51.41	48.59
8	8	9	7	15	389	9.8	160		212	177	54.5	45.5
8	27	9	5	16	389	9.8	161	3971	199	190	51.16	48.84
9	7	9	2	13	389	9.8	162		149	240	38.3	61.7
10	14	9	4	13	389	9.8	163		213	176	54.76	45.24
10	19	9	2	13	389	9.8	164		153	236	39.33	60.67
9	3	9	5	13	388	9.77	165		205	183	52.84	47.16
9	24	9	5	17	388	9.77	166		194	194	50	50
10	14	9	4	17	388	9.77	167		215	173	55.41	44.59
10	21	9	4	12	388	9.77	168		144	244	37.11	62.89
7	3	9	6	14	387	9.75	169		205	182	52.97	47.03
9	25	9	6	16	387	9.75	170		192	195	49.61	50.39
10	11	9	1	18	387	9.75	171		138	249	35.66	64.34
4	17	9	6	17	386	9.72	172		209	177	54.15	45.85
4	24	9	6	16	386	9.72	173		221	165	57.25	42.75

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	24	9	6	18	386	9.72	174		207	179	53.63	46.37
8	7	9	6	20	386	9.72	175		301	85	77.98	22.02
8	28	9	6	18	386	9.72	176		203	183	52.59	47.41
8	24	9	2	18	385	9.7	177		210	175	54.55	45.45
9	27	9	1	16	385	9.7	178		180	205	46.75	53.25
6	19	9	6	17	384	9.67	179		219	165	57.03	42.97
8	15	9	7	12	384	9.67	180		200	184	52.08	47.92
8	16	9	1	14	384	9.67	181	3971	167	217	43.49	56.51
8	20	9	5	16	384	9.67	182		200	184	52.08	47.92
8	28	9	6	14	384	9.67	183		166	218	43.23	56.77
8	31	9	2	15	384	9.67	184		148	236	38.54	61.46
9	25	9	6	15	384	9.67	185		177	207	46.09	53.91
10	16	9	6	19	384	9.67	186		264	120	68.75	31.25
6	5	9	6	18	383	9.64	187		183	200	47.78	52.22
6	21	9	1	14	383	9.64	188		161	222	42.04	57.96
7	15	9	4	17	383	9.64	189		211	172	55.09	44.91
7	25	9	7	15	383	9.64	190		199	184	51.96	48.04
7	30	9	5	17	383	9.64	191		190	193	49.61	50.39
8	7	9	6	13	383	9.64	192		201	182	52.48	47.52
10	4	9	1	16	383	9.64	193		169	214	44.13	55.87
10	2	9	6	15	382	9.62	194		185	197	48.43	51.57
10	8	9	5	16	382	9.62	195		181	201	47.38	52.62
10	15	9	5	16	382	9.62	196		205	177	53.66	46.34
10	21	9	4	14	382	9.62	197		182	200	47.64	52.36
5	22	9	6	12	381	9.59	198		214	167	56.17	43.83
7	1	9	4	17	381	9.59	199		223	158	58.53	41.47
7	3	9	6	12	381	9.59	200		219	162	57.48	42.52

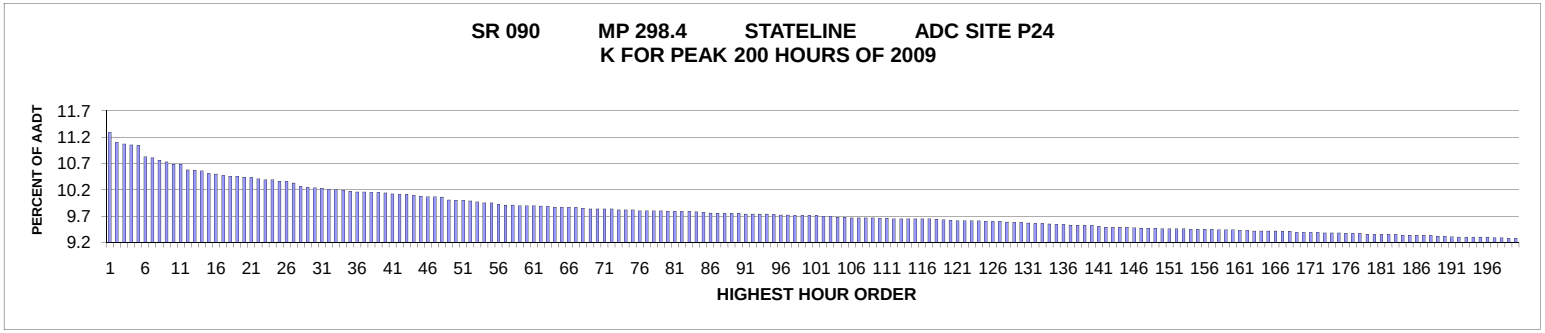

AADT= 47313 **K 30 FACTOR=** 10.24 **K 100 FACTOR=** 9.71 **K 200 FACTOR=** 9.27 **D FACTOR=** 56.62

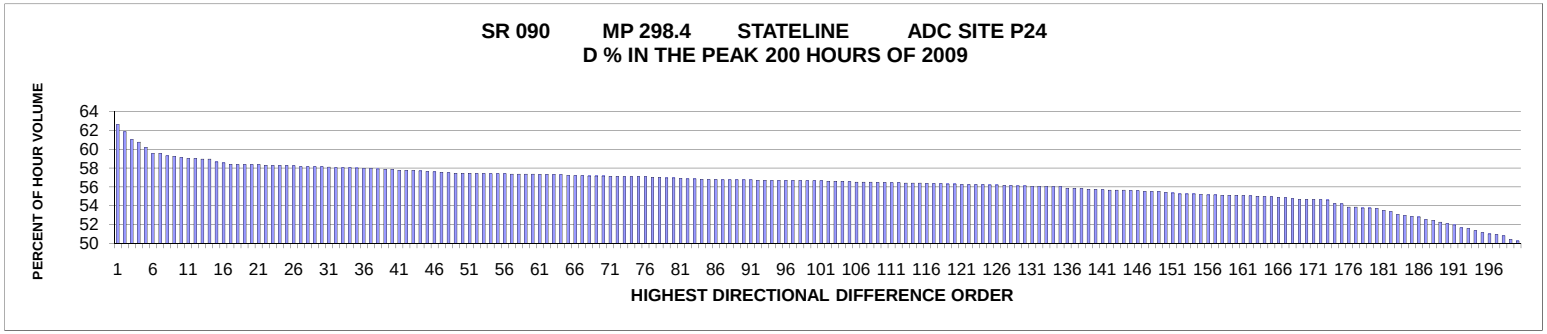

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	14	9	6	17	5344	11.29	1	47313	3153	2191	59	41
7	31	9	6	16	5253	11.1	2		2944	2309	56.04	43.96
7	31	9	6	18	5238	11.07	3		2886	2352	55.1	44.9
7	31	9	6	17	5226	11.05	4		2998	2228	57.37	42.63
8	14	9	6	18	5223	11.04	5		3087	2136	59.1	40.9
7	17	9	6	17	5126	10.83	6		2853	2273	55.66	44.34
8	7	9	6	17	5116	10.81	7		2960	2156	57.86	42.14
7	30	9	5	18	5092	10.76	8		2859	2233	56.15	43.85
8	6	9	5	18	5077	10.73	9		2917	2160	57.46	42.54
8	7	9	6	16	5058	10.69	10		2778	2280	54.92	45.08
7	24	9	6	18	5055	10.68	11		2995	2060	59.25	40.75
8	7	9	6	18	5005	10.58	12		2953	2052	59	41
7	16	9	5	18	4999	10.57	13		2856	2143	57.13	42.87
9	4	9	6	17	4998	10.56	14		2926	2072	58.54	41.46
8	6	9	5	17	4973	10.51	15		2832	2141	56.95	43.05
7	24	9	6	17	4969	10.5	16		2851	2118	57.38	42.62
7	23	9	5	18	4953	10.47	17		2874	2079	58.03	41.97

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	13	9	5	18	4951	10.46	18		2864	2087	57.85	42.15
7	2	9	5	17	4950	10.46	19		2859	2091	57.76	42.24
7	24	9	6	16	4938	10.44	20		2775	2163	56.2	43.8
7	29	9	4	18	4935	10.43	21	47313	2818	2117	57.1	42.9
6	12	9	6	17	4923	10.41	22		2918	2005	59.27	40.73
7	31	9	6	15	4918	10.39	23		2697	2221	54.84	45.16
8	13	9	5	17	4918	10.39	24		2803	2115	56.99	43.01
7	15	9	4	18	4902	10.36	25		2778	2124	56.67	43.33
7	17	9	6	18	4901	10.36	26		2856	2045	58.27	41.73
9	25	9	6	17	4886	10.33	27		2755	2131	56.39	43.61
8	11	9	3	18	4854	10.26	28		2720	2134	56.04	43.96
7	2	9	5	16	4848	10.25	29		2778	2070	57.3	42.7
6	12	9	6	18	4844	10.24	30		2943	1901	60.76	39.24
8	28	9	6	17	4838	10.23	31		2801	2037	57.9	42.1
5	29	9	6	17	4830	10.21	32		2663	2167	55.13	44.87
6	18	9	5	17	4826	10.2	33		2801	2025	58.04	41.96
7	23	9	5	17	4820	10.19	34		2732	2088	56.68	43.32
7	1	9	4	18	4810	10.17	35		2704	2106	56.22	43.78
9	4	9	6	18	4808	10.16	36		2750	2058	57.2	42.8
7	22	9	4	17	4807	10.16	37		2732	2075	56.83	43.17
5	22	9	6	17	4801	10.15	38		2759	2042	57.47	42.53
7	28	9	3	18	4800	10.15	39		2656	2144	55.33	44.67
7	30	9	5	17	4798	10.14	40		2670	2128	55.65	44.35
8	1	9	7	12	4789	10.12	41	47313	2852	1937	59.55	40.45
7	17	9	6	16	4782	10.11	42		2717	2065	56.82	43.18
5	15	9	6	17	4781	10.11	43		2691	2090	56.29	43.71
8	12	9	4	18	4776	10.09	44		2777	1999	58.14	41.86
7	2	9	5	18	4767	10.08	45		2717	2050	57	43
8	5	9	4	18	4766	10.07	46		2771	1995	58.14	41.86
8	1	9	7	13	4764	10.07	47		2838	1926	59.57	40.43
6	5	9	6	17	4760	10.06	48		2773	1987	58.26	41.74
9	4	9	6	16	4737	10.01	49		2689	2048	56.77	43.23
7	1	9	4	17	4732	10	50		2584	2148	54.61	45.39
7	17	9	6	15	4731	10	51		2683	2048	56.71	43.29
7	22	9	4	18	4725	9.99	52		2680	2045	56.72	43.28
8	13	9	5	16	4719	9.97	53		2620	2099	55.52	44.48
7	21	9	3	17	4710	9.95	54		2601	2109	55.22	44.78
8	3	9	2	17	4710	9.95	55		2666	2044	56.6	43.4
8	1	9	7	14	4693	9.92	56		2663	2030	56.74	43.26
5	15	9	6	18	4688	9.91	57		2635	2053	56.21	43.79
8	3	9	2	18	4688	9.91	58		2669	2019	56.93	43.07
5	29	9	6	18	4686	9.9	59		2690	1996	57.41	42.59
7	15	9	4	17	4685	9.9	60		2561	2124	54.66	45.34
8	10	9	2	17	4683	9.9	61	47313	2651	2032	56.61	43.39
9	3	9	5	18	4677	9.89	62		2670	2007	57.09	42.91
8	11	9	3	17	4676	9.88	63		2622	2054	56.07	43.93
5	8	9	6	18	4672	9.87	64		2651	2021	56.74	43.26
7	21	9	3	18	4671	9.87	65		2602	2069	55.71	44.29
8	12	9	4	17	4668	9.87	66		2578	2090	55.23	44.77
11	20	9	6	17	4666	9.86	67		2691	1975	57.67	42.33
7	29	9	4	17	4660	9.85	68		2622	2038	56.27	43.73
8	5	9	4	17	4657	9.84	69		2663	1994	57.18	42.82

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	2	9	1	15	4656	9.84	70		2346	2310	50.39	49.61
7	3	9	6	14	4655	9.84	71		2803	1852	60.21	39.79
8	28	9	6	16	4654	9.84	72		2713	1941	58.29	41.71
6	24	9	4	18	4648	9.82	73		2554	2094	54.95	45.05
8	14	9	6	15	4648	9.82	74		2440	2208	52.5	47.5
12	18	9	6	17	4647	9.82	75		2596	2051	55.86	44.14
2	13	9	6	18	4639	9.8	76		2734	1905	58.94	41.06
8	1	9	7	15	4638	9.8	77		2582	2056	55.67	44.33
6	5	9	6	18	4636	9.8	78		2694	1942	58.11	41.89
7	8	9	4	18	4635	9.8	79		2605	2030	56.2	43.8
8	2	9	1	14	4634	9.79	80		2495	2139	53.84	46.16
8	7	9	6	15	4634	9.79	81	47313	2393	2241	51.64	48.36
5	14	9	5	17	4633	9.79	82		2548	2085	55	45
7	27	9	2	18	4632	9.79	83		2576	2056	55.61	44.39
8	28	9	6	18	4627	9.78	84		2507	2120	54.18	45.82
8	26	9	4	18	4622	9.77	85		2623	1999	56.75	43.25
7	28	9	3	17	4620	9.76	86		2564	2056	55.5	44.5
5	1	9	6	17	4615	9.75	87		2618	1997	56.73	43.27
7	8	9	4	17	4614	9.75	88		2602	2012	56.39	43.61
12	23	9	4	17	4614	9.75	89		2650	1964	57.43	42.57
9	25	9	6	18	4611	9.75	90		2610	2001	56.6	43.4
7	20	9	2	18	4610	9.74	91		2575	2035	55.86	44.14
8	4	9	3	17	4610	9.74	92		2582	2028	56.01	43.99
8	4	9	3	18	4610	9.74	93		2595	2015	56.29	43.71
3	20	9	6	17	4609	9.74	94		2641	1968	57.3	42.7
9	18	9	6	18	4603	9.73	95		2607	1996	56.64	43.36
9	18	9	6	17	4601	9.72	96		2592	2009	56.34	43.66
6	18	9	5	18	4597	9.72	97		2683	1914	58.36	41.64
7	26	9	1	14	4594	9.71	98		2307	2287	50.22	49.78
2	13	9	6	17	4593	9.71	99		2680	1913	58.35	41.65
7	30	9	5	16	4593	9.71	100		2560	2033	55.74	44.26
7	20	9	2	17	4592	9.71	101	47313	2555	2037	55.64	44.36
7	7	9	3	18	4586	9.69	102		2629	1957	57.33	42.67
6	12	9	6	16	4583	9.69	103		2638	1945	57.56	42.44
8	1	9	7	16	4580	9.68	104		2417	2163	52.77	47.23
8	2	9	1	13	4580	9.68	105		2392	2188	52.23	47.77
5	8	9	6	17	4575	9.67	106		2458	2117	53.73	46.27
5	15	9	6	16	4574	9.67	107		2462	2112	53.83	46.17
5	22	9	6	16	4573	9.67	108		2582	1991	56.46	43.54
7	24	9	6	15	4573	9.67	109		2610	1963	57.07	42.93
5	1	9	6	18	4572	9.66	110		2592	1980	56.69	43.31
10	2	9	6	17	4569	9.66	111		2631	1938	57.58	42.42
7	6	9	2	17	4568	9.65	112		2494	2074	54.6	45.4
8	10	9	2	18	4568	9.65	113		2580	1988	56.48	43.52
6	23	9	3	17	4566	9.65	114		2677	1889	58.63	41.37
7	31	9	6	14	4565	9.65	115		2453	2112	53.73	46.27
10	2	9	6	18	4565	9.65	116		2648	1917	58.01	41.99
9	25	9	6	16	4564	9.65	117		2577	1987	56.46	43.54
5	21	9	5	18	4562	9.64	118		2614	1948	57.3	42.7
7	3	9	6	13	4558	9.63	119		2781	1777	61.01	38.99
8	7	9	6	14	4552	9.62	120		2327	2225	51.12	48.88
6	11	9	5	17	4549	9.61	121	47313	2570	1979	56.5	43.5

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
10	9	9	6	17	4547	9.61	122		2495	2052	54.87	45.13
9	17	9	5	17	4546	9.61	123		2597	1949	57.13	42.87
7	31	9	6	12	4545	9.61	124		2565	1980	56.44	43.56
3	13	9	6	17	4543	9.6	125		2549	1994	56.11	43.89
6	10	9	4	18	4543	9.6	126		2567	1976	56.5	43.5
8	27	9	5	18	4542	9.6	127		2604	1938	57.33	42.67
4	24	9	6	17	4537	9.59	128		2591	1946	57.11	42.89
4	10	9	6	17	4533	9.58	129		2571	1962	56.72	43.28
7	2	9	5	15	4533	9.58	130		2627	1906	57.95	42.05
12	23	9	4	16	4529	9.57	131		2560	1969	56.52	43.48
8	26	9	4	17	4525	9.56	132		2635	1890	58.23	41.77
6	24	9	4	17	4522	9.56	133		2542	1980	56.21	43.79
9	3	9	5	17	4519	9.55	134		2572	1947	56.92	43.08
7	17	9	6	14	4513	9.54	135		2487	2026	55.11	44.89
6	16	9	3	18	4512	9.54	136		2530	1982	56.07	43.93
9	10	9	5	17	4511	9.53	137		2507	2004	55.58	44.42
6	11	9	5	18	4509	9.53	138		2527	1982	56.04	43.96
7	31	9	6	13	4508	9.53	139		2485	2023	55.12	44.88
10	2	9	6	16	4503	9.52	140		2481	2022	55.1	44.9
8	15	9	7	14	4496	9.5	141	47313	2399	2097	53.36	46.64
8	15	9	7	13	4492	9.49	142		2378	2114	52.94	47.06
9	1	9	3	18	4490	9.49	143		2603	1887	57.97	42.03
8	14	9	6	14	4489	9.49	144		2304	2185	51.33	48.67
9	24	9	5	17	4489	9.49	145		2621	1868	58.39	41.61
7	6	9	2	18	4483	9.48	146		2528	1955	56.39	43.61
4	17	9	6	17	4481	9.47	147		2510	1971	56.01	43.99
7	16	9	5	17	4481	9.47	148		2378	2103	53.07	46.93
12	4	9	6	17	4479	9.47	149		2604	1875	58.14	41.86
4	24	9	6	18	4478	9.46	150		2559	1919	57.15	42.85
5	28	9	5	17	4477	9.46	151		2556	1921	57.09	42.91
7	7	9	3	17	4477	9.46	152		2523	1954	56.35	43.65
8	2	9	1	16	4477	9.46	153		2110	2367	47.13	52.87
7	16	9	5	16	4473	9.45	154		2478	1995	55.4	44.6
6	4	9	5	17	4472	9.45	155		2569	1903	57.45	42.55
5	21	9	5	17	4470	9.45	156		2568	1902	57.45	42.55
11	25	9	4	16	4470	9.45	157		2424	2046	54.23	45.77
6	5	9	6	16	4468	9.44	158		2459	2009	55.04	44.96
7	25	9	7	13	4468	9.44	159		2575	1893	57.63	42.37
7	18	9	7	13	4466	9.44	160		2602	1864	58.26	41.74
8	14	9	6	16	4463	9.43	161	47313	2318	2145	51.94	48.06
5	22	9	6	18	4460	9.43	162		2558	1902	57.35	42.65
7	3	9	6	12	4459	9.42	163		2758	1701	61.85	38.15
6	22	9	2	18	4458	9.42	164		2488	1970	55.81	44.19
9	16	9	4	17	4458	9.42	165		2395	2063	53.72	46.28
4	3	9	6	18	4455	9.42	166		2459	1996	55.2	44.8
11	6	9	6	17	4454	9.41	167		2600	1854	58.37	41.63
3	6	9	6	17	4452	9.41	168		2572	1880	57.77	42.23
4	3	9	6	17	4445	9.39	169		2577	1868	57.98	42.02
2	27	9	6	17	4444	9.39	170		2507	1937	56.41	43.59
8	1	9	7	11	4444	9.39	171		2783	1661	62.62	37.38
7	18	9	7	14	4443	9.39	172		2541	1902	57.19	42.81
8	8	9	7	14	4438	9.38	173		2263	2175	50.99	49.01

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
9	18	9	6	16	4438	9.38	174		2513	1925	56.62	43.38
6	3	9	4	18	4437	9.38	175		2499	1938	56.32	43.68
8	15	9	7	15	4433	9.37	176		2308	2125	52.06	47.94
7	1	9	4	16	4432	9.37	177		2425	2007	54.72	45.28
10	1	9	5	17	4431	9.37	178		2510	1921	56.65	43.35
7	27	9	2	17	4427	9.36	179		2445	1982	55.23	44.77
6	10	9	4	17	4426	9.35	180		2584	1842	58.38	41.62
6	16	9	3	17	4425	9.35	181	47313	2535	1890	57.29	42.71
8	9	9	1	14	4424	9.35	182		2281	2143	51.56	48.44
9	4	9	6	15	4424	9.35	183		2367	2057	53.5	46.5
4	16	9	5	17	4421	9.34	184		2506	1915	56.68	43.32
5	14	9	5	18	4421	9.34	185		2434	1987	55.06	44.94
6	4	9	5	18	4418	9.34	186		2521	1897	57.06	42.94
7	14	9	3	17	4418	9.34	187		2503	1915	56.65	43.35
10	16	9	6	17	4416	9.33	188		2532	1884	57.34	42.66
7	14	9	3	18	4411	9.32	189		2411	2000	54.66	45.34
3	26	9	5	17	4410	9.32	190		2497	1913	56.62	43.38
7	26	9	1	13	4407	9.31	191		2164	2243	49.1	50.9
7	19	9	1	14	4401	9.3	192		2308	2093	52.44	47.56
9	2	9	4	17	4401	9.3	193		2500	1901	56.81	43.19
9	23	9	4	17	4401	9.3	194		2542	1859	57.76	42.24
10	9	9	6	18	4399	9.3	195		2442	1957	55.51	44.49
4	17	9	6	18	4398	9.3	196		2593	1805	58.96	41.04
7	3	9	6	15	4397	9.29	197		2556	1841	58.13	41.87
8	8	9	7	12	4397	9.29	198		2233	2164	50.78	49.22
8	28	9	6	15	4387	9.27	199		2398	1989	54.66	45.34
7	13	9	2	17	4386	9.27	200		2517	1869	57.39	42.61

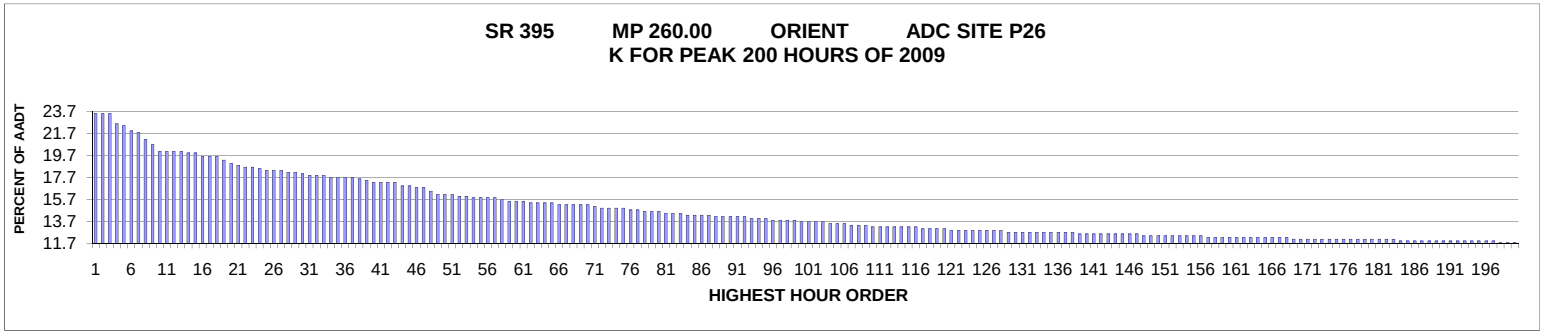

AADT= 638 **K 30 FACTOR=** 18.03 **K 100 FACTOR=** 13.64 **K 200 FACTOR=** 11.76 **D FACTOR=** 57.48

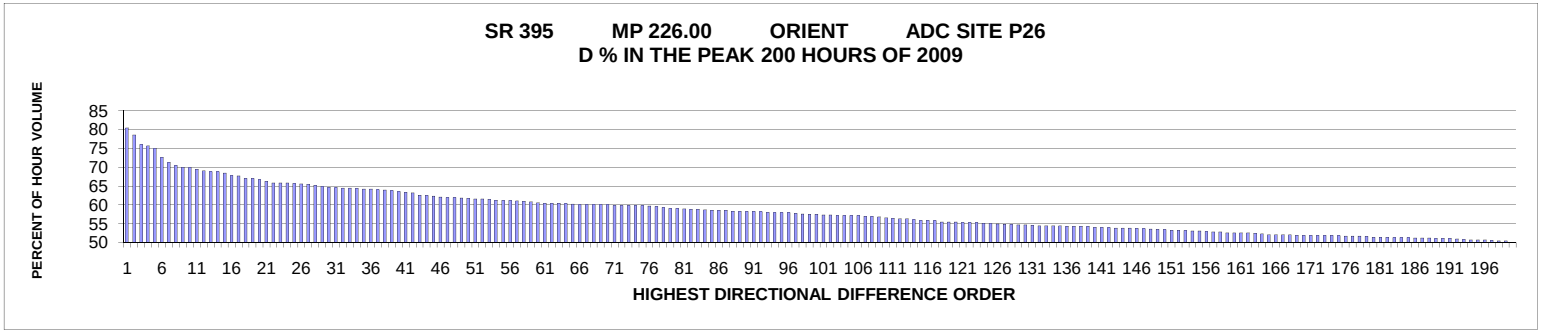

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	18	9	7	16	150	23.51	1	638	69	81	46	54
7	18	9	7	17	150	23.51	2		72	78	48	52
7	25	9	7	13	150	23.51	3		78	72	52	48
7	18	9	7	18	144	22.57	4		57	87	39.58	60.42
7	18	9	7	15	143	22.41	5		92	51	64.34	35.66
8	1	9	7	18	140	21.94	6		63	77	45	55
7	18	9	7	13	139	21.79	7		99	40	71.22	28.78
7	11	9	7	17	135	21.16	8		65	70	48.15	51.85
7	19	9	1	15	132	20.69	9		73	59	55.3	44.7
7	19	9	1	17	128	20.06	10		57	71	44.53	55.47
7	19	9	1	18	128	20.06	11		49	79	38.28	61.72
7	25	9	7	18	128	20.06	12		68	60	53.13	46.88
7	26	9	1	11	128	20.06	13		25	103	19.53	80.47
7	25	9	7	14	127	19.91	14		67	60	52.76	47.24
8	2	9	1	18	127	19.91	15		54	73	42.52	57.48
7	5	9	1	15	125	19.59	16		57	68	45.6	54.4
7	18	9	7	14	125	19.59	17		77	48	61.6	38.4

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	26	9	1	17	125	19.59	18		58	67	46.4	53.6
7	11	9	7	14	123	19.28	19		86	37	69.92	30.08
8	1	9	7	13	121	18.97	20		82	39	67.77	32.23
7	25	9	7	17	120	18.81	21	638	59	61	49.17	50.83
7	11	9	7	18	119	18.65	22		48	71	40.34	59.66
7	18	9	7	19	119	18.65	23		49	70	41.18	58.82
7	4	9	7	16	118	18.5	24		56	62	47.46	52.54
7	25	9	7	12	117	18.34	25		58	59	49.57	50.43
7	26	9	1	14	117	18.34	26		57	60	48.72	51.28
8	1	9	7	16	117	18.34	27		53	64	45.3	54.7
7	5	9	1	16	116	18.18	28		60	56	51.72	48.28
8	1	9	7	12	116	18.18	29		50	66	43.1	56.9
7	25	9	7	16	115	18.03	30		72	43	62.61	37.39
7	25	9	7	19	114	17.87	31		52	62	45.61	54.39
8	1	9	7	14	114	17.87	32		74	40	64.91	35.09
8	2	9	1	15	114	17.87	33		69	45	60.53	39.47
7	3	9	6	16	113	17.71	34		63	50	55.75	44.25
7	11	9	7	16	113	17.71	35		58	55	51.33	48.67
7	19	9	1	19	113	17.71	36		48	65	42.48	57.52
8	1	9	7	17	113	17.71	37		56	57	49.56	50.44
8	15	9	7	13	112	17.55	38		63	49	56.25	43.75
7	17	9	6	17	111	17.4	39		58	53	52.25	47.75
7	17	9	6	15	110	17.24	40		71	39	64.55	35.45
7	18	9	7	20	110	17.24	41	638	38	72	34.55	65.45
7	26	9	1	12	110	17.24	42		46	64	41.82	58.18
7	26	9	1	15	110	17.24	43		56	54	50.91	49.09
7	5	9	1	17	108	16.93	44		57	51	52.78	47.22
7	31	9	6	15	108	16.93	45		58	50	53.7	46.3
7	11	9	7	13	107	16.77	46		60	47	56.07	43.93
8	1	9	7	19	107	16.77	47		43	64	40.19	59.81
7	11	9	7	15	105	16.46	48		63	42	60	40
7	4	9	7	13	103	16.14	49		69	34	66.99	33.01
7	26	9	1	16	103	16.14	50		59	44	57.28	42.72
8	11	9	3	12	103	16.14	51		40	63	38.83	61.17
7	8	9	4	15	102	15.99	52		47	55	46.08	53.92
8	2	9	1	14	102	15.99	53		61	41	59.8	40.2
7	18	9	7	12	101	15.83	54		56	45	55.45	44.55
7	19	9	1	16	101	15.83	55		48	53	47.52	52.48
7	31	9	6	16	101	15.83	56		47	54	46.53	53.47
8	2	9	1	16	101	15.83	57		57	44	56.44	43.56
7	24	9	6	15	100	15.67	58		67	33	67	33
7	25	9	7	15	99	15.52	59		67	32	67.68	32.32
8	1	9	7	15	99	15.52	60		65	34	65.66	34.34
8	2	9	1	17	99	15.52	61	638	47	52	47.47	52.53
7	4	9	7	17	98	15.36	62		45	53	45.92	54.08
7	26	9	1	19	98	15.36	63		42	56	42.86	57.14
7	31	9	6	17	98	15.36	64		51	47	52.04	47.96
8	3	9	2	15	98	15.36	65		59	39	60.2	39.8
7	22	9	4	14	97	15.2	66		58	39	59.79	40.21
7	22	9	4	17	97	15.2	67		56	41	57.73	42.27
7	24	9	6	16	97	15.2	68		60	37	61.86	38.14
8	2	9	1	13	97	15.2	69		53	44	54.64	45.36

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	3	9	2	17	97	15.2	70		58	39	59.79	40.21
7	4	9	7	14	96	15.05	71		61	35	63.54	36.46
7	3	9	6	17	95	14.89	72		55	40	57.89	42.11
7	16	9	5	17	95	14.89	73		57	38	60	40
7	31	9	6	13	95	14.89	74		52	43	54.74	45.26
8	4	9	3	16	95	14.89	75		44	51	46.32	53.68
7	25	9	7	11	94	14.73	76		50	44	53.19	46.81
7	26	9	1	13	94	14.73	77		43	51	45.74	54.26
7	11	9	7	19	93	14.58	78		42	51	45.16	54.84
7	24	9	6	17	93	14.58	79		61	32	65.59	34.41
8	9	9	1	14	93	14.58	80		45	48	48.39	51.61
7	24	9	6	13	92	14.42	81	638	54	38	58.7	41.3
7	24	9	6	19	92	14.42	82		60	32	65.22	34.78
7	27	9	2	14	92	14.42	83		45	47	48.91	51.09
7	8	9	4	12	91	14.26	84		33	58	36.26	63.74
7	8	9	4	14	91	14.26	85		38	53	41.76	58.24
7	27	9	2	19	91	14.26	86		49	42	53.85	46.15
8	22	9	7	17	91	14.26	87		47	44	51.65	48.35
7	3	9	6	12	90	14.11	88		46	44	51.11	48.89
7	8	9	4	11	90	14.11	89		33	57	36.67	63.33
7	8	9	4	13	90	14.11	90		35	55	38.89	61.11
8	3	9	2	16	90	14.11	91		46	44	51.11	48.89
8	9	9	1	13	90	14.11	92		37	53	41.11	58.89
7	19	9	1	14	89	13.95	93		51	38	57.3	42.7
7	31	9	6	18	89	13.95	94		57	32	64.04	35.96
8	6	9	5	15	89	13.95	95		53	36	59.55	40.45
7	20	9	2	18	88	13.79	96		44	44	50	50
8	3	9	2	12	88	13.79	97		38	50	43.18	56.82
8	3	9	2	18	88	13.79	98		66	22	75	25
8	4	9	3	13	88	13.79	99		47	41	53.41	46.59
7	22	9	4	16	87	13.64	100		54	33	62.07	37.93
7	24	9	6	12	87	13.64	101	638	42	45	48.28	51.72
7	29	9	4	14	87	13.64	102		46	41	52.87	47.13
9	4	9	6	15	87	13.64	103		51	36	58.62	41.38
7	21	9	3	13	86	13.48	104		34	52	39.53	60.47
7	28	9	3	17	86	13.48	105		49	37	56.98	43.02
9	4	9	6	12	86	13.48	106		31	55	36.05	63.95
7	4	9	7	12	85	13.32	107		50	35	58.82	41.18
7	12	9	1	16	85	13.32	108		44	41	51.76	48.24
7	28	9	3	16	85	13.32	109		51	34	60	40
7	3	9	6	13	84	13.17	110		58	26	69.05	30.95
7	17	9	6	18	84	13.17	111		43	41	51.19	48.81
7	27	9	2	17	84	13.17	112		52	32	61.9	38.1
7	29	9	4	13	84	13.17	113		41	43	48.81	51.19
8	6	9	5	11	84	13.17	114		18	66	21.43	78.57
8	8	9	7	11	84	13.17	115		23	61	27.38	72.62
8	9	9	1	16	84	13.17	116		49	35	58.33	41.67
8	8	9	7	13	83	13.01	117		39	44	46.99	53.01
8	9	9	1	15	83	13.01	118		42	41	50.6	49.4
8	15	9	7	12	83	13.01	119		37	46	44.58	55.42
8	22	9	7	16	83	13.01	120		51	32	61.45	38.55
7	4	9	7	15	82	12.85	121	638	45	37	54.88	45.12

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	7	9	3	11	82	12.85	122		29	53	35.37	64.63
7	19	9	1	12	82	12.85	123		48	34	58.54	41.46
8	2	9	1	19	82	12.85	124		32	50	39.02	60.98
8	8	9	7	15	82	12.85	125		42	40	51.22	48.78
8	17	9	2	11	82	12.85	126		28	54	34.15	65.85
9	6	9	1	11	82	12.85	127		25	57	30.49	69.51
10	9	9	6	13	82	12.85	128		34	48	41.46	58.54
7	12	9	1	17	81	12.7	129		49	32	60.49	39.51
7	20	9	2	16	81	12.7	130		44	37	54.32	45.68
7	26	9	1	18	81	12.7	131		44	37	54.32	45.68
7	28	9	3	18	81	12.7	132		52	29	64.2	35.8
7	30	9	5	12	81	12.7	133		29	52	35.8	64.2
7	31	9	6	12	81	12.7	134		37	44	45.68	54.32
8	1	9	7	11	81	12.7	135		38	43	46.91	53.09
8	7	9	6	14	81	12.7	136		42	39	51.85	48.15
8	9	9	1	17	81	12.7	137		47	34	58.02	41.98
8	28	9	6	16	81	12.7	138		48	33	59.26	40.74
7	5	9	1	12	80	12.54	139		41	39	51.25	48.75
7	7	9	3	13	80	12.54	140		25	55	31.25	68.75
7	19	9	1	13	80	12.54	141	638	45	35	56.25	43.75
7	21	9	3	16	80	12.54	142		50	30	62.5	37.5
8	7	9	6	16	80	12.54	143		46	34	57.5	42.5
8	8	9	7	12	80	12.54	144		24	56	30	70
8	8	9	7	14	80	12.54	145		49	31	61.25	38.75
8	11	9	3	16	80	12.54	146		48	32	60	40
8	15	9	7	18	80	12.54	147		41	39	51.25	48.75
7	5	9	1	13	79	12.38	148		36	43	45.57	54.43
7	12	9	1	13	79	12.38	149		31	48	39.24	60.76
7	22	9	4	18	79	12.38	150		41	38	51.9	48.1
8	3	9	2	14	79	12.38	151		46	33	58.23	41.77
8	15	9	7	10	79	12.38	152		38	41	48.1	51.9
8	15	9	7	17	79	12.38	153		38	41	48.1	51.9
8	18	9	3	13	79	12.38	154		39	40	49.37	50.63
8	30	9	1	18	79	12.38	155		43	36	54.43	45.57
9	7	9	2	13	79	12.38	156		33	46	41.77	58.23
7	3	9	6	15	78	12.23	157		41	37	52.56	47.44
7	16	9	5	19	78	12.23	158		48	30	61.54	38.46
7	22	9	4	15	78	12.23	159		43	35	55.13	44.87
7	27	9	2	13	78	12.23	160		41	37	52.56	47.44
7	28	9	3	14	78	12.23	161	638	46	32	58.97	41.03
8	3	9	2	10	78	12.23	162		23	55	29.49	70.51
8	4	9	3	17	78	12.23	163		47	31	60.26	39.74
8	11	9	3	11	78	12.23	164		26	52	33.33	66.67
8	14	9	6	17	78	12.23	165		59	19	75.64	24.36
8	18	9	3	11	78	12.23	166		36	42	46.15	53.85
8	29	9	7	14	78	12.23	167		36	42	46.15	53.85
9	7	9	2	11	78	12.23	168		32	46	41.03	58.97
7	5	9	1	18	77	12.07	169		38	39	49.35	50.65
7	17	9	6	16	77	12.07	170		48	29	62.34	37.66
7	26	9	1	20	77	12.07	171		31	46	40.26	59.74
7	29	9	4	17	77	12.07	172		38	39	49.35	50.65
8	2	9	1	11	77	12.07	173		33	44	42.86	57.14

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	2	9	1	12	77	12.07	174		37	40	48.05	51.95
8	6	9	5	14	77	12.07	175		36	41	46.75	53.25
8	15	9	7	14	77	12.07	176		44	33	57.14	42.86
8	16	9	1	15	77	12.07	177		30	47	38.96	61.04
8	19	9	4	15	77	12.07	178		53	24	68.83	31.17
8	22	9	7	13	77	12.07	179		43	34	55.84	44.16
8	23	9	1	14	77	12.07	180		44	33	57.14	42.86
9	3	9	5	17	77	12.07	181	638	35	42	45.45	54.55
9	7	9	2	12	77	12.07	182		26	51	33.77	66.23
10	8	9	5	16	77	12.07	183		43	34	55.84	44.16
7	13	9	2	15	76	11.91	184		44	32	57.89	42.11
7	20	9	2	14	76	11.91	185		50	26	65.79	34.21
7	28	9	3	15	76	11.91	186		39	37	51.32	48.68
7	31	9	6	10	76	11.91	187		27	49	35.53	64.47
7	31	9	6	19	76	11.91	188		37	39	48.68	51.32
8	4	9	3	12	76	11.91	189		28	48	36.84	63.16
8	9	9	1	18	76	11.91	190		42	34	55.26	44.74
8	11	9	3	13	76	11.91	191		29	47	38.16	61.84
8	12	9	4	11	76	11.91	192		24	52	31.58	68.42
8	14	9	6	18	76	11.91	193		50	26	65.79	34.21
8	15	9	7	16	76	11.91	194		43	33	56.58	43.42
8	16	9	1	12	76	11.91	195		27	49	35.53	64.47
8	17	9	2	16	76	11.91	196		42	34	55.26	44.74
9	2	9	4	14	76	11.91	197		32	44	42.11	57.89
7	13	9	2	13	75	11.76	198		18	57	24	76
7	20	9	2	17	75	11.76	199		36	39	48	52
7	22	9	4	13	75	11.76	200		45	30	60	40

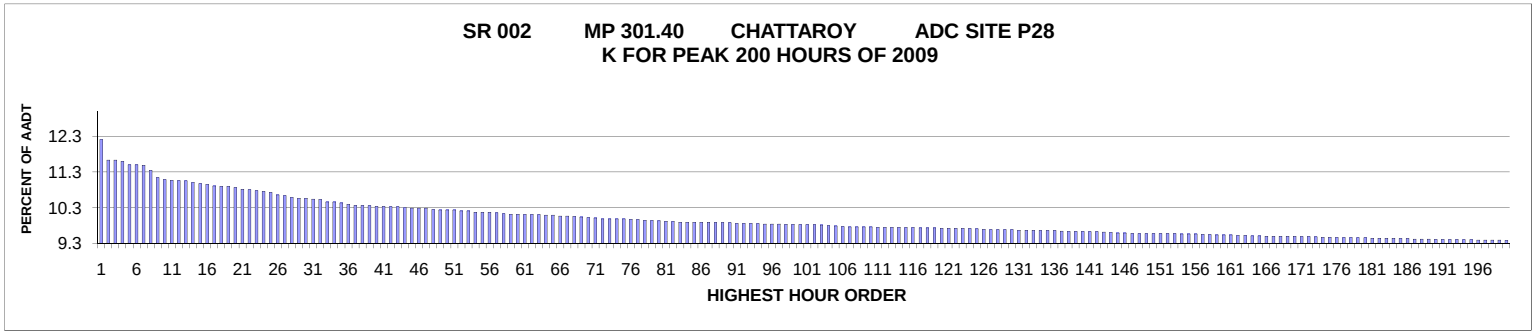

AADT= 17309 **K 30 FACTOR=** 10.57 **K 100 FACTOR=** 9.82 **K 200 FACTOR=** 9.38 **D FACTOR=** 67.21

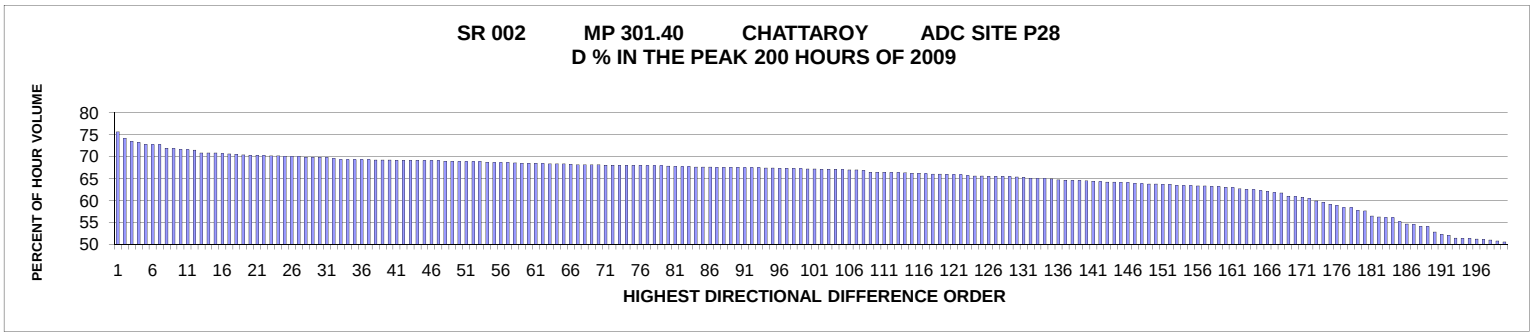

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
5	22	9	6	17	2114	12.21	1	17309	1513	601	71.57	28.43
9	4	9	6	17	2015	11.64	2		1419	596	70.42	29.58
9	4	9	6	18	2014	11.64	3		1440	574	71.5	28.5
7	2	9	5	17	2008	11.6	4		1413	595	70.37	29.63
5	22	9	6	18	1991	11.5	5		1478	513	74.23	25.77
6	5	9	6	18	1990	11.5	6		1259	731	63.27	36.73
7	5	9	1	15	1989	11.49	7		735	1254	36.95	63.05
7	31	9	6	17	1965	11.35	8		1332	633	67.79	32.21
7	31	9	6	18	1928	11.14	9		1381	547	71.63	28.37
7	24	9	6	18	1920	11.09	10		1381	539	71.93	28.07
6	26	9	6	17	1916	11.07	11		1290	626	67.33	32.67
7	10	9	6	18	1915	11.06	12		1347	568	70.34	29.66
7	17	9	6	18	1913	11.05	13		1353	560	70.73	29.27
6	5	9	6	17	1905	11.01	14		1194	711	62.68	37.32
7	3	9	6	13	1899	10.97	15		1204	695	63.4	36.6
7	5	9	1	16	1896	10.95	16		594	1302	31.33	68.67
6	12	9	6	18	1889	10.91	17		1321	568	69.93	30.07

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	24	9	6	17	1887	10.9	18		1299	588	68.84	31.16
7	2	9	5	18	1886	10.9	19		1372	514	72.75	27.25
8	14	9	6	17	1879	10.86	20		1233	646	65.62	34.38
8	14	9	6	18	1873	10.82	21	17309	1322	551	70.58	29.42
9	25	9	6	17	1869	10.8	22		1305	564	69.82	30.18
6	12	9	6	17	1865	10.77	23		1262	603	67.67	32.33
5	29	9	6	18	1862	10.76	24		1282	580	68.85	31.15
8	28	9	6	18	1857	10.73	25		1352	505	72.81	27.19
5	15	9	6	17	1845	10.66	26		1224	621	66.34	33.66
7	8	9	4	18	1842	10.64	27		1245	597	67.59	32.41
6	26	9	6	18	1833	10.59	28		1267	566	69.12	30.88
5	22	9	6	16	1830	10.57	29		1183	647	64.64	35.36
7	5	9	1	14	1829	10.57	30		602	1227	32.91	67.09
7	1	9	4	18	1825	10.54	31		1243	582	68.11	31.89
8	7	9	6	18	1822	10.53	32		1237	585	67.89	32.11
8	28	9	6	17	1811	10.46	33		1243	568	68.64	31.36
7	18	9	7	13	1810	10.46	34		1016	794	56.13	43.87
10	16	9	6	17	1805	10.43	35		1150	655	63.71	36.29
7	10	9	6	17	1800	10.4	36		1235	565	68.61	31.39
7	17	9	6	17	1794	10.36	37		1254	540	69.9	30.1
5	1	9	6	17	1793	10.36	38		1175	618	65.53	34.47
7	26	9	1	15	1791	10.35	39		871	920	48.63	51.37
8	7	9	6	17	1788	10.33	40		1222	566	68.34	31.66
9	11	9	6	18	1788	10.33	41	17309	1222	566	68.34	31.66
9	4	9	6	16	1787	10.32	42		1138	649	63.68	36.32
7	31	9	6	16	1786	10.32	43		1133	653	63.44	36.56
7	5	9	1	13	1783	10.3	44		568	1215	31.86	68.14
7	1	9	4	17	1781	10.29	45		1184	597	66.48	33.52
8	21	9	6	17	1781	10.29	46		1216	565	68.28	31.72
10	2	9	6	18	1781	10.29	47		1230	551	69.06	30.94
9	11	9	6	17	1773	10.24	48		1177	596	66.38	33.62
8	11	9	3	18	1771	10.23	49		1196	575	67.53	32.47
6	19	9	6	17	1770	10.23	50		1225	545	69.21	30.79
6	19	9	6	18	1770	10.23	51		1297	473	73.28	26.72
9	8	9	3	18	1768	10.21	52		1175	593	66.46	33.54
10	16	9	6	18	1767	10.21	53		1210	557	68.48	31.52
7	2	9	5	16	1761	10.17	54		1096	665	62.24	37.76
9	25	9	6	18	1761	10.17	55		1248	513	70.87	29.13
8	21	9	6	18	1760	10.17	56		1265	495	71.88	28.13
10	9	9	6	18	1756	10.15	57		1211	545	68.96	31.04
7	30	9	5	18	1754	10.13	58		1214	540	69.21	30.79
7	3	9	6	12	1752	10.12	59		1094	658	62.44	37.56
8	26	9	4	18	1751	10.12	60		1181	570	67.45	32.55
7	24	9	6	16	1750	10.11	61	17309	1139	611	65.09	34.91
9	18	9	6	17	1750	10.11	62		1136	614	64.91	35.09
6	18	9	5	18	1749	10.1	63		1172	577	67.01	32.99
5	29	9	6	17	1746	10.09	64		1127	619	64.55	35.45
7	5	9	1	17	1746	10.09	65		531	1215	30.41	69.59
5	21	9	5	18	1741	10.06	66		1220	521	70.07	29.93
7	28	9	3	18	1741	10.06	67		1176	565	67.55	32.45
4	24	9	6	17	1740	10.05	68		1170	570	67.24	32.76
7	26	9	1	17	1737	10.04	69		603	1134	34.72	65.28

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
9	18	9	6	18	1734	10.02	70		1098	636	63.32	36.68
8	1	9	7	13	1733	10.01	71		937	796	54.07	45.93
6	18	9	5	17	1728	9.98	72		1095	633	63.37	36.63
8	6	9	5	18	1728	9.98	73		1181	547	68.34	31.66
7	14	9	3	18	1727	9.98	74		1220	507	70.64	29.36
9	23	9	4	18	1727	9.98	75		1177	550	68.15	31.85
7	3	9	6	16	1725	9.97	76		1158	567	67.13	32.87
7	9	9	5	18	1724	9.96	77		1192	532	69.14	30.86
8	31	9	2	17	1722	9.95	78		1127	595	65.45	34.55
7	17	9	6	16	1720	9.94	79		1106	614	64.3	35.7
8	1	9	7	12	1719	9.93	80		834	885	48.52	51.48
7	16	9	5	17	1717	9.92	81	17309	1111	606	64.71	35.29
10	2	9	6	17	1715	9.91	82		1121	594	65.36	34.64
7	20	9	2	18	1712	9.89	83		1186	526	69.28	30.72
8	9	9	1	15	1712	9.89	84		880	832	51.4	48.6
8	25	9	3	18	1712	9.89	85		1172	540	68.46	31.54
5	22	9	6	19	1711	9.89	86		1295	416	75.69	24.31
7	18	9	7	12	1711	9.89	87		876	835	51.2	48.8
5	27	9	4	18	1710	9.88	88		1165	545	68.13	31.87
7	12	9	1	15	1710	9.88	89		815	895	47.66	52.34
10	8	9	5	17	1709	9.87	90		1111	598	65.01	34.99
8	2	9	1	16	1707	9.86	91		666	1041	39.02	60.98
9	7	9	2	14	1707	9.86	92		531	1176	31.11	68.89
8	7	9	6	16	1706	9.86	93		1060	646	62.13	37.87
8	10	9	2	18	1705	9.85	94		1132	573	66.39	33.61
6	3	9	4	18	1704	9.84	95		1153	551	67.66	32.34
6	4	9	5	18	1704	9.84	96		1159	545	68.02	31.98
7	3	9	6	15	1704	9.84	97		1149	555	67.43	32.57
6	10	9	4	18	1702	9.83	98		1195	507	70.21	29.79
8	19	9	4	18	1702	9.83	99		1146	556	67.33	32.67
7	12	9	1	14	1700	9.82	100		772	928	45.41	54.59
7	3	9	6	14	1699	9.82	101	17309	1116	583	65.69	34.31
7	26	9	1	14	1699	9.82	102		830	869	48.85	51.15
10	1	9	5	18	1698	9.81	103		1137	561	66.96	33.04
8	1	9	7	11	1695	9.79	104		989	706	58.35	41.65
7	9	9	5	17	1692	9.78	105		1058	634	62.53	37.47
6	11	9	5	18	1691	9.77	106		1164	527	68.84	31.16
9	3	9	5	18	1690	9.76	107		1171	519	69.29	30.71
6	25	9	5	18	1689	9.76	108		1147	542	67.91	32.09
8	20	9	5	18	1689	9.76	109		1148	541	67.97	32.03
9	10	9	5	18	1689	9.76	110		1116	573	66.07	33.93
8	13	9	5	17	1688	9.75	111		1076	612	63.74	36.26
10	9	9	6	17	1688	9.75	112		1089	599	64.51	35.49
7	3	9	6	17	1687	9.75	113		1118	569	66.27	33.73
7	16	9	5	18	1687	9.75	114		1111	576	65.86	34.14
6	24	9	4	18	1686	9.74	115		1105	581	65.54	34.46
7	22	9	4	18	1686	9.74	116		1162	524	68.92	31.08
9	9	9	4	18	1685	9.73	117		1182	503	70.15	29.85
6	29	9	2	18	1684	9.73	118		1167	517	69.3	30.7
6	30	9	3	18	1684	9.73	119		1154	530	68.53	31.47
6	10	9	4	17	1683	9.72	120		1138	545	67.62	32.38
8	3	9	2	18	1683	9.72	121	17309	1181	502	70.17	29.83

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
4	24	9	6	18	1682	9.72	122		1176	506	69.92	30.08
5	15	9	6	16	1682	9.72	123		1039	643	61.77	38.23
5	25	9	2	14	1680	9.71	124		554	1126	32.98	67.02
5	21	9	5	17	1679	9.7	125		1133	546	67.48	32.52
7	27	9	2	18	1677	9.69	126		1160	517	69.17	30.83
8	17	9	2	18	1676	9.68	127		1151	525	68.68	31.32
6	16	9	3	18	1675	9.68	128		1186	489	70.81	29.19
7	23	9	5	18	1675	9.68	129		1158	517	69.13	30.87
8	6	9	5	17	1675	9.68	130		1110	565	66.27	33.73
5	15	9	6	18	1674	9.67	131		1134	540	67.74	32.26
6	5	9	6	16	1674	9.67	132		977	697	58.36	41.64
8	11	9	3	17	1674	9.67	133		1070	604	63.92	36.08
7	30	9	5	17	1672	9.66	134		1073	599	64.17	35.83
8	9	9	1	16	1672	9.66	135		688	984	41.15	58.85
9	25	9	6	16	1672	9.66	136		966	706	57.78	42.22
7	19	9	1	15	1668	9.64	137		851	817	51.02	48.98
5	8	9	6	17	1667	9.63	138		1084	583	65.03	34.97
6	2	9	3	18	1667	9.63	139		1171	496	70.25	29.75
9	7	9	2	16	1666	9.63	140		559	1107	33.55	66.45
9	24	9	5	17	1665	9.62	141	17309	1152	513	69.19	30.81
10	1	9	5	17	1665	9.62	142		1097	568	65.89	34.11
8	27	9	5	17	1664	9.61	143		1098	566	65.99	34.01
5	1	9	6	18	1661	9.6	144		1138	523	68.51	31.49
4	17	9	6	17	1660	9.59	145		1110	550	66.87	33.13
8	26	9	4	17	1660	9.59	146		1059	601	63.8	36.2
7	2	9	5	19	1658	9.58	147		1219	439	73.52	26.48
5	22	9	6	15	1657	9.57	148		988	669	59.63	40.37
5	28	9	5	17	1657	9.57	149		1061	596	64.03	35.97
5	28	9	5	18	1657	9.57	150		1161	496	70.07	29.93
8	14	9	6	16	1657	9.57	151		1023	634	61.74	38.26
6	30	9	3	17	1656	9.57	152		1070	586	64.61	35.39
8	18	9	3	18	1656	9.57	153		1148	508	69.32	30.68
6	15	9	2	18	1655	9.56	154		1173	482	70.88	29.12
7	3	9	6	11	1654	9.56	155		934	720	56.47	43.53
8	9	9	1	14	1654	9.56	156		742	912	44.86	55.14
7	21	9	3	18	1653	9.55	157		1143	510	69.15	30.85
7	11	9	7	13	1652	9.54	158		895	757	54.18	45.82
6	9	9	3	17	1650	9.53	159		1122	528	68	32
6	24	9	4	17	1650	9.53	160		1109	541	67.21	32.79
8	5	9	4	18	1650	9.53	161	17309	1109	541	67.21	32.79
6	28	9	1	16	1648	9.52	162		811	837	49.21	50.79
11	6	9	6	17	1647	9.52	163		1088	559	66.06	33.94
6	26	9	6	16	1646	9.51	164		1003	643	60.94	39.06
8	27	9	5	18	1646	9.51	165		1131	515	68.71	31.29
6	4	9	5	17	1645	9.5	166		1056	589	64.19	35.81
8	24	9	2	18	1645	9.5	167		1110	535	67.48	32.52
9	4	9	6	19	1645	9.5	168		1197	448	72.77	27.23
10	16	9	6	16	1645	9.5	169		985	660	59.88	40.12
8	8	9	7	13	1644	9.5	170		831	813	50.55	49.45
6	3	9	4	17	1643	9.49	171		1077	566	65.55	34.45
7	23	9	5	17	1642	9.49	172		1042	600	63.46	36.54
7	6	9	2	18	1641	9.48	173		1105	536	67.34	32.66

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	7	9	3	18	1640	9.47	174		1115	525	67.99	32.01
7	19	9	1	16	1639	9.47	175		694	945	42.34	57.66
5	18	9	2	18	1638	9.46	176		1113	525	67.95	32.05
6	2	9	3	17	1637	9.46	177		1106	531	67.56	32.44
7	29	9	4	17	1637	9.46	178		1074	563	65.61	34.39
7	11	9	7	12	1636	9.45	179		864	772	52.81	47.19
7	28	9	3	17	1635	9.45	180		1053	582	64.4	35.6
6	25	9	5	17	1634	9.44	181	17309	1110	524	67.93	32.07
7	25	9	7	13	1634	9.44	182		852	782	52.14	47.86
9	14	9	2	18	1634	9.44	183		1097	537	67.14	32.86
9	30	9	4	18	1634	9.44	184		1106	528	67.69	32.31
9	17	9	5	17	1633	9.43	185		1043	590	63.87	36.13
6	17	9	4	17	1632	9.43	186		1102	530	67.52	32.48
7	29	9	4	18	1631	9.42	187		1129	502	69.22	30.78
9	5	9	7	12	1631	9.42	188		918	713	56.28	43.72
9	16	9	4	18	1630	9.42	189		1076	554	66.01	33.99
7	10	9	6	16	1629	9.41	190		1029	600	63.17	36.83
6	23	9	3	18	1628	9.41	191		1128	500	69.29	30.71
7	6	9	2	17	1628	9.41	192		990	638	60.81	39.19
9	2	9	4	18	1628	9.41	193		1110	518	68.18	31.82
8	8	9	7	12	1627	9.4	194		738	889	45.36	54.64
8	15	9	7	12	1627	9.4	195		714	913	43.88	56.12
6	12	9	6	16	1626	9.39	196		983	643	60.46	39.54
7	26	9	1	16	1626	9.39	197		602	1024	37.02	62.98
10	9	9	6	16	1626	9.39	198		962	664	59.16	40.84
9	7	9	2	15	1625	9.39	199		519	1106	31.94	68.06
8	3	9	2	17	1624	9.38	200		1043	581	64.22	35.78

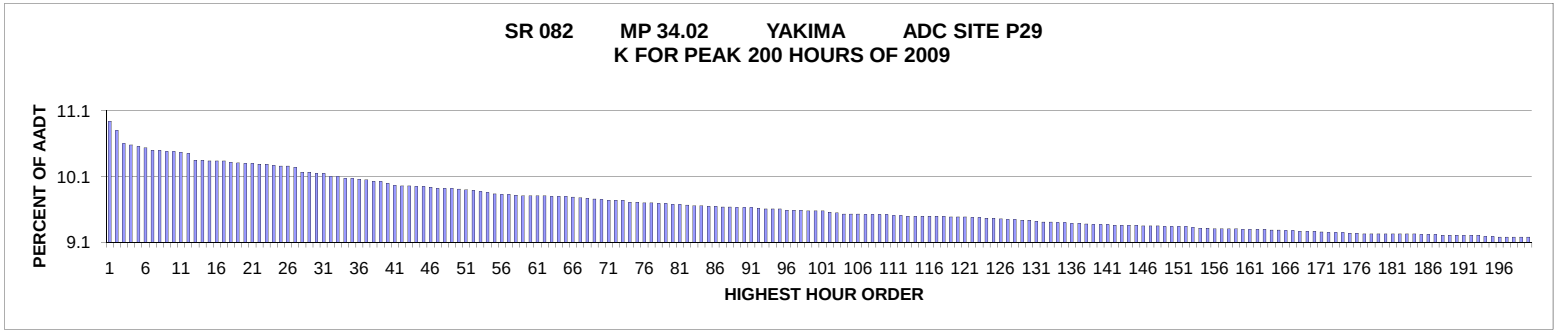

AADT= 45611 **K 30 FACTOR=** 10.15 **K 100 FACTOR=** 9.58 **K 200 FACTOR=** 9.18 **D FACTOR=** 50.89

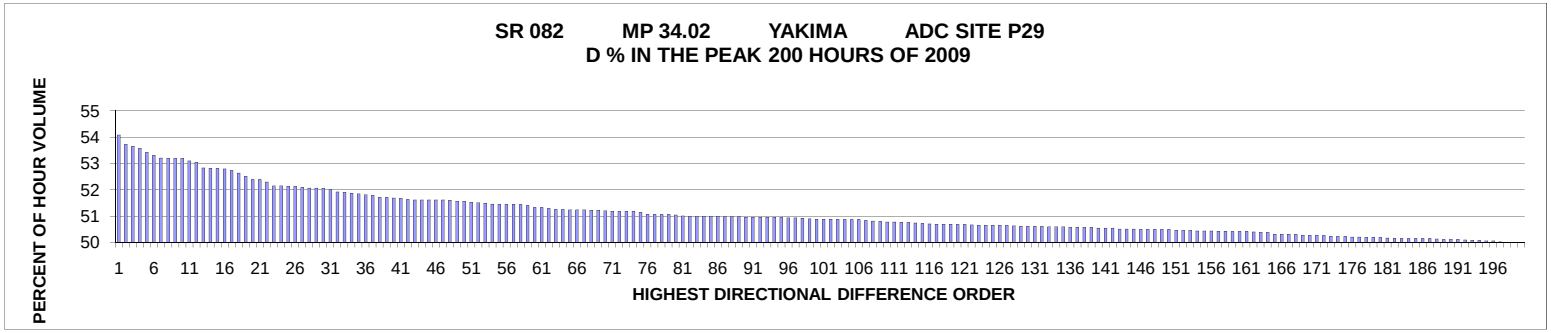

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
10	2	9	6	17	4988	10.94	1	45611	2478	2510	49.68	50.32
9	4	9	6	16	4927	10.8	2		2306	2621	46.8	53.2
9	25	9	6	17	4836	10.6	3		2433	2403	50.31	49.69
9	4	9	6	17	4827	10.58	4		2249	2578	46.59	53.41
6	19	9	6	17	4816	10.56	5		2543	2273	52.8	47.2
8	7	9	6	18	4809	10.54	6		2278	2531	47.37	52.63
8	7	9	6	17	4790	10.5	7		2335	2455	48.75	51.25
9	11	9	6	17	4789	10.5	8		2313	2476	48.3	51.7
10	2	9	6	18	4781	10.48	9		2422	2359	50.66	49.34
5	8	9	6	17	4778	10.48	10		2389	2389	50	50
10	9	9	6	17	4774	10.47	11		2450	2324	51.32	48.68
5	22	9	6	16	4766	10.45	12		2384	2382	50.02	49.98
9	4	9	6	18	4722	10.35	13		2277	2445	48.22	51.78
6	5	9	6	17	4719	10.35	14		2258	2461	47.85	52.15
6	19	9	6	16	4718	10.34	15		2324	2394	49.26	50.74
9	18	9	6	17	4717	10.34	16		2311	2406	48.99	51.01
10	9	9	6	16	4716	10.34	17		2347	2369	49.77	50.23

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
9	11	9	6	18	4708	10.32	18		2349	2359	49.89	50.11
6	26	9	6	16	4704	10.31	19		2240	2464	47.62	52.38
10	2	9	6	16	4699	10.3	20		2296	2403	48.86	51.14
5	15	9	6	17	4698	10.3	21	45611	2251	2447	47.91	52.09
10	9	9	6	18	4693	10.29	22		2404	2289	51.23	48.77
9	18	9	6	16	4692	10.29	23		2300	2392	49.02	50.98
5	8	9	6	16	4684	10.27	24		2422	2262	51.71	48.29
5	22	9	6	17	4681	10.26	25		2186	2495	46.7	53.3
9	25	9	6	18	4680	10.26	26		2426	2254	51.84	48.16
8	14	9	6	17	4672	10.24	27		2351	2321	50.32	49.68
6	26	9	6	17	4638	10.17	28		2276	2362	49.07	50.93
11	25	9	4	16	4637	10.17	29		2394	2243	51.63	48.37
11	25	9	4	17	4631	10.15	30		2446	2185	52.82	47.18
6	26	9	6	18	4630	10.15	31		2381	2249	51.43	48.57
4	24	9	6	17	4608	10.1	32		2301	2307	49.93	50.07
10	23	9	6	17	4605	10.1	33		2357	2248	51.18	48.82
7	10	9	6	17	4595	10.07	34		2272	2323	49.45	50.55
6	12	9	6	16	4593	10.07	35		2285	2308	49.75	50.25
5	15	9	6	18	4588	10.06	36		2225	2363	48.5	51.5
6	12	9	6	17	4585	10.05	37		2284	2301	49.81	50.19
10	16	9	6	17	4576	10.03	38		2356	2220	51.49	48.51
7	10	9	6	16	4573	10.03	39		2201	2372	48.13	51.87
8	14	9	6	16	4563	10	40		2188	2375	47.95	52.05
11	25	9	4	15	4549	9.97	41	45611	2319	2230	50.98	49.02
8	7	9	6	16	4544	9.96	42		2181	2363	48	52
6	19	9	6	18	4542	9.96	43		2312	2230	50.9	49.1
9	18	9	6	18	4540	9.95	44		2317	2223	51.04	48.96
9	11	9	6	16	4537	9.95	45		2225	2312	49.04	50.96
5	1	9	6	17	4536	9.94	46		2223	2313	49.01	50.99
4	17	9	6	17	4525	9.92	47		2297	2228	50.76	49.24
5	8	9	6	18	4525	9.92	48		2370	2155	52.38	47.62
8	14	9	6	18	4523	9.92	49		2305	2218	50.96	49.04
8	7	9	6	15	4520	9.91	50		2092	2428	46.28	53.72
4	10	9	6	17	4517	9.9	51		2258	2259	49.99	50.01
9	25	9	6	16	4509	9.89	52		2235	2274	49.57	50.43
6	25	9	5	18	4501	9.87	53		2277	2224	50.59	49.41
5	29	9	6	17	4497	9.86	54		2109	2388	46.9	53.1
10	30	9	6	17	4488	9.84	55		2199	2289	49	51
6	26	9	6	15	4485	9.83	56		2206	2279	49.19	50.81
7	2	9	5	18	4484	9.83	57		2254	2230	50.27	49.73
4	17	9	6	18	4481	9.82	58		2216	2265	49.45	50.55
7	2	9	5	17	4476	9.81	59		2233	2243	49.89	50.11
6	5	9	6	18	4475	9.81	60		2313	2162	51.69	48.31
10	16	9	6	18	4475	9.81	61	45611	2420	2055	54.08	45.92
7	24	9	6	17	4474	9.81	62		2276	2198	50.87	49.13
6	19	9	6	15	4472	9.8	63		2328	2144	52.06	47.94
7	2	9	5	16	4471	9.8	64		2204	2267	49.3	50.7
5	22	9	6	18	4469	9.8	65		2091	2378	46.79	53.21
5	15	9	6	16	4465	9.79	66		2180	2285	48.82	51.18
8	28	9	6	17	4461	9.78	67		2217	2244	49.7	50.3
4	24	9	6	18	4457	9.77	68		2314	2143	51.92	48.08
9	8	9	3	17	4451	9.76	69		2173	2278	48.82	51.18

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
10	23	9	6	18	4447	9.75	70		2278	2169	51.23	48.77
2	13	9	6	17	4442	9.74	71		2183	2259	49.14	50.86
4	3	9	6	17	4441	9.74	72		2267	2174	51.05	48.95
6	25	9	5	17	4441	9.74	73		2212	2229	49.81	50.19
7	17	9	6	15	4429	9.71	74		2214	2215	49.99	50.01
6	5	9	6	16	4428	9.71	75		2182	2246	49.28	50.72
7	17	9	6	17	4425	9.7	76		2143	2282	48.43	51.57
9	17	9	5	17	4423	9.7	77		2218	2205	50.15	49.85
7	17	9	6	16	4420	9.69	78		2219	2201	50.2	49.8
10	1	9	5	18	4418	9.69	79		2235	2183	50.59	49.41
3	13	9	6	17	4414	9.68	80		2203	2211	49.91	50.09
7	31	9	6	18	4413	9.68	81	45611	2327	2086	52.73	47.27
7	31	9	6	17	4409	9.67	82		2192	2217	49.72	50.28
10	1	9	5	17	4408	9.66	83		2169	2239	49.21	50.79
8	21	9	6	17	4404	9.66	84		2246	2158	51	49
11	6	9	6	17	4402	9.65	85		2168	2234	49.25	50.75
5	29	9	6	16	4401	9.65	86		2110	2291	47.94	52.06
5	22	9	6	15	4399	9.64	87		2254	2145	51.24	48.76
10	16	9	6	16	4397	9.64	88		2225	2172	50.6	49.4
9	3	9	5	17	4393	9.63	89		2074	2319	47.21	52.79
9	3	9	5	18	4393	9.63	90		2203	2190	50.15	49.85
7	10	9	6	18	4392	9.63	91		2216	2176	50.46	49.54
2	27	9	6	17	4389	9.62	92		2225	2164	50.69	49.31
3	20	9	6	17	4385	9.61	93		2152	2233	49.08	50.92
8	28	9	6	18	4385	9.61	94		2214	2171	50.49	49.51
7	9	9	5	18	4384	9.61	95		2091	2293	47.7	52.3
6	18	9	5	18	4376	9.59	96		2150	2226	49.13	50.87
9	4	9	6	15	4375	9.59	97		2117	2258	48.39	51.61
10	8	9	5	17	4372	9.59	98		2216	2156	50.69	49.31
2	20	9	6	17	4370	9.58	99		2160	2210	49.43	50.57
3	27	9	6	17	4370	9.58	100		2157	2213	49.36	50.64
7	1	9	4	18	4369	9.58	101	45611	2092	2277	47.88	52.12
5	29	9	6	18	4359	9.56	102		2243	2116	51.46	48.54
10	6	9	3	17	4358	9.55	103		2159	2199	49.54	50.46
10	23	9	6	16	4349	9.53	104		2165	2184	49.78	50.22
8	6	9	5	17	4345	9.53	105		2144	2201	49.34	50.66
12	22	9	3	17	4345	9.53	106		2201	2144	50.66	49.34
8	13	9	5	17	4341	9.52	107		2233	2108	51.44	48.56
4	24	9	6	16	4340	9.52	108		2152	2188	49.59	50.41
8	6	9	5	18	4340	9.52	109		2238	2102	51.57	48.43
8	28	9	6	16	4340	9.52	110		2148	2192	49.49	50.51
8	14	9	6	15	4337	9.51	111		2163	2174	49.87	50.13
12	23	9	4	16	4336	9.51	112		2192	2144	50.55	49.45
8	24	9	2	17	4333	9.5	113		2137	2196	49.32	50.68
7	1	9	4	17	4332	9.5	114		2202	2130	50.83	49.17
7	24	9	6	18	4332	9.5	115		2183	2149	50.39	49.61
7	31	9	6	16	4332	9.5	116		2109	2223	48.68	51.32
6	12	9	6	15	4331	9.5	117		2127	2204	49.11	50.89
7	9	9	5	17	4331	9.5	118		2140	2191	49.41	50.59
10	5	9	2	17	4329	9.49	119		2135	2194	49.32	50.68
2	13	9	6	16	4327	9.49	120		2094	2233	48.39	51.61
8	21	9	6	16	4327	9.49	121	45611	2217	2110	51.24	48.76

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	10	9	6	15	4326	9.48	122		2093	2233	48.38	51.62
9	8	9	3	18	4325	9.48	123		2124	2201	49.11	50.89
7	17	9	6	18	4321	9.47	124		2185	2136	50.57	49.43
4	10	9	6	18	4319	9.47	125		2169	2150	50.22	49.78
8	31	9	2	18	4317	9.46	126		2201	2116	50.98	49.02
9	29	9	3	17	4310	9.45	127		2128	2182	49.37	50.63
9	24	9	5	17	4308	9.45	128		2108	2200	48.93	51.07
10	30	9	6	18	4306	9.44	129		2190	2116	50.86	49.14
6	30	9	3	17	4304	9.44	130		2173	2131	50.49	49.51
7	24	9	6	16	4295	9.42	131		2139	2156	49.8	50.2
9	1	9	3	18	4293	9.41	132		2093	2200	48.75	51.25
11	25	9	4	14	4290	9.41	133		2151	2139	50.14	49.86
9	30	9	4	17	4288	9.4	134		2082	2206	48.55	51.45
7	31	9	6	15	4286	9.4	135		2150	2136	50.16	49.84
8	7	9	6	14	4282	9.39	136		2033	2249	47.48	52.52
6	12	9	6	18	4281	9.39	137		2183	2098	50.99	49.01
3	27	9	6	18	4277	9.38	138		2210	2067	51.67	48.33
7	7	9	3	17	4275	9.37	139		2072	2203	48.47	51.53
12	4	9	6	17	4275	9.37	140		2056	2219	48.09	51.91
7	16	9	5	18	4274	9.37	141	45611	2096	2178	49.04	50.96
12	23	9	4	17	4271	9.36	142		2138	2133	50.06	49.94
4	10	9	6	16	4269	9.36	143		2203	2066	51.6	48.4
7	8	9	4	17	4269	9.36	144		2095	2174	49.07	50.93
10	8	9	5	18	4269	9.36	145		2108	2161	49.38	50.62
9	15	9	3	18	4264	9.35	146		2138	2126	50.14	49.86
11	6	9	6	16	4264	9.35	147		2077	2187	48.71	51.29
9	28	9	2	17	4263	9.35	148		2157	2106	50.6	49.4
9	9	9	4	17	4260	9.34	149		2079	2181	48.8	51.2
2	6	9	6	17	4259	9.34	150		2079	2180	48.81	51.19
9	10	9	5	18	4259	9.34	151		2108	2151	49.5	50.5
10	15	9	5	17	4259	9.34	152		2141	2118	50.27	49.73
9	30	9	4	18	4257	9.33	153		2169	2088	50.95	49.05
6	29	9	2	18	4249	9.32	154		2056	2193	48.39	51.61
9	28	9	2	18	4249	9.32	155		2106	2143	49.56	50.44
7	15	9	4	18	4248	9.31	156		2106	2142	49.58	50.42
1	30	9	6	17	4247	9.31	157		2128	2119	50.11	49.89
11	24	9	3	17	4247	9.31	158		2120	2127	49.92	50.08
9	10	9	5	17	4246	9.31	159		2003	2243	47.17	52.83
4	3	9	6	18	4243	9.3	160		2273	1970	53.57	46.43
6	5	9	6	15	4243	9.3	161	45611	2069	2174	48.76	51.24
10	7	9	4	17	4242	9.3	162		2139	2103	50.42	49.58
10	30	9	6	16	4242	9.3	163		2142	2100	50.5	49.5
3	13	9	6	18	4238	9.29	164		2254	1984	53.19	46.81
3	6	9	6	17	4237	9.29	165		2101	2136	49.59	50.41
5	21	9	5	18	4231	9.28	166		2133	2098	50.41	49.59
6	8	9	2	17	4231	9.28	167		2025	2206	47.86	52.14
9	8	9	3	16	4229	9.27	168		2070	2159	48.95	51.05
6	11	9	5	17	4227	9.27	169		2086	2141	49.35	50.65
8	25	9	3	18	4226	9.27	170		2137	2089	50.57	49.43
7	6	9	2	17	4224	9.26	171		2079	2145	49.22	50.78
9	22	9	3	18	4221	9.25	172		2103	2118	49.82	50.18
5	14	9	5	17	4220	9.25	173		2092	2128	49.57	50.43

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
9	2	9	4	18	4217	9.25	174		2134	2083	50.6	49.4
9	21	9	2	17	4214	9.24	175		2039	2175	48.39	51.61
5	1	9	6	16	4213	9.24	176		2109	2104	50.06	49.94
7	2	9	5	15	4212	9.23	177		2085	2127	49.5	50.5
6	18	9	5	17	4211	9.23	178		2061	2150	48.94	51.06
7	8	9	4	18	4211	9.23	179		2065	2146	49.04	50.96
9	17	9	5	18	4211	9.23	180		2084	2127	49.49	50.51
5	7	9	5	17	4210	9.23	181	45611	2029	2181	48.19	51.81
8	26	9	4	17	4208	9.23	182		2071	2137	49.22	50.78
8	27	9	5	17	4208	9.23	183		2121	2087	50.4	49.6
10	29	9	5	17	4208	9.23	184		2111	2097	50.17	49.83
10	22	9	5	17	4207	9.22	185		2082	2125	49.49	50.51
12	11	9	6	17	4207	9.22	186		2043	2164	48.56	51.44
10	15	9	5	18	4206	9.22	187		2119	2087	50.38	49.62
5	28	9	5	17	4202	9.21	188		1973	2229	46.95	53.05
2	27	9	6	18	4201	9.21	189		2191	2010	52.15	47.85
8	17	9	2	17	4201	9.21	190		2120	2081	50.46	49.54
8	26	9	4	18	4201	9.21	191		2059	2142	49.01	50.99
9	15	9	3	17	4201	9.21	192		2042	2159	48.61	51.39
6	24	9	4	18	4200	9.21	193		2063	2137	49.12	50.88
4	17	9	6	16	4192	9.19	194		2120	2072	50.57	49.43
11	20	9	6	17	4192	9.19	195		2090	2102	49.86	50.14
8	21	9	6	18	4189	9.18	196		2248	1941	53.66	46.34
6	25	9	5	16	4188	9.18	197		1960	2228	46.8	53.2
8	31	9	2	17	4188	9.18	198		2065	2123	49.31	50.69
5	14	9	5	18	4186	9.18	199		2053	2133	49.04	50.96
6	22	9	2	18	4186	9.18	200		2065	2121	49.33	50.67

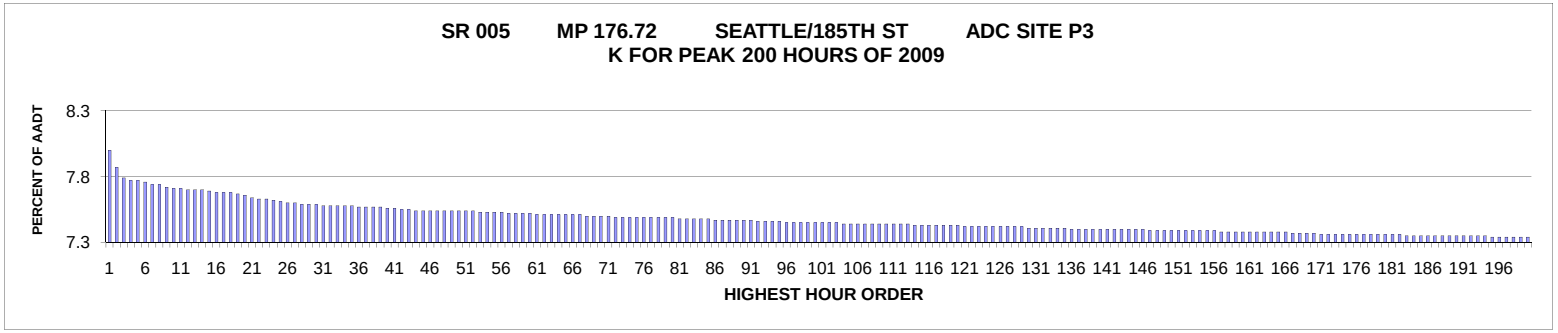

AADT= 185290 **K 30 FACTOR=** 7.59 **K 100 FACTOR=** 7.45 **K 200 FACTOR=** 7.35 **D FACTOR=** 56.27

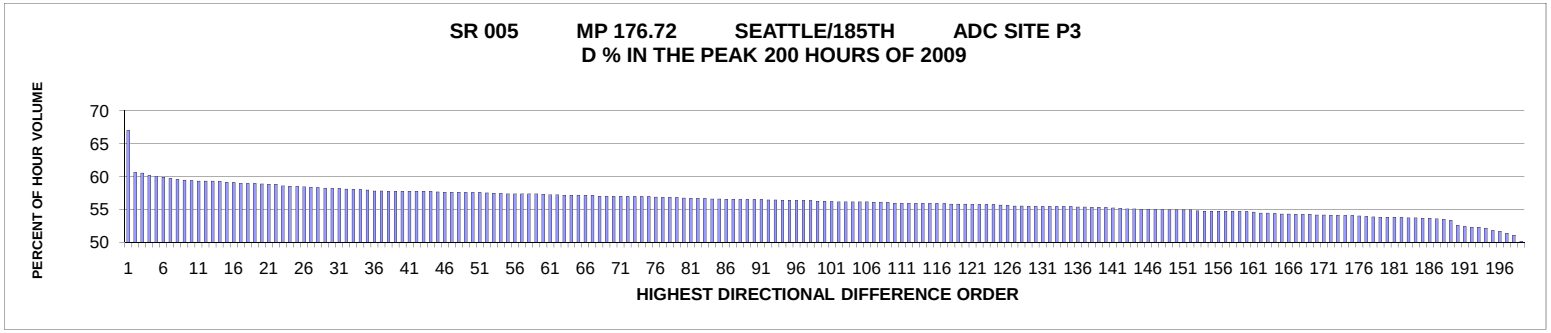

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
9	3	9	5	17	14815	8	1	185290	7992	6823	53.95	46.05
12	6	9	1	18	14589	7.87	2		7315	7274	50.14	49.86
8	5	9	4	18	14442	7.79	3		7600	6842	52.62	47.38
3	26	9	5	18	14399	7.77	4		8412	5987	58.42	41.58
4	16	9	5	18	14392	7.77	5		7912	6480	54.97	45.03
4	10	9	6	18	14382	7.76	6		8151	6231	56.68	43.32
8	11	9	3	18	14347	7.74	7		8052	6295	56.12	43.88
7	13	9	2	18	14338	7.74	8		8093	6245	56.44	43.56
8	12	9	4	18	14297	7.72	9		7730	6567	54.07	45.93
3	6	9	6	18	14289	7.71	10		8163	6126	57.13	42.87
3	19	9	5	18	14288	7.71	11		8036	6252	56.24	43.76
6	5	9	6	18	14275	7.7	12		7645	6630	53.56	46.44
12	3	9	5	17	14272	7.7	13		7465	6807	52.31	47.69
8	20	9	5	18	14259	7.7	14		7478	6781	52.44	47.56
5	22	9	6	16	14247	7.69	15		7959	6288	55.86	44.14
3	19	9	5	17	14235	7.68	16		8041	6194	56.49	43.51
4	21	9	3	18	14223	7.68	17		7875	6348	55.37	44.63

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
5	15	9	6	17	14222	7.68	18		7639	6583	53.71	46.29
12	3	9	5	18	14221	7.67	19		6956	7265	48.91	51.09
11	25	9	4	15	14185	7.66	20		8066	6119	56.86	43.14
8	25	9	3	17	14150	7.64	21	185290	8133	6017	57.48	42.52
8	31	9	2	18	14145	7.63	22		7847	6298	55.48	44.52
8	5	9	4	17	14138	7.63	23		7397	6741	52.32	47.68
3	17	9	3	18	14120	7.62	24		8310	5810	58.85	41.15
5	20	9	4	18	14099	7.61	25		7722	6377	54.77	45.23
8	11	9	3	17	14088	7.6	26		8168	5920	57.98	42.02
10	13	9	3	18	14088	7.6	27		7884	6204	55.96	44.04
5	21	9	5	18	14071	7.59	28		7666	6405	54.48	45.52
7	28	9	3	18	14059	7.59	29		7657	6402	54.46	45.54
12	4	9	6	8	14057	7.59	30		4578	9479	32.57	67.43
6	3	9	4	18	14053	7.58	31		7848	6205	55.85	44.15
10	2	9	6	18	14049	7.58	32		7602	6447	54.11	45.89
4	21	9	3	17	14046	7.58	33		8092	5954	57.61	42.39
4	22	9	4	17	14040	7.58	34		8024	6016	57.15	42.85
7	14	9	3	18	14036	7.58	35		7825	6211	55.75	44.25
10	12	9	2	18	14029	7.57	36		7954	6075	56.7	43.3
3	5	9	5	18	14026	7.57	37		8044	5982	57.35	42.65
8	12	9	4	17	14024	7.57	38		7777	6247	55.45	44.55
4	15	9	4	18	14018	7.57	39		7741	6277	55.22	44.78
3	27	9	6	16	14007	7.56	40		8285	5722	59.15	40.85
3	19	9	5	16	14000	7.56	41	185290	8037	5963	57.41	42.59
8	25	9	3	16	13984	7.55	42		8228	5756	58.84	41.16
8	31	9	2	17	13981	7.55	43		8025	5956	57.4	42.6
10	9	9	6	18	13979	7.54	44		8021	5958	57.38	42.62
6	17	9	4	18	13978	7.54	45		7523	6455	53.82	46.18
10	20	9	3	18	13976	7.54	46		7874	6102	56.34	43.66
4	9	9	5	16	13975	7.54	47		8055	5920	57.64	42.36
4	24	9	6	18	13970	7.54	48		7696	6274	55.09	44.91
2	25	9	4	17	13969	7.54	49		8342	5627	59.72	40.28
8	24	9	2	18	13968	7.54	50		7929	6039	56.77	43.23
5	27	9	4	18	13966	7.54	51		7783	6183	55.73	44.27
4	15	9	4	17	13963	7.54	52		8067	5896	57.77	42.23
5	15	9	6	16	13956	7.53	53		7778	6178	55.73	44.27
8	14	9	6	18	13956	7.53	54		7578	6378	54.3	45.7
12	3	9	5	16	13956	7.53	55		7884	6072	56.49	43.51
6	16	9	3	18	13944	7.53	56		7792	6152	55.88	44.12
2	27	9	6	18	13934	7.52	57		7840	6094	56.27	43.73
3	18	9	4	18	13933	7.52	58		7965	5968	57.17	42.83
9	18	9	6	18	13930	7.52	59		7793	6137	55.94	44.06
12	22	9	3	17	13927	7.52	60		7612	6315	54.66	45.34
5	15	9	6	18	13924	7.51	61	185290	7725	6199	55.48	44.52
10	28	9	4	18	13916	7.51	62		7602	6314	54.63	45.37
12	1	9	3	18	13916	7.51	63		7208	6708	51.8	48.2
5	15	9	6	15	13915	7.51	64		7695	6220	55.3	44.7
6	5	9	6	17	13914	7.51	65		7717	6197	55.46	44.54
12	18	9	6	16	13911	7.51	66		7900	6011	56.79	43.21
2	6	9	6	18	13909	7.51	67		7921	5988	56.95	43.05
4	29	9	4	18	13899	7.5	68		7809	6090	56.18	43.82
6	19	9	6	15	13898	7.5	69		7804	6094	56.15	43.85

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
9	16	9	4	17	13894	7.5	70		7749	6145	55.77	44.23
3	26	9	5	17	13890	7.5	71		8233	5657	59.27	40.73
9	15	9	3	18	13886	7.49	72		7466	6420	53.77	46.23
11	12	9	5	17	13886	7.49	73		7667	6219	55.21	44.79
8	3	9	2	18	13885	7.49	74		8028	5857	57.82	42.18
12	18	9	6	18	13883	7.49	75		7500	6383	54.02	45.98
5	28	9	5	18	13882	7.49	76		7726	6156	55.65	44.35
12	22	9	3	18	13881	7.49	77		7406	6475	53.35	46.65
3	26	9	5	16	13878	7.49	78		8326	5552	59.99	40.01
7	27	9	2	18	13874	7.49	79		7628	6246	54.98	45.02
12	4	9	6	9	13873	7.49	80		4578	9295	33	67
6	24	9	4	18	13862	7.48	81	185290	7534	6328	54.35	45.65
8	12	9	4	16	13862	7.48	82		7847	6015	56.61	43.39
6	19	9	6	18	13859	7.48	83		7618	6241	54.97	45.03
3	20	9	6	18	13854	7.48	84		7782	6072	56.17	43.83
2	18	9	4	18	13853	7.48	85		8094	5759	58.43	41.57
9	28	9	2	18	13850	7.47	86		8048	5802	58.11	41.89
8	20	9	5	17	13840	7.47	87		7606	6234	54.96	45.04
9	28	9	2	17	13840	7.47	88		8179	5661	59.1	40.9
2	3	9	3	18	13839	7.47	89		7923	5916	57.25	42.75
5	20	9	4	17	13839	7.47	90		7622	6217	55.08	44.92
5	22	9	6	17	13835	7.47	91		7835	6000	56.63	43.37
8	5	9	4	16	13827	7.46	92		7755	6072	56.09	43.91
2	17	9	3	17	13825	7.46	93		8280	5545	59.89	40.11
2	12	9	5	18	13824	7.46	94		7872	5952	56.94	43.06
1	30	9	6	16	13816	7.46	95		8138	5678	58.9	41.1
4	3	9	6	18	13812	7.45	96		7981	5831	57.78	42.22
6	23	9	3	18	13809	7.45	97		7468	6341	54.08	45.92
12	18	9	6	15	13809	7.45	98		7813	5996	56.58	43.42
4	9	9	5	18	13808	7.45	99		7602	6206	55.06	44.94
1	19	9	2	17	13804	7.45	100		8052	5752	58.33	41.67
5	1	9	6	18	13801	7.45	101	185290	7435	6366	53.87	46.13
7	16	9	5	18	13800	7.45	102		7596	6204	55.04	44.96
5	14	9	5	18	13797	7.45	103		7717	6080	55.93	44.07
4	17	9	6	18	13792	7.44	104		7482	6310	54.25	45.75
4	10	9	6	17	13791	7.44	105		7631	6160	55.33	44.67
6	3	9	4	17	13788	7.44	106		8027	5761	58.22	41.78
8	4	9	3	18	13788	7.44	107		7657	6131	55.53	44.47
8	6	9	5	16	13785	7.44	108		8026	5759	58.22	41.78
10	9	9	6	15	13785	7.44	109		7843	5942	56.9	43.1
10	12	9	2	17	13783	7.44	110		8032	5751	58.27	41.73
4	15	9	4	16	13782	7.44	111		8125	5657	58.95	41.05
9	1	9	3	18	13781	7.44	112		7465	6316	54.17	45.83
12	22	9	3	16	13781	7.44	113		7692	6089	55.82	44.18
6	19	9	6	17	13772	7.43	114		7457	6315	54.15	45.85
4	7	9	3	18	13771	7.43	115		7935	5836	57.62	42.38
6	5	9	6	16	13769	7.43	116		7845	5924	56.98	43.02
2	19	9	5	16	13765	7.43	117		8170	5595	59.35	40.65
4	16	9	5	17	13762	7.43	118		7781	5981	56.54	43.46
9	14	9	2	17	13759	7.43	119		8117	5642	58.99	41.01
9	17	9	5	18	13759	7.43	120		7789	5970	56.61	43.39
10	27	9	3	18	13753	7.42	121	185290	7729	6024	56.2	43.8

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
6	17	9	4	16	13750	7.42	122		7986	5764	58.08	41.92
9	16	9	4	16	13750	7.42	123		8159	5591	59.34	40.66
8	21	9	6	18	13749	7.42	124		7886	5863	57.36	42.64
7	10	9	6	16	13748	7.42	125		7768	5980	56.5	43.5
5	18	9	2	17	13744	7.42	126		8056	5688	58.61	41.39
8	10	9	2	17	13744	7.42	127		7751	5993	56.4	43.6
8	31	9	2	16	13744	7.42	128		8104	5640	58.96	41.04
2	3	9	3	17	13742	7.42	129		8153	5589	59.33	40.67
3	4	9	4	18	13738	7.41	130		7972	5766	58.03	41.97
6	4	9	5	18	13737	7.41	131		7614	6123	55.43	44.57
2	25	9	4	18	13729	7.41	132		7902	5827	57.56	42.44
6	2	9	3	18	13729	7.41	133		7707	6022	56.14	43.86
6	19	9	6	16	13725	7.41	134		7733	5992	56.34	43.66
6	8	9	2	18	13724	7.41	135		7846	5878	57.17	42.83
9	2	9	4	18	13719	7.4	136		7545	6174	55	45
10	29	9	5	17	13719	7.4	137		7368	6351	53.71	46.29
11	12	9	5	18	13719	7.4	138		7428	6291	54.14	45.86
3	18	9	4	16	13717	7.4	139		8174	5543	59.59	40.41
12	4	9	6	18	13716	7.4	140		7050	6666	51.4	48.6
5	12	9	3	18	13715	7.4	141	185290	7731	5984	56.37	43.63
7	27	9	2	17	13713	7.4	142		7816	5897	57	43
11	6	9	6	16	13710	7.4	143		8140	5570	59.37	40.63
8	27	9	5	16	13709	7.4	144		7904	5805	57.66	42.34
3	27	9	6	15	13707	7.4	145		7653	6054	55.83	44.17
10	22	9	5	18	13705	7.4	146		7589	6116	55.37	44.63
2	13	9	6	15	13699	7.39	147		7596	6103	55.45	44.55
6	12	9	6	15	13699	7.39	148		7498	6201	54.73	45.27
5	28	9	5	16	13694	7.39	149		7807	5887	57.01	42.99
10	30	9	6	16	13694	7.39	150		8010	5684	58.49	41.51
5	21	9	5	17	13693	7.39	151		7603	6090	55.52	44.48
5	27	9	4	17	13693	7.39	152		7909	5784	57.76	42.24
6	5	9	6	15	13692	7.39	153		7729	5963	56.45	43.55
2	17	9	3	18	13688	7.39	154		7851	5837	57.36	42.64
2	12	9	5	17	13686	7.39	155		7916	5770	57.84	42.16
5	14	9	5	16	13684	7.39	156		8013	5671	58.56	41.44
6	17	9	4	17	13682	7.38	157		7501	6181	54.82	45.18
8	21	9	6	15	13679	7.38	158		7828	5851	57.23	42.77
9	25	9	6	18	13678	7.38	159		7795	5883	56.99	43.01
12	4	9	6	17	13677	7.38	160		7069	6608	51.69	48.31
7	28	9	3	17	13676	7.38	161	185290	7717	5959	56.43	43.57
2	26	9	5	17	13672	7.38	162		8129	5543	59.46	40.54
12	4	9	6	16	13671	7.38	163		7422	6249	54.29	45.71
4	22	9	4	18	13667	7.38	164		7510	6157	54.95	45.05
3	31	9	3	17	13666	7.38	165		8275	5391	60.55	39.45
10	8	9	5	18	13666	7.38	166		7577	6089	55.44	44.56
10	29	9	5	18	13663	7.37	167		7128	6535	52.17	47.83
1	19	9	2	16	13656	7.37	168		7854	5802	57.51	42.49
8	19	9	4	17	13650	7.37	169		7667	5983	56.17	43.83
12	22	9	3	15	13648	7.37	170		7669	5979	56.19	43.81
1	29	9	5	18	13646	7.36	171		7758	5888	56.85	43.15
8	21	9	6	17	13646	7.36	172		7797	5849	57.14	42.86
11	11	9	4	17	13645	7.36	173		7632	6013	55.93	44.07

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
9	16	9	4	18	13640	7.36	174		7308	6332	53.58	46.42
8	24	9	2	17	13639	7.36	175		7828	5811	57.39	42.61
2	18	9	4	17	13638	7.36	176		8206	5432	60.17	39.83
5	20	9	4	16	13638	7.36	177		7878	5760	57.77	42.23
5	21	9	5	16	13637	7.36	178		7628	6009	55.94	44.06
7	10	9	6	17	13637	7.36	179		7340	6297	53.82	46.18
4	30	9	5	18	13635	7.36	180		7468	6167	54.77	45.23
5	29	9	6	15	13635	7.36	181	185290	7877	5758	57.77	42.23
9	14	9	2	18	13632	7.36	182		7847	5785	57.56	42.44
5	14	9	5	17	13627	7.35	183		7762	5865	56.96	43.04
12	10	9	5	18	13627	7.35	184		7323	6304	53.74	46.26
12	11	9	6	18	13623	7.35	185		7461	6162	54.77	45.23
8	14	9	6	17	13622	7.35	186		7390	6232	54.25	45.75
5	29	9	6	18	13620	7.35	187		7699	5921	56.53	43.47
2	17	9	3	16	13619	7.35	188		8261	5358	60.66	39.34
7	15	9	4	18	13619	7.35	189		7401	6218	54.34	45.66
8	6	9	5	17	13617	7.35	190		7534	6083	55.33	44.67
7	10	9	6	15	13616	7.35	191		7584	6032	55.7	44.3
2	13	9	6	17	13611	7.35	192		7815	5796	57.42	42.58
5	7	9	5	18	13611	7.35	193		7671	5940	56.36	43.64
6	22	9	2	18	13610	7.35	194		7873	5737	57.85	42.15
2	19	9	5	17	13603	7.34	195		7892	5711	58.02	41.98
8	10	9	2	16	13601	7.34	196		7944	5657	58.41	41.59
9	18	9	6	15	13598	7.34	197		7622	5976	56.05	43.95
3	5	9	5	17	13594	7.34	198		7890	5704	58.04	41.96
6	18	9	5	18	13594	7.34	199		7382	6212	54.30	45.70
7	10	9	6	18	13594	7.34	200		7094	6500	52.18	47.82

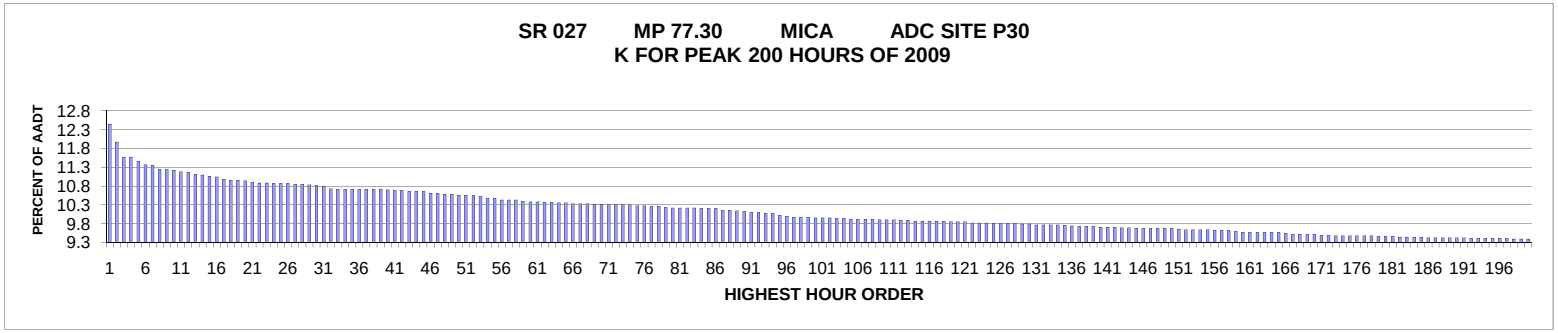

AADT= 6058 **K 30 FACTOR=** 10.81 **K 100 FACTOR=** 9.95 **K 200 FACTOR=** 9.39 **D FACTOR=** 56.39

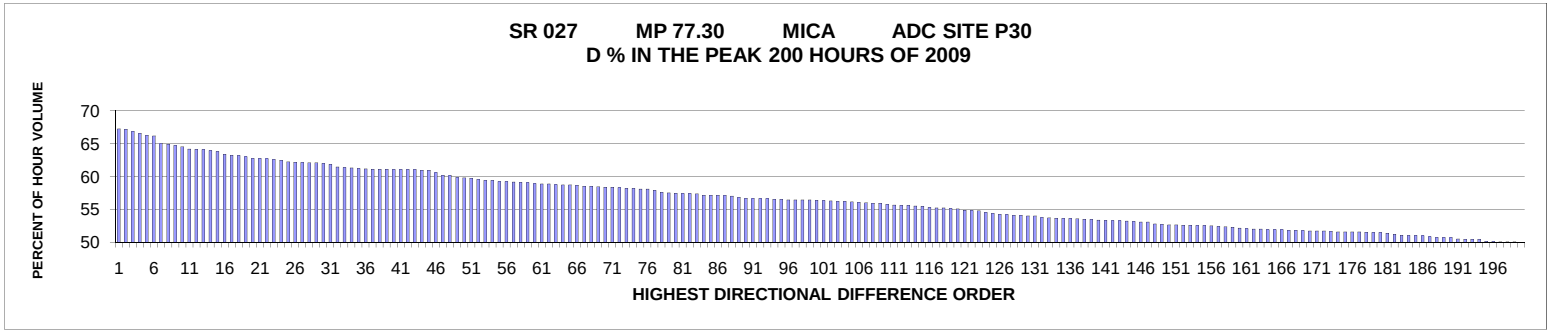

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
10	9	9	6	17	754	12.45	1	6058	352	402	46.68	53.32
9	25	9	6	16	725	11.97	2		363	362	50.07	49.93
7	3	9	6	15	701	11.57	3		311	390	44.37	55.63
9	25	9	6	17	701	11.57	4		311	390	44.37	55.63
8	7	9	6	17	694	11.46	5		279	415	40.2	59.8
5	1	9	6	17	689	11.37	6		300	389	43.54	56.46
7	2	9	5	18	688	11.36	7		244	444	35.47	64.53
9	18	9	6	18	681	11.24	8		263	418	38.62	61.38
9	25	9	6	18	681	11.24	9		258	423	37.89	62.11
5	8	9	6	17	680	11.22	10		341	339	50.15	49.85
9	18	9	6	17	677	11.18	11		314	363	46.38	53.62
9	4	9	6	17	676	11.16	12		279	397	41.27	58.73
7	31	9	6	18	673	11.11	13		262	411	38.93	61.07
10	2	9	6	18	672	11.09	14		274	398	40.77	59.23
5	22	9	6	17	670	11.06	15		298	372	44.48	55.52
9	4	9	6	18	669	11.04	16		250	419	37.37	62.63
11	6	9	6	16	665	10.98	17		343	322	51.58	48.42

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
3	20	9	6	18	664	10.96	18		251	413	37.8	62.2
5	22	9	6	18	664	10.96	19		224	440	33.73	66.27
6	5	9	6	16	663	10.94	20		346	317	52.19	47.81
10	2	9	6	16	660	10.89	21	6058	347	313	52.58	47.42
3	13	9	6	18	659	10.88	22		283	376	42.94	57.06
5	29	9	6	18	659	10.88	23		249	410	37.78	62.22
6	19	9	6	17	658	10.86	24		264	394	40.12	59.88
6	26	9	6	18	658	10.86	25		275	383	41.79	58.21
10	22	9	5	18	658	10.86	26		236	422	35.87	64.13
6	5	9	6	17	657	10.85	27		271	386	41.25	58.75
10	9	9	6	16	657	10.85	28		315	342	47.95	52.05
5	15	9	6	16	656	10.83	29		333	323	50.76	49.24
6	26	9	6	17	655	10.81	30		267	388	40.76	59.24
12	4	9	6	16	654	10.8	31		370	284	56.57	43.43
4	17	9	6	18	650	10.73	32		267	383	41.08	58.92
5	1	9	6	18	649	10.71	33		250	399	38.52	61.48
5	8	9	6	16	649	10.71	34		328	321	50.54	49.46
7	3	9	6	17	649	10.71	35		270	379	41.6	58.4
7	17	9	6	17	649	10.71	36		275	374	42.37	57.63
8	7	9	6	18	649	10.71	37		251	398	38.67	61.33
9	24	9	5	16	649	10.71	38		324	325	49.92	50.08
10	16	9	6	17	649	10.71	39		293	356	45.15	54.85
7	3	9	6	16	648	10.7	40		252	396	38.89	61.11
7	3	9	6	14	647	10.68	41	6058	255	392	39.41	60.59
12	18	9	6	16	647	10.68	42		362	285	55.95	44.05
9	4	9	6	16	645	10.65	43		318	327	49.3	50.7
9	11	9	6	16	645	10.65	44		347	298	53.8	46.2
10	16	9	6	18	645	10.65	45		250	395	38.76	61.24
5	22	9	6	16	642	10.6	46		321	321	50	50
11	20	9	6	16	642	10.6	47		367	275	57.17	42.83
6	3	9	4	18	641	10.58	48		260	381	40.56	59.44
10	16	9	6	16	641	10.58	49		326	315	50.86	49.14
9	11	9	6	18	640	10.56	50		263	377	41.09	58.91
4	24	9	6	17	639	10.55	51		277	362	43.35	56.65
7	1	9	4	18	639	10.55	52		281	358	43.97	56.03
7	3	9	6	13	637	10.52	53		264	373	41.44	58.56
7	3	9	6	12	635	10.48	54		264	371	41.57	58.43
9	25	9	6	19	634	10.47	55		210	424	33.12	66.88
4	30	9	5	18	632	10.43	56		221	411	34.97	65.03
5	29	9	6	17	632	10.43	57		299	333	47.31	52.69
10	9	9	6	18	632	10.43	58		261	371	41.3	58.7
7	2	9	5	17	630	10.4	59		245	385	38.89	61.11
5	1	9	6	16	629	10.38	60		304	325	48.33	51.67
8	28	9	6	17	629	10.38	61	6058	231	398	36.72	63.28
4	24	9	6	18	628	10.37	62		234	394	37.26	62.74
6	5	9	6	18	628	10.37	63		238	390	37.9	62.1
4	24	9	6	16	627	10.35	64		304	323	48.48	51.52
9	5	9	7	13	627	10.35	65		244	383	38.92	61.08
2	13	9	6	17	626	10.33	66		261	365	41.69	58.31
6	26	9	6	16	626	10.33	67		302	324	48.24	51.76
12	11	9	6	16	626	10.33	68		321	305	51.28	48.72
6	12	9	6	18	625	10.32	69		243	382	38.88	61.12

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
10	2	9	6	17	625	10.32	70		286	339	45.76	54.24
5	8	9	6	18	624	10.3	71		279	345	44.71	55.29
7	2	9	5	16	624	10.3	72		290	334	46.47	53.53
8	14	9	6	18	624	10.3	73		234	390	37.5	62.5
12	1	9	3	16	624	10.3	74		325	299	52.08	47.92
6	12	9	6	17	623	10.28	75		270	353	43.34	56.66
8	7	9	6	19	623	10.28	76		232	391	37.24	62.76
7	24	9	6	17	621	10.25	77		224	397	36.07	63.93
9	23	9	4	16	621	10.25	78		325	296	52.33	47.67
9	26	9	7	14	620	10.23	79		325	295	52.42	47.58
4	10	9	6	17	619	10.22	80		277	342	44.75	55.25
5	15	9	6	18	619	10.22	81	6058	241	378	38.93	61.07
5	29	9	6	16	619	10.22	82		327	292	52.83	47.17
12	11	9	6	17	619	10.22	83		321	298	51.86	48.14
9	24	9	5	18	618	10.2	84		259	359	41.91	58.09
10	30	9	6	17	618	10.2	85		263	355	42.56	57.44
11	17	9	3	16	618	10.2	86		334	284	54.05	45.95
6	18	9	5	18	615	10.15	87		229	386	37.24	62.76
9	18	9	6	16	615	10.15	88		314	301	51.06	48.94
11	20	9	6	17	614	10.14	89		310	304	50.49	49.51
8	21	9	6	17	613	10.12	90		258	355	42.09	57.91
9	22	9	3	18	612	10.1	91		290	322	47.39	52.61
11	13	9	6	16	612	10.1	92		350	262	57.19	42.81
6	4	9	5	17	610	10.07	93		278	332	45.57	54.43
6	12	9	6	16	610	10.07	94		255	355	41.8	58.2
10	8	9	5	17	607	10.02	95		293	314	48.27	51.73
12	3	9	5	16	606	10	96		332	274	54.79	45.21
4	10	9	6	18	604	9.97	97		263	341	43.54	56.46
8	28	9	6	18	604	9.97	98		253	351	41.89	58.11
9	26	9	7	16	604	9.97	99		293	311	48.51	51.49
2	27	9	6	16	603	9.95	100		292	311	48.42	51.58
3	20	9	6	16	603	9.95	101	6058	311	292	51.58	48.42
8	21	9	6	18	603	9.95	102		230	373	38.14	61.86
4	10	9	6	16	602	9.94	103		298	304	49.5	50.5
10	22	9	5	17	602	9.94	104		279	323	46.35	53.65
2	13	9	6	16	601	9.92	105		307	294	51.08	48.92
8	7	9	6	16	601	9.92	106		310	291	51.58	48.42
10	7	9	4	18	601	9.92	107		282	319	46.92	53.08
11	6	9	6	17	601	9.92	108		282	319	46.92	53.08
4	17	9	6	16	600	9.9	109		316	284	52.67	47.33
6	26	9	6	19	600	9.9	110		228	372	38	62
7	31	9	6	16	600	9.9	111		262	338	43.67	56.33
3	20	9	6	17	599	9.89	112		255	344	42.57	57.43
5	14	9	5	17	599	9.89	113		284	315	47.41	52.59
5	1	9	6	19	598	9.87	114		258	340	43.14	56.86
5	14	9	5	18	598	9.87	115		214	384	35.79	64.21
7	24	9	6	18	598	9.87	116		200	398	33.44	66.56
9	22	9	3	16	598	9.87	117		293	305	49	51
12	4	9	6	17	598	9.87	118		302	296	50.5	49.5
10	7	9	4	16	597	9.85	119		309	288	51.76	48.24
10	8	9	5	16	597	9.85	120		320	277	53.6	46.4
11	5	9	5	16	597	9.85	121	6058	329	268	55.11	44.89

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	25	9	3	18	595	9.82	122		255	340	42.86	57.14
9	26	9	7	17	595	9.82	123		322	273	54.12	45.88
10	22	9	5	16	595	9.82	124		314	281	52.77	47.23
3	13	9	6	17	594	9.81	125		258	336	43.43	56.57
4	17	9	6	17	594	9.81	126		243	351	40.91	59.09
6	19	9	6	18	594	9.81	127		239	355	40.24	59.76
9	26	9	7	15	594	9.81	128		309	285	52.02	47.98
7	10	9	6	18	593	9.79	129		208	385	35.08	64.92
7	30	9	5	18	593	9.79	130		218	375	36.76	63.24
9	10	9	5	16	592	9.77	131		327	265	55.24	44.76
9	16	9	4	18	592	9.77	132		277	315	46.79	53.21
9	18	9	6	19	592	9.77	133		209	383	35.3	64.7
9	26	9	7	13	592	9.77	134		282	310	47.64	52.36
5	15	9	6	17	591	9.76	135		262	329	44.33	55.67
12	9	9	4	16	590	9.74	136		317	273	53.73	46.27
3	6	9	6	17	589	9.72	137		255	334	43.29	56.71
5	1	9	6	15	589	9.72	138		283	306	48.05	51.95
9	3	9	5	16	589	9.72	139		305	284	51.78	48.22
2	6	9	6	18	588	9.71	140		199	389	33.84	66.16
2	26	9	5	18	588	9.71	141	6058	213	375	36.22	63.78
4	23	9	5	17	588	9.71	142		240	348	40.82	59.18
3	16	9	2	16	587	9.69	143		305	282	51.96	48.04
5	29	9	6	19	587	9.69	144		217	370	36.97	63.03
2	27	9	6	18	586	9.67	145		243	343	41.47	58.53
7	3	9	6	11	586	9.67	146		251	335	42.83	57.17
7	10	9	6	17	586	9.67	147		228	358	38.91	61.09
9	10	9	5	18	586	9.67	148		255	331	43.52	56.48
11	18	9	4	16	586	9.67	149		332	254	56.66	43.34
11	19	9	5	16	586	9.67	150		312	274	53.24	46.76
10	6	9	3	18	585	9.66	151		269	316	45.98	54.02
4	8	9	4	18	584	9.64	152		243	341	41.61	58.39
6	1	9	2	18	584	9.64	153		228	356	39.04	60.96
8	21	9	6	16	584	9.64	154		267	317	45.72	54.28
9	17	9	5	16	584	9.64	155		328	256	56.16	43.84
5	28	9	5	18	583	9.62	156		232	351	39.79	60.21
10	21	9	4	18	583	9.62	157		265	318	45.45	54.55
9	26	9	7	12	582	9.61	158		248	334	42.61	57.39
5	7	9	5	16	581	9.59	159		291	290	50.09	49.91
7	31	9	6	17	580	9.57	160		231	349	39.83	60.17
1	30	9	6	17	579	9.56	161	6058	226	353	39.03	60.97
2	27	9	6	17	579	9.56	162		246	333	42.49	57.51
7	17	9	6	18	579	9.56	163		212	367	36.61	63.39
11	3	9	3	16	579	9.56	164		324	255	55.96	44.04
11	16	9	2	16	579	9.56	165		327	252	56.48	43.52
6	10	9	4	17	578	9.54	166		288	290	49.83	50.17
10	9	9	6	15	577	9.52	167		269	308	46.62	53.38
11	10	9	3	16	577	9.52	168		303	274	52.51	47.49
6	18	9	5	17	576	9.51	169		268	308	46.53	53.47
12	18	9	6	17	576	9.51	170		269	307	46.7	53.3
6	8	9	2	16	575	9.49	171		294	281	51.13	48.87
9	14	9	2	18	575	9.49	172		251	324	43.65	56.35
2	20	9	6	16	574	9.48	173		278	296	48.43	51.57

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
5	27	9	4	18	574	9.48	174		232	342	40.42	59.58
6	25	9	5	18	574	9.48	175		236	338	41.11	58.89
9	5	9	7	12	574	9.48	176		244	330	42.51	57.49
10	5	9	2	17	574	9.48	177		276	298	48.08	51.92
10	28	9	4	17	574	9.48	178		279	295	48.61	51.39
1	9	9	6	18	573	9.46	179		188	385	32.81	67.19
2	5	9	5	16	573	9.46	180		282	291	49.21	50.79
5	21	9	5	16	573	9.46	181	6058	318	255	55.5	44.5
2	6	9	6	17	572	9.44	182		222	350	38.81	61.19
5	2	9	7	16	572	9.44	183		251	321	43.88	56.12
8	14	9	6	17	572	9.44	184		232	340	40.56	59.44
10	15	9	5	18	572	9.44	185		265	307	46.33	53.67
1	16	9	6	18	571	9.43	186		205	366	35.9	64.1
6	10	9	4	18	571	9.43	187		216	355	37.83	62.17
6	19	9	6	19	571	9.43	188		187	384	32.75	67.25
7	10	9	6	16	571	9.43	189		249	322	43.61	56.39
9	11	9	6	17	571	9.43	190		256	315	44.83	55.17
10	1	9	5	16	571	9.43	191		309	262	54.12	45.88
3	27	9	6	17	570	9.41	192		235	335	41.23	58.77
4	18	9	7	16	570	9.41	193		270	300	47.37	52.63

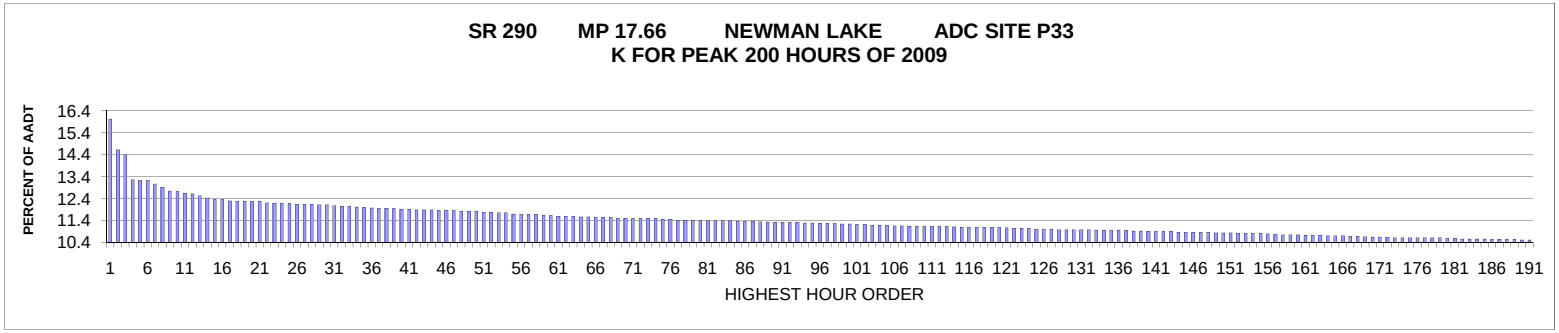

AADT= 7156 **K 30 FACTOR=** 12.12 **K 100 FACTOR=** 11.32 **K 200 FACTOR=** 10.51 **D FACTOR=** 65.38

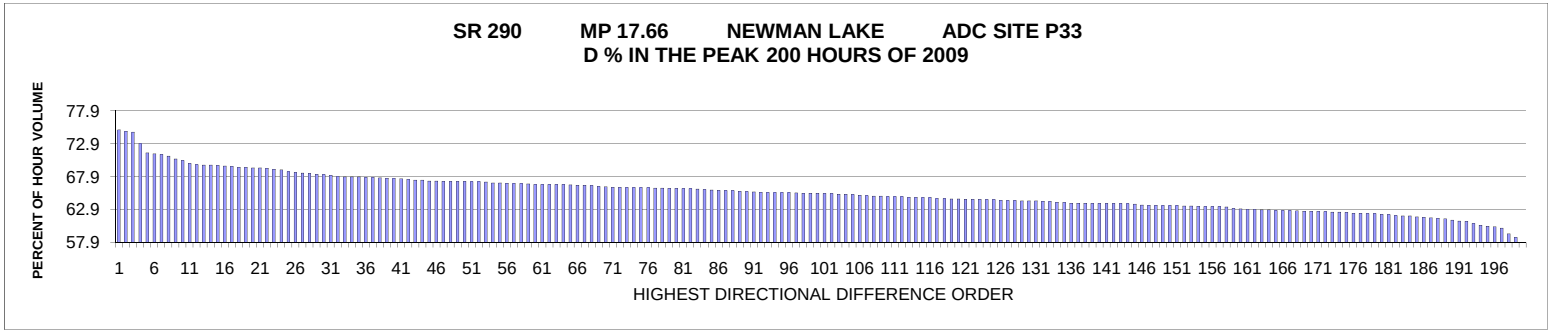

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
6	19	9	6	18	1147	16.03	1	7156	820	327	71.49	28.51
8	14	9	6	17	1047	14.63	2		783	264	74.79	25.21
8	27	9	5	17	1030	14.39	3		734	296	71.26	28.74
7	31	9	6	18	948	13.25	4		624	324	65.82	34.18
6	19	9	6	19	947	13.23	5		707	240	74.66	25.34
7	2	9	5	17	947	13.23	6		658	289	69.48	30.52
8	21	9	6	18	935	13.07	7		660	275	70.59	29.41
7	16	9	5	18	924	12.91	8		656	268	71	29
3	27	9	6	17	912	12.74	9		684	228	75	25
7	31	9	6	17	910	12.72	10		630	280	69.23	30.77
7	15	9	4	17	904	12.63	11		585	319	64.71	35.29
7	1	9	4	17	903	12.62	12		629	274	69.66	30.34
9	11	9	6	18	897	12.53	13		654	243	72.91	27.09
8	27	9	5	16	889	12.42	14		602	287	67.72	32.28
7	2	9	5	18	884	12.35	15		631	253	71.38	28.62
8	14	9	6	18	884	12.35	16		618	266	69.91	30.09
8	13	9	5	17	880	12.3	17		568	312	64.55	35.45

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	20	9	5	17	879	12.28	18		573	306	65.19	34.81
8	27	9	5	18	879	12.28	19		612	267	69.62	30.38
8	5	9	4	18	878	12.27	20		582	296	66.29	33.71
8	20	9	5	18	877	12.26	21	7156	584	293	66.59	33.41
7	22	9	4	17	873	12.2	22		554	319	63.46	36.54
7	1	9	4	18	872	12.19	23		601	271	68.92	31.08
7	17	9	6	17	871	12.17	24		590	281	67.74	32.26
8	28	9	6	18	871	12.17	25		597	274	68.54	31.46
6	12	9	6	17	869	12.14	26		579	290	66.63	33.37
8	18	9	3	18	869	12.14	27		601	268	69.16	30.84
7	15	9	4	18	868	12.13	28		601	267	69.24	30.76
7	16	9	5	17	867	12.12	29		568	299	65.51	34.49
7	29	9	4	18	867	12.12	30		584	283	67.36	32.64
6	12	9	6	18	864	12.07	31		599	265	69.33	30.67
6	10	9	4	17	862	12.05	32		585	277	67.87	32.13
8	19	9	4	17	862	12.05	33		583	279	67.63	32.37
8	5	9	4	17	860	12.02	34		549	311	63.84	36.16
7	21	9	3	17	858	11.99	35		547	311	63.75	36.25
7	28	9	3	17	857	11.98	36		545	312	63.59	36.41
7	9	9	5	18	856	11.96	37		595	261	69.51	30.49
7	17	9	6	18	856	11.96	38		573	283	66.94	33.06
6	11	9	5	17	855	11.95	39		559	296	65.38	34.62
8	26	9	4	18	853	11.92	40		568	285	66.59	33.41
8	14	9	6	16	852	11.91	41	7156	568	284	66.67	33.33
7	10	9	6	17	851	11.89	42		547	304	64.28	35.72
8	11	9	3	17	851	11.89	43		543	308	63.81	36.19
9	24	9	5	17	851	11.89	44		549	302	64.51	35.49
7	10	9	6	18	848	11.85	45		552	296	65.09	34.91
7	24	9	6	17	848	11.85	46		576	272	67.92	32.08
8	24	9	2	17	848	11.85	47		513	335	60.5	39.5
8	21	9	6	17	846	11.82	48		554	292	65.48	34.52
9	2	9	4	18	846	11.82	49		554	292	65.48	34.52
9	11	9	6	17	846	11.82	50		540	306	63.83	36.17
8	25	9	3	17	843	11.78	51		535	308	63.46	36.54
6	29	9	2	18	842	11.77	52		551	291	65.44	34.56
8	19	9	4	18	841	11.75	53		563	278	66.94	33.06
9	10	9	5	18	841	11.75	54		565	276	67.18	32.82
6	3	9	4	17	837	11.7	55		559	278	66.79	33.21
5	22	9	6	17	836	11.68	56		542	294	64.83	35.17
7	30	9	5	18	835	11.67	57		557	278	66.71	33.29
8	11	9	3	18	835	11.67	58		529	306	63.35	36.65
8	28	9	6	17	833	11.64	59		548	285	65.79	34.21
8	10	9	2	17	832	11.63	60		518	314	62.26	37.74
7	7	9	3	17	830	11.6	61	7156	523	307	63.01	36.99
7	14	9	3	17	830	11.6	62		517	313	62.29	37.71
8	4	9	3	18	830	11.6	63		550	280	66.27	33.73
7	30	9	5	17	827	11.56	64		517	310	62.52	37.48
8	3	9	2	17	827	11.56	65		517	310	62.52	37.48
7	6	9	2	17	826	11.54	66		498	328	60.29	39.71
7	22	9	4	18	826	11.54	67		552	274	66.83	33.17
7	20	9	2	17	825	11.53	68		478	347	57.94	42.06
5	21	9	5	17	823	11.5	69		544	279	66.1	33.9

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
9	1	9	3	18	823	11.5	70		565	258	68.65	31.35
5	29	9	6	17	822	11.49	71		552	270	67.15	32.85
7	14	9	3	18	822	11.49	72		530	292	64.48	35.52
8	17	9	2	18	822	11.49	73		533	289	64.84	35.16
9	15	9	3	17	822	11.49	74		508	314	61.8	38.2
9	2	9	4	17	820	11.46	75		551	269	67.2	32.8
9	16	9	4	17	820	11.46	76		521	299	63.54	36.46
6	2	9	3	17	817	11.42	77		523	294	64.01	35.99
7	9	9	5	17	817	11.42	78		511	306	62.55	37.45
7	23	9	5	17	817	11.42	79		540	277	66.1	33.9
6	4	9	5	17	816	11.4	80		512	304	62.75	37.25
5	26	9	3	17	815	11.39	81	7156	538	277	66.01	33.99
6	29	9	2	16	815	11.39	82		526	289	64.54	35.46
8	4	9	3	17	815	11.39	83		520	295	63.8	36.2
8	26	9	4	17	815	11.39	84		523	292	64.17	35.83
8	3	9	2	18	813	11.36	85		540	273	66.42	33.58
8	12	9	4	18	813	11.36	86		534	279	65.68	34.32
8	17	9	2	17	813	11.36	87		528	285	64.94	35.06
8	21	9	6	16	812	11.35	88		523	289	64.41	35.59
7	31	9	6	16	811	11.33	89		523	288	64.49	35.51
6	5	9	6	17	810	11.32	90		499	311	61.6	38.4
7	8	9	4	18	810	11.32	91		526	284	64.94	35.06
8	25	9	3	18	810	11.32	92		520	290	64.2	35.8
9	4	9	6	17	810	11.32	93		536	274	66.17	33.83
7	29	9	4	17	808	11.29	94		528	280	65.35	34.65
11	4	9	4	17	808	11.29	95		528	280	65.35	34.65
5	18	9	2	17	807	11.28	96		511	296	63.32	36.68
8	6	9	5	18	807	11.28	97		533	274	66.05	33.95
8	6	9	5	17	806	11.26	98		511	295	63.4	36.6
6	24	9	4	17	805	11.25	99		506	299	62.86	37.14
7	8	9	4	17	804	11.24	100		500	304	62.19	37.81
4	15	9	4	17	803	11.22	101	7156	499	304	62.14	37.86
9	1	9	3	17	802	11.21	102		532	270	66.33	33.67
10	8	9	5	17	801	11.19	103		527	274	65.79	34.21
6	11	9	5	18	800	11.18	104		524	276	65.5	34.5
7	2	9	5	16	799	11.17	105		473	326	59.2	40.8
6	10	9	4	18	798	11.15	106		526	272	65.91	34.09
8	12	9	4	17	798	11.15	107		531	267	66.54	33.46
8	10	9	2	18	797	11.14	108		545	252	68.38	31.62
9	25	9	6	17	797	11.14	109		506	291	63.49	36.51
5	8	9	6	18	796	11.12	110		543	253	68.22	31.78
6	30	9	3	17	796	11.12	111		504	292	63.32	36.68
7	23	9	5	18	796	11.12	112		527	269	66.21	33.79
9	18	9	6	17	796	11.12	113		499	297	62.69	37.31
4	8	9	4	17	795	11.11	114		489	306	61.51	38.49
8	7	9	6	18	794	11.1	115		553	241	69.65	30.35
6	25	9	5	17	793	11.08	116		491	302	61.92	38.08
6	25	9	5	18	793	11.08	117		509	284	64.19	35.81
6	29	9	2	17	793	11.08	118		510	283	64.31	35.69
7	17	9	6	16	793	11.08	119		485	308	61.16	38.84
7	27	9	2	17	793	11.08	120		502	291	63.3	36.7
10	1	9	5	17	792	11.07	121	7156	536	256	67.68	32.32

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
5	21	9	5	18	791	11.05	122		494	297	62.45	37.55
9	4	9	6	18	791	11.05	123		546	245	69.03	30.97
9	28	9	2	17	790	11.04	124		495	295	62.66	37.34
9	30	9	4	17	788	11.01	125		508	280	64.47	35.53
10	1	9	5	18	787	11	126		531	256	67.47	32.53
12	3	9	5	16	787	11	127		536	251	68.11	31.89
4	7	9	3	17	786	10.98	128		492	294	62.6	37.4
6	22	9	2	17	786	10.98	129		502	284	63.87	36.13
8	13	9	5	18	786	10.98	130		511	275	65.01	34.99
9	9	9	4	18	786	10.98	131		548	238	69.72	30.28
9	10	9	5	17	786	10.98	132		509	277	64.76	35.24
5	20	9	4	17	785	10.97	133		520	265	66.24	33.76
6	26	9	6	16	784	10.96	134		460	324	58.67	41.33
7	28	9	3	18	784	10.96	135		484	300	61.73	38.27
8	31	9	2	17	784	10.96	136		527	257	67.22	32.78
5	28	9	5	17	783	10.94	137		536	247	68.45	31.55
4	24	9	6	17	782	10.93	138		523	259	66.88	33.12
9	8	9	3	17	782	10.93	139		496	286	63.43	36.57
6	30	9	3	18	781	10.91	140		522	259	66.84	33.16
4	21	9	3	17	780	10.9	141	7156	471	309	60.38	39.62
5	13	9	4	17	780	10.9	142		510	270	65.38	34.62
8	24	9	2	18	779	10.89	143		502	277	64.44	35.56
7	24	9	6	18	778	10.87	144		524	254	67.35	32.65
5	27	9	4	17	777	10.86	145		518	259	66.67	33.33
8	18	9	3	17	777	10.86	146		479	298	61.65	38.35
8	31	9	2	18	777	10.86	147		508	269	65.38	34.62
10	5	9	2	17	777	10.86	148		487	290	62.68	37.32
9	3	9	5	18	776	10.84	149		526	250	67.78	32.22
9	22	9	3	17	776	10.84	150		488	288	62.89	37.11
5	19	9	3	17	775	10.83	151		471	304	60.77	39.23
5	7	9	5	17	774	10.82	152		505	269	65.25	34.75
11	10	9	3	17	774	10.82	153		507	267	65.5	34.5
6	24	9	4	18	773	10.8	154		491	282	63.52	36.48
9	15	9	3	18	773	10.8	155		509	264	65.85	34.15
5	22	9	6	16	772	10.79	156		496	276	64.25	35.75
9	14	9	2	17	770	10.76	157		477	293	61.95	38.05
5	1	9	6	17	769	10.75	158		492	277	63.98	36.02
5	29	9	6	18	769	10.75	159		508	261	66.06	33.94
9	30	9	4	18	769	10.75	160		517	252	67.23	32.77
5	22	9	6	18	768	10.73	161	7156	521	247	67.84	32.16
5	27	9	4	18	768	10.73	162		498	270	64.84	35.16
6	26	9	6	17	767	10.72	163		461	306	60.1	39.9
9	3	9	5	17	766	10.7	164		511	255	66.71	33.29
9	16	9	4	18	766	10.7	165		514	252	67.1	32.9
10	6	9	3	17	766	10.7	166		468	298	61.1	38.9
6	26	9	6	18	765	10.69	167		519	246	67.84	32.16
5	28	9	5	18	764	10.68	168		513	251	67.15	32.85
7	7	9	3	18	763	10.66	169		480	283	62.91	37.09
5	20	9	4	18	762	10.65	170		515	247	67.59	32.41
11	3	9	3	17	761	10.63	171		504	257	66.23	33.77
12	2	9	4	17	761	10.63	172		480	281	63.07	36.93
9	23	9	4	17	760	10.62	173		488	272	64.21	35.79

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
11	5	9	5	17	760	10.62	174		477	283	62.76	37.24
4	30	9	5	17	759	10.61	175		477	282	62.85	37.15
6	4	9	5	18	759	10.61	176		510	249	67.19	32.81
8	7	9	6	17	759	10.61	177		502	257	66.14	33.86
9	21	9	2	17	759	10.61	178		526	233	69.3	30.7
9	24	9	5	18	759	10.61	179		506	253	66.67	33.33
6	1	9	2	17	758	10.59	180		497	261	65.57	34.43
9	17	9	5	18	758	10.59	181	7156	533	225	70.32	29.68
6	3	9	4	18	756	10.56	182		482	274	63.76	36.24
9	8	9	3	18	756	10.56	183		483	273	63.89	36.11
10	9	9	6	17	756	10.56	184		487	269	64.42	35.58

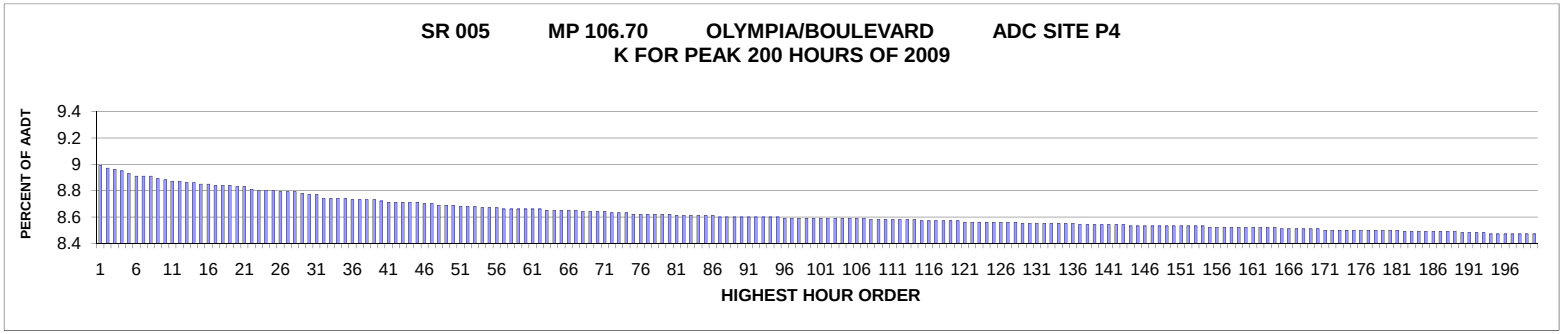

AADT= 138427 **K 30 FACTOR=** 8.77 **K 100 FACTOR=** 8.59 **K 200 FACTOR=** 8.47 **D FACTOR=** 51.53

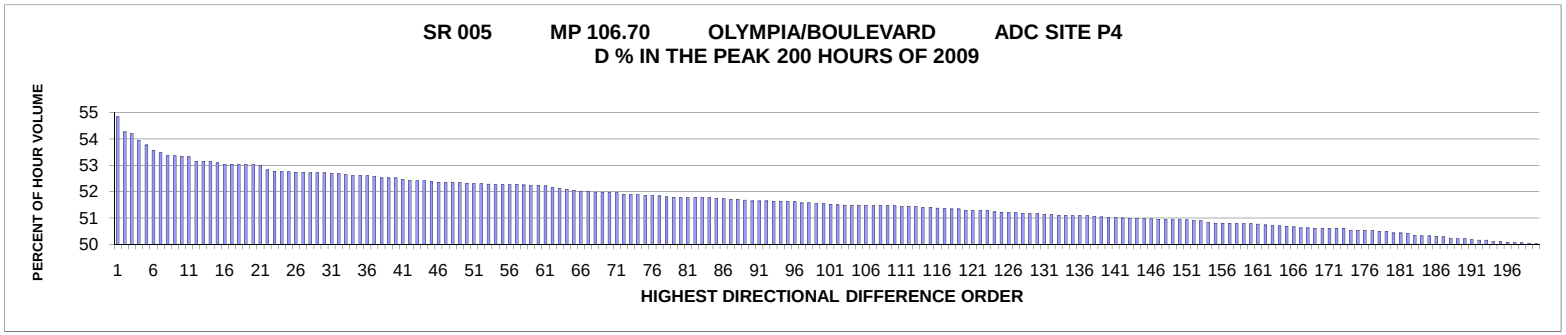

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
6	11	9	5	18	12450	8.99	1	138427	6657	5793	53.47	46.53
2	13	9	6	17	12411	8.97	2		6332	6079	51.02	48.98
6	11	9	5	17	12406	8.96	3		6453	5953	52.02	47.98
5	15	9	6	17	12389	8.95	4		6461	5928	52.15	47.85
8	6	9	5	17	12365	8.93	5		6462	5903	52.26	47.74
8	5	9	4	17	12335	8.91	6		6537	5798	53	47
2	27	9	6	17	12327	8.91	7		6374	5953	51.71	48.29
4	17	9	6	17	12327	8.91	8		6327	6000	51.33	48.67
8	13	9	5	17	12310	8.89	9		6681	5629	54.27	45.73
2	20	9	6	17	12290	8.88	10		6453	5837	52.51	47.49
8	11	9	3	17	12285	8.87	11		6343	5942	51.63	48.37
9	3	9	5	17	12277	8.87	12		6425	5852	52.33	47.67
1	30	9	6	17	12264	8.86	13		6364	5900	51.89	48.11
6	18	9	5	17	12263	8.86	14		6503	5760	53.03	46.97
4	10	9	6	17	12254	8.85	15		6138	6116	50.09	49.91
12	18	9	6	16	12250	8.85	16		6117	6133	49.93	50.07
5	1	9	6	17	12243	8.84	17		6304	5939	51.49	48.51

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	14	9	6	17	12239	8.84	18		6439	5800	52.61	47.39
4	3	9	6	17	12236	8.84	19		6327	5909	51.71	48.29
6	12	9	6	17	12229	8.83	20		6326	5903	51.73	48.27
6	12	9	6	16	12225	8.83	21	138427	6310	5915	51.62	48.38
3	6	9	6	18	12200	8.81	22		6535	5665	53.57	46.43
3	27	9	6	16	12188	8.8	23		6019	6169	49.38	50.62
4	30	9	5	17	12181	8.8	24		6207	5974	50.96	49.04
5	21	9	5	17	12178	8.8	25		6329	5849	51.97	48.03
6	16	9	3	17	12173	8.79	26		6241	5932	51.27	48.73
6	5	9	6	17	12172	8.79	27		6265	5907	51.47	48.53
1	16	9	6	17	12162	8.79	28		6263	5899	51.5	48.5
3	27	9	6	17	12157	8.78	29		6116	6041	50.31	49.69
8	31	9	2	17	12145	8.77	30		6476	5669	53.32	46.68
12	23	9	4	17	12134	8.77	31		6349	5785	52.32	47.68
10	30	9	6	16	12099	8.74	32		5975	6124	49.38	50.62
9	24	9	5	17	12094	8.74	33		6182	5912	51.12	48.88
4	17	9	6	16	12093	8.74	34		6129	5964	50.68	49.32
8	6	9	5	18	12092	8.74	35		6289	5803	52.01	47.99
4	2	9	5	18	12091	8.73	36		6452	5639	53.36	46.64
5	20	9	4	17	12090	8.73	37		6163	5927	50.98	49.02
5	8	9	6	16	12088	8.73	38		6065	6023	50.17	49.83
5	21	9	5	18	12084	8.73	39		6214	5870	51.42	48.58
3	20	9	6	17	12066	8.72	40		6315	5751	52.34	47.66
5	15	9	6	16	12062	8.71	41	138427	6171	5891	51.16	48.84
5	8	9	6	17	12061	8.71	42		6207	5854	51.46	48.54
6	17	9	4	17	12061	8.71	43		6228	5833	51.64	48.36
7	6	9	2	17	12059	8.71	44		6402	5657	53.09	46.91
4	15	9	4	17	12051	8.71	45		6339	5712	52.6	47.4
3	13	9	6	16	12050	8.7	46		6089	5961	50.53	49.47
6	23	9	3	17	12037	8.7	47		6230	5807	51.76	48.24
3	26	9	5	18	12030	8.69	48		6380	5650	53.03	46.97
7	9	9	5	17	12030	8.69	49		6289	5741	52.28	47.72
10	9	9	6	16	12027	8.69	50		5975	6052	49.68	50.32
10	15	9	5	18	12017	8.68	51		6205	5812	51.64	48.36
5	7	9	5	17	12012	8.68	52		6105	5907	50.82	49.18
4	2	9	5	17	12009	8.68	53		6160	5849	51.29	48.71
6	18	9	5	18	12008	8.67	54		6330	5678	52.71	47.29
5	1	9	6	16	12005	8.67	55		6075	5930	50.6	49.4
4	3	9	6	18	11995	8.67	56		6061	5934	50.53	49.47
8	26	9	4	17	11993	8.66	57		6268	5725	52.26	47.74
8	14	9	6	16	11991	8.66	58		6316	5675	52.67	47.33
5	27	9	4	17	11989	8.66	59		6205	5784	51.76	48.24
7	1	9	4	17	11986	8.66	60		6107	5879	50.95	49.05
9	18	9	6	16	11984	8.66	61	138427	6084	5900	50.77	49.23
7	7	9	3	17	11981	8.66	62		6328	5653	52.82	47.18
9	30	9	4	17	11978	8.65	63		6062	5916	50.61	49.39
4	16	9	5	17	11975	8.65	64		6098	5877	50.92	49.08
9	10	9	5	17	11975	8.65	65		6207	5768	51.83	48.17
6	30	9	3	17	11974	8.65	66		6262	5712	52.3	47.7
9	22	9	3	17	11972	8.65	67		6153	5819	51.39	48.61
9	8	9	3	17	11967	8.64	68		6217	5750	51.95	48.05
4	24	9	6	17	11964	8.64	69		6001	5963	50.16	49.84

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
10	2	9	6	17	11959	8.64	70		6200	5759	51.84	48.16
10	8	9	5	17	11957	8.64	71		6071	5886	50.77	49.23
8	28	9	6	17	11948	8.63	72		6128	5820	51.29	48.71
10	20	9	3	17	11947	8.63	73		6184	5763	51.76	48.24
6	12	9	6	18	11942	8.63	74		6250	5692	52.34	47.66
4	10	9	6	18	11938	8.62	75		5976	5962	50.06	49.94
9	18	9	6	17	11936	8.62	76		6151	5785	51.53	48.47
3	13	9	6	17	11935	8.62	77		6179	5756	51.77	48.23
6	10	9	4	17	11935	8.62	78		6155	5780	51.57	48.43
8	18	9	3	17	11934	8.62	79		6290	5644	52.71	47.29
7	16	9	5	17	11926	8.62	80		6264	5662	52.52	47.48
1	23	9	6	17	11922	8.61	81	138427	6045	5877	50.7	49.3
2	13	9	6	18	11922	8.61	82		6154	5768	51.62	48.38
9	1	9	3	17	11919	8.61	83		6270	5649	52.61	47.39
6	17	9	4	18	11915	8.61	84		6288	5627	52.77	47.23
7	1	9	4	18	11914	8.61	85		6264	5650	52.58	47.42
8	20	9	5	18	11914	8.61	86		6319	5595	53.04	46.96
6	24	9	4	17	11911	8.6	87		6143	5768	51.57	48.43
8	28	9	6	16	11909	8.6	88		6089	5820	51.13	48.87
3	30	9	2	17	11906	8.6	89		5957	5949	50.03	49.97
4	10	9	6	16	11905	8.6	90		5862	6043	49.24	50.76
8	25	9	3	17	11905	8.6	91		6111	5794	51.33	48.67
3	19	9	5	17	11901	8.6	92		6014	5887	50.53	49.47
9	17	9	5	17	11900	8.6	93		6072	5828	51.03	48.97
7	31	9	6	15	11899	8.6	94		6045	5854	50.8	49.2
2	12	9	5	18	11898	8.6	95		6347	5551	53.35	46.65
8	5	9	4	18	11897	8.59	96		6273	5624	52.73	47.27
4	17	9	6	18	11896	8.59	97		6160	5736	51.78	48.22
3	20	9	6	18	11893	8.59	98		6156	5737	51.76	48.24
5	18	9	2	18	11893	8.59	99		6445	5448	54.19	45.81
6	12	9	6	15	11893	8.59	100		5853	6040	49.21	50.79
2	13	9	6	15	11892	8.59	101	138427	5620	6272	47.26	52.74
3	27	9	6	15	11890	8.59	102		5720	6170	48.11	51.89
4	23	9	5	17	11890	8.59	103		6057	5833	50.94	49.06
8	10	9	2	17	11890	8.59	104		6270	5620	52.73	47.27
9	3	9	5	18	11888	8.59	105		6218	5670	52.3	47.7
8	21	9	6	17	11887	8.59	106		6224	5663	52.36	47.64
7	8	9	4	17	11884	8.59	107		6112	5772	51.43	48.57
10	22	9	5	17	11879	8.58	108		6055	5824	50.97	49.03
6	2	9	3	17	11878	8.58	109		6069	5809	51.09	48.91
6	4	9	5	17	11877	8.58	110		6258	5619	52.69	47.31
1	15	9	5	17	11876	8.58	111		6133	5743	51.64	48.36
2	6	9	6	17	11875	8.58	112		6079	5796	51.19	48.81
4	23	9	5	18	11874	8.58	113		6113	5761	51.48	48.52
2	5	9	5	17	11871	8.58	114		6007	5864	50.6	49.4
8	27	9	5	18	11868	8.57	115		6219	5649	52.4	47.6
9	15	9	3	17	11866	8.57	116		6201	5665	52.26	47.74
3	12	9	5	18	11865	8.57	117		6181	5684	52.09	47.91
6	19	9	6	17	11862	8.57	118		6002	5860	50.6	49.4
8	14	9	6	15	11860	8.57	119		6148	5712	51.84	48.16
4	28	9	3	17	11859	8.57	120		5977	5882	50.4	49.6
5	8	9	6	15	11851	8.56	121	138427	5820	6031	49.11	50.89

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
6	8	9	2	17	11851	8.56	122		6119	5732	51.63	48.37
7	31	9	6	16	11849	8.56	123		6061	5788	51.15	48.85
6	23	9	3	18	11847	8.56	124		6370	5477	53.77	46.23
10	1	9	5	17	11847	8.56	125		5979	5868	50.47	49.53
4	3	9	6	16	11846	8.56	126		6068	5778	51.22	48.78
7	13	9	2	17	11846	8.56	127		6191	5655	52.26	47.74
3	18	9	4	17	11843	8.56	128		6047	5796	51.06	48.94
2	20	9	6	16	11841	8.55	129		5809	6032	49.06	50.94
5	1	9	6	18	11841	8.55	130		5897	5944	49.8	50.2
5	19	9	3	18	11839	8.55	131		6035	5804	50.98	49.02
10	8	9	5	18	11839	8.55	132		6062	5777	51.2	48.8
6	5	9	6	16	11835	8.55	133		6010	5825	50.78	49.22
12	23	9	4	14	11835	8.55	134		5919	5916	50.01	49.99
7	9	9	5	18	11830	8.55	135		6213	5617	52.52	47.48
11	20	9	6	17	11829	8.55	136		6087	5742	51.46	48.54
3	19	9	5	18	11828	8.54	137		6225	5603	52.63	47.37
8	21	9	6	16	11827	8.54	138		5992	5835	50.66	49.34
10	6	9	3	17	11827	8.54	139		5974	5853	50.51	49.49
4	3	9	6	15	11824	8.54	140		5806	6018	49.1	50.9
8	3	9	2	17	11824	8.54	141	138427	6284	5540	53.15	46.85
8	13	9	5	16	11822	8.54	142		5905	5917	49.95	50.05
3	24	9	3	18	11818	8.54	143		6173	5645	52.23	47.77
10	9	9	6	15	11813	8.53	144		5874	5939	49.72	50.28
9	17	9	5	18	11812	8.53	145		6170	5642	52.24	47.76
3	26	9	5	17	11810	8.53	146		6079	5731	51.47	48.53
1	22	9	5	17	11809	8.53	147		5999	5810	50.8	49.2
12	23	9	4	15	11809	8.53	148		5944	5865	50.33	49.67
3	31	9	3	18	11805	8.53	149		6273	5532	53.14	46.86
2	19	9	5	18	11803	8.53	150		6271	5532	53.13	46.87
8	4	9	3	17	11803	8.53	151		6132	5671	51.95	48.05
5	5	9	3	17	11802	8.53	152		5927	5875	50.22	49.78
2	12	9	5	17	11801	8.53	153		6184	5617	52.4	47.6
6	19	9	6	15	11801	8.53	154		6069	5732	51.43	48.57
9	10	9	5	18	11796	8.52	155		6224	5572	52.76	47.24
8	14	9	6	14	11795	8.52	156		6016	5779	51	49
3	18	9	4	18	11794	8.52	157		6183	5611	52.42	47.58
4	30	9	5	18	11794	8.52	158		6072	5722	51.48	48.52
9	11	9	6	16	11794	8.52	159		5872	5922	49.79	50.21
9	21	9	2	17	11793	8.52	160		6102	5691	51.74	48.26
9	24	9	5	18	11793	8.52	161	138427	6162	5631	52.25	47.75
6	25	9	5	17	11792	8.52	162		6359	5433	53.93	46.07
4	16	9	5	18	11790	8.52	163		6144	5646	52.11	47.89
11	3	9	3	17	11788	8.52	164		6116	5672	51.88	48.12
6	16	9	3	18	11782	8.51	165		6249	5533	53.04	46.96
12	22	9	3	17	11781	8.51	166		6171	5610	52.38	47.62
9	1	9	3	18	11779	8.51	167		6180	5599	52.47	47.53
6	29	9	2	17	11778	8.51	168		5946	5832	50.48	49.52
4	9	9	5	17	11776	8.51	169		6281	5495	53.34	46.66
10	28	9	4	17	11776	8.51	170		5877	5899	49.91	50.09
8	13	9	5	18	11773	8.5	171		6455	5318	54.83	45.17
12	3	9	5	17	11772	8.5	172		6028	5744	51.21	48.79
4	24	9	6	18	11770	8.5	173		5774	5996	49.06	50.94

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
2	27	9	6	18	11769	8.5	174		6003	5766	51.01	48.99
4	27	9	2	17	11768	8.5	175		6033	5735	51.27	48.73
10	30	9	6	17	11768	8.5	176		5865	5903	49.84	50.16
4	7	9	3	17	11766	8.5	177		6080	5686	51.67	48.33
9	18	9	6	15	11765	8.5	178		5833	5932	49.58	50.42
6	25	9	5	18	11763	8.5	179		6142	5621	52.21	47.79
5	20	9	4	18	11761	8.5	180		6042	5719	51.37	48.63
7	8	9	4	18	11761	8.5	181	138427	6055	5706	51.48	48.52
5	12	9	3	17	11759	8.49	182		6038	5721	51.35	48.65
8	24	9	2	17	11757	8.49	183		6120	5637	52.05	47.95
1	30	9	6	16	11755	8.49	184		6005	5750	51.08	48.92
6	26	9	6	17	11754	8.49	185		5926	5828	50.42	49.58
6	10	9	4	18	11751	8.49	186		6230	5521	53.02	46.98
10	15	9	5	17	11751	8.49	187		5957	5794	50.69	49.31
1	16	9	6	16	11750	8.49	188		5712	6038	48.61	51.39
7	14	9	3	17	11747	8.49	189		6047	5700	51.48	48.52
11	13	9	6	17	11743	8.48	190		5942	5801	50.6	49.4
4	15	9	4	18	11739	8.48	191		6102	5637	51.98	48.02
6	1	9	2	17	11735	8.48	192		5994	5741	51.08	48.92
6	5	9	6	18	11734	8.48	193		5997	5737	51.11	48.89
4	28	9	3	18	11731	8.47	194		6077	5654	51.8	48.2
2	13	9	6	16	11727	8.47	195		5828	5899	49.7	50.3
4	21	9	3	17	11727	8.47	196		5949	5778	50.73	49.27
8	21	9	6	13	11726	8.47	197		5736	5990	48.92	51.08
9	2	9	4	17	11726	8.47	198		6043	5683	51.54	48.46
3	24	9	3	17	11724	8.47	199		6000	5724	51.18	48.82
8	25	9	3	18	11718	8.47	200		6176	5542	52.71	47.29

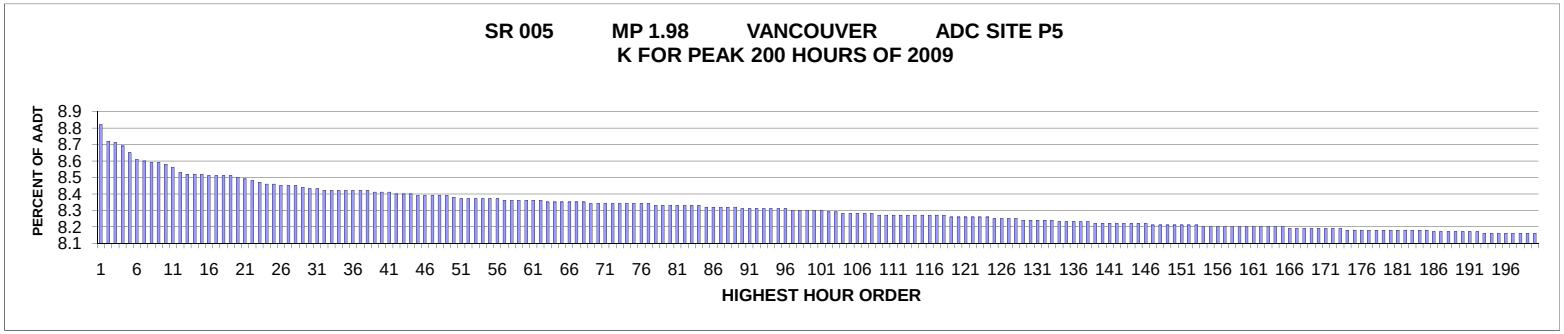

AADT= 123359 **K 30 FACTOR=** 8.43 **K 100 FACTOR=** 8.3 **K 200 FACTOR=** 8.16 **D FACTOR=** 60.02

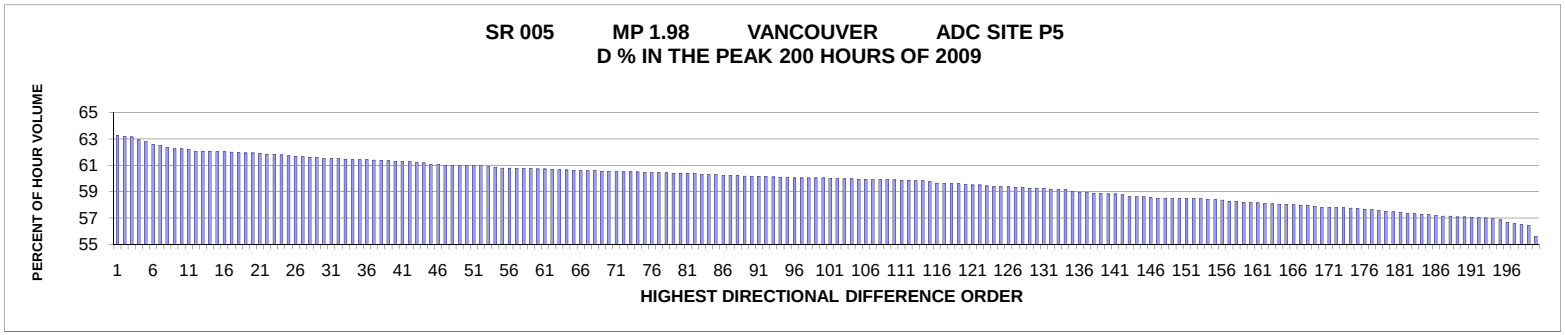

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
4	15	9	4	18	10877	8.82	1	123359	6321	4556	58.11	41.89
10	1	9	5	18	10763	8.72	2		6563	4200	60.98	39.02
6	17	9	4	18	10747	8.71	3		6357	4390	59.15	40.85
10	27	9	3	18	10721	8.69	4		6388	4333	59.58	40.42
8	6	9	5	18	10670	8.65	5		6150	4520	57.64	42.36
4	9	9	5	18	10621	8.61	6		6588	4033	62.03	37.97
10	20	9	3	18	10613	8.6	7		6397	4216	60.28	39.72
8	13	9	5	18	10602	8.59	8		6196	4406	58.44	41.56
9	30	9	4	18	10596	8.59	9		6354	4242	59.97	40.03
9	23	9	4	18	10586	8.58	10		6202	4384	58.59	41.41
4	8	9	4	18	10559	8.56	11		6490	4069	61.46	38.54
11	3	9	3	18	10525	8.53	12		6304	4221	59.9	40.1
5	21	9	5	18	10513	8.52	13		6308	4205	60	40
5	7	9	5	18	10509	8.52	14		6297	4212	59.92	40.08
10	22	9	5	18	10506	8.52	15		6294	4212	59.91	40.09
10	8	9	5	18	10503	8.51	16		6252	4251	59.53	40.47
6	3	9	4	18	10502	8.51	17		6231	4271	59.33	40.67

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
4	23	9	5	18	10500	8.51	18		6346	4154	60.44	39.56
9	24	9	5	18	10500	8.51	19		6274	4226	59.75	40.25
4	28	9	3	18	10491	8.5	20		6289	4202	59.95	40.05
5	15	9	6	17	10472	8.49	21	123359	6013	4459	57.42	42.58
2	13	9	6	16	10463	8.48	22		6023	4440	57.56	42.44
10	28	9	4	18	10448	8.47	23		6309	4139	60.38	39.62
7	23	9	5	18	10433	8.46	24		5954	4479	57.07	42.93
10	7	9	4	18	10433	8.46	25		6191	4242	59.34	40.66
6	16	9	3	18	10425	8.45	26		6378	4047	61.18	38.82
4	14	9	3	18	10420	8.45	27		6513	3907	62.5	37.5
10	6	9	3	18	10418	8.45	28		6291	4127	60.39	39.61
2	6	9	6	17	10410	8.44	29		6076	4334	58.37	41.63
3	13	9	6	18	10403	8.43	30		6118	4285	58.81	41.19
6	5	9	6	17	10399	8.43	31		6032	4367	58.01	41.99
9	29	9	3	18	10392	8.42	32		6392	4000	61.51	38.49
6	2	9	3	18	10389	8.42	33		6521	3868	62.77	37.23
5	12	9	3	18	10388	8.42	34		6398	3990	61.59	38.41
4	29	9	4	18	10387	8.42	35		6275	4112	60.41	39.59
7	9	9	5	18	10383	8.42	36		5919	4464	57.01	42.99
6	17	9	4	17	10382	8.42	37		6215	4167	59.86	40.14
4	22	9	4	18	10381	8.42	38		6289	4092	60.58	39.42
3	18	9	4	18	10380	8.41	39		6353	4027	61.2	38.8
10	13	9	3	18	10377	8.41	40		6370	4007	61.39	38.61
8	26	9	4	18	10371	8.41	41	123359	6116	4255	58.97	41.03
6	10	9	4	18	10367	8.4	42		6160	4207	59.42	40.58
10	15	9	5	17	10367	8.4	43		6300	4067	60.77	39.23
12	1	9	3	18	10363	8.4	44		6310	4053	60.89	39.11
2	18	9	4	18	10354	8.39	45		6352	4002	61.35	38.65
11	4	9	4	18	10353	8.39	46		6216	4137	60.04	39.96
10	15	9	5	18	10352	8.39	47		6310	4042	60.95	39.05
9	9	9	4	18	10348	8.39	48		6238	4110	60.28	39.72
4	30	9	5	18	10345	8.39	49		6248	4097	60.4	39.6
3	26	9	5	18	10340	8.38	50		6199	4141	59.95	40.05
10	30	9	6	17	10327	8.37	51		5988	4339	57.98	42.02
11	17	9	3	18	10327	8.37	52		6183	4144	59.87	40.13
6	11	9	5	18	10326	8.37	53		6367	3959	61.66	38.34
10	21	9	4	18	10326	8.37	54		6130	4196	59.36	40.64
3	11	9	4	18	10322	8.37	55		6263	4059	60.68	39.32
2	20	9	6	17	10319	8.37	56		5962	4357	57.78	42.22
1	21	9	4	18	10318	8.36	57		6266	4052	60.73	39.27
4	16	9	5	18	10318	8.36	58		6196	4122	60.05	39.95
8	27	9	5	18	10315	8.36	59		6111	4204	59.24	40.76
10	14	9	4	18	10310	8.36	60		6297	4013	61.08	38.92
10	30	9	6	16	10308	8.36	61	123359	6027	4281	58.47	41.53
5	14	9	5	18	10307	8.36	62		6148	4159	59.65	40.35
12	3	9	5	17	10306	8.35	63		6171	4135	59.88	40.12
1	16	9	6	17	10303	8.35	64		6060	4243	58.82	41.18
10	1	9	5	17	10302	8.35	65		6202	4100	60.2	39.8
3	6	9	6	18	10301	8.35	66		6162	4139	59.82	40.18
12	18	9	6	17	10299	8.35	67		5947	4352	57.74	42.26
2	26	9	5	18	10295	8.35	68		6375	3920	61.92	38.08
12	3	9	5	18	10294	8.34	69		6193	4101	60.16	39.84

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
1	23	9	6	17	10293	8.34	70		6185	4108	60.09	39.91
2	4	9	4	18	10293	8.34	71		6417	3876	62.34	37.66
8	12	9	4	18	10293	8.34	72		6169	4124	59.93	40.07
4	17	9	6	18	10292	8.34	73		6044	4248	58.73	41.27
5	19	9	3	18	10290	8.34	74		6338	3952	61.59	38.41
2	13	9	6	17	10289	8.34	75		5929	4360	57.62	42.38
2	27	9	6	17	10284	8.34	76		6220	4064	60.48	39.52
7	8	9	4	18	10283	8.34	77		6085	4198	59.18	40.82
11	19	9	5	18	10280	8.33	78		6301	3979	61.29	38.71
7	1	9	4	18	10278	8.33	79		5889	4389	57.3	42.7
11	13	9	6	17	10275	8.33	80		5939	4336	57.8	42.2
12	18	9	6	18	10273	8.33	81	123359	5903	4370	57.46	42.54
1	15	9	5	18	10272	8.33	82		6392	3880	62.23	37.77
3	4	9	4	18	10272	8.33	83		6240	4032	60.75	39.25
9	1	9	3	18	10271	8.33	84		6394	3877	62.25	37.75
10	2	9	6	18	10267	8.32	85		5867	4400	57.14	42.86
1	16	9	6	18	10265	8.32	86		6095	4170	59.38	40.62
9	21	9	2	18	10264	8.32	87		6188	4076	60.29	39.71
5	8	9	6	17	10260	8.32	88		5854	4406	57.06	42.94
2	6	9	6	18	10258	8.32	89		6078	4180	59.25	40.75
3	27	9	6	16	10255	8.31	90		5830	4425	56.85	43.15
2	19	9	5	18	10251	8.31	91		6215	4036	60.63	39.37
11	23	9	2	17	10250	8.31	92		6231	4019	60.79	39.21
4	17	9	6	17	10247	8.31	93		5854	4393	57.13	42.87
6	12	9	6	17	10246	8.31	94		5948	4298	58.05	41.95
5	8	9	6	18	10245	8.31	95		5917	4328	57.76	42.24
9	2	9	4	18	10245	8.31	96		6207	4038	60.59	39.41
9	3	9	5	18	10241	8.3	97		6148	4093	60.03	39.97
6	1	9	2	18	10239	8.3	98		6354	3885	62.06	37.94
12	4	9	6	17	10237	8.3	99		5956	4281	58.18	41.82
12	18	9	6	16	10236	8.3	100		5905	4331	57.69	42.31
5	8	9	6	16	10233	8.3	101	123359	5688	4545	55.58	44.42
4	21	9	3	18	10224	8.29	102		5965	4259	58.34	41.66
12	11	9	6	17	10223	8.29	103		5994	4229	58.63	41.37
11	24	9	3	18	10218	8.28	104		6261	3957	61.27	38.73
5	1	9	6	16	10217	8.28	105		5772	4445	56.49	43.51
11	5	9	5	18	10215	8.28	106		6151	4064	60.22	39.78
5	1	9	6	18	10212	8.28	107		5948	4264	58.25	41.75
11	12	9	5	17	10209	8.28	108		6222	3987	60.95	39.05
3	27	9	6	17	10207	8.27	109		5935	4272	58.15	41.85
3	3	9	3	18	10205	8.27	110		6449	3756	63.19	36.81
6	5	9	6	16	10203	8.27	111		5809	4394	56.93	43.07
5	18	9	2	18	10202	8.27	112		6321	3881	61.96	38.04
5	14	9	5	17	10201	8.27	113		6124	4077	60.03	39.97
8	18	9	3	18	10200	8.27	114		6136	4064	60.16	39.84
4	7	9	3	18	10199	8.27	115		6380	3819	62.56	37.44
7	22	9	4	18	10199	8.27	116		6017	4182	59	41
2	17	9	3	18	10198	8.27	117		6196	4002	60.76	39.24
4	13	9	2	18	10197	8.27	118		6221	3976	61.01	38.99
2	6	9	6	16	10192	8.26	119		5960	4232	58.48	41.52
11	23	9	2	18	10190	8.26	120		6269	3921	61.52	38.48
4	9	9	5	17	10188	8.26	121	123359	6184	4004	60.7	39.3

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
6	5	9	6	18	10187	8.26	122		5896	4291	57.88	42.12
7	7	9	3	18	10187	8.26	123		6129	4058	60.16	39.84
9	23	9	4	17	10184	8.26	124		5911	4273	58.04	41.96
6	18	9	5	18	10182	8.25	125		6217	3965	61.06	38.94
3	13	9	6	17	10181	8.25	126		5806	4375	57.03	42.97
3	20	9	6	17	10173	8.25	127		5897	4276	57.97	42.03
4	30	9	5	17	10171	8.25	128		6082	4089	59.8	40.2
5	5	9	3	17	10170	8.24	129		6311	3859	62.06	37.94
5	1	9	6	17	10168	8.24	130		5890	4278	57.93	42.07
6	4	9	5	17	10168	8.24	131		6155	4013	60.53	39.47
6	24	9	4	18	10166	8.24	132		6187	3979	60.86	39.14
11	20	9	6	17	10162	8.24	133		5906	4256	58.12	41.88
11	4	9	4	17	10158	8.23	134		6190	3968	60.94	39.06
11	6	9	6	16	10154	8.23	135		5839	4315	57.5	42.5
8	7	9	6	18	10149	8.23	136		5810	4339	57.25	42.75
9	17	9	5	18	10149	8.23	137		6051	4098	59.62	40.38
6	26	9	6	18	10148	8.23	138		5723	4425	56.4	43.6
3	19	9	5	18	10146	8.22	139		6417	3729	63.25	36.75
10	20	9	3	17	10145	8.22	140		6142	4003	60.54	39.46
6	12	9	6	18	10142	8.22	141	123359	5942	4200	58.59	41.41
10	9	9	6	17	10142	8.22	142		5925	4217	58.42	41.58
12	1	9	3	17	10141	8.22	143		6126	4015	60.41	39.59
4	24	9	6	17	10138	8.22	144		5797	4341	57.18	42.82
4	10	9	6	16	10136	8.22	145		5802	4334	57.24	42.76
12	9	9	4	18	10136	8.22	146		6130	4006	60.48	39.52
9	9	9	4	17	10132	8.21	147		6086	4046	60.07	39.93
3	5	9	5	18	10131	8.21	148		6289	3842	62.08	37.92
1	28	9	4	18	10128	8.21	149		6258	3870	61.79	38.21
1	30	9	6	17	10125	8.21	150		6092	4033	60.17	39.83
10	9	9	6	18	10124	8.21	151		5956	4168	58.83	41.17
3	10	9	3	18	10123	8.21	152		6391	3732	63.13	36.87
5	5	9	3	18	10123	8.21	153		6219	3904	61.43	38.57
2	20	9	6	18	10121	8.2	154		5737	4384	56.68	43.32
9	30	9	4	17	10121	8.2	155		6138	3983	60.65	39.35
11	24	9	3	17	10121	8.2	156		6075	4046	60.02	39.98
4	8	9	4	17	10120	8.2	157		6245	3875	61.71	38.29
5	26	9	3	18	10117	8.2	158		6239	3878	61.67	38.33
8	10	9	2	18	10116	8.2	159		6261	3855	61.89	38.11
3	6	9	6	17	10115	8.2	160		5845	4270	57.79	42.21
6	2	9	3	17	10115	8.2	161	123359	6290	3825	62.18	37.82
9	11	9	6	18	10115	8.2	162		6059	4056	59.9	40.1
11	30	9	2	18	10115	8.2	163		6272	3843	62.01	37.99
11	12	9	5	18	10114	8.2	164		6163	3951	60.94	39.06
4	17	9	6	16	10110	8.2	165		5761	4349	56.98	43.02
11	3	9	3	17	10108	8.19	166		6124	3984	60.59	39.41
10	16	9	6	16	10105	8.19	167		5790	4315	57.3	42.7
6	8	9	2	18	10102	8.19	168		6200	3902	61.37	38.63
2	11	9	4	18	10100	8.19	169		6110	3990	60.5	39.5
11	13	9	6	18	10099	8.19	170		5984	4115	59.25	40.75
2	4	9	4	17	10098	8.19	171		6253	3845	61.92	38.08
9	14	9	2	18	10098	8.19	172		6131	3967	60.71	39.29
6	3	9	4	17	10097	8.19	173		5905	4192	58.48	41.52

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
9	28	9	2	18	10096	8.18	174		6102	3994	60.44	39.56
10	16	9	6	18	10096	8.18	175		5990	4106	59.33	40.67
3	27	9	6	18	10095	8.18	176		5902	4193	58.46	41.54
4	22	9	4	17	10094	8.18	177		6200	3894	61.42	38.58
10	23	9	6	18	10093	8.18	178		6059	4034	60.03	39.97
3	20	9	6	18	10091	8.18	179		6106	3985	60.51	39.49
8	13	9	5	17	10090	8.18	180		5902	4188	58.49	41.51
8	6	9	5	17	10089	8.18	181	123359	5877	4212	58.25	41.75
5	11	9	2	17	10087	8.18	182		6194	3893	61.41	38.59
4	28	9	3	17	10086	8.18	183		6235	3851	61.82	38.18
1	14	9	4	18	10085	8.18	184		6203	3882	61.51	38.49
5	15	9	6	16	10085	8.18	185		5704	4381	56.56	43.44
3	24	9	3	18	10083	8.17	186		6343	3740	62.91	37.09
2	27	9	6	16	10082	8.17	187		5999	4083	59.5	40.5
2	13	9	6	18	10080	8.17	188		5943	4137	58.96	41.04
9	8	9	3	18	10078	8.17	189		6247	3831	61.99	38.01
3	18	9	4	17	10077	8.17	190		6008	4069	59.62	40.38
12	4	9	6	18	10076	8.17	191		5895	4181	58.51	41.49
12	8	9	3	18	10074	8.17	192		6173	3901	61.28	38.72
10	28	9	4	17	10071	8.16	193		6066	4005	60.23	39.77
10	13	9	3	17	10068	8.16	194		6225	3843	61.83	38.17
7	15	9	4	18	10067	8.16	195		5922	4145	58.83	41.17
11	20	9	6	16	10067	8.16	196		5954	4113	59.14	40.86
11	18	9	4	17	10065	8.16	197		6078	3987	60.39	39.61
12	23	9	4	17	10064	8.16	198		5881	4183	58.44	41.56
6	30	9	3	18	10063	8.16	199		6099	3964	60.61	39.39
3	26	9	5	17	10060	8.16	200		5985	4075	59.49	40.51

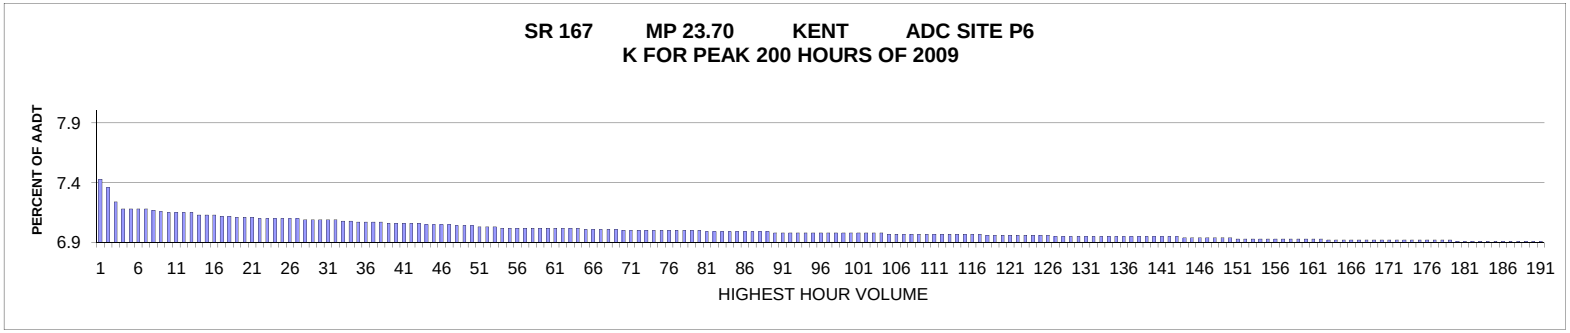

AADT= 114340 **K 30 FACTOR=** 7.09 **K 100 FACTOR=** 6.98 **K 200 FACTOR=** 6.91 **D FACTOR=** 56.41

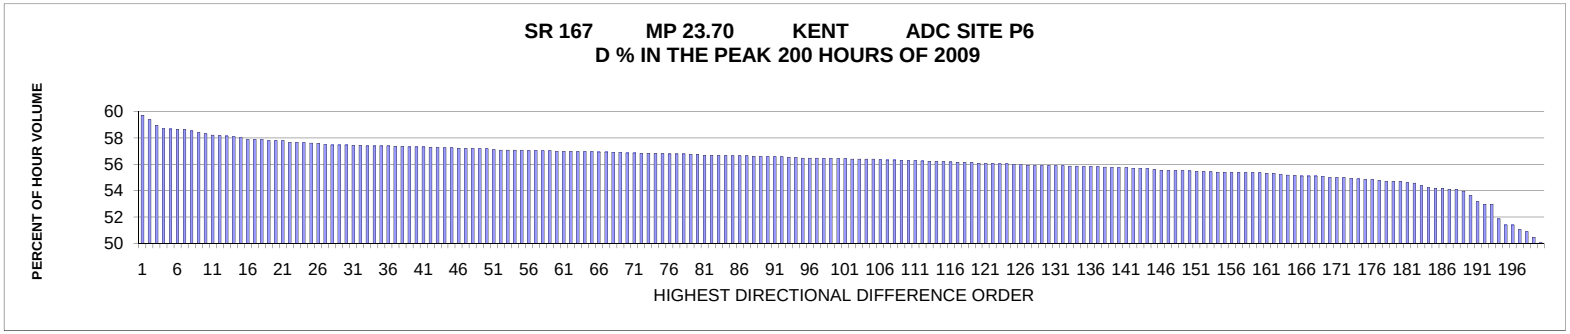

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
12	18	9	6	15	8495	7.43	1	114340	3810	4685	44.85	55.15
12	22	9	3	15	8413	7.36	2		3771	4642	44.82	55.18
6	12	9	6	16	8273	7.24	3		3749	4524	45.32	54.68
10	9	9	6	15	8214	7.18	4		3701	4513	45.06	54.94
3	18	9	4	17	8213	7.18	5		3479	4734	42.36	57.64
4	15	9	4	17	8213	7.18	6		3611	4602	43.97	56.03
4	17	9	6	17	8205	7.18	7		3744	4461	45.63	54.37
12	22	9	3	16	8199	7.17	8		3648	4551	44.49	55.51
7	8	9	4	17	8189	7.16	9		3565	4624	43.53	56.47
4	16	9	5	17	8180	7.15	10		3554	4626	43.45	56.55
5	8	9	6	16	8177	7.15	11		3623	4554	44.31	55.69
6	23	9	3	17	8172	7.15	12		3443	4729	42.13	57.87
6	11	9	5	17	8171	7.15	13		3464	4707	42.39	57.61
2	27	9	6	16	8157	7.13	14		3595	4562	44.07	55.93
4	24	9	6	16	8151	7.13	15		3623	4528	44.45	55.55
12	18	9	6	16	8151	7.13	16		3435	4716	42.14	57.86
5	14	9	5	16	8145	7.12	17		3546	4599	43.54	56.46

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
12	21	9	2	15	8141	7.12	18		3608	4533	44.32	55.68
12	18	9	6	17	8131	7.11	19		3461	4670	42.57	57.43
8	14	9	6	15	8127	7.11	20		3630	4497	44.67	55.33
6	24	9	4	17	8126	7.11	21	114340	3499	4627	43.06	56.94
6	25	9	5	17	8123	7.1	22		3462	4661	42.62	57.38
8	25	9	3	17	8122	7.1	23		3507	4615	43.18	56.82
3	27	9	6	16	8121	7.1	24		3584	4537	44.13	55.87
12	11	9	6	16	8120	7.1	25		3562	4558	43.87	56.13
2	27	9	6	17	8117	7.1	26		3655	4462	45.03	54.97
11	25	9	4	15	8116	7.1	27		3617	4499	44.57	55.43
6	4	9	5	17	8110	7.09	28		3424	4686	42.22	57.78
7	29	9	4	15	8110	7.09	29		3944	4166	48.63	51.37
12	23	9	4	15	8109	7.09	30		3547	4562	43.74	56.26
5	14	9	5	17	8107	7.09	31		3513	4594	43.33	56.67
5	20	9	4	17	8107	7.09	32		3483	4624	42.96	57.04
8	21	9	6	15	8096	7.08	33		3636	4460	44.91	55.09
3	18	9	4	16	8094	7.08	34		3455	4639	42.69	57.31
10	2	9	6	15	8084	7.07	35		3656	4428	45.23	54.77
6	10	9	4	16	8083	7.07	36		3573	4510	44.2	55.8
4	10	9	6	16	8081	7.07	37		3536	4545	43.76	56.24
7	23	9	5	17	8081	7.07	38		3567	4514	44.14	55.86
10	20	9	3	17	8076	7.06	39		3460	4616	42.84	57.16
12	21	9	2	16	8075	7.06	40		3466	4609	42.92	57.08
11	13	9	6	16	8072	7.06	41	114340	3540	4532	43.86	56.14
11	11	9	4	15	8070	7.06	42		3602	4468	44.63	55.37
7	9	9	5	17	8069	7.06	43		3633	4436	45.02	54.98
9	18	9	6	15	8065	7.05	44		3604	4461	44.69	55.31
4	9	9	5	17	8060	7.05	45		3246	4814	40.27	59.73
6	16	9	3	17	8057	7.05	46		3476	4581	43.14	56.86
6	10	9	4	17	8056	7.05	47		3481	4575	43.21	56.79
3	26	9	5	17	8051	7.04	48		3369	4682	41.85	58.15
3	24	9	3	17	8048	7.04	49		3269	4779	40.62	59.38
3	26	9	5	16	8044	7.04	50		3489	4555	43.37	56.63
9	22	9	3	15	8043	7.03	51		3644	4399	45.31	54.69
4	22	9	4	17	8039	7.03	52		3476	4563	43.24	56.76
4	15	9	4	16	8033	7.03	53		3483	4550	43.36	56.64
7	8	9	4	16	8032	7.02	54		3538	4494	44.05	55.95
2	13	9	6	16	8031	7.02	55		3573	4458	44.49	55.51
8	7	9	6	15	8031	7.02	56		3725	4306	46.38	53.62
4	10	9	6	17	8025	7.02	57		3496	4529	43.56	56.44
12	17	9	5	15	8023	7.02	58		3624	4399	45.17	54.83
5	5	9	3	17	8022	7.02	59		3337	4685	41.6	58.4
3	11	9	4	17	8021	7.02	60		3368	4653	41.99	58.01
4	18	9	7	17	8021	7.02	61	114340	4158	3863	51.84	48.16
5	7	9	5	16	8021	7.02	62		3466	4555	43.21	56.79
6	5	9	6	17	8021	7.02	63		3539	4482	44.12	55.88
11	13	9	6	17	8021	7.02	64		3579	4442	44.62	55.38
9	3	9	5	17	8020	7.01	65		3671	4349	45.77	54.23
9	2	9	4	17	8015	7.01	66		3341	4674	41.68	58.32
10	2	9	6	17	8014	7.01	67		3465	4549	43.24	56.76
12	11	9	6	17	8012	7.01	68		3488	4524	43.53	56.47
2	3	9	3	17	8011	7.01	69		3311	4700	41.33	58.67

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
10	28	9	4	16	8006	7	70		3429	4577	42.83	57.17
4	30	9	5	16	8005	7	71		3425	4580	42.79	57.21
4	16	9	5	16	8004	7	72		3436	4568	42.93	57.07
6	3	9	4	16	8002	7	73		3447	4555	43.08	56.92
8	26	9	4	15	8002	7	74		3610	4392	45.11	54.89
10	28	9	4	17	8002	7	75		3443	4559	43.03	56.97
11	11	9	4	16	8001	7	76		3542	4459	44.27	55.73
7	7	9	3	17	8000	7	77		3410	4590	42.63	57.38
4	9	9	5	16	7999	7	78		3416	4583	42.71	57.29
6	2	9	3	17	7999	7	79		3392	4607	42.41	57.59
9	26	9	7	16	7999	7	80		3929	4070	49.12	50.88
5	1	9	6	17	7996	6.99	81	114340	3557	4439	44.48	55.52
6	19	9	6	16	7996	6.99	82		3669	4327	45.89	54.11
9	23	9	4	16	7996	6.99	83		3466	4530	43.35	56.65
8	7	9	6	17	7994	6.99	84		3558	4436	44.51	55.49
9	25	9	6	15	7994	6.99	85		3566	4428	44.61	55.39
4	29	9	4	17	7993	6.99	86		3384	4609	42.34	57.66
10	9	9	6	16	7993	6.99	87		3550	4443	44.41	55.59
9	30	9	4	16	7990	6.99	88		3492	4498	43.7	56.3
5	12	9	3	16	7989	6.99	89		3397	4592	42.52	57.48
5	1	9	6	16	7986	6.98	90		3626	4360	45.4	54.6
11	4	9	4	16	7986	6.98	91		3429	4557	42.94	57.06
5	1	9	6	15	7984	6.98	92		3658	4326	45.82	54.18
9	24	9	5	16	7984	6.98	93		3507	4477	43.93	56.07
2	17	9	3	16	7982	6.98	94		3310	4672	41.47	58.53
4	17	9	6	16	7982	6.98	95		3522	4460	44.12	55.88
6	9	9	3	16	7982	6.98	96		3436	4546	43.05	56.95
12	11	9	6	15	7982	6.98	97		3605	4377	45.16	54.84
5	15	9	6	15	7981	6.98	98		3616	4365	45.31	54.69
12	22	9	3	17	7980	6.98	99		3379	4601	42.34	57.66
7	16	9	5	17	7979	6.98	100		3479	4500	43.6	56.4
4	29	9	4	16	7978	6.98	101	114340	3434	4544	43.04	56.96
6	11	9	5	16	7976	6.98	102		3531	4445	44.27	55.73
6	23	9	3	16	7976	6.98	103		3409	4567	42.74	57.26
11	12	9	5	17	7976	6.98	104		3411	4565	42.77	57.23
11	11	9	4	17	7974	6.97	105		3476	4498	43.59	56.41
8	26	9	4	17	7973	6.97	106		3464	4509	43.45	56.55
9	11	9	6	15	7972	6.97	107		3670	4302	46.04	53.96
4	21	9	3	17	7970	6.97	108		3534	4436	44.34	55.66
7	22	9	4	17	7969	6.97	109		3455	4514	43.36	56.64
12	23	9	4	16	7969	6.97	110		3389	4580	42.53	57.47
6	2	9	3	16	7968	6.97	111		3503	4465	43.96	56.04
9	26	9	7	17	7968	6.97	112		3948	4020	49.55	50.45
12	29	9	3	16	7968	6.97	113		3401	4567	42.68	57.32
4	7	9	3	16	7967	6.97	114		3291	4676	41.31	58.69
5	27	9	4	17	7966	6.97	115		3418	4548	42.91	57.09
9	29	9	3	16	7966	6.97	116		3410	4556	42.81	57.19
2	20	9	6	16	7965	6.97	117		3513	4452	44.11	55.89
7	1	9	4	16	7963	6.96	118		3431	4532	43.09	56.91
8	6	9	5	17	7963	6.96	119		3478	4485	43.68	56.32
7	15	9	4	17	7960	6.96	120		3438	4522	43.19	56.81
11	12	9	5	16	7960	6.96	121	114340	3461	4499	43.48	56.52

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	13	9	5	16	7959	6.96	122		3470	4489	43.6	56.4
9	2	9	4	16	7959	6.96	123		3386	4573	42.54	57.46
6	5	9	6	16	7956	6.96	124		3468	4488	43.59	56.41
10	22	9	5	16	7955	6.96	125		3414	4541	42.92	57.08
12	12	9	7	18	7954	6.96	126		3978	3976	50.01	49.99
2	13	9	6	17	7952	6.95	127		3484	4468	43.81	56.19
3	5	9	5	17	7952	6.95	128		3333	4619	41.91	58.09
9	24	9	5	17	7951	6.95	129		3511	4440	44.16	55.84
5	8	9	6	17	7950	6.95	130		3464	4486	43.57	56.43
6	5	9	6	15	7949	6.95	131		3611	4338	45.43	54.57
6	9	9	3	17	7948	6.95	132		3392	4556	42.68	57.32
6	17	9	4	16	7948	6.95	133		3455	4493	43.47	56.53
10	30	9	6	16	7948	6.95	134		3467	4481	43.62	56.38
9	30	9	4	17	7947	6.95	135		3389	4558	42.65	57.35
11	4	9	4	15	7947	6.95	136		3514	4433	44.22	55.78
4	30	9	5	17	7946	6.95	137		3470	4476	43.67	56.33
8	12	9	4	15	7946	6.95	138		3723	4223	46.85	53.15
3	10	9	3	16	7945	6.95	139		3431	4514	43.18	56.82
5	7	9	5	17	7944	6.95	140		3427	4517	43.14	56.86
9	22	9	3	17	7943	6.95	141	114340	3386	4557	42.63	57.37
12	21	9	2	17	7943	6.95	142		3323	4620	41.84	58.16
5	19	9	3	16	7941	6.95	143		3384	4557	42.61	57.39
4	23	9	5	16	7940	6.94	144		3383	4557	42.61	57.39
8	26	9	4	16	7940	6.94	145		3449	4491	43.44	56.56
12	17	9	5	16	7939	6.94	146		3398	4541	42.8	57.2
6	18	9	5	17	7938	6.94	147		3468	4470	43.69	56.31
2	20	9	6	15	7936	6.94	148		3564	4372	44.91	55.09
2	5	9	5	17	7935	6.94	149		3343	4592	42.13	57.87
10	29	9	5	17	7933	6.94	150		3377	4556	42.57	57.43
8	20	9	5	16	7929	6.93	151		3536	4393	44.6	55.4
3	27	9	6	17	7927	6.93	152		3436	4491	43.35	56.65
3	10	9	3	17	7925	6.93	153		3388	4537	42.75	57.25
9	26	9	7	15	7923	6.93	154		3726	4197	47.03	52.97
11	25	9	4	14	7923	6.93	155		3726	4197	47.03	52.97
3	12	9	5	16	7922	6.93	156		3412	4510	43.07	56.93
8	27	9	5	16	7922	6.93	157		3408	4514	43.02	56.98
5	9	9	7	16	7921	6.93	158		4042	3879	51.03	48.97
10	23	9	6	15	7921	6.93	159		3638	4283	45.93	54.07
7	16	9	5	16	7919	6.93	160		3487	4432	44.03	55.97
9	3	9	5	15	7919	6.93	161	114340	3537	4382	44.66	55.34
9	8	9	3	15	7919	6.93	162		3534	4385	44.63	55.37
6	24	9	4	18	7918	6.92	163		3504	4414	44.25	55.75
9	11	9	6	16	7918	6.92	164		3546	4372	44.78	55.22
8	5	9	4	18	7917	6.92	165		3557	4360	44.93	55.07
5	21	9	5	16	7916	6.92	166		3467	4449	43.8	56.2
7	1	9	4	15	7916	6.92	167		3627	4289	45.82	54.18
8	6	9	5	16	7916	6.92	168		3480	4436	43.96	56.04
4	8	9	4	17	7911	6.92	169		3248	4663	41.06	58.94
8	12	9	4	16	7911	6.92	170		3552	4359	44.9	55.1
5	27	9	4	16	7910	6.92	171		3415	4495	43.17	56.83
6	23	9	3	18	7910	6.92	172		3418	4492	43.21	56.79
7	7	9	3	16	7910	6.92	173		3527	4383	44.59	55.41

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	25	9	3	16	7910	6.92	174		3449	4461	43.6	56.4
4	7	9	3	17	7909	6.92	175		3305	4604	41.79	58.21
6	24	9	4	16	7909	6.92	176		3399	4510	42.98	57.02
10	9	9	6	17	7908	6.92	177		3398	4510	42.97	57.03
2	18	9	4	16	7907	6.92	178		3402	4505	43.03	56.97
8	4	9	3	17	7907	6.92	179		3363	4544	42.53	57.47
2	20	9	6	17	7906	6.91	180		3407	4499	43.09	56.91
7	23	9	5	16	7906	6.91	181	114340	3433	4473	43.42	56.58
9	23	9	4	15	7905	6.91	182		3476	4429	43.97	56.03
9	29	9	3	15	7905	6.91	183		3528	4377	44.63	55.37
12	9	9	4	17	7905	6.91	184		3431	4474	43.4	56.6
10	30	9	6	15	7904	6.91	185		3460	4444	43.78	56.22
10	2	9	6	16	7903	6.91	186		3488	4415	44.14	55.86
2	18	9	4	17	7902	6.91	187		3267	4635	41.34	58.66
9	9	9	4	17	7902	6.91	188		3337	4565	42.23	57.77
9	23	9	4	17	7902	6.91	189		3491	4411	44.18	55.82
2	4	9	4	17	7901	6.91	190		3268	4633	41.36	58.64
6	3	9	4	17	7901	6.91	191		3463	4438	43.83	56.17
9	2	9	4	15	7901	6.91	192		3728	4173	47.18	52.82

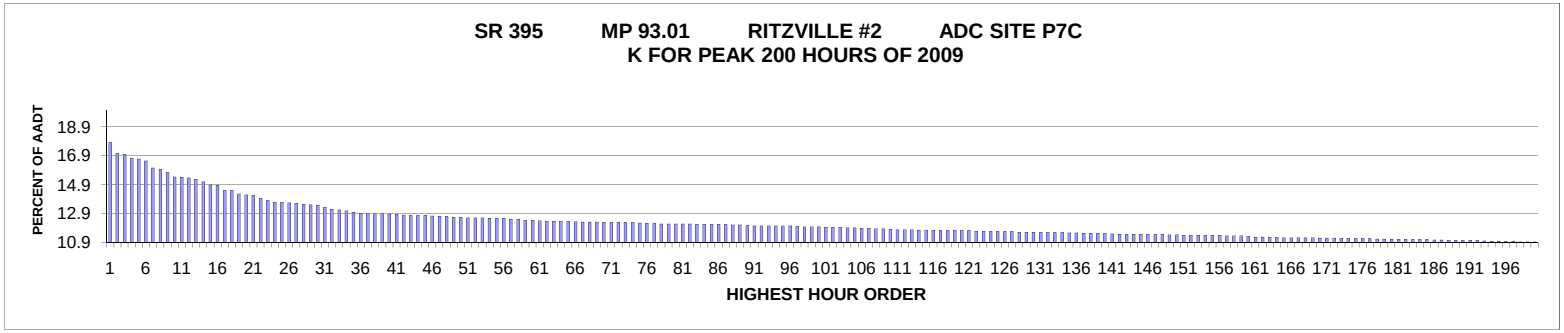

AADT= 7029 **K 30 FACTOR=** 13.47 **K 100 FACTOR=** 11.98 **K 200 FACTOR=** 10.94 **D FACTOR=** 55.97

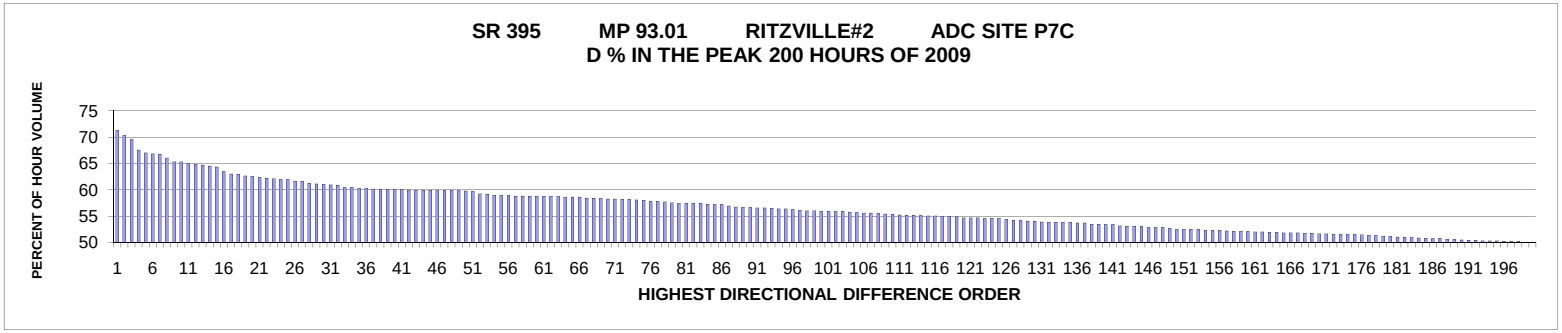

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
11	29	9	1	15	1251	17.8	1	7029	637	614	50.92	49.08
10	4	9	1	15	1200	17.07	2		439	761	36.58	63.42
11	29	9	1	16	1194	16.99	3		700	494	58.63	41.37
11	25	9	4	15	1177	16.74	4		608	569	51.66	48.34
11	29	9	1	14	1171	16.66	5		525	646	44.83	55.17
10	4	9	1	17	1162	16.53	6		573	589	49.31	50.69
7	5	9	1	15	1128	16.05	7		400	728	35.46	64.54
11	25	9	4	16	1121	15.95	8		586	535	52.27	47.73
10	4	9	1	18	1106	15.73	9		511	595	46.2	53.8
10	4	9	1	14	1085	15.44	10		358	727	33	67
11	29	9	1	17	1084	15.42	11		664	420	61.25	38.75
10	4	9	1	16	1080	15.36	12		445	635	41.2	58.8
11	25	9	4	17	1072	15.25	13		562	510	52.43	47.57
7	5	9	1	16	1062	15.11	14		415	647	39.08	60.92
10	4	9	1	19	1045	14.87	15		608	437	58.18	41.82
9	7	9	2	16	1044	14.85	16		441	603	42.24	57.76
8	2	9	1	18	1018	14.48	17		615	403	60.41	39.59

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
9	7	9	2	15	1018	14.48	18		382	636	37.52	62.48
8	9	9	1	18	1002	14.26	19		591	411	58.98	41.02
7	5	9	1	14	998	14.2	20		346	652	34.67	65.33
8	16	9	1	18	994	14.14	21	7029	586	408	58.95	41.05
7	5	9	1	13	980	13.94	22		318	662	32.45	67.55
11	29	9	1	13	969	13.79	23		388	581	40.04	59.96
11	25	9	4	14	962	13.69	24		484	478	50.31	49.69
10	4	9	1	13	961	13.67	25		293	668	30.49	69.51
9	7	9	2	17	958	13.63	26		455	503	47.49	52.51
8	9	9	1	19	957	13.62	27		620	337	64.79	35.21
8	9	9	1	15	950	13.52	28		446	504	46.95	53.05
7	5	9	1	17	949	13.5	29		401	548	42.26	57.74
8	2	9	1	16	947	13.47	30		378	569	39.92	60.08
8	16	9	1	17	938	13.34	31		477	461	50.85	49.15
11	29	9	1	12	927	13.19	32		378	549	40.78	59.22
8	16	9	1	15	925	13.16	33		394	531	42.59	57.41
6	28	9	1	18	920	13.09	34		366	554	39.78	60.22
6	26	9	6	15	914	13	35		547	367	59.85	40.15
7	26	9	1	15	907	12.9	36		411	496	45.31	54.69
5	22	9	6	15	906	12.89	37		494	412	54.53	45.47
8	9	9	1	14	905	12.88	38		403	502	44.53	55.47
8	9	9	1	16	905	12.88	39		418	487	46.19	53.81
8	16	9	1	14	904	12.86	40		363	541	40.15	59.85
6	28	9	1	17	903	12.85	41	7029	395	508	43.74	56.26
9	4	9	6	17	900	12.8	42		542	358	60.22	39.78
5	22	9	6	18	897	12.76	43		498	399	55.52	44.48
11	25	9	4	18	897	12.76	44		471	426	52.51	47.49
6	26	9	6	16	896	12.75	45		564	332	62.95	37.05
10	4	9	1	12	895	12.73	46		266	629	29.72	70.28
8	16	9	1	16	894	12.72	47		383	511	42.84	57.16
7	24	9	6	16	893	12.7	48		464	429	51.96	48.04
8	9	9	1	17	889	12.65	49		444	445	49.94	50.06
9	4	9	6	15	889	12.65	50		498	391	56.02	43.98
6	28	9	1	15	885	12.59	51		386	499	43.62	56.38
8	2	9	1	15	885	12.59	52		410	475	46.33	53.67
8	7	9	6	17	885	12.59	53		499	386	56.38	43.62
8	2	9	1	17	884	12.58	54		381	503	43.1	56.9
7	2	9	5	15	883	12.56	55		531	352	60.14	39.86
7	24	9	6	15	883	12.56	56		472	411	53.45	46.55
8	16	9	1	19	879	12.51	57		517	362	58.82	41.18
5	25	9	2	15	878	12.49	58		373	505	42.48	57.52
8	14	9	6	15	874	12.43	59		478	396	54.69	45.31
9	4	9	6	16	874	12.43	60		480	394	54.92	45.08
8	2	9	1	13	871	12.39	61	7029	340	531	39.04	60.96
7	31	9	6	17	870	12.38	62		486	384	55.86	44.14
8	14	9	6	12	870	12.38	63		459	411	52.76	47.24
11	29	9	1	18	870	12.38	64		568	302	65.29	34.71
9	7	9	2	14	869	12.36	65		310	559	35.67	64.33
7	12	9	1	16	867	12.33	66		418	449	48.21	51.79
6	26	9	6	14	866	12.32	67		505	361	58.31	41.69
7	12	9	1	13	866	12.32	68		348	518	40.18	59.82
11	25	9	4	13	865	12.31	69		439	426	50.75	49.25

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	3	9	6	12	864	12.29	70		535	329	61.92	38.08
8	2	9	1	19	863	12.28	71		537	326	62.22	37.78
8	23	9	1	15	863	12.28	72		380	483	44.03	55.97
7	19	9	1	15	862	12.26	73		413	449	47.91	52.09
8	23	9	1	17	862	12.26	74		408	454	47.33	52.67
8	14	9	6	17	861	12.25	75		488	373	56.68	43.32
7	10	9	6	16	859	12.22	76		479	380	55.76	44.24
8	7	9	6	16	858	12.21	77		444	414	51.75	48.25
7	17	9	6	13	857	12.19	78		425	432	49.59	50.41
8	9	9	1	13	857	12.19	79		342	515	39.91	60.09
7	12	9	1	14	856	12.18	80		333	523	38.9	61.1
7	26	9	1	16	856	12.18	81	7029	401	455	46.85	53.15
9	4	9	6	18	856	12.18	82		539	317	62.97	37.03
7	31	9	6	15	855	12.16	83		511	344	59.77	40.23
8	23	9	1	14	855	12.16	84		354	501	41.4	58.6
5	25	9	2	16	854	12.15	85		394	460	46.14	53.86
7	12	9	1	15	854	12.15	86		377	477	44.15	55.85
7	5	9	1	12	853	12.14	87		245	608	28.72	71.28
7	26	9	1	14	851	12.11	88		382	469	44.89	55.11
8	23	9	1	16	851	12.11	89		410	441	48.18	51.82
8	2	9	1	14	848	12.06	90		336	512	39.62	60.38
7	3	9	6	11	847	12.05	91		462	385	54.55	45.45
7	5	9	1	18	847	12.05	92		391	456	46.16	53.84
12	27	9	1	15	847	12.05	93		442	405	52.18	47.82
5	25	9	2	14	846	12.04	94		316	530	37.35	62.65
6	26	9	6	17	846	12.04	95		524	322	61.94	38.06
12	27	9	1	16	846	12.04	96		436	410	51.54	48.46
7	3	9	6	14	844	12.01	97		491	353	58.18	41.82
8	13	9	5	17	843	11.99	98		441	402	52.31	47.69
8	7	9	6	15	842	11.98	99		439	403	52.14	47.86
8	13	9	5	15	842	11.98	100		390	452	46.32	53.68
5	22	9	6	17	841	11.96	101	7029	463	378	55.05	44.95
8	21	9	6	16	839	11.94	102		463	376	55.18	44.82
9	7	9	2	18	839	11.94	103		409	430	48.75	51.25
7	2	9	5	16	838	11.92	104		493	345	58.83	41.17
7	30	9	5	15	838	11.92	105		385	453	45.94	54.06
6	12	9	6	15	835	11.88	106		502	333	60.12	39.88
7	24	9	6	17	834	11.87	107		449	385	53.84	46.16
8	6	9	5	16	833	11.85	108		381	452	45.74	54.26
6	19	9	6	15	832	11.84	109		426	406	51.2	48.8
7	12	9	1	17	830	11.81	110		400	430	48.19	51.81
7	10	9	6	15	829	11.79	111		426	403	51.39	48.61
8	7	9	6	12	829	11.79	112		424	405	51.15	48.85
6	28	9	1	16	828	11.78	113		368	460	44.44	55.56
8	7	9	6	14	827	11.77	114		407	420	49.21	50.79
8	7	9	6	13	826	11.75	115		417	409	50.48	49.52
6	12	9	6	14	825	11.74	116		450	375	54.55	45.45
6	21	9	1	17	824	11.72	117		471	353	57.16	42.84
7	2	9	5	17	824	11.72	118		483	341	58.62	41.38
7	26	9	1	17	823	11.71	119		416	407	50.55	49.45
8	14	9	6	11	823	11.71	120		399	424	48.48	51.52
9	7	9	2	13	823	11.71	121	7029	273	550	33.17	66.83

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
6	21	9	1	16	821	11.68	122		414	407	50.43	49.57
8	14	9	6	16	821	11.68	123		470	351	57.25	42.75
4	5	9	1	16	819	11.65	124		478	341	58.36	41.64
7	6	9	2	16	819	11.65	125		393	426	47.99	52.01
7	24	9	6	14	819	11.65	126		412	407	50.31	49.69
7	3	9	6	13	818	11.64	127		490	328	59.9	40.1
6	12	9	6	16	816	11.61	128		457	359	56	44
6	14	9	1	14	816	11.61	129		353	463	43.26	56.74
7	19	9	1	16	816	11.61	130		410	406	50.25	49.75
7	19	9	1	18	816	11.61	131		396	420	48.53	51.47
4	5	9	1	17	815	11.59	132		476	339	58.4	41.6
6	12	9	6	17	815	11.59	133		423	392	51.9	48.1
7	24	9	6	12	814	11.58	134		407	407	50	50
8	14	9	6	13	813	11.57	135		434	379	53.38	46.62
7	17	9	6	15	812	11.55	136		444	368	54.68	45.32
7	19	9	1	17	811	11.54	137		363	448	44.76	55.24
7	31	9	6	16	811	11.54	138		468	343	57.71	42.29
7	3	9	6	15	810	11.52	139		499	311	61.6	38.4
8	21	9	6	15	809	11.51	140		437	372	54.02	45.98
3	22	9	1	17	808	11.5	141	7029	464	344	57.43	42.57
6	28	9	1	13	807	11.48	142		351	456	43.49	56.51
7	19	9	1	14	807	11.48	143		339	468	42.01	57.99
7	31	9	6	12	807	11.48	144		437	370	54.15	45.85
8	16	9	1	12	807	11.48	145		304	503	37.67	62.33
8	2	9	1	12	805	11.45	146		332	473	41.24	58.76
7	2	9	5	18	804	11.44	147		531	273	66.04	33.96
7	24	9	6	13	804	11.44	148		377	427	46.89	53.11
8	23	9	1	13	803	11.42	149		324	479	40.35	59.65
8	30	9	1	14	803	11.42	150		342	461	42.59	57.41
6	5	9	6	15	802	11.41	151		454	348	56.61	43.39
6	21	9	1	14	802	11.41	152		399	403	49.75	50.25
12	27	9	1	14	801	11.4	153		366	435	45.69	54.31
5	25	9	2	17	800	11.38	154		384	416	48	52
7	19	9	1	13	800	11.38	155		334	466	41.75	58.25
9	4	9	6	14	800	11.38	156		414	386	51.75	48.25
7	17	9	6	16	799	11.37	157		478	321	59.82	40.18
10	4	9	1	20	799	11.37	158		470	329	58.82	41.18
11	25	9	4	19	799	11.37	159		446	353	55.82	44.18
7	26	9	1	13	796	11.32	160		353	443	44.35	55.65
3	22	9	1	16	793	11.28	161	7029	466	327	58.76	41.24
7	5	9	1	19	793	11.28	162		378	415	47.67	52.33
8	13	9	5	16	792	11.27	163		408	384	51.52	48.48
7	30	9	5	16	790	11.24	164		356	434	45.06	54.94
5	22	9	6	16	789	11.22	165		480	309	60.84	39.16
6	14	9	1	17	789	11.22	166		387	402	49.05	50.95
7	10	9	6	12	789	11.22	167		392	397	49.68	50.32
7	31	9	6	14	789	11.22	168		463	326	58.68	41.32
8	16	9	1	13	789	11.22	169		343	446	43.47	56.53
9	7	9	2	12	788	11.21	170		276	512	35.03	64.97
5	22	9	6	19	787	11.2	171		445	342	56.54	43.46
5	25	9	2	18	787	11.2	172		413	374	52.48	47.52
3	22	9	1	18	786	11.18	173		465	321	59.16	40.84

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	23	9	1	18	786	11.18	174		409	377	52.04	47.96
6	28	9	1	14	785	11.17	175		366	419	46.62	53.38
7	17	9	6	14	785	11.17	176		432	353	55.03	44.97
8	7	9	6	18	785	11.17	177		456	329	58.09	41.91
7	31	9	6	13	784	11.15	178		430	354	54.85	45.15
11	29	9	1	11	782	11.13	179		260	522	33.25	66.75
5	3	9	1	15	781	11.11	180		296	485	37.9	62.1
5	22	9	6	14	781	11.11	181	7029	438	343	56.08	43.92
6	14	9	1	16	781	11.11	182		392	389	50.19	49.81
7	2	9	5	14	780	11.1	183		417	363	53.46	46.54
8	9	9	1	12	780	11.1	184		313	467	40.13	59.87
8	21	9	6	14	780	11.1	185		414	366	53.08	46.92
4	5	9	1	18	778	11.07	186		459	319	59	41
6	19	9	6	14	778	11.07	187		397	381	51.03	48.97
8	30	9	1	15	777	11.05	188		331	446	42.6	57.4
6	5	9	6	17	776	11.04	189		430	346	55.41	44.59
11	25	9	4	11	776	11.04	190		311	465	40.08	59.92
6	21	9	1	13	775	11.03	191		376	399	48.52	51.48
8	30	9	1	16	775	11.03	192		366	409	47.23	52.77
6	26	9	6	18	773	11	193		500	273	64.68	35.32
7	2	9	5	19	772	10.98	194		476	296	61.66	38.34
6	28	9	1	19	771	10.97	195		364	407	47.21	52.79
7	17	9	6	17	771	10.97	196		463	308	60.05	39.95
7	30	9	5	17	771	10.97	197		373	398	48.38	51.62
6	19	9	6	16	770	10.95	198		426	344	55.32	44.68
6	21	9	1	15	769	10.94	199		389	380	50.59	49.41
7	2	9	5	13	769	10.94	200		448	321	58.26	41.74

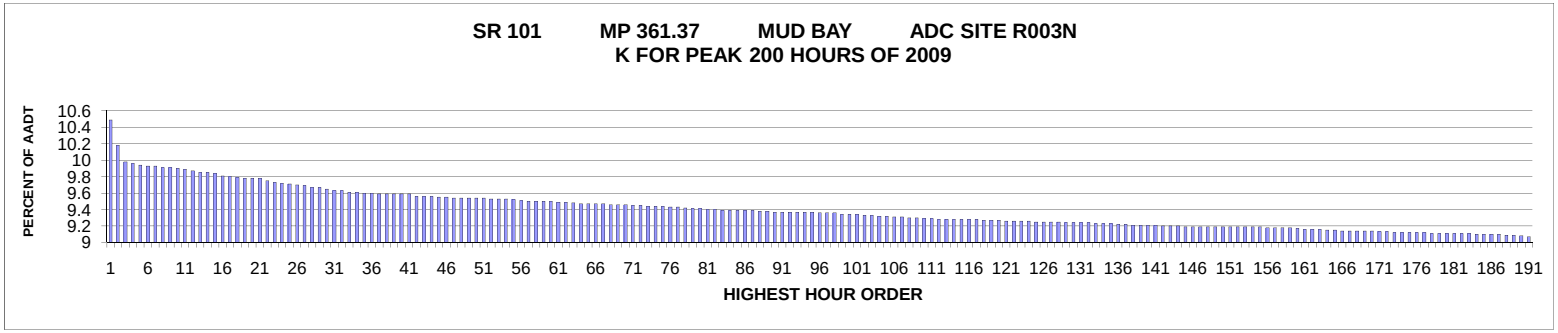

AADT= 30635 **K 30 FACTOR=** 9.65 **K 100 FACTOR=** 9.37 **K 200 FACTOR=** 9.07 **D FACTOR=** 61.69

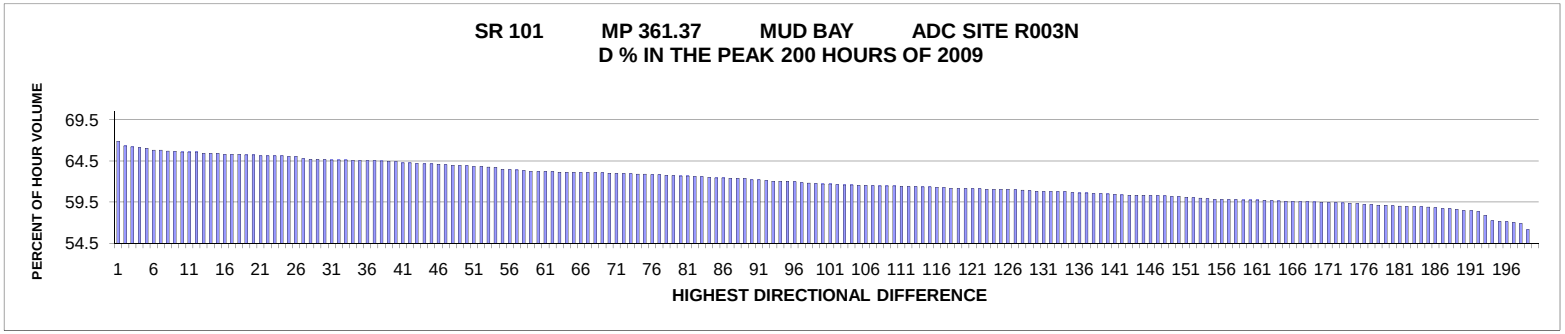

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
6	12	9	6	18	3213	10.49	1	30635	1462	1751	45.5	54.5
5	15	9	6	18	3120	10.18	2		1109	2011	35.54	64.46
5	15	9	6	17	3057	9.98	3		1196	1861	39.12	60.88
5	20	9	4	18	3051	9.96	4		1101	1950	36.09	63.91
9	8	9	3	18	3045	9.94	5		1128	1917	37.04	62.96
9	1	9	3	18	3043	9.93	6		1064	1979	34.97	65.03
10	2	9	6	18	3043	9.93	7		1145	1898	37.63	62.37
5	22	9	6	16	3037	9.91	8		1239	1798	40.8	59.2
10	2	9	6	17	3036	9.91	9		1232	1804	40.58	59.42
9	15	9	3	18	3033	9.9	10		1128	1905	37.19	62.81
9	17	9	5	18	3031	9.89	11		1166	1865	38.47	61.53
9	24	9	5	18	3023	9.87	12		1175	1848	38.87	61.13
9	8	9	3	17	3019	9.85	13		1175	1844	38.92	61.08
5	21	9	5	18	3018	9.85	14		1134	1884	37.57	62.43
6	16	9	3	18	3013	9.84	15		1051	1962	34.88	65.12
5	8	9	6	17	3005	9.81	16		1219	1786	40.57	59.43
5	1	9	6	16	3002	9.8	17		1251	1751	41.67	58.33

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
11	3	9	3	17	3000	9.79	18		1205	1795	40.17	59.83
5	18	9	2	18	2996	9.78	19		1108	1888	36.98	63.02
5	27	9	4	18	2996	9.78	20		1105	1891	36.88	63.12
6	10	9	4	18	2995	9.78	21	30635	1079	1916	36.03	63.97
6	19	9	6	17	2987	9.75	22		1215	1772	40.68	59.32
5	27	9	4	17	2982	9.73	23		1170	1812	39.24	60.76
9	16	9	4	18	2978	9.72	24		1011	1967	33.95	66.05
6	2	9	3	18	2976	9.71	25		1068	1908	35.89	64.11
6	12	9	6	17	2973	9.7	26		1272	1701	42.79	57.21
5	1	9	6	18	2970	9.69	27		1117	1853	37.61	62.39
5	15	9	6	16	2962	9.67	28		1198	1764	40.45	59.55
10	9	9	6	17	2962	9.67	29		1167	1795	39.4	60.6
5	28	9	5	18	2955	9.65	30		1150	1805	38.92	61.08
4	29	9	4	18	2951	9.63	31		1089	1862	36.9	63.1
5	22	9	6	17	2950	9.63	32		1078	1872	36.54	63.46
5	29	9	6	17	2945	9.61	33		1204	1741	40.88	59.12
6	5	9	6	17	2944	9.61	34		1185	1759	40.25	59.75
11	2	9	2	17	2941	9.6	35		1202	1739	40.87	59.13
10	20	9	3	18	2940	9.6	36		1046	1894	35.58	64.42
5	29	9	6	18	2939	9.59	37		1134	1805	38.58	61.42
6	11	9	5	18	2939	9.59	38		1130	1809	38.45	61.55
6	16	9	3	17	2938	9.59	39		1193	1745	40.61	59.39
6	3	9	4	17	2937	9.59	40		1188	1749	40.45	59.55
10	20	9	3	17	2937	9.59	41	30635	1207	1730	41.1	58.9
5	26	9	3	17	2929	9.56	42		1183	1746	40.39	59.61
4	17	9	6	17	2928	9.56	43		1127	1801	38.49	61.51
12	4	9	6	18	2928	9.56	44		1139	1789	38.9	61.1
9	23	9	4	18	2927	9.55	45		1113	1814	38.03	61.97
6	10	9	4	17	2925	9.55	46		1185	1740	40.51	59.49
5	11	9	2	18	2924	9.54	47		1094	1830	37.41	62.59
5	29	9	6	16	2924	9.54	48		1253	1671	42.85	57.15
6	9	9	3	18	2923	9.54	49		1035	1888	35.41	64.59
6	22	9	2	17	2922	9.54	50		1091	1831	37.34	62.66
11	4	9	4	18	2922	9.54	51		1072	1850	36.69	63.31
6	15	9	2	18	2920	9.53	52		984	1936	33.7	66.3
9	3	9	5	18	2919	9.53	53		1103	1816	37.79	62.21
5	1	9	6	17	2918	9.53	54		1150	1768	39.41	60.59
4	24	9	6	18	2915	9.52	55		1157	1758	39.69	60.31
10	9	9	6	18	2913	9.51	56		1072	1841	36.8	63.2
12	4	9	6	17	2911	9.5	57		1146	1765	39.37	60.63
6	3	9	4	18	2910	9.5	58		1141	1769	39.21	60.79
9	29	9	3	18	2909	9.5	59		1055	1854	36.27	63.73
10	7	9	4	18	2909	9.5	60		1015	1894	34.89	65.11
3	20	9	6	17	2906	9.49	61	30635	1124	1782	38.68	61.32
5	20	9	4	17	2906	9.49	62		1170	1736	40.26	59.74
5	26	9	3	18	2904	9.48	63		1078	1826	37.12	62.88
2	5	9	5	18	2901	9.47	64		1003	1898	34.57	65.43
10	8	9	5	18	2901	9.47	65		1040	1861	35.85	64.15
5	12	9	3	17	2900	9.47	66		1152	1748	39.72	60.28
9	4	9	6	18	2900	9.47	67		1008	1892	34.76	65.24
5	12	9	3	18	2899	9.46	68		1036	1863	35.74	64.26
2	3	9	3	18	2897	9.46	69		997	1900	34.41	65.59

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
10	13	9	3	17	2897	9.46	70		1197	1700	41.32	58.68
1	16	9	6	17	2896	9.45	71		1135	1761	39.19	60.81
10	15	9	5	18	2894	9.45	72		1068	1826	36.9	63.1
3	18	9	4	18	2892	9.44	73		980	1912	33.89	66.11
10	5	9	2	17	2892	9.44	74		1156	1736	39.97	60.03
5	8	9	6	18	2891	9.44	75		1123	1768	38.84	61.16
6	11	9	5	17	2890	9.43	76		1161	1729	40.17	59.83
5	21	9	5	17	2889	9.43	77		1170	1719	40.5	59.5
9	30	9	4	18	2886	9.42	78		1056	1830	36.59	63.41
4	22	9	4	18	2884	9.41	79		1068	1816	37.03	62.97
1	30	9	6	17	2882	9.41	80		1165	1717	40.42	59.58
9	4	9	6	17	2881	9.4	81	30635	1059	1822	36.76	63.24
6	1	9	2	18	2879	9.4	82		1018	1861	35.36	64.64
6	15	9	2	17	2877	9.39	83		1142	1735	39.69	60.31
9	3	9	5	17	2877	9.39	84		1159	1718	40.29	59.71
6	19	9	6	18	2876	9.39	85		1097	1779	38.14	61.86
9	29	9	3	17	2876	9.39	86		1109	1767	38.56	61.44
12	2	9	4	18	2876	9.39	87		1063	1813	36.96	63.04
4	15	9	4	18	2875	9.38	88		1058	1817	36.8	63.2
6	8	9	2	18	2873	9.38	89		993	1880	34.56	65.44
9	1	9	3	17	2872	9.37	90		1126	1746	39.21	60.79
12	1	9	3	17	2872	9.37	91		1146	1726	39.9	60.1
12	1	9	3	18	2872	9.37	92		1070	1802	37.26	62.74
6	22	9	2	18	2871	9.37	93		1050	1821	36.57	63.43
4	22	9	4	17	2870	9.37	94		1118	1752	38.95	61.05
9	21	9	2	18	2869	9.37	95		1072	1797	37.36	62.64
4	27	9	2	18	2867	9.36	96		1057	1810	36.87	63.13
9	25	9	6	18	2867	9.36	97		1088	1779	37.95	62.05
4	16	9	5	18	2866	9.36	98		1031	1835	35.97	64.03
5	22	9	6	18	2862	9.34	99		1032	1830	36.06	63.94
9	9	9	4	17	2862	9.34	100		1105	1757	38.61	61.39
11	3	9	3	18	2862	9.34	101	30635	1015	1847	35.46	64.54
6	5	9	6	18	2859	9.33	102		1054	1805	36.87	63.13
10	27	9	3	17	2857	9.33	103		1134	1723	39.69	60.31
3	13	9	6	18	2856	9.32	104		1097	1759	38.41	61.59
10	1	9	5	18	2856	9.32	105		1062	1794	37.18	62.82
5	13	9	4	18	2853	9.31	106		1012	1841	35.47	64.53
11	20	9	6	17	2853	9.31	107		1226	1627	42.97	57.03
2	27	9	6	18	2850	9.3	108		1071	1779	37.58	62.42
5	7	9	5	18	2848	9.3	109		1032	1816	36.24	63.76
5	14	9	5	17	2847	9.29	110		1097	1750	38.53	61.47
5	18	9	2	17	2847	9.29	111		1148	1699	40.32	59.68
5	6	9	4	18	2844	9.28	112		1062	1782	37.34	62.66
6	1	9	2	17	2844	9.28	113		1123	1721	39.49	60.51
9	9	9	4	18	2843	9.28	114		972	1871	34.19	65.81
5	11	9	2	17	2842	9.28	115		1126	1716	39.62	60.38
10	28	9	4	17	2842	9.28	116		1166	1676	41.03	58.97
12	2	9	4	17	2842	9.28	117		1060	1782	37.3	62.7
10	16	9	6	17	2841	9.27	118		1091	1750	38.4	61.6
5	19	9	3	17	2840	9.27	119		1085	1755	38.2	61.8
6	2	9	3	17	2839	9.27	120		1086	1753	38.25	61.75
4	8	9	4	18	2838	9.26	121	30635	1004	1834	35.38	64.62

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
10	8	9	5	17	2838	9.26	122		1163	1675	40.98	59.02
9	10	9	5	18	2836	9.26	123		974	1862	34.34	65.66
10	28	9	4	18	2836	9.26	124		1001	1835	35.3	64.7
4	24	9	6	17	2834	9.25	125		1163	1671	41.04	58.96
10	27	9	3	18	2834	9.25	126		969	1865	34.19	65.81
6	5	9	6	16	2833	9.25	127		1221	1612	43.1	56.9
9	14	9	2	18	2833	9.25	128		1096	1737	38.69	61.31
2	27	9	6	17	2831	9.24	129		1125	1706	39.74	60.26
3	25	9	4	18	2831	9.24	130		1004	1827	35.46	64.54
9	28	9	2	17	2831	9.24	131		1172	1659	41.4	58.6
10	1	9	5	17	2831	9.24	132		1091	1740	38.54	61.46
10	21	9	4	17	2829	9.23	133		1101	1728	38.92	61.08
5	28	9	5	17	2828	9.23	134		1137	1691	40.21	59.79
4	28	9	3	18	2827	9.23	135		1023	1804	36.19	63.81
11	13	9	6	17	2826	9.22	136		1174	1652	41.54	58.46
10	30	9	6	18	2824	9.22	137		1043	1781	36.93	63.07
3	13	9	6	17	2823	9.21	138		1116	1707	39.53	60.47
10	22	9	5	17	2823	9.21	139		1147	1676	40.63	59.37
10	30	9	6	17	2820	9.21	140		1101	1719	39.04	60.96
11	10	9	3	17	2820	9.21	141	30635	1188	1632	42.13	57.87
10	12	9	2	17	2819	9.2	142		1171	1648	41.54	58.46
2	3	9	3	17	2818	9.2	143		1065	1753	37.79	62.21
2	4	9	4	18	2817	9.2	144		966	1851	34.29	65.71
1	15	9	5	17	2816	9.19	145		1088	1728	38.64	61.36
3	3	9	3	18	2816	9.19	146		977	1839	34.69	65.31
4	1	9	4	18	2816	9.19	147		977	1839	34.69	65.31
4	30	9	5	18	2816	9.19	148		1036	1780	36.79	63.21
5	7	9	5	17	2816	9.19	149		1132	1684	40.2	59.8
9	16	9	4	17	2816	9.19	150		1138	1678	40.41	59.59
9	30	9	4	17	2816	9.19	151		1122	1694	39.84	60.16
10	22	9	5	18	2816	9.19	152		1009	1807	35.83	64.17
4	15	9	4	17	2815	9.19	153		1069	1746	37.98	62.02
4	20	9	2	17	2815	9.19	154		1127	1688	40.04	59.96
10	5	9	2	18	2814	9.19	155		982	1832	34.9	65.1
5	13	9	4	17	2813	9.18	156		1156	1657	41.09	58.91
3	18	9	4	17	2812	9.18	157		1054	1758	37.48	62.52
11	4	9	4	17	2812	9.18	158		1158	1654	41.18	58.82
5	19	9	3	18	2811	9.18	159		998	1813	35.5	64.5
12	23	9	4	17	2810	9.17	160		1093	1717	38.9	61.1
3	20	9	6	18	2807	9.16	161	30635	1056	1751	37.62	62.38
5	8	9	6	16	2806	9.16	162		1231	1575	43.87	56.13
12	3	9	5	18	2806	9.16	163		1065	1741	37.95	62.05
5	5	9	3	18	2804	9.15	164		990	1814	35.31	64.69
3	26	9	5	18	2803	9.15	165		973	1830	34.71	65.29
4	14	9	3	18	2801	9.14	166		992	1809	35.42	64.58
4	23	9	5	18	2801	9.14	167		991	1810	35.38	64.62
6	8	9	2	17	2801	9.14	168		1115	1686	39.81	60.19
10	2	9	6	16	2801	9.14	169		1202	1599	42.91	57.09
11	30	9	2	18	2799	9.14	170		986	1813	35.23	64.77
5	14	9	5	18	2798	9.13	171		1086	1712	38.81	61.19
12	9	9	4	17	2798	9.13	172		1072	1726	38.31	61.69
11	24	9	3	17	2794	9.12	173		1144	1650	40.94	59.06

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
12	10	9	5	17	2794	9.12	174		1097	1697	39.26	60.74
3	11	9	4	17	2793	9.12	175		1035	1758	37.06	62.94
3	27	9	6	18	2793	9.12	176		1090	1703	39.03	60.97
12	11	9	6	17	2793	9.12	177		1058	1735	37.88	62.12
1	20	9	3	17	2792	9.11	178		1073	1719	38.43	61.57
3	24	9	3	18	2792	9.11	179		1010	1782	36.17	63.83
4	2	9	5	18	2792	9.11	180		924	1868	33.09	66.91
3	12	9	5	18	2791	9.11	181	30635	943	1848	33.79	66.21
1	28	9	4	18	2790	9.11	182		975	1815	34.95	65.05
4	29	9	4	17	2790	9.11	183		1079	1711	38.67	61.33
10	19	9	2	17	2789	9.1	184		1103	1686	39.55	60.45
10	19	9	2	18	2789	9.1	185		960	1829	34.42	65.58
5	4	9	2	17	2788	9.1	186		1101	1687	39.49	60.51
9	15	9	3	17	2788	9.1	187		1118	1670	40.1	59.9
12	3	9	5	17	2786	9.09	188		1068	1718	38.33	61.67
6	12	9	6	16	2784	9.09	189		1136	1648	40.8	59.2
3	2	9	2	18	2782	9.08	190		971	1811	34.9	65.1
4	28	9	3	17	2779	9.07	191		1076	1703	38.72	61.28
2	13	9	6	17	2778	9.07	192		1092	1686	39.31	60.69
4	13	9	2	18	2778	9.07	193		964	1814	34.7	65.3

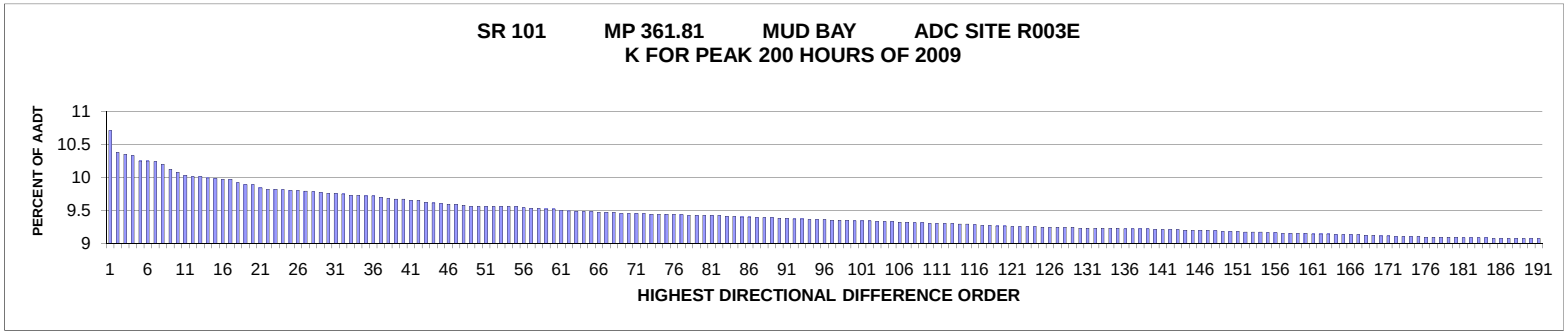

AADT= 47785 **K 30 FACTOR=** 9.76 **K 100 FACTOR=** 9.38 **K 200 FACTOR=** 9.07 **D FACTOR=** 61.15

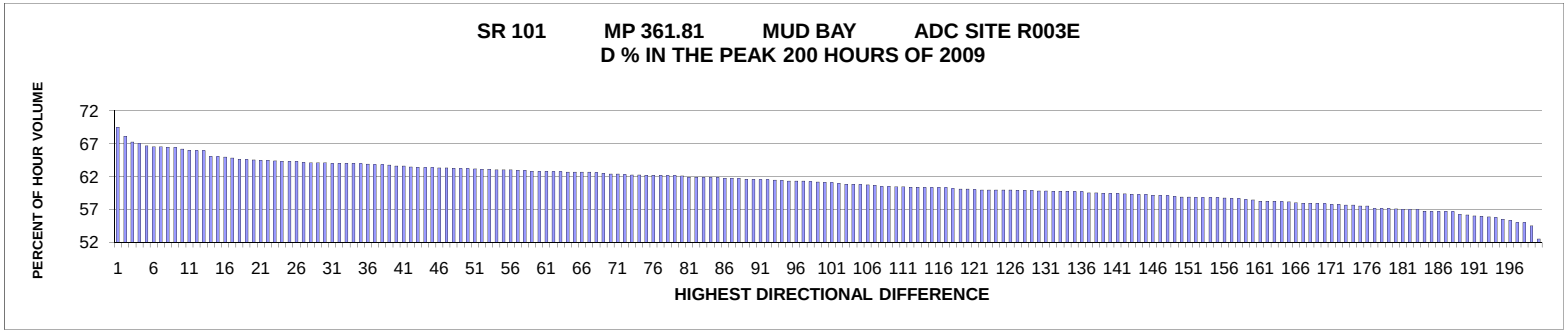

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	5	9	1	14	5118	10.71	1	47785	3400	1718	66.43	33.57
7	5	9	1	13	4958	10.38	2		3335	1623	67.27	32.73
7	5	9	1	15	4945	10.35	3		3368	1577	68.11	31.89
7	3	9	6	13	4934	10.33	4		1838	3096	37.25	62.75
8	14	9	6	17	4900	10.25	5		1907	2993	38.92	61.08
6	12	9	6	18	4897	10.25	6		2061	2836	42.09	57.91
5	22	9	6	16	4891	10.24	7		1892	2999	38.68	61.32
7	26	9	1	13	4872	10.2	8		2560	2312	52.55	47.45
5	22	9	6	17	4837	10.12	9		1712	3125	35.39	64.61
8	21	9	6	18	4815	10.08	10		1762	3053	36.59	63.41
5	15	9	6	18	4795	10.03	11		1720	3075	35.87	64.13
7	3	9	6	14	4785	10.01	12		1619	3166	33.83	66.17
7	5	9	1	16	4785	10.01	13		3206	1579	67	33
7	3	9	6	12	4772	9.99	14		1805	2967	37.82	62.18
7	31	9	6	17	4768	9.98	15		1818	2950	38.13	61.87
5	22	9	6	18	4766	9.97	16		1589	3177	33.34	66.66
7	31	9	6	18	4766	9.97	17		1725	3041	36.19	63.81

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
9	4	9	6	17	4738	9.92	18		1682	3056	35.5	64.5
8	21	9	6	17	4727	9.89	19		1827	2900	38.65	61.35
7	3	9	6	16	4725	9.89	20		1655	3070	35.03	64.97
6	5	9	6	17	4700	9.84	21	47785	1911	2789	40.66	59.34
8	7	9	6	18	4694	9.82	22		1719	2975	36.62	63.38
8	14	9	6	16	4694	9.82	23		2011	2683	42.84	57.16
10	2	9	6	17	4690	9.81	24		1910	2780	40.72	59.28
5	15	9	6	17	4684	9.8	25		1828	2856	39.03	60.97
8	14	9	6	18	4681	9.8	26		1688	2993	36.06	63.94
8	7	9	6	17	4680	9.79	27		1791	2889	38.27	61.73
9	4	9	6	18	4672	9.78	28		1588	3084	33.99	66.01
7	3	9	6	15	4667	9.77	29		1564	3103	33.51	66.49
7	24	9	6	18	4665	9.76	30		1661	3004	35.61	64.39
7	31	9	6	16	4665	9.76	31		1999	2666	42.85	57.15
9	11	9	6	17	4659	9.75	32		1862	2797	39.97	60.03
8	7	9	6	16	4650	9.73	33		1964	2686	42.24	57.76
10	9	9	6	17	4650	9.73	34		1806	2844	38.84	61.16
8	28	9	6	17	4647	9.72	35		1759	2888	37.85	62.15
7	26	9	1	14	4646	9.72	36		2532	2114	54.5	45.5
9	18	9	6	18	4635	9.7	37		1765	2870	38.08	61.92
8	2	9	1	14	4625	9.68	38		2597	2028	56.15	43.85
6	5	9	6	18	4622	9.67	39		1692	2930	36.61	63.39
7	24	9	6	17	4621	9.67	40		1723	2898	37.29	62.71
4	24	9	6	17	4611	9.65	41	47785	1778	2833	38.56	61.44
9	4	9	6	16	4610	9.65	42		1808	2802	39.22	60.78
5	25	9	2	13	4596	9.62	43		2894	1702	62.97	37.03
5	1	9	6	16	4590	9.61	44		1938	2652	42.22	57.78
8	28	9	6	18	4585	9.6	45		1647	2938	35.92	64.08
6	12	9	6	17	4583	9.59	46		1866	2717	40.72	59.28
4	24	9	6	18	4582	9.59	47		1680	2902	36.67	63.33
10	9	9	6	18	4576	9.58	48		1624	2952	35.49	64.51
8	16	9	1	13	4569	9.56	49		2570	1999	56.25	43.75
5	23	9	7	12	4568	9.56	50		1813	2755	39.69	60.31
8	20	9	5	17	4568	9.56	51		1908	2660	41.77	58.23
9	18	9	6	17	4568	9.56	52		1810	2758	39.62	60.38
5	25	9	2	14	4567	9.56	53		3012	1555	65.95	34.05
7	2	9	5	17	4567	9.56	54		1631	2936	35.71	64.29
10	2	9	6	18	4567	9.56	55		1645	2922	36.02	63.98
5	29	9	6	16	4560	9.54	56		1895	2665	41.56	58.44
7	2	9	5	18	4555	9.53	57		1524	3031	33.46	66.54
8	23	9	1	14	4553	9.53	58		2671	1882	58.66	41.34
7	6	9	2	17	4549	9.52	59		1955	2594	42.98	57.02
5	8	9	6	17	4547	9.52	60		1799	2748	39.56	60.44
8	16	9	1	14	4541	9.5	61	47785	2646	1895	58.27	41.73
6	19	9	6	17	4533	9.49	62		1781	2752	39.29	60.71
5	29	9	6	17	4530	9.48	63		1825	2705	40.29	59.71
7	26	9	1	15	4529	9.48	64		2569	1960	56.72	43.28
9	11	9	6	18	4528	9.48	65		1731	2797	38.23	61.77
5	22	9	6	15	4525	9.47	66		1820	2705	40.22	59.78
8	2	9	1	13	4523	9.47	67		2487	2036	54.99	45.01
8	6	9	5	17	4523	9.47	68		1860	2663	41.12	58.88
5	15	9	6	16	4518	9.45	69		1809	2709	40.04	59.96

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	2	9	5	16	4518	9.45	70		1666	2852	36.87	63.13
8	26	9	4	18	4518	9.45	71		1670	2848	36.96	63.04
9	25	9	6	17	4518	9.45	72		1810	2708	40.06	59.94
5	8	9	6	18	4513	9.44	73		1689	2824	37.43	62.57
8	5	9	4	17	4513	9.44	74		1897	2616	42.03	57.97
5	29	9	6	18	4512	9.44	75		1710	2802	37.9	62.1
8	5	9	4	18	4512	9.44	76		1696	2816	37.59	62.41
7	10	9	6	18	4506	9.43	77		1657	2849	36.77	63.23
9	25	9	6	18	4503	9.42	78		1688	2815	37.49	62.51
12	4	9	6	17	4502	9.42	79		1718	2784	38.16	61.84
5	1	9	6	17	4501	9.42	80		1784	2717	39.64	60.36
6	26	9	6	17	4501	9.42	81	47785	1699	2802	37.75	62.25
7	24	9	6	16	4500	9.42	82		1821	2679	40.47	59.53
7	17	9	6	18	4498	9.41	83		1733	2765	38.53	61.47
8	20	9	5	18	4498	9.41	84		1671	2827	37.15	62.85
5	1	9	6	18	4492	9.4	85		1675	2817	37.29	62.71
8	21	9	6	16	4492	9.4	86		1889	2603	42.05	57.95
7	30	9	5	18	4487	9.39	87		1743	2744	38.85	61.15
8	18	9	3	18	4487	9.39	88		1697	2790	37.82	62.18
8	13	9	5	18	4486	9.39	89		1727	2759	38.5	61.5
7	26	9	1	16	4482	9.38	90		2636	1846	58.81	41.19
7	17	9	6	16	4480	9.38	91		1794	2686	40.04	59.96
8	28	9	6	16	4479	9.37	92		1923	2556	42.93	57.07
1	16	9	6	17	4477	9.37	93		1772	2705	39.58	60.42
6	5	9	6	16	4474	9.36	94		1893	2581	42.31	57.69
8	13	9	5	17	4474	9.36	95		1783	2691	39.85	60.15
8	27	9	5	18	4471	9.36	96		1654	2817	36.99	63.01
7	8	9	4	18	4470	9.35	97		1614	2856	36.11	63.89
8	4	9	3	18	4469	9.35	98		1608	2861	35.98	64.02
8	26	9	4	17	4468	9.35	99		1811	2657	40.53	59.47
8	6	9	5	18	4464	9.34	100		1618	2846	36.25	63.75
8	10	9	2	17	4461	9.34	101	47785	1768	2693	39.63	60.37
8	23	9	1	15	4461	9.34	102		2610	1851	58.51	41.49
5	27	9	4	17	4460	9.33	103		1764	2696	39.55	60.45
7	10	9	6	17	4458	9.33	104		1762	2696	39.52	60.48
11	20	9	6	17	4457	9.33	105		1893	2564	42.47	57.53
7	6	9	2	18	4455	9.32	106		1745	2710	39.17	60.83
6	19	9	6	18	4452	9.32	107		1589	2863	35.69	64.31
8	7	9	6	15	4447	9.31	108		1955	2492	43.96	56.04
10	16	9	6	17	4447	9.31	109		1655	2792	37.22	62.78
7	3	9	6	11	4446	9.3	110		1783	2663	40.1	59.9
9	18	9	6	16	4444	9.3	111		1911	2533	43	57
5	25	9	2	15	4443	9.3	112		2956	1487	66.53	33.47
8	25	9	3	18	4443	9.3	113		1629	2814	36.66	63.34
3	20	9	6	17	4439	9.29	114		1678	2761	37.8	62.2
6	12	9	6	16	4439	9.29	115		1777	2662	40.03	59.97
7	17	9	6	17	4434	9.28	116		1644	2790	37.08	62.92
8	25	9	3	17	4432	9.27	117		1750	2682	39.49	60.51
8	12	9	4	18	4428	9.27	118		1548	2880	34.96	65.04
7	22	9	4	17	4426	9.26	119		1824	2602	41.21	58.79
8	17	9	2	17	4425	9.26	120		1847	2578	41.74	58.26
6	11	9	5	17	4422	9.25	121	47785	1796	2626	40.62	59.38

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
11	3	9	3	17	4421	9.25	122		1806	2615	40.85	59.15
8	14	9	6	15	4418	9.25	123		1915	2503	43.35	56.65
8	19	9	4	17	4418	9.25	124		1870	2548	42.33	57.67
7	15	9	4	17	4417	9.24	125		1817	2600	41.14	58.86
7	31	9	6	15	4417	9.24	126		1963	2454	44.44	55.56
2	13	9	6	17	4415	9.24	127		1698	2717	38.46	61.54
8	11	9	3	17	4414	9.24	128		1787	2627	40.48	59.52
8	27	9	5	17	4414	9.24	129		1842	2572	41.73	58.27
7	23	9	5	18	4412	9.23	130		1626	2786	36.85	63.15
8	16	9	1	16	4411	9.23	131		2537	1874	57.52	42.48
7	5	9	1	12	4409	9.23	132		3064	1345	69.49	30.51
7	14	9	3	18	4409	9.23	133		1572	2837	35.65	64.35
8	2	9	1	15	4409	9.23	134		2519	1890	57.13	42.87
8	31	9	2	18	4409	9.23	135		1679	2730	38.08	61.92
7	22	9	4	18	4407	9.22	136		1641	2766	37.24	62.76
8	24	9	2	17	4406	9.22	137		1849	2557	41.97	58.03
6	16	9	3	17	4405	9.22	138		1788	2617	40.59	59.41
8	31	9	2	17	4404	9.22	139		1786	2618	40.55	59.45
3	13	9	6	17	4401	9.21	140		1755	2646	39.88	60.12
8	1	9	7	13	4401	9.21	141	47785	1964	2437	44.63	55.37
9	24	9	5	18	4401	9.21	142		1654	2747	37.58	62.42
4	17	9	6	17	4400	9.21	143		1690	2710	38.41	61.59
8	18	9	3	17	4398	9.2	144		1768	2630	40.2	59.8
5	23	9	7	13	4397	9.2	145		1657	2740	37.68	62.32
5	21	9	5	18	4394	9.2	146		1613	2781	36.71	63.29
8	1	9	7	12	4394	9.2	147		1943	2451	44.22	55.78
6	16	9	3	18	4392	9.19	148		1534	2858	34.93	65.07
3	27	9	6	17	4389	9.18	149		1634	2755	37.23	62.77
6	24	9	4	17	4386	9.18	150		1762	2624	40.17	59.83
9	3	9	5	17	4386	9.18	151		1721	2665	39.24	60.76
9	8	9	3	17	4383	9.17	152		1671	2712	38.12	61.88
1	30	9	6	17	4382	9.17	153		1789	2593	40.83	59.17
5	27	9	4	18	4382	9.17	154		1600	2782	36.51	63.49
9	25	9	6	16	4377	9.16	155		1877	2500	42.88	57.12
10	8	9	5	18	4376	9.16	156		1593	2783	36.4	63.6
7	15	9	4	18	4373	9.15	157		1609	2764	36.79	63.21
7	30	9	5	17	4372	9.15	158		1711	2661	39.14	60.86
8	16	9	1	15	4372	9.15	159		2443	1929	55.88	44.12
7	24	9	6	15	4371	9.15	160		1924	2447	44.02	55.98
6	26	9	6	16	4369	9.14	161	47785	1891	2478	43.28	56.72
3	27	9	6	18	4367	9.14	162		1568	2799	35.91	64.09
6	26	9	6	18	4366	9.14	163		1571	2795	35.98	64.02
5	21	9	5	17	4365	9.13	164		1741	2624	39.89	60.11
8	12	9	4	17	4365	9.13	165		1786	2579	40.92	59.08
8	11	9	3	18	4363	9.13	166		1578	2785	36.17	63.83
2	13	9	6	18	4361	9.13	167		1534	2827	35.18	64.82
8	9	9	1	15	4360	9.12	168		2524	1836	57.89	42.11
10	9	9	6	16	4358	9.12	169		1799	2559	41.28	58.72
9	17	9	5	17	4354	9.11	170		1672	2682	38.4	61.6
9	22	9	3	17	4351	9.11	171		1795	2556	41.25	58.75
7	23	9	5	17	4350	9.1	172		1647	2703	37.86	62.14
9	17	9	5	18	4349	9.1	173		1562	2787	35.92	64.08

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
10	20	9	3	17	4349	9.1	174		1783	2566	41	59
3	13	9	6	18	4347	9.1	175		1640	2707	37.73	62.27
5	28	9	5	18	4346	9.09	176		1684	2662	38.75	61.25
5	8	9	6	16	4345	9.09	177		1818	2527	41.84	58.16
7	3	9	6	17	4345	9.09	178		1479	2866	34.04	65.96
6	17	9	4	17	4344	9.09	179		1722	2622	39.64	60.36
7	7	9	3	18	4342	9.09	180		1581	2761	36.41	63.59
6	2	9	3	18	4341	9.08	181	47785	1540	2801	35.48	64.52
8	9	9	1	14	4341	9.08	182		2464	1877	56.76	43.24
6	3	9	4	17	4340	9.08	183		1740	2600	40.09	59.91
6	10	9	4	17	4337	9.08	184		1787	2550	41.2	58.8
5	23	9	7	14	4336	9.07	185		1617	2719	37.29	62.71
10	6	9	3	18	4336	9.07	186		1535	2801	35.4	64.6
5	20	9	4	17	4335	9.07	187		1735	2600	40.02	59.98
6	22	9	2	17	4335	9.07	188		1676	2659	38.66	61.34
7	20	9	2	18	4334	9.07	189		1618	2716	37.33	62.67
9	3	9	5	18	4334	9.07	190		1560	2774	35.99	64.01
6	1	9	2	17	4333	9.07	191		1743	2590	40.23	59.77
11	13	9	6	17	4332	9.07	192		1741	2591	40.19	59.81
7	21	9	3	18	4331	9.06	193		1588	2743	36.67	63.33

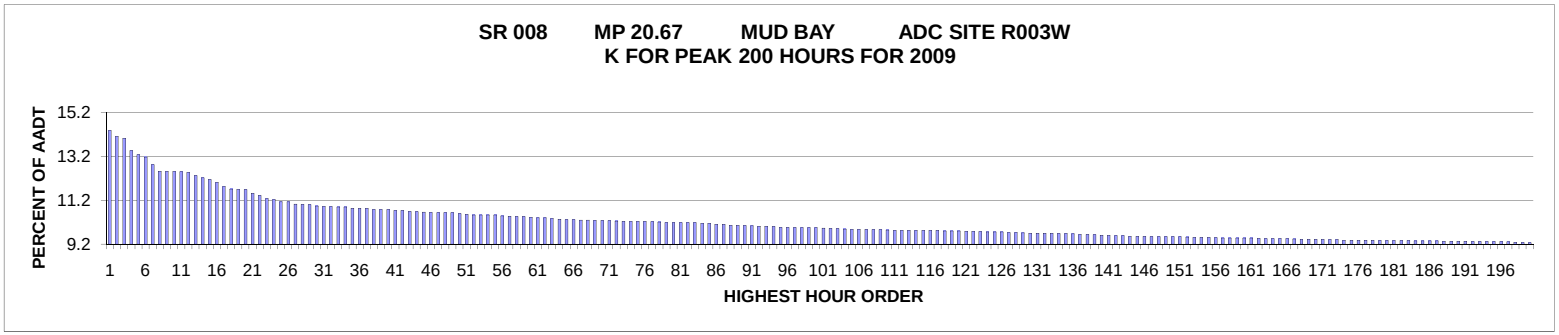

AADT= 17145 **K 30 FACTOR=** 10.93 **K 100 FACTOR=** 9.94 **K 200 FACTOR=** 9.26 **D FACTOR=** 63.31

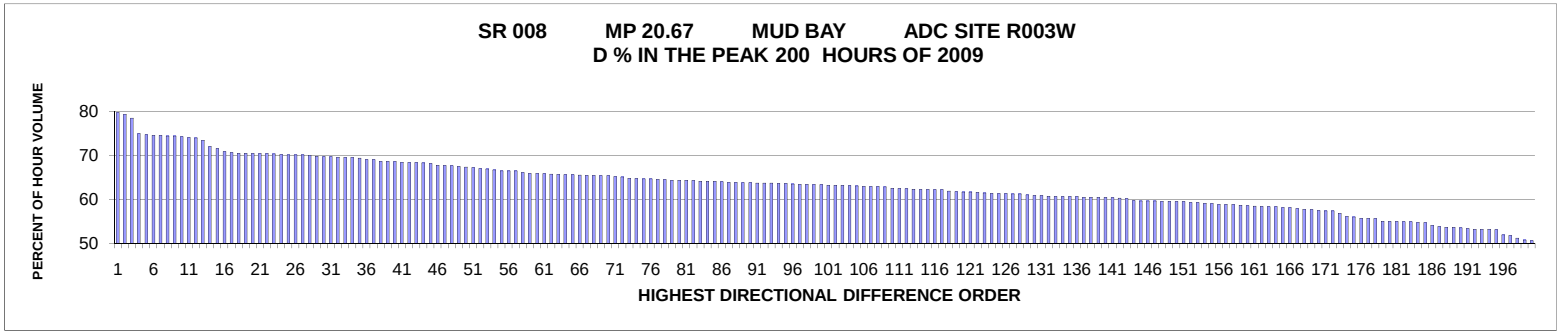

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	5	9	1	14	2464	14.37	1	17145	1847	617	74.96	25.04
7	5	9	1	13	2420	14.11	2		1798	622	74.3	25.7
7	5	9	1	15	2406	14.03	3		1797	609	74.69	25.31
7	5	9	1	16	2308	13.46	4		1721	587	74.57	25.43
7	3	9	6	13	2273	13.26	5		712	1561	31.32	68.68
7	26	9	1	13	2258	13.17	6		1234	1024	54.65	45.35
7	3	9	6	14	2197	12.81	7		649	1548	29.54	70.46
7	3	9	6	12	2148	12.53	8		636	1512	29.61	70.39
7	26	9	1	15	2148	12.53	9		1320	828	61.45	38.55
7	5	9	1	12	2144	12.51	10		1595	549	74.39	25.61
7	3	9	6	15	2142	12.49	11		624	1518	29.13	70.87
5	25	9	2	14	2136	12.46	12		1590	546	74.44	25.56
7	26	9	1	14	2113	12.32	13		1247	866	59.02	40.98
7	3	9	6	11	2093	12.21	14		634	1459	30.29	69.71
5	25	9	2	13	2082	12.14	15		1429	653	68.64	31.36
7	3	9	6	16	2059	12.01	16		622	1437	30.21	69.79
7	5	9	1	17	2029	11.83	17		1611	418	79.4	20.6

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
5	25	9	2	15	2008	11.71	18		1497	511	74.55	25.45
7	5	9	1	18	2004	11.69	19		1573	431	78.49	21.51
7	3	9	6	17	2001	11.67	20		646	1355	32.28	67.72
7	26	9	1	12	1975	11.52	21	17145	1011	964	51.19	48.81
7	26	9	1	16	1957	11.41	22		1311	646	66.99	33.01
7	19	9	1	14	1932	11.27	23		1248	684	64.6	35.4
5	23	9	7	12	1923	11.22	24		656	1267	34.11	65.89
7	31	9	6	17	1909	11.13	25		737	1172	38.61	61.39
7	19	9	1	13	1906	11.12	26		1209	697	63.43	36.57
5	22	9	6	18	1889	11.02	27		560	1329	29.65	70.35
5	23	9	7	13	1887	11.01	28		613	1274	32.49	67.51
7	25	9	7	12	1885	10.99	29		690	1195	36.6	63.4
5	23	9	7	11	1874	10.93	30		571	1303	30.47	69.53
7	31	9	6	16	1872	10.92	31		780	1092	41.67	58.33
5	22	9	6	17	1869	10.9	32		638	1231	34.14	65.86
9	4	9	6	16	1867	10.89	33		687	1180	36.8	63.2
9	7	9	2	13	1867	10.89	34		1344	523	71.99	28.01
5	25	9	2	16	1857	10.83	35		1374	483	73.99	26.01
5	25	9	2	12	1856	10.83	36		1302	554	70.15	29.85
7	5	9	1	19	1856	10.83	37		1480	376	79.74	20.26
7	24	9	6	16	1848	10.78	38		728	1120	39.39	60.61
7	12	9	1	14	1846	10.77	39		1322	524	71.61	28.39
7	25	9	7	13	1846	10.77	40		708	1138	38.35	61.65
7	12	9	1	13	1839	10.73	41	17145	1247	592	67.81	32.19
7	31	9	6	18	1839	10.73	42		666	1173	36.22	63.78
5	22	9	6	16	1831	10.68	43		653	1178	35.66	64.34
9	4	9	6	17	1829	10.67	44		628	1201	34.34	65.66
2	7	9	7	14	1827	10.66	45		632	1195	34.59	65.41
7	31	9	6	15	1824	10.64	46		808	1016	44.3	55.7
3	29	9	1	14	1823	10.63	47		1192	631	65.39	34.61
4	26	9	1	13	1823	10.63	48		1269	554	69.61	30.39
3	29	9	1	15	1822	10.63	49		1250	572	68.61	31.39
7	24	9	6	15	1814	10.58	50		768	1046	42.34	57.66
7	26	9	1	17	1808	10.55	51		1238	570	68.47	31.53
7	19	9	1	15	1806	10.53	52		1151	655	63.73	36.27
7	24	9	6	14	1805	10.53	53		814	991	45.1	54.9
5	23	9	7	14	1803	10.52	54		532	1271	29.51	70.49
7	17	9	6	16	1803	10.52	55		699	1104	38.77	61.23
7	24	9	6	13	1797	10.48	56		753	1044	41.9	58.1
7	26	9	1	18	1795	10.47	57		1257	538	70.03	29.97
9	7	9	2	14	1792	10.45	58		1258	534	70.2	29.8
4	26	9	1	15	1791	10.45	59		1261	530	70.41	29.59
3	29	9	1	13	1786	10.42	60		1137	649	63.66	36.34
3	29	9	1	16	1783	10.4	61	17145	1231	552	69.04	30.96
7	31	9	6	14	1782	10.39	62		826	956	46.35	53.65
6	28	9	1	15	1776	10.36	63		1163	613	65.48	34.52
9	11	9	6	17	1771	10.33	64		738	1033	41.67	58.33
7	2	9	5	16	1767	10.31	65		636	1131	35.99	64.01
6	5	9	6	17	1766	10.3	66		733	1033	41.51	58.49
7	17	9	6	15	1765	10.29	67		730	1035	41.36	58.64
7	26	9	1	19	1765	10.29	68		1297	468	73.48	26.52
2	7	9	7	13	1762	10.28	69		591	1171	33.54	66.46

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	17	9	6	18	1762	10.28	70		645	1117	36.61	63.39
7	2	9	5	14	1759	10.26	71		665	1094	37.81	62.19
12	31	9	5	15	1758	10.25	72		630	1128	35.84	64.16
6	5	9	6	18	1756	10.24	73		637	1119	36.28	63.72
6	21	9	1	13	1756	10.24	74		1045	711	59.51	40.49
7	19	9	1	12	1756	10.24	75		1041	715	59.28	40.72
7	31	9	6	13	1754	10.23	76		805	949	45.9	54.1
6	28	9	1	14	1753	10.22	77		1046	707	59.67	40.33
5	25	9	2	17	1750	10.21	78		1296	454	74.06	25.94
7	4	9	7	12	1746	10.18	79		532	1214	30.47	69.53
9	12	9	7	12	1746	10.18	80		693	1053	39.69	60.31
7	2	9	5	18	1745	10.18	81	17145	578	1167	33.12	66.88
7	4	9	7	13	1745	10.18	82		552	1193	31.63	68.37
7	25	9	7	11	1745	10.18	83		585	1160	33.52	66.48
7	2	9	5	17	1739	10.14	84		640	1099	36.8	63.2
7	25	9	7	17	1738	10.14	85		899	839	51.73	48.27
4	24	9	6	17	1731	10.1	86		618	1113	35.7	64.3
7	17	9	6	14	1731	10.1	87		719	1012	41.54	58.46
5	22	9	6	15	1725	10.06	88		636	1089	36.87	63.13
7	2	9	5	15	1724	10.06	89		638	1086	37.01	62.99
7	19	9	1	16	1723	10.05	90		1100	623	63.84	36.16
5	24	9	1	14	1720	10.03	91		850	870	49.42	50.58
7	12	9	1	15	1718	10.02	92		1204	514	70.08	29.92
4	26	9	1	14	1717	10.01	93		1210	507	70.47	29.53
7	31	9	6	19	1714	10	94		677	1037	39.5	60.5
5	10	9	1	14	1707	9.96	95		1067	640	62.51	37.49
6	28	9	1	13	1706	9.95	96		1062	644	62.25	37.75
7	2	9	5	13	1706	9.95	97		626	1080	36.69	63.31
7	24	9	6	17	1705	9.94	98		643	1062	37.71	62.29
7	30	9	5	17	1705	9.94	99		727	978	42.64	57.36
7	30	9	5	18	1704	9.94	100		771	933	45.25	54.75
7	24	9	6	18	1702	9.93	101	17145	599	1103	35.19	64.81
9	4	9	6	18	1699	9.91	102		520	1179	30.61	69.39
12	31	9	5	16	1697	9.9	103		575	1122	33.88	66.12
12	31	9	5	14	1694	9.88	104		650	1044	38.37	61.63
7	30	9	5	15	1693	9.87	105		751	942	44.36	55.64
4	24	9	6	18	1692	9.87	106		535	1157	31.62	68.38
7	19	9	1	17	1692	9.87	107		1128	564	66.67	33.33
5	24	9	1	13	1691	9.86	108		786	905	46.48	53.52
5	22	9	6	14	1690	9.86	109		639	1051	37.81	62.19
4	24	9	6	16	1687	9.84	110		633	1054	37.52	62.48
4	26	9	1	16	1686	9.83	111		1191	495	70.64	29.36
6	21	9	1	14	1685	9.83	112		1022	663	60.65	39.35
9	11	9	6	18	1685	9.83	113		667	1018	39.58	60.42
7	18	9	7	12	1684	9.82	114		689	995	40.91	59.09
7	25	9	7	14	1684	9.82	115		683	1001	40.56	59.44
2	13	9	6	18	1683	9.82	116		534	1149	31.73	68.27
10	9	9	6	17	1683	9.82	117		647	1036	38.44	61.56
7	6	9	2	17	1680	9.8	118		786	894	46.79	53.21
6	28	9	1	16	1678	9.79	119		1080	598	64.36	35.64
9	4	9	6	15	1678	9.79	120		660	1018	39.33	60.67
5	22	9	6	19	1676	9.78	121	17145	501	1175	29.89	70.11

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	6	9	2	14	1676	9.78	122		1081	595	64.5	35.5
5	15	9	6	18	1674	9.76	123		611	1063	36.5	63.5
9	13	9	1	14	1672	9.75	124		1096	576	65.55	34.45
5	23	9	7	15	1671	9.75	125		548	1123	32.79	67.21
6	26	9	6	16	1671	9.75	126		711	960	42.55	57.45
7	6	9	2	15	1669	9.73	127		981	688	58.78	41.22
9	13	9	1	13	1669	9.73	128		1087	582	65.13	34.87
4	26	9	1	12	1664	9.71	129		1067	597	64.12	35.88
7	11	9	7	12	1663	9.7	130		649	1014	39.03	60.97
5	24	9	1	12	1662	9.69	131		660	1002	39.71	60.29
6	26	9	6	17	1661	9.69	132		600	1061	36.12	63.88
7	18	9	7	14	1661	9.69	133		747	914	44.97	55.03
7	17	9	6	17	1659	9.68	134		592	1067	35.68	64.32
9	13	9	1	15	1659	9.68	135		1117	542	67.33	32.67
5	24	9	1	18	1657	9.66	136		1072	585	64.7	35.3
6	12	9	6	18	1653	9.64	137		614	1039	37.14	62.86
9	7	9	2	15	1653	9.64	138		1127	526	68.18	31.82
7	10	9	6	17	1650	9.62	139		607	1043	36.79	63.21
9	5	9	7	13	1648	9.61	140		743	905	45.08	54.92
2	13	9	6	17	1646	9.6	141	17145	608	1038	36.94	63.06
6	12	9	6	17	1641	9.57	142		610	1031	37.17	62.83
9	18	9	6	18	1640	9.57	143		597	1043	36.4	63.6
10	2	9	6	17	1638	9.55	144		661	977	40.35	59.65
7	11	9	7	14	1637	9.55	145		769	868	46.98	53.02
7	30	9	5	14	1637	9.55	146		764	873	46.67	53.33
7	18	9	7	13	1636	9.54	147		698	938	42.67	57.33
9	4	9	6	14	1636	9.54	148		641	995	39.18	60.82
5	10	9	1	13	1635	9.54	149		972	663	59.45	40.55
4	26	9	1	17	1634	9.53	150		1074	560	65.73	34.27
5	23	9	7	16	1634	9.53	151		634	1000	38.8	61.2
6	19	9	6	18	1633	9.52	152		562	1071	34.42	65.58
7	4	9	7	14	1629	9.5	153		560	1069	34.38	65.62
4	24	9	6	19	1628	9.5	154		494	1134	30.34	69.66
6	5	9	6	16	1628	9.5	155		678	950	41.65	58.35
6	19	9	6	17	1627	9.49	156		643	984	39.52	60.48
7	6	9	2	13	1625	9.48	157		1042	583	64.12	35.88
7	10	9	6	18	1625	9.48	158		603	1022	37.11	62.89
7	31	9	6	12	1625	9.48	159		754	871	46.4	53.6
12	4	9	6	17	1624	9.47	160		611	1013	37.62	62.38
9	18	9	6	17	1623	9.47	161	17145	656	967	40.42	59.58
9	5	9	7	12	1622	9.46	162		731	891	45.07	54.93
6	21	9	1	15	1621	9.45	163		987	634	60.89	39.11
9	7	9	2	16	1620	9.45	164		1055	565	65.12	34.88
7	25	9	7	16	1619	9.44	165		748	871	46.2	53.8
7	26	9	1	11	1618	9.44	166		779	839	48.15	51.85
7	17	9	6	13	1617	9.43	167		709	908	43.85	56.15
6	28	9	1	18	1615	9.42	168		1092	523	67.62	32.38
7	25	9	7	18	1615	9.42	169		859	756	53.19	46.81
10	16	9	6	17	1614	9.41	170		570	1044	35.32	64.68
7	10	9	6	16	1613	9.41	171		696	917	43.15	56.85
3	27	9	6	16	1612	9.4	172		570	1042	35.36	64.64
6	12	9	6	16	1612	9.4	173		643	969	39.89	60.11

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
6	14	9	1	14	1608	9.38	174		1024	584	63.68	36.32
5	9	9	7	12	1607	9.37	175		815	792	50.72	49.28
7	25	9	7	19	1607	9.37	176		985	622	61.29	38.71
7	11	9	7	11	1606	9.37	177		606	1000	37.73	62.27
9	25	9	6	17	1606	9.37	178		650	956	40.47	59.53
9	18	9	6	16	1605	9.36	179		673	932	41.93	58.07
11	20	9	6	17	1605	9.36	180		661	944	41.18	58.82
5	22	9	6	13	1604	9.36	181	17145	611	993	38.09	61.91
9	12	9	7	11	1604	9.36	182		632	972	39.4	60.6
9	20	9	1	13	1604	9.36	183		990	614	61.72	38.28
3	27	9	6	17	1603	9.35	184		581	1022	36.24	63.76
7	2	9	5	19	1603	9.35	185		548	1055	34.19	65.81
6	19	9	6	15	1602	9.34	186		710	892	44.32	55.68
7	3	9	6	10	1601	9.34	187		496	1105	30.98	69.02
7	25	9	7	15	1600	9.33	188		674	926	42.13	57.88
5	24	9	1	15	1599	9.33	189		851	748	53.22	46.78
7	17	9	6	19	1599	9.33	190		632	967	39.52	60.48
7	24	9	6	19	1599	9.33	191		536	1063	33.52	66.48
6	19	9	6	16	1598	9.32	192		628	970	39.3	60.7
9	11	9	6	15	1598	9.32	193		676	922	42.3	57.7
10	9	9	6	18	1598	9.32	194		552	1046	34.54	65.46
6	26	9	6	15	1597	9.31	195		658	939	41.2	58.8
9	5	9	7	14	1596	9.31	196		703	893	44.05	55.95
11	14	9	7	13	1594	9.3	197		617	977	38.71	61.29
5	29	9	6	16	1591	9.28	198		648	943	40.73	59.27
9	12	9	7	13	1590	9.27	199		718	872	45.16	54.84
1	16	9	6	17	1588	9.26	200		641	947	40.37	59.63

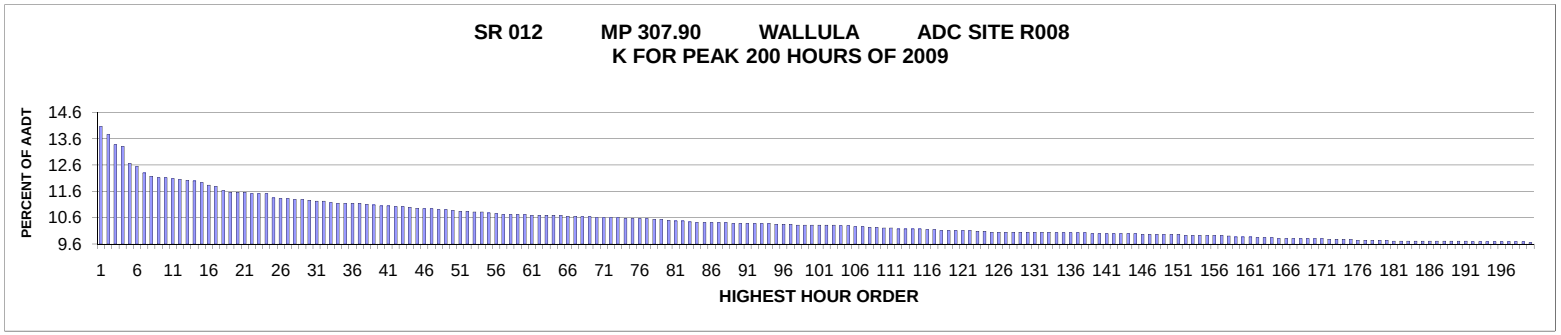

AADT= 3294 **K 30 FACTOR=** 11.26 **K 100 FACTOR=** 10.32 **K 200 FACTOR=** 9.65 **D FACTOR=** 53.95

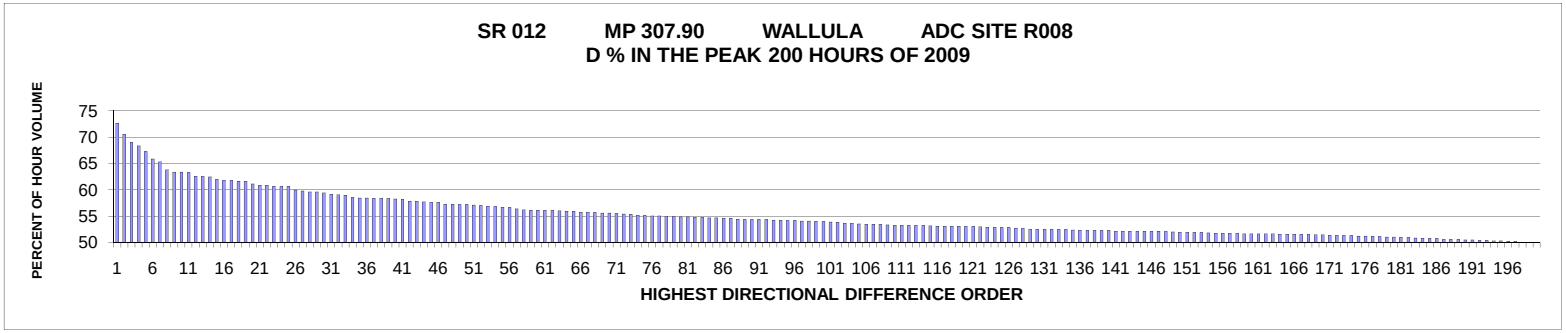

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
9	4	9	6	17	463	14.06	1	3294	350	813	56.95	43.05
9	4	9	6	16	453	13.75	2		334	787	57.56	42.44
9	4	9	6	18	440	13.36	3		298	738	59.62	40.38
5	22	9	6	17	438	13.3	4		402	840	52.14	47.86
9	4	9	6	19	417	12.66	5		241	658	63.37	36.63
10	23	9	6	18	413	12.54	6		285	698	59.17	40.83
8	7	9	6	17	405	12.3	7		334	739	54.8	45.2
5	8	9	6	17	401	12.17	8		313	714	56.16	43.84
9	18	9	6	17	399	12.11	9		367	766	52.09	47.91
9	25	9	6	17	399	12.11	10		369	768	51.95	48.05
10	2	9	6	16	398	12.08	11		397	795	50.06	49.94
5	22	9	6	16	397	12.05	12		354	751	52.86	47.14
8	21	9	6	17	396	12.02	13		338	734	53.95	46.05
6	12	9	6	17	395	11.99	14		366	761	51.91	48.09
6	12	9	6	16	393	11.93	15		366	759	51.78	48.22
5	1	9	6	16	390	11.84	16		317	707	55.16	44.84
10	23	9	6	17	388	11.78	17		317	705	55.04	44.96

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
9	18	9	6	16	383	11.63	18		360	743	51.55	48.45
6	12	9	6	18	381	11.57	19		273	654	58.26	41.74
7	24	9	6	16	381	11.57	20		363	744	51.21	48.79
9	11	9	6	17	381	11.57	21	3294	341	722	52.77	47.23
6	12	9	6	15	379	11.51	22		333	712	53.23	46.77
6	19	9	6	17	379	11.51	23		328	707	53.61	46.39
8	16	9	1	17	379	11.51	24		253	632	59.97	40.03
9	11	9	6	18	374	11.35	25		315	689	54.28	45.72
6	19	9	6	16	373	11.32	26		341	714	52.24	47.76
10	16	9	6	18	373	11.32	27		316	689	54.14	45.86
3	29	9	1	17	372	11.29	28		193	565	65.84	34.16
10	9	9	6	17	372	11.29	29		384	756	49.21	50.79
5	8	9	6	16	371	11.26	30		287	658	56.38	43.62
5	8	9	6	18	370	11.23	31		271	641	57.72	42.28
10	23	9	6	15	370	11.23	32		313	683	54.17	45.83
6	5	9	6	16	368	11.17	33		311	679	54.2	45.8
4	17	9	6	17	367	11.14	34		329	696	52.73	47.27
6	5	9	6	17	367	11.14	35		325	692	53.03	46.97
6	19	9	6	18	367	11.14	36		274	641	57.25	42.75
8	7	9	6	18	367	11.14	37		268	635	57.8	42.2
7	24	9	6	18	366	11.11	38		267	633	57.82	42.18
7	24	9	6	15	365	11.08	39		300	665	54.89	45.11
2	16	9	2	17	364	11.05	40		247	611	59.57	40.43
7	23	9	5	17	364	11.05	41	3294	399	763	47.71	52.29
5	22	9	6	18	363	11.02	42		284	647	56.11	43.89
10	23	9	6	16	363	11.02	43		364	727	49.93	50.07
4	24	9	6	17	362	10.99	44		333	695	52.09	47.91
7	24	9	6	17	361	10.96	45		321	682	52.93	47.07
8	14	9	6	16	360	10.93	46		368	728	49.45	50.55
9	25	9	6	16	360	10.93	47		337	697	51.65	48.35
6	26	9	6	17	359	10.9	48		333	692	51.88	48.12
10	16	9	6	17	359	10.9	49		315	674	53.26	46.74
8	14	9	6	18	358	10.87	50		301	659	54.32	45.68
5	1	9	6	17	357	10.84	51		323	680	52.5	47.5
9	20	9	1	18	357	10.84	52		263	620	57.58	42.42
8	23	9	1	19	356	10.81	53		165	521	68.33	31.67
10	2	9	6	18	356	10.81	54		327	683	52.12	47.88
4	24	9	6	15	355	10.78	55		329	684	51.9	48.1
10	15	9	5	17	354	10.75	56		297	651	54.38	45.62
3	29	9	1	18	353	10.72	57		172	525	67.24	32.76
7	10	9	6	17	353	10.72	58		292	645	54.73	45.27
8	23	9	1	17	353	10.72	59		265	618	57.12	42.88
9	3	9	5	16	353	10.72	60		285	638	55.33	44.67
7	9	9	5	17	352	10.69	61	3294	287	639	55.09	44.91
7	17	9	6	17	352	10.69	62		320	672	52.38	47.62
8	26	9	4	17	352	10.69	63		276	628	56.05	43.95
10	2	9	6	17	352	10.69	64		371	723	48.69	51.31
10	9	9	6	15	352	10.69	65		328	680	51.76	48.24
7	10	9	6	18	351	10.66	66		295	646	54.33	45.67
9	17	9	5	17	351	10.66	67		323	674	52.08	47.92
4	24	9	6	16	350	10.63	68		336	686	51.02	48.98
7	17	9	6	18	350	10.63	69		281	631	55.47	44.53

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
4	23	9	5	17	349	10.6	70		342	691	50.51	49.49
4	24	9	6	18	349	10.6	71		308	657	53.12	46.88
8	14	9	6	17	349	10.6	72		331	680	51.32	48.68
10	17	9	7	17	349	10.6	73		209	558	62.54	37.46
5	8	9	6	15	348	10.56	74		309	657	52.97	47.03
6	26	9	6	16	348	10.56	75		306	654	53.21	46.79
7	17	9	6	15	348	10.56	76		326	674	51.63	48.37
8	11	9	3	17	348	10.56	77		278	626	55.59	44.41
3	29	9	1	16	347	10.53	78		221	568	61.09	38.91
8	23	9	1	16	347	10.53	79		315	662	52.42	47.58
10	4	9	1	19	346	10.5	80		184	530	65.28	34.72
8	13	9	5	17	345	10.47	81	3294	289	634	54.42	45.58
8	20	9	5	17	345	10.47	82		304	649	53.16	46.84
10	11	9	1	18	344	10.44	83		263	607	56.67	43.33
4	5	9	1	17	343	10.41	84		321	664	51.66	48.34
7	3	9	6	16	343	10.41	85		238	581	59.04	40.96
8	21	9	6	18	343	10.41	86		300	643	53.34	46.66
8	27	9	5	17	343	10.41	87		299	642	53.43	46.57
9	24	9	5	17	343	10.41	88		276	619	55.41	44.59
5	22	9	6	15	342	10.38	89		382	724	47.24	52.76
6	26	9	6	18	342	10.38	90		302	644	53.11	46.89
8	9	9	1	16	342	10.38	91		320	662	51.66	48.34
8	23	9	1	18	342	10.38	92		210	552	61.96	38.04
9	13	9	1	16	342	10.38	93		256	598	57.19	42.81
9	18	9	6	18	342	10.38	94		312	654	52.29	47.71
7	31	9	6	17	341	10.35	95		357	698	48.85	51.15
8	15	9	7	16	341	10.35	96		272	613	55.63	44.37
9	18	9	6	15	341	10.35	97		346	687	49.64	50.36
8	7	9	6	15	340	10.32	98		339	679	50.07	49.93
8	13	9	5	18	340	10.32	99		280	620	54.84	45.16
8	21	9	6	16	340	10.32	100		336	676	50.3	49.7
9	25	9	6	15	340	10.32	101	3294	270	610	55.74	44.26
10	9	9	6	16	340	10.32	102		365	705	48.23	51.77
10	23	9	6	19	340	10.32	103		193	533	63.79	36.21
8	9	9	1	17	339	10.29	104		240	579	58.55	41.45
10	25	9	1	18	339	10.29	105		220	559	60.64	39.36
6	5	9	6	18	338	10.26	106		276	614	55.05	44.95
8	17	9	2	17	338	10.26	107		287	625	54.08	45.92
8	9	9	1	18	337	10.23	108		242	579	58.2	41.8
9	20	9	1	17	337	10.23	109		325	662	50.91	49.09
6	19	9	6	15	336	10.2	110		297	633	53.08	46.92
10	25	9	1	16	336	10.2	111		326	662	50.76	49.24
7	16	9	5	17	335	10.17	112		324	659	50.83	49.17
7	23	9	5	18	335	10.17	113		257	592	56.59	43.41
8	28	9	6	17	335	10.17	114		358	693	48.34	51.66
8	30	9	1	19	335	10.17	115		140	475	70.53	29.47
4	3	9	6	16	334	10.14	116		349	683	48.9	51.1
7	10	9	6	16	334	10.14	117		303	637	52.43	47.57
6	19	9	6	19	333	10.11	118		214	547	60.88	39.12
7	19	9	1	18	333	10.11	119		224	557	59.78	40.22
8	9	9	1	15	333	10.11	120		314	647	51.47	48.53
8	16	9	1	16	333	10.11	121	3294	289	622	53.54	46.46

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
10	16	9	6	16	333	10.11	122		362	695	47.91	52.09
2	14	9	7	17	332	10.08	123		260	592	56.08	43.92
8	7	9	6	16	332	10.08	124		326	658	50.46	49.54
4	10	9	6	16	331	10.05	125		291	622	53.22	46.78
5	1	9	6	18	331	10.05	126		282	613	54	46
8	2	9	1	18	331	10.05	127		205	536	61.75	38.25
8	22	9	7	17	331	10.05	128		215	546	60.62	39.38
9	11	9	6	16	331	10.05	129		304	635	52.13	47.87
9	25	9	6	18	331	10.05	130		347	678	48.82	51.18
9	27	9	1	17	331	10.05	131		252	583	56.78	43.22
10	4	9	1	17	331	10.05	132		248	579	57.17	42.83
10	22	9	5	17	331	10.05	133		300	631	52.46	47.54
5	3	9	1	18	330	10.02	134		262	592	55.74	44.26
8	4	9	3	17	330	10.02	135		260	590	55.93	44.07
8	16	9	1	19	330	10.02	136		192	522	63.22	36.78
9	4	9	6	15	330	10.02	137		337	667	49.48	50.52
9	25	9	6	19	330	10.02	138		235	565	58.41	41.59
1	19	9	2	17	329	9.99	139		229	558	58.96	41.04
3	8	9	1	16	329	9.99	140		235	564	58.33	41.67
7	20	9	2	17	329	9.99	141	3294	287	616	53.41	46.59
8	16	9	1	18	329	9.99	142		205	534	61.61	38.39
8	21	9	6	15	329	9.99	143		327	656	50.15	49.85
9	24	9	5	16	329	9.99	144		304	633	51.97	48.03
10	8	9	5	18	329	9.99	145		271	600	54.83	45.17
4	19	9	1	17	328	9.96	146		279	607	54.04	45.96
5	8	9	6	19	328	9.96	147		203	531	61.77	38.23
5	29	9	6	18	328	9.96	148		297	625	52.48	47.52
7	18	9	7	16	328	9.96	149		288	616	53.25	46.75
7	31	9	6	16	328	9.96	150		309	637	51.49	48.51
10	18	9	1	18	328	9.96	151		224	552	59.42	40.58
3	20	9	6	17	327	9.93	152		308	635	51.5	48.5
5	1	9	6	15	327	9.93	153		341	668	48.95	51.05
6	22	9	2	17	327	9.93	154		290	617	53	47
7	22	9	4	17	327	9.93	155		296	623	52.49	47.51
9	1	9	3	17	327	9.93	156		248	575	56.87	43.13
9	27	9	1	18	327	9.93	157		233	560	58.39	41.61
10	18	9	1	17	326	9.9	158		255	581	56.11	43.89
7	12	9	1	16	325	9.87	159		279	604	53.81	46.19
8	18	9	3	17	325	9.87	160		267	592	54.9	45.1
10	11	9	1	16	325	9.87	161	3294	309	634	51.26	48.74
2	13	9	6	17	324	9.84	162		347	671	48.29	51.71
4	5	9	1	16	324	9.84	163		296	620	52.26	47.74
8	6	9	5	17	324	9.84	164		304	628	51.59	48.41
5	17	9	1	17	323	9.81	165		194	517	62.48	37.52
7	2	9	5	17	323	9.81	166		291	614	52.61	47.39
7	19	9	1	16	323	9.81	167		328	651	49.62	50.38
7	19	9	1	17	323	9.81	168		268	591	54.65	45.35
7	31	9	6	15	323	9.81	169		347	670	48.21	51.79
8	30	9	1	17	323	9.81	170		254	577	55.98	44.02
9	10	9	5	17	323	9.81	171		279	602	53.65	46.35
7	5	9	1	18	322	9.78	172		201	523	61.57	38.43
7	17	9	6	16	322	9.78	173		319	641	50.23	49.77

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
9	13	9	1	18	322	9.78	174		209	531	60.64	39.36
10	12	9	2	17	322	9.78	175		257	579	55.61	44.39
5	3	9	1	19	321	9.74	176		144	465	69.03	30.97
5	15	9	6	18	321	9.74	177		325	646	49.69	50.31
7	16	9	5	16	321	9.74	178		305	626	51.28	48.72
9	11	9	6	15	321	9.74	179		327	648	49.54	50.46
10	15	9	5	16	321	9.74	180		272	593	54.13	45.87
4	5	9	1	18	320	9.71	181	3294	239	559	57.25	42.75
4	23	9	5	18	320	9.71	182		283	603	53.07	46.93
4	26	9	1	18	320	9.71	183		206	526	60.84	39.16
6	18	9	5	18	320	9.71	184		265	585	54.7	45.3
7	26	9	1	18	320	9.71	185		185	505	63.37	36.63
8	7	9	6	19	320	9.71	186		228	548	58.39	41.61
8	24	9	2	17	320	9.71	187		252	572	55.94	44.06
8	28	9	6	18	320	9.71	188		311	631	50.71	49.29
9	9	9	4	17	320	9.71	189		266	586	54.61	45.39
10	8	9	5	16	320	9.71	190		308	628	50.96	49.04
10	9	9	6	18	320	9.71	191		341	661	48.41	51.59
3	29	9	1	19	319	9.68	192		120	439	72.67	27.33
6	7	9	1	17	319	9.68	193		273	592	53.89	46.11
6	14	9	1	17	319	9.68	194		293	612	52.12	47.88
6	18	9	5	17	319	9.68	195		301	620	51.45	48.55
7	27	9	2	17	319	9.68	196		291	610	52.3	47.7
8	9	9	1	19	319	9.68	197		192	511	62.43	37.57
8	11	9	3	16	319	9.68	198		278	597	53.43	46.57
9	3	9	5	17	319	9.68	199		265	584	54.62	45.38
5	23	9	7	17	318	9.65	200		226	544	58.46	41.54

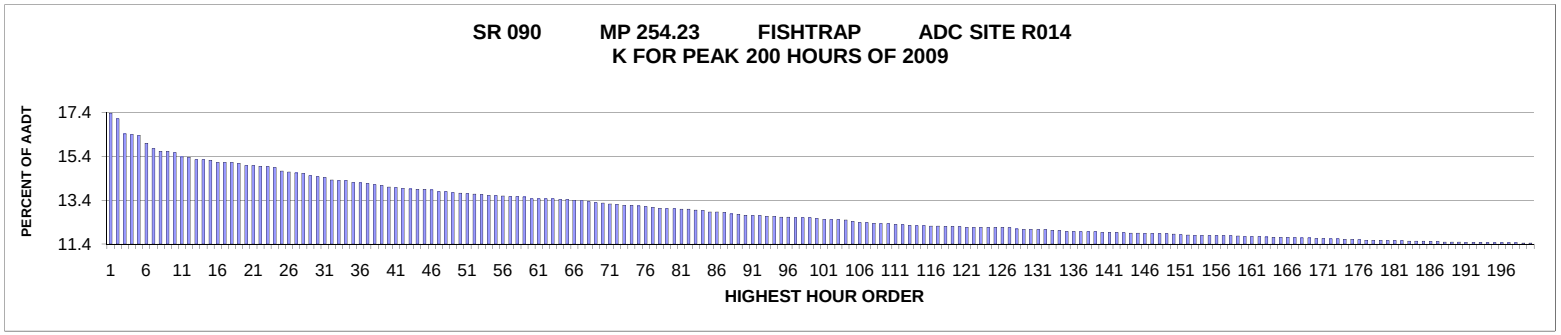

AADT= 16441 **K 30 FACTOR=** 14.46 **K 100 FACTOR=** 12.57 **K 200 FACTOR=** 11.44 **D FACTOR=** 55.81

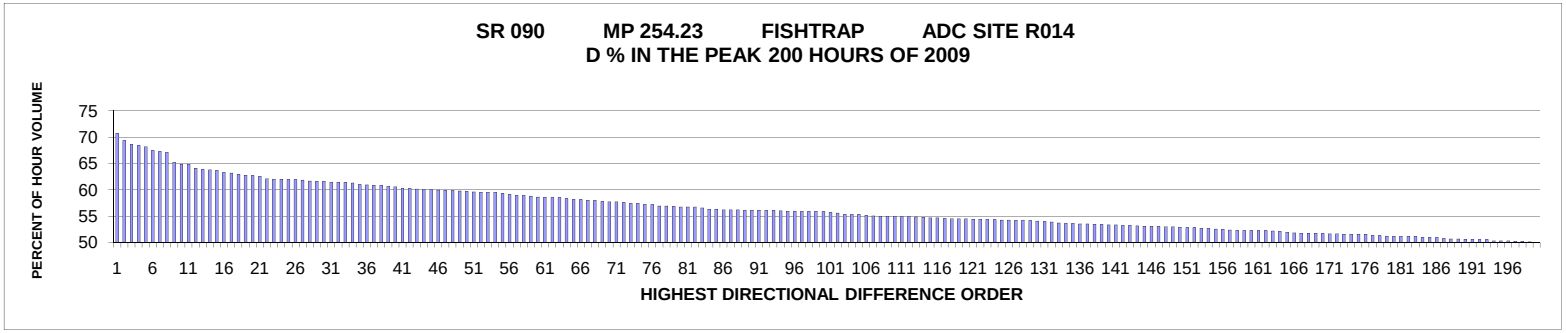

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
11	29	9	1	16	2854	17.36	1	16441	1750	1104	61.32	38.68
11	29	9	1	15	2812	17.1	2		1487	1325	52.88	47.12
11	25	9	4	16	2698	16.41	3		1508	1190	55.89	44.11
6	28	9	1	17	2693	16.38	4		1027	1666	38.14	61.86
6	28	9	1	16	2687	16.34	5		1088	1599	40.49	59.51
11	29	9	1	14	2629	15.99	6		1124	1505	42.75	57.25
11	25	9	4	17	2588	15.74	7		1485	1103	57.38	42.62
7	5	9	1	15	2569	15.63	8		1005	1564	39.12	60.88
11	25	9	4	15	2569	15.63	9		1290	1279	50.21	49.79
6	28	9	1	15	2558	15.56	10		1022	1536	39.95	60.05
8	9	9	1	15	2527	15.37	11		1196	1331	47.33	52.67
7	5	9	1	14	2524	15.35	12		906	1618	35.9	64.1
9	7	9	2	15	2506	15.24	13		1049	1457	41.86	58.14
7	5	9	1	16	2505	15.24	14		1123	1382	44.83	55.17
8	16	9	1	16	2503	15.22	15		1163	1340	46.46	53.54
6	26	9	6	16	2486	15.12	16		1620	866	65.16	34.84
8	9	9	1	16	2484	15.11	17		1281	1203	51.57	48.43

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	16	9	1	15	2484	15.11	18		1137	1347	45.77	54.23
8	16	9	1	14	2477	15.07	19		1003	1474	40.49	59.51
8	9	9	1	14	2461	14.97	20		1081	1380	43.93	56.07
11	29	9	1	13	2461	14.97	21	16441	923	1538	37.51	62.49
11	29	9	1	17	2457	14.94	22		1569	888	63.86	36.14
11	25	9	4	18	2453	14.92	23		1507	946	61.43	38.57
6	26	9	6	17	2447	14.88	24		1646	801	67.27	32.73
5	22	9	6	17	2420	14.72	25		1182	1238	48.84	51.16
6	28	9	1	18	2414	14.68	26		976	1438	40.43	59.57
8	2	9	1	16	2407	14.64	27		1054	1353	43.79	56.21
6	26	9	6	15	2403	14.62	28		1488	915	61.92	38.08
6	28	9	1	14	2384	14.5	29		939	1445	39.39	60.61
8	9	9	1	13	2377	14.46	30		1005	1372	42.28	57.72
5	22	9	6	16	2373	14.43	31		1260	1113	53.1	46.9
9	7	9	2	16	2352	14.31	32		1096	1256	46.6	53.4
8	16	9	1	17	2350	14.29	33		1216	1134	51.74	48.26
11	25	9	4	14	2348	14.28	34		1058	1290	45.06	54.94
8	2	9	1	15	2334	14.2	35		990	1344	42.42	57.58
11	29	9	1	12	2332	14.18	36		759	1573	32.55	67.45
9	4	9	6	16	2328	14.16	37		1195	1133	51.33	48.67
5	22	9	6	18	2316	14.09	38		1171	1145	50.56	49.44
7	12	9	1	15	2313	14.07	39		1042	1271	45.05	54.95
8	9	9	1	17	2300	13.99	40		1188	1112	51.65	48.35
5	22	9	6	15	2297	13.97	41	16441	1230	1067	53.55	46.45
7	5	9	1	17	2292	13.94	42		1095	1197	47.77	52.23
7	12	9	1	16	2286	13.9	43		1059	1227	46.33	53.67
7	12	9	1	13	2284	13.89	44		876	1408	38.35	61.65
8	14	9	6	16	2284	13.89	45		1255	1029	54.95	45.05
7	12	9	1	17	2279	13.86	46		1133	1146	49.71	50.29
6	26	9	6	18	2266	13.78	47		1570	696	69.29	30.71
7	5	9	1	13	2266	13.78	48		722	1544	31.86	68.14
8	16	9	1	18	2258	13.73	49		1281	977	56.73	43.27
9	7	9	2	14	2256	13.72	50		899	1357	39.85	60.15
7	31	9	6	16	2251	13.69	51		1312	939	58.29	41.71
8	9	9	1	12	2249	13.68	52		834	1415	37.08	62.92
8	7	9	6	15	2246	13.66	53		1149	1097	51.16	48.84
9	4	9	6	17	2240	13.62	54		1175	1065	52.46	47.54
9	4	9	6	18	2236	13.6	55		1192	1044	53.31	46.69
8	14	9	6	15	2235	13.59	56		1219	1016	54.54	45.46
8	7	9	6	16	2228	13.55	57		1181	1047	53.01	46.99
8	14	9	6	17	2228	13.55	58		1239	989	55.61	44.39
7	31	9	6	15	2226	13.54	59		1259	967	56.56	43.44
8	2	9	1	14	2213	13.46	60		895	1318	40.44	59.56
8	16	9	1	13	2212	13.45	61	16441	866	1346	39.15	60.85
9	7	9	2	17	2212	13.45	62		1143	1069	51.67	48.33
8	7	9	6	14	2211	13.45	63		1058	1153	47.85	52.15
7	12	9	1	14	2207	13.42	64		907	1300	41.1	58.9
8	2	9	1	13	2206	13.42	65		838	1368	37.99	62.01
4	19	9	1	19	2203	13.4	66		859	1344	38.99	61.01
8	2	9	1	17	2196	13.36	67		1049	1147	47.77	52.23
8	7	9	6	17	2192	13.33	68		1231	961	56.16	43.84
7	5	9	1	12	2184	13.28	69		639	1545	29.26	70.74

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
5	3	9	1	16	2182	13.27	70		766	1416	35.11	64.89
11	29	9	1	18	2174	13.22	71		1487	687	68.4	31.6
8	16	9	1	12	2170	13.2	72		799	1371	36.82	63.18
7	2	9	5	16	2164	13.16	73		1279	885	59.1	40.9
9	7	9	2	12	2163	13.16	74		834	1329	38.56	61.44
5	25	9	2	15	2160	13.14	75		965	1195	44.68	55.32
6	12	9	6	16	2153	13.1	76		1260	893	58.52	41.48
9	4	9	6	15	2151	13.08	77		1082	1069	50.3	49.7
7	2	9	5	18	2143	13.03	78		1345	798	62.76	37.24
7	3	9	6	12	2138	13	79		1163	975	54.4	45.6
9	7	9	2	13	2137	13	80		859	1278	40.2	59.8
5	25	9	2	16	2135	12.99	81	16441	1068	1067	50.02	49.98
6	26	9	6	14	2135	12.99	82		1161	974	54.38	45.62
6	21	9	1	16	2128	12.94	83		1078	1050	50.66	49.34
7	5	9	1	18	2126	12.93	84		1029	1097	48.4	51.6
8	14	9	6	13	2113	12.85	85		1023	1090	48.41	51.59
8	14	9	6	14	2112	12.85	86		1071	1041	50.71	49.29
7	10	9	6	15	2111	12.84	87		1144	967	54.19	45.81
8	9	9	1	18	2099	12.77	88		1178	921	56.12	43.88
7	10	9	6	16	2098	12.76	89		1173	925	55.91	44.09
7	17	9	6	16	2090	12.71	90		1134	956	54.26	45.74
8	7	9	6	13	2088	12.7	91		933	1155	44.68	55.32
5	3	9	1	15	2087	12.69	92		655	1432	31.38	68.62
7	3	9	6	13	2082	12.66	93		1181	901	56.72	43.28
5	25	9	2	17	2081	12.66	94		1108	973	53.24	46.76
6	14	9	1	16	2077	12.63	95		1026	1051	49.4	50.6
7	17	9	6	15	2077	12.63	96		1166	911	56.14	43.86
6	28	9	1	13	2072	12.6	97		800	1272	38.61	61.39
8	16	9	1	19	2072	12.6	98		1276	796	61.58	38.42
6	14	9	1	17	2070	12.59	99		1090	980	52.66	47.34
7	2	9	5	15	2066	12.57	100		1192	874	57.7	42.3
6	14	9	1	15	2058	12.52	101	16441	958	1100	46.55	53.45
6	12	9	6	17	2057	12.51	102		1155	902	56.15	43.85
7	2	9	5	17	2056	12.51	103		1240	816	60.31	39.69
8	2	9	1	12	2054	12.49	104		755	1299	36.76	63.24
6	21	9	1	15	2046	12.44	105		976	1070	47.7	52.3
4	5	9	1	16	2035	12.38	106		1191	844	58.53	41.47
5	3	9	1	17	2033	12.37	107		759	1274	37.33	62.67
7	17	9	6	17	2028	12.34	108		1154	874	56.9	43.1
7	12	9	1	12	2025	12.32	109		770	1255	38.02	61.98
8	14	9	6	11	2025	12.32	110		855	1170	42.22	57.78
9	11	9	6	17	2020	12.29	111		1109	911	54.9	45.1
5	25	9	2	14	2018	12.27	112		807	1211	39.99	60.01
6	12	9	6	15	2014	12.25	113		1168	846	57.99	42.01
8	9	9	1	19	2011	12.23	114		1218	793	60.57	39.43
9	7	9	2	18	2011	12.23	115		1065	946	52.96	47.04
6	7	9	1	17	2007	12.21	116		971	1036	48.38	51.62
8	7	9	6	12	2007	12.21	117		784	1223	39.06	60.94
6	14	9	1	14	2006	12.2	118		839	1167	41.82	58.18
6	19	9	6	15	2006	12.2	119		1075	931	53.59	46.41
5	22	9	6	14	2002	12.18	120		982	1020	49.05	50.95
7	31	9	6	14	2000	12.16	121	16441	1070	930	53.5	46.5

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	17	9	6	14	1999	12.16	122		1031	968	51.58	48.42
3	29	9	1	16	1997	12.15	123		1011	986	50.63	49.37
4	5	9	1	17	1997	12.15	124		1171	826	58.64	41.36
6	21	9	1	14	1997	12.15	125		954	1043	47.77	52.23
8	14	9	6	12	1997	12.15	126		902	1095	45.17	54.83
7	31	9	6	17	1996	12.14	127		1124	872	56.31	43.69
7	3	9	6	11	1988	12.09	128		1017	971	51.16	48.84
7	3	9	6	14	1985	12.07	129		1098	887	55.31	44.69
11	25	9	4	19	1985	12.07	130		1287	698	64.84	35.16
6	21	9	1	17	1983	12.06	131		1080	903	54.46	45.54
5	17	9	1	17	1982	12.06	132		1055	927	53.23	46.77
7	17	9	6	13	1977	12.02	133		930	1047	47.04	52.96
7	10	9	6	14	1975	12.01	134		943	1032	47.75	52.25
7	2	9	5	19	1966	11.96	135		1254	712	63.78	36.22
8	7	9	6	18	1966	11.96	136		1150	816	58.49	41.51
11	25	9	4	13	1965	11.95	137		864	1101	43.97	56.03
6	19	9	6	16	1964	11.95	138		1097	867	55.86	44.14
7	10	9	6	17	1964	11.95	139		1094	870	55.7	44.3
8	1	9	7	12	1962	11.93	140		1022	940	52.09	47.91
7	31	9	6	18	1960	11.92	141	16441	1152	808	58.78	41.22
9	4	9	6	14	1959	11.92	142		944	1015	48.19	51.81
7	6	9	2	13	1958	11.91	143		752	1206	38.41	61.59
7	31	9	6	12	1955	11.89	144		989	966	50.59	49.41
8	8	9	7	12	1955	11.89	145		931	1024	47.62	52.38
5	8	9	6	16	1953	11.88	146		1060	893	54.28	45.72
7	6	9	2	16	1953	11.88	147		942	1011	48.23	51.77
7	31	9	6	13	1952	11.87	148		1001	951	51.28	48.72
9	20	9	1	16	1950	11.86	149		951	999	48.77	51.23
7	10	9	6	18	1949	11.85	150		1119	830	57.41	42.59
12	27	9	1	14	1944	11.82	151		837	1107	43.06	56.94
5	10	9	1	17	1941	11.81	152		797	1144	41.06	58.94
6	28	9	1	12	1938	11.79	153		638	1300	32.92	67.08
7	6	9	2	14	1938	11.79	154		781	1157	40.3	59.7
6	5	9	6	16	1936	11.78	155		1088	848	56.2	43.8
8	14	9	6	18	1936	11.78	156		1049	887	54.18	45.82
6	5	9	6	17	1935	11.77	157		1027	908	53.07	46.93
8	28	9	6	17	1935	11.77	158		1080	855	55.81	44.19
8	2	9	1	19	1934	11.76	159		1159	775	59.93	40.07
8	15	9	7	11	1930	11.74	160		885	1045	45.85	54.15
9	18	9	6	18	1930	11.74	161	16441	1095	835	56.74	43.26
9	25	9	6	17	1929	11.73	162		1050	879	54.43	45.57
8	15	9	7	12	1927	11.72	163		961	966	49.87	50.13
6	12	9	6	18	1925	11.71	164		1153	772	59.9	40.1
8	9	9	1	11	1925	11.71	165		700	1225	36.36	63.64
5	15	9	6	17	1923	11.7	166		999	924	51.95	48.05
8	28	9	6	16	1922	11.69	167		1074	848	55.88	44.12
8	2	9	1	18	1921	11.68	168		965	956	50.23	49.77
11	25	9	4	12	1918	11.67	169		727	1191	37.9	62.1
4	5	9	1	15	1914	11.64	170		979	935	51.15	48.85
12	27	9	1	15	1913	11.64	171		908	1005	47.46	52.54
5	15	9	6	16	1912	11.63	172		1009	903	52.77	47.23
5	25	9	2	18	1912	11.63	173		1048	864	54.81	45.19

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
6	19	9	6	17	1911	11.62	174		1086	825	56.83	43.17
7	6	9	2	15	1910	11.62	175		866	1044	45.34	54.66
8	13	9	5	16	1906	11.59	176		1016	890	53.31	46.69
9	4	9	6	19	1904	11.58	177		1065	839	55.93	44.07
6	7	9	1	16	1903	11.57	178		891	1012	46.82	53.18
6	26	9	6	13	1902	11.57	179		898	1004	47.21	52.79
8	28	9	6	15	1901	11.56	180		1066	835	56.08	43.92
5	10	9	1	16	1900	11.56	181	16441	721	1179	37.95	62.05
7	17	9	6	18	1899	11.55	182		1044	855	54.98	45.02
8	7	9	6	11	1896	11.53	183		771	1125	40.66	59.34
5	17	9	1	15	1895	11.53	184		874	1021	46.12	53.88
6	7	9	1	15	1895	11.53	185		871	1024	45.96	54.04
7	2	9	5	14	1894	11.52	186		1035	859	54.65	45.35
9	18	9	6	17	1892	11.51	187		1021	871	53.96	46.04
8	1	9	7	13	1888	11.48	188		1029	859	54.5	45.5
6	28	9	1	19	1887	11.48	189		859	1028	45.52	54.48
8	15	9	7	14	1887	11.48	190		961	926	50.93	49.07
6	21	9	1	18	1886	11.47	191		1093	793	57.95	42.05
7	3	9	6	16	1886	11.47	192		1129	757	59.86	40.14
6	14	9	1	13	1885	11.47	193		749	1136	39.73	60.27
9	27	9	1	16	1884	11.46	194		936	948	49.68	50.32
7	12	9	1	18	1883	11.45	195		952	931	50.56	49.44
9	13	9	1	16	1883	11.45	196		974	909	51.73	48.27
12	27	9	1	16	1883	11.45	197		1036	847	55.02	44.98
6	19	9	6	14	1882	11.45	198		923	959	49.04	50.96
6	21	9	1	13	1881	11.44	199		806	1075	42.85	57.15
7	10	9	6	12	1881	11.44	200		822	1059	43.7	56.3

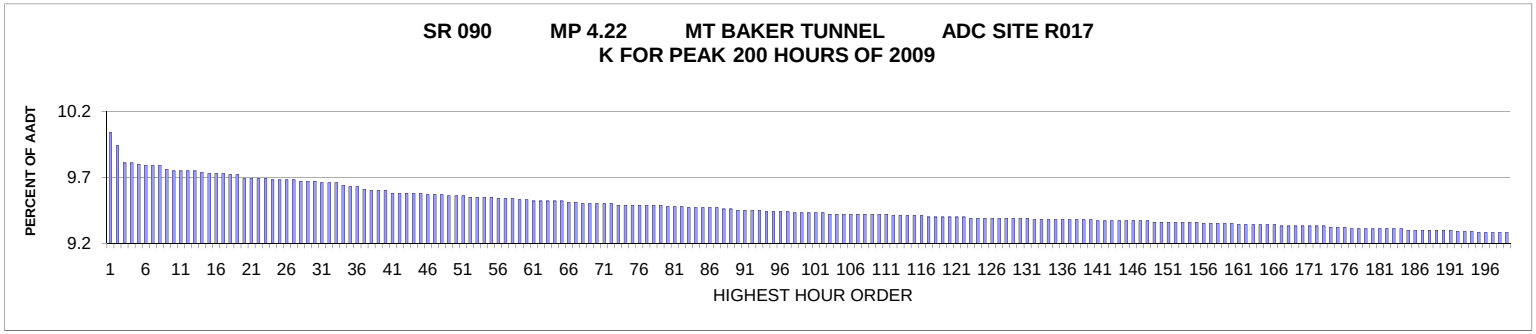

AADT= 112454 **K 30 FACTOR=** 9.67 **K 100 FACTOR=** 9.43 **K 200 FACTOR=** 9.28 **D FACTOR=** 50.76

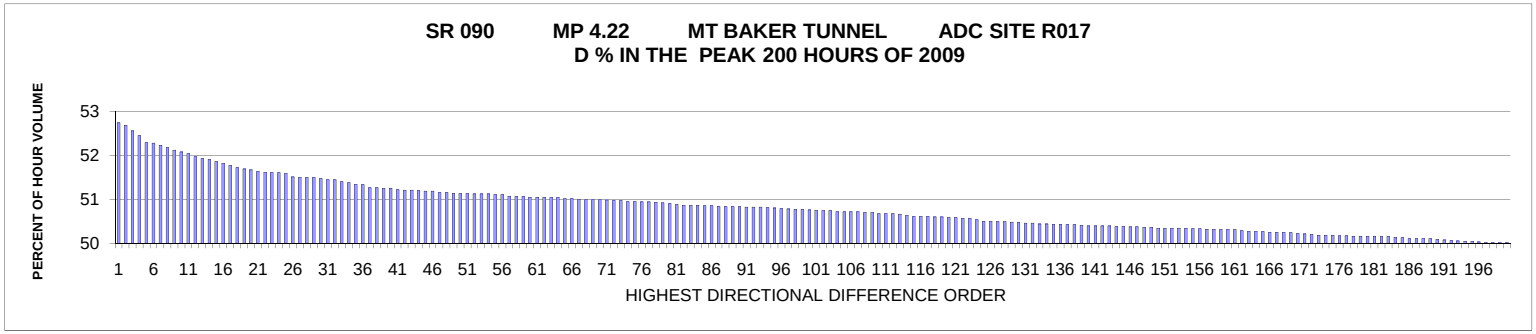

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
2	25	9	4	8	11342	10.09	1	112454	5544	5798	48.88	51.12
5	13	9	4	8	11286	10.04	2		5433	5853	48.14	51.86
3	4	9	4	8	11183	9.94	3		5645	5538	50.48	49.52
2	3	9	3	8	11029	9.81	4		5570	5459	50.5	49.5
2	12	9	5	8	11027	9.81	5		5622	5405	50.98	49.02
4	15	9	4	18	11021	9.8	6		5400	5621	49	51
1	15	9	5	8	11013	9.79	7		5615	5398	50.99	49.01
5	7	9	5	8	11008	9.79	8		5326	5682	48.38	51.62
1	13	9	3	8	11006	9.79	9		5661	5345	51.44	48.56
4	29	9	4	8	10974	9.76	10		5469	5505	49.84	50.16
2	5	9	5	9	10968	9.75	11		5389	5579	49.13	50.87
5	12	9	3	8	10967	9.75	12		5481	5486	49.98	50.02
4	28	9	3	8	10966	9.75	13		5405	5561	49.29	50.71
1	14	9	4	8	10959	9.75	14		5556	5403	50.7	49.3
4	16	9	5	18	10953	9.74	15		5298	5655	48.37	51.63
10	22	9	5	18	10945	9.73	16		5279	5666	48.23	51.77
4	21	9	3	8	10942	9.73	17		5378	5564	49.15	50.85

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
3	24	9	3	18	10937	9.73	18		5472	5465	50.03	49.97
1	29	9	5	8	10929	9.72	19		5617	5312	51.4	48.6
2	25	9	4	9	10927	9.72	20		5318	5609	48.67	51.33
11	4	9	4	8	10899	9.69	21	112454	5444	5455	49.95	50.05
10	28	9	4	18	10896	9.69	22		5325	5571	48.87	51.13
4	15	9	4	8	10894	9.69	23		5357	5537	49.17	50.83
2	4	9	4	8	10893	9.69	24		5597	5296	51.38	48.62
1	28	9	4	8	10889	9.68	25		5655	5234	51.93	48.07
2	27	9	6	17	10886	9.68	26		5370	5516	49.33	50.67
1	22	9	5	8	10883	9.68	27		5431	5452	49.9	50.1
3	26	9	5	9	10883	9.68	28		5605	5278	51.5	48.5
5	27	9	4	8	10879	9.67	29		5430	5449	49.91	50.09
4	30	9	5	8	10873	9.67	30		5301	5572	48.75	51.25
2	23	9	2	8	10870	9.67	31		5431	5439	49.96	50.04
4	16	9	5	8	10867	9.66	32		5353	5514	49.26	50.74
4	22	9	4	9	10862	9.66	33		5310	5552	48.89	51.11
1	22	9	5	18	10858	9.66	34		5319	5539	48.99	51.01
3	24	9	3	8	10841	9.64	35		5344	5497	49.29	50.71
3	17	9	3	18	10834	9.63	36		5152	5682	47.55	52.45
10	27	9	3	18	10827	9.63	37		5283	5544	48.79	51.21
3	17	9	3	8	10803	9.61	38		5453	5350	50.48	49.52
3	4	9	4	18	10801	9.6	39		5382	5419	49.83	50.17
2	27	9	6	18	10799	9.6	40		5219	5580	48.33	51.67
4	14	9	3	8	10793	9.6	41	112454	5377	5416	49.82	50.18
10	28	9	4	17	10777	9.58	42		5269	5508	48.89	51.11
1	13	9	3	17	10775	9.58	43		5264	5511	48.85	51.15
3	11	9	4	18	10774	9.58	44		5406	5368	50.18	49.82
1	15	9	5	18	10773	9.58	45		5339	5434	49.56	50.44
3	26	9	5	17	10771	9.58	46		5272	5499	48.95	51.05
4	7	9	3	18	10766	9.57	47		5163	5603	47.96	52.04
9	30	9	4	18	10757	9.57	48		5332	5425	49.57	50.43
10	6	9	3	9	10757	9.57	49		5352	5405	49.75	50.25
4	9	9	5	18	10755	9.56	50		5102	5653	47.44	52.56
4	21	9	3	9	10751	9.56	51		5465	5286	50.83	49.17
11	4	9	4	18	10745	9.56	52		5323	5422	49.54	50.46
2	2	9	2	8	10741	9.55	53		5334	5407	49.66	50.34
3	6	9	6	8	10740	9.55	54		5407	5333	50.34	49.66
10	7	9	4	9	10739	9.55	55		5476	5263	50.99	49.01
3	25	9	4	18	10738	9.55	56		5234	5504	48.74	51.26
3	18	9	4	18	10727	9.54	57		5382	5345	50.17	49.83
11	3	9	3	8	10725	9.54	58		5279	5446	49.22	50.78
9	30	9	4	17	10723	9.54	59		5239	5484	48.86	51.14
9	16	9	4	17	10721	9.53	60		5260	5461	49.06	50.94
1	23	9	6	17	10716	9.53	61	112454	5227	5489	48.78	51.22
1	12	9	2	8	10711	9.52	62		5560	5151	51.91	48.09
2	19	9	5	8	10709	9.52	63		5430	5279	50.71	49.29
6	9	9	3	8	10707	9.52	64		5315	5392	49.64	50.36
3	18	9	4	8	10704	9.52	65		5285	5419	49.37	50.63
9	15	9	3	8	10703	9.52	66		5325	5378	49.75	50.25
3	26	9	5	8	10695	9.51	67		5248	5447	49.07	50.93
4	22	9	4	18	10692	9.51	68		5306	5386	49.63	50.37
10	15	9	5	9	10688	9.5	69		5589	5099	52.29	47.71

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
9	30	9	4	8	10687	9.5	70		5463	5224	51.12	48.88
10	13	9	3	18	10686	9.5	71		5310	5376	49.69	50.31
9	29	9	3	8	10684	9.5	72		5240	5444	49.05	50.95
2	19	9	5	18	10683	9.5	73		5234	5449	48.99	51.01
1	21	9	4	18	10676	9.49	74		5376	5300	50.36	49.64
2	5	9	5	18	10673	9.49	75		5223	5450	48.94	51.06
11	5	9	5	9	10673	9.49	76		5377	5296	50.38	49.62
2	24	9	3	18	10672	9.49	77		5362	5310	50.24	49.76
2	4	9	4	9	10670	9.49	78		5242	5428	49.13	50.87
3	12	9	5	8	10670	9.49	79		5216	5454	48.88	51.12
3	5	9	5	9	10667	9.49	80		5323	5344	49.9	50.1
5	11	9	2	8	10663	9.48	81	112454	5304	5359	49.74	50.26
11	3	9	3	18	10660	9.48	82		5296	5364	49.68	50.32
1	26	9	2	17	10656	9.48	83		5415	5241	50.82	49.18
10	22	9	5	17	10655	9.47	84		5222	5433	49.01	50.99
3	11	9	4	9	10654	9.47	85		5282	5372	49.58	50.42
1	14	9	4	17	10650	9.47	86		5211	5439	48.93	51.07
11	9	9	2	18	10648	9.47	87		5308	5340	49.85	50.15
12	3	9	5	17	10644	9.47	88		5321	5323	49.99	50.01
4	16	9	5	17	10637	9.46	89		5148	5489	48.4	51.6
6	11	9	5	8	10633	9.46	90		5284	5349	49.69	50.31
6	8	9	2	8	10630	9.45	91		5386	5244	50.67	49.33
3	17	9	3	9	10623	9.45	92		5347	5276	50.33	49.67
1	22	9	5	17	10622	9.45	93		5224	5398	49.18	50.82
10	21	9	4	18	10622	9.45	94		5208	5414	49.03	50.97
4	20	9	2	8	10620	9.44	95		5269	5351	49.61	50.39
6	10	9	4	8	10613	9.44	96		5329	5284	50.21	49.79
9	1	9	3	18	10613	9.44	97		5216	5397	49.15	50.85
5	28	9	5	8	10612	9.44	98		5416	5196	51.04	48.96
1	13	9	3	9	10605	9.43	99		5329	5276	50.25	49.75
6	2	9	3	8	10603	9.43	100		5285	5318	49.84	50.16
1	29	9	5	9	10602	9.43	101	112454	5305	5297	50.04	49.96
5	21	9	5	8	10602	9.43	102		5295	5307	49.94	50.06
5	15	9	6	8	10599	9.43	103		5091	5508	48.03	51.97
5	8	9	6	8	10598	9.42	104		5014	5584	47.31	52.69
1	28	9	4	18	10596	9.42	105		5265	5331	49.69	50.31
2	12	9	5	18	10596	9.42	106		5361	5235	50.59	49.41
5	20	9	4	8	10596	9.42	107		5386	5210	50.83	49.17
9	10	9	5	8	10595	9.42	108		5066	5529	47.82	52.18
1	22	9	5	9	10592	9.42	109		5312	5280	50.15	49.85
1	12	9	2	9	10591	9.42	110		5226	5365	49.34	50.66
12	1	9	3	17	10589	9.42	111		5355	5234	50.57	49.43
9	24	9	5	8	10588	9.42	112		5346	5242	50.49	49.51
4	13	9	2	8	10583	9.41	113		5159	5424	48.75	51.25
9	23	9	4	8	10583	9.41	114		5394	5189	50.97	49.03
3	18	9	4	9	10582	9.41	115		5330	5252	50.37	49.63
4	15	9	4	17	10578	9.41	116		5194	5384	49.1	50.9
12	3	9	5	9	10578	9.41	117		5386	5192	50.92	49.08
2	20	9	6	17	10576	9.4	118		5129	5447	48.5	51.5
12	1	9	3	9	10575	9.4	119		5289	5286	50.01	49.99
9	17	9	5	9	10572	9.4	120		5397	5175	51.05	48.95
3	26	9	5	18	10571	9.4	121	112454	5229	5342	49.47	50.53

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
5	13	9	4	9	10570	9.4	122		5185	5385	49.05	50.95
3	10	9	3	8	10567	9.4	123		5312	5255	50.27	49.73
5	20	9	4	17	10565	9.39	124		5156	5409	48.8	51.2
10	23	9	6	17	10563	9.39	125		5123	5440	48.5	51.5
9	24	9	5	17	10562	9.39	126		5268	5294	49.88	50.12
10	8	9	5	9	10562	9.39	127		5459	5103	51.69	48.31
2	18	9	4	8	10556	9.39	128		5319	5237	50.39	49.61
3	12	9	5	18	10555	9.39	129		5267	5288	49.9	50.1
5	12	9	3	17	10555	9.39	130		5204	5351	49.3	50.7
6	3	9	4	8	10555	9.39	131		5244	5311	49.68	50.32
10	7	9	4	18	10554	9.39	132		5278	5276	50.01	49.99
2	18	9	4	18	10553	9.38	133		5213	5340	49.4	50.6
2	4	9	4	18	10551	9.38	134		5192	5359	49.21	50.79
5	14	9	5	17	10551	9.38	135		5319	5232	50.41	49.59
10	1	9	5	9	10551	9.38	136		5435	5116	51.51	48.49
3	31	9	3	8	10549	9.38	137		5175	5374	49.06	50.94
5	12	9	3	18	10548	9.38	138		5230	5318	49.58	50.42
4	23	9	5	17	10547	9.38	139		5154	5393	48.87	51.13
10	20	9	3	18	10547	9.38	140		5252	5295	49.8	50.2
4	20	9	2	18	10546	9.38	141	112454	5192	5354	49.23	50.77
11	4	9	4	17	10542	9.37	142		5079	5463	48.18	51.82
1	21	9	4	9	10540	9.37	143		5229	5311	49.61	50.39
4	30	9	5	9	10539	9.37	144		5305	5234	50.34	49.66
11	4	9	4	9	10537	9.37	145		5330	5207	50.58	49.42
3	13	9	6	17	10535	9.37	146		5157	5378	48.95	51.05
3	27	9	6	18	10535	9.37	147		5142	5393	48.81	51.19
4	15	9	4	9	10535	9.37	148		5244	5291	49.78	50.22
2	25	9	4	18	10532	9.37	149		5318	5214	50.49	49.51
1	20	9	3	8	10531	9.36	150		5506	5025	52.28	47.72
2	3	9	3	9	10531	9.36	151		5156	5375	48.96	51.04
5	12	9	3	9	10528	9.36	152		4976	5552	47.26	52.74
9	30	9	4	9	10527	9.36	153		5389	5138	51.19	48.81
9	9	9	4	18	10524	9.36	154		5269	5255	50.07	49.93
9	17	9	5	17	10521	9.36	155		5225	5296	49.66	50.34
12	2	9	4	18	10521	9.36	156		5140	5381	48.85	51.15
4	22	9	4	17	10519	9.35	157		5079	5440	48.28	51.72
10	28	9	4	8	10517	9.35	158		5219	5298	49.62	50.38
1	20	9	3	18	10515	9.35	159		5328	5187	50.67	49.33
9	16	9	4	9	10509	9.35	160		5340	5169	50.81	49.19
12	10	9	5	17	10509	9.35	161	112454	5190	5319	49.39	50.61
1	30	9	6	18	10504	9.34	162		5111	5393	48.66	51.34
2	27	9	6	8	10504	9.34	163		5267	5237	50.14	49.86
5	19	9	3	8	10502	9.34	164		5332	5170	50.77	49.23
10	5	9	2	18	10501	9.34	165		5240	5261	49.9	50.1
10	13	9	3	8	10501	9.34	166		5162	5339	49.16	50.84
11	2	9	2	8	10501	9.34	167		5081	5420	48.39	51.61
10	1	9	5	8	10496	9.33	168		5184	5312	49.39	50.61
2	6	9	6	17	10495	9.33	169		5231	5264	49.84	50.16
4	2	9	5	8	10494	9.33	170		5374	5120	51.21	48.79
12	3	9	5	18	10494	9.33	171		5115	5379	48.74	51.26
2	19	9	5	17	10493	9.33	172		5012	5481	47.77	52.23
10	15	9	5	8	10492	9.33	173		5155	5337	49.13	50.87

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
6	16	9	3	8	10488	9.33	174		5296	5192	50.5	49.5
4	14	9	3	18	10482	9.32	175		5352	5130	51.06	48.94
9	16	9	4	8	10478	9.32	176		5317	5161	50.74	49.26
2	17	9	3	8	10476	9.32	177		5298	5178	50.57	49.43
1	28	9	4	9	10474	9.31	178		5201	5273	49.66	50.34
5	21	9	5	17	10474	9.31	179		5278	5196	50.39	49.61
11	20	9	6	17	10473	9.31	180		5014	5459	47.88	52.12
6	18	9	5	8	10471	9.31	181	112454	5282	5189	50.44	49.56
10	6	9	3	18	10467	9.31	182		5215	5252	49.82	50.18
9	24	9	5	18	10466	9.31	183		5147	5319	49.18	50.82
1	15	9	5	9	10465	9.31	184		5450	5015	52.08	47.92
2	10	9	3	8	10464	9.31	185		5386	5078	51.47	48.53
10	27	9	3	8	10462	9.3	186		5167	5295	49.39	50.61
10	8	9	5	8	10458	9.3	187		5166	5292	49.4	50.6
10	2	9	6	17	10457	9.3	188		5062	5395	48.41	51.59
9	2	9	4	18	10455	9.3	189		5211	5244	49.84	50.16
9	17	9	5	8	10454	9.3	190		5261	5193	50.33	49.67
10	19	9	2	9	10453	9.3	191		5319	5134	50.88	49.12
12	9	9	4	18	10453	9.3	192		5076	5377	48.56	51.44
6	2	9	3	17	10449	9.29	193		5196	5253	49.73	50.27
3	18	9	4	17	10445	9.29	194		5143	5302	49.24	50.76
6	1	9	2	8	10443	9.29	195		5251	5192	50.28	49.72
6	4	9	5	8	10440	9.28	196		5298	5142	50.75	49.25
1	29	9	5	18	10439	9.28	197		5294	5145	50.71	49.29
6	9	9	3	17	10439	9.28	198		5172	5267	49.54	50.46
12	7	9	2	18	10439	9.28	199		5136	5303	49.2	50.8
12	8	9	3	17	10439	9.28	200		5264	5175	50.43	49.57

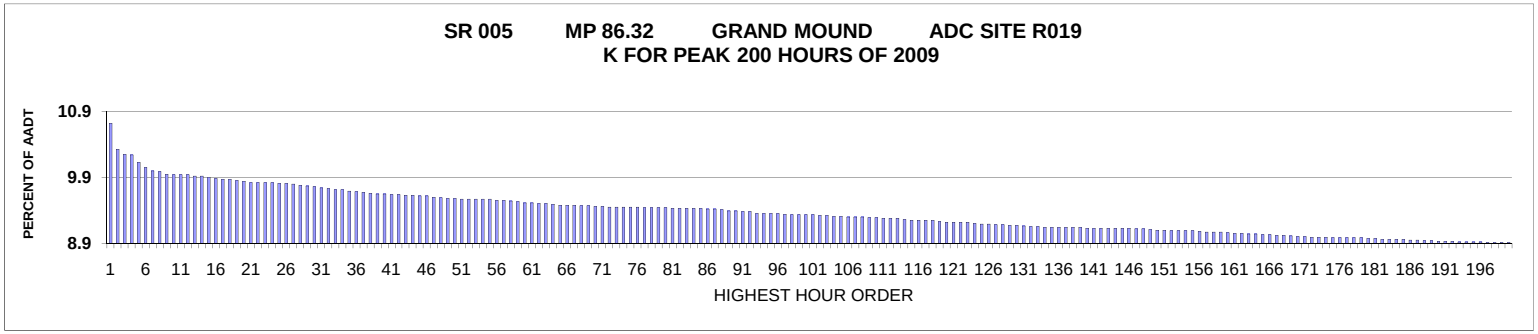

AADT= 59609 **K 30 FACTOR=** 9.76 **K 100 FACTOR=** 9.33 **K 200 FACTOR=** 8.91 **D FACTOR=** 51.94

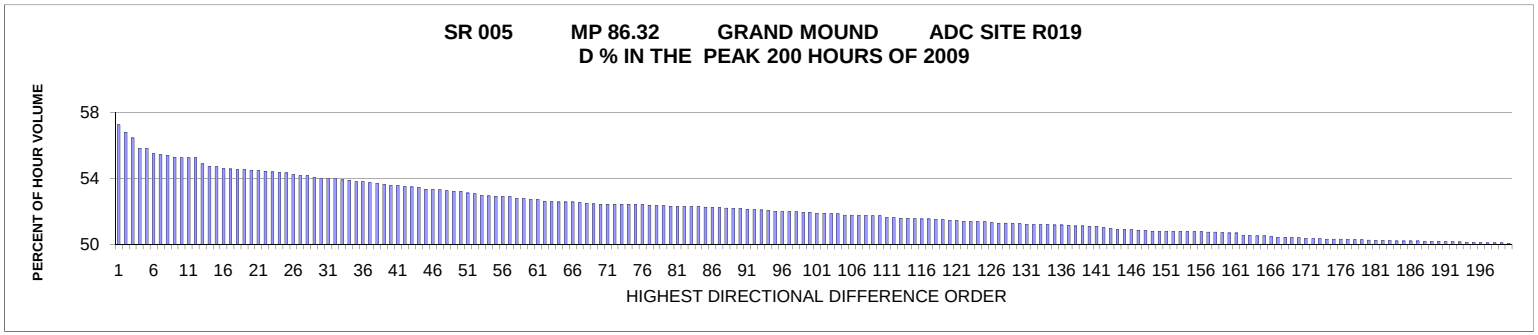

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
11	29	9	1	14	6392	10.72	1	59609	3481	2911	54.46	45.54
12	26	9	7	14	6157	10.33	2		3031	3126	49.23	50.77
12	26	9	7	13	6108	10.25	3		2915	3193	47.72	52.28
11	29	9	1	15	6102	10.24	4		3325	2777	54.49	45.51
8	16	9	1	15	6040	10.13	5		3117	2923	51.61	48.39
8	15	9	7	12	5993	10.05	6		2978	3015	49.69	50.31
12	27	9	1	15	5963	10	7		3181	2782	53.35	46.65
8	14	9	6	17	5956	9.99	8		3031	2925	50.89	49.11
8	28	9	6	16	5930	9.95	9		2884	3046	48.63	51.37
12	26	9	7	15	5927	9.94	10		2957	2970	49.89	50.11
8	23	9	1	14	5926	9.94	11		2981	2945	50.3	49.7
8	16	9	1	16	5923	9.94	12		2904	3019	49.03	50.97
11	25	9	4	14	5914	9.92	13		2864	3050	48.43	51.57
11	25	9	4	13	5911	9.92	14		2750	3161	46.52	53.48
11	28	9	7	14	5901	9.9	15		3171	2730	53.74	46.26
11	25	9	4	15	5888	9.88	16		2904	2984	49.32	50.68
8	9	9	1	15	5885	9.87	17		2987	2898	50.76	49.24

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	14	9	6	15	5885	9.87	18		3031	2854	51.5	48.5
8	16	9	1	14	5872	9.85	19		2926	2946	49.83	50.17
7	12	9	1	14	5867	9.84	20		3071	2796	52.34	47.66
12	27	9	1	14	5855	9.82	21	59609	3023	2832	51.63	48.37
8	15	9	7	13	5854	9.82	22		2968	2886	50.7	49.3
7	31	9	6	16	5851	9.82	23		2955	2896	50.5	49.5
8	9	9	1	14	5851	9.82	24		2990	2861	51.1	48.9
7	17	9	6	15	5850	9.81	25		2969	2881	50.75	49.25
8	7	9	6	18	5847	9.81	26		2969	2878	50.78	49.22
11	25	9	4	16	5841	9.8	27		2985	2856	51.1	48.9
11	29	9	1	16	5828	9.78	28		3036	2792	52.09	47.91
11	28	9	7	15	5821	9.77	29		3216	2605	55.25	44.75
8	23	9	1	13	5816	9.76	30		2937	2879	50.5	49.5
7	5	9	1	14	5804	9.74	31		2870	2934	49.45	50.55
7	5	9	1	16	5801	9.73	32		2923	2878	50.39	49.61
7	5	9	1	13	5789	9.71	33		2820	2969	48.71	51.29
12	27	9	1	16	5789	9.71	34		3125	2664	53.98	46.02
8	7	9	6	17	5776	9.69	35		2861	2915	49.53	50.47
7	24	9	6	14	5772	9.68	36		2952	2820	51.14	48.86
8	30	9	1	14	5767	9.67	37		3155	2612	54.71	45.29
7	3	9	6	15	5758	9.66	38		3027	2731	52.57	47.43
7	24	9	6	17	5754	9.65	39		3070	2684	53.35	46.65
11	28	9	7	13	5754	9.65	40		2983	2771	51.84	48.16
7	3	9	6	12	5744	9.64	41	59609	2940	2804	51.18	48.82
8	9	9	1	13	5744	9.64	42		2858	2886	49.76	50.24
8	1	9	7	12	5742	9.63	43		2841	2901	49.48	50.52
7	31	9	6	15	5741	9.63	44		2866	2875	49.92	50.08
8	16	9	1	17	5737	9.62	45		2830	2907	49.33	50.67
8	14	9	6	14	5736	9.62	46		2936	2800	51.19	48.81
8	21	9	6	16	5723	9.6	47		2848	2875	49.76	50.24
8	30	9	1	17	5716	9.59	48		3096	2620	54.16	45.84
7	17	9	6	16	5710	9.58	49		2862	2848	50.12	49.88
8	28	9	6	15	5709	9.58	50		2844	2865	49.82	50.18
3	27	9	6	16	5705	9.57	51		2753	2952	48.26	51.74
7	19	9	1	13	5704	9.57	52		2980	2724	52.24	47.76
7	26	9	1	13	5704	9.57	53		2994	2710	52.49	47.51
8	22	9	7	12	5702	9.57	54		2624	3078	46.02	53.98
11	27	9	6	14	5702	9.57	55		2839	2863	49.79	50.21
8	2	9	1	15	5694	9.55	56		2984	2710	52.41	47.59
12	26	9	7	12	5692	9.55	57		2609	3083	45.84	54.16
7	12	9	1	15	5687	9.54	58		3153	2534	55.44	44.56
7	5	9	1	15	5683	9.53	59		2770	2913	48.74	51.26
7	10	9	6	15	5671	9.51	60		2909	2762	51.3	48.7
8	8	9	7	13	5669	9.51	61	59609	2697	2972	47.57	52.43
8	16	9	1	13	5665	9.5	62		2719	2946	48	52
6	19	9	6	15	5660	9.5	63		2819	2841	49.81	50.19
8	29	9	7	12	5655	9.49	64		2531	3124	44.76	55.24
8	2	9	1	14	5653	9.48	65		2837	2816	50.19	49.81
3	29	9	1	16	5650	9.48	66		2759	2891	48.83	51.17
7	10	9	6	17	5648	9.48	67		2701	2947	47.82	52.18
7	12	9	1	16	5647	9.47	68		3072	2575	54.4	45.6
11	29	9	1	13	5647	9.47	69		3019	2628	53.46	46.54

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
6	19	9	6	17	5638	9.46	70		2653	2985	47.06	52.94
11	27	9	6	13	5637	9.46	71		2712	2925	48.11	51.89
9	5	9	7	12	5635	9.45	72		2706	2929	48.02	51.98
8	14	9	6	13	5633	9.45	73		2767	2866	49.12	50.88
8	23	9	1	15	5632	9.45	74		2832	2800	50.28	49.72
12	24	9	5	13	5632	9.45	75		2661	2971	47.25	52.75
11	27	9	6	12	5631	9.45	76		2505	3126	44.49	55.51
8	14	9	6	16	5630	9.44	77		2882	2748	51.19	48.81
5	22	9	6	16	5627	9.44	78		2803	2824	49.81	50.19
8	8	9	7	14	5625	9.44	79		2685	2940	47.73	52.27
9	4	9	6	15	5625	9.44	80		2630	2995	46.76	53.24
3	29	9	1	15	5624	9.43	81	59609	2873	2751	51.08	48.92
8	23	9	1	16	5621	9.43	82		2829	2792	50.33	49.67
7	26	9	1	15	5619	9.43	83		2947	2672	52.45	47.55
11	26	9	5	11	5619	9.43	84		2915	2704	51.88	48.12
11	27	9	6	15	5619	9.43	85		2871	2748	51.09	48.91
8	1	9	7	13	5616	9.42	86		2859	2757	50.91	49.09
7	12	9	1	13	5613	9.42	87		2851	2762	50.79	49.21
7	26	9	1	14	5607	9.41	88		2929	2678	52.24	47.76
6	12	9	6	16	5598	9.39	89		2803	2795	50.07	49.93
7	11	9	7	12	5598	9.39	90		2555	3043	45.64	54.36
8	23	9	1	17	5593	9.38	91		2868	2725	51.28	48.72
5	23	9	7	12	5592	9.38	92		2781	2811	49.73	50.27
7	10	9	6	14	5576	9.35	93		2792	2784	50.07	49.93
8	7	9	6	16	5576	9.35	94		2770	2806	49.68	50.32
8	14	9	6	12	5572	9.35	95		2545	3027	45.67	54.33
7	3	9	6	14	5571	9.35	96		2795	2776	50.17	49.83
11	28	9	7	16	5567	9.34	97		3075	2492	55.24	44.76
8	28	9	6	14	5564	9.33	98		2631	2933	47.29	52.71
6	21	9	1	17	5559	9.33	99		2900	2659	52.17	47.83
7	24	9	6	13	5559	9.33	100		2646	2913	47.6	52.4
11	25	9	4	17	5559	9.33	101	59609	2652	2907	47.71	52.29
8	21	9	6	13	5557	9.32	102		2668	2889	48.01	51.99
8	28	9	6	17	5556	9.32	103		2649	2907	47.68	52.32
7	26	9	1	16	5548	9.31	104		2901	2647	52.29	47.71
7	17	9	6	14	5547	9.31	105		2709	2838	48.84	51.16
7	10	9	6	13	5546	9.3	106		2638	2908	47.57	52.43
8	30	9	1	13	5546	9.3	107		2871	2675	51.77	48.23
8	30	9	1	15	5546	9.3	108		3073	2473	55.41	44.59
5	15	9	6	16	5540	9.29	109		2750	2790	49.64	50.36
6	14	9	1	17	5537	9.29	110		3091	2446	55.82	44.18
9	4	9	6	14	5533	9.28	111		2681	2852	48.45	51.55
6	26	9	6	15	5532	9.28	112		2757	2775	49.84	50.16
12	27	9	1	13	5529	9.28	113		2768	2761	50.06	49.94
7	19	9	1	17	5518	9.26	114		2843	2675	51.52	48.48
5	22	9	6	15	5516	9.25	115		2717	2799	49.26	50.74
5	23	9	7	11	5516	9.25	116		2549	2967	46.21	53.79
8	30	9	1	18	5512	9.25	117		2938	2574	53.3	46.7
8	2	9	1	13	5511	9.25	118		2714	2797	49.25	50.75
6	12	9	6	15	5504	9.23	119		2651	2853	48.16	51.84
3	27	9	6	15	5496	9.22	120		2594	2902	47.2	52.8
6	26	9	6	16	5494	9.22	121	59609	2733	2761	49.75	50.25

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	22	9	7	13	5494	9.22	122		2640	2854	48.05	51.95
11	26	9	5	12	5494	9.22	123		2831	2663	51.53	48.47
8	15	9	7	11	5486	9.2	124		2493	2993	45.44	54.56
8	8	9	7	12	5481	9.19	125		2645	2836	48.26	51.74
6	28	9	1	15	5479	9.19	126		2953	2526	53.9	46.1
9	13	9	1	18	5473	9.18	127		2815	2658	51.43	48.57
5	22	9	6	17	5470	9.18	128		2621	2849	47.92	52.08
6	21	9	1	16	5466	9.17	129		2980	2486	54.52	45.48
9	18	9	6	15	5464	9.17	130		2638	2826	48.28	51.72
6	28	9	1	14	5463	9.16	131		2990	2473	54.73	45.27
4	17	9	6	16	5457	9.15	132		2655	2802	48.65	51.35
8	30	9	1	16	5457	9.15	133		2886	2571	52.89	47.11
7	31	9	6	14	5451	9.14	134		2702	2749	49.57	50.43
9	18	9	6	16	5451	9.14	135		2685	2766	49.26	50.74
5	25	9	2	16	5450	9.14	136		2975	2475	54.59	45.41
7	3	9	6	16	5450	9.14	137		2720	2730	49.91	50.09
11	25	9	4	18	5449	9.14	138		2459	2990	45.13	54.87
8	15	9	7	14	5447	9.14	139		2922	2525	53.64	46.36
6	28	9	1	16	5445	9.13	140		2855	2590	52.43	47.57
6	28	9	1	17	5445	9.13	141	59609	2924	2521	53.7	46.3
7	3	9	6	11	5445	9.13	142		2590	2855	47.57	52.43
8	29	9	7	13	5444	9.13	143		2574	2870	47.28	52.72
8	28	9	6	13	5443	9.13	144		2500	2943	45.93	54.07
7	24	9	6	18	5441	9.13	145		3115	2326	57.25	42.75
12	24	9	5	14	5440	9.13	146		2597	2843	47.74	52.26
8	16	9	1	20	5439	9.12	147		2730	2709	50.19	49.81
6	21	9	1	14	5435	9.12	148		2846	2589	52.36	47.64
6	21	9	1	18	5431	9.11	149		2857	2574	52.61	47.39
7	19	9	1	16	5425	9.1	150		2824	2601	52.06	47.94
11	25	9	4	12	5424	9.1	151		2396	3028	44.17	55.83
8	1	9	7	11	5421	9.09	152		2494	2927	46.01	53.99
11	28	9	7	12	5421	9.09	153		2718	2703	50.14	49.86
7	24	9	6	12	5419	9.09	154		2516	2903	46.43	53.57
12	26	9	7	16	5418	9.09	155		2754	2664	50.83	49.17
7	26	9	1	12	5411	9.08	156		2873	2538	53.1	46.9
7	10	9	6	16	5404	9.07	157		2787	2617	51.57	48.43
8	21	9	6	17	5404	9.07	158		2544	2860	47.08	52.92
8	21	9	6	18	5404	9.07	159		2497	2907	46.21	53.79
3	22	9	1	16	5402	9.06	160		3069	2333	56.81	43.19
12	24	9	5	15	5397	9.05	161	59609	2633	2764	48.79	51.21
6	28	9	1	13	5395	9.05	162		2836	2559	52.57	47.43
8	16	9	1	12	5390	9.04	163		2617	2773	48.55	51.45
4	12	9	1	18	5387	9.04	164		2937	2450	54.52	45.48
8	21	9	6	14	5383	9.03	165		2677	2706	49.73	50.27
8	23	9	1	18	5381	9.03	166		2817	2564	52.35	47.65
8	7	9	6	15	5379	9.02	167		2533	2846	47.09	52.91
7	25	9	7	12	5378	9.02	168		2667	2711	49.59	50.41
4	10	9	6	16	5369	9.01	169		2602	2767	48.46	51.54
8	9	9	1	18	5363	9	170		2727	2636	50.85	49.15
4	3	9	6	15	5362	9	171		2697	2665	50.3	49.7
9	5	9	7	13	5361	8.99	172		2586	2775	48.24	51.76
7	31	9	6	13	5356	8.99	173		2519	2837	47.03	52.97

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	21	9	6	15	5356	8.99	174		2605	2751	48.64	51.36
6	14	9	1	16	5355	8.98	175		2961	2394	55.29	44.71
6	26	9	6	14	5355	8.98	176		2469	2886	46.11	53.89
7	26	9	1	18	5354	8.98	177		2849	2505	53.21	46.79
8	29	9	7	14	5354	8.98	178		2547	2807	47.57	52.43
6	19	9	6	18	5352	8.98	179		2485	2867	46.43	53.57
11	26	9	5	13	5346	8.97	180		2748	2598	51.4	48.6
8	7	9	6	12	5344	8.97	181	59609	2559	2785	47.89	52.11
8	2	9	1	17	5342	8.96	182		2694	2648	50.43	49.57
5	17	9	1	19	5340	8.96	183		2483	2857	46.5	53.5
9	4	9	6	17	5340	8.96	184		2532	2808	47.42	52.58
9	4	9	6	16	5339	8.96	185		2566	2773	48.06	51.94
7	3	9	6	13	5337	8.95	186		2534	2803	47.48	52.52
9	20	9	1	17	5334	8.95	187		2838	2496	53.21	46.79
8	14	9	6	18	5330	8.94	188		2657	2673	49.85	50.15
5	25	9	2	15	5328	8.94	189		3008	2320	56.46	43.54
7	26	9	1	17	5324	8.93	190		2799	2525	52.57	47.43
8	8	9	7	11	5324	8.93	191		2438	2886	45.79	54.21
5	22	9	6	14	5321	8.93	192		2619	2702	49.22	50.78
2	13	9	6	16	5320	8.92	193		2594	2726	48.76	51.24
7	12	9	1	17	5319	8.92	194		2776	2543	52.19	47.81
8	22	9	7	14	5319	8.92	195		2606	2713	48.99	51.01
9	7	9	2	16	5316	8.92	196		2894	2422	54.44	45.56
3	29	9	1	17	5313	8.91	197		2748	2565	51.72	48.28
3	27	9	6	14	5312	8.91	198		2493	2819	46.93	53.07
3	29	9	1	14	5312	8.91	199		2552	2760	48.04	51.96
8	13	9	5	15	5311	8.91	200		2614	2697	49.22	50.78

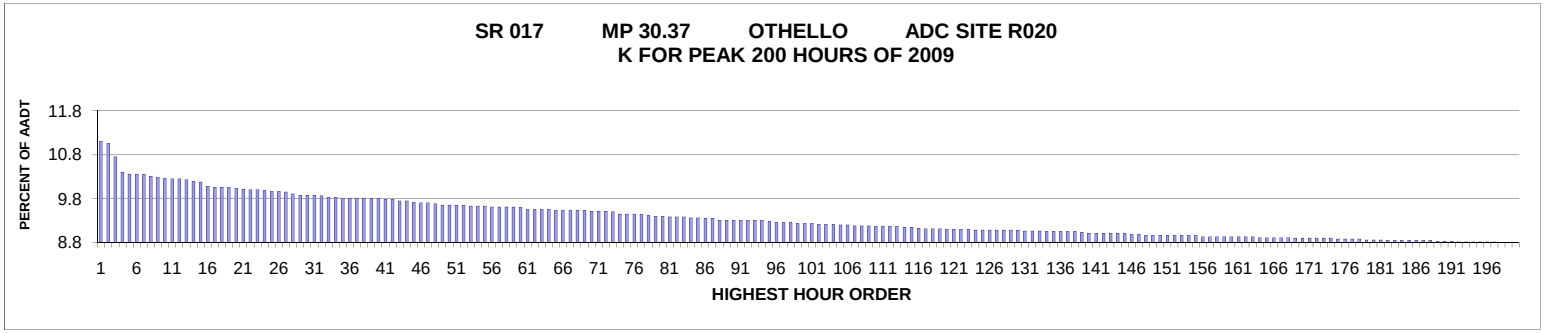

AADT= 6002 **K 30 FACTOR=** 9.88 **K 100 FACTOR=** 9.23 **K 200 FACTOR=** 8.8 **D FACTOR=** 53.32

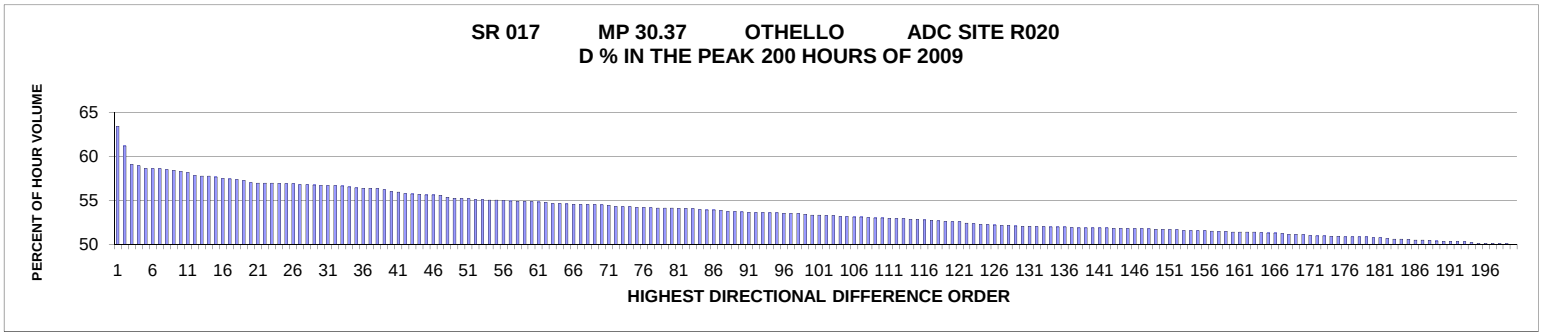

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
6	5	9	6	17	667	11.11	1	6002	327	340	49.03	50.97
9	18	9	6	17	663	11.05	2		339	324	51.13	48.87
6	5	9	6	18	645	10.75	3		306	339	47.44	52.56
7	31	9	6	18	624	10.4	4		306	318	49.04	50.96
6	26	9	6	17	622	10.36	5		298	324	47.91	52.09
9	4	9	6	17	622	10.36	6		326	296	52.41	47.59
3	13	9	6	18	621	10.35	7		282	339	45.41	54.59
9	11	9	6	18	619	10.31	8		305	314	49.27	50.73
5	15	9	6	18	617	10.28	9		300	317	48.62	51.38
9	25	9	6	18	616	10.26	10		329	287	53.41	46.59
4	17	9	6	17	615	10.25	11		302	313	49.11	50.89
9	4	9	6	18	615	10.25	12		336	279	54.63	45.37
5	8	9	6	18	614	10.23	13		266	348	43.32	56.68
7	23	9	5	18	612	10.2	14		287	325	46.9	53.1
9	25	9	6	17	611	10.18	15		295	316	48.28	51.72
10	16	9	6	18	605	10.08	16		298	307	49.26	50.74
8	6	9	5	17	604	10.06	17		250	354	41.39	58.61

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
9	18	9	6	18	604	10.06	18		260	344	43.05	56.95
5	22	9	6	18	603	10.05	19		296	307	49.09	50.91
6	12	9	6	17	602	10.03	20		303	299	50.33	49.67
10	1	9	5	18	601	10.01	21	6002	284	317	47.25	52.75
5	29	9	6	16	600	10	22		284	316	47.33	52.67
10	9	9	6	16	600	10	23		311	289	51.83	48.17
5	22	9	6	17	599	9.98	24		280	319	46.74	53.26
6	12	9	6	18	598	9.96	25		282	316	47.16	52.84
6	26	9	6	18	598	9.96	26		272	326	45.48	54.52
5	15	9	6	16	597	9.95	27		295	302	49.41	50.59
9	4	9	6	16	595	9.91	28		347	248	58.32	41.68
5	1	9	6	18	593	9.88	29		250	343	42.16	57.84
10	16	9	6	17	593	9.88	30		289	304	48.74	51.26
10	23	9	6	17	593	9.88	31		297	296	50.08	49.92
5	1	9	6	17	592	9.86	32		298	294	50.34	49.66
5	15	9	6	17	590	9.83	33		254	336	43.05	56.95
8	27	9	5	17	590	9.83	34		260	330	44.07	55.93
6	19	9	6	17	589	9.81	35		254	335	43.12	56.88
8	14	9	6	16	589	9.81	36		295	294	50.08	49.92
10	8	9	5	18	589	9.81	37		275	314	46.69	53.31
11	25	9	4	16	589	9.81	38		270	319	45.84	54.16
8	28	9	6	17	588	9.8	39		317	271	53.91	46.09
9	25	9	6	16	588	9.8	40		296	292	50.34	49.66
5	22	9	6	16	587	9.78	41	6002	294	293	50.09	49.91
10	16	9	6	16	587	9.78	42		318	269	54.17	45.83
7	10	9	6	17	585	9.75	43		259	326	44.27	55.73
10	2	9	6	17	585	9.75	44		305	280	52.14	47.86
4	3	9	6	18	583	9.71	45		244	339	41.85	58.15
8	21	9	6	18	582	9.7	46		306	276	52.58	47.42
10	4	9	1	18	582	9.7	47		255	327	43.81	56.19
8	20	9	5	18	581	9.68	48		282	299	48.54	51.46
3	27	9	6	17	579	9.65	49		284	295	49.05	50.95
8	6	9	5	18	579	9.65	50		251	328	43.35	56.65
10	2	9	6	18	579	9.65	51		283	296	48.88	51.12
10	30	9	6	17	579	9.65	52		268	311	46.29	53.71
7	16	9	5	18	578	9.63	53		252	326	43.6	56.4
8	13	9	5	18	578	9.63	54		260	318	44.98	55.02
8	27	9	5	18	578	9.63	55		280	298	48.44	51.56
3	27	9	6	18	577	9.61	56		240	337	41.59	58.41
9	4	9	6	19	577	9.61	57		331	246	57.37	42.63
9	17	9	5	18	577	9.61	58		237	340	41.07	58.93
10	30	9	6	18	577	9.61	59		276	301	47.83	52.17
10	15	9	5	17	576	9.6	60		279	297	48.44	51.56
3	23	9	2	18	573	9.55	61	6002	250	323	43.63	56.37
6	5	9	6	16	573	9.55	62		297	276	51.83	48.17
7	2	9	5	17	573	9.55	63		259	314	45.2	54.8
7	24	9	6	17	573	9.55	64		266	307	46.42	53.58
2	27	9	6	18	572	9.53	65		209	363	36.54	63.46
4	24	9	6	18	572	9.53	66		266	306	46.5	53.5
10	9	9	6	17	572	9.53	67		285	287	49.83	50.17
11	20	9	6	17	572	9.53	68		267	305	46.68	53.32
11	25	9	4	17	572	9.53	69		253	319	44.23	55.77

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
4	17	9	6	18	571	9.51	70		243	328	42.56	57.44
6	26	9	6	16	571	9.51	71		296	275	51.84	48.16
9	3	9	5	17	571	9.51	72		260	311	45.53	54.47
7	2	9	5	18	570	9.5	73		255	315	44.74	55.26
3	24	9	3	18	567	9.45	74		245	322	43.21	56.79
8	31	9	2	17	567	9.45	75		266	301	46.91	53.09
9	17	9	5	16	567	9.45	76		294	273	51.85	48.15
9	24	9	5	18	566	9.43	77		256	310	45.23	54.77
5	8	9	6	17	565	9.41	78		271	294	47.96	52.04
3	26	9	5	18	564	9.4	79		271	293	48.05	51.95
4	10	9	6	18	564	9.4	80		244	320	43.26	56.74
2	6	9	6	17	563	9.38	81	6002	279	284	49.56	50.44
8	18	9	3	18	563	9.38	82		273	290	48.49	51.51
8	21	9	6	16	563	9.38	83		298	265	52.93	47.07
7	21	9	3	17	562	9.36	84		256	306	45.55	54.45
9	15	9	3	18	562	9.36	85		257	305	45.73	54.27
4	24	9	6	17	561	9.35	86		270	291	48.13	51.87
9	18	9	6	16	561	9.35	87		257	304	45.81	54.19
4	3	9	6	16	559	9.31	88		239	320	42.75	57.25
7	10	9	6	18	559	9.31	89		254	305	45.44	54.56
10	4	9	1	17	559	9.31	90		243	316	43.47	56.53
6	19	9	6	18	558	9.3	91		272	286	48.75	51.25
9	18	9	6	19	558	9.3	92		240	318	43.01	56.99
10	8	9	5	16	558	9.3	93		285	273	51.08	48.92
10	23	9	6	18	558	9.3	94		289	269	51.79	48.21
8	19	9	4	17	557	9.28	95		289	268	51.89	48.11
4	10	9	6	16	555	9.25	96		286	269	51.53	48.47
7	8	9	4	17	555	9.25	97		227	328	40.9	59.1
7	30	9	5	17	555	9.25	98		240	315	43.24	56.76
2	20	9	6	18	554	9.23	99		215	339	38.81	61.19
2	27	9	6	17	554	9.23	100		252	302	45.49	54.51
3	6	9	6	18	554	9.23	101	6002	230	324	41.52	58.48
3	20	9	6	18	553	9.21	102		257	296	46.47	53.53
5	29	9	6	18	553	9.21	103		238	315	43.04	56.96
8	17	9	2	17	553	9.21	104		254	299	45.93	54.07
9	10	9	5	18	552	9.2	105		261	291	47.28	52.72
9	15	9	3	17	552	9.2	106		292	260	52.9	47.1
8	20	9	5	17	551	9.18	107		258	293	46.82	53.18
8	28	9	6	16	551	9.18	108		297	254	53.9	46.1
9	11	9	6	16	551	9.18	109		292	259	52.99	47.01
7	17	9	6	18	550	9.16	110		261	289	47.45	52.55
8	19	9	4	16	550	9.16	111		284	266	51.64	48.36
9	11	9	6	17	550	9.16	112		308	242	56	44
10	7	9	4	17	550	9.16	113		286	264	52	48
8	28	9	6	18	549	9.15	114		276	273	50.27	49.73
10	8	9	5	17	549	9.15	115		258	291	46.99	53.01
10	16	9	6	15	548	9.13	116		267	281	48.72	51.28
5	29	9	6	17	547	9.11	117		252	295	46.07	53.93
10	15	9	5	18	547	9.11	118		251	296	45.89	54.11
11	5	9	5	17	547	9.11	119		247	300	45.16	54.84
4	24	9	6	16	546	9.1	120		273	273	50	50
10	7	9	4	18	546	9.1	121	6002	262	284	47.99	52.01

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
11	6	9	6	17	546	9.1	122		275	271	50.37	49.63
11	20	9	6	16	546	9.1	123		294	252	53.85	46.15
2	20	9	6	17	545	9.08	124		242	303	44.4	55.6
6	12	9	6	16	545	9.08	125		296	249	54.31	45.69
6	19	9	6	16	545	9.08	126		263	282	48.26	51.74
6	25	9	5	18	545	9.08	127		250	295	45.87	54.13
7	10	9	6	16	545	9.08	128		270	275	49.54	50.46
8	13	9	5	16	545	9.08	129		277	268	50.83	49.17
10	8	9	5	8	545	9.08	130		280	265	51.38	48.62
9	17	9	5	17	544	9.06	131		280	264	51.47	48.53
10	5	9	2	18	544	9.06	132		255	289	46.88	53.13
10	21	9	4	18	544	9.06	133		241	303	44.3	55.7
4	16	9	5	18	543	9.05	134		237	306	43.65	56.35
5	8	9	6	16	543	9.05	135		268	275	49.36	50.64
7	30	9	5	18	543	9.05	136		245	298	45.12	54.88
8	18	9	3	17	543	9.05	137		247	296	45.49	54.51
9	1	9	3	18	543	9.05	138		252	291	46.41	53.59
7	28	9	3	18	542	9.03	139		274	268	50.55	49.45
5	22	9	6	15	541	9.01	140		259	282	47.87	52.13
7	28	9	3	17	541	9.01	141	6002	230	311	42.51	57.49
8	14	9	6	17	541	9.01	142		243	298	44.92	55.08
8	14	9	6	18	541	9.01	143		278	263	51.39	48.61
12	4	9	6	17	541	9.01	144		278	263	51.39	48.61
7	7	9	3	17	540	9	145		243	297	45	55
7	31	9	6	16	539	8.98	146		257	282	47.68	52.32
9	30	9	4	17	539	8.98	147		269	270	49.91	50.09
3	20	9	6	17	538	8.96	148		241	297	44.8	55.2
6	4	9	5	17	538	8.96	149		259	279	48.14	51.86
6	5	9	6	19	538	8.96	150		259	279	48.14	51.86
6	18	9	5	17	538	8.96	151		253	285	47.03	52.97
8	6	9	5	15	538	8.96	152		247	291	45.91	54.09
9	16	9	4	17	538	8.96	153		261	277	48.51	51.49
10	9	9	6	18	538	8.96	154		281	257	52.23	47.77
10	20	9	3	17	538	8.96	155		258	280	47.96	52.04
4	8	9	4	18	536	8.93	156		231	305	43.1	56.9
4	30	9	5	18	536	8.93	157		227	309	42.35	57.65
6	9	9	3	17	536	8.93	158		248	288	46.27	53.73
8	7	9	6	18	536	8.93	159		280	256	52.24	47.76
8	20	9	5	15	536	8.93	160		275	261	51.31	48.69
10	4	9	1	16	536	8.93	161	6002	241	295	44.96	55.04
10	4	9	1	19	536	8.93	162		232	304	43.28	56.72
10	23	9	6	16	536	8.93	163		294	242	54.85	45.15
4	3	9	6	15	535	8.91	164		257	278	48.04	51.96
7	16	9	5	17	535	8.91	165		226	309	42.24	57.76
7	24	9	6	18	535	8.91	166		272	263	50.84	49.16
10	5	9	2	17	535	8.91	167		258	277	48.22	51.78
11	13	9	6	18	535	8.91	168		248	287	46.36	53.64
2	27	9	6	16	534	8.9	169		245	289	45.88	54.12
4	30	9	5	17	534	8.9	170		248	286	46.44	53.56
5	12	9	3	18	534	8.9	171		230	304	43.07	56.93
5	28	9	5	18	534	8.9	172		240	294	44.94	55.06
9	28	9	2	17	534	8.9	173		258	276	48.31	51.69

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
12	4	9	6	16	534	8.9	174		297	237	55.62	44.38
4	9	9	5	17	533	8.88	175		238	295	44.65	55.35
5	21	9	5	18	533	8.88	176		249	284	46.72	53.28
8	12	9	4	17	533	8.88	177		257	276	48.22	51.78
10	30	9	6	16	533	8.88	178		271	262	50.84	49.16
5	15	9	6	14	532	8.86	179		269	263	50.56	49.44
6	9	9	3	18	532	8.86	180		232	300	43.61	56.39
8	13	9	5	17	532	8.86	181	6002	220	312	41.35	58.65
2	20	9	6	16	531	8.85	182		247	284	46.52	53.48
3	6	9	6	17	531	8.85	183		265	266	49.91	50.09
4	17	9	6	16	531	8.85	184		293	238	55.18	44.82
6	3	9	4	17	531	8.85	185		236	295	44.44	55.56
6	10	9	4	17	531	8.85	186		250	281	47.08	52.92
7	7	9	3	18	531	8.85	187		244	287	45.95	54.05
10	30	9	6	15	531	8.85	188		241	290	45.39	54.61
5	27	9	4	17	530	8.83	189		250	280	47.17	52.83
8	25	9	3	18	530	8.83	190		256	274	48.3	51.7
11	25	9	4	18	530	8.83	191		239	291	45.09	54.91
2	13	9	6	18	529	8.81	192		219	310	41.4	58.6
3	27	9	6	16	529	8.81	193		262	267	49.53	50.47
5	12	9	3	16	529	8.81	194		275	254	51.98	48.02
7	2	9	5	16	529	8.81	195		245	284	46.31	53.69
9	14	9	2	18	529	8.81	196		260	269	49.15	50.85
10	22	9	5	17	529	8.81	197		242	287	45.75	54.25
1	30	9	6	18	528	8.8	198		223	305	42.23	57.77
4	2	9	5	18	528	8.8	199		245	283	46.4	53.6
4	3	9	6	17	528	8.8	200		229	299	43.37	56.63

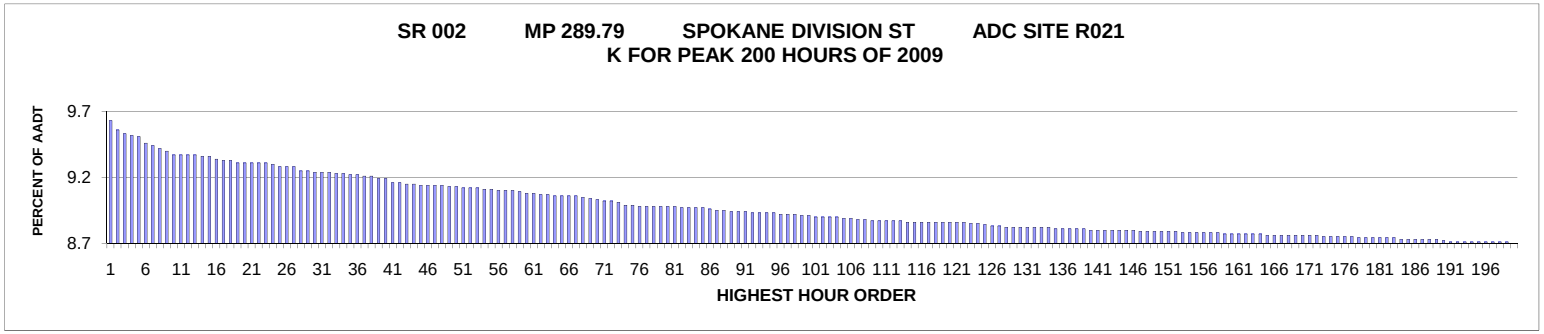

AADT= 42561 **K 30 FACTOR=** 9.24 **K 100 FACTOR=** 8.91 **K 200 FACTOR=** 8.7 **D FACTOR=** 56.63

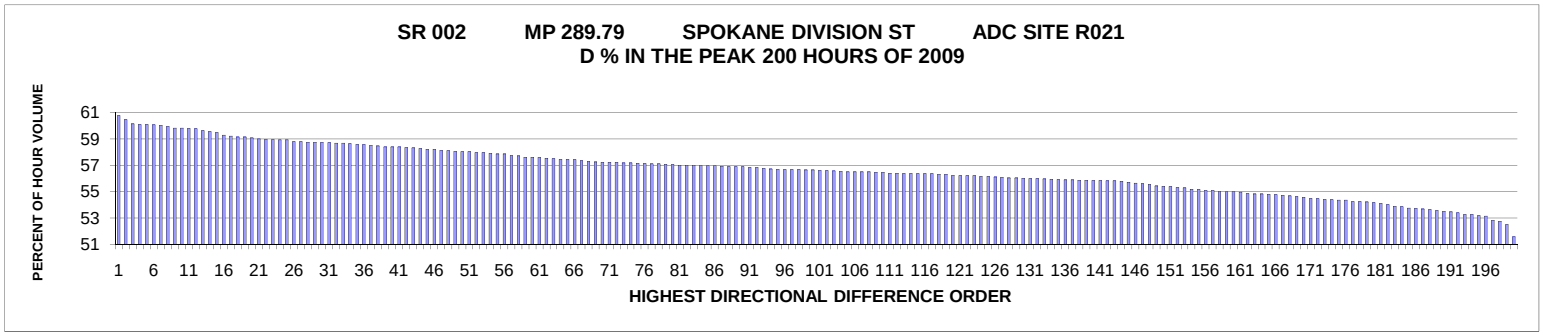

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
12	23	9	4	16	4099	9.63	1	42561	2342	1757	57.14	42.86
12	22	9	3	16	4067	9.56	2		2360	1707	58.03	41.97
11	20	9	6	16	4054	9.53	3		2306	1748	56.88	43.12
12	23	9	4	15	4051	9.52	4		2309	1742	57	43
12	4	9	6	16	4046	9.51	5		2274	1772	56.2	43.8
12	23	9	4	17	4028	9.46	6		2345	1683	58.22	41.78
9	4	9	6	16	4017	9.44	7		2307	1710	57.43	42.57
4	17	9	6	16	4010	9.42	8		2175	1835	54.24	45.76
12	11	9	6	16	3999	9.4	9		2244	1755	56.11	43.89
6	5	9	6	16	3990	9.37	10		2159	1831	54.11	45.89
12	18	9	6	15	3989	9.37	11		2226	1763	55.8	44.2
10	9	9	6	15	3988	9.37	12		2255	1733	56.54	43.46
5	8	9	6	16	3986	9.37	13		2133	1853	53.51	46.49
6	5	9	6	17	3985	9.36	14		2160	1825	54.2	45.8
12	21	9	2	16	3984	9.36	15		2283	1701	57.3	42.7
5	7	9	5	17	3975	9.34	16		2221	1754	55.87	44.13
12	22	9	3	17	3970	9.33	17		2304	1666	58.04	41.96

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
12	22	9	3	15	3969	9.33	18		2221	1748	55.96	44.04
2	13	9	6	16	3963	9.31	19		2172	1791	54.81	45.19
5	1	9	6	16	3963	9.31	20		2214	1749	55.87	44.13
8	14	9	6	15	3962	9.31	21	42561	2204	1758	55.63	44.37
12	4	9	6	15	3962	9.31	22		2242	1720	56.59	43.41
10	16	9	6	16	3961	9.31	23		2245	1716	56.68	43.32
12	4	9	6	17	3959	9.3	24		2286	1673	57.74	42.26
5	1	9	6	17	3949	9.28	25		2254	1695	57.08	42.92
11	20	9	6	17	3948	9.28	26		2246	1702	56.89	43.11
12	22	9	3	14	3948	9.28	27		2174	1774	55.07	44.93
4	24	9	6	16	3939	9.25	28		2207	1732	56.03	43.97
9	4	9	6	15	3936	9.25	29		2164	1772	54.98	45.02
4	10	9	6	16	3934	9.24	30		2238	1696	56.89	43.11
12	11	9	6	17	3934	9.24	31		2295	1639	58.34	41.66
12	17	9	5	16	3934	9.24	32		2217	1717	56.35	43.65
5	7	9	5	16	3930	9.23	33		2210	1720	56.23	43.77
10	16	9	6	17	3929	9.23	34		2239	1690	56.99	43.01
5	8	9	6	17	3925	9.22	35		2152	1773	54.83	45.17
10	2	9	6	16	3924	9.22	36		2210	1714	56.32	43.68
12	21	9	2	15	3920	9.21	37		2220	1700	56.63	43.37
10	9	9	6	16	3919	9.21	38		2146	1773	54.76	45.24
5	5	9	3	18	3913	9.19	39		2289	1624	58.5	41.5
12	23	9	4	14	3911	9.19	40		2262	1649	57.84	42.16
4	10	9	6	15	3899	9.16	41	42561	2197	1702	56.35	43.65
12	18	9	6	16	3897	9.16	42		2132	1765	54.71	45.29
5	14	9	5	18	3894	9.15	43		2219	1675	56.99	43.01
12	21	9	2	14	3894	9.15	44		2256	1638	57.94	42.06
12	21	9	2	17	3892	9.14	45		2328	1564	59.82	40.18
10	2	9	6	17	3890	9.14	46		2204	1686	56.66	43.34
8	7	9	6	16	3889	9.14	47		2200	1689	56.57	43.43
12	23	9	4	13	3889	9.14	48		2175	1714	55.93	44.07
5	14	9	5	17	3885	9.13	49		2257	1628	58.1	41.9
9	4	9	6	17	3884	9.13	50		2277	1607	58.63	41.37
2	13	9	6	15	3881	9.12	51		2158	1723	55.6	44.4
8	7	9	6	15	3880	9.12	52		2137	1743	55.08	44.92
10	30	9	6	16	3880	9.12	53		2186	1694	56.34	43.66
11	20	9	6	15	3878	9.11	54		2190	1688	56.47	43.53
10	2	9	6	15	3877	9.11	55		2190	1687	56.49	43.51
5	5	9	3	17	3875	9.1	56		2327	1548	60.05	39.95
10	30	9	6	15	3872	9.1	57		2187	1685	56.48	43.52
3	13	9	6	16	3871	9.1	58		2161	1710	55.83	44.17
5	15	9	6	16	3869	9.09	59		2103	1766	54.36	45.64
4	3	9	6	17	3865	9.08	60		2183	1682	56.48	43.52
12	22	9	3	13	3864	9.08	61	42561	2256	1608	58.39	41.61
5	8	9	6	15	3862	9.07	62		2124	1738	55	45
8	14	9	6	16	3859	9.07	63		2157	1702	55.9	44.1
6	5	9	6	18	3857	9.06	64		2168	1689	56.21	43.79
8	12	9	4	17	3857	9.06	65		2260	1597	58.59	41.41
12	18	9	6	17	3857	9.06	66		2294	1563	59.48	40.52
12	17	9	5	15	3855	9.06	67		2049	1806	53.15	46.85
5	8	9	6	18	3852	9.05	68		2202	1650	57.17	42.83
12	17	9	5	17	3847	9.04	69		2257	1590	58.67	41.33

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
12	16	9	4	17	3842	9.03	70		2275	1567	59.21	40.79
5	6	9	4	16	3841	9.02	71		2129	1712	55.43	44.57
12	10	9	5	17	3839	9.02	72		2256	1583	58.77	41.23
3	6	9	6	16	3834	9.01	73		2162	1672	56.39	43.61
8	28	9	6	15	3826	8.99	74		2115	1711	55.28	44.72
10	9	9	6	17	3825	8.99	75		2189	1636	57.23	42.77
4	24	9	6	17	3824	8.98	76		2239	1585	58.55	41.45
12	11	9	6	15	3824	8.98	77		2159	1665	56.46	43.54
2	21	9	7	14	3823	8.98	78		1971	1852	51.56	48.44
5	21	9	5	16	3823	8.98	79		2055	1768	53.75	46.25
5	22	9	6	16	3823	8.98	80		2140	1683	55.98	44.02
6	3	9	4	18	3822	8.98	81	42561	2266	1556	59.29	40.71
2	13	9	6	14	3819	8.97	82		2071	1748	54.23	45.77
4	10	9	6	17	3819	8.97	83		2253	1566	58.99	41.01
2	13	9	6	17	3818	8.97	84		2223	1595	58.22	41.78
4	3	9	6	16	3816	8.97	85		2182	1634	57.18	42.82
5	7	9	5	18	3814	8.96	86		2282	1532	59.83	40.17
3	13	9	6	17	3810	8.95	87		2194	1616	57.59	42.41
5	6	9	4	17	3809	8.95	88		2227	1582	58.47	41.53
10	24	9	7	14	3807	8.94	89		2121	1686	55.71	44.29
3	20	9	6	16	3806	8.94	90		2079	1727	54.62	45.38
5	1	9	6	14	3806	8.94	91		2086	1720	54.81	45.19
11	6	9	6	17	3802	8.93	92		2161	1641	56.84	43.16
11	20	9	6	14	3802	8.93	93		2039	1763	53.63	46.37
10	10	9	7	14	3801	8.93	94		2130	1671	56.04	43.96
5	22	9	6	15	3800	8.93	95		2074	1726	54.58	45.42
3	6	9	6	17	3797	8.92	96		2191	1606	57.7	42.3
5	29	9	6	16	3797	8.92	97		2040	1757	53.73	46.27
2	20	9	6	17	3796	8.92	98		2163	1633	56.98	43.02
11	6	9	6	16	3791	8.91	99		2147	1644	56.63	43.37
11	21	9	7	14	3791	8.91	100		2146	1645	56.61	43.39
5	15	9	6	15	3788	8.9	101	42561	2060	1728	54.38	45.62
2	20	9	6	16	3787	8.9	102		2135	1652	56.38	43.62
6	12	9	6	16	3786	8.9	103		2097	1689	55.39	44.61
10	2	9	6	14	3786	8.9	104		1997	1789	52.75	47.25
5	20	9	4	18	3784	8.89	105		2224	1560	58.77	41.23
12	4	9	6	14	3784	8.89	106		2092	1692	55.29	44.71
5	15	9	6	18	3780	8.88	107		2159	1621	57.12	42.88
5	1	9	6	18	3779	8.88	108		2284	1495	60.44	39.56
4	17	9	6	17	3777	8.87	109		2140	1637	56.66	43.34
5	20	9	4	17	3777	8.87	110		2216	1561	58.67	41.33
5	29	9	6	17	3777	8.87	111		2134	1643	56.5	43.5
10	30	9	6	17	3776	8.87	112		2140	1636	56.67	43.33
8	13	9	5	17	3775	8.87	113		2129	1646	56.4	43.6
8	12	9	4	16	3773	8.86	114		2107	1666	55.84	44.16
8	14	9	6	17	3773	8.86	115		2174	1599	57.62	42.38
2	21	9	7	15	3772	8.86	116		2016	1756	53.45	46.55
2	27	9	6	16	3772	8.86	117		2139	1633	56.71	43.29
5	1	9	6	15	3772	8.86	118		2202	1570	58.38	41.62
10	24	9	7	13	3771	8.86	119		2182	1589	57.86	42.14
8	7	9	6	14	3770	8.86	120		1991	1779	52.81	47.19
11	11	9	4	15	3770	8.86	121	42561	2012	1758	53.37	46.63

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	7	9	6	17	3769	8.86	122		2165	1604	57.44	42.56
5	15	9	6	17	3768	8.85	123		2186	1582	58.01	41.99
6	5	9	6	15	3767	8.85	124		2022	1745	53.68	46.32
5	9	9	7	13	3761	8.84	125		2044	1717	54.35	45.65
8	28	9	6	16	3758	8.83	126		2066	1692	54.98	45.02
10	24	9	7	15	3758	8.83	127		2001	1757	53.25	46.75
2	13	9	6	13	3756	8.82	128		2096	1660	55.8	44.2
10	15	9	5	17	3756	8.82	129		2237	1519	59.56	40.44
6	3	9	4	17	3755	8.82	130		2156	1599	57.42	42.58
6	1	9	2	17	3754	8.82	131		2174	1580	57.91	42.09
9	3	9	5	17	3754	8.82	132		2220	1534	59.14	40.86
5	15	9	6	14	3753	8.82	133		1999	1754	53.26	46.74
6	4	9	5	17	3752	8.82	134		2204	1548	58.74	41.26
9	1	9	3	17	3751	8.81	135		2280	1471	60.78	39.22
5	8	9	6	13	3750	8.81	136		1968	1782	52.48	47.52
12	21	9	2	13	3750	8.81	137		2128	1622	56.75	43.25
5	14	9	5	16	3749	8.81	138		2061	1688	54.97	45.03
8	21	9	6	15	3748	8.81	139		2105	1643	56.16	43.84
9	25	9	6	15	3747	8.8	140		2094	1653	55.88	44.12
12	4	9	6	13	3747	8.8	141	42561	2038	1709	54.39	45.61
10	16	9	6	15	3746	8.8	142		2066	1680	55.15	44.85
5	2	9	7	14	3745	8.8	143		2005	1740	53.54	46.46
8	28	9	6	17	3745	8.8	144		2132	1613	56.93	43.07
12	10	9	5	16	3745	8.8	145		2100	1645	56.07	43.93
5	21	9	5	17	3744	8.8	146		2206	1538	58.92	41.08
12	18	9	6	13	3743	8.79	147		2137	1606	57.09	42.91
6	11	9	5	17	3742	8.79	148		2151	1591	57.48	42.52
11	25	9	4	16	3742	8.79	149		2185	1557	58.39	41.61
12	2	9	4	16	3742	8.79	150		2131	1611	56.95	43.05
10	1	9	5	17	3740	8.79	151		2205	1535	58.96	41.04
10	30	9	6	18	3739	8.79	152		2151	1588	57.53	42.47
5	21	9	5	18	3738	8.78	153		2202	1536	58.91	41.09
8	24	9	2	16	3737	8.78	154		2138	1599	57.21	42.79
5	13	9	4	18	3736	8.78	155		2239	1497	59.93	40.07
6	9	9	3	18	3736	8.78	156		2244	1492	60.06	39.94
5	9	9	7	12	3735	8.78	157		2206	1529	59.06	40.94
8	13	9	5	15	3735	8.78	158		2042	1693	54.67	45.33
4	10	9	6	14	3734	8.77	159		2046	1688	54.79	45.21
12	17	9	5	14	3732	8.77	160		2059	1673	55.17	44.83
12	22	9	3	12	3732	8.77	161	42561	2073	1659	55.55	44.45
6	2	9	3	17	3731	8.77	162		2162	1569	57.95	42.05
8	31	9	2	17	3731	8.77	163		2244	1487	60.14	39.86
11	14	9	7	14	3731	8.77	164		2009	1722	53.85	46.15
8	21	9	6	17	3730	8.76	165		2088	1642	55.98	44.02
9	3	9	5	16	3730	8.76	166		2124	1606	56.94	43.06
12	2	9	4	17	3730	8.76	167		2224	1506	59.62	40.38
3	20	9	6	17	3729	8.76	168		2119	1610	56.82	43.18
8	27	9	5	17	3729	8.76	169		2167	1562	58.11	41.89
8	31	9	2	16	3729	8.76	170		2102	1627	56.37	43.63
4	3	9	6	15	3728	8.76	171		2095	1633	56.2	43.8
12	16	9	4	16	3727	8.76	172		2093	1634	56.16	43.84
2	27	9	6	17	3726	8.75	173		2132	1594	57.22	42.78

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
12	3	9	5	16	3726	8.75	174		2127	1599	57.09	42.91
11	6	9	6	18	3725	8.75	175		2187	1538	58.71	41.29
11	20	9	6	18	3724	8.75	176		2132	1592	57.25	42.75
9	10	9	5	17	3722	8.75	177		2201	1521	59.13	40.87
5	22	9	6	17	3721	8.74	178		2134	1587	57.35	42.65
10	10	9	7	15	3721	8.74	179		2026	1695	54.45	45.55
8	26	9	4	17	3720	8.74	180		2235	1485	60.08	39.92
8	21	9	6	14	3719	8.74	181	42561	1976	1743	53.13	46.87
10	16	9	6	18	3719	8.74	182		2167	1552	58.27	41.73
6	10	9	4	16	3718	8.74	183		2094	1624	56.32	43.68
5	6	9	4	18	3717	8.73	184		2183	1534	58.73	41.27
9	25	9	6	16	3717	8.73	185		2058	1659	55.37	44.63
6	9	9	3	17	3716	8.73	186		2141	1575	57.62	42.38
4	24	9	6	18	3714	8.73	187		2166	1548	58.32	41.68
5	27	9	4	17	3714	8.73	188		2182	1532	58.75	41.25
9	8	9	3	16	3714	8.73	189		2072	1642	55.79	44.21
10	23	9	6	17	3711	8.72	190		2117	1594	57.05	42.95
5	5	9	3	16	3709	8.71	191		2077	1632	56	44
11	24	9	3	16	3709	8.71	192		2073	1636	55.89	44.11
5	28	9	5	18	3708	8.71	193		2216	1492	59.76	40.24
9	4	9	6	14	3707	8.71	194		2002	1705	54.01	45.99
7	24	9	6	15	3706	8.71	195		2007	1699	54.16	45.84
9	22	9	3	17	3706	8.71	196		2227	1479	60.09	39.91
10	10	9	7	13	3706	8.71	197		2216	1490	59.79	40.21
10	16	9	6	14	3705	8.71	198		2018	1687	54.47	45.53
10	17	9	7	15	3705	8.71	199		1997	1708	53.9	46.1
8	5	9	4	17	3704	8.7	200		2183	1521	58.94	41.06

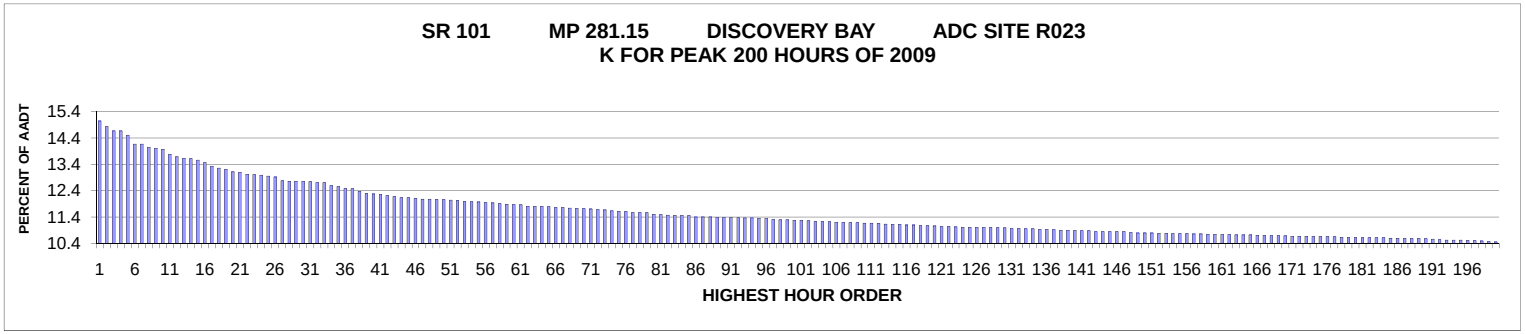

AADT= 10913 **K 30 FACTOR=** 12.76 **K 100 FACTOR=** 11.27 **K 200 FACTOR=** 10.45 **D FACTOR=** 56.34

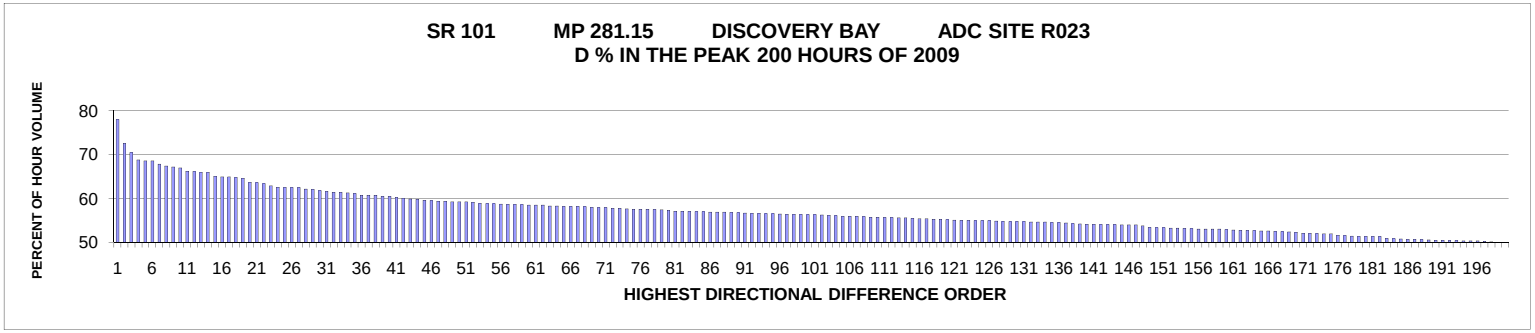

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	18	9	7	12	1641	15.04	1	10913	1125	516	68.56	31.44
7	17	9	6	18	1619	14.84	2		778	841	48.05	51.95
7	19	9	1	12	1601	14.67	3		995	606	62.15	37.85
7	19	9	1	13	1601	14.67	4		875	726	54.65	45.35
7	18	9	7	14	1584	14.51	5		933	651	58.9	41.1
7	26	9	1	17	1546	14.17	6		681	865	44.05	55.95
7	19	9	1	17	1545	14.16	7		636	909	41.17	58.83
7	18	9	7	11	1533	14.05	8		1113	420	72.6	27.4
7	18	9	7	17	1529	14.01	9		619	910	40.48	59.52
7	26	9	1	16	1525	13.97	10		741	784	48.59	51.41
7	19	9	1	14	1504	13.78	11		715	789	47.54	52.46
7	18	9	7	15	1493	13.68	12		820	673	54.92	45.08
8	16	9	1	17	1487	13.63	13		621	866	41.76	58.24
7	17	9	6	12	1485	13.61	14		1018	467	68.55	31.45
7	19	9	1	15	1480	13.56	15		598	882	40.41	59.59
8	23	9	1	16	1469	13.46	16		563	906	38.33	61.67
7	18	9	7	13	1455	13.33	17		981	474	67.42	32.58

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	17	9	6	16	1447	13.26	18		730	717	50.45	49.55
7	18	9	7	16	1442	13.21	19		628	814	43.55	56.45
7	5	9	1	13	1431	13.11	20		643	788	44.93	55.07
7	18	9	7	18	1430	13.1	21	10913	501	929	35.03	64.97
7	19	9	1	16	1421	13.02	22		480	941	33.78	66.22
7	17	9	6	15	1419	13	23		746	673	52.57	47.43
7	26	9	1	12	1418	12.99	24		708	710	49.93	50.07
8	16	9	1	14	1413	12.95	25		606	807	42.89	57.11
7	17	9	6	14	1410	12.92	26		775	635	54.96	45.04
7	5	9	1	14	1394	12.77	27		506	888	36.3	63.7
8	23	9	1	17	1393	12.76	28		486	907	34.89	65.11
8	2	9	1	14	1392	12.76	29		599	793	43.03	56.97
8	2	9	1	15	1392	12.76	30		591	801	42.46	57.54
7	5	9	1	15	1389	12.73	31		531	858	38.23	61.77
8	14	9	6	16	1385	12.69	32		790	595	57.04	42.96
8	23	9	1	15	1385	12.69	33		597	788	43.1	56.9
8	9	9	1	14	1373	12.58	34		595	778	43.34	56.66
7	17	9	6	11	1370	12.55	35		907	463	66.2	33.8
7	19	9	1	19	1362	12.48	36		447	915	32.82	67.18
8	16	9	1	15	1361	12.47	37		617	744	45.33	54.67
8	9	9	1	15	1350	12.37	38		662	688	49.04	50.96
8	16	9	1	18	1342	12.3	39		595	747	44.34	55.66
8	2	9	1	17	1339	12.27	40		502	837	37.49	62.51
7	26	9	1	13	1338	12.26	41	10913	662	676	49.48	50.52
7	31	9	6	17	1333	12.21	42		743	590	55.74	44.26
7	18	9	7	10	1328	12.17	43		901	427	67.85	32.15
7	31	9	6	18	1324	12.13	44		750	574	56.65	43.35
8	22	9	7	12	1324	12.13	45		743	581	56.12	43.88
7	26	9	1	14	1321	12.1	46		490	831	37.09	62.91
7	2	9	5	16	1318	12.08	47		760	558	57.66	42.34
7	24	9	6	15	1317	12.07	48		747	570	56.72	43.28
8	23	9	1	14	1316	12.06	49		526	790	39.97	60.03
8	2	9	1	12	1315	12.05	50		651	664	49.51	50.49
8	16	9	1	16	1314	12.04	51		574	740	43.68	56.32
7	19	9	1	18	1313	12.03	52		447	866	34.04	65.96
7	3	9	6	15	1308	11.99	53		767	541	58.64	41.36
7	17	9	6	17	1307	11.98	54		547	760	41.85	58.15
8	15	9	7	12	1305	11.96	55		714	591	54.71	45.29
8	30	9	1	17	1303	11.94	56		553	750	42.44	57.56
7	26	9	1	18	1302	11.93	57		531	771	40.78	59.22
7	17	9	6	19	1299	11.9	58		610	689	46.96	53.04
7	3	9	6	12	1296	11.88	59		855	441	65.97	34.03
8	1	9	7	12	1295	11.87	60		710	585	54.83	45.17
7	24	9	6	18	1294	11.86	61	10913	730	564	56.41	43.59
7	31	9	6	15	1289	11.81	62		684	605	53.06	46.94
8	7	9	6	15	1289	11.81	63		672	617	52.13	47.87
8	8	9	7	12	1288	11.8	64		707	581	54.89	45.11
8	23	9	1	13	1286	11.78	65		592	694	46.03	53.97
7	25	9	7	12	1283	11.76	66		773	510	60.25	39.75
8	1	9	7	13	1283	11.76	67		711	572	55.42	44.58
8	21	9	6	16	1281	11.74	68		716	565	55.89	44.11
7	17	9	6	13	1279	11.72	69		801	478	62.63	37.37

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	25	9	7	16	1278	11.71	70		702	576	54.93	45.07
8	2	9	1	16	1277	11.7	71		537	740	42.05	57.95
8	2	9	1	18	1275	11.68	72		492	783	38.59	61.41
8	30	9	1	14	1273	11.66	73		499	774	39.2	60.8
8	21	9	6	15	1268	11.62	74		744	524	58.68	41.32
8	21	9	6	18	1267	11.61	75		685	582	54.06	45.94
8	15	9	7	16	1266	11.6	76		662	604	52.29	47.71
7	17	9	6	10	1261	11.56	77		868	393	68.83	31.17
8	1	9	7	15	1261	11.56	78		672	589	53.29	46.71
8	2	9	1	13	1260	11.55	79		571	689	45.32	54.68
7	5	9	1	17	1255	11.5	80		503	752	40.08	59.92
7	18	9	7	21	1253	11.48	81	10913	276	977	22.03	77.97
7	16	9	5	16	1252	11.47	82		729	523	58.23	41.77
7	24	9	6	16	1249	11.45	83		695	554	55.64	44.36
9	18	9	6	17	1249	11.45	84		732	517	58.61	41.39
8	16	9	1	13	1248	11.44	85		586	662	46.96	53.04
8	14	9	6	17	1244	11.4	86		661	583	53.14	46.86
8	16	9	1	12	1244	11.4	87		581	663	46.7	53.3
9	11	9	6	16	1244	11.4	88		696	548	55.95	44.05
7	25	9	7	13	1242	11.38	89		727	515	58.53	41.47
8	30	9	1	15	1242	11.38	90		507	735	40.82	59.18
9	13	9	1	18	1242	11.38	91		519	723	41.79	58.21
7	30	9	5	15	1241	11.37	92		600	641	48.35	51.65
7	31	9	6	14	1240	11.36	93		638	602	51.45	48.55
9	12	9	7	12	1240	11.36	94		704	536	56.77	43.23
8	15	9	7	13	1239	11.35	95		687	552	55.45	44.55
7	10	9	6	15	1237	11.34	96		718	519	58.04	41.96
7	12	9	1	14	1233	11.3	97		487	746	39.5	60.5
7	3	9	6	16	1232	11.29	98		681	551	55.28	44.72
8	1	9	7	17	1232	11.29	99		625	607	50.73	49.27
8	9	9	1	17	1230	11.27	100		501	729	40.73	59.27
8	14	9	6	15	1230	11.27	101	10913	717	513	58.29	41.71
7	5	9	1	12	1228	11.25	102		477	751	38.84	61.16
8	23	9	1	12	1225	11.23	103		588	637	48	52
8	14	9	6	13	1224	11.22	104		703	521	57.43	42.57
8	28	9	6	15	1223	11.21	105		697	526	56.99	43.01
8	21	9	6	17	1222	11.2	106		681	541	55.73	44.27
8	28	9	6	18	1221	11.19	107		680	541	55.69	44.31
8	15	9	7	14	1220	11.18	108		659	561	54.02	45.98
9	4	9	6	16	1219	11.17	109		688	531	56.44	43.56
7	24	9	6	14	1218	11.16	110		626	592	51.4	48.6
8	22	9	7	17	1218	11.16	111		638	580	52.38	47.62
8	9	9	1	12	1217	11.15	112		546	671	44.86	55.14
8	22	9	7	16	1215	11.13	113		609	606	50.12	49.88
7	3	9	6	14	1214	11.12	114		746	468	61.45	38.55
8	7	9	6	17	1214	11.12	115		657	557	54.12	45.88
8	30	9	1	16	1210	11.09	116		516	694	42.64	57.36
9	11	9	6	18	1210	11.09	117		654	556	54.05	45.95
6	27	9	7	16	1208	11.07	118		704	504	58.28	41.72
8	30	9	1	18	1208	11.07	119		439	769	36.34	63.66
8	28	9	6	16	1206	11.05	120		697	509	57.79	42.21
7	16	9	5	15	1204	11.03	121	10913	650	554	53.99	46.01

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	8	9	7	14	1204	11.03	122		609	595	50.58	49.42
6	28	9	1	17	1203	11.02	123		609	594	50.62	49.38
8	1	9	7	11	1202	11.01	124		684	518	56.91	43.09
8	9	9	1	16	1202	11.01	125		529	673	44.01	55.99
11	27	9	6	14	1202	11.01	126		605	597	50.33	49.67
8	22	9	7	13	1201	11.01	127		703	498	58.53	41.47
8	7	9	6	16	1199	10.99	128		664	535	55.38	44.62
8	30	9	1	13	1199	10.99	129		495	704	41.28	58.72
7	25	9	7	14	1198	10.98	130		659	539	55.01	44.99
6	21	9	1	14	1196	10.96	131		505	691	42.22	57.78
8	21	9	6	14	1196	10.96	132		607	589	50.75	49.25
8	15	9	7	11	1195	10.95	133		651	544	54.48	45.52
7	3	9	6	13	1194	10.94	134		732	462	61.31	38.69
7	3	9	6	17	1192	10.92	135		612	580	51.34	48.66
7	10	9	6	14	1192	10.92	136		678	514	56.88	43.12
8	9	9	1	18	1191	10.91	137		484	707	40.64	59.36
7	12	9	1	16	1189	10.9	138		490	699	41.21	58.79
8	22	9	7	14	1189	10.9	139		668	521	56.18	43.82
8	23	9	1	18	1188	10.89	140		435	753	36.62	63.38
7	25	9	7	11	1186	10.87	141	10913	717	469	60.46	39.54
8	15	9	7	15	1186	10.87	142		646	540	54.47	45.53
7	3	9	6	11	1183	10.84	143		765	418	64.67	35.33
8	7	9	6	13	1183	10.84	144		622	561	52.58	47.42
8	20	9	5	15	1183	10.84	145		610	573	51.56	48.44
7	25	9	7	15	1182	10.83	146		636	546	53.81	46.19
10	10	9	7	12	1182	10.83	147		792	390	67.01	32.99
9	11	9	6	17	1179	10.8	148		594	585	50.38	49.62
9	12	9	7	15	1178	10.79	149		666	512	56.54	43.46
4	26	9	1	17	1177	10.79	150		551	626	46.81	53.19
8	8	9	7	13	1177	10.79	151		638	539	54.21	45.79
7	12	9	1	15	1176	10.78	152		500	676	42.52	57.48
8	1	9	7	16	1176	10.78	153		622	554	52.89	47.11
8	21	9	6	12	1174	10.76	154		636	538	54.17	45.83
8	28	9	6	14	1174	10.76	155		603	571	51.36	48.64
10	11	9	1	17	1174	10.76	156		413	761	35.18	64.82
7	19	9	1	11	1173	10.75	157		617	556	52.6	47.4
7	24	9	6	12	1173	10.75	158		662	511	56.44	43.56
8	8	9	7	15	1172	10.74	159		618	554	52.73	47.27
9	12	9	7	14	1172	10.74	160		625	547	53.33	46.67
7	19	9	1	20	1171	10.73	161	10913	346	825	29.55	70.45
8	7	9	6	18	1171	10.73	162		596	575	50.9	49.1
8	7	9	6	14	1170	10.72	163		545	625	46.58	53.42
9	13	9	1	15	1170	10.72	164		492	678	42.05	57.95
8	22	9	7	11	1169	10.71	165		668	501	57.14	42.86
7	12	9	1	13	1168	10.7	166		476	692	40.75	59.25
9	7	9	2	14	1168	10.7	167		458	710	39.21	60.79
8	1	9	7	14	1167	10.69	168		616	551	52.78	47.22
9	12	9	7	13	1167	10.69	169		683	484	58.53	41.47
7	5	9	1	16	1166	10.68	170		457	709	39.19	60.81
9	4	9	6	18	1164	10.67	171		613	551	52.66	47.34
6	27	9	7	12	1163	10.66	172		727	436	62.51	37.49
8	9	9	1	13	1163	10.66	173		467	696	40.15	59.85

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	25	9	7	18	1162	10.65	174		557	605	47.93	52.07
9	5	9	7	12	1162	10.65	175		690	472	59.38	40.62
9	12	9	7	16	1162	10.65	176		636	526	54.73	45.27
7	30	9	5	16	1161	10.64	177		584	577	50.3	49.7
12	26	9	7	13	1160	10.63	178		615	545	53.02	46.98
7	11	9	7	16	1159	10.62	179		602	557	51.94	48.06
9	4	9	6	17	1159	10.62	180		627	532	54.1	45.9
8	15	9	7	17	1158	10.61	181	10913	570	588	49.22	50.78
8	30	9	1	19	1158	10.61	182		439	719	37.91	62.09
9	13	9	1	17	1158	10.61	183		491	667	42.4	57.6
9	13	9	1	16	1157	10.6	184		506	651	43.73	56.27
7	26	9	1	19	1156	10.59	185		405	751	35.03	64.97
8	28	9	6	17	1156	10.59	186		636	520	55.02	44.98
7	31	9	6	13	1155	10.58	187		632	523	54.72	45.28
7	31	9	6	16	1155	10.58	188		578	577	50.04	49.96
9	12	9	7	17	1155	10.58	189		582	573	50.39	49.61
9	25	9	6	17	1153	10.57	190		544	609	47.18	52.82
7	10	9	6	16	1152	10.56	191		649	503	56.34	43.66
8	8	9	7	16	1149	10.53	192		613	536	53.35	46.65
7	2	9	5	17	1148	10.52	193		579	569	50.44	49.56
7	10	9	6	17	1148	10.52	194		626	522	54.53	45.47
7	11	9	7	12	1148	10.52	195		718	430	62.54	37.46
8	21	9	6	13	1147	10.51	196		638	509	55.62	44.38
9	20	9	1	14	1145	10.49	197		512	633	44.72	55.28
8	16	9	1	11	1144	10.48	198		523	621	45.72	54.28
9	13	9	1	14	1142	10.46	199		492	650	43.08	56.92
6	28	9	1	14	1140	10.45	200		495	645	43.42	56.58

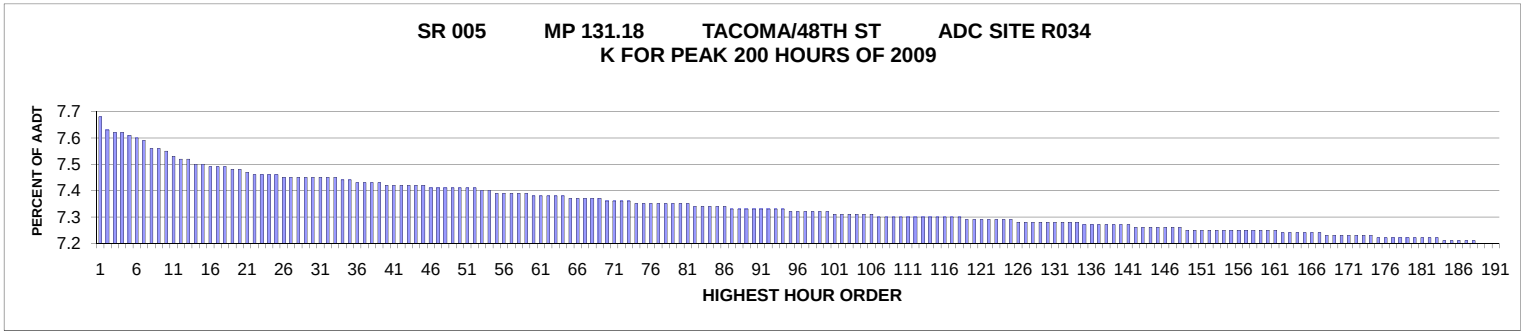

AADT= 185645 **K 30 FACTOR=** 7.45 **K 100 FACTOR=** 7.33 **K 200 FACTOR=** 7.2 **D FACTOR=** 53.39

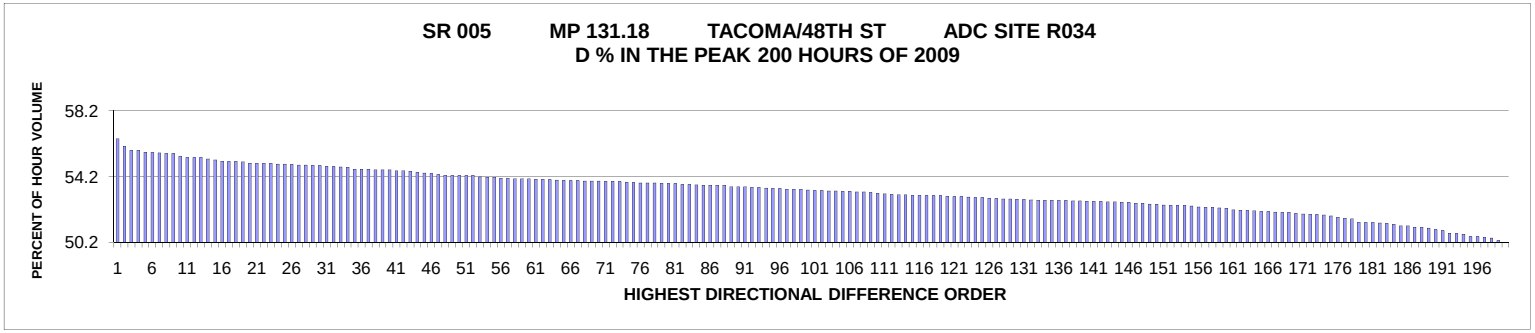

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
2	13	9	6	15	14266	7.68	1	185645	6765	7501	47.42	52.58
4	16	9	5	16	14165	7.63	2		6630	7535	46.81	53.19
1	15	9	5	16	14148	7.62	3		6393	7755	45.19	54.81
4	15	9	4	16	14140	7.62	4		6686	7454	47.28	52.72
2	20	9	6	15	14124	7.61	5		6775	7349	47.97	52.03
1	23	9	6	16	14114	7.6	6		6523	7591	46.22	53.78
1	16	9	6	16	14082	7.59	7		6804	7278	48.32	51.68
2	12	9	5	16	14035	7.56	8		6329	7706	45.09	54.91
4	8	9	4	16	14030	7.56	9		6464	7566	46.07	53.93
4	30	9	5	16	14025	7.55	10		6588	7437	46.97	53.03
5	20	9	4	16	13979	7.53	11		6575	7404	47.03	52.97
4	23	9	5	17	13966	7.52	12		6380	7586	45.68	54.32
1	23	9	6	15	13955	7.52	13		6395	7560	45.83	54.17
1	22	9	5	17	13930	7.5	14		6299	7631	45.22	54.78
2	13	9	6	16	13917	7.5	15		6503	7414	46.73	53.27
3	6	9	6	15	13911	7.49	16		6628	7283	47.65	52.35
4	9	9	5	16	13910	7.49	17		6559	7351	47.15	52.85

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
1	30	9	6	16	13909	7.49	18		6655	7254	47.85	52.15
1	14	9	4	16	13892	7.48	19		6162	7730	44.36	55.64
4	24	9	6	15	13883	7.48	20		6575	7308	47.36	52.64
3	18	9	4	16	13873	7.47	21	185645	6440	7433	46.42	53.58
2	20	9	6	16	13858	7.46	22		6640	7218	47.91	52.09
1	22	9	5	16	13848	7.46	23		6202	7646	44.79	55.21
1	21	9	4	17	13843	7.46	24		6246	7597	45.12	54.88
4	7	9	3	16	13842	7.46	25		6375	7467	46.06	53.94
1	16	9	6	15	13838	7.45	26		6522	7316	47.13	52.87
11	13	9	6	16	13838	7.45	27		6551	7287	47.34	52.66
6	25	9	5	16	13837	7.45	28		6638	7199	47.97	52.03
2	3	9	3	17	13836	7.45	29		6226	7610	45	55
5	8	9	6	16	13834	7.45	30		6767	7067	48.92	51.08
3	27	9	6	15	13830	7.45	31		6748	7082	48.79	51.21
4	15	9	4	17	13827	7.45	32		6405	7422	46.32	53.68
12	18	9	6	15	13822	7.45	33		6571	7251	47.54	52.46
5	12	9	3	17	13815	7.44	34		6395	7420	46.29	53.71
1	21	9	4	16	13814	7.44	35		6106	7708	44.2	55.8
4	29	9	4	16	13799	7.43	36		6207	7592	44.98	55.02
2	12	9	5	17	13798	7.43	37		6263	7535	45.39	54.61
5	7	9	5	16	13791	7.43	38		6351	7440	46.05	53.95
2	5	9	5	16	13787	7.43	39		6253	7534	45.35	54.65
1	23	9	6	17	13782	7.42	40		6509	7273	47.23	52.77
11	25	9	4	13	13780	7.42	41	185645	6693	7087	48.57	51.43
3	18	9	4	17	13779	7.42	42		6224	7555	45.17	54.83
4	22	9	4	16	13779	7.42	43		6350	7429	46.08	53.92
6	5	9	6	15	13769	7.42	44		6809	6960	49.45	50.55
3	27	9	6	16	13767	7.42	45		6536	7231	47.48	52.52
4	17	9	6	16	13761	7.41	46		6724	7037	48.86	51.14
1	15	9	5	17	13760	7.41	47		6189	7571	44.98	55.02
1	30	9	6	15	13759	7.41	48		6524	7235	47.42	52.58
2	3	9	3	16	13753	7.41	49		6094	7659	44.31	55.69
2	27	9	6	15	13753	7.41	50		6560	7193	47.7	52.3
2	17	9	3	16	13751	7.41	51		6287	7464	45.72	54.28
10	22	9	5	16	13750	7.41	52		6463	7287	47	53
8	13	9	5	15	13747	7.4	53		6682	7065	48.61	51.39
5	8	9	6	15	13736	7.4	54		6798	6938	49.49	50.51
2	13	9	6	14	13724	7.39	55		6904	6820	50.31	49.69
1	13	9	3	16	13719	7.39	56		6030	7689	43.95	56.05
12	3	9	5	16	13716	7.39	57		6442	7274	46.97	53.03
2	5	9	5	17	13712	7.39	58		6329	7383	46.16	53.84
4	30	9	5	17	13710	7.39	59		6306	7404	46	54
4	22	9	4	17	13708	7.38	60		6270	7438	45.74	54.26
2	19	9	5	16	13701	7.38	61	185645	6289	7412	45.9	54.1
4	10	9	6	17	13701	7.38	62		6456	7245	47.12	52.88
5	5	9	3	17	13695	7.38	63		6210	7485	45.35	54.65
1	14	9	4	17	13692	7.38	64		6147	7545	44.89	55.11
8	5	9	4	16	13690	7.37	65		6499	7191	47.47	52.53
5	12	9	3	16	13689	7.37	66		6388	7301	46.67	53.33
1	28	9	4	17	13687	7.37	67		6067	7620	44.33	55.67
10	29	9	5	16	13681	7.37	68		6371	7310	46.57	53.43
5	15	9	6	15	13677	7.37	69		6713	6964	49.08	50.92

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
2	2	9	2	16	13669	7.36	70		6159	7510	45.06	54.94
6	5	9	6	16	13659	7.36	71		6565	7094	48.06	51.94
6	11	9	5	16	13658	7.36	72		6446	7212	47.2	52.8
3	24	9	3	17	13657	7.36	73		6098	7559	44.65	55.35
10	2	9	6	16	13653	7.35	74		6516	7137	47.73	52.27
3	25	9	4	17	13651	7.35	75		6336	7315	46.41	53.59
6	10	9	4	16	13651	7.35	76		6437	7214	47.15	52.85
4	7	9	3	17	13649	7.35	77		6126	7523	44.88	55.12
2	6	9	6	15	13648	7.35	78		6545	7103	47.96	52.04
5	1	9	6	15	13648	7.35	79		6750	6898	49.46	50.54
3	26	9	5	16	13646	7.35	80		6532	7114	47.87	52.13
4	28	9	3	17	13642	7.35	81	185645	6151	7491	45.09	54.91
4	16	9	5	17	13632	7.34	82		6197	7435	45.46	54.54
4	8	9	4	17	13630	7.34	83		6295	7335	46.18	53.82
10	1	9	5	16	13628	7.34	84		6441	7187	47.26	52.74
1	2	9	6	15	13626	7.34	85		6439	7187	47.26	52.74
4	27	9	2	16	13624	7.34	86		6294	7330	46.2	53.8
8	11	9	3	17	13616	7.33	87		6267	7349	46.03	53.97
10	9	9	6	15	13616	7.33	88		6546	7070	48.08	51.92
3	13	9	6	15	13615	7.33	89		6432	7183	47.24	52.76
6	11	9	5	18	13615	7.33	90		6472	7143	47.54	52.46
1	26	9	2	16	13614	7.33	91		6157	7457	45.23	54.77
4	1	9	4	16	13609	7.33	92		6207	7402	45.61	54.39
1	28	9	4	16	13607	7.33	93		6076	7531	44.65	55.35
10	30	9	6	15	13606	7.33	94		6363	7243	46.77	53.23
9	24	9	5	16	13596	7.32	95		6401	7195	47.08	52.92
11	25	9	4	14	13595	7.32	96		6769	6826	49.79	50.21
11	13	9	6	15	13594	7.32	97		6504	7090	47.84	52.16
10	30	9	6	16	13583	7.32	98		6512	7071	47.94	52.06
4	21	9	3	17	13581	7.32	99		6239	7342	45.94	54.06
10	8	9	5	16	13580	7.32	100		6319	7261	46.53	53.47
10	28	9	4	17	13575	7.31	101	185645	6274	7301	46.22	53.78
5	18	9	2	16	13574	7.31	102		6541	7033	48.19	51.81
10	9	9	6	16	13574	7.31	103		6534	7040	48.14	51.86
4	14	9	3	16	13572	7.31	104		6025	7547	44.39	55.61
9	30	9	4	17	13571	7.31	105		6333	7238	46.67	53.33
8	14	9	6	13	13563	7.31	106		6686	6877	49.3	50.7
10	28	9	4	16	13561	7.3	107		6326	7235	46.65	53.35
1	16	9	6	14	13556	7.3	108		6383	7173	47.09	52.91
4	9	9	5	17	13556	7.3	109		6365	7191	46.95	53.05
5	7	9	5	17	13554	7.3	110		6413	7141	47.31	52.69
3	4	9	4	16	13553	7.3	111		6086	7467	44.91	55.09
6	11	9	5	17	13553	7.3	112		6460	7093	47.66	52.34
1	12	9	2	16	13552	7.3	113		6102	7450	45.03	54.97
8	11	9	3	16	13551	7.3	114		6409	7142	47.3	52.7
3	30	9	2	17	13549	7.3	115		6158	7391	45.45	54.55
6	2	9	3	17	13546	7.3	116		6301	7245	46.52	53.48
4	10	9	6	16	13545	7.3	117		6552	6993	48.37	51.63
5	1	9	6	16	13543	7.3	118		6608	6935	48.79	51.21
4	28	9	3	16	13542	7.29	119		6111	7431	45.13	54.87
2	11	9	4	16	13540	7.29	120		6057	7483	44.73	55.27
3	25	9	4	16	13539	7.29	121	185645	6145	7394	45.39	54.61

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
2	13	9	6	17	13538	7.29	122		6472	7066	47.81	52.19
11	4	9	4	16	13536	7.29	123		6509	7027	48.09	51.91
9	9	9	4	17	13535	7.29	124		6315	7220	46.66	53.34
8	7	9	6	13	13533	7.29	125		6830	6703	50.47	49.53
6	25	9	5	18	13521	7.28	126		6275	7246	46.41	53.59
9	15	9	3	16	13521	7.28	127		6320	7201	46.74	53.26
3	31	9	3	16	13519	7.28	128		6025	7494	44.57	55.43
10	27	9	3	16	13519	7.28	129		6287	7232	46.5	53.5
10	7	9	4	16	13518	7.28	130		6221	7297	46.02	53.98
2	26	9	5	16	13517	7.28	131		6208	7309	45.93	54.07
3	27	9	6	14	13514	7.28	132		6656	6858	49.25	50.75
4	21	9	3	16	13512	7.28	133		6205	7307	45.92	54.08
6	10	9	4	17	13512	7.28	134		6279	7233	46.47	53.53
8	17	9	2	16	13505	7.27	135		6233	7272	46.15	53.85
10	13	9	3	17	13504	7.27	136		6157	7347	45.59	54.41
2	2	9	2	17	13500	7.27	137		6081	7419	45.04	54.96
3	6	9	6	16	13500	7.27	138		6516	6984	48.27	51.73
3	11	9	4	17	13500	7.27	139		6224	7276	46.1	53.9
8	10	9	2	16	13494	7.27	140		6385	7109	47.32	52.68
6	1	9	2	16	13493	7.27	141	185645	6328	7165	46.9	53.1
5	19	9	3	18	13487	7.26	142		6281	7206	46.57	53.43
1	2	9	6	16	13479	7.26	143		6413	7066	47.58	52.42
8	5	9	4	15	13479	7.26	144		6550	6929	48.59	51.41
4	23	9	5	16	13471	7.26	145		6291	7180	46.7	53.3
5	27	9	4	17	13471	7.26	146		6193	7278	45.97	54.03
2	27	9	6	16	13470	7.26	147		6335	7135	47.03	52.97
12	22	9	3	16	13469	7.26	148		6204	7265	46.06	53.94
2	6	9	6	16	13464	7.25	149		6320	7144	46.94	53.06
1	9	9	6	16	13463	7.25	150		6185	7278	45.94	54.06
2	17	9	3	17	13463	7.25	151		6188	7275	45.96	54.04
4	1	9	4	17	13462	7.25	152		6171	7291	45.84	54.16
5	20	9	4	17	13462	7.25	153		6011	7451	44.65	55.35
12	18	9	6	16	13460	7.25	154		6545	6915	48.63	51.37
4	10	9	6	14	13459	7.25	155		6576	6883	48.86	51.14
6	11	9	5	15	13459	7.25	156		6375	7084	47.37	52.63
3	26	9	5	17	13456	7.25	157		6153	7303	45.73	54.27
3	4	9	4	17	13455	7.25	158		6215	7240	46.19	53.81
5	22	9	6	13	13455	7.25	159		6624	6831	49.23	50.77
12	11	9	6	15	13455	7.25	160		6552	6903	48.7	51.3
10	27	9	3	17	13453	7.25	161	185645	6153	7300	45.74	54.26
9	30	9	4	16	13449	7.24	162		6231	7218	46.33	53.67
10	6	9	3	16	13444	7.24	163		6122	7322	45.54	54.46
2	6	9	6	17	13443	7.24	164		6227	7216	46.32	53.68
1	30	9	6	17	13439	7.24	165		6346	7093	47.22	52.78
12	23	9	4	15	13439	7.24	166		6531	6908	48.6	51.4
5	11	9	2	16	13434	7.24	167		5964	7470	44.39	55.61
1	29	9	5	17	13429	7.23	168		6025	7404	44.87	55.13
3	27	9	6	17	13427	7.23	169		6200	7227	46.18	53.82
5	14	9	5	16	13424	7.23	170		5840	7584	43.5	56.5
5	21	9	5	16	13424	7.23	171		6294	7130	46.89	53.11
8	25	9	3	17	13424	7.23	172		6150	7274	45.81	54.19
9	22	9	3	16	13419	7.23	173		6267	7152	46.7	53.3

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
11	20	9	6	16	13415	7.23	174		6283	7132	46.84	53.16
6	8	9	2	16	13411	7.22	175		6251	7160	46.61	53.39
9	29	9	3	16	13411	7.22	176		6247	7164	46.58	53.42
8	5	9	4	17	13407	7.22	177		6288	7119	46.9	53.1
8	26	9	4	17	13406	7.22	178		6093	7313	45.45	54.55
3	11	9	4	16	13398	7.22	179		6292	7106	46.96	53.04
5	21	9	5	17	13398	7.22	180		6367	7031	47.52	52.48
8	25	9	3	16	13396	7.22	181	185645	6223	7173	46.45	53.55
5	26	9	3	16	13395	7.22	182		6320	7075	47.18	52.82
10	8	9	5	17	13395	7.22	183		6127	7268	45.74	54.26
3	13	9	6	14	13387	7.21	184		6441	6946	48.11	51.89
5	21	9	5	15	13387	7.21	185		6328	7059	47.27	52.73
10	19	9	2	16	13384	7.21	186		6168	7216	46.08	53.92
5	1	9	6	14	13379	7.21	187		6558	6821	49.02	50.98
10	29	9	5	17	13376	7.21	188		6377	6999	47.67	52.33
8	26	9	4	16	13374	7.2	189		6291	7083	47.04	52.96
6	4	9	5	16	13372	7.2	190		6330	7042	47.34	52.66
9	8	9	3	17	13372	7.2	191		6193	7179	46.31	53.69
5	14	9	5	18	13369	7.2	192		6167	7202	46.13	53.87
10	2	9	6	15	13369	7.2	193		6456	6913	48.29	51.71
4	9	9	5	15	13368	7.2	194		6310	7058	47.2	52.8
10	13	9	3	16	13367	7.2	195		6069	7298	45.4	54.6
11	12	9	5	16	13367	7.2	196		6226	7141	46.58	53.42
6	2	9	3	16	13366	7.20	197		6255	7111	46.80	53.20
2	16	9	2	16	13362	7.20	198		6280	7082	47.00	53.00
3	2	9	2	16	13362	7.20	199		5915	7447	44.27	55.73
4	29	9	4	17	13362	7.20	200		6293	7069	47.10	52.90

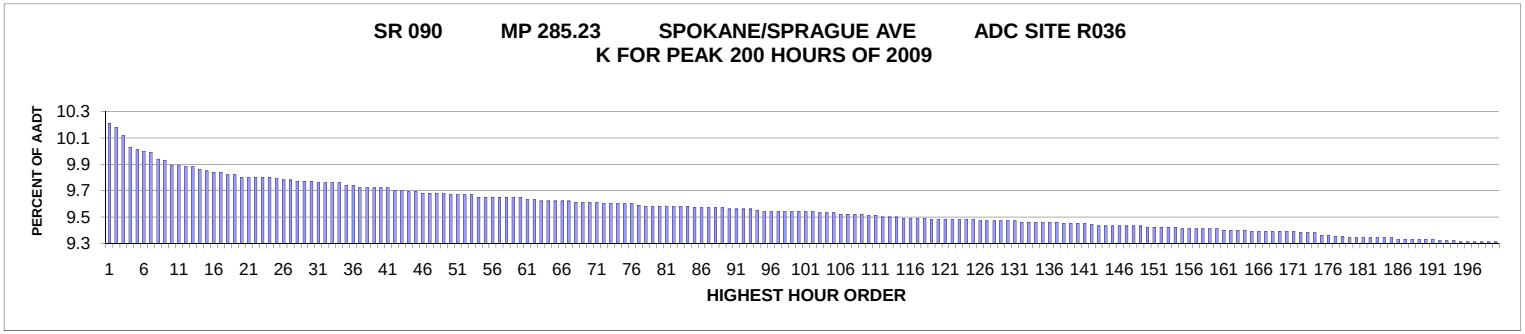

AADT= 107345 **K 30 FACTOR=** 9.77 **K 100 FACTOR=** 9.54 **K 200 FACTOR=** 9.31 **D FACTOR=** 55.42

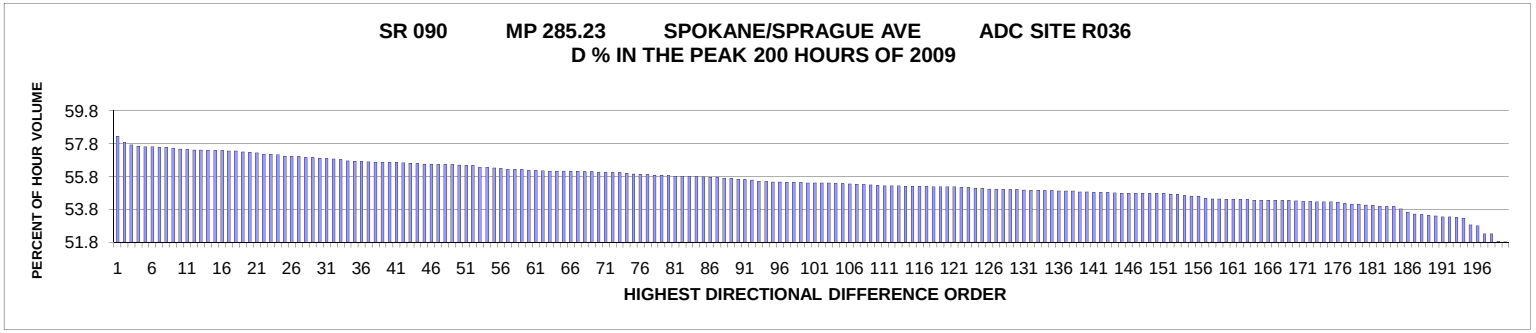

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
5	14	9	5	17	10962	10.21	1	107345	6093	4869	55.58	44.42
4	24	9	6	17	10933	10.18	2		6063	4870	55.46	44.54
5	14	9	5	18	10867	10.12	3		5686	5181	52.32	47.68
11	20	9	6	17	10772	10.03	4		5744	5028	53.32	46.68
9	25	9	6	17	10748	10.01	5		5903	4845	54.92	45.08
5	15	9	6	17	10733	10	6		5836	4897	54.37	45.63
8	14	9	6	17	10727	9.99	7		5820	4907	54.26	45.74
9	24	9	5	17	10665	9.94	8		6029	4636	56.53	43.47
5	13	9	4	18	10659	9.93	9		5793	4866	54.35	45.65
6	26	9	6	17	10615	9.89	10		5883	4732	55.42	44.58
5	7	9	5	17	10612	9.89	11		6002	4610	56.56	43.44
4	15	9	4	17	10602	9.88	12		5827	4775	54.96	45.04
11	5	9	5	17	10602	9.88	13		6083	4519	57.38	42.62
5	21	9	5	17	10582	9.86	14		6125	4457	57.88	42.12
4	16	9	5	17	10577	9.85	15		5942	4635	56.18	43.82
5	12	9	3	17	10566	9.84	16		6035	4531	57.12	42.88
8	20	9	5	17	10563	9.84	17		5930	4633	56.14	43.86

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
6	5	9	6	17	10543	9.82	18		5761	4782	54.64	45.36
10	15	9	5	17	10540	9.82	19		6051	4489	57.41	42.59
5	8	9	6	18	10524	9.8	20		5811	4713	55.22	44.78
10	22	9	5	17	10518	9.8	21	107345	5889	4629	55.99	44.01
4	30	9	5	17	10516	9.8	22		6034	4482	57.38	42.62
8	18	9	3	17	10516	9.8	23		5945	4571	56.53	43.47
4	15	9	4	18	10515	9.8	24		5918	4597	56.28	43.72
6	11	9	5	17	10507	9.79	25		5893	4614	56.09	43.91
4	8	9	4	18	10498	9.78	26		5667	4831	53.98	46.02
10	1	9	5	17	10494	9.78	27		5902	4592	56.24	43.76
10	8	9	5	17	10491	9.77	28		5940	4551	56.62	43.38
9	30	9	4	17	10488	9.77	29		5979	4509	57.01	42.99
5	7	9	5	18	10485	9.77	30		5838	4647	55.68	44.32
11	6	9	6	17	10477	9.76	31		5740	4737	54.79	45.21
10	2	9	6	17	10476	9.76	32		5741	4735	54.8	45.2
4	16	9	5	18	10475	9.76	33		5695	4780	54.37	45.63
5	21	9	5	18	10475	9.76	34		5771	4704	55.09	44.91
4	23	9	5	17	10456	9.74	35		5949	4507	56.9	43.1
6	4	9	5	17	10454	9.74	36		5922	4532	56.65	43.35
6	30	9	3	17	10439	9.72	37		5921	4518	56.72	43.28
6	12	9	6	17	10434	9.72	38		5852	4582	56.09	43.91
5	28	9	5	17	10431	9.72	39		6009	4422	57.61	42.39
12	2	9	4	17	10431	9.72	40		5756	4675	55.18	44.82
5	29	9	6	17	10429	9.72	41	107345	5821	4608	55.82	44.18
4	8	9	4	17	10413	9.7	42		5801	4612	55.71	44.29
5	13	9	4	17	10408	9.7	43		6001	4407	57.66	42.34
5	12	9	3	18	10404	9.69	44		5790	4614	55.65	44.35
4	9	9	5	17	10400	9.69	45		5891	4509	56.64	43.36
11	24	9	3	17	10394	9.68	46		5824	4570	56.03	43.97
10	16	9	6	17	10392	9.68	47		5675	4717	54.61	45.39
3	13	9	6	17	10390	9.68	48		5718	4672	55.03	44.97
9	18	9	6	17	10390	9.68	49		5720	4670	55.05	44.95
10	15	9	5	18	10383	9.67	50		5546	4837	53.41	46.59
8	19	9	4	18	10382	9.67	51		5682	4700	54.73	45.27
9	16	9	4	17	10381	9.67	52		5850	4531	56.35	43.65
6	10	9	4	17	10379	9.67	53		5952	4427	57.35	42.65
3	20	9	6	17	10363	9.65	54		5781	4582	55.79	44.21
11	12	9	5	17	10363	9.65	55		5749	4614	55.48	44.52
4	30	9	5	18	10360	9.65	56		5641	4719	54.45	45.55
8	25	9	3	17	10358	9.65	57		5723	4635	55.25	44.75
5	15	9	6	16	10357	9.65	58		5746	4611	55.48	44.52
12	11	9	6	17	10355	9.65	59		5695	4660	55	45
3	26	9	5	17	10354	9.65	60		5740	4614	55.44	44.56
12	17	9	5	17	10339	9.63	61	107345	5707	4632	55.2	44.8
12	22	9	3	17	10338	9.63	62		5769	4569	55.8	44.2
4	22	9	4	17	10330	9.62	63		5930	4400	57.41	42.59
4	21	9	3	17	10329	9.62	64		5916	4413	57.28	42.72
11	10	9	3	17	10329	9.62	65		5772	4557	55.88	44.12
6	3	9	4	17	10326	9.62	66		5903	4423	57.17	42.83
8	14	9	6	16	10324	9.62	67		5651	4673	54.74	45.26
4	24	9	6	18	10320	9.61	68		5616	4704	54.42	45.58
5	15	9	6	18	10314	9.61	69		5447	4867	52.81	47.19

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
10	27	9	3	17	10314	9.61	70		5953	4361	57.72	42.28
3	19	9	5	17	10312	9.61	71		5826	4486	56.5	43.5
10	9	9	6	17	10308	9.6	72		5603	4705	54.36	45.64
4	22	9	4	18	10307	9.6	73		5610	4697	54.43	45.57
6	9	9	3	18	10303	9.6	74		5713	4590	55.45	44.55
7	7	9	3	17	10300	9.6	75		5875	4425	57.04	42.96
8	21	9	6	17	10300	9.6	76		5546	4754	53.84	46.16
10	1	9	5	18	10296	9.59	77		5586	4710	54.25	45.75
9	17	9	5	17	10286	9.58	78		5563	4723	54.08	45.92
6	9	9	3	17	10285	9.58	79		5926	4359	57.62	42.38
12	10	9	5	17	10285	9.58	80		5699	4586	55.41	44.59
4	9	9	5	18	10284	9.58	81	107345	5654	4630	54.98	45.02
10	30	9	6	17	10284	9.58	82		5765	4519	56.06	43.94
5	5	9	3	17	10283	9.58	83		5906	4377	57.43	42.57
12	18	9	6	17	10280	9.58	84		5503	4777	53.53	46.47
4	14	9	3	18	10278	9.57	85		5772	4506	56.16	43.84
7	1	9	4	17	10277	9.57	86		5715	4562	55.61	44.39
10	7	9	4	17	10274	9.57	87		5858	4416	57.02	42.98
10	22	9	5	18	10273	9.57	88		5589	4684	54.4	45.6
4	29	9	4	18	10272	9.57	89		5690	4582	55.39	44.61
12	9	9	4	17	10265	9.56	90		5589	4676	54.45	45.55
4	14	9	3	17	10264	9.56	91		5892	4372	57.4	42.6
7	1	9	4	18	10260	9.56	92		5622	4638	54.8	45.2
7	23	9	5	17	10260	9.56	93		5737	4523	55.92	44.08
12	23	9	4	17	10249	9.55	94		5620	4629	54.83	45.17
3	6	9	6	17	10246	9.54	95		5718	4528	55.81	44.19
4	17	9	6	17	10246	9.54	96		5547	4699	54.14	45.86
5	5	9	3	18	10244	9.54	97		5611	4633	54.77	45.23
2	19	9	5	17	10243	9.54	98		5648	4595	55.14	44.86
9	16	9	4	18	10243	9.54	99		5529	4714	53.98	46.02
11	19	9	5	17	10242	9.54	100		5620	4622	54.87	45.13
5	26	9	3	17	10236	9.54	101	107345	5789	4447	56.56	43.44
8	6	9	5	18	10236	9.54	102		5578	4658	54.49	45.51
3	3	9	3	17	10231	9.53	103		5742	4489	56.12	43.88
12	4	9	6	17	10228	9.53	104		5553	4675	54.29	45.71
5	20	9	4	18	10226	9.53	105		5666	4560	55.41	44.59
2	20	9	6	17	10224	9.52	106		5773	4451	56.47	43.53
6	2	9	3	17	10219	9.52	107		5880	4339	57.54	42.46
10	20	9	3	17	10219	9.52	108		5883	4336	57.57	42.43
6	11	9	5	18	10216	9.52	109		5657	4559	55.37	44.63
4	24	9	6	16	10206	9.51	110		5597	4609	54.84	45.16
4	10	9	6	17	10204	9.51	111		5609	4595	54.97	45.03
7	8	9	4	17	10202	9.5	112		5688	4514	55.75	44.25
9	25	9	6	18	10202	9.5	113		5291	4911	51.86	48.14
9	3	9	5	18	10196	9.5	114		5440	4756	53.35	46.65
2	27	9	6	17	10187	9.49	115		5623	4564	55.2	44.8
4	17	9	6	18	10185	9.49	116		5526	4659	54.26	45.74
1	30	9	6	17	10184	9.49	117		5691	4493	55.88	44.12
9	22	9	3	17	10182	9.49	118		5786	4396	56.83	43.17
11	4	9	4	17	10179	9.48	119		5712	4467	56.12	43.88
5	19	9	3	17	10178	9.48	120		5838	4340	57.36	42.64
12	1	9	3	17	10177	9.48	121	107345	5825	4352	57.24	42.76

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
2	13	9	6	17	10173	9.48	122		5701	4472	56.04	43.96
6	30	9	3	18	10172	9.48	123		5581	4591	54.87	45.13
9	4	9	6	17	10172	9.48	124		5530	4642	54.36	45.64
8	6	9	5	17	10171	9.48	125		5678	4493	55.83	44.17
10	8	9	5	18	10169	9.47	126		5534	4635	54.42	45.58
4	23	9	5	18	10165	9.47	127		5622	4543	55.31	44.69
8	11	9	3	17	10165	9.47	128		5746	4419	56.53	43.47
10	28	9	4	17	10163	9.47	129		5751	4412	56.59	43.41
12	3	9	5	17	10163	9.47	130		5823	4340	57.3	42.7
11	18	9	4	17	10161	9.47	131		5757	4404	56.66	43.34
9	15	9	3	17	10160	9.46	132		5725	4435	56.35	43.65
5	20	9	4	17	10158	9.46	133		5917	4241	58.25	41.75
10	2	9	6	16	10158	9.46	134		5622	4536	55.35	44.65
2	10	9	3	17	10154	9.46	135		5636	4518	55.51	44.49
10	28	9	4	18	10151	9.46	136		5565	4586	54.82	45.18
6	10	9	4	18	10150	9.46	137		5594	4556	55.11	44.89
3	12	9	5	18	10141	9.45	138		5539	4602	54.62	45.38
4	28	9	3	17	10140	9.45	139		5683	4457	56.05	43.95
8	18	9	3	18	10140	9.45	140		5509	4631	54.33	45.67
7	9	9	5	17	10139	9.45	141	107345	5600	4539	55.23	44.77
5	28	9	5	18	10130	9.44	142		5587	4543	55.15	44.85
3	18	9	4	18	10127	9.43	143		5592	4535	55.22	44.78
4	7	9	3	18	10127	9.43	144		5549	4578	54.79	45.21
11	2	9	2	17	10124	9.43	145		5661	4463	55.92	44.08
5	29	9	6	16	10120	9.43	146		5701	4419	56.33	43.67
5	19	9	3	18	10118	9.43	147		5690	4428	56.24	43.76
8	7	9	6	17	10118	9.43	148		5599	4519	55.34	44.66
9	3	9	5	17	10118	9.43	149		5463	4655	53.99	46.01
4	7	9	3	17	10117	9.42	150		5541	4576	54.77	45.23
10	21	9	4	17	10114	9.42	151		5738	4376	56.73	43.27
3	18	9	4	17	10113	9.42	152		5650	4463	55.87	44.13
9	23	9	4	17	10112	9.42	153		5734	4378	56.7	43.3
10	23	9	6	17	10111	9.42	154		5585	4526	55.24	44.76
6	4	9	5	18	10106	9.41	155		5600	4506	55.41	44.59
10	20	9	3	18	10106	9.41	156		5551	4555	54.93	45.07
4	20	9	2	17	10101	9.41	157		5754	4347	56.96	43.04
7	15	9	4	17	10100	9.41	158		5556	4544	55.01	44.99
6	26	9	6	18	10098	9.41	159		5379	4719	53.27	46.73
4	17	9	6	16	10097	9.41	160		5572	4525	55.18	44.82
4	29	9	4	17	10094	9.4	161	107345	5746	4348	56.92	43.08
9	2	9	4	17	10089	9.4	162		5527	4562	54.78	45.22
7	15	9	4	18	10088	9.4	163		5382	4706	53.35	46.65
7	23	9	5	18	10088	9.4	164		5568	4520	55.19	44.81
4	27	9	2	17	10082	9.39	165		5713	4369	56.67	43.33
5	6	9	4	18	10082	9.39	166		5470	4612	54.26	45.74
8	26	9	4	17	10082	9.39	167		5695	4387	56.49	43.51
10	29	9	5	18	10081	9.39	168		5547	4534	55.02	44.98
4	20	9	2	18	10077	9.39	169		5457	4620	54.15	45.85
9	22	9	3	18	10077	9.39	170		5406	4671	53.65	46.35
9	29	9	3	17	10077	9.39	171		5720	4357	56.76	43.24
9	21	9	2	17	10071	9.38	172		5708	4363	56.68	43.32
10	5	9	2	17	10068	9.38	173		5755	4313	57.16	42.84

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
6	3	9	4	18	10064	9.38	174		5448	4616	54.13	45.87
9	11	9	6	17	10052	9.36	175		5457	4595	54.29	45.71
10	29	9	5	17	10050	9.36	176		5521	4529	54.94	45.06
7	30	9	5	17	10041	9.35	177		5517	4524	54.94	45.06
9	8	9	3	17	10041	9.35	178		5542	4499	55.19	44.81
11	25	9	4	16	10030	9.34	179		5546	4484	55.29	44.71
8	3	9	2	17	10027	9.34	180		5710	4317	56.95	43.05
8	4	9	3	17	10027	9.34	181	107345	5628	4399	56.13	43.87
5	8	9	6	17	10025	9.34	182		5197	4828	51.84	48.16
5	11	9	2	18	10025	9.34	183		5564	4461	55.5	44.5
10	6	9	3	17	10022	9.34	184		5760	4262	57.47	42.53
3	13	9	6	18	10021	9.34	185		5297	4724	52.86	47.14
10	21	9	4	18	10020	9.33	186		5446	4574	54.35	45.65
3	3	9	3	18	10019	9.33	187		5415	4604	54.05	45.95
3	12	9	5	17	10017	9.33	188		5698	4319	56.88	43.12
7	21	9	3	17	10013	9.33	189		5624	4389	56.17	43.83
5	22	9	6	17	10012	9.33	190		5500	4512	54.93	45.07
9	14	9	2	17	10010	9.33	191		5583	4427	55.77	44.23
11	3	9	3	17	10007	9.32	192		5599	4408	55.95	44.05
6	2	9	3	18	10003	9.32	193		5526	4477	55.24	44.76
5	29	9	6	18	10002	9.32	194		5344	4658	53.43	46.57
12	2	9	4	18	9999	9.31	195		5231	4768	52.32	47.68
2	17	9	3	17	9998	9.31	196		5756	4242	57.57	42.43
7	9	9	5	18	9998	9.31	197		5482	4516	54.83	45.17
12	10	9	5	18	9997	9.31	198		5347	4650	53.49	46.51
3	25	9	4	17	9995	9.31	199		5621	4374	56.24	43.76
4	28	9	3	18	9994	9.31	200		5608	4386	56.11	43.89

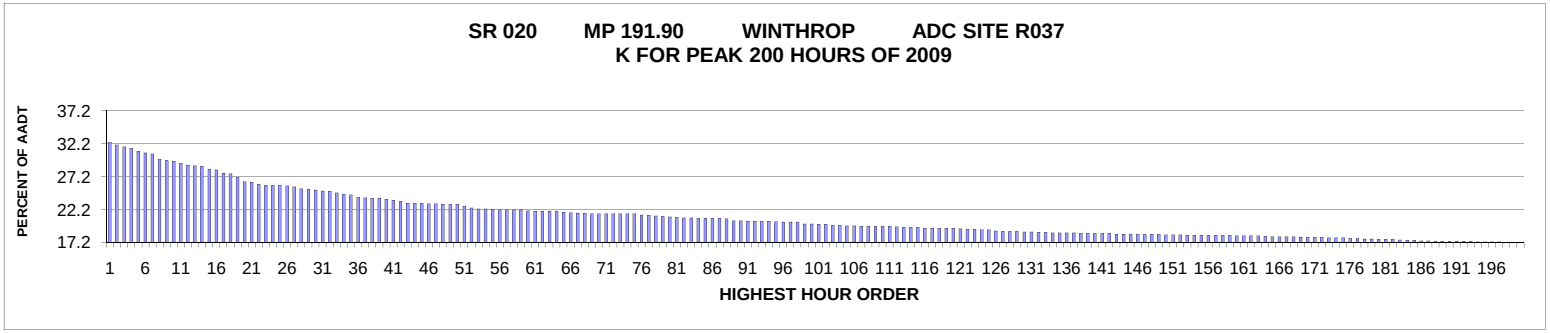

AADT= 1759 **K 30 FACTOR=** 25.18 **K 100 FACTOR=** 20.01 **K 200 FACTOR=** 17.23 **D FACTOR=** 59.49

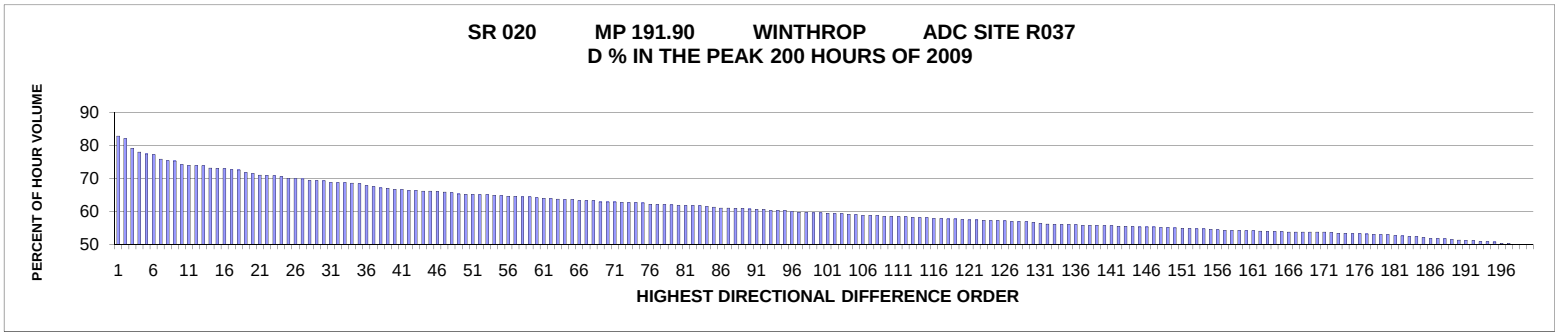

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	19	9	1	13	570	32.4	1	1759	192	378	33.68	66.32
8	22	9	7	14	563	32.01	2		237	326	42.1	57.9
7	18	9	7	12	558	31.72	3		251	307	44.98	55.02
7	18	9	7	14	555	31.55	4		279	276	50.27	49.73
7	19	9	1	14	546	31.04	5		219	327	40.11	59.89
8	22	9	7	12	542	30.81	6		240	302	44.28	55.72
7	19	9	1	12	539	30.64	7		180	359	33.4	66.6
7	18	9	7	13	525	29.85	8		238	287	45.33	54.67
8	22	9	7	15	521	29.62	9		232	289	44.53	55.47
7	19	9	1	15	520	29.56	10		210	310	40.38	59.62
8	22	9	7	13	514	29.22	11		241	273	46.89	53.11
7	18	9	7	15	509	28.94	12		226	283	44.4	55.6
7	17	9	6	16	508	28.88	13		292	216	57.48	42.52
9	7	9	2	13	506	28.77	14		122	384	24.11	75.89
8	23	9	1	13	498	28.31	15		243	255	48.8	51.2
7	19	9	1	16	497	28.25	16		237	260	47.69	52.31
7	5	9	1	13	488	27.74	17		127	361	26.02	73.98

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	18	9	7	17	486	27.63	18		261	225	53.7	46.3
9	7	9	2	14	476	27.06	19		129	347	27.1	72.9
7	19	9	1	11	465	26.44	20		192	273	41.29	58.71
7	19	9	1	17	463	26.32	21	1759	201	262	43.41	56.59
8	22	9	7	17	458	26.04	22		214	244	46.72	53.28
7	11	9	7	13	455	25.87	23		311	144	68.35	31.65
7	18	9	7	11	455	25.87	24		238	217	52.31	47.69
8	23	9	1	12	455	25.87	25		210	245	46.15	53.85
8	21	9	6	16	454	25.81	26		251	203	55.29	44.71
7	18	9	7	16	451	25.64	27		245	206	54.32	45.68
8	21	9	6	17	446	25.36	28		263	183	58.97	41.03
8	21	9	6	14	445	25.3	29		241	204	54.16	45.84
7	3	9	6	15	443	25.18	30		277	166	62.53	37.47
7	5	9	1	14	440	25.01	31		138	302	31.36	68.64
9	7	9	2	12	439	24.96	32		100	339	22.78	77.22
8	22	9	7	16	435	24.73	33		193	242	44.37	55.63
7	18	9	7	18	431	24.5	34		228	203	52.9	47.1
7	17	9	6	13	430	24.45	35		228	202	53.02	46.98
7	17	9	6	15	423	24.05	36		263	160	62.17	37.83
8	9	9	1	15	422	23.99	37		142	280	33.65	66.35
8	22	9	7	11	420	23.88	38		211	209	50.24	49.76
9	7	9	2	15	420	23.88	39		129	291	30.71	69.29
5	23	9	7	13	418	23.76	40		309	109	73.92	26.08
5	24	9	1	15	415	23.59	41	1759	169	246	40.72	59.28
8	21	9	6	15	413	23.48	42		228	185	55.21	44.79
8	16	9	1	14	408	23.19	43		161	247	39.46	60.54
8	23	9	1	15	408	23.19	44		174	234	42.65	57.35
7	5	9	1	15	407	23.14	45		156	251	38.33	61.67
5	24	9	1	16	406	23.08	46		151	255	37.19	62.81
7	3	9	6	16	406	23.08	47		260	146	64.04	35.96
8	23	9	1	14	405	23.02	48		127	278	31.36	68.64
7	3	9	6	14	404	22.97	49		246	158	60.89	39.11
7	17	9	6	12	404	22.97	50		199	205	49.26	50.74
7	17	9	6	17	400	22.74	51		224	176	56	44
6	21	9	1	14	395	22.46	52		134	261	33.92	66.08
7	17	9	6	14	392	22.29	53		212	180	54.08	45.92
8	30	9	1	15	392	22.29	54		151	241	38.52	61.48
5	24	9	1	14	391	22.23	55		219	172	56.01	43.99
5	22	9	6	15	390	22.17	56		280	110	71.79	28.21
7	5	9	1	12	390	22.17	57		107	283	27.44	72.56
8	9	9	1	14	390	22.17	58		136	254	34.87	65.13
8	23	9	1	11	390	22.17	59		195	195	50	50
7	12	9	1	13	387	22	60		133	254	34.37	65.63
5	22	9	6	17	386	21.94	61	1759	301	85	77.98	22.02
9	6	9	1	14	386	21.94	62		193	193	50	50
9	6	9	1	15	386	21.94	63		174	212	45.08	54.92
8	21	9	6	19	385	21.89	64		216	169	56.1	43.9
5	22	9	6	18	384	21.83	65		289	95	75.26	24.74
5	24	9	1	13	382	21.72	66		205	177	53.66	46.34
7	12	9	1	12	381	21.66	67		140	241	36.75	63.25
7	20	9	2	11	381	21.66	68		195	186	51.18	48.82
5	22	9	6	16	379	21.55	69		300	79	79.16	20.84

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
5	23	9	7	16	379	21.55	70		220	159	58.05	41.95
7	19	9	1	18	379	21.55	71		182	197	48.02	51.98
8	9	9	1	13	379	21.55	72		114	265	30.08	69.92
8	15	9	7	13	379	21.55	73		235	144	62.01	37.99
8	21	9	6	13	379	21.55	74		174	205	45.91	54.09
8	23	9	1	16	379	21.55	75		167	212	44.06	55.94
7	17	9	6	18	376	21.38	76		215	161	57.18	42.82
9	5	9	7	13	375	21.32	77		226	149	60.27	39.73
7	19	9	1	10	373	21.21	78		156	217	41.82	58.18
6	28	9	1	12	372	21.15	79		130	242	34.95	65.05
8	21	9	6	18	371	21.09	80		201	170	54.18	45.82
7	26	9	1	13	369	20.98	81	1759	133	236	36.04	63.96
8	23	9	1	10	368	20.92	82		210	158	57.07	42.93
8	30	9	1	14	368	20.92	83		140	228	38.04	61.96
5	23	9	7	14	367	20.86	84		237	130	64.58	35.42
7	3	9	6	13	367	20.86	85		225	142	61.31	38.69
7	26	9	1	15	367	20.86	86		154	213	41.96	58.04
8	16	9	1	16	367	20.86	87		173	194	47.14	52.86
7	26	9	1	14	366	20.81	88		156	210	42.62	57.38
7	12	9	1	14	361	20.52	89		135	226	37.4	62.6
8	21	9	6	12	361	20.52	90		163	198	45.15	54.85
5	23	9	7	15	360	20.47	91		226	134	62.78	37.22
8	16	9	1	13	360	20.47	92		116	244	32.22	67.78
7	3	9	6	12	359	20.41	93		211	148	58.77	41.23
7	5	9	1	11	359	20.41	94		105	254	29.25	70.75
7	26	9	1	12	358	20.35	95		118	240	32.96	67.04
5	23	9	7	12	357	20.3	96		265	92	74.23	25.77
7	18	9	7	19	357	20.3	97		151	206	42.3	57.7
7	20	9	2	12	357	20.3	98		190	167	53.22	46.78
7	18	9	7	10	352	20.01	99		182	170	51.7	48.3
9	7	9	2	11	352	20.01	100		63	289	17.9	82.1
6	28	9	1	15	351	19.95	101	1759	100	251	28.49	71.51
8	21	9	6	21	351	19.95	102		163	188	46.44	53.56
6	27	9	7	15	349	19.84	103		207	142	59.31	40.69
9	5	9	7	17	348	19.78	104		183	165	52.59	47.41
7	17	9	6	20	347	19.73	105		226	121	65.13	34.87
9	4	9	6	17	347	19.73	106		252	95	72.62	27.38
6	28	9	1	13	346	19.67	107		102	244	29.48	70.52
6	28	9	1	14	345	19.61	108		131	214	37.97	62.03
8	2	9	1	13	345	19.61	109		127	218	36.81	63.19
8	30	9	1	13	345	19.61	110		129	216	37.39	62.61
9	6	9	1	13	345	19.61	111		155	190	44.93	55.07
6	27	9	7	14	344	19.56	112		177	167	51.45	48.55
8	2	9	1	12	343	19.5	113		134	209	39.07	60.93
8	15	9	7	15	343	19.5	114		195	148	56.85	43.15
8	22	9	7	10	343	19.5	115		166	177	48.4	51.6
5	22	9	6	14	341	19.39	116		238	103	69.79	30.21
7	16	9	5	16	341	19.39	117		191	150	56.01	43.99
7	19	9	1	19	341	19.39	118		162	179	47.51	52.49
8	16	9	1	15	341	19.39	119		147	194	43.11	56.89
9	7	9	2	16	341	19.39	120		124	217	36.36	63.64
8	30	9	1	12	339	19.27	121	1759	115	224	33.92	66.08

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
5	22	9	6	19	338	19.22	122		280	58	82.84	17.16
7	12	9	1	15	338	19.22	123		133	205	39.35	60.65
9	4	9	6	15	337	19.16	124		213	124	63.2	36.8
9	20	9	1	14	337	19.16	125		154	183	45.7	54.3
9	4	9	6	18	333	18.93	126		236	97	70.87	29.13
7	17	9	6	19	332	18.87	127		179	153	53.92	46.08
8	2	9	1	15	332	18.87	128		138	194	41.57	58.43
9	6	9	1	16	332	18.87	129		117	215	35.24	64.76
8	9	9	1	12	331	18.82	130		104	227	31.42	68.58
8	15	9	7	14	331	18.82	131		176	155	53.17	46.83
7	18	9	7	20	330	18.76	132		123	207	37.27	62.73
6	20	9	7	15	329	18.7	133		214	115	65.05	34.95
7	16	9	5	14	328	18.65	134		179	149	54.57	45.43
8	8	9	7	14	328	18.65	135		176	152	53.66	46.34
9	5	9	7	12	328	18.65	136		216	112	65.85	34.15
9	20	9	1	13	328	18.65	137		101	227	30.79	69.21
9	13	9	1	12	327	18.59	138		125	202	38.23	61.77
6	21	9	1	13	326	18.53	139		106	220	32.52	67.48
6	27	9	7	13	326	18.53	140		180	146	55.21	44.79
8	9	9	1	16	326	18.53	141	1759	138	188	42.33	57.67
8	21	9	6	20	326	18.53	142		176	150	53.99	46.01
7	26	9	1	16	325	18.48	143		135	190	41.54	58.46
9	20	9	1	15	325	18.48	144		127	198	39.08	60.92
5	23	9	7	11	324	18.42	145		237	87	73.15	26.85
5	23	9	7	17	324	18.42	146		158	166	48.77	51.23
5	24	9	1	18	324	18.42	147		97	227	29.94	70.06
7	11	9	7	15	324	18.42	148		150	174	46.3	53.7
7	12	9	1	16	324	18.42	149		150	174	46.3	53.7
7	12	9	1	11	323	18.36	150		101	222	31.27	68.73
7	17	9	6	11	323	18.36	151		151	172	46.75	53.25
7	24	9	6	14	323	18.36	152		185	138	57.28	42.72
7	10	9	6	14	322	18.31	153		183	139	56.83	43.17
7	11	9	7	14	322	18.31	154		189	133	58.7	41.3
5	24	9	1	17	321	18.25	155		117	204	36.45	63.55
7	20	9	2	10	321	18.25	156		163	158	50.78	49.22
7	25	9	7	15	321	18.25	157		178	143	55.45	44.55
9	5	9	7	15	321	18.25	158		173	148	53.89	46.11
10	16	9	6	14	321	18.25	159		228	93	71.03	28.97
5	24	9	1	12	320	18.19	160		162	158	50.63	49.38
8	7	9	6	14	320	18.19	161	1759	194	126	60.63	39.38
9	4	9	6	16	320	18.19	162		222	98	69.38	30.63
9	13	9	1	15	320	18.19	163		135	185	42.19	57.81
6	28	9	1	16	319	18.14	164		122	197	38.24	61.76
6	14	9	1	14	318	18.08	165		124	194	38.99	61.01
7	16	9	5	18	318	18.08	166		174	144	54.72	45.28
8	2	9	1	14	318	18.08	167		159	159	50	50
9	13	9	1	13	318	18.08	168		128	190	40.25	59.75
7	20	9	2	13	317	18.02	169		164	153	51.74	48.26
7	16	9	5	17	316	17.96	170		188	128	59.49	40.51
8	14	9	6	16	316	17.96	171		188	128	59.49	40.51
10	16	9	6	13	316	17.96	172		238	78	75.32	24.68
7	3	9	6	17	315	17.91	173		190	125	60.32	39.68

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	16	9	5	15	315	17.91	174		169	146	53.65	46.35
8	7	9	6	16	315	17.91	175		208	107	66.03	33.97
8	21	9	6	11	313	17.79	176		134	179	42.81	57.19
9	20	9	1	12	313	17.79	177		82	231	26.2	73.8
7	5	9	1	16	312	17.74	178		111	201	35.58	64.42
8	13	9	5	16	312	17.74	179		182	130	58.33	41.67
8	16	9	1	17	311	17.68	180		136	175	43.73	56.27
8	29	9	7	14	311	17.68	181	1759	203	108	65.27	34.73
10	16	9	6	16	311	17.68	182		227	84	72.99	27.01
6	21	9	1	12	309	17.57	183		110	199	35.6	64.4
8	16	9	1	12	308	17.51	184		109	199	35.39	64.61
9	27	9	1	15	308	17.51	185		125	183	40.58	59.42
8	22	9	7	18	307	17.45	186		171	136	55.7	44.3
9	4	9	6	13	307	17.45	187		199	108	64.82	35.18
9	4	9	6	19	306	17.4	188		237	69	77.45	22.55
9	18	9	6	16	306	17.4	189		189	117	61.76	38.24
6	27	9	7	17	305	17.34	190		184	121	60.33	39.67
7	10	9	6	15	305	17.34	191		195	110	63.93	36.07
8	22	9	7	19	305	17.34	192		135	170	44.26	55.74
9	6	9	1	12	305	17.34	193		127	178	41.64	58.36
6	7	9	1	13	304	17.28	194		100	204	32.89	67.11
8	9	9	1	17	304	17.28	195		138	166	45.39	54.61
8	29	9	7	13	304	17.28	196		168	136	55.26	44.74
9	5	9	7	11	304	17.28	197		191	113	62.83	37.17
5	22	9	6	13	303	17.23	198		202	101	66.67	33.33
7	6	9	2	12	303	17.23	199		110	193	36.3	63.7
7	25	9	7	14	303	17.23	200		179	124	59.08	40.92

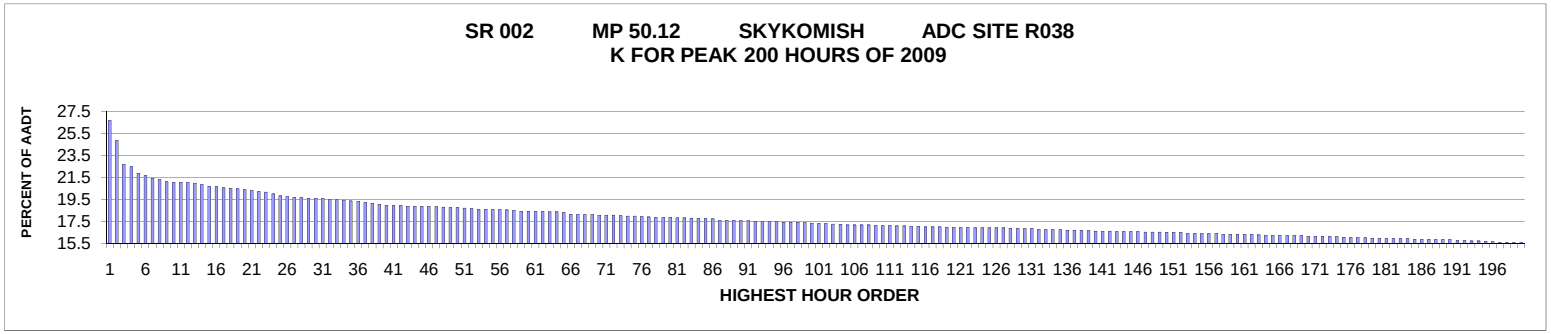

AADT= 4903 **K 30 FACTOR=** 19.62 **K 100 FACTOR=** 17.34 **K 200 FACTOR=** 15.56 **D FACTOR=** 73.56

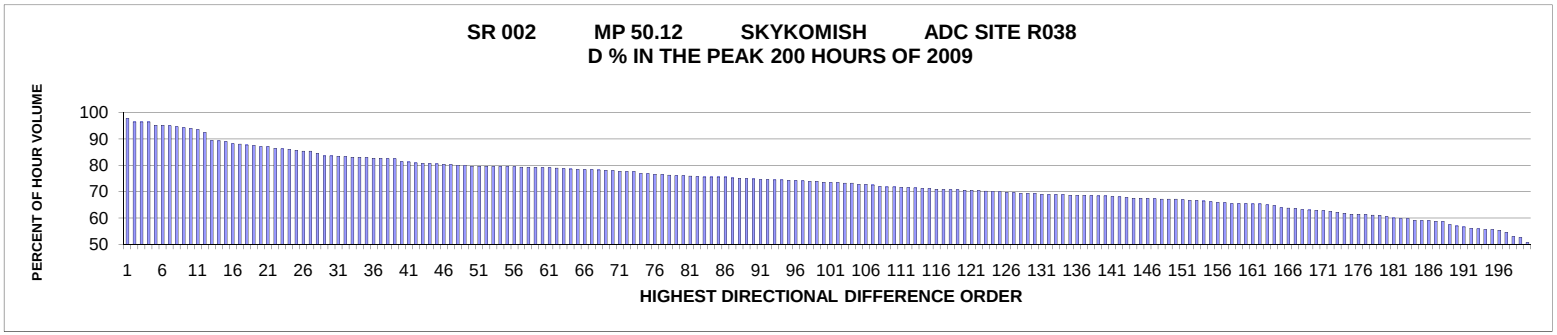

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
4	5	9	1	17	1307	26.66	1	4903	161	1146	12.32	87.68
4	19	9	1	17	1221	24.9	2		146	1075	11.96	88.04
5	25	9	2	12	1113	22.7	3		220	893	19.77	80.23
4	19	9	1	16	1102	22.48	4		181	921	16.42	83.58
4	4	9	7	17	1073	21.88	5		139	934	12.95	87.05
10	11	9	1	12	1062	21.66	6		484	578	45.57	54.43
10	11	9	1	13	1050	21.42	7		431	619	41.05	58.95
10	11	9	1	17	1044	21.29	8		212	832	20.31	79.69
10	11	9	1	15	1034	21.09	9		313	721	30.27	69.73
4	5	9	1	18	1033	21.07	10		122	911	11.81	88.19
5	25	9	2	13	1033	21.07	11		228	805	22.07	77.93
8	23	9	1	13	1031	21.03	12		347	684	33.66	66.34
8	9	9	1	13	1029	20.99	13		397	632	38.58	61.42
8	23	9	1	15	1022	20.84	14		319	703	31.21	68.79
10	11	9	1	16	1015	20.7	15		270	745	26.6	73.4
10	11	9	1	14	1013	20.66	16		333	680	32.87	67.13
8	9	9	1	15	1007	20.54	17		309	698	30.69	69.31

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
3	8	9	1	16	1005	20.5	18		171	834	17.01	82.99
7	5	9	1	13	1003	20.46	19		302	701	30.11	69.89
8	16	9	1	15	999	20.38	20		307	692	30.73	69.27
8	9	9	1	14	996	20.31	21	4903	332	664	33.33	66.67
8	16	9	1	14	992	20.23	22		379	613	38.21	61.79
1	3	9	7	10	989	20.17	23		929	60	93.93	6.07
1	18	9	1	16	980	19.99	24		197	783	20.1	79.9
10	4	9	1	14	972	19.82	25		281	691	28.91	71.09
8	16	9	1	17	967	19.72	26		246	721	25.44	74.56
7	19	9	1	13	965	19.68	27		373	592	38.65	61.35
8	23	9	1	14	964	19.66	28		326	638	33.82	66.18
7	19	9	1	14	962	19.62	29		333	629	34.62	65.38
9	20	9	1	16	962	19.62	30		246	716	25.57	74.43
8	9	9	1	16	960	19.58	31		304	656	31.67	68.33
12	27	9	1	15	956	19.5	32		427	529	44.67	55.33
9	20	9	1	17	954	19.46	33		224	730	23.48	76.52
8	2	9	1	13	953	19.44	34		391	562	41.03	58.97
8	23	9	1	16	948	19.34	35		232	716	24.47	75.53
8	16	9	1	13	947	19.31	36		367	580	38.75	61.25
7	19	9	1	15	941	19.19	37		297	644	31.56	68.44
8	16	9	1	16	938	19.13	38		292	646	31.13	68.87
8	2	9	1	15	934	19.05	39		324	610	34.69	65.31
7	12	9	1	14	929	18.95	40		317	612	34.12	65.88
7	26	9	1	15	928	18.93	41	4903	321	607	34.59	65.41
12	27	9	1	17	928	18.93	42		285	643	30.71	69.29
3	29	9	1	16	925	18.87	43		194	731	20.97	79.03
10	4	9	1	12	925	18.87	44		316	609	34.16	65.84
4	5	9	1	16	924	18.85	45		158	766	17.1	82.9
5	25	9	2	11	924	18.85	46		193	731	20.89	79.11
9	7	9	2	13	923	18.83	47		219	704	23.73	76.27
9	27	9	1	17	921	18.78	48		221	700	24	76
7	19	9	1	16	919	18.74	49		271	648	29.49	70.51
8	2	9	1	14	919	18.74	50		340	579	37	63
8	30	9	1	16	917	18.7	51		246	671	26.83	73.17
3	8	9	1	15	915	18.66	52		195	720	21.31	78.69
5	25	9	2	14	912	18.6	53		176	736	19.3	80.7
6	28	9	1	15	912	18.6	54		260	652	28.51	71.49
7	5	9	1	14	910	18.56	55		301	609	33.08	66.92
10	4	9	1	16	910	18.56	56		229	681	25.16	74.84
3	29	9	1	17	909	18.54	57		160	749	17.6	82.4
10	4	9	1	13	906	18.48	58		283	623	31.24	68.76
9	20	9	1	15	902	18.4	59		264	638	29.27	70.73
9	27	9	1	16	902	18.4	60		248	654	27.49	72.51
1	4	9	1	16	901	18.38	61	4903	156	745	17.31	82.69
6	21	9	1	14	901	18.38	62		266	635	29.52	70.48
7	26	9	1	14	900	18.36	63		334	566	37.11	62.89
8	30	9	1	15	900	18.36	64		264	636	29.33	70.67
12	26	9	7	13	897	18.29	65		667	230	74.36	25.64
10	4	9	1	15	890	18.15	66		231	659	25.96	74.04
1	3	9	7	17	888	18.11	67		148	740	16.67	83.33
8	9	9	1	12	887	18.09	68		378	509	42.62	57.38
10	4	9	1	17	887	18.09	69		194	693	21.87	78.13

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
1	31	9	7	9	886	18.07	70		841	45	94.92	5.08
2	16	9	2	16	886	18.07	71		198	688	22.35	77.65
12	26	9	7	16	885	18.05	72		393	492	44.41	55.59
6	21	9	1	15	883	18.01	73		250	633	28.31	71.69
7	12	9	1	15	881	17.97	74		282	599	32.01	67.99
7	26	9	1	16	881	17.97	75		249	632	28.26	71.74
6	28	9	1	14	879	17.93	76		280	599	31.85	68.15
11	29	9	1	16	877	17.89	77		170	707	19.38	80.62
9	27	9	1	15	876	17.87	78		223	653	25.46	74.54
7	5	9	1	12	875	17.85	79		261	614	29.83	70.17
8	9	9	1	17	875	17.85	80		239	636	27.31	72.69
1	4	9	1	15	872	17.79	81	4903	218	654	25	75
7	19	9	1	12	872	17.79	82		383	489	43.92	56.08
10	11	9	1	18	871	17.76	83		177	694	20.32	79.68
11	28	9	7	17	871	17.76	84		96	775	11.02	88.98
12	26	9	7	15	870	17.74	85		510	360	58.62	41.38
12	27	9	1	16	868	17.7	86		226	642	26.04	73.96
9	20	9	1	18	862	17.58	87		222	640	25.75	74.25
3	1	9	1	16	861	17.56	88		185	676	21.49	78.51
7	26	9	1	13	861	17.56	89		352	509	40.88	59.12
7	5	9	1	15	860	17.54	90		280	580	32.56	67.44
8	2	9	1	16	860	17.54	91		255	605	29.65	70.35
9	27	9	1	14	859	17.52	92		282	577	32.83	67.17
3	8	9	1	8	857	17.48	93		826	31	96.38	3.62
12	27	9	1	12	857	17.48	94		596	261	69.54	30.46
4	5	9	1	19	856	17.46	95		111	745	12.97	87.03
3	8	9	1	14	854	17.42	96		221	633	25.88	74.12
7	12	9	1	13	854	17.42	97		299	555	35.01	64.99
8	23	9	1	17	854	17.42	98		191	663	22.37	77.63
2	15	9	1	16	851	17.36	99		225	626	26.44	73.56
8	23	9	1	12	850	17.34	100		351	499	41.29	58.71
5	25	9	2	15	848	17.3	101	4903	176	672	20.75	79.25
3	29	9	1	15	847	17.28	102		254	593	29.99	70.01
12	26	9	7	14	846	17.25	103		547	299	64.66	35.34
1	18	9	1	17	844	17.21	104		143	701	16.94	83.06
8	16	9	1	18	842	17.17	105		205	637	24.35	75.65
8	30	9	1	17	842	17.17	106		165	677	19.6	80.4
9	27	9	1	18	842	17.17	107		220	622	26.13	73.87
12	31	9	5	16	842	17.17	108		337	505	40.02	59.98
11	27	9	6	17	840	17.13	109		177	663	21.07	78.93
4	4	9	7	9	838	17.09	110		774	64	92.36	7.64
4	18	9	7	17	838	17.09	111		123	715	14.68	85.32
1	2	9	6	12	837	17.07	112		565	272	67.5	32.5
12	24	9	5	15	837	17.07	113		263	574	31.42	68.58
7	26	9	1	12	836	17.05	114		363	473	43.42	56.58
12	27	9	1	13	835	17.03	115		499	336	59.76	40.24
9	20	9	1	14	833	16.99	116		262	571	31.45	68.55
6	21	9	1	13	832	16.97	117		236	596	28.37	71.63
8	9	9	1	18	832	16.97	118		170	662	20.43	79.57
3	15	9	1	9	831	16.95	119		801	30	96.39	3.61
8	30	9	1	14	831	16.95	120		268	563	32.25	67.75
5	25	9	2	16	830	16.93	121	4903	122	708	14.7	85.3

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	30	9	1	13	830	16.93	122		271	559	32.65	67.35
3	15	9	1	17	829	16.91	123		114	715	13.75	86.25
6	21	9	1	16	829	16.91	124		206	623	24.85	75.15
3	25	9	4	17	828	16.89	125		45	783	5.43	94.57
8	30	9	1	18	828	16.89	126		145	683	17.51	82.49
12	26	9	7	12	828	16.89	127		625	203	75.48	24.52
9	7	9	2	14	827	16.87	128		192	635	23.22	76.78
3	29	9	1	9	826	16.85	129		786	40	95.16	4.84
11	21	9	7	9	826	16.85	130		796	30	96.37	3.63
8	16	9	1	12	825	16.83	131		356	469	43.15	56.85
6	28	9	1	16	821	16.74	132		201	620	24.48	75.52
4	3	9	6	17	820	16.72	133		231	589	28.17	71.83
4	19	9	1	15	820	16.72	134		169	651	20.61	79.39
8	30	9	1	19	820	16.72	135		142	678	17.32	82.68
8	2	9	1	12	819	16.7	136		364	455	44.44	55.56
9	7	9	2	12	818	16.68	137		206	612	25.18	74.82
3	22	9	1	16	817	16.66	138		183	634	22.4	77.6
11	22	9	1	9	816	16.64	139		769	47	94.24	5.76
9	20	9	1	13	814	16.6	140		295	519	36.24	63.76
10	10	9	7	12	814	16.6	141	4903	638	176	78.38	21.62
10	18	9	1	14	814	16.6	142		218	596	26.78	73.22
6	28	9	1	13	812	16.56	143		271	541	33.37	66.63
1	19	9	2	16	811	16.54	144		165	646	20.35	79.65
11	28	9	7	16	811	16.54	145		158	653	19.48	80.52
11	29	9	1	15	811	16.54	146		199	612	24.54	75.46
1	2	9	6	13	810	16.52	147		400	410	49.38	50.62
1	16	9	6	16	810	16.52	148		484	326	59.75	40.25
4	5	9	1	20	810	16.52	149		87	723	10.74	89.26
8	7	9	6	15	809	16.5	150		511	298	63.16	36.84
12	26	9	7	17	809	16.5	151		254	555	31.4	68.6
7	19	9	1	17	808	16.48	152		221	587	27.35	72.65
9	27	9	1	13	804	16.4	153		291	513	36.19	63.81
12	27	9	1	14	804	16.4	154		422	382	52.49	47.51
2	28	9	7	9	803	16.38	155		764	39	95.14	4.86
10	10	9	7	11	802	16.36	156		628	174	78.3	21.7
11	22	9	1	17	802	16.36	157		100	702	12.47	87.53
7	12	9	1	16	800	16.32	158		235	565	29.38	70.63
3	7	9	7	9	799	16.3	159		781	18	97.75	2.25
7	12	9	1	12	799	16.3	160		291	508	36.42	63.58
8	8	9	7	12	799	16.3	161	4903	568	231	71.09	28.91
7	3	9	6	14	798	16.28	162		537	261	67.29	32.71
1	25	9	1	16	797	16.26	163		153	644	19.2	80.8
6	28	9	1	12	796	16.23	164		315	481	39.57	60.43
6	28	9	1	17	796	16.23	165		166	630	20.85	79.15
10	18	9	1	13	796	16.23	166		252	544	31.66	68.34
3	1	9	1	17	795	16.21	167		132	663	16.6	83.4
10	18	9	1	12	795	16.21	168		276	519	34.72	65.28
4	19	9	1	18	794	16.19	169		108	686	13.6	86.4
3	6	9	6	16	792	16.15	170		297	495	37.5	62.5
6	20	9	7	14	792	16.15	171		602	190	76.01	23.99
9	13	9	1	14	791	16.13	172		246	545	31.1	68.9
11	29	9	1	17	790	16.11	173		110	680	13.92	86.08

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
12	31	9	5	15	790	16.11	174		372	418	47.09	52.91
3	22	9	1	17	787	16.05	175		147	640	18.68	81.32
1	3	9	7	16	786	16.03	176		229	557	29.13	70.87
11	22	9	1	16	786	16.03	177		112	674	14.25	85.75
5	22	9	6	20	784	15.99	178		662	122	84.44	15.56
10	10	9	7	13	783	15.97	179		623	160	79.57	20.43
8	1	9	7	12	781	15.93	180		490	291	62.74	37.26
5	17	9	1	16	780	15.91	181	4903	183	597	23.46	76.54
7	3	9	6	12	780	15.91	182		592	188	75.9	24.1
3	8	9	1	17	779	15.89	183		128	651	16.43	83.57
9	13	9	1	12	779	15.89	184		344	435	44.16	55.84
2	15	9	1	17	777	15.85	185		169	608	21.75	78.25
4	5	9	1	21	777	15.85	186		51	726	6.56	93.44
8	8	9	7	13	777	15.85	187		508	269	65.38	34.62
8	14	9	6	15	776	15.83	188		474	302	61.08	38.92
1	2	9	6	11	775	15.81	189		553	222	71.35	28.65
2	16	9	2	17	775	15.81	190		159	616	20.52	79.48
12	30	9	4	16	773	15.77	191		302	471	39.07	60.93
9	13	9	1	16	771	15.73	192		205	566	26.59	73.41
2	8	9	1	17	770	15.7	193		145	625	18.83	81.17
5	22	9	6	17	770	15.7	194		616	154	80	20
8	30	9	1	12	768	15.66	195		291	477	37.89	62.11
2	8	9	1	16	767	15.64	196		168	599	21.9	78.1
5	22	9	6	15	764	15.58	197		604	160	79.06	20.94
1	17	9	7	16	763	15.56	198		251	512	32.9	67.1
7	26	9	1	17	763	15.56	199		177	586	23.2	76.8
11	21	9	7	17	763	15.56	200		81	682	10.62	89.38

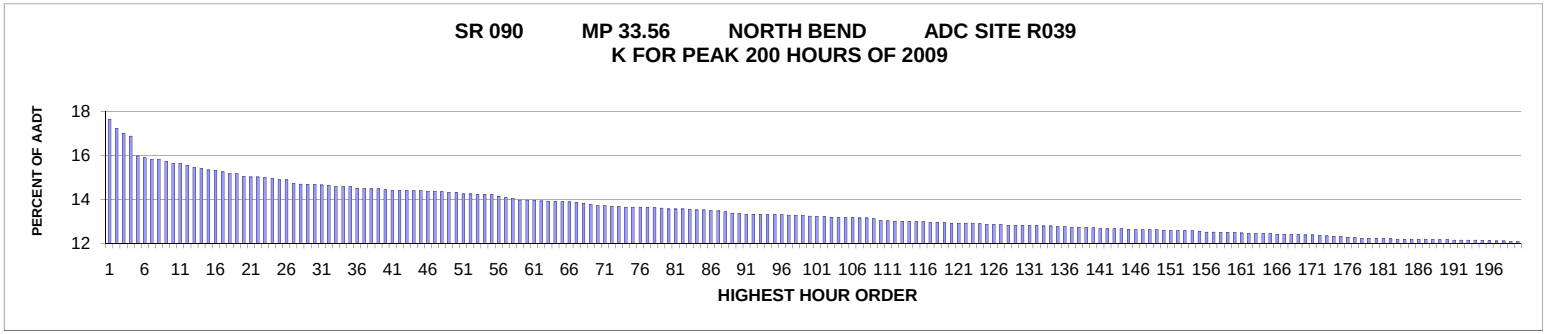

AADT= 32946 **K 30 FACTOR** 14.67 **K 100 FACTOR=** 13.24 **K 200 FACTOR** 12.07 **D FACTOR=** 62.57

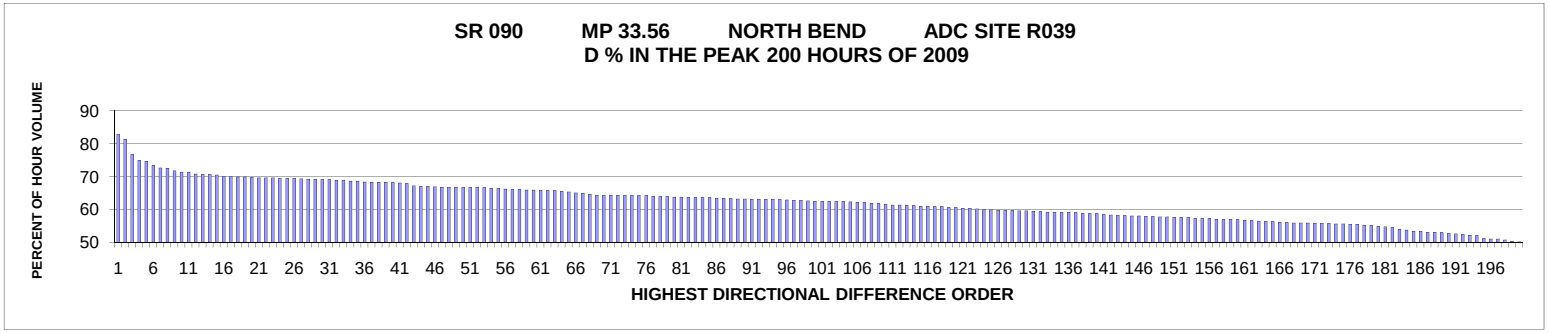

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
11	29	9	1	15	5816	17.65	1	32946	2769	3047	47.61	52.39
11	29	9	1	16	5677	17.23	2		2321	3356	40.88	59.12
11	29	9	1	14	5603	17.01	3		2973	2630	53.06	46.94
8	16	9	1	15	5566	16.89	4		2172	3394	39.02	60.98
5	22	9	6	16	5265	15.98	5		3679	1586	69.88	30.12
8	23	9	1	16	5236	15.89	6		1945	3291	37.15	62.85
8	9	9	1	14	5216	15.83	7		2057	3159	39.44	60.56
5	22	9	6	15	5214	15.83	8		3631	1583	69.64	30.36
5	22	9	6	17	5184	15.73	9		3653	1531	70.47	29.53
8	16	9	1	17	5150	15.63	10		1917	3233	37.22	62.78
7	26	9	1	16	5148	15.63	11		1838	3310	35.7	64.3
7	5	9	1	14	5125	15.56	12		2028	3097	39.57	60.43
8	9	9	1	15	5092	15.46	13		1929	3163	37.88	62.12
11	25	9	4	16	5075	15.4	14		2730	2345	53.79	46.21
8	23	9	1	15	5053	15.34	15		1934	3119	38.27	61.73
11	25	9	4	15	5049	15.33	16		2825	2224	55.95	44.05
7	5	9	1	15	5025	15.25	17		1848	3177	36.78	63.22

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	16	9	1	18	5002	15.18	18		1845	3157	36.89	63.11
11	29	9	1	13	4994	15.16	19		2910	2084	58.27	41.73
8	9	9	1	16	4960	15.05	20		1831	3129	36.92	63.08
8	9	9	1	17	4947	15.02	21	32946	1728	3219	34.93	65.07
11	29	9	1	17	4945	15.01	22		1633	3312	33.02	66.98
12	27	9	1	16	4937	14.99	23		1510	3427	30.59	69.41
7	26	9	1	15	4930	14.96	24		1979	2951	40.14	59.86
7	26	9	1	17	4905	14.89	25		1667	3238	33.99	66.01
7	12	9	1	16	4902	14.88	26		1628	3274	33.21	66.79
8	9	9	1	13	4851	14.72	27		2071	2780	42.69	57.31
5	22	9	6	18	4842	14.7	28		3387	1455	69.95	30.05
7	19	9	1	14	4838	14.68	29		1972	2866	40.76	59.24
8	16	9	1	14	4834	14.67	30		2188	2646	45.26	54.74
7	12	9	1	17	4828	14.65	31		1609	3219	33.33	66.67
5	22	9	6	14	4824	14.64	32		3344	1480	69.32	30.68
8	23	9	1	19	4810	14.6	33		1210	3600	25.16	74.84
7	26	9	1	18	4808	14.59	34		1471	3337	30.59	69.41
8	23	9	1	14	4805	14.58	35		2081	2724	43.31	56.69
7	12	9	1	15	4778	14.5	36		1763	3015	36.9	63.1
8	2	9	1	16	4774	14.49	37		1726	3048	36.15	63.85
9	4	9	6	17	4772	14.48	38		3261	1511	68.34	31.66
9	7	9	2	13	4771	14.48	39		1703	3068	35.69	64.31
9	4	9	6	15	4754	14.43	40		3288	1466	69.16	30.84
5	23	9	7	11	4749	14.41	41	32946	3645	1104	76.75	23.25
5	25	9	2	12	4748	14.41	42		1701	3047	35.83	64.17
8	16	9	1	13	4745	14.4	43		2278	2467	48.01	51.99
7	3	9	6	12	4741	14.39	44		3269	1472	68.95	31.05
8	16	9	1	16	4740	14.39	45		2039	2701	43.02	56.98
7	5	9	1	13	4737	14.38	46		1933	2804	40.81	59.19
7	26	9	1	14	4730	14.36	47		2059	2671	43.53	56.47
9	4	9	6	16	4726	14.34	48		3273	1453	69.26	30.74
5	17	9	1	18	4718	14.32	49		1580	3138	33.49	66.51
7	5	9	1	17	4713	14.31	50		1614	3099	34.25	65.75
5	10	9	1	17	4692	14.24	51		1609	3083	34.29	65.71
12	27	9	1	15	4690	14.24	52		1764	2926	37.61	62.39
7	12	9	1	14	4685	14.22	53		1796	2889	38.34	61.66
8	16	9	1	19	4684	14.22	54		1564	3120	33.39	66.61
11	25	9	4	14	4682	14.21	55		2606	2076	55.66	44.34
7	5	9	1	16	4658	14.14	56		1748	2910	37.53	62.47
5	25	9	2	13	4639	14.08	57		1670	2969	36	64
8	16	9	1	12	4633	14.06	58		2353	2280	50.79	49.21
8	14	9	6	16	4603	13.97	59		2485	2118	53.99	46.01
9	4	9	6	14	4598	13.96	60		3255	1343	70.79	29.21
9	7	9	2	14	4597	13.95	61	32946	1642	2955	35.72	64.28
5	22	9	6	19	4589	13.93	62		3116	1473	67.9	32.1
7	19	9	1	15	4582	13.91	63		1920	2662	41.9	58.1
7	26	9	1	19	4580	13.9	64		1342	3238	29.3	70.7
8	21	9	6	16	4580	13.9	65		2544	2036	55.55	44.45
8	7	9	6	15	4573	13.88	66		2601	1972	56.88	43.12
5	25	9	2	14	4566	13.86	67		1661	2905	36.38	63.62
8	9	9	1	18	4552	13.82	68		1530	3022	33.61	66.39
8	2	9	1	17	4532	13.76	69		1617	2915	35.68	64.32

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	23	9	1	13	4518	13.71	70		2160	2358	47.81	52.19
5	17	9	1	15	4516	13.71	71		1637	2879	36.25	63.75
12	27	9	1	14	4511	13.69	72		2102	2409	46.6	53.4
11	25	9	4	17	4503	13.67	73		2393	2110	53.14	46.86
8	7	9	6	14	4498	13.65	74		2656	1842	59.05	40.95
5	23	9	7	12	4497	13.65	75		3178	1319	70.67	29.33
5	10	9	1	18	4493	13.64	76		1430	3063	31.83	68.17
7	19	9	1	16	4491	13.63	77		1815	2676	40.41	59.59
6	14	9	1	16	4483	13.61	78		1632	2851	36.4	63.6
8	7	9	6	17	4481	13.6	79		2619	1862	58.45	41.55
6	14	9	1	18	4468	13.56	80		1366	3102	30.57	69.43
12	27	9	1	17	4468	13.56	81	32946	1131	3337	25.31	74.69
9	13	9	1	18	4467	13.56	82		1970	2497	44.1	55.9
7	19	9	1	17	4461	13.54	83		1545	2916	34.63	65.37
7	3	9	6	13	4451	13.51	84		2812	1639	63.18	36.82
4	26	9	1	17	4450	13.51	85		1336	3114	30.02	69.98
7	19	9	1	13	4446	13.49	86		1954	2492	43.95	56.05
10	11	9	1	18	4438	13.47	87		1689	2749	38.06	61.94
7	5	9	1	18	4424	13.43	88		1326	3098	29.97	70.03
7	19	9	1	19	4406	13.37	89		1362	3044	30.91	69.09
8	14	9	6	15	4402	13.36	90		2413	1989	54.82	45.18
8	7	9	6	16	4391	13.33	91		2579	1812	58.73	41.27
8	9	9	1	12	4391	13.33	92		2147	2244	48.9	51.1
8	2	9	1	15	4389	13.32	93		1698	2691	38.69	61.31
4	19	9	1	17	4381	13.3	94		1482	2899	33.83	66.17
11	29	9	1	12	4381	13.3	95		2821	1560	64.39	35.61
9	13	9	1	17	4377	13.29	96		1763	2614	40.28	59.72
7	19	9	1	18	4375	13.28	97		1390	2985	31.77	68.23
8	14	9	6	17	4373	13.27	98		2505	1868	57.28	42.72
7	12	9	1	18	4369	13.26	99		1642	2727	37.58	62.42
8	30	9	1	13	4361	13.24	100		1844	2517	42.28	57.72
7	3	9	6	14	4359	13.23	101	32946	2457	1902	56.37	43.63
8	2	9	1	14	4359	13.23	102		1841	2518	42.23	57.77
9	7	9	2	12	4343	13.18	103		1687	2656	38.84	61.16
7	24	9	6	15	4337	13.16	104		2414	1923	55.66	44.34
7	17	9	6	16	4336	13.16	105		2417	1919	55.74	44.26
8	7	9	6	13	4336	13.16	106		2587	1749	59.66	40.34
7	24	9	6	16	4334	13.15	107		2425	1909	55.95	44.05
7	26	9	1	13	4334	13.15	108		2048	2286	47.25	52.75
5	17	9	1	16	4322	13.12	109		1542	2780	35.68	64.32
3	29	9	1	15	4292	13.03	110		1817	2475	42.33	57.67
9	7	9	2	17	4290	13.02	111		1303	2987	30.37	69.63
7	12	9	1	13	4287	13.01	112		1699	2588	39.63	60.37
9	13	9	1	15	4282	13	113		1840	2442	42.97	57.03
3	29	9	1	16	4281	12.99	114		1676	2605	39.15	60.85
6	14	9	1	15	4277	12.98	115		1552	2725	36.29	63.71
5	17	9	1	17	4275	12.98	116		1529	2746	35.77	64.23
10	18	9	1	17	4268	12.95	117		1717	2551	40.23	59.77
3	29	9	1	17	4266	12.95	118		1418	2848	33.24	66.76
5	25	9	2	16	4264	12.94	119		1580	2684	37.05	62.95
1	4	9	1	15	4255	12.92	120		1216	3039	28.58	71.42
6	14	9	1	17	4255	12.92	121	32946	1410	2845	33.14	66.86

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	3	9	6	11	4255	12.92	122		3122	1133	73.37	26.63
9	4	9	6	18	4254	12.91	123		2806	1448	65.96	34.04
5	22	9	6	13	4248	12.89	124		2902	1346	68.31	31.69
7	10	9	6	15	4232	12.85	125		2260	1972	53.4	46.6
9	7	9	2	16	4231	12.84	126		1481	2750	35	65
9	5	9	7	12	4230	12.84	127		2670	1560	63.12	36.88
9	4	9	6	13	4225	12.82	128		3032	1193	71.76	28.24
8	15	9	7	12	4224	12.82	129		2575	1649	60.96	39.04
7	17	9	6	15	4223	12.82	130		2329	1894	55.15	44.85
5	23	9	7	10	4220	12.81	131		3435	785	81.4	18.6
3	1	9	1	16	4217	12.8	132		1398	2819	33.15	66.85
12	26	9	7	13	4211	12.78	133		2664	1547	63.26	36.74
5	10	9	1	16	4210	12.78	134		1539	2671	36.56	63.44
5	3	9	1	18	4203	12.76	135		1272	2931	30.26	69.74
8	14	9	6	14	4201	12.75	136		2332	1869	55.51	44.49
9	13	9	1	16	4195	12.73	137		1793	2402	42.74	57.26
5	25	9	2	11	4191	12.72	138		1621	2570	38.68	61.32
7	5	9	1	12	4186	12.71	139		1815	2371	43.36	56.64
10	11	9	1	16	4183	12.7	140		1532	2651	36.62	63.38
5	25	9	2	15	4172	12.66	141	32946	1516	2656	36.34	63.66
9	7	9	2	15	4171	12.66	142		1577	2594	37.81	62.19
7	24	9	6	17	4168	12.65	143		2421	1747	58.09	41.91
6	7	9	1	16	4167	12.65	144		1331	2836	31.94	68.06
10	25	9	1	17	4164	12.64	145		1385	2779	33.26	66.74
6	7	9	1	17	4156	12.61	146		1303	2853	31.35	68.65
7	26	9	1	12	4156	12.61	147		2121	2035	51.03	48.97
7	12	9	1	19	4155	12.61	148		1283	2872	30.88	69.12
5	17	9	1	14	4153	12.61	149		1678	2475	40.4	59.6
9	20	9	1	17	4149	12.59	150		1623	2526	39.12	60.88
7	19	9	1	12	4142	12.57	151		2062	2080	49.78	50.22
8	2	9	1	18	4140	12.57	152		1414	2726	34.15	65.85
9	5	9	7	11	4140	12.57	153		2828	1312	68.31	31.69
12	27	9	1	13	4137	12.56	154		2309	1828	55.81	44.19
9	27	9	1	18	4132	12.54	155		1529	2603	37	63
8	16	9	1	20	4123	12.51	156		1130	2993	27.41	72.59
5	25	9	2	17	4122	12.51	157		1361	2761	33.02	66.98
2	16	9	2	16	4114	12.49	158		1714	2400	41.66	58.34
6	19	9	6	15	4114	12.49	159		2477	1637	60.21	39.79
8	21	9	6	17	4114	12.49	160		2493	1621	60.6	39.4
9	4	9	6	19	4104	12.46	161	32946	2568	1536	62.57	37.43
10	18	9	1	18	4103	12.45	162		1717	2386	41.85	58.15
6	19	9	6	16	4101	12.45	163		2517	1584	61.38	38.62
12	26	9	7	15	4100	12.44	164		1799	2301	43.88	56.12
7	17	9	6	17	4096	12.43	165		2404	1692	58.69	41.31
2	8	9	1	16	4088	12.41	166		1242	2846	30.38	69.62
4	26	9	1	16	4087	12.41	167		1446	2641	35.38	64.62
6	19	9	6	17	4085	12.4	168		2611	1474	63.92	36.08
2	8	9	1	17	4082	12.39	169		1116	2966	27.34	72.66
7	2	9	5	17	4077	12.37	170		2540	1537	62.3	37.7
12	26	9	7	16	4075	12.37	171		1357	2718	33.3	66.7
6	14	9	1	14	4068	12.35	172		1674	2394	41.15	58.85
7	17	9	6	14	4066	12.34	173		2269	1797	55.8	44.2

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	31	9	6	16	4059	12.32	174		2338	1721	57.6	42.4
8	14	9	6	18	4057	12.31	175		2336	1721	57.58	42.42
7	2	9	5	15	4041	12.27	176		2423	1618	59.96	40.04
12	26	9	7	14	4031	12.24	177		2138	1893	53.04	46.96
4	4	9	7	19	4030	12.23	178		692	3338	17.17	82.83
4	19	9	1	18	4029	12.23	179		1374	2655	34.1	65.9
3	22	9	1	15	4025	12.22	180		1835	2190	45.59	54.41
9	5	9	7	13	4022	12.21	181	32946	2514	1508	62.51	37.49
5	25	9	2	18	4018	12.2	182		1151	2867	28.65	71.35
7	24	9	6	14	4014	12.18	183		2219	1795	55.28	44.72
7	3	9	6	15	4013	12.18	184		2020	1993	50.34	49.66
7	31	9	6	17	4010	12.17	185		2324	1686	57.96	42.04
8	7	9	6	18	4010	12.17	186		2320	1690	57.86	42.14
4	19	9	1	16	4009	12.17	187		1499	2510	37.39	62.61
7	10	9	6	16	4008	12.17	188		2107	1901	52.57	47.43
9	18	9	6	14	4007	12.16	189		2764	1243	68.98	31.02
9	27	9	1	17	4005	12.16	190		1380	2625	34.46	65.54
10	11	9	1	15	4004	12.15	191		1629	2375	40.68	59.32
7	12	9	1	12	4002	12.15	192		1719	2283	42.95	57.05
5	3	9	1	17	3999	12.14	193		1255	2744	31.38	68.62
8	21	9	6	15	3999	12.14	194		2364	1635	59.11	40.89
8	2	9	1	13	3995	12.13	195		1951	2044	48.84	51.16
6	12	9	6	15	3990	12.11	196		2247	1743	56.32	43.68
10	25	9	1	16	3987	12.1	197		1451	2536	36.39	63.61
8	15	9	7	11	3986	12.1	198		2639	1347	66.21	33.79
8	30	9	1	18	3978	12.07	199		1305	2673	32.81	67.19
10	11	9	1	17	3976	12.07	200		1610	2366	40.49	59.51

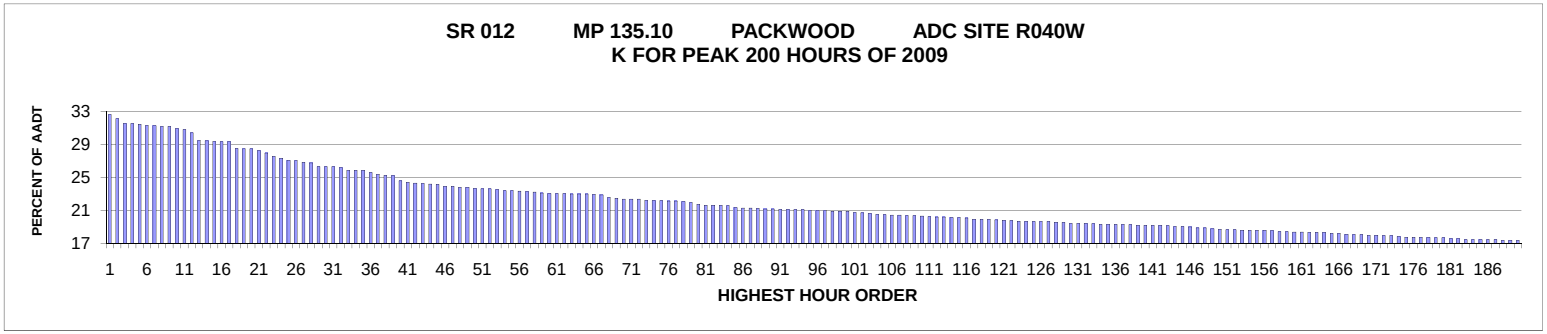

AADT= 1814 **K 30 FACTOR** 26.3 **K 100 FACTOR=** 20.89 **K 200 FACTOR** 17.36 **D FACTOR=** 55.17

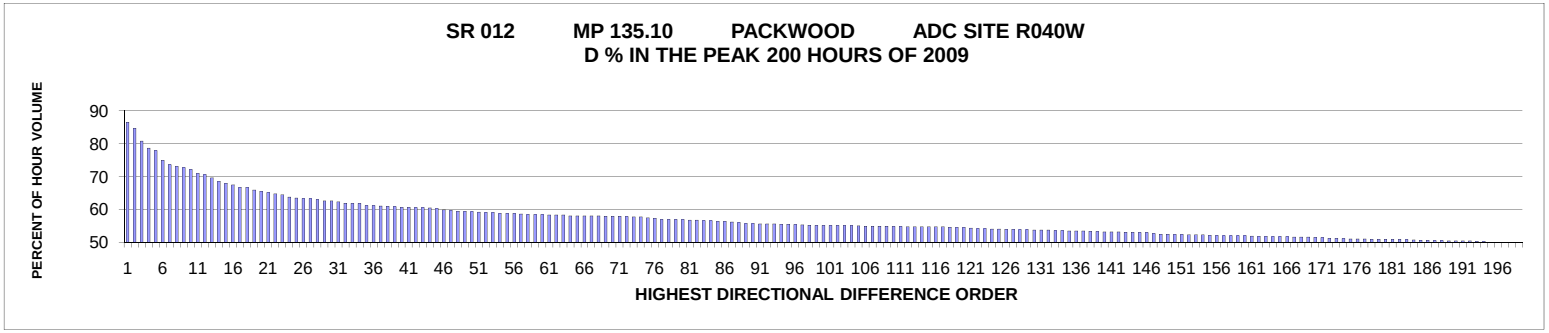

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
9	5	9	7	11	594	32.75	1	1814	162	432	27.27	72.73
9	5	9	7	12	592	32.64	2		186	406	31.42	68.58
5	23	9	7	15	583	32.14	3		337	246	57.8	42.2
5	23	9	7	14	572	31.53	4		266	306	46.5	53.5
5	25	9	2	13	572	31.53	5		258	314	45.1	54.9
9	6	9	1	14	571	31.48	6		308	263	53.94	46.06
9	6	9	1	13	568	31.31	7		261	307	45.95	54.05
9	5	9	7	14	567	31.26	8		292	275	51.5	48.5
5	24	9	1	16	566	31.2	9		310	256	54.77	45.23
5	25	9	2	15	566	31.2	10		283	283	50	50
5	23	9	7	17	561	30.93	11		396	165	70.59	29.41
5	23	9	7	12	559	30.82	12		140	419	25.04	74.96
5	23	9	7	16	552	30.43	13		368	184	66.67	33.33
5	25	9	2	12	535	29.49	14		253	282	47.29	52.71
5	24	9	1	12	534	29.44	15		182	352	34.08	65.92
5	24	9	1	15	533	29.38	16		315	218	59.1	40.9
5	23	9	7	13	532	29.33	17		195	337	36.65	63.35

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
5	24	9	1	14	532	29.33	18		242	290	45.49	54.51
9	5	9	7	13	517	28.5	19		204	313	39.46	60.54
5	25	9	2	14	516	28.45	20		263	253	50.97	49.03
9	7	9	2	14	516	28.45	21	1814	291	225	56.4	43.6
7	26	9	1	13	512	28.22	22		235	277	45.9	54.1
5	25	9	2	16	507	27.95	23		265	242	52.27	47.73
5	23	9	7	11	500	27.56	24		96	404	19.2	80.8
9	5	9	7	15	496	27.34	25		280	216	56.45	43.55
5	24	9	1	13	491	27.07	26		178	313	36.25	63.75
9	5	9	7	16	490	27.01	27		297	193	60.61	39.39
9	7	9	2	15	487	26.85	28		282	205	57.91	42.09
7	26	9	1	14	485	26.74	29		237	248	48.87	51.13
5	24	9	1	17	477	26.3	30		277	200	58.07	41.93
7	5	9	1	15	477	26.3	31		272	205	57.02	42.98
9	6	9	1	12	477	26.3	32		145	332	30.4	69.6
9	7	9	2	12	475	26.19	33		252	223	53.05	46.95
7	19	9	1	15	469	25.85	34		234	235	49.89	50.11
7	26	9	1	15	469	25.85	35		215	254	45.84	54.16
8	16	9	1	15	469	25.85	36		223	246	47.55	52.45
9	7	9	2	13	464	25.58	37		268	196	57.76	42.24
8	16	9	1	14	461	25.41	38		224	237	48.59	51.41
7	3	9	6	14	458	25.25	39		192	266	41.92	58.08
9	6	9	1	17	457	25.19	40		296	161	64.77	35.23
5	25	9	2	17	446	24.59	41	1814	206	240	46.19	53.81
7	26	9	1	16	443	24.42	42		202	241	45.6	54.4
7	19	9	1	13	441	24.31	43		223	218	50.57	49.43
9	5	9	7	17	440	24.26	44		272	168	61.82	38.18
9	7	9	2	16	439	24.2	45		228	211	51.94	48.06
7	5	9	1	13	438	24.15	46		236	202	53.88	46.12
8	16	9	1	17	434	23.93	47		195	239	44.93	55.07
9	6	9	1	15	434	23.93	48		219	215	50.46	49.54
8	9	9	1	13	432	23.81	49		223	209	51.62	48.38
8	16	9	1	13	432	23.81	50		214	218	49.54	50.46
7	12	9	1	14	429	23.65	51		180	249	41.96	58.04
9	5	9	7	10	428	23.59	52		113	315	26.4	73.6
9	6	9	1	16	428	23.59	53		224	204	52.34	47.66
7	3	9	6	13	426	23.48	54		191	235	44.84	55.16
8	23	9	1	15	424	23.37	55		197	227	46.46	53.54
9	4	9	6	17	424	23.37	56		192	232	45.28	54.72
8	9	9	1	16	423	23.32	57		234	189	55.32	44.68
7	19	9	1	14	422	23.26	58		211	211	50	50
5	23	9	7	18	421	23.21	59		281	140	66.75	33.25
8	16	9	1	16	419	23.1	60		211	208	50.36	49.64
6	28	9	1	16	418	23.04	61	1814	165	253	39.47	60.53
7	5	9	1	14	418	23.04	62		211	207	50.48	49.52
7	26	9	1	17	418	23.04	63		202	216	48.33	51.67
5	24	9	1	18	417	22.99	64		253	164	60.67	39.33
7	5	9	1	16	417	22.99	65		236	181	56.59	43.41
8	2	9	1	18	417	22.99	66		156	261	37.41	62.59
7	18	9	7	14	416	22.93	67		169	247	40.63	59.38
7	3	9	6	15	415	22.88	68		155	260	37.35	62.65
6	28	9	1	15	409	22.55	69		174	235	42.54	57.46

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
9	4	9	6	18	408	22.49	70		191	217	46.81	53.19
5	25	9	2	11	406	22.38	71		189	217	46.55	53.45
7	19	9	1	12	406	22.38	72		208	198	51.23	48.77
8	2	9	1	16	406	22.38	73		225	181	55.42	44.58
8	23	9	1	16	403	22.22	74		211	192	52.36	47.64
7	12	9	1	16	402	22.16	75		205	197	51	49
8	2	9	1	13	402	22.16	76		193	209	48.01	51.99
4	5	9	1	19	401	22.11	77		49	352	12.22	87.78
7	5	9	1	17	401	22.11	78		236	165	58.85	41.15
7	19	9	1	16	400	22.05	79		193	207	48.25	51.75
7	19	9	1	17	398	21.94	80		206	192	51.76	48.24
9	4	9	6	13	394	21.72	81	1814	163	231	41.37	58.63
8	2	9	1	15	392	21.61	82		234	158	59.69	40.31
8	16	9	1	12	392	21.61	83		193	199	49.23	50.77
9	4	9	6	15	392	21.61	84		188	204	47.96	52.04
6	28	9	1	14	391	21.55	85		153	238	39.13	60.87
7	24	9	6	16	387	21.33	86		151	236	39.02	60.98
9	13	9	1	16	386	21.28	87		189	197	48.96	51.04
9	13	9	1	17	386	21.28	88		212	174	54.92	45.08
9	20	9	1	16	385	21.22	89		145	240	37.66	62.34
7	11	9	7	14	384	21.17	90		180	204	46.88	53.13
9	5	9	7	18	384	21.17	91		259	125	67.45	32.55
6	28	9	1	13	383	21.11	92		185	198	48.3	51.7
7	12	9	1	15	382	21.06	93		176	206	46.07	53.93
7	18	9	7	13	382	21.06	94		133	249	34.82	65.18
9	4	9	6	19	382	21.06	95		184	198	48.17	51.83
8	2	9	1	12	380	20.95	96		178	202	46.84	53.16
8	9	9	1	15	380	20.95	97		199	181	52.37	47.63
9	4	9	6	16	380	20.95	98		182	198	47.89	52.11
5	22	9	6	17	379	20.89	99		186	193	49.08	50.92
5	23	9	7	10	379	20.89	100		102	277	26.91	73.09
8	23	9	1	17	379	20.89	101	1814	186	193	49.08	50.92
8	23	9	1	14	376	20.73	102		184	192	48.94	51.06
7	25	9	7	12	375	20.67	103		169	206	45.07	54.93
9	6	9	1	11	374	20.62	104		133	241	35.56	64.44
8	9	9	1	14	372	20.51	105		184	188	49.46	50.54
8	15	9	7	13	371	20.45	106		136	235	36.66	63.34
7	11	9	7	13	370	20.4	107		144	226	38.92	61.08
7	26	9	1	12	370	20.4	108		185	185	50	50
7	3	9	6	17	369	20.34	109		152	217	41.19	58.81
7	12	9	1	13	369	20.34	110		167	202	45.26	54.74
6	28	9	1	17	368	20.29	111		153	215	41.58	58.42
7	12	9	1	17	367	20.23	112		209	158	56.95	43.05
7	19	9	1	18	366	20.18	113		189	177	51.64	48.36
7	26	9	1	11	366	20.18	114		195	171	53.28	46.72
7	3	9	6	11	365	20.12	115		152	213	41.64	58.36
8	1	9	7	12	365	20.12	116		191	174	52.33	47.67
8	9	9	1	12	364	20.07	117		178	186	48.9	51.1
7	17	9	6	16	361	19.9	118		156	205	43.21	56.79
7	18	9	7	15	361	19.9	119		150	211	41.55	58.45
7	25	9	7	14	361	19.9	120		162	199	44.88	55.12
9	7	9	2	17	360	19.85	121	1814	177	183	49.17	50.83

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	30	9	1	16	359	19.79	122		153	206	42.62	57.38
7	11	9	7	12	358	19.74	123		146	212	40.78	59.22
8	30	9	1	15	357	19.68	124		161	196	45.1	54.9
4	5	9	1	18	356	19.63	125		76	280	21.35	78.65
7	17	9	6	14	356	19.63	126		156	200	43.82	56.18
7	17	9	6	15	356	19.63	127		130	226	36.52	63.48
9	13	9	1	15	356	19.63	128		161	195	45.22	54.78
5	24	9	1	11	355	19.57	129		103	252	29.01	70.99
7	25	9	7	13	354	19.51	130		131	223	37.01	62.99
4	5	9	1	20	352	19.4	131		54	298	15.34	84.66
8	23	9	1	12	352	19.4	132		176	176	50	50
10	11	9	1	16	352	19.4	133		98	254	27.84	72.16
8	23	9	1	13	351	19.35	134		178	173	50.71	49.29
7	12	9	1	12	350	19.29	135		159	191	45.43	54.57
7	17	9	6	12	350	19.29	136		147	203	42	58
8	15	9	7	16	350	19.29	137		157	193	44.86	55.14
9	20	9	1	17	350	19.29	138		136	214	38.86	61.14
7	31	9	6	13	349	19.24	139		164	185	46.99	53.01
7	3	9	6	16	348	19.18	140		145	203	41.67	58.33
7	24	9	6	18	348	19.18	141	1814	146	202	41.95	58.05
8	7	9	6	15	348	19.18	142		156	192	44.83	55.17
8	9	9	1	17	348	19.18	143		167	181	47.99	52.01
9	7	9	2	11	347	19.13	144		193	154	55.62	44.38
5	22	9	6	19	345	19.02	145		179	166	51.88	48.12
9	13	9	1	13	345	19.02	146		156	189	45.22	54.78
7	5	9	1	12	344	18.96	147		206	138	59.88	40.12
8	1	9	7	11	342	18.85	148		144	198	42.11	57.89
8	7	9	6	14	342	18.85	149		142	200	41.52	58.48
7	18	9	7	12	340	18.74	150		151	189	44.41	55.59
7	17	9	6	17	339	18.69	151		149	190	43.95	56.05
5	22	9	6	15	338	18.63	152		156	182	46.15	53.85
7	5	9	1	18	338	18.63	153		192	146	56.8	43.2
7	3	9	6	12	337	18.58	154		151	186	44.81	55.19
7	11	9	7	15	337	18.58	155		150	187	44.51	55.49
8	14	9	6	15	337	18.58	156		137	200	40.65	59.35
9	20	9	1	15	337	18.58	157		145	192	43.03	56.97
6	21	9	1	13	336	18.52	158		132	204	39.29	60.71
2	15	9	1	17	334	18.41	159		45	289	13.47	86.53
8	16	9	1	18	334	18.41	160		155	179	46.41	53.59
5	25	9	2	18	333	18.36	161	1814	151	182	45.35	54.65
8	15	9	7	12	333	18.36	162		175	158	52.55	47.45
5	22	9	6	14	332	18.3	163		144	188	43.37	56.63
5	22	9	6	16	332	18.3	164		182	150	54.82	45.18
8	14	9	6	16	332	18.3	165		150	182	45.18	54.82
4	5	9	1	17	330	18.19	166		73	257	22.12	77.88
7	25	9	7	15	330	18.19	167		142	188	43.03	56.97
5	22	9	6	18	328	18.08	168		163	165	49.7	50.3
6	21	9	1	14	327	18.03	169		153	174	46.79	53.21
8	14	9	6	14	327	18.03	170		148	179	45.26	54.74
5	17	9	1	16	326	17.97	171		124	202	38.04	61.96
6	21	9	1	17	326	17.97	172		152	174	46.63	53.37
5	23	9	7	19	325	17.92	173		213	112	65.54	34.46

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	30	9	1	14	325	17.92	174		149	176	45.85	54.15
8	2	9	1	17	323	17.81	175		180	143	55.73	44.27
5	22	9	6	13	322	17.75	176		158	164	49.07	50.93
8	30	9	1	13	322	17.75	177		157	165	48.76	51.24
9	5	9	7	19	322	17.75	178		219	103	68.01	31.99
8	1	9	7	17	321	17.7	179		130	191	40.5	59.5
7	24	9	6	17	320	17.64	180		122	198	38.13	61.88
8	8	9	7	12	320	17.64	181	1814	149	171	46.56	53.44
5	24	9	1	19	318	17.53	182		188	130	59.12	40.88
6	27	9	7	13	318	17.53	183		147	171	46.23	53.77
5	22	9	6	20	316	17.42	184		160	156	50.63	49.37
6	14	9	1	15	316	17.42	185		150	166	47.47	52.53
6	28	9	1	12	316	17.42	186		130	186	41.14	58.86
7	24	9	6	15	316	17.42	187		146	170	46.2	53.8
8	15	9	7	17	316	17.42	188		140	176	44.3	55.7
8	7	9	6	16	315	17.36	189		125	190	39.68	60.32
8	7	9	6	17	315	17.36	190		140	175	44.44	55.56
9	4	9	6	14	315	17.36	191		156	159	49.52	50.48
12	27	9	1	17	315	17.36	192		62	253	19.68	80.32
8	1	9	7	14	314	17.31	193		143	171	45.54	54.46
8	16	9	1	11	313	17.25	194		150	163	47.92	52.08
7	25	9	7	16	312	17.2	195		138	174	44.23	55.77
8	21	9	6	16	312	17.2	196		136	176	43.59	56.41
7	31	9	6	17	311	17.14	197		123	188	39.55	60.45
2	14	9	7	17	310	17.09	198		36	274	11.61	88.39
7	5	9	1	11	309	17.03	199		180	129	58.25	41.75
10	11	9	1	17	309	17.03	200		107	202	34.63	65.37

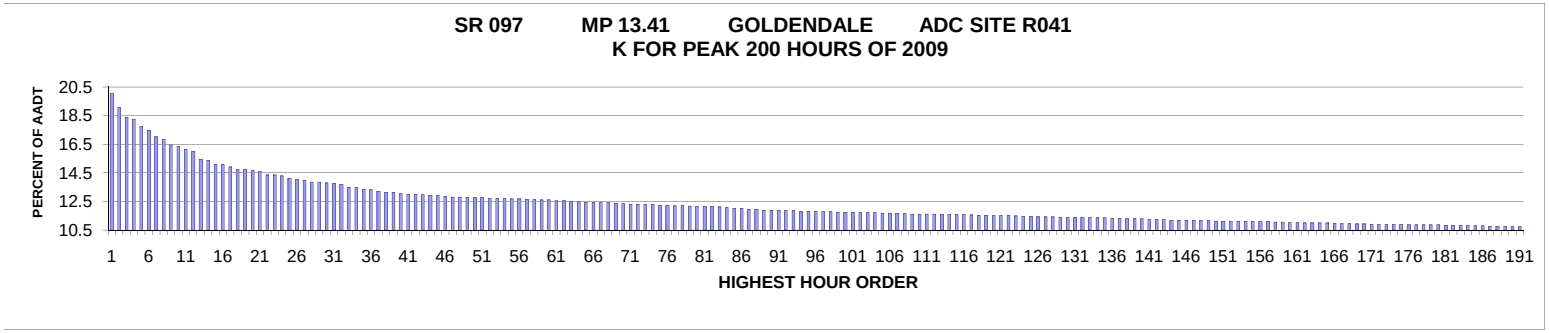

AADT= 4769 **K 30 FACTOR=** 14.59 **K 100 FACTOR=** 11.87 **K 200 FACTOR=** 10.72 **D FACTOR=** 53.74

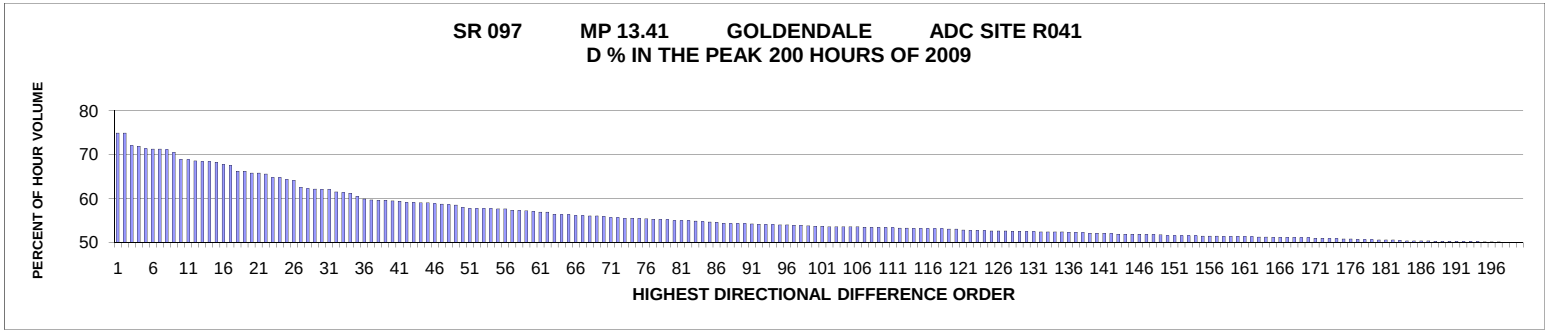

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	9	9	1	14	955	20.03	1	4769	300	655	31.41	68.59
8	9	9	1	15	909	19.06	2		320	589	35.2	64.8
8	9	9	1	16	877	18.39	3		359	518	40.94	59.06
8	9	9	1	13	870	18.24	4		251	619	28.85	71.15
9	7	9	2	14	846	17.74	5		291	555	34.4	65.6
8	7	9	6	16	833	17.47	6		442	391	53.06	46.94
5	17	9	1	14	811	17.01	7		233	578	28.73	71.27
8	7	9	6	14	802	16.82	8		553	249	68.95	31.05
9	7	9	2	13	784	16.44	9		244	540	31.12	68.88
5	17	9	1	15	779	16.33	10		224	555	28.75	71.25
8	7	9	6	15	770	16.15	11		555	215	72.08	27.92
5	22	9	6	17	763	16	12		414	349	54.26	45.74
8	7	9	6	13	737	15.45	13		520	217	70.56	29.44
9	7	9	2	15	733	15.37	14		322	411	43.93	56.07
8	9	9	1	17	719	15.08	15		334	385	46.45	53.55
9	7	9	2	16	718	15.06	16		340	378	47.35	52.65
8	7	9	6	12	711	14.91	17		471	240	66.24	33.76

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
5	17	9	1	12	703	14.74	18		176	527	25.04	74.96
9	4	9	6	14	702	14.72	19		436	266	62.11	37.89
5	17	9	1	16	699	14.66	20		239	460	34.19	65.81
5	22	9	6	18	696	14.59	21	4769	415	281	59.63	40.37
8	9	9	1	12	684	14.34	22		216	468	31.58	68.42
9	7	9	2	12	684	14.34	23		217	467	31.73	68.27
5	17	9	1	13	681	14.28	24		191	490	28.05	71.95
5	22	9	6	16	672	14.09	25		369	303	54.91	45.09
9	4	9	6	17	669	14.03	26		381	288	56.95	43.05
8	23	9	1	16	667	13.99	27		385	282	57.72	42.28
9	4	9	6	15	660	13.84	28		406	254	61.52	38.48
9	4	9	6	16	660	13.84	29		404	256	61.21	38.79
5	22	9	6	15	657	13.78	30		363	294	55.25	44.75
5	25	9	2	14	655	13.73	31		282	373	43.05	56.95
8	16	9	1	16	652	13.67	32		357	295	54.75	45.25
8	7	9	6	17	644	13.5	33		323	321	50.16	49.84
9	4	9	6	13	641	13.44	34		411	230	64.12	35.88
8	23	9	1	15	637	13.36	35		379	258	59.5	40.5
9	5	9	7	12	635	13.32	36		343	292	54.02	45.98
5	15	9	6	16	630	13.21	37		408	222	64.76	35.24
8	16	9	1	15	626	13.13	38		326	300	52.08	47.92
9	6	9	1	14	626	13.13	39		263	363	42.01	57.99
9	6	9	1	15	622	13.04	40		295	327	47.43	52.57
6	21	9	1	16	620	13	41	4769	344	276	55.48	44.52
11	25	9	4	16	620	13	42		285	335	45.97	54.03
5	25	9	2	15	618	12.96	43		287	331	46.44	53.56
9	7	9	2	17	617	12.94	44		294	323	47.65	52.35
5	16	9	7	12	615	12.9	45		417	198	67.8	32.2
8	23	9	1	17	614	12.87	46		346	268	56.35	43.65
5	25	9	2	16	610	12.79	47		286	324	46.89	53.11
7	17	9	6	17	610	12.79	48		294	316	48.2	51.8
6	19	9	6	17	609	12.77	49		284	325	46.63	53.37
7	5	9	1	15	609	12.77	50		305	304	50.08	49.92
5	15	9	6	18	608	12.75	51		378	230	62.17	37.83
9	6	9	1	13	606	12.71	52		229	377	37.79	62.21
8	16	9	1	17	605	12.69	53		354	251	58.51	41.49
11	25	9	4	15	605	12.69	54		291	314	48.1	51.9
5	22	9	6	19	604	12.67	55		357	247	59.11	40.89
5	25	9	2	17	604	12.67	56		325	279	53.81	46.19
9	4	9	6	12	603	12.64	57		356	247	59.04	40.96
7	12	9	1	14	602	12.62	58		302	300	50.17	49.83
8	7	9	6	19	601	12.6	59		232	369	38.6	61.4
11	29	9	1	15	601	12.6	60		315	286	52.41	47.59
7	19	9	1	15	598	12.54	61	4769	307	291	51.34	48.66
7	26	9	1	14	598	12.54	62		308	290	51.51	48.49
8	7	9	6	11	596	12.5	63		373	223	62.58	37.42
7	5	9	1	16	594	12.46	64		312	282	52.53	47.47
7	5	9	1	14	593	12.43	65		315	278	53.12	46.88
5	15	9	6	15	592	12.41	66		350	242	59.12	40.88
9	5	9	7	14	592	12.41	67		348	244	58.78	41.22
6	26	9	6	17	591	12.39	68		289	302	48.9	51.1
9	5	9	7	13	590	12.37	69		324	266	54.92	45.08

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	19	9	1	14	588	12.33	70		272	316	46.26	53.74
5	15	9	6	17	587	12.31	71		355	232	60.48	39.52
8	16	9	1	14	587	12.31	72		292	295	49.74	50.26
11	29	9	1	16	587	12.31	73		319	268	54.34	45.66
8	9	9	1	11	586	12.29	74		168	418	28.67	71.33
7	5	9	1	17	582	12.2	75		302	280	51.89	48.11
7	26	9	1	16	582	12.2	76		299	283	51.37	48.63
8	23	9	1	13	582	12.2	77		311	271	53.44	46.56
11	25	9	4	14	582	12.2	78		272	310	46.74	53.26
8	14	9	6	17	581	12.18	79		275	306	47.33	52.67
7	24	9	6	16	580	12.16	80		302	278	52.07	47.93
9	18	9	6	17	580	12.16	81	4769	292	288	50.34	49.66
7	24	9	6	15	578	12.12	82		303	275	52.42	47.58
6	26	9	6	16	577	12.1	83		289	288	50.09	49.91
6	19	9	6	16	575	12.06	84		265	310	46.09	53.91
7	19	9	1	17	573	12.02	85		310	263	54.1	45.9
7	26	9	1	13	573	12.02	86		273	300	47.64	52.36
5	23	9	7	11	570	11.95	87		311	259	54.56	45.44
9	5	9	7	11	570	11.95	88		308	262	54.04	45.96
8	21	9	6	17	567	11.89	89		283	284	49.91	50.09
7	12	9	1	16	566	11.87	90		311	255	54.95	45.05
8	16	9	1	18	566	11.87	91		338	228	59.72	40.28
5	17	9	1	17	565	11.85	92		241	324	42.65	57.35
8	9	9	1	18	565	11.85	93		234	331	41.42	58.58
5	22	9	6	20	562	11.78	94		334	228	59.43	40.57
7	3	9	6	12	562	11.78	95		250	312	44.48	55.52
7	12	9	1	13	562	11.78	96		238	324	42.35	57.65
7	31	9	6	16	561	11.76	97		262	299	46.7	53.3
9	4	9	6	18	561	11.76	98		294	267	52.41	47.59
7	5	9	1	13	560	11.74	99		272	288	48.57	51.43
7	12	9	1	15	560	11.74	100		290	270	51.79	48.21
6	21	9	1	15	559	11.72	101	4769	291	268	52.06	47.94
7	17	9	6	15	558	11.7	102		287	271	51.43	48.57
7	19	9	1	13	558	11.7	103		281	277	50.36	49.64
8	14	9	6	15	558	11.7	104		261	297	46.77	53.23
8	21	9	6	15	557	11.68	105		282	275	50.63	49.37
7	26	9	1	15	556	11.66	106		283	273	50.9	49.1
8	14	9	6	16	556	11.66	107		301	255	54.14	45.86
8	2	9	1	15	555	11.64	108		285	270	51.35	48.65
6	28	9	1	16	554	11.62	109		296	258	53.43	46.57
7	11	9	7	15	554	11.62	110		332	222	59.93	40.07
8	23	9	1	14	554	11.62	111		311	243	56.14	43.86
11	25	9	4	17	554	11.62	112		276	278	49.82	50.18
6	28	9	1	14	553	11.6	113		296	257	53.53	46.47
8	6	9	5	17	553	11.6	114		308	245	55.7	44.3
7	3	9	6	15	552	11.57	115		315	237	57.07	42.93
9	25	9	6	16	552	11.57	116		279	273	50.54	49.46
7	3	9	6	13	551	11.55	117		286	265	51.91	48.09
7	3	9	6	14	550	11.53	118		310	240	56.36	43.64
7	31	9	6	15	550	11.53	119		276	274	50.18	49.82
7	24	9	6	17	549	11.51	120		283	266	51.55	48.45
7	17	9	6	18	548	11.49	121	4769	247	301	45.07	54.93

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	31	9	6	17	548	11.49	122		273	275	49.82	50.18
11	25	9	4	13	547	11.47	123		266	281	48.63	51.37
7	12	9	1	12	546	11.45	124		231	315	42.31	57.69
9	18	9	6	15	546	11.45	125		278	268	50.92	49.08
6	28	9	1	15	544	11.41	126		277	267	50.92	49.08
7	2	9	5	17	544	11.41	127		269	275	49.45	50.55
8	23	9	1	18	544	11.41	128		307	237	56.43	43.57
7	17	9	6	13	543	11.39	129		290	253	53.41	46.59
5	16	9	7	11	542	11.37	130		366	176	67.53	32.47
6	12	9	6	17	542	11.37	131		277	265	51.11	48.89
8	16	9	1	13	542	11.37	132		256	286	47.23	52.77
11	29	9	1	17	542	11.37	133		310	232	57.2	42.8
7	2	9	5	18	541	11.34	134		280	261	51.76	48.24
10	16	9	6	17	541	11.34	135		254	287	46.95	53.05
6	26	9	6	13	540	11.32	136		266	274	49.26	50.74
8	30	9	1	14	539	11.3	137		274	265	50.83	49.17
5	25	9	2	13	538	11.28	138		230	308	42.75	57.25
6	14	9	1	16	538	11.28	139		281	257	52.23	47.77
7	17	9	6	14	538	11.28	140		289	249	53.72	46.28
7	10	9	6	14	536	11.24	141	4769	260	276	48.51	51.49
8	2	9	1	14	536	11.24	142		265	271	49.44	50.56
8	21	9	6	18	534	11.2	143		260	274	48.69	51.31
5	16	9	7	13	533	11.18	144		343	190	64.35	35.65
6	12	9	6	16	533	11.18	145		238	295	44.65	55.35
7	3	9	6	16	533	11.18	146		283	250	53.1	46.9
7	31	9	6	13	533	11.18	147		265	268	49.72	50.28
8	21	9	6	14	533	11.18	148		268	265	50.28	49.72
9	13	9	1	15	532	11.16	149		277	255	52.07	47.93
5	8	9	6	16	530	11.11	150		293	237	55.28	44.72
7	24	9	6	14	530	11.11	151		251	279	47.36	52.64
8	8	9	7	12	530	11.11	152		252	278	47.55	52.45
8	22	9	7	12	530	11.11	153		224	306	42.26	57.74
6	21	9	1	17	529	11.09	154		289	240	54.63	45.37
8	21	9	6	16	529	11.09	155		279	250	52.74	47.26
9	4	9	6	19	528	11.07	156		268	260	50.76	49.24
9	5	9	7	15	528	11.07	157		310	218	58.71	41.29
8	14	9	6	14	527	11.05	158		265	262	50.28	49.72
8	30	9	1	13	527	11.05	159		271	256	51.42	48.58
8	28	9	6	15	525	11.01	160		260	265	49.52	50.48
9	20	9	1	17	525	11.01	161	4769	285	240	54.29	45.71
7	10	9	6	17	524	10.99	162		264	260	50.38	49.62
8	6	9	5	16	524	10.99	163		277	247	52.86	47.14
9	25	9	6	17	524	10.99	164		249	275	47.52	52.48
9	27	9	1	15	524	10.99	165		256	268	48.85	51.15
8	8	9	7	14	523	10.97	166		280	243	53.54	46.46
6	28	9	1	17	522	10.95	167		292	230	55.94	44.06
8	15	9	7	14	522	10.95	168		251	271	48.08	51.92
8	7	9	6	18	521	10.92	169		283	238	54.32	45.68
11	29	9	1	14	521	10.92	170		277	244	53.17	46.83
6	26	9	6	14	520	10.9	171		242	278	46.54	53.46
5	23	9	7	12	519	10.88	172		299	220	57.61	42.39
6	19	9	6	14	519	10.88	173		263	256	50.67	49.33

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	21	9	6	13	519	10.88	174		253	266	48.75	51.25
9	18	9	6	16	519	10.88	175		289	230	55.68	44.32
7	17	9	6	16	518	10.86	176		265	253	51.16	48.84
7	24	9	6	13	518	10.86	177		255	263	49.23	50.77
8	14	9	6	12	518	10.86	178		247	271	47.68	52.32
8	14	9	6	18	517	10.84	179		265	252	51.26	48.74
8	28	9	6	17	517	10.84	180		259	258	50.1	49.9
6	12	9	6	14	516	10.82	181	4769	266	250	51.55	48.45
9	6	9	1	16	516	10.82	182		252	264	48.84	51.16
9	18	9	6	18	516	10.82	183		266	250	51.55	48.45
8	6	9	5	18	515	10.8	184		289	226	56.12	43.88
5	23	9	7	13	514	10.78	185		259	255	50.39	49.61
11	25	9	4	18	514	10.78	186		263	251	51.17	48.83
7	17	9	6	12	513	10.76	187		235	278	45.81	54.19
7	19	9	1	16	513	10.76	188		296	217	57.7	42.3
7	26	9	1	12	513	10.76	189		228	285	44.44	55.56
7	2	9	5	16	512	10.74	190		236	276	46.09	53.91
4	3	9	6	16	511	10.72	191		282	229	55.19	44.81
6	19	9	6	18	510	10.69	192		230	280	45.1	54.9
9	20	9	1	14	510	10.69	193		256	254	50.2	49.8

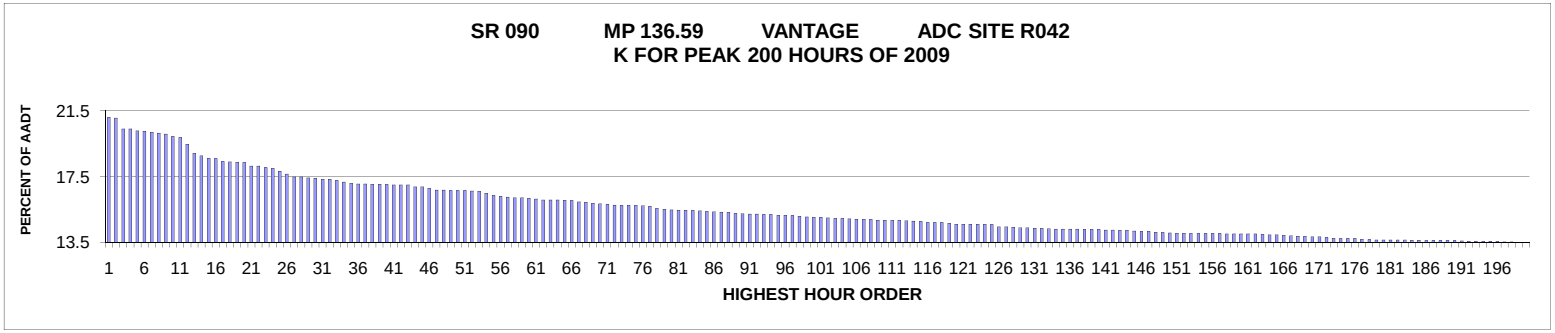

AADT= 14287 **K 30 FACTOR=** 17.4 **K 100 FACTOR=** 15.03 **K 200 FACTOR=** 13.5 **D FACTOR=** 60.55

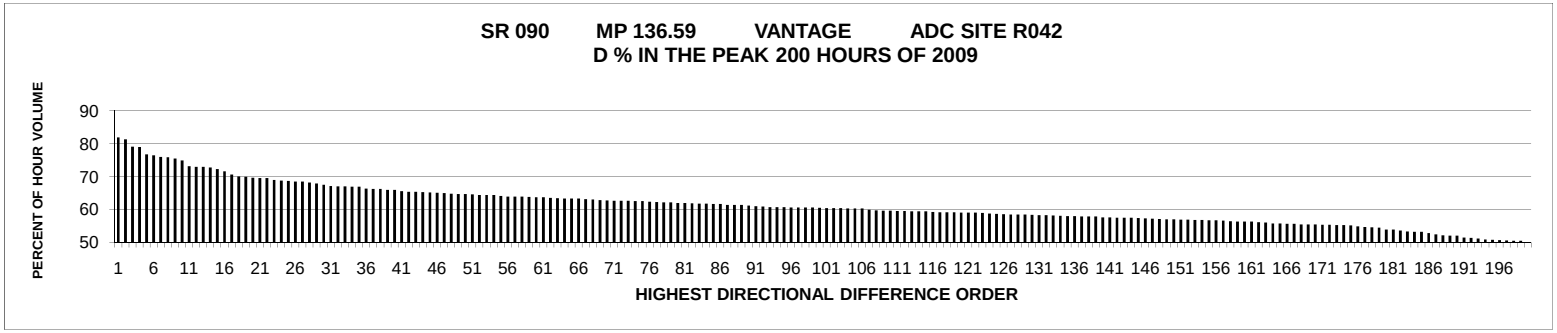

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
11	29	9	1	15	3015	21.1	1	14287	1645	1370	54.56	45.44
8	9	9	1	13	3010	21.07	2		917	2093	30.47	69.53
8	9	9	1	14	2915	20.4	3		1018	1897	34.92	65.08
11	29	9	1	14	2915	20.4	4		1552	1363	53.24	46.76
9	4	9	6	17	2898	20.28	5		1977	921	68.22	31.78
11	29	9	1	16	2894	20.26	6		1667	1227	57.6	42.4
5	25	9	2	13	2888	20.21	7		1036	1852	35.87	64.13
5	25	9	2	12	2879	20.15	8		845	2034	29.35	70.65
9	4	9	6	18	2870	20.09	9		1883	987	65.61	34.39
9	4	9	6	16	2849	19.94	10		1960	889	68.8	31.2
8	9	9	1	12	2840	19.88	11		786	2054	27.68	72.32
8	9	9	1	15	2781	19.47	12		1056	1725	37.97	62.03
8	7	9	6	15	2703	18.92	13		1767	936	65.37	34.63
5	25	9	2	11	2680	18.76	14		630	2050	23.51	76.49
8	7	9	6	16	2660	18.62	15		1700	960	63.91	36.09
9	4	9	6	15	2658	18.6	16		1825	833	68.66	31.34
5	25	9	2	14	2631	18.42	17		1040	1591	39.53	60.47

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	9	9	1	16	2627	18.39	18		1057	1570	40.24	59.76
8	16	9	1	15	2624	18.37	19		1172	1452	44.66	55.34
11	29	9	1	13	2623	18.36	20		1347	1276	51.35	48.65
9	7	9	2	13	2592	18.14	21	14287	874	1718	33.72	66.28
9	7	9	2	12	2591	18.14	22		701	1890	27.06	72.94
9	4	9	6	19	2578	18.04	23		1607	971	62.34	37.66
9	7	9	2	11	2573	18.01	24		539	2034	20.95	79.05
8	16	9	1	16	2549	17.84	25		1099	1450	43.11	56.89
7	5	9	1	14	2523	17.66	26		898	1625	35.59	64.41
8	16	9	1	17	2498	17.48	27		1120	1378	44.84	55.16
8	23	9	1	15	2498	17.48	28		1023	1475	40.95	59.05
8	7	9	6	14	2490	17.43	29		1510	980	60.64	39.36
5	22	9	6	16	2486	17.4	30		1648	838	66.29	33.71
8	23	9	1	16	2478	17.34	31		1074	1404	43.34	56.66
8	7	9	6	17	2477	17.34	32		1618	859	65.32	34.68
8	23	9	1	14	2467	17.27	33		1032	1435	41.83	58.17
5	22	9	6	15	2453	17.17	34		1618	835	65.96	34.04
8	9	9	1	11	2443	17.1	35		613	1830	25.09	74.91
7	5	9	1	15	2437	17.06	36		934	1503	38.33	61.67
7	5	9	1	16	2436	17.05	37		892	1544	36.62	63.38
7	5	9	1	13	2434	17.04	38		803	1631	32.99	67.01
9	7	9	2	15	2433	17.03	39		1013	1420	41.64	58.36
7	26	9	1	16	2432	17.02	40		981	1451	40.34	59.66
8	16	9	1	14	2429	17	41	14287	1084	1345	44.63	55.37
11	29	9	1	17	2428	16.99	42		1381	1047	56.88	43.12
9	4	9	6	14	2427	16.99	43		1648	779	67.9	32.1
5	25	9	2	15	2413	16.89	44		1030	1383	42.69	57.31
9	7	9	2	14	2412	16.88	45		901	1511	37.35	62.65
7	26	9	1	15	2398	16.78	46		945	1453	39.41	60.59
8	23	9	1	17	2384	16.69	47		1011	1373	42.41	57.59
8	7	9	6	13	2383	16.68	48		1353	1030	56.78	43.22
7	12	9	1	15	2379	16.65	49		908	1471	38.17	61.83
11	25	9	4	16	2379	16.65	50		1362	1017	57.25	42.75
8	16	9	1	13	2377	16.64	51		1052	1325	44.26	55.74
5	23	9	7	12	2376	16.63	52		1664	712	70.03	29.97
7	19	9	1	15	2373	16.61	53		887	1486	37.38	62.62
7	12	9	1	16	2357	16.5	54		914	1443	38.78	61.22
6	26	9	6	15	2337	16.36	55		1480	857	63.33	36.67
7	12	9	1	14	2327	16.29	56		858	1469	36.87	63.13
7	26	9	1	17	2322	16.25	57		988	1334	42.55	57.45
4	5	9	1	16	2316	16.21	58		973	1343	42.01	57.99
7	19	9	1	16	2316	16.21	59		957	1359	41.32	58.68
11	25	9	4	17	2311	16.18	60		1318	993	57.03	42.97
7	26	9	1	14	2307	16.15	61	14287	971	1336	42.09	57.91
9	7	9	2	16	2299	16.09	62		986	1313	42.89	57.11
6	28	9	1	16	2297	16.08	63		808	1489	35.18	64.82
6	28	9	1	21	2297	16.08	64		416	1881	18.11	81.89
8	16	9	1	18	2294	16.06	65		974	1320	42.46	57.54
6	28	9	1	15	2292	16.04	66		856	1436	37.35	62.65
9	4	9	6	20	2282	15.97	67		1471	811	64.46	35.54
6	28	9	1	14	2277	15.94	68		878	1399	38.56	61.44
8	9	9	1	17	2270	15.89	69		900	1370	39.65	60.35

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
5	23	9	7	13	2265	15.85	70		1584	681	69.93	30.07
7	19	9	1	14	2259	15.81	71		844	1415	37.36	62.64
8	15	9	7	12	2254	15.78	72		1442	812	63.98	36.02
5	22	9	6	14	2252	15.76	73		1469	783	65.23	34.77
9	7	9	2	10	2252	15.76	74		421	1831	18.69	81.31
7	5	9	1	17	2250	15.75	75		893	1357	39.69	60.31
11	25	9	4	15	2249	15.74	76		1171	1078	52.07	47.93
5	17	9	1	12	2243	15.7	77		550	1693	24.52	75.48
4	5	9	1	15	2222	15.55	78		845	1377	38.03	61.97
5	23	9	7	11	2217	15.52	79		1587	630	71.58	28.42
9	7	9	2	17	2212	15.48	80		990	1222	44.76	55.24
6	26	9	6	16	2209	15.46	81	14287	1298	911	58.76	41.24
8	2	9	1	15	2209	15.46	82		930	1279	42.1	57.9
6	14	9	1	15	2207	15.45	83		950	1257	43.04	56.96
5	25	9	2	16	2203	15.42	84		902	1301	40.94	59.06
8	14	9	6	15	2199	15.39	85		1185	1014	53.89	46.11
5	17	9	1	13	2196	15.37	86		666	1530	30.33	69.67
6	28	9	1	17	2191	15.34	87		800	1391	36.51	63.49
8	7	9	6	18	2189	15.32	88		1423	766	65.01	34.99
8	23	9	1	13	2182	15.27	89		859	1323	39.37	60.63
7	5	9	1	12	2177	15.24	90		685	1492	31.47	68.53
8	14	9	6	16	2176	15.23	91		1208	968	55.51	44.49
9	6	9	1	16	2174	15.22	92		1070	1104	49.22	50.78
7	12	9	1	17	2170	15.19	93		853	1317	39.31	60.69
7	12	9	1	13	2169	15.18	94		795	1374	36.65	63.35
8	2	9	1	14	2164	15.15	95		877	1287	40.53	59.47
8	15	9	7	11	2164	15.15	96		1394	770	64.42	35.58
5	25	9	2	17	2161	15.13	97		874	1287	40.44	59.56
7	19	9	1	17	2157	15.1	98		874	1283	40.52	59.48
9	4	9	6	13	2150	15.05	99		1375	775	63.95	36.05
8	16	9	1	12	2148	15.03	100		877	1271	40.83	59.17
8	23	9	1	18	2147	15.03	101	14287	942	1205	43.88	56.12
5	17	9	1	14	2141	14.99	102		708	1433	33.07	66.93
6	14	9	1	16	2138	14.96	103		808	1330	37.79	62.21
8	14	9	6	14	2136	14.95	104		1152	984	53.93	46.07
6	21	9	1	15	2134	14.94	105		890	1244	41.71	58.29
7	19	9	1	13	2132	14.92	106		772	1360	36.21	63.79
5	22	9	6	18	2131	14.92	107		1262	869	59.22	40.78
7	2	9	5	16	2127	14.89	108		1330	797	62.53	37.47
6	21	9	1	16	2122	14.85	109		939	1183	44.25	55.75
7	26	9	1	13	2122	14.85	110		866	1256	40.81	59.19
6	21	9	1	14	2120	14.84	111		850	1270	40.09	59.91
8	30	9	1	17	2120	14.84	112		870	1250	41.04	58.96
5	22	9	6	13	2118	14.82	113		1320	798	62.32	37.68
8	2	9	1	16	2115	14.8	114		854	1261	40.38	59.62
8	30	9	1	15	2112	14.78	115		830	1282	39.3	60.7
9	6	9	1	14	2101	14.71	116		885	1216	42.12	57.88
4	5	9	1	14	2100	14.7	117		850	1250	40.48	59.52
5	22	9	6	17	2100	14.7	118		1208	892	57.52	42.48
6	26	9	6	14	2094	14.66	119		1277	817	60.98	39.02
5	16	9	7	14	2088	14.61	120		1528	560	73.18	26.82
7	11	9	7	18	2088	14.61	121	14287	1585	503	75.91	24.09

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	30	9	1	16	2088	14.61	122		796	1292	38.12	61.88
6	21	9	1	17	2087	14.61	123		865	1222	41.45	58.55
8	14	9	6	13	2086	14.6	124		1088	998	52.16	47.84
9	5	9	7	12	2084	14.59	125		1145	939	54.94	45.06
5	17	9	1	15	2065	14.45	126		780	1285	37.77	62.23
5	25	9	2	18	2065	14.45	127		819	1246	39.66	60.34
11	25	9	4	14	2062	14.43	128		1021	1041	49.52	50.48
8	9	9	1	18	2058	14.4	129		854	1204	41.5	58.5
6	28	9	1	13	2057	14.4	130		785	1272	38.16	61.84
11	29	9	1	12	2054	14.38	131		1015	1039	49.42	50.58
7	24	9	6	17	2052	14.36	132		1119	933	54.53	45.47
8	30	9	1	14	2047	14.33	133		757	1290	36.98	63.02
9	6	9	1	17	2046	14.32	134		1053	993	51.47	48.53
7	2	9	5	18	2044	14.31	135		1236	808	60.47	39.53
7	3	9	6	15	2044	14.31	136		1285	759	62.87	37.13
7	24	9	6	14	2044	14.31	137		1081	963	52.89	47.11
7	11	9	7	17	2042	14.29	138		1490	552	72.97	27.03
9	6	9	1	13	2042	14.29	139		761	1281	37.27	62.73
5	23	9	7	14	2041	14.29	140		1485	556	72.76	27.24
5	17	9	1	11	2037	14.26	141	14287	473	1564	23.22	76.78
8	2	9	1	17	2037	14.26	142		825	1212	40.5	59.5
9	5	9	7	13	2035	14.24	143		1235	800	60.69	39.31
9	5	9	7	14	2034	14.24	144		1331	703	65.44	34.56
7	2	9	5	17	2029	14.2	145		1252	777	61.71	38.29
6	26	9	6	13	2026	14.18	146		1201	825	59.28	40.72
9	6	9	1	15	2024	14.17	147		962	1062	47.53	52.47
6	19	9	6	17	2017	14.12	148		1169	848	57.96	42.04
3	22	9	1	16	2015	14.1	149		1074	941	53.3	46.7
8	2	9	1	13	2011	14.08	150		843	1168	41.92	58.08
6	14	9	1	14	2010	14.07	151		835	1175	41.54	58.46
8	30	9	1	13	2009	14.06	152		726	1283	36.14	63.86
4	19	9	1	17	2008	14.05	153		931	1077	46.36	53.64
5	25	9	2	10	2008	14.05	154		419	1589	20.87	79.13
5	22	9	6	19	2007	14.05	155		1217	790	60.64	39.36
8	7	9	6	19	2007	14.05	156		1347	660	67.12	32.88
5	17	9	1	16	2006	14.04	157		775	1231	38.63	61.37
7	17	9	6	15	2005	14.03	158		1109	896	55.31	44.69
5	8	9	6	16	2004	14.03	159		1143	861	57.04	42.96
5	10	9	1	16	2004	14.03	160		650	1354	32.44	67.56
3	22	9	1	15	2003	14.02	161	14287	987	1016	49.28	50.72
6	26	9	6	17	2003	14.02	162		1273	730	63.55	36.45
8	15	9	7	13	1997	13.98	163		1128	869	56.48	43.52
9	7	9	2	18	1995	13.96	164		877	1118	43.96	56.04
4	26	9	1	17	1994	13.96	165		871	1123	43.68	56.32
4	5	9	1	17	1993	13.95	166		788	1205	39.54	60.46
7	24	9	6	16	1988	13.91	167		1107	881	55.68	44.32
7	5	9	1	18	1985	13.89	168		827	1158	41.66	58.34
5	10	9	1	17	1980	13.86	169		665	1315	33.59	66.41
7	19	9	1	18	1979	13.85	170		822	1157	41.54	58.46
7	3	9	6	16	1978	13.84	171		1281	697	64.76	35.24
7	24	9	6	15	1973	13.81	172		1027	946	52.05	47.95
9	5	9	7	15	1965	13.75	173		1296	669	65.95	34.05

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
9	13	9	1	15	1962	13.73	174		1004	958	51.17	48.83
4	19	9	1	16	1961	13.73	175		766	1195	39.06	60.94
8	29	9	7	17	1961	13.73	176		1344	617	68.54	31.46
8	21	9	6	14	1957	13.7	177		1112	845	56.82	43.18
5	16	9	7	13	1955	13.68	178		1360	595	69.57	30.43
5	10	9	1	18	1952	13.66	179		688	1264	35.25	64.75
7	10	9	6	14	1951	13.66	180		1100	851	56.38	43.62
7	10	9	6	16	1951	13.66	181	14287	1086	865	55.66	44.34
8	21	9	6	16	1951	13.66	182		1083	868	55.51	44.49
9	13	9	1	16	1951	13.66	183		973	978	49.87	50.13
5	3	9	1	17	1947	13.63	184		688	1259	35.34	64.66
9	18	9	6	16	1947	13.63	185		1104	843	56.7	43.3
11	25	9	4	13	1946	13.62	186		882	1064	45.32	54.68
8	16	9	1	19	1945	13.61	187		866	1079	44.52	55.48
5	3	9	1	16	1944	13.61	188		642	1302	33.02	66.98
6	14	9	1	17	1944	13.61	189		849	1095	43.67	56.33
7	11	9	7	16	1944	13.61	190		1342	602	69.03	30.97
5	22	9	6	20	1941	13.59	191		1302	639	67.08	32.92
5	22	9	6	21	1939	13.57	192		1474	465	76.02	23.98
7	2	9	5	14	1939	13.57	193		1190	749	61.37	38.63
7	24	9	6	13	1939	13.57	194		987	952	50.9	49.1
9	13	9	1	17	1939	13.57	195		1032	907	53.22	46.78
8	14	9	6	17	1936	13.55	196		1114	822	57.54	42.46
5	24	9	1	13	1934	13.54	197		957	977	49.48	50.52
8	16	9	1	11	1934	13.54	198		763	1171	39.45	60.55
7	19	9	1	12	1932	13.52	199		700	1232	36.23	63.77
8	21	9	6	17	1929	13.5	200		1139	790	59.05	40.95

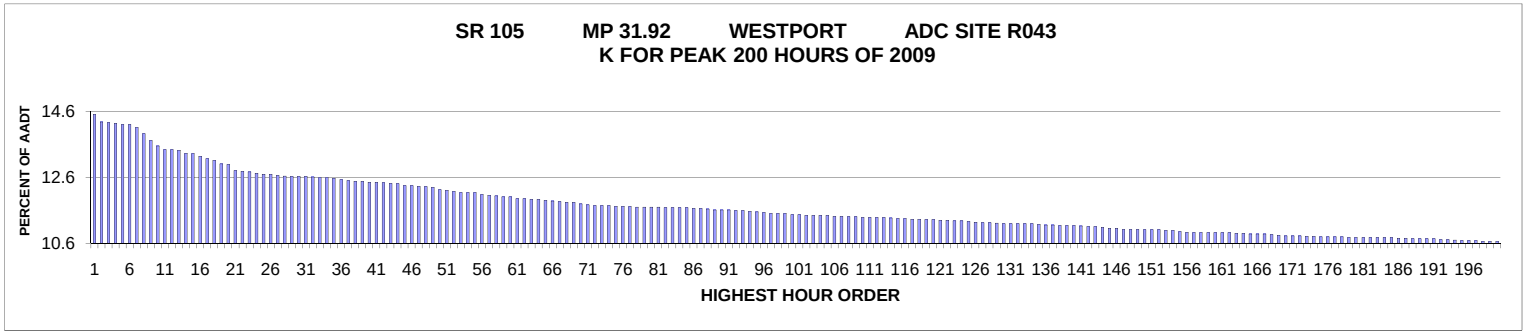

AADT= 5497 **K 30 FACTOR=** 12.63 **K 100 FACTOR=** 11.46 **K 200 FACTOR=** 10.66 **D FACTOR=** 56.12

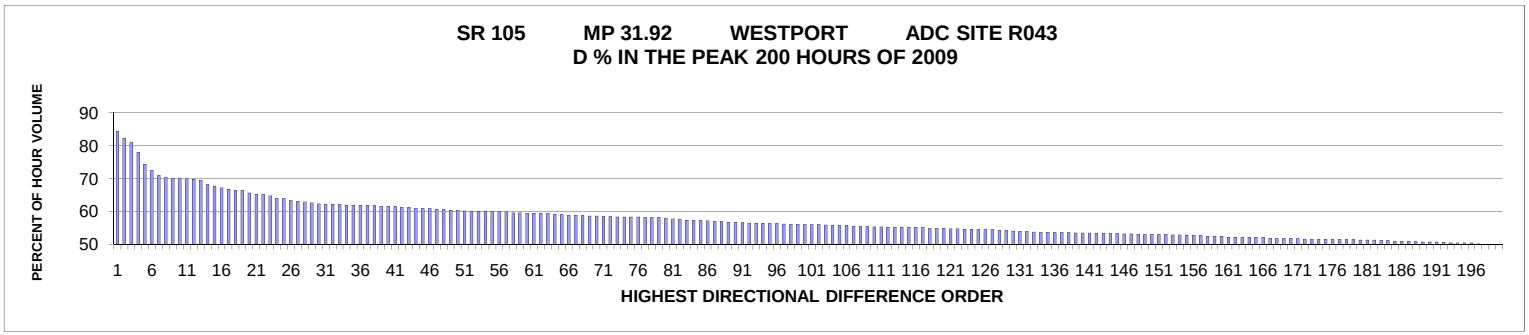

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	5	9	1	12	798	14.52	1	5497	646	152	80.95	19.05
7	3	9	6	17	785	14.28	2		302	483	38.47	61.53
4	11	9	7	8	784	14.26	3		201	583	25.64	74.36
6	27	9	7	13	783	14.24	4		299	484	38.19	61.81
6	27	9	7	14	781	14.21	5		325	456	41.61	58.39
7	3	9	6	15	781	14.21	6		272	509	34.83	65.17
7	5	9	1	13	776	14.12	7		562	214	72.42	27.58
7	31	9	6	17	765	13.92	8		372	393	48.63	51.37
8	16	9	1	14	754	13.72	9		416	338	55.17	44.83
7	3	9	6	14	745	13.55	10		241	504	32.35	67.65
7	3	9	6	16	739	13.44	11		282	457	38.16	61.84
7	29	9	4	17	739	13.44	12		455	284	61.57	38.43
8	1	9	7	15	738	13.43	13		326	412	44.17	55.83
7	25	9	7	17	733	13.33	14		426	307	58.12	41.88
6	27	9	7	16	732	13.32	15		414	318	56.56	43.44
7	26	9	1	13	728	13.24	16		391	337	53.71	46.29
7	30	9	5	17	724	13.17	17		436	288	60.22	39.78

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	25	9	7	16	721	13.12	18		357	364	49.51	50.49
6	27	9	7	15	715	13.01	19		347	368	48.53	51.47
8	21	9	6	17	714	12.99	20		372	342	52.1	47.9
8	1	9	7	14	704	12.81	21	5497	305	399	43.32	56.68
7	3	9	6	18	703	12.79	22		282	421	40.11	59.89
8	30	9	1	14	702	12.77	23		427	275	60.83	39.17
8	16	9	1	15	700	12.73	24		410	290	58.57	41.43
7	26	9	1	14	698	12.7	25		355	343	50.86	49.14
8	2	9	1	13	698	12.7	26		400	298	57.31	42.69
7	25	9	7	14	696	12.66	27		263	433	37.79	62.21
6	27	9	7	12	695	12.64	28		228	467	32.81	67.19
7	26	9	1	15	694	12.63	29		383	311	55.19	44.81
7	31	9	6	16	694	12.63	30		311	383	44.81	55.19
8	21	9	6	16	694	12.63	31		324	370	46.69	53.31
6	28	9	1	14	693	12.61	32		416	277	60.03	39.97
7	31	9	6	15	692	12.59	33		325	367	46.97	53.03
8	1	9	7	17	692	12.59	34		417	275	60.26	39.74
8	2	9	1	16	691	12.57	35		419	272	60.64	39.36
7	24	9	6	17	689	12.53	36		324	365	47.02	52.98
7	3	9	6	13	687	12.5	37		286	401	41.63	58.37
6	28	9	1	16	686	12.48	38		482	204	70.26	29.74
7	26	9	1	18	686	12.48	39		480	206	69.97	30.03
7	26	9	1	17	685	12.46	40		467	218	68.18	31.82
8	15	9	7	14	685	12.46	41	5497	326	359	47.59	52.41
7	24	9	6	16	684	12.44	42		315	369	46.05	53.95
8	2	9	1	14	683	12.42	43		366	317	53.59	46.41
9	4	9	6	17	682	12.41	44		316	366	46.33	53.67
6	28	9	1	13	679	12.35	45		359	320	52.87	47.13
11	4	9	4	18	679	12.35	46		291	388	42.86	57.14
8	7	9	6	17	678	12.33	47		302	376	44.54	55.46
7	5	9	1	14	677	12.32	48		480	197	70.9	29.1
8	1	9	7	13	676	12.3	49		287	389	42.46	57.54
7	25	9	7	12	672	12.22	50		281	391	41.82	58.18
8	15	9	7	15	671	12.21	51		321	350	47.84	52.16
8	16	9	1	13	669	12.17	52		389	280	58.15	41.85
7	18	9	7	14	667	12.13	53		312	355	46.78	53.22
8	1	9	7	16	667	12.13	54		345	322	51.72	48.28
8	2	9	1	15	667	12.13	55		370	297	55.47	44.53
8	3	9	2	16	664	12.08	56		329	335	49.55	50.45
7	25	9	7	13	663	12.06	57		268	395	40.42	59.58
7	2	9	5	16	662	12.04	58		301	361	45.47	54.53
7	25	9	7	18	660	12.01	59		393	267	59.55	40.45
8	2	9	1	17	660	12.01	60		441	219	66.82	33.18
7	3	9	6	19	657	11.95	61	5497	262	395	39.88	60.12
7	26	9	1	16	657	11.95	62		395	262	60.12	39.88
7	19	9	1	13	656	11.93	63		408	248	62.2	37.8
7	28	9	3	17	656	11.93	64		403	253	61.43	38.57
7	29	9	4	18	654	11.9	65		395	259	60.4	39.6
7	11	9	7	15	653	11.88	66		332	321	50.84	49.16
7	17	9	6	16	652	11.86	67		301	351	46.17	53.83
8	17	9	2	16	651	11.84	68		350	301	53.76	46.24
8	28	9	6	16	651	11.84	69		288	363	44.24	55.76

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
5	23	9	7	14	648	11.79	70		251	397	38.73	61.27
5	23	9	7	15	647	11.77	71		282	365	43.59	56.41
7	4	9	7	14	646	11.75	72		272	374	42.11	57.89
7	30	9	5	16	646	11.75	73		324	322	50.15	49.85
8	16	9	1	16	646	11.75	74		392	254	60.68	39.32
7	3	9	6	12	645	11.73	75		232	413	35.97	64.03
7	17	9	6	17	645	11.73	76		341	304	52.87	47.13
7	19	9	1	14	644	11.72	77		355	289	55.12	44.88
7	11	9	7	13	643	11.7	78		278	365	43.23	56.77
7	29	9	4	14	643	11.7	79		261	382	40.59	59.41
8	1	9	7	18	643	11.7	80		378	265	58.79	41.21
8	16	9	1	12	643	11.7	81	5497	382	261	59.41	40.59
6	28	9	1	17	642	11.68	82		450	192	70.09	29.91
7	30	9	5	15	642	11.68	83		288	354	44.86	55.14
8	8	9	7	13	642	11.68	84		310	332	48.29	51.71
8	15	9	7	13	642	11.68	85		286	356	44.55	55.45
5	23	9	7	13	641	11.66	86		223	418	34.79	65.21
9	4	9	6	16	641	11.66	87		305	336	47.58	52.42
6	27	9	7	17	640	11.64	88		425	215	66.41	33.59
4	24	9	6	16	638	11.61	89		288	350	45.14	54.86
5	24	9	1	13	638	11.61	90		305	333	47.81	52.19
9	18	9	6	16	638	11.61	91		324	314	50.78	49.22
8	23	9	1	15	637	11.59	92		352	285	55.26	44.74
8	30	9	1	13	637	11.59	93		368	269	57.77	42.23
5	23	9	7	16	636	11.57	94		291	345	45.75	54.25
7	31	9	6	14	635	11.55	95		262	373	41.26	58.74
5	24	9	1	14	634	11.53	96		326	308	51.42	48.58
6	26	9	6	16	632	11.5	97		298	334	47.15	52.85
7	11	9	7	16	632	11.5	98		357	275	56.49	43.51
11	4	9	4	17	632	11.5	99		259	373	40.98	59.02
7	2	9	5	17	630	11.46	100		321	309	50.95	49.05
7	4	9	7	15	630	11.46	101	5497	278	352	44.13	55.87
2	6	9	6	16	629	11.44	102		305	324	48.49	51.51
7	11	9	7	17	629	11.44	103		358	271	56.92	43.08
7	25	9	7	15	629	11.44	104		276	353	43.88	56.12
10	16	9	6	16	629	11.44	105		246	383	39.11	60.89
7	11	9	7	18	628	11.42	106		333	295	53.03	46.97
12	2	9	4	17	628	11.42	107		353	275	56.21	43.79
6	26	9	6	17	627	11.41	108		304	323	48.48	51.52
9	12	9	7	16	627	11.41	109		347	280	55.34	44.66
7	26	9	1	12	626	11.39	110		341	285	54.47	45.53
7	29	9	4	16	626	11.39	111		335	291	53.51	46.49
7	31	9	6	18	626	11.39	112		313	313	50	50
8	7	9	6	15	626	11.39	113		297	329	47.44	52.56
7	4	9	7	13	625	11.37	114		239	386	38.24	61.76
6	26	9	6	15	624	11.35	115		249	375	39.9	60.1
7	27	9	2	17	624	11.35	116		334	290	53.53	46.47
7	10	9	6	16	623	11.33	117		311	312	49.92	50.08
8	14	9	6	17	623	11.33	118		333	290	53.45	46.55
5	24	9	1	17	622	11.32	119		394	228	63.34	36.66
7	29	9	4	13	622	11.32	120		257	365	41.32	58.68
2	7	9	7	16	621	11.3	121	5497	219	402	35.27	64.73

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
9	11	9	6	17	621	11.3	122		324	297	52.17	47.83
8	14	9	6	16	620	11.28	123		258	362	41.61	58.39
9	18	9	6	17	620	11.28	124		300	320	48.39	51.61
7	28	9	3	15	619	11.26	125		272	347	43.94	56.06
4	10	9	6	7	618	11.24	126		97	521	15.7	84.3
8	9	9	1	14	617	11.22	127		394	223	63.86	36.14
8	16	9	1	17	617	11.22	128		405	212	65.64	34.36
9	11	9	6	16	616	11.21	129		313	303	50.81	49.19
7	11	9	7	14	615	11.19	130		263	352	42.76	57.24
7	31	9	6	13	615	11.19	131		296	319	48.13	51.87
8	14	9	6	15	615	11.19	132		282	333	45.85	54.15
8	22	9	7	16	615	11.19	133		319	296	51.87	48.13
8	28	9	6	17	615	11.19	134		302	313	49.11	50.89
5	25	9	2	13	614	11.17	135		386	228	62.87	37.13
2	6	9	6	15	613	11.15	136		239	374	38.99	61.01
5	22	9	6	16	613	11.15	137		290	323	47.31	52.69
7	5	9	1	11	612	11.13	138		477	135	77.94	22.06
7	19	9	1	15	612	11.13	139		365	247	59.64	40.36
12	2	9	4	16	612	11.13	140		264	348	43.14	56.86
9	12	9	7	13	611	11.12	141	5497	250	361	40.92	59.08
7	18	9	7	13	610	11.1	142		232	378	38.03	61.97
8	7	9	6	16	610	11.1	143		277	333	45.41	54.59
8	22	9	7	15	609	11.08	144		300	309	49.26	50.74
4	11	9	7	9	608	11.06	145		423	185	69.57	30.43
8	19	9	4	15	608	11.06	146		307	301	50.49	49.51
5	24	9	1	15	606	11.02	147		276	330	45.54	54.46
8	15	9	7	16	606	11.02	148		325	281	53.63	46.37
8	17	9	2	13	606	11.02	149		321	285	52.97	47.03
4	10	9	6	8	605	11.01	150		355	250	58.68	41.32
6	28	9	1	12	605	11.01	151		316	289	52.23	47.77
8	8	9	7	15	605	11.01	152		322	283	53.22	46.78
7	18	9	7	16	604	10.99	153		265	339	43.87	56.13
9	5	9	7	13	604	10.99	154		226	378	37.42	62.58
5	1	9	6	16	602	10.95	155		308	294	51.16	48.84
5	22	9	6	17	601	10.93	156		280	321	46.59	53.41
5	25	9	2	12	600	10.92	157		419	181	69.83	30.17
6	28	9	1	15	600	10.92	158		360	240	60	40
8	3	9	2	17	600	10.92	159		350	250	58.33	41.67
8	19	9	4	14	600	10.92	160		283	317	47.17	52.83
8	21	9	6	18	600	10.92	161	5497	262	338	43.67	56.33
9	11	9	6	15	600	10.92	162		268	332	44.67	55.33
7	5	9	1	15	599	10.9	163		372	227	62.1	37.9
8	29	9	7	14	599	10.9	164		262	337	43.74	56.26
7	4	9	7	16	598	10.88	165		302	296	50.5	49.5
7	17	9	6	15	598	10.88	166		265	333	44.31	55.69
7	24	9	6	15	598	10.88	167		270	328	45.15	54.85
3	29	9	1	13	597	10.86	168		370	227	61.98	38.02
9	25	9	6	16	596	10.84	169		262	334	43.96	56.04
7	29	9	4	12	595	10.82	170		241	354	40.5	59.5
7	29	9	4	15	595	10.82	171		261	334	43.87	56.13
8	5	9	4	17	595	10.82	172		350	245	58.82	41.18
7	28	9	3	16	594	10.81	173		305	289	51.35	48.65

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	20	9	5	17	594	10.81	174		375	219	63.13	36.87
6	19	9	6	16	593	10.79	175		296	297	49.92	50.08
8	18	9	3	16	593	10.79	176		316	277	53.29	46.71
8	27	9	5	15	593	10.79	177		275	318	46.37	53.63
9	6	9	1	14	593	10.79	178		305	288	51.43	48.57
4	11	9	7	10	592	10.77	179		487	105	82.26	17.74
7	19	9	1	18	592	10.77	180		414	178	69.93	30.07
8	7	9	6	14	592	10.77	181	5497	304	288	51.35	48.65
8	9	9	1	13	592	10.77	182		362	230	61.15	38.85
8	21	9	6	14	592	10.77	183		258	334	43.58	56.42
8	30	9	1	15	592	10.77	184		393	199	66.39	33.61
9	12	9	7	15	592	10.77	185		268	324	45.27	54.73
8	17	9	2	15	591	10.75	186		304	287	51.44	48.56
8	22	9	7	13	591	10.75	187		267	324	45.18	54.82
5	15	9	6	16	590	10.73	188		269	321	45.59	54.41
8	6	9	5	17	590	10.73	189		315	275	53.39	46.61
8	8	9	7	14	590	10.73	190		285	305	48.31	51.69
9	4	9	6	15	590	10.73	191		267	323	45.25	54.75
2	7	9	7	15	589	10.71	192		222	367	37.69	62.31
8	21	9	6	15	589	10.71	193		282	307	47.88	52.12
8	19	9	4	16	588	10.7	194		312	276	53.06	46.94
6	12	9	6	16	587	10.68	195		284	303	48.38	51.62
8	28	9	6	15	587	10.68	196		297	290	50.6	49.4
9	12	9	7	14	587	10.68	197		244	343	41.57	58.43
7	17	9	6	13	586	10.66	198		269	317	45.9	54.1
7	24	9	6	14	586	10.66	199		300	286	51.19	48.81
8	23	9	1	14	586	10.66	200		336	250	57.34	42.66

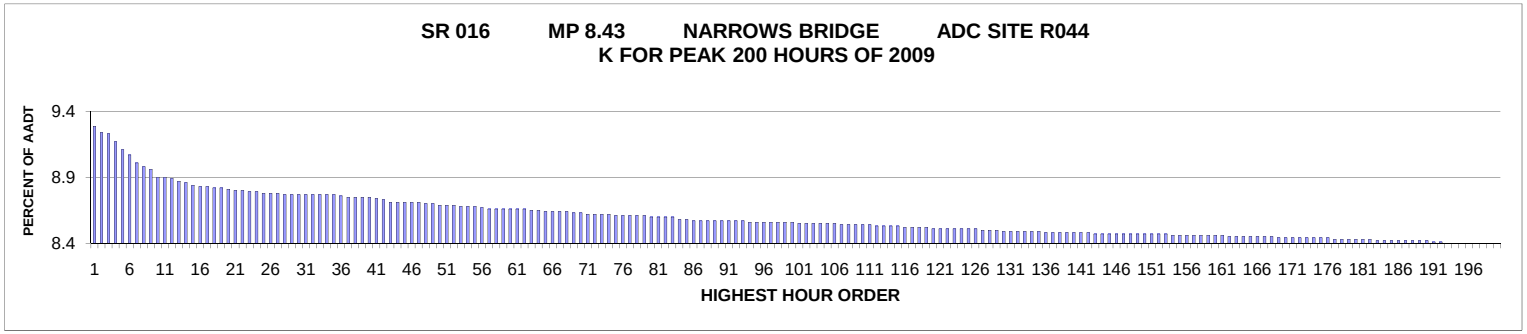

AADT= 78925 **K 30 FACTOR=** 8.77 **K 100 FACTOR=** 8.56 **K 200 FACTOR=** 8.4 **D FACTOR=** 61.36

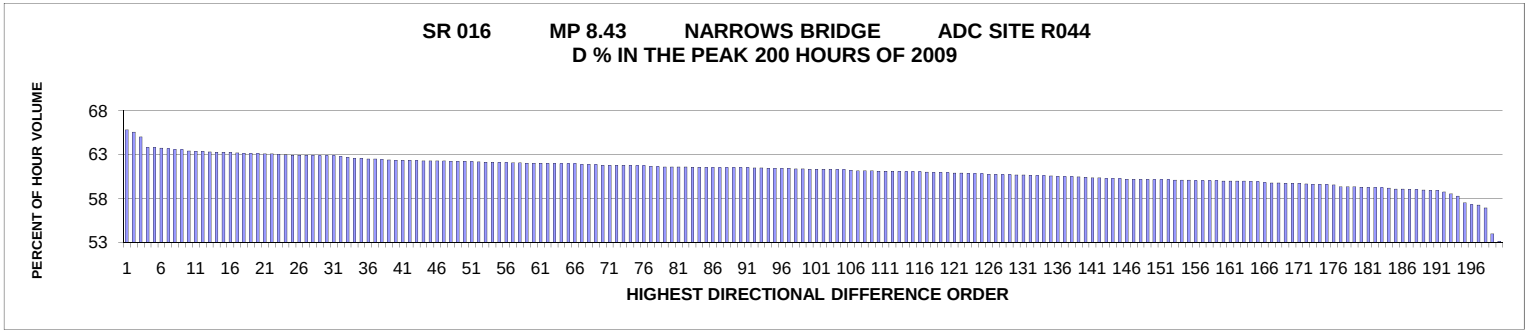

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
11	18	9	4	17	7333	9.29	1	78925	2505	4828	34.16	65.84
6	5	9	6	18	7296	9.24	2		3357	3939	46.01	53.99
6	5	9	6	17	7287	9.23	3		3115	4172	42.75	57.25
7	24	9	6	17	7236	9.17	4		2819	4417	38.96	61.04
9	11	9	6	17	7189	9.11	5		2824	4365	39.28	60.72
5	27	9	4	17	7155	9.07	6		2650	4505	37.04	62.96
9	10	9	5	17	7112	9.01	7		2819	4293	39.64	60.36
6	11	9	5	17	7088	8.98	8		2908	4180	41.03	58.97
7	24	9	6	16	7072	8.96	9		2899	4173	40.99	59.01
9	1	9	3	18	7024	8.9	10		2457	4567	34.98	65.02
8	28	9	6	17	7023	8.9	11		2730	4293	38.87	61.13
6	18	9	5	17	7020	8.89	12		2895	4125	41.24	58.76
6	12	9	6	17	7000	8.87	13		2731	4269	39.01	60.99
9	3	9	5	17	6996	8.86	14		2774	4222	39.65	60.35
5	15	9	6	17	6974	8.84	15		2792	4182	40.03	59.97
7	23	9	5	17	6973	8.83	16		2835	4138	40.66	59.34
6	17	9	4	17	6969	8.83	17		2810	4159	40.32	59.68

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
4	17	9	6	17	6965	8.82	18		2839	4126	40.76	59.24
8	14	9	6	17	6958	8.82	19		2802	4156	40.27	59.73
6	19	9	6	17	6956	8.81	20		2955	4001	42.48	57.52
11	26	9	5	13	6948	8.8	21	78925	3255	3693	46.85	53.15
9	11	9	6	18	6945	8.8	22		2692	4253	38.76	61.24
12	22	9	3	17	6941	8.79	23		2770	4171	39.91	60.09
8	7	9	6	17	6934	8.79	24		2789	4145	40.22	59.78
8	20	9	5	17	6932	8.78	25		2791	4141	40.26	59.74
8	31	9	2	18	6929	8.78	26		2652	4277	38.27	61.73
10	9	9	6	17	6927	8.78	27		2693	4234	38.88	61.12
8	6	9	5	18	6925	8.77	28		2667	4258	38.51	61.49
8	11	9	3	17	6923	8.77	29		2639	4284	38.12	61.88
7	15	9	4	17	6922	8.77	30		2707	4215	39.11	60.89
9	4	9	6	17	6922	8.77	31		2710	4212	39.15	60.85
7	16	9	5	17	6921	8.77	32		2798	4123	40.43	59.57
7	9	9	5	17	6918	8.77	33		2786	4132	40.27	59.73
8	31	9	2	17	6918	8.77	34		2619	4299	37.86	62.14
9	24	9	5	17	6918	8.77	35		2731	4187	39.48	60.52
11	26	9	5	14	6915	8.76	36		2979	3936	43.08	56.92
8	21	9	6	17	6909	8.75	37		2548	4361	36.88	63.12
9	30	9	4	17	6906	8.75	38		2662	4244	38.55	61.45
7	10	9	6	17	6904	8.75	39		2721	4183	39.41	60.59
10	8	9	5	17	6904	8.75	40		2705	4199	39.18	60.82
8	20	9	5	18	6901	8.74	41	78925	2741	4160	39.72	60.28
6	11	9	5	18	6889	8.73	42		2714	4175	39.4	60.6
5	8	9	6	17	6878	8.71	43		2813	4065	40.9	59.1
12	18	9	6	17	6877	8.71	44		2797	4080	40.67	59.33
7	22	9	4	17	6876	8.71	45		2800	4076	40.72	59.28
8	12	9	4	17	6876	8.71	46		2607	4269	37.91	62.09
7	17	9	6	17	6871	8.71	47		2594	4277	37.75	62.25
6	25	9	5	18	6868	8.7	48		2534	4334	36.9	63.1
8	14	9	6	18	6867	8.7	49		2593	4274	37.76	62.24
7	14	9	3	17	6861	8.69	50		2607	4254	38	62
10	22	9	5	17	6860	8.69	51		2645	4215	38.56	61.44
10	2	9	6	18	6856	8.69	52		2582	4274	37.66	62.34
12	11	9	6	17	6852	8.68	53		2668	4184	38.94	61.06
10	30	9	6	17	6849	8.68	54		2629	4220	38.39	61.61
10	2	9	6	17	6847	8.68	55		2633	4214	38.45	61.55
6	5	9	6	16	6842	8.67	56		2752	4090	40.22	59.78
6	10	9	4	18	6837	8.66	57		2655	4182	38.83	61.17
9	17	9	5	17	6835	8.66	58		2704	4131	39.56	60.44
2	13	9	6	17	6834	8.66	59		2731	4103	39.96	60.04
6	16	9	3	17	6834	8.66	60		2641	4193	38.65	61.35
7	8	9	4	17	6834	8.66	61	78925	2699	4135	39.49	60.51
5	12	9	3	17	6833	8.66	62		2640	4193	38.64	61.36
7	1	9	4	17	6826	8.65	63		2663	4163	39.01	60.99
8	5	9	4	17	6824	8.65	64		2718	4106	39.83	60.17
1	16	9	6	17	6820	8.64	65		2753	4067	40.37	59.63
4	24	9	6	17	6817	8.64	66		2679	4138	39.3	60.7
12	3	9	5	17	6817	8.64	67		2726	4091	39.99	60.01
8	13	9	5	17	6816	8.64	68		2681	4135	39.33	60.67
9	25	9	6	18	6815	8.63	69		2653	4162	38.93	61.07

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
6	25	9	5	17	6808	8.63	70		2789	4019	40.97	59.03
8	26	9	4	18	6807	8.62	71		2528	4279	37.14	62.86
8	28	9	6	18	6807	8.62	72		2521	4286	37.04	62.96
11	12	9	5	17	6807	8.62	73		2714	4093	39.87	60.13
4	22	9	4	17	6800	8.62	74		2626	4174	38.62	61.38
4	21	9	3	17	6798	8.61	75		2585	4213	38.03	61.97
8	11	9	3	18	6798	8.61	76		2460	4338	36.19	63.81
5	15	9	6	18	6797	8.61	77		2780	4017	40.9	59.1
7	23	9	5	18	6797	8.61	78		2683	4114	39.47	60.53
10	1	9	5	17	6796	8.61	79		2607	4189	38.36	61.64
10	28	9	4	17	6789	8.6	80		2588	4201	38.12	61.88
7	21	9	3	17	6785	8.6	81	78925	2594	4191	38.23	61.77
8	26	9	4	17	6785	8.6	82		2662	4123	39.23	60.77
9	16	9	4	18	6784	8.6	83		2738	4046	40.36	59.64
6	12	9	6	16	6771	8.58	84		2780	3991	41.06	58.94
7	2	9	5	17	6770	8.58	85		2688	4082	39.7	60.3
4	10	9	6	17	6766	8.57	86		2551	4215	37.7	62.3
8	10	9	2	17	6766	8.57	87		2602	4164	38.46	61.54
10	9	9	6	18	6764	8.57	88		2712	4052	40.09	59.91
9	3	9	5	18	6763	8.57	89		2662	4101	39.36	60.64
5	21	9	5	18	6762	8.57	90		2662	4100	39.37	60.63
6	26	9	6	17	6762	8.57	91		2753	4009	40.71	59.29
7	16	9	5	18	6760	8.57	92		2543	4217	37.62	62.38
8	27	9	5	17	6760	8.57	93		2696	4064	39.88	60.12
6	16	9	3	18	6758	8.56	94		2461	4297	36.42	63.58
7	31	9	6	16	6758	8.56	95		2748	4010	40.66	59.34
1	9	9	6	17	6757	8.56	96		2562	4195	37.92	62.08
6	19	9	6	18	6755	8.56	97		2582	4173	38.22	61.78
9	28	9	2	17	6755	8.56	98		2473	4282	36.61	63.39
7	14	9	3	18	6754	8.56	99		2564	4190	37.96	62.04
1	30	9	6	17	6753	8.56	100		2627	4126	38.9	61.1
2	12	9	5	17	6751	8.55	101	78925	2686	4065	39.79	60.21
9	24	9	5	18	6750	8.55	102		2607	4143	38.62	61.38
12	4	9	6	17	6750	8.55	103		2669	4081	39.54	60.46
8	13	9	5	18	6747	8.55	104		2551	4196	37.81	62.19
7	31	9	6	17	6745	8.55	105		2574	4171	38.16	61.84
9	17	9	5	18	6745	8.55	106		2458	4287	36.44	63.56
11	24	9	3	17	6742	8.54	107		2553	4189	37.87	62.13
9	8	9	3	17	6740	8.54	108		2542	4198	37.72	62.28
8	19	9	4	17	6739	8.54	109		2595	4144	38.51	61.49
5	1	9	6	17	6737	8.54	110		2636	4101	39.13	60.87
8	6	9	5	17	6737	8.54	111		2617	4120	38.85	61.15
12	9	9	4	17	6734	8.53	112		2473	4261	36.72	63.28
7	1	9	4	18	6732	8.53	113		2499	4233	37.12	62.88
7	7	9	3	17	6732	8.53	114		2691	4041	39.97	60.03
11	20	9	6	17	6730	8.53	115		2689	4041	39.96	60.04
7	31	9	6	18	6728	8.52	116		2475	4253	36.79	63.21
6	4	9	5	18	6723	8.52	117		2600	4123	38.67	61.33
10	27	9	3	17	6723	8.52	118		2489	4234	37.02	62.98
11	13	9	6	17	6722	8.52	119		2569	4153	38.22	61.78
6	23	9	3	17	6719	8.51	120		2674	4045	39.8	60.2
8	19	9	4	18	6719	8.51	121	78925	2435	4284	36.24	63.76

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
2	20	9	6	17	6717	8.51	122		2677	4040	39.85	60.15
3	18	9	4	17	6717	8.51	123		2457	4260	36.58	63.42
10	8	9	5	18	6717	8.51	124		2638	4079	39.27	60.73
8	4	9	3	17	6714	8.51	125		2583	4131	38.47	61.53
8	21	9	6	18	6713	8.51	126		2598	4115	38.7	61.3
1	23	9	6	17	6711	8.5	127		2480	4231	36.95	63.05
6	10	9	4	17	6706	8.5	128		2676	4030	39.9	60.1
8	12	9	4	18	6705	8.5	129		2529	4176	37.72	62.28
4	30	9	5	17	6703	8.49	130		2583	4120	38.53	61.47
12	16	9	4	17	6703	8.49	131		2573	4130	38.39	61.61
6	9	9	3	17	6701	8.49	132		2601	4100	38.82	61.18
8	27	9	5	18	6700	8.49	133		2617	4083	39.06	60.94
9	25	9	6	17	6700	8.49	134		2751	3949	41.06	58.94
9	10	9	5	18	6699	8.49	135		2574	4125	38.42	61.58
6	2	9	3	17	6696	8.48	136		2505	4191	37.41	62.59
6	9	9	3	18	6696	8.48	137		2517	4179	37.59	62.41
10	23	9	6	17	6695	8.48	138		2705	3990	40.4	59.6
7	24	9	6	18	6694	8.48	139		2510	4184	37.5	62.5
9	8	9	3	18	6693	8.48	140		2420	4273	36.16	63.84
12	17	9	5	17	6690	8.48	141	78925	2590	4100	38.71	61.29
12	15	9	3	17	6689	8.48	142		2494	4195	37.29	62.71
10	29	9	5	17	6688	8.47	143		2676	4012	40.01	59.99
5	21	9	5	17	6687	8.47	144		2675	4012	40	60
2	27	9	6	17	6686	8.47	145		2673	4013	39.98	60.02
10	6	9	3	17	6686	8.47	146		2449	4237	36.63	63.37
12	11	9	6	18	6686	8.47	147		2607	4079	38.99	61.01
4	23	9	5	17	6684	8.47	148		2520	4164	37.7	62.3
7	8	9	4	18	6684	8.47	149		2462	4222	36.83	63.17
7	9	9	5	18	6684	8.47	150		2533	4151	37.9	62.1
9	9	9	4	18	6683	8.47	151		2451	4232	36.68	63.32
2	27	9	6	18	6682	8.47	152		2506	4176	37.5	62.5
6	24	9	4	18	6682	8.47	153		2536	4146	37.95	62.05
4	7	9	3	17	6681	8.46	154		2466	4215	36.91	63.09
10	20	9	3	18	6681	8.46	155		2300	4381	34.43	65.57
8	7	9	6	18	6680	8.46	156		2565	4115	38.4	61.6
10	7	9	4	17	6677	8.46	157		2484	4193	37.2	62.8
10	16	9	6	17	6676	8.46	158		2569	4107	38.48	61.52
7	15	9	4	18	6675	8.46	159		2504	4171	37.51	62.49
6	17	9	4	18	6674	8.46	160		2534	4140	37.97	62.03
9	1	9	3	17	6674	8.46	161	78925	2521	4153	37.77	62.23
9	2	9	4	18	6670	8.45	162		2450	4220	36.73	63.27
4	30	9	5	18	6669	8.45	163		2549	4120	38.22	61.78
5	20	9	4	17	6669	8.45	164		2527	4142	37.89	62.11
8	21	9	6	16	6668	8.45	165		2721	3947	40.81	59.19
1	22	9	5	17	6667	8.45	166		2471	4196	37.06	62.94
6	29	9	2	17	6667	8.45	167		2495	4172	37.42	62.58
12	18	9	6	18	6667	8.45	168		2765	3902	41.47	58.53
7	17	9	6	16	6665	8.44	169		2657	4008	39.86	60.14
6	26	9	6	18	6663	8.44	170		2567	4096	38.53	61.47
9	21	9	2	17	6661	8.44	171		2562	4099	38.46	61.54
7	22	9	4	18	6660	8.44	172		2562	4098	38.47	61.53
10	21	9	4	17	6660	8.44	173		2530	4130	37.99	62.01

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
6	24	9	4	17	6659	8.44	174		2845	3814	42.72	57.28
5	29	9	6	17	6658	8.44	175		2664	3994	40.01	59.99
9	16	9	4	17	6658	8.44	176		2602	4056	39.08	60.92
9	15	9	3	17	6657	8.43	177		2651	4006	39.82	60.18
10	2	9	6	16	6655	8.43	178		2573	4082	38.66	61.34
7	6	9	2	17	6654	8.43	179		2675	3979	40.2	59.8
8	18	9	3	18	6652	8.43	180		2442	4210	36.71	63.29
9	23	9	4	17	6651	8.43	181	78925	2544	4107	38.25	61.75
12	21	9	2	17	6650	8.43	182		2509	4141	37.73	62.27
11	12	9	5	18	6648	8.42	183		2556	4092	38.45	61.55
8	18	9	3	17	6647	8.42	184		2451	4196	36.87	63.13
8	14	9	6	16	6646	8.42	185		2707	3939	40.73	59.27
3	27	9	6	17	6644	8.42	186		2540	4104	38.23	61.77
7	2	9	5	16	6643	8.42	187		2638	4005	39.71	60.29
7	7	9	3	18	6643	8.42	188		2527	4116	38.04	61.96
9	29	9	3	17	6642	8.42	189		2546	4096	38.33	61.67
10	15	9	5	17	6642	8.42	190		2500	4142	37.64	62.36
9	22	9	3	17	6637	8.41	191		2554	4083	38.48	61.52
11	19	9	5	17	6637	8.41	192		2463	4174	37.11	62.89
6	18	9	5	18	6633	8.4	193		2523	4110	38.04	61.96
4	28	9	3	17	6632	8.4	194		2497	4135	37.65	62.35
5	15	9	6	16	6632	8.4	195		2767	3865	41.72	58.28
6	30	9	3	18	6631	8.4	196		2459	4172	37.08	62.92
10	15	9	5	18	6631	8.4	197		2410	4221	36.34	63.66
12	23	9	4	17	6630	8.4	198		2546	4084	38.4	61.6
3	6	9	6	17	6628	8.4	199		2600	4028	39.23	60.77
4	16	9	5	17	6626	8.4	200		2577	4049	38.89	61.11

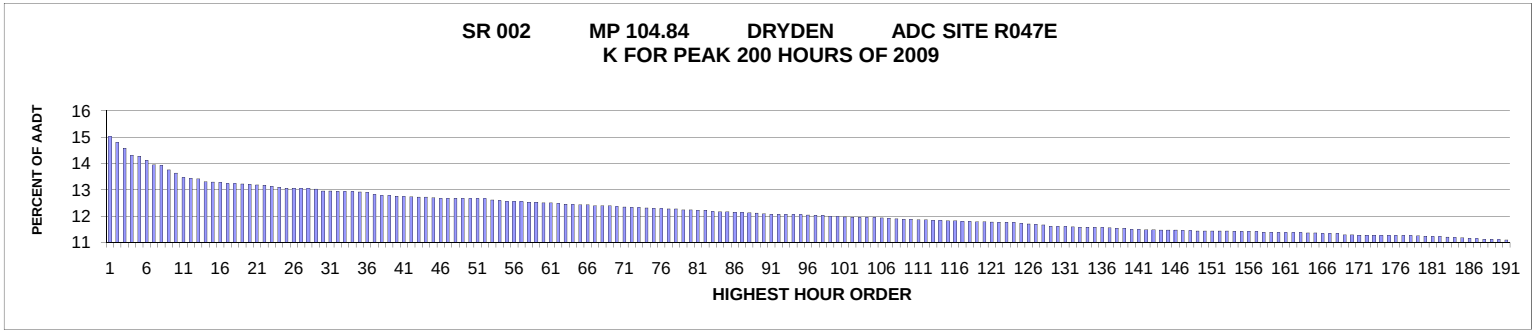

AADT= 14784 K 30 FACTOR= 13.18 K 100 FACTOR= 12.07 K 200 FACTOR= 11.1 D FACTOR= 58.67

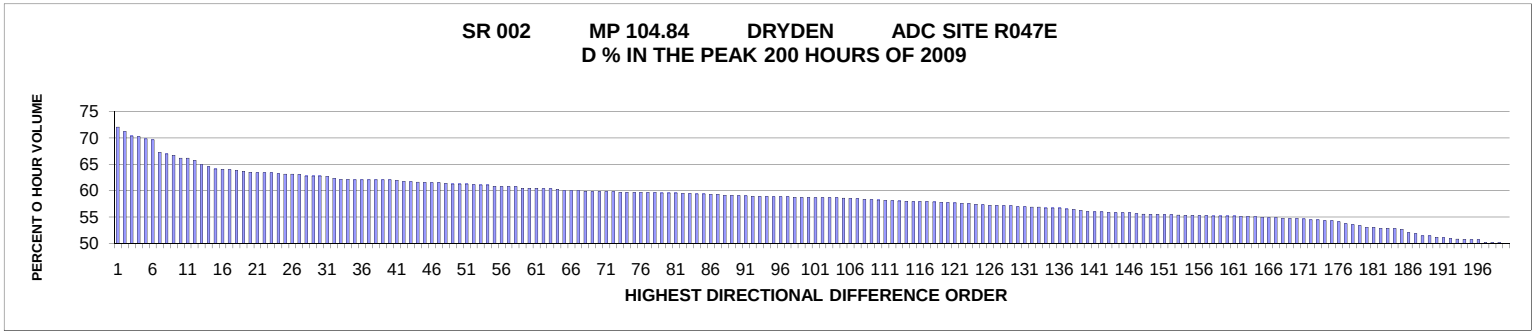

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
5	25	9	2	13	2220	15.02	1	14784	659	1561	29.68	70.32
5	22	9	6	16	2188	14.8	2		1465	723	66.96	33.04
5	25	9	2	12	2156	14.58	3		602	1554	27.92	72.08
8	9	9	1	14	2117	14.32	4		816	1301	38.55	61.45
8	9	9	1	13	2111	14.28	5		849	1262	40.22	59.78
7	19	9	1	13	2087	14.12	6		864	1223	41.4	58.6
7	5	9	1	13	2063	13.95	7		698	1365	33.83	66.17
6	21	9	1	13	2060	13.93	8		780	1280	37.86	62.14
7	12	9	1	13	2034	13.76	9		788	1246	38.74	61.26
8	23	9	1	14	2016	13.64	10		766	1250	38	62
8	23	9	1	15	1990	13.46	11		787	1203	39.55	60.45
7	5	9	1	14	1987	13.44	12		728	1259	36.64	63.36
6	28	9	1	14	1984	13.42	13		754	1230	38	62
9	4	9	6	16	1968	13.31	14		1235	733	62.75	37.25
7	19	9	1	14	1965	13.29	15		771	1194	39.24	60.76
6	28	9	1	15	1964	13.28	16		761	1203	38.75	61.25
8	16	9	1	13	1957	13.24	17		797	1160	40.73	59.27

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	16	9	1	15	1956	13.23	18		806	1150	41.21	58.79
8	16	9	1	14	1954	13.22	19		800	1154	40.94	59.06
6	19	9	6	17	1953	13.21	20		1186	767	60.73	39.27
9	7	9	2	13	1948	13.18	21	14784	638	1310	32.75	67.25
8	9	9	1	15	1947	13.17	22		786	1161	40.37	59.63
7	19	9	1	15	1943	13.14	23		785	1158	40.4	59.6
8	7	9	6	17	1936	13.1	24		1083	853	55.94	44.06
8	8	9	7	13	1933	13.07	25		951	982	49.2	50.8
8	7	9	6	16	1931	13.06	26		1137	794	58.88	41.12
5	22	9	6	17	1930	13.05	27		1197	733	62.02	37.98
9	4	9	6	17	1930	13.05	28		1196	734	61.97	38.03
8	14	9	6	15	1927	13.03	29		1017	910	52.78	47.22
5	25	9	2	14	1914	12.95	30		581	1333	30.36	69.64
8	9	9	1	17	1914	12.95	31		766	1148	40.02	59.98
8	16	9	1	16	1913	12.94	32		775	1138	40.51	59.49
5	22	9	6	18	1912	12.93	33		1214	698	63.49	36.51
6	21	9	1	14	1912	12.93	34		705	1207	36.87	63.13
6	21	9	1	15	1910	12.92	35		700	1210	36.65	63.35
7	26	9	1	13	1908	12.91	36		757	1151	39.68	60.32
6	26	9	6	16	1895	12.82	37		1078	817	56.89	43.11
7	3	9	6	16	1891	12.79	38		1228	663	64.94	35.06
7	5	9	1	15	1889	12.78	39		678	1211	35.89	64.11
8	2	9	1	14	1886	12.76	40		767	1119	40.67	59.33
8	7	9	6	15	1885	12.75	41	14784	1068	817	56.66	43.34
9	7	9	2	12	1884	12.74	42		569	1315	30.2	69.8
8	2	9	1	13	1882	12.73	43		776	1106	41.23	58.77
8	23	9	1	16	1881	12.72	44		789	1092	41.95	58.05
8	9	9	1	16	1877	12.7	45		795	1082	42.35	57.65
5	22	9	6	15	1875	12.68	46		1199	676	63.95	36.05
6	28	9	1	13	1875	12.68	47		678	1197	36.16	63.84
8	21	9	6	16	1874	12.68	48		1108	766	59.12	40.88
9	18	9	6	16	1874	12.68	49		1062	812	56.67	43.33
7	26	9	1	14	1872	12.66	50		774	1098	41.35	58.65
8	23	9	1	13	1872	12.66	51		744	1128	39.74	60.26
6	28	9	1	16	1871	12.66	52		742	1129	39.66	60.34
7	19	9	1	16	1865	12.61	53		792	1073	42.47	57.53
7	2	9	5	17	1861	12.59	54		1154	707	62.01	37.99
7	3	9	6	12	1856	12.55	55		1102	754	59.38	40.63
7	26	9	1	15	1856	12.55	56		779	1077	41.97	58.03
8	14	9	6	16	1856	12.55	57		1038	818	55.93	44.07
5	25	9	2	11	1852	12.53	58		533	1319	28.78	71.22
7	12	9	1	15	1852	12.53	59		772	1080	41.68	58.32
7	17	9	6	15	1848	12.5	60		1067	781	57.74	42.26
10	9	9	6	17	1848	12.5	61	14784	1052	796	56.93	43.07
7	5	9	1	12	1845	12.48	62		549	1296	29.76	70.24
7	24	9	6	17	1842	12.46	63		1086	756	58.96	41.04
7	3	9	6	15	1841	12.45	64		1147	694	62.3	37.7
6	19	9	6	16	1837	12.43	65		1064	773	57.92	42.08
7	10	9	6	17	1837	12.43	66		986	851	53.67	46.33
5	23	9	7	12	1832	12.39	67		1093	739	59.66	40.34
7	12	9	1	14	1832	12.39	68		676	1156	36.9	63.1
8	28	9	6	16	1832	12.39	69		1061	771	57.91	42.09

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	14	9	6	17	1827	12.36	70		950	877	52	48
7	17	9	6	16	1826	12.35	71		1056	770	57.83	42.17
10	2	9	6	17	1823	12.33	72		996	827	54.64	45.36
10	16	9	6	17	1822	12.32	73		1041	781	57.14	42.86
6	21	9	1	16	1820	12.31	74		737	1083	40.49	59.51
9	18	9	6	17	1819	12.3	75		1027	792	56.46	43.54
7	31	9	6	15	1817	12.29	76		1004	813	55.26	44.74
7	31	9	6	16	1815	12.28	77		1056	759	58.18	41.82
7	26	9	1	16	1814	12.27	78		786	1028	43.33	56.67
7	10	9	6	16	1810	12.24	79		1009	801	55.75	44.25
9	4	9	6	18	1810	12.24	80		1064	746	58.78	41.22
7	17	9	6	17	1808	12.23	81	14784	1059	749	58.57	41.43
7	3	9	6	17	1807	12.22	82		1113	694	61.59	38.41
7	2	9	5	16	1800	12.18	83		1111	689	61.72	38.28
6	26	9	6	17	1797	12.16	84		1059	738	58.93	41.07
7	24	9	6	18	1797	12.16	85		1006	791	55.98	44.02
8	30	9	1	13	1796	12.15	86		669	1127	37.25	62.75
9	25	9	6	17	1795	12.14	87		992	803	55.26	44.74
8	21	9	6	17	1794	12.13	88		1033	761	57.58	42.42
7	5	9	1	16	1792	12.12	89		744	1048	41.52	58.48
8	14	9	6	14	1787	12.09	90		905	882	50.64	49.36
8	8	9	7	14	1784	12.07	91		908	876	50.9	49.1
8	28	9	6	17	1784	12.07	92		1034	750	57.96	42.04
10	9	9	6	16	1784	12.07	93		974	810	54.6	45.4
6	21	9	1	17	1783	12.06	94		722	1061	40.49	59.51
6	14	9	1	13	1782	12.05	95		801	981	44.95	55.05
8	7	9	6	18	1780	12.04	96		1048	732	58.88	41.12
8	9	9	1	12	1779	12.03	97		685	1094	38.5	61.5
9	11	9	6	17	1778	12.03	98		964	814	54.22	45.78
6	21	9	1	12	1772	11.99	99		644	1128	36.34	63.66
9	13	9	1	13	1771	11.98	100		730	1041	41.22	58.78
8	2	9	1	15	1770	11.97	101	14784	749	1021	42.32	57.68
7	10	9	6	15	1768	11.96	102		980	788	55.43	44.57
6	12	9	6	17	1767	11.95	103		1059	708	59.93	40.07
8	16	9	1	17	1767	11.95	104		793	974	44.88	55.12
7	24	9	6	16	1766	11.95	105		1009	757	57.13	42.87
9	25	9	6	16	1763	11.93	106		928	835	52.64	47.36
6	14	9	1	14	1762	11.92	107		738	1024	41.88	58.12
9	20	9	1	14	1759	11.9	108		728	1031	41.39	58.61
8	30	9	1	14	1758	11.89	109		647	1111	36.8	63.2
7	12	9	1	16	1757	11.88	110		784	973	44.62	55.38
8	2	9	1	12	1753	11.86	111		738	1015	42.1	57.9
10	11	9	1	13	1753	11.86	112		717	1036	40.9	59.1
6	14	9	1	15	1751	11.84	113		686	1065	39.18	60.82
8	21	9	6	15	1751	11.84	114		950	801	54.25	45.75
7	3	9	6	14	1748	11.82	115		1043	705	59.67	40.33
7	24	9	6	15	1747	11.82	116		944	803	54.04	45.96
5	22	9	6	14	1745	11.8	117		1117	628	64.01	35.99
6	28	9	1	17	1745	11.8	118		685	1060	39.26	60.74
6	26	9	6	15	1743	11.79	119		1019	724	58.46	41.54
8	8	9	7	12	1743	11.79	120		868	875	49.8	50.2
7	19	9	1	17	1740	11.77	121	14784	779	961	44.77	55.23

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
5	23	9	7	13	1739	11.76	122		1070	669	61.53	38.47
8	21	9	6	18	1738	11.76	123		953	785	54.83	45.17
9	7	9	2	14	1738	11.76	124		596	1142	34.29	65.71
9	4	9	6	15	1734	11.73	125		1037	697	59.8	40.2
9	20	9	1	13	1730	11.7	126		703	1027	40.64	59.36
10	11	9	1	14	1728	11.69	127		638	1090	36.92	63.08
6	26	9	6	13	1725	11.67	128		951	774	55.13	44.87
6	14	9	1	16	1718	11.62	129		664	1054	38.65	61.35
7	31	9	6	14	1715	11.6	130		845	870	49.27	50.73
8	23	9	1	17	1715	11.6	131		768	947	44.78	55.22
6	5	9	6	17	1713	11.59	132		1005	708	58.67	41.33
6	7	9	1	14	1712	11.58	133		638	1074	37.27	62.73
8	14	9	6	18	1712	11.58	134		948	764	55.37	44.63
9	25	9	6	18	1712	11.58	135		967	745	56.48	43.52
8	16	9	1	12	1710	11.57	136		691	1019	40.41	59.59
9	6	9	1	13	1709	11.56	137		779	930	45.58	54.42
7	26	9	1	17	1708	11.55	138		766	942	44.85	55.15
8	14	9	6	13	1706	11.54	139		769	937	45.08	54.92
5	25	9	2	15	1700	11.5	140		566	1134	33.29	66.71
7	24	9	6	13	1700	11.5	141	14784	802	898	47.18	52.82
7	2	9	5	18	1699	11.49	142		966	733	56.86	43.14
6	26	9	6	14	1697	11.48	143		946	751	55.75	44.25
6	19	9	6	18	1695	11.47	144		970	725	57.23	42.77
7	6	9	2	15	1695	11.47	145		708	987	41.77	58.23
8	23	9	1	12	1695	11.47	146		660	1035	38.94	61.06
8	6	9	5	17	1694	11.46	147		1009	685	59.56	40.44
10	2	9	6	16	1693	11.45	148		934	759	55.17	44.83
8	16	9	1	18	1692	11.44	149		748	944	44.21	55.79
8	22	9	7	14	1692	11.44	150		815	877	48.17	51.83
7	19	9	1	12	1691	11.44	151		720	971	42.58	57.42
7	3	9	6	13	1690	11.43	152		951	739	56.27	43.73
10	11	9	1	15	1690	11.43	153		680	1010	40.24	59.76
6	5	9	6	16	1688	11.42	154		1041	647	61.67	38.33
8	28	9	6	15	1688	11.42	155		937	751	55.51	44.49
9	20	9	1	17	1688	11.42	156		833	855	49.35	50.65
6	19	9	6	15	1687	11.41	157		990	697	58.68	41.32
7	17	9	6	13	1684	11.39	158		865	819	51.37	48.63
10	11	9	1	16	1684	11.39	159		674	1010	40.02	59.98
7	12	9	1	17	1682	11.38	160		759	923	45.12	54.88
8	9	9	1	18	1682	11.38	161	14784	676	1006	40.19	59.81
7	31	9	6	13	1681	11.37	162		839	842	49.91	50.09
8	21	9	6	13	1681	11.37	163		842	839	50.09	49.91
7	31	9	6	17	1680	11.36	164		930	750	55.36	44.64
10	16	9	6	16	1679	11.36	165		962	717	57.3	42.7
6	12	9	6	16	1677	11.34	166		953	724	56.83	43.17
6	26	9	6	18	1677	11.34	167		886	791	52.83	47.17
5	23	9	7	15	1676	11.34	168		1024	652	61.1	38.9
6	7	9	1	16	1669	11.29	169		592	1077	35.47	64.53
7	31	9	6	18	1669	11.29	170		885	784	53.03	46.97
7	2	9	5	15	1668	11.28	171		995	673	59.65	40.35
8	7	9	6	13	1667	11.28	172		889	778	53.33	46.67
9	25	9	6	15	1667	11.28	173		919	748	55.13	44.87

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	18	9	7	14	1666	11.27	174		850	816	51.02	48.98
9	20	9	1	15	1666	11.27	175		715	951	42.92	57.08
8	21	9	6	14	1665	11.26	176		917	748	55.08	44.92
8	28	9	6	18	1665	11.26	177		906	759	54.41	45.59
8	7	9	6	14	1664	11.26	178		890	774	53.49	46.51
8	8	9	7	15	1663	11.25	179		855	808	51.41	48.59
9	7	9	2	15	1661	11.24	180		657	1004	39.55	60.45
8	30	9	1	16	1660	11.23	181	14784	676	984	40.72	59.28
9	6	9	1	14	1660	11.23	182		752	908	45.3	54.7
5	24	9	1	14	1658	11.21	183		750	908	45.24	54.76
9	11	9	6	18	1655	11.19	184		918	737	55.47	44.53
9	11	9	6	16	1653	11.18	185		919	734	55.6	44.4
8	30	9	1	15	1650	11.16	186		616	1034	37.33	62.67
6	7	9	1	13	1648	11.15	187		642	1006	38.96	61.04
7	10	9	6	13	1644	11.12	188		822	822	50	50
10	11	9	1	17	1644	11.12	189		726	918	44.16	55.84
10	16	9	6	18	1642	11.11	190		871	771	53.05	46.95
8	8	9	7	16	1641	11.1	191		802	839	48.87	51.13
9	6	9	1	15	1641	11.1	192		666	975	40.59	59.41
9	13	9	1	14	1640	11.09	193		672	968	40.98	59.02
7	25	9	7	12	1636	11.07	194		831	805	50.79	49.21
7	26	9	1	18	1636	11.07	195		696	940	42.54	57.46
5	24	9	1	13	1635	11.06	196		731	904	44.71	55.29
8	15	9	7	14	1635	11.06	197		831	804	50.83	49.17
7	10	9	6	14	1634	11.05	198		828	806	50.67	49.33
7	26	9	1	12	1634	11.05	199		658	976	40.27	59.73
8	30	9	1	17	1633	11.05	200		672	961	41.15	58.85

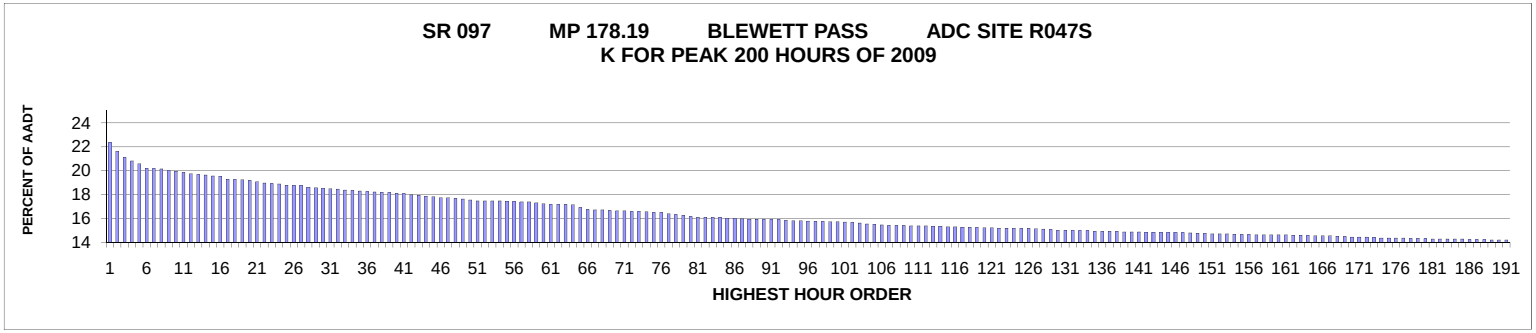

AADT= 5167 K 30 FACTOR= 18.52 K 100 FACTOR= 15.73 K 200 FACTOR= 14.21 D FACTOR= 64.94

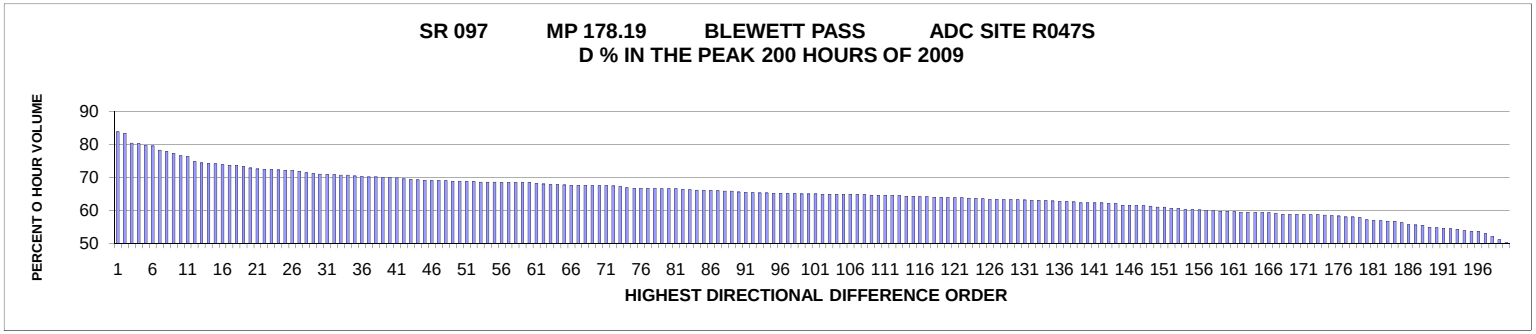

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
4	5	9	1	18	1155	22.35	1	5167	964	191	83.46	16.54
5	25	9	2	12	1117	21.62	2		227	890	20.32	79.68
5	25	9	2	13	1091	21.11	3		223	868	20.44	79.56
8	9	9	1	15	1076	20.82	4		397	679	36.9	63.1
8	9	9	1	13	1063	20.57	5		391	672	36.78	63.22
8	9	9	1	17	1044	20.21	6		350	694	33.52	66.48
8	9	9	1	14	1042	20.17	7		338	704	32.44	67.56
8	16	9	1	16	1041	20.15	8		369	672	35.45	64.55
8	23	9	1	16	1034	20.01	9		329	705	31.82	68.18
8	9	9	1	16	1032	19.97	10		374	658	36.24	63.76
6	28	9	1	15	1025	19.84	11		341	684	33.27	66.73
8	30	9	1	16	1020	19.74	12		431	589	42.25	57.75
5	25	9	2	14	1016	19.66	13		199	817	19.59	80.41
8	23	9	1	15	1015	19.64	14		354	661	34.88	65.12
7	5	9	1	14	1010	19.55	15		301	709	29.8	70.2
9	7	9	2	13	1009	19.53	16		265	744	26.26	73.74
8	23	9	1	14	996	19.28	17		324	672	32.53	67.47

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	5	9	1	13	995	19.26	18		270	725	27.14	72.86
8	16	9	1	14	994	19.24	19		357	637	35.92	64.08
5	22	9	6	16	991	19.18	20		758	233	76.49	23.51
7	19	9	1	13	986	19.08	21	5167	337	649	34.18	65.82
7	19	9	1	15	980	18.97	22		345	635	35.2	64.8
8	16	9	1	15	977	18.91	23		354	623	36.23	63.77
6	28	9	1	16	976	18.89	24		331	645	33.91	66.09
4	5	9	1	17	971	18.79	25		756	215	77.86	22.14
7	3	9	6	16	969	18.75	26		690	279	71.21	28.79
8	23	9	1	13	969	18.75	27		343	626	35.4	64.6
7	12	9	1	13	962	18.62	28		281	681	29.21	70.79
6	21	9	1	15	959	18.56	29		292	667	30.45	69.55
8	16	9	1	13	957	18.52	30		336	621	35.11	64.89
6	28	9	1	14	956	18.5	31		336	620	35.15	64.85
6	28	9	1	17	954	18.46	32		288	666	30.19	69.81
9	7	9	2	14	950	18.39	33		285	665	30	70
8	30	9	1	17	948	18.35	34		455	493	48	52
7	19	9	1	16	945	18.29	35		365	580	38.62	61.38
7	19	9	1	14	943	18.25	36		326	617	34.57	65.43
6	21	9	1	14	942	18.23	37		302	640	32.06	67.94
7	5	9	1	12	940	18.19	38		213	727	22.66	77.34
8	16	9	1	17	939	18.17	39		385	554	41	59
7	3	9	6	15	936	18.11	40		664	272	70.94	29.06
7	5	9	1	15	935	18.1	41	5167	288	647	30.8	69.2
8	2	9	1	13	929	17.98	42		360	569	38.75	61.25
7	12	9	1	14	928	17.96	43		339	589	36.53	63.47
5	25	9	2	11	923	17.86	44		149	774	16.14	83.86
9	7	9	2	12	920	17.81	45		182	738	19.78	80.22
4	5	9	1	19	916	17.73	46		717	199	78.28	21.72
7	12	9	1	15	916	17.73	47		365	551	39.85	60.15
7	12	9	1	16	914	17.69	48		357	557	39.06	60.94
7	26	9	1	16	911	17.63	49		321	590	35.24	64.76
8	23	9	1	12	907	17.55	50		304	603	33.52	66.48
5	25	9	2	15	903	17.48	51		251	652	27.8	72.2
8	2	9	1	14	903	17.48	52		361	542	39.98	60.02
8	9	9	1	12	903	17.48	53		271	632	30.01	69.99
6	21	9	1	16	902	17.46	54		277	625	30.71	69.29
7	26	9	1	13	901	17.44	55		331	570	36.74	63.26
7	26	9	1	14	900	17.42	56		346	554	38.44	61.56
5	22	9	6	15	899	17.4	57		649	250	72.19	27.81
6	21	9	1	13	899	17.4	58		298	601	33.15	66.85
8	23	9	1	17	895	17.32	59		314	581	35.08	64.92
8	30	9	1	18	890	17.22	60		471	419	52.92	47.08
7	26	9	1	15	888	17.19	61	5167	311	577	35.02	64.98
8	14	9	6	16	888	17.19	62		546	342	61.49	38.51
8	7	9	6	15	887	17.17	63		533	354	60.09	39.91
8	8	9	7	13	886	17.15	64		482	404	54.4	45.6
7	19	9	1	17	874	16.92	65		304	570	34.78	65.22
7	5	9	1	16	866	16.76	66		307	559	35.45	64.55
6	19	9	6	17	864	16.72	67		584	280	67.59	32.41
7	12	9	1	17	864	16.72	68		324	540	37.5	62.5
8	30	9	1	14	861	16.66	69		255	606	29.62	70.38

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	7	9	6	16	860	16.64	70		580	280	67.44	32.56
8	9	9	1	18	860	16.64	71		296	564	34.42	65.58
7	17	9	6	16	857	16.59	72		592	265	69.08	30.92
8	8	9	7	12	857	16.59	73		502	355	58.58	41.42
8	16	9	1	18	856	16.57	74		353	503	41.24	58.76
8	2	9	1	12	853	16.51	75		342	511	40.09	59.91
8	14	9	6	15	853	16.51	76		498	355	58.38	41.62
7	26	9	1	17	847	16.39	77		297	550	35.06	64.94
6	26	9	6	16	843	16.32	78		547	296	64.89	35.11
8	16	9	1	12	840	16.26	79		305	535	36.31	63.69
6	14	9	1	16	835	16.16	80		272	563	32.57	67.43
7	3	9	6	14	833	16.12	81	5167	602	231	72.27	27.73
8	7	9	6	18	833	16.12	82		576	257	69.15	30.85
8	30	9	1	13	833	16.12	83		259	574	31.09	68.91
9	4	9	6	17	831	16.08	84		547	284	65.82	34.18
8	23	9	1	18	829	16.04	85		334	495	40.29	59.71
8	30	9	1	15	829	16.04	86		269	560	32.45	67.55
9	7	9	2	15	825	15.97	87		278	547	33.7	66.3
5	23	9	7	15	824	15.95	88		604	220	73.3	26.7
6	21	9	1	17	824	15.95	89		266	558	32.28	67.72
6	28	9	1	13	823	15.93	90		304	519	36.94	63.06
7	19	9	1	12	823	15.93	91		302	521	36.7	63.3
8	28	9	6	16	823	15.93	92		520	303	63.18	36.82
9	5	9	7	13	818	15.83	93		554	264	67.73	32.27
6	14	9	1	13	817	15.81	94		322	495	39.41	60.59
7	17	9	6	15	817	15.81	95		514	303	62.91	37.09
8	2	9	1	15	816	15.79	96		343	473	42.03	57.97
6	14	9	1	14	814	15.75	97		294	520	36.12	63.88
7	3	9	6	12	814	15.75	98		521	293	64	36
8	7	9	6	17	813	15.73	99		509	304	62.61	37.39
8	21	9	6	16	813	15.73	100		521	292	64.08	35.92
7	26	9	1	12	811	15.7	101	5167	306	505	37.73	62.27
6	7	9	1	16	810	15.68	102		276	534	34.07	65.93
7	19	9	1	18	808	15.64	103		328	480	40.59	59.41
5	25	9	2	16	804	15.56	104		203	601	25.25	74.75
7	26	9	1	18	802	15.52	105		295	507	36.78	63.22
8	21	9	6	15	800	15.48	106		504	296	63	37
10	9	9	6	16	797	15.42	107		521	276	65.37	34.63
9	18	9	6	16	796	15.41	108		467	329	58.67	41.33
10	16	9	6	17	796	15.41	109		568	228	71.36	28.64
7	3	9	6	17	795	15.39	110		534	261	67.17	32.83
7	12	9	1	12	795	15.39	111		250	545	31.45	68.55
8	21	9	6	17	795	15.39	112		517	278	65.03	34.97
6	7	9	1	15	793	15.35	113		203	590	25.6	74.4
7	10	9	6	17	793	15.35	114		498	295	62.8	37.2
8	14	9	6	18	791	15.31	115		523	268	66.12	33.88
9	7	9	2	16	791	15.31	116		255	536	32.24	67.76
5	23	9	7	12	790	15.29	117		554	236	70.13	29.87
7	24	9	6	15	789	15.27	118		463	326	58.68	41.32
8	9	9	1	19	788	15.25	119		329	459	41.75	58.25
5	17	9	1	15	787	15.23	120		267	520	33.93	66.07
7	17	9	6	13	787	15.23	121	5167	447	340	56.8	43.2

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	2	9	1	16	786	15.21	122		317	469	40.33	59.67
8	14	9	6	13	786	15.21	123		394	392	50.13	49.87
10	9	9	6	17	786	15.21	124		484	302	61.58	38.42
6	14	9	1	15	784	15.17	125		262	522	33.42	66.58
6	26	9	6	17	784	15.17	126		523	261	66.71	33.29
10	11	9	1	14	783	15.15	127		246	537	31.42	68.58
7	2	9	5	17	782	15.13	128		562	220	71.87	28.13
7	31	9	6	14	779	15.08	129		419	360	53.79	46.21
6	14	9	1	17	776	15.02	130		262	514	33.76	66.24
9	4	9	6	18	776	15.02	131		500	276	64.43	35.57
8	22	9	7	12	775	15	132		462	313	59.61	40.39
8	8	9	7	14	774	14.98	133		442	332	57.11	42.89
8	21	9	6	13	774	14.98	134		422	352	54.52	45.48
6	14	9	1	12	772	14.94	135		279	493	36.14	63.86
8	8	9	7	15	772	14.94	136		428	344	55.44	44.56
10	11	9	1	17	772	14.94	137		225	547	29.15	70.85
8	2	9	1	17	771	14.92	138		304	467	39.43	60.57
6	19	9	6	19	769	14.88	139		558	211	72.56	27.44
6	28	9	1	18	769	14.88	140		280	489	36.41	63.59
7	10	9	6	15	769	14.88	141	5167	456	313	59.3	40.7
9	4	9	6	19	768	14.86	142		529	239	68.88	31.12
5	25	9	2	17	767	14.84	143		197	570	25.68	74.32
6	28	9	1	12	767	14.84	144		290	477	37.81	62.19
6	19	9	6	18	766	14.82	145		525	241	68.54	31.46
7	3	9	6	11	766	14.82	146		510	256	66.58	33.42
8	7	9	6	13	766	14.82	147		425	341	55.48	44.52
5	22	9	6	18	764	14.79	148		563	201	73.69	26.31
8	7	9	6	19	763	14.77	149		535	228	70.12	29.88
10	11	9	1	15	763	14.77	150		268	495	35.12	64.88
6	26	9	6	14	761	14.73	151		447	314	58.74	41.26
6	21	9	1	12	760	14.71	152		223	537	29.34	70.66
6	26	9	6	15	760	14.71	153		450	310	59.21	40.79
7	25	9	7	12	759	14.69	154		415	344	54.68	45.32
8	15	9	7	12	758	14.67	155		416	342	54.88	45.12
9	6	9	1	15	758	14.67	156		313	445	41.29	58.71
7	5	9	1	17	757	14.65	157		239	518	31.57	68.43
9	4	9	6	16	757	14.65	158		523	234	69.09	30.91
5	17	9	1	14	756	14.63	159		236	520	31.22	68.78
7	17	9	6	14	756	14.63	160		474	282	62.7	37.3
10	10	9	7	13	756	14.63	161	5167	510	246	67.46	32.54
6	12	9	6	17	755	14.61	162		492	263	65.17	34.83
9	13	9	1	13	755	14.61	163		264	491	34.97	65.03
8	16	9	1	19	754	14.59	164		294	460	38.99	61.01
7	17	9	6	17	753	14.57	165		491	262	65.21	34.79
7	25	9	7	13	752	14.55	166		428	324	56.91	43.09
7	31	9	6	15	752	14.55	167		441	311	58.64	41.36
7	18	9	7	14	750	14.52	168		435	315	58	42
5	23	9	7	13	749	14.5	169		553	196	73.83	26.17
7	10	9	6	14	746	14.44	170		423	323	56.7	43.3
7	24	9	6	16	746	14.44	171		482	264	64.61	35.39
10	11	9	1	16	746	14.44	172		193	553	25.87	74.13
7	24	9	6	14	745	14.42	173		419	326	56.24	43.76

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	10	9	6	13	743	14.38	174		403	340	54.24	45.76
7	24	9	6	13	743	14.38	175		364	379	48.99	51.01
8	22	9	7	13	743	14.38	176		421	322	56.66	43.34
9	4	9	6	15	742	14.36	177		481	261	64.82	35.18
5	23	9	7	14	741	14.34	178		566	175	76.38	23.62
8	14	9	6	14	741	14.34	179		397	344	53.58	46.42
8	14	9	6	17	740	14.32	180		439	301	59.32	40.68
9	18	9	6	17	739	14.3	181	5167	460	279	62.25	37.75
10	9	9	6	18	739	14.3	182		508	231	68.74	31.26
10	11	9	1	13	739	14.3	183		264	475	35.72	64.28
5	10	9	1	16	738	14.28	184		233	505	31.57	68.43
8	21	9	6	19	738	14.28	185		535	203	72.49	27.51
7	10	9	6	16	736	14.24	186		457	279	62.09	37.91
8	30	9	1	12	736	14.24	187		232	504	31.52	68.48
9	13	9	1	14	736	14.24	188		293	443	39.81	60.19
5	22	9	6	14	734	14.21	189		519	215	70.71	29.29
8	22	9	7	14	734	14.21	190		408	326	55.59	44.41
9	7	9	2	17	734	14.21	191		246	488	33.51	66.49
9	13	9	1	17	734	14.21	192		276	458	37.6	62.4
5	17	9	1	17	733	14.19	193		265	468	36.15	63.85

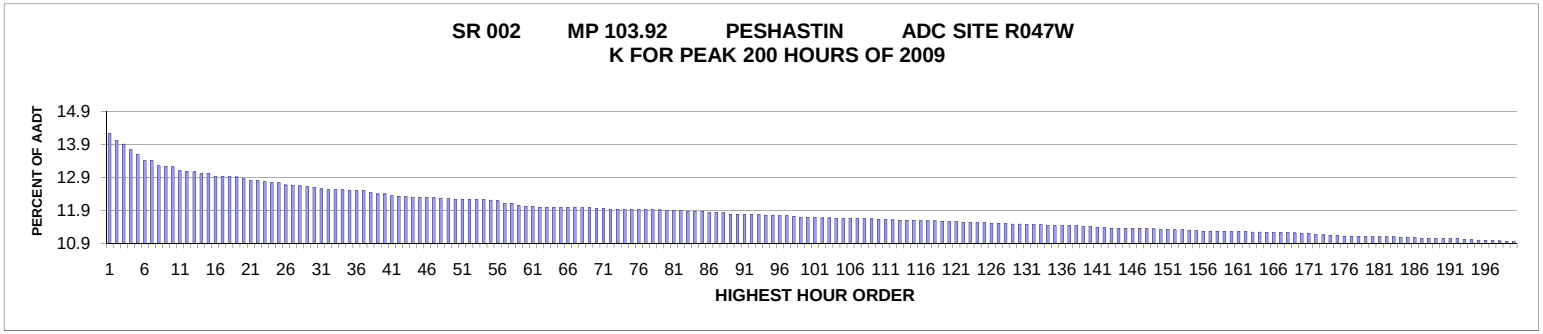

AADT= 12169 **K 30 FACTOR=** 12.6 **K 100 FACTOR=** 11.69 **K 200 FACTOR=** 10.96 **D FACTOR=** 53.29

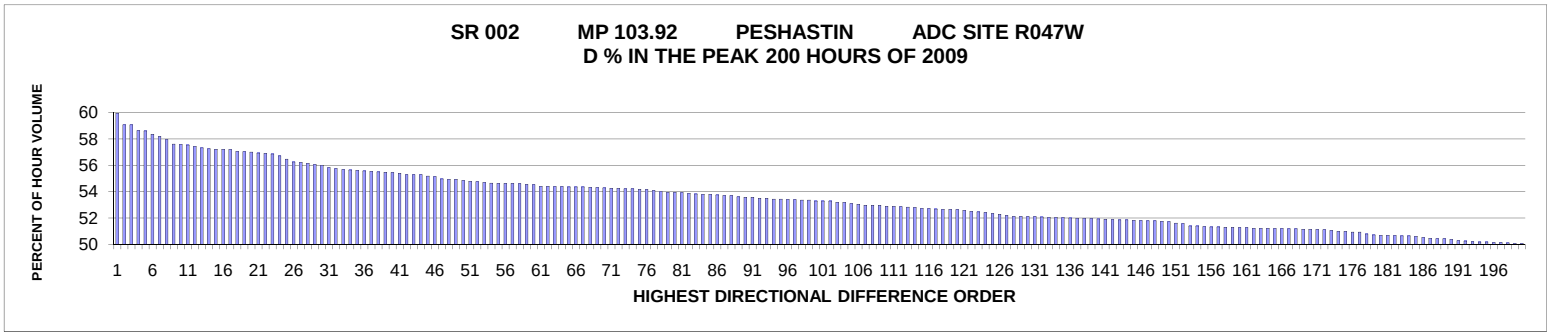

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	12	9	1	13	1730	14.22	1	12169	787	943	45.49	54.51
6	21	9	1	13	1706	14.02	2		748	958	43.85	56.15
5	25	9	2	13	1693	13.91	3		701	992	41.41	58.59
8	9	9	1	13	1672	13.74	4		791	881	47.31	52.69
7	19	9	1	13	1655	13.6	5		795	860	48.04	51.96
10	9	9	6	17	1632	13.41	6		872	760	53.43	46.57
10	11	9	1	13	1632	13.41	7		759	873	46.51	53.49
5	25	9	2	12	1612	13.25	8		686	926	42.56	57.44
8	23	9	1	14	1611	13.24	9		759	852	47.11	52.89
5	22	9	6	16	1609	13.22	10		927	682	57.61	42.39
6	28	9	1	14	1594	13.1	11		685	909	42.97	57.03
8	9	9	1	14	1593	13.09	12		734	859	46.08	53.92
10	9	9	6	16	1591	13.07	13		764	827	48.02	51.98
8	16	9	1	13	1584	13.02	14		739	845	46.65	53.35
9	20	9	1	14	1584	13.02	15		672	912	42.42	57.58
8	2	9	1	13	1573	12.93	16		718	855	45.65	54.35
8	21	9	6	16	1573	12.93	17		846	727	53.78	46.22

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	2	9	1	14	1572	12.92	18		717	855	45.61	54.39
9	4	9	6	16	1571	12.91	19		928	643	59.07	40.93
9	25	9	6	17	1564	12.85	20		815	749	52.11	47.89
7	19	9	1	14	1558	12.8	21	12169	702	856	45.06	54.94
8	23	9	1	15	1556	12.79	22		744	812	47.81	52.19
5	22	9	6	17	1554	12.77	23		911	643	58.62	41.38
7	5	9	1	13	1550	12.74	24		671	879	43.29	56.71
7	26	9	1	13	1550	12.74	25		689	861	44.45	55.55
8	23	9	1	13	1542	12.67	26		705	837	45.72	54.28
10	2	9	6	17	1541	12.66	27		768	773	49.84	50.16
8	30	9	1	13	1538	12.64	28		697	841	45.32	54.68
8	16	9	1	15	1536	12.62	29		740	796	48.18	51.82
8	7	9	6	16	1533	12.6	30		796	737	51.92	48.08
10	10	9	7	16	1527	12.55	31		844	683	55.27	44.73
10	10	9	7	13	1524	12.52	32		624	900	40.94	59.06
10	16	9	6	17	1524	12.52	33		736	788	48.29	51.71
8	8	9	7	13	1523	12.52	34		697	826	45.76	54.24
8	7	9	6	17	1520	12.49	35		788	732	51.84	48.16
9	18	9	6	17	1520	12.49	36		810	710	53.29	46.71
9	20	9	1	13	1520	12.49	37		655	865	43.09	56.91
5	23	9	7	12	1512	12.43	38		760	752	50.26	49.74
6	19	9	6	17	1509	12.4	39		846	663	56.06	43.94
6	28	9	1	13	1509	12.4	40		650	859	43.07	56.93
10	11	9	1	14	1502	12.34	41	12169	665	837	44.27	55.73
9	18	9	6	16	1500	12.33	42		809	691	53.93	46.07
5	25	9	2	14	1499	12.32	43		656	843	43.76	56.24
10	2	9	6	18	1497	12.3	44		698	799	46.63	53.37
7	5	9	1	14	1496	12.29	45		679	817	45.39	54.61
6	26	9	6	16	1495	12.29	46		775	720	51.84	48.16
7	17	9	6	16	1494	12.28	47		767	727	51.34	48.66
10	10	9	7	15	1492	12.26	48		740	752	49.6	50.4
9	6	9	1	13	1491	12.25	49		695	796	46.61	53.39
5	23	9	7	13	1490	12.24	50		773	717	51.88	48.12
8	14	9	6	15	1489	12.24	51		718	771	48.22	51.78
5	24	9	1	13	1488	12.23	52		632	856	42.47	57.53
8	9	9	1	15	1488	12.23	53		692	796	46.51	53.49
7	26	9	1	14	1487	12.22	54		675	812	45.39	54.61
9	26	9	7	16	1486	12.21	55		807	679	54.31	45.69
8	16	9	1	14	1484	12.19	56		711	773	47.91	52.09
7	24	9	6	17	1474	12.11	57		793	681	53.8	46.2
10	10	9	7	14	1474	12.11	58		670	804	45.45	54.55
9	20	9	1	15	1465	12.04	59		680	785	46.42	53.58
7	10	9	6	16	1464	12.03	60		749	715	51.16	48.84
7	12	9	1	14	1463	12.02	61	12169	609	854	41.63	58.37
8	14	9	6	16	1460	12	62		760	700	52.05	47.95
8	28	9	6	16	1460	12	63		784	676	53.7	46.3
5	25	9	2	11	1459	11.99	64		647	812	44.35	55.65
7	10	9	6	17	1459	11.99	65		728	731	49.9	50.1
7	31	9	6	16	1459	11.99	66		782	677	53.6	46.4
10	11	9	1	16	1459	11.99	67		727	732	49.83	50.17
5	22	9	6	18	1458	11.98	68		834	624	57.2	42.8
8	22	9	7	14	1458	11.98	69		679	779	46.57	53.43

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
6	21	9	1	14	1455	11.96	70		658	797	45.22	54.78
10	11	9	1	15	1455	11.96	71		689	766	47.35	52.65
6	21	9	1	15	1452	11.93	72		663	789	45.66	54.34
7	3	9	6	16	1452	11.93	73		793	659	54.61	45.39
9	25	9	6	16	1452	11.93	74		735	717	50.62	49.38
9	7	9	2	13	1451	11.92	75		624	827	43	57
9	4	9	6	17	1450	11.92	76		830	620	57.24	42.76
10	3	9	7	14	1450	11.92	77		745	705	51.38	48.62
10	10	9	7	17	1450	11.92	78		831	619	57.31	42.69
7	19	9	1	15	1449	11.91	79		685	764	47.27	52.73
8	7	9	6	15	1448	11.9	80		752	696	51.93	48.07
9	11	9	6	17	1448	11.9	81	12169	750	698	51.8	48.2
8	28	9	6	17	1447	11.89	82		786	661	54.32	45.68
6	26	9	6	17	1444	11.87	83		758	686	52.49	47.51
7	12	9	1	15	1444	11.87	84		663	781	45.91	54.09
8	21	9	6	17	1444	11.87	85		751	693	52.01	47.99
6	28	9	1	15	1440	11.83	86		653	787	45.35	54.65
9	20	9	1	17	1440	11.83	87		786	654	54.58	45.42
5	24	9	1	14	1439	11.83	88		677	762	47.05	52.95
8	8	9	7	12	1434	11.78	89		654	780	45.61	54.39
6	21	9	1	12	1433	11.78	90		657	776	45.85	54.15
9	6	9	1	14	1432	11.77	91		699	733	48.81	51.19
8	2	9	1	12	1431	11.76	92		662	769	46.26	53.74
9	27	9	1	14	1431	11.76	93		682	749	47.66	52.34
8	30	9	1	17	1430	11.75	94		598	832	41.82	58.18
10	10	9	7	12	1430	11.75	95		573	857	40.07	59.93
8	9	9	1	17	1428	11.73	96		692	736	48.46	51.54
10	2	9	6	16	1428	11.73	97		730	698	51.12	48.88
8	14	9	6	14	1426	11.72	98		703	723	49.3	50.7
7	3	9	6	12	1423	11.69	99		758	665	53.27	46.73
9	25	9	6	18	1423	11.69	100		711	712	49.96	50.04
10	3	9	7	13	1423	11.69	101	12169	675	748	47.43	52.57
7	26	9	1	15	1420	11.67	102		694	726	48.87	51.13
10	18	9	1	13	1420	11.67	103		668	752	47.04	52.96
7	5	9	1	12	1419	11.66	104		607	812	42.78	57.22
7	17	9	6	17	1419	11.66	105		750	669	52.85	47.15
9	27	9	1	13	1419	11.66	106		627	792	44.19	55.81
10	16	9	6	16	1419	11.66	107		742	677	52.29	47.71
7	3	9	6	15	1418	11.65	108		726	692	51.2	48.8
7	17	9	6	15	1417	11.64	109		718	699	50.67	49.33
9	25	9	6	15	1415	11.63	110		724	691	51.17	48.83
8	9	9	1	16	1414	11.62	111		701	713	49.58	50.42
7	24	9	6	16	1413	11.61	112		744	669	52.65	47.35
8	15	9	7	14	1412	11.6	113		665	747	47.1	52.9
5	22	9	6	15	1411	11.6	114		785	626	55.63	44.37
8	14	9	6	17	1411	11.6	115		690	721	48.9	51.1
6	20	9	7	16	1409	11.58	116		748	661	53.09	46.91
7	3	9	6	17	1409	11.58	117		789	620	56	44
7	24	9	6	15	1409	11.58	118		704	705	49.96	50.04
6	19	9	6	16	1408	11.57	119		764	644	54.26	45.74
8	8	9	7	14	1406	11.55	120		685	721	48.72	51.28
8	22	9	7	12	1405	11.55	121	12169	601	804	42.78	57.22

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
5	24	9	1	15	1404	11.54	122		684	720	48.72	51.28
8	22	9	7	13	1403	11.53	123		590	813	42.05	57.95
6	14	9	1	13	1402	11.52	124		676	726	48.22	51.78
7	2	9	5	17	1402	11.52	125		770	632	54.92	45.08
9	18	9	6	15	1401	11.51	126		770	631	54.96	45.04
8	9	9	1	12	1399	11.5	127		673	726	48.11	51.89
7	31	9	6	15	1398	11.49	128		728	670	52.07	47.93
8	23	9	1	12	1397	11.48	129		661	736	47.32	52.68
10	4	9	1	13	1397	11.48	130		657	740	47.03	52.97
7	19	9	1	16	1396	11.47	131		689	707	49.36	50.64
8	2	9	1	15	1396	11.47	132		637	759	45.63	54.37
10	9	9	6	15	1394	11.46	133		663	731	47.56	52.44
8	16	9	1	17	1392	11.44	134		712	680	51.15	48.85
6	12	9	6	17	1391	11.43	135		769	622	55.28	44.72
8	1	9	7	13	1391	11.43	136		619	772	44.5	55.5
8	22	9	7	16	1391	11.43	137		782	609	56.22	43.78
9	20	9	1	16	1391	11.43	138		705	686	50.68	49.32
8	16	9	1	16	1388	11.41	139		650	738	46.83	53.17
9	13	9	1	13	1388	11.41	140		655	733	47.19	52.81
6	14	9	1	16	1385	11.38	141	12169	643	742	46.43	53.57
6	26	9	6	15	1384	11.37	142		759	625	54.84	45.16
7	19	9	1	12	1383	11.36	143		677	706	48.95	51.05
8	21	9	6	15	1383	11.36	144		694	689	50.18	49.82
9	6	9	1	15	1383	11.36	145		617	766	44.61	55.39
6	20	9	7	14	1382	11.36	146		631	751	45.66	54.34
8	30	9	1	14	1382	11.36	147		640	742	46.31	53.69
8	7	9	6	14	1381	11.35	148		694	687	50.25	49.75
9	19	9	7	16	1380	11.34	149		734	646	53.19	46.81
7	2	9	5	16	1378	11.32	150		778	600	56.46	43.54
8	21	9	6	18	1378	11.32	151		684	694	49.64	50.36
6	28	9	1	16	1376	11.31	152		660	716	47.97	52.03
9	13	9	1	14	1376	11.31	153		611	765	44.4	55.6
7	12	9	1	16	1375	11.3	154		705	670	51.27	48.73
7	3	9	6	13	1373	11.28	155		700	673	50.98	49.02
7	10	9	6	15	1372	11.27	156		715	657	52.11	47.89
10	11	9	1	12	1372	11.27	157		677	695	49.34	50.66
5	23	9	7	15	1371	11.27	158		673	698	49.09	50.91
8	16	9	1	12	1370	11.26	159		652	718	47.59	52.41
8	22	9	7	15	1369	11.25	160		697	672	50.91	49.09
9	5	9	7	14	1369	11.25	161	12169	713	656	52.08	47.92
10	11	9	1	17	1369	11.25	162		759	610	55.44	44.56
8	23	9	1	16	1368	11.24	163		691	677	50.51	49.49
9	4	9	6	18	1368	11.24	164		741	627	54.17	45.83
6	14	9	1	14	1367	11.23	165		667	700	48.79	51.21
5	17	9	1	13	1366	11.23	166		607	759	44.44	55.56
10	18	9	1	14	1366	11.23	167		645	721	47.22	52.78
10	4	9	1	14	1365	11.22	168		630	735	46.15	53.85
8	6	9	5	17	1364	11.21	169		754	610	55.28	44.72
7	5	9	1	15	1363	11.2	170		588	775	43.14	56.86
8	30	9	1	16	1362	11.19	171		624	738	45.81	54.19
7	24	9	6	18	1358	11.16	172		733	625	53.98	46.02
7	26	9	1	12	1357	11.15	173		619	738	45.62	54.38

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
9	27	9	1	15	1356	11.14	174		665	691	49.04	50.96
7	3	9	6	14	1354	11.13	175		718	636	53.03	46.97
6	20	9	7	15	1351	11.1	176		674	677	49.89	50.11
6	26	9	6	13	1351	11.1	177		693	658	51.3	48.7
7	19	9	1	17	1351	11.1	178		711	640	52.63	47.37
7	31	9	6	13	1351	11.1	179		654	697	48.41	51.59
7	31	9	6	14	1351	11.1	180		652	699	48.26	51.74
9	4	9	6	15	1350	11.09	181	12169	739	611	54.74	45.26
9	7	9	2	12	1350	11.09	182		580	770	42.96	57.04
8	28	9	6	18	1349	11.09	183		676	673	50.11	49.89
6	20	9	7	13	1348	11.08	184		690	658	51.19	48.81
9	26	9	7	15	1347	11.07	185		684	663	50.78	49.22
10	3	9	7	16	1347	11.07	186		747	600	55.46	44.54
7	2	9	5	15	1345	11.05	187		742	603	55.17	44.83
7	29	9	4	17	1345	11.05	188		699	646	51.97	48.03
8	8	9	7	15	1345	11.05	189		655	690	48.7	51.3
5	23	9	7	14	1344	11.04	190		725	619	53.94	46.06
9	18	9	6	18	1344	11.04	191		680	664	50.6	49.4
9	24	9	5	17	1343	11.04	192		728	615	54.21	45.79
8	1	9	7	12	1340	11.01	193		625	715	46.64	53.36
8	8	9	7	16	1340	11.01	194		653	687	48.73	51.27
6	14	9	1	15	1338	11	195		618	720	46.19	53.81
5	24	9	1	17	1337	10.99	196		600	737	44.88	55.12
9	27	9	1	16	1336	10.98	197		624	712	46.71	53.29
7	10	9	6	18	1335	10.97	198		686	649	51.39	48.61
6	26	9	6	18	1334	10.96	199		651	683	48.8	51.2
8	21	9	6	14	1334	10.96	200		673	661	50.45	49.55

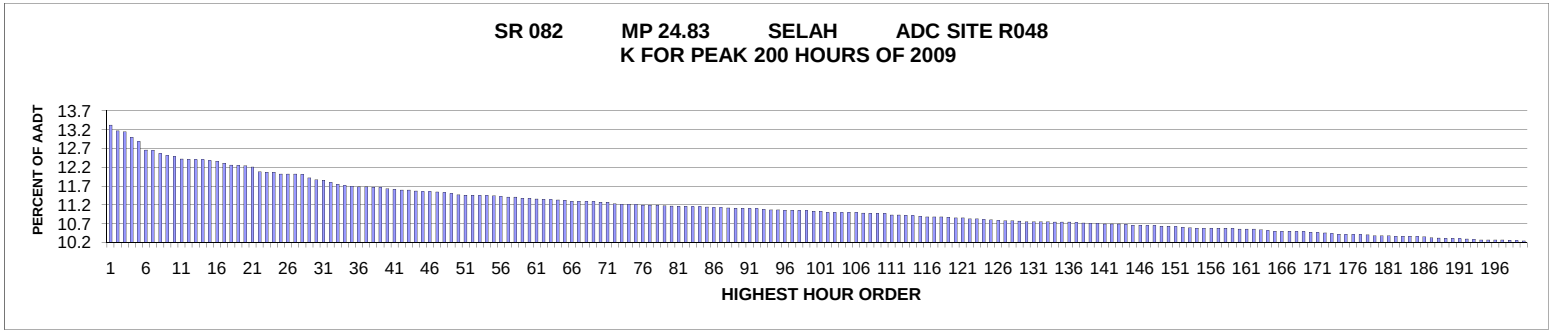

AADT= 15896 **K 30 FACTOR=** 11.87 **K 100 FACTOR=** 11.03 **K 200 FACTOR=** 10.24 **D FACTOR=** 53.48

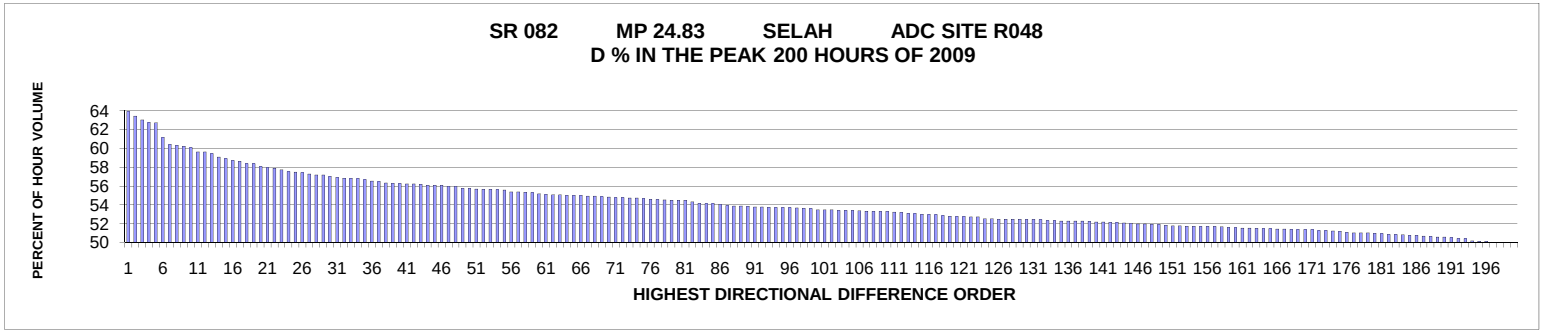

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	7	9	6	17	2117	13.32	1	15896	1026	1091	48.46	51.54
11	25	9	4	15	2094	13.17	2		1104	990	52.72	47.28
11	25	9	4	16	2088	13.14	3		1230	858	58.91	41.09
8	7	9	6	15	2066	13	4		870	1196	42.11	57.89
8	9	9	1	15	2049	12.89	5		1121	928	54.71	45.29
8	21	9	6	14	2013	12.66	6		813	1200	40.39	59.61
11	25	9	4	17	2011	12.65	7		1215	796	60.42	39.58
9	4	9	6	17	1996	12.56	8		874	1122	43.79	56.21
8	9	9	1	14	1988	12.51	9		1107	881	55.68	44.32
5	22	9	6	16	1985	12.49	10		1066	919	53.7	46.3
9	18	9	6	16	1975	12.42	11		1033	942	52.3	47.7
8	9	9	1	13	1973	12.41	12		1104	869	55.96	44.04
5	17	9	1	15	1971	12.4	13		941	1030	47.74	52.26
8	9	9	1	12	1971	12.4	14		1150	821	58.35	41.65
9	4	9	6	16	1968	12.38	15		913	1055	46.39	53.61
5	17	9	1	14	1965	12.36	16		954	1011	48.55	51.45
9	4	9	6	18	1957	12.31	17		856	1101	43.74	56.26

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
11	29	9	1	15	1949	12.26	18		847	1102	43.46	56.54
11	29	9	1	14	1947	12.25	19		874	1073	44.89	55.11
8	7	9	6	14	1945	12.24	20		857	1088	44.06	55.94
5	15	9	6	17	1941	12.21	21	15896	971	970	50.03	49.97
6	28	9	1	16	1920	12.08	22		805	1115	41.93	58.07
5	17	9	1	16	1919	12.07	23		885	1034	46.12	53.88
8	7	9	6	16	1919	12.07	24		923	996	48.1	51.9
6	28	9	1	14	1910	12.02	25		818	1092	42.83	57.17
9	4	9	6	15	1910	12.02	26		908	1002	47.54	52.46
11	25	9	4	14	1910	12.02	27		978	932	51.2	48.8
8	7	9	6	18	1909	12.01	28		869	1040	45.52	54.48
5	8	9	6	17	1895	11.92	29		1094	801	57.73	42.27
8	9	9	1	16	1887	11.87	30		986	901	52.25	47.75
11	29	9	1	16	1885	11.86	31		817	1068	43.34	56.66
8	16	9	1	15	1875	11.8	32		869	1006	46.35	53.65
6	19	9	6	17	1867	11.75	33		1103	764	59.08	40.92
6	26	9	6	15	1861	11.71	34		1025	836	55.08	44.92
5	22	9	6	15	1860	11.7	35		1030	830	55.38	44.62
6	26	9	6	16	1857	11.68	36		1033	824	55.63	44.37
8	16	9	1	16	1856	11.68	37		859	997	46.28	53.72
7	5	9	1	15	1855	11.67	38		928	927	50.03	49.97
5	22	9	6	17	1854	11.66	39		799	1055	43.1	56.9
6	28	9	1	15	1849	11.63	40		812	1037	43.92	56.08
8	14	9	6	15	1845	11.61	41	15896	922	923	49.97	50.03
10	2	9	6	17	1843	11.59	42		1017	826	55.18	44.82
6	21	9	1	15	1842	11.59	43		795	1047	43.16	56.84
8	14	9	6	16	1839	11.57	44		974	865	52.96	47.04
4	3	9	6	17	1836	11.55	45		1103	733	60.08	39.92
9	18	9	6	17	1836	11.55	46		937	899	51.03	48.97
8	9	9	1	17	1835	11.54	47		858	977	46.76	53.24
6	19	9	6	16	1833	11.53	48		1020	813	55.65	44.35
5	10	9	1	18	1828	11.5	49		727	1101	39.77	60.23
11	25	9	4	18	1824	11.47	50		1166	658	63.93	36.07
8	7	9	6	13	1822	11.46	51		787	1035	43.19	56.81
10	16	9	6	17	1822	11.46	52		942	880	51.7	48.3
6	26	9	6	17	1820	11.45	53		1046	774	57.47	42.53
10	2	9	6	16	1820	11.45	54		998	822	54.84	45.16
5	22	9	6	18	1819	11.44	55		828	991	45.52	54.48
5	17	9	1	13	1815	11.42	56		993	822	54.71	45.29
8	23	9	1	15	1814	11.41	57		853	961	47.02	52.98
10	9	9	6	18	1814	11.41	58		975	839	53.75	46.25
5	15	9	6	16	1807	11.37	59		935	872	51.74	48.26
7	19	9	1	16	1807	11.37	60		888	919	49.14	50.86
10	9	9	6	17	1805	11.36	61	15896	934	871	51.75	48.25
8	23	9	1	16	1804	11.35	62		858	946	47.56	52.44
7	17	9	6	16	1802	11.34	63		946	856	52.5	47.5
9	5	9	7	13	1801	11.33	64		939	862	52.14	47.86
5	22	9	6	14	1800	11.32	65		968	832	53.78	46.22
6	12	9	6	17	1797	11.3	66		929	868	51.7	48.3
6	21	9	1	17	1797	11.3	67		795	1002	44.24	55.76
6	19	9	6	15	1794	11.29	68		1006	788	56.08	43.92
6	21	9	1	18	1794	11.29	69		802	992	44.7	55.3

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	19	9	1	15	1792	11.27	70		872	920	48.66	51.34
7	12	9	1	14	1791	11.27	71		806	985	45	55
8	14	9	6	13	1785	11.23	72		870	915	48.74	51.26
6	28	9	1	17	1783	11.22	73		736	1047	41.28	58.72
7	26	9	1	15	1783	11.22	74		833	950	46.72	53.28
6	19	9	6	18	1782	11.21	75		971	811	54.49	45.51
5	8	9	6	18	1778	11.19	76		1057	721	59.45	40.55
7	17	9	6	15	1778	11.19	77		858	920	48.26	51.74
7	24	9	6	17	1778	11.19	78		949	829	53.37	46.63
8	23	9	1	17	1777	11.18	79		871	906	49.02	50.98
6	21	9	1	14	1775	11.17	80		775	1000	43.66	56.34
4	12	9	1	18	1774	11.16	81	15896	656	1118	36.98	63.02
8	14	9	6	14	1774	11.16	82		896	878	50.51	49.49
7	12	9	1	15	1773	11.15	83		838	935	47.26	52.74
7	12	9	1	17	1773	11.15	84		862	911	48.62	51.38
10	2	9	6	18	1771	11.14	85		997	774	56.3	43.7
7	5	9	1	16	1770	11.13	86		898	872	50.73	49.27
8	9	9	1	18	1770	11.13	87		946	824	53.45	46.55
8	23	9	1	14	1767	11.12	88		851	916	48.16	51.84
5	15	9	6	18	1766	11.11	89		893	873	50.57	49.43
7	24	9	6	16	1766	11.11	90		942	824	53.34	46.66
5	10	9	1	17	1765	11.1	91		730	1035	41.36	58.64
5	15	9	6	15	1764	11.1	92		922	842	52.27	47.73
9	25	9	6	18	1761	11.08	93		953	808	54.12	45.88
5	8	9	6	16	1759	11.07	94		1003	756	57.02	42.98
8	16	9	1	17	1759	11.07	95		836	923	47.53	52.47
5	10	9	1	16	1758	11.06	96		655	1103	37.26	62.74
9	7	9	2	12	1758	11.06	97		988	770	56.2	43.8
11	29	9	1	17	1757	11.05	98		792	965	45.08	54.92
7	24	9	6	18	1756	11.05	99		914	842	52.05	47.95
8	14	9	6	18	1753	11.03	100		900	853	51.34	48.66
8	21	9	6	16	1753	11.03	101	15896	975	778	55.62	44.38
6	21	9	1	16	1749	11	102		706	1043	40.37	59.63
7	12	9	1	16	1749	11	103		831	918	47.51	52.49
4	24	9	6	18	1748	11	104		960	788	54.92	45.08
8	14	9	6	17	1748	11	105		905	843	51.77	48.23
10	9	9	6	16	1748	11	106		942	806	53.89	46.11
6	12	9	6	16	1745	10.98	107		922	823	52.84	47.16
6	26	9	6	14	1744	10.97	108		959	785	54.99	45.01
7	17	9	6	18	1743	10.97	109		931	812	53.41	46.59
9	4	9	6	14	1743	10.97	110		812	931	46.59	53.41
7	24	9	6	15	1738	10.93	111		858	880	49.37	50.63
7	5	9	1	14	1737	10.93	112		898	839	51.7	48.3
4	5	9	1	16	1736	10.92	113		800	936	46.08	53.92
6	14	9	1	15	1735	10.91	114		739	996	42.59	57.41
4	24	9	6	17	1732	10.9	115		906	826	52.31	47.69
5	23	9	7	11	1730	10.88	116		878	852	50.75	49.25
9	7	9	2	13	1730	10.88	117		983	747	56.82	43.18
9	7	9	2	15	1729	10.88	118		964	765	55.75	44.25
9	5	9	7	12	1728	10.87	119		878	850	50.81	49.19
9	25	9	6	17	1725	10.85	120		943	782	54.67	45.33
9	18	9	6	18	1724	10.85	121	15896	889	835	51.57	48.43

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	21	9	6	15	1722	10.83	122		880	842	51.1	48.9
4	10	9	6	17	1721	10.83	123		917	804	53.28	46.72
10	16	9	6	16	1718	10.81	124		898	820	52.27	47.73
7	24	9	6	14	1716	10.8	125		851	865	49.59	50.41
7	23	9	5	15	1715	10.79	126		912	803	53.18	46.82
9	4	9	6	19	1714	10.78	127		867	847	50.58	49.42
6	19	9	6	14	1713	10.78	128		916	797	53.47	46.53
9	7	9	2	14	1712	10.77	129		948	764	55.37	44.63
6	14	9	1	16	1709	10.75	130		769	940	45	55
7	17	9	6	17	1709	10.75	131		880	829	51.49	48.51
7	26	9	1	17	1709	10.75	132		830	879	48.57	51.43
9	11	9	6	17	1709	10.75	133		827	882	48.39	51.61
5	17	9	1	12	1708	10.74	134		997	711	58.37	41.63
8	16	9	1	14	1708	10.74	135		801	907	46.9	53.1
6	26	9	6	18	1707	10.74	136		932	775	54.6	45.4
6	12	9	6	15	1706	10.73	137		874	832	51.23	48.77
10	23	9	6	17	1704	10.72	138		895	809	52.52	47.48
6	14	9	1	14	1703	10.71	139		748	955	43.92	56.08
9	4	9	6	13	1702	10.71	140		814	888	47.83	52.17
10	2	9	6	15	1700	10.69	141	15896	927	773	54.53	45.47
8	6	9	5	17	1699	10.69	142		912	787	53.68	46.32
9	11	9	6	15	1699	10.69	143		927	772	54.56	45.44
7	19	9	1	17	1698	10.68	144		874	824	51.47	48.53
6	28	9	1	13	1694	10.66	145		672	1022	39.67	60.33
8	16	9	1	13	1694	10.66	146		831	863	49.06	50.94
6	26	9	6	12	1693	10.65	147		872	821	51.51	48.49
7	17	9	6	14	1693	10.65	148		800	893	47.25	52.75
7	26	9	1	14	1690	10.63	149		845	845	50	50
5	25	9	2	15	1689	10.63	150		878	811	51.98	48.02
11	29	9	1	13	1688	10.62	151		739	949	43.78	56.22
8	21	9	6	17	1686	10.61	152		916	770	54.33	45.67
6	14	9	1	17	1683	10.59	153		783	900	46.52	53.48
4	5	9	1	17	1682	10.58	154		838	844	49.82	50.18
4	12	9	1	17	1682	10.58	155		615	1067	36.56	63.44
7	31	9	6	15	1682	10.58	156		862	820	51.25	48.75
8	23	9	1	18	1682	10.58	157		888	794	52.79	47.21
9	5	9	7	11	1682	10.58	158		773	909	45.96	54.04
7	10	9	6	14	1680	10.57	159		857	823	51.01	48.99
4	17	9	6	17	1679	10.56	160		929	750	55.33	44.67
10	16	9	6	18	1679	10.56	161	15896	881	798	52.47	47.53
5	25	9	2	13	1678	10.56	162		815	863	48.57	51.43
7	10	9	6	17	1675	10.54	163		872	803	52.06	47.94
5	10	9	1	19	1671	10.51	164		710	961	42.49	57.51
5	17	9	1	17	1669	10.5	165		766	903	45.9	54.1
6	28	9	1	18	1669	10.5	166		755	914	45.24	54.76
8	16	9	1	18	1669	10.5	167		867	802	51.95	48.05
8	28	9	6	17	1668	10.49	168		798	870	47.84	52.16
11	25	9	4	13	1667	10.49	169		798	869	47.87	52.13
6	26	9	6	13	1664	10.47	170		911	753	54.75	45.25
7	3	9	6	16	1663	10.46	171		964	699	57.97	42.03
7	5	9	1	13	1661	10.45	172		808	853	48.65	51.35
9	7	9	2	17	1659	10.44	173		893	766	53.83	46.17

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	10	9	6	18	1656	10.42	174		869	787	52.48	47.52
9	25	9	6	15	1655	10.41	175		911	744	55.05	44.95
5	22	9	6	13	1654	10.41	176		872	782	52.72	47.28
7	24	9	6	13	1654	10.41	177		816	838	49.33	50.67
7	26	9	1	16	1653	10.4	178		789	864	47.73	52.27
6	5	9	6	16	1650	10.38	179		832	818	50.42	49.58
7	31	9	6	14	1650	10.38	180		823	827	49.88	50.12
8	30	9	1	17	1650	10.38	181	15896	839	811	50.85	49.15
4	3	9	6	16	1649	10.37	182		931	718	56.46	43.54
4	26	9	1	16	1648	10.37	183		640	1008	38.83	61.17
10	23	9	6	16	1648	10.37	184		873	775	52.97	47.03
7	5	9	1	17	1647	10.36	185		856	791	51.97	48.03
9	7	9	2	16	1646	10.35	186		891	755	54.13	45.87
5	10	9	1	15	1642	10.33	187		612	1030	37.27	62.73
4	24	9	6	16	1640	10.32	188		881	759	53.72	46.28
7	2	9	5	16	1639	10.31	189		911	728	55.58	44.42
9	11	9	6	18	1639	10.31	190		836	803	51.01	48.99
6	5	9	6	17	1638	10.3	191		869	769	53.05	46.95
11	6	9	6	17	1635	10.29	192		857	778	52.42	47.58
10	23	9	6	18	1634	10.28	193		871	763	53.3	46.7
8	21	9	6	18	1633	10.27	194		872	761	53.4	46.6
7	10	9	6	15	1632	10.27	195		814	818	49.88	50.12
8	7	9	6	12	1632	10.27	196		699	933	42.83	57.17
10	25	9	1	16	1632	10.27	197		697	935	42.71	57.29
9	18	9	6	15	1631	10.26	198		754	877	46.23	53.77
8	28	9	6	15	1630	10.25	199		842	788	51.66	48.34
7	3	9	6	15	1628	10.24	200		893	735	54.85	45.15

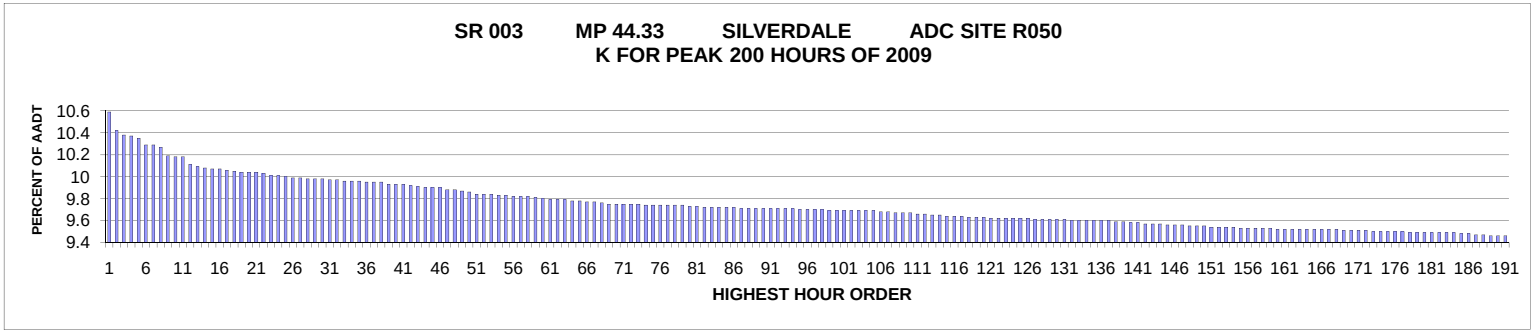

AADT= 42748 **K 30 FACTOR=** 9.98 **K 100 FACTOR=** 9.71 **K 200 FACTOR=** 9.46 **D FACTOR=** 51.95

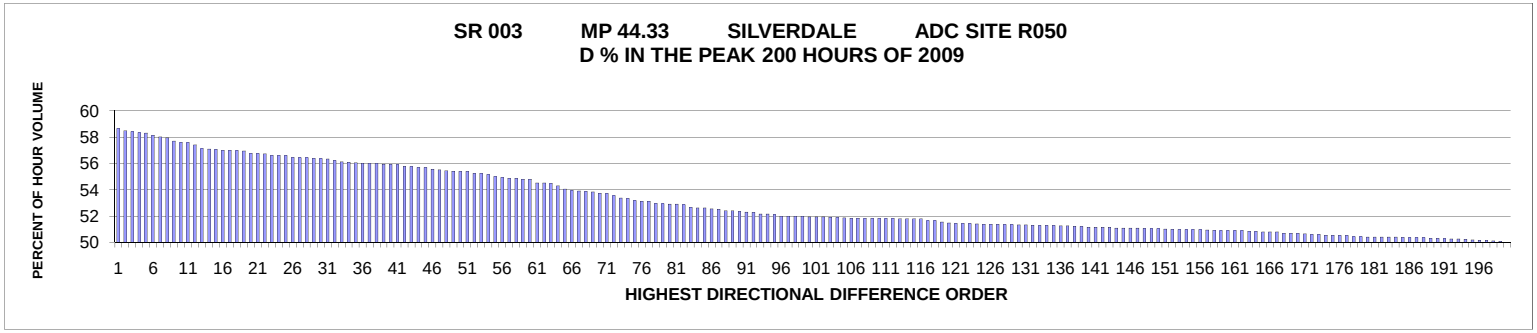

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
9	11	9	6	17	4528	10.59	1	42748	2383	2145	52.63	47.37
9	24	9	5	17	4454	10.42	2		2142	2312	48.09	51.91
9	1	9	3	17	4439	10.38	3		2168	2271	48.84	51.16
8	26	9	4	17	4434	10.37	4		2160	2274	48.71	51.29
12	18	9	6	17	4425	10.35	5		2218	2207	50.12	49.88
9	2	9	4	17	4399	10.29	6		2258	2141	51.33	48.67
10	8	9	5	17	4398	10.29	7		2223	2175	50.55	49.45
10	6	9	3	17	4392	10.27	8		2256	2136	51.37	48.63
7	15	9	4	17	4357	10.19	9		2142	2215	49.16	50.84
9	30	9	4	17	4352	10.18	10		2303	2049	52.92	47.08
10	20	9	3	17	4352	10.18	11		2231	2121	51.26	48.74
9	29	9	3	17	4323	10.11	12		2212	2111	51.17	48.83
12	1	9	3	17	4315	10.09	13		2153	2162	49.9	50.1
10	27	9	3	17	4307	10.08	14		2167	2140	50.31	49.69
8	27	9	5	17	4306	10.07	15		2135	2171	49.58	50.42
9	25	9	6	16	4306	10.07	16		1988	2318	46.17	53.83
6	16	9	3	17	4301	10.06	17		2166	2135	50.36	49.64

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
9	9	9	4	17	4297	10.05	18		2132	2165	49.62	50.38
10	1	9	5	17	4292	10.04	19		2223	2069	51.79	48.21
10	15	9	5	17	4292	10.04	20		2133	2159	49.7	50.3
10	5	9	2	17	4291	10.04	21	42748	2231	2060	51.99	48.01
12	1	9	3	16	4289	10.03	22		1868	2421	43.55	56.45
8	25	9	3	17	4278	10.01	23		2058	2220	48.11	51.89
11	25	9	4	16	4278	10.01	24		1933	2345	45.18	54.82
9	3	9	5	17	4275	10	25		2115	2160	49.47	50.53
8	5	9	4	17	4272	9.99	26		2051	2221	48.01	51.99
10	22	9	5	17	4270	9.99	27		2182	2088	51.1	48.9
9	22	9	3	17	4268	9.98	28		2078	2190	48.69	51.31
9	18	9	6	17	4266	9.98	29		2148	2118	50.35	49.65
7	22	9	4	17	4265	9.98	30		2090	2175	49	51
9	8	9	3	17	4261	9.97	31		2156	2105	50.6	49.4
2	12	9	5	16	4260	9.97	32		1922	2338	45.12	54.88
12	2	9	4	17	4258	9.96	33		2085	2173	48.97	51.03
12	18	9	6	16	4257	9.96	34		1919	2338	45.08	54.92
12	3	9	5	17	4256	9.96	35		2036	2220	47.84	52.16
6	5	9	6	16	4252	9.95	36		1954	2298	45.95	54.05
8	12	9	4	17	4252	9.95	37		2098	2154	49.34	50.66
10	7	9	4	17	4252	9.95	38		2136	2116	50.24	49.76
6	10	9	4	16	4247	9.93	39		1822	2425	42.9	57.1
7	15	9	4	16	4246	9.93	40		1893	2353	44.58	55.42
10	21	9	4	17	4244	9.93	41	42748	2174	2070	51.23	48.77
8	4	9	3	17	4242	9.92	42		2091	2151	49.29	50.71
9	16	9	4	17	4235	9.91	43		2016	2219	47.6	52.4
7	14	9	3	17	4234	9.9	44		2076	2158	49.03	50.97
8	26	9	4	16	4233	9.9	45		1820	2413	43	57
8	18	9	3	17	4231	9.9	46		2054	2177	48.55	51.45
11	24	9	3	17	4225	9.88	47		2055	2170	48.64	51.36
9	3	9	5	16	4224	9.88	48		1921	2303	45.48	54.52
9	10	9	5	17	4218	9.87	49		2071	2147	49.1	50.9
8	19	9	4	17	4213	9.86	50		2061	2152	48.92	51.08
7	9	9	5	17	4206	9.84	51		2026	2180	48.17	51.83
8	31	9	2	17	4205	9.84	52		2026	2179	48.18	51.82
9	17	9	5	17	4205	9.84	53		2136	2069	50.8	49.2
7	16	9	5	17	4202	9.83	54		2043	2159	48.62	51.38
9	25	9	6	17	4201	9.83	55		2184	2017	51.99	48.01
6	12	9	6	16	4199	9.82	56		2003	2196	47.7	52.3
7	1	9	4	17	4197	9.82	57		2021	2176	48.15	51.85
8	11	9	3	17	4196	9.82	58		2047	2149	48.78	51.22
9	10	9	5	16	4194	9.81	59		1814	2380	43.25	56.75
8	20	9	5	16	4188	9.8	60		1829	2359	43.67	56.33
10	29	9	5	17	4187	9.79	61	42748	2102	2085	50.2	49.8
9	15	9	3	17	4186	9.79	62		2093	2093	50	50
12	10	9	5	17	4184	9.79	63		2099	2085	50.17	49.83
6	10	9	4	17	4182	9.78	64		2016	2166	48.21	51.79
6	12	9	6	17	4181	9.78	65		2128	2053	50.9	49.1
9	1	9	3	16	4177	9.77	66		1838	2339	44	56
8	20	9	5	17	4175	9.77	67		2073	2102	49.65	50.35
8	6	9	5	17	4171	9.76	68		2046	2125	49.05	50.95
8	14	9	6	17	4170	9.75	69		2207	1963	52.93	47.07

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
9	23	9	4	16	4170	9.75	70		1724	2446	41.34	58.66
11	24	9	3	16	4170	9.75	71		1833	2337	43.96	56.04
9	28	9	2	17	4168	9.75	72		2165	2003	51.94	48.06
4	24	9	6	16	4167	9.75	73		1964	2203	47.13	52.87
11	17	9	3	17	4165	9.74	74		2069	2096	49.68	50.32
10	2	9	6	17	4163	9.74	75		2243	1920	53.88	46.12
10	20	9	3	16	4163	9.74	76		1903	2260	45.71	54.29
7	16	9	5	16	4162	9.74	77		1835	2327	44.09	55.91
9	21	9	2	17	4162	9.74	78		2058	2104	49.45	50.55
10	7	9	4	16	4162	9.74	79		1747	2415	41.98	58.02
4	29	9	4	17	4160	9.73	80		2020	2140	48.56	51.44
9	24	9	5	16	4159	9.73	81	42748	1855	2304	44.6	55.4
10	13	9	3	17	4157	9.72	82		2112	2045	50.81	49.19
10	28	9	4	17	4157	9.72	83		2062	2095	49.6	50.4
7	31	9	6	17	4156	9.72	84		2131	2025	51.28	48.72
10	23	9	6	16	4155	9.72	85		1956	2199	47.08	52.92
10	30	9	6	16	4154	9.72	86		1937	2217	46.63	53.37
8	6	9	5	16	4152	9.71	87		1787	2365	43.04	56.96
10	9	9	6	16	4151	9.71	88		1971	2180	47.48	52.52
11	4	9	4	17	4151	9.71	89		2054	2097	49.48	50.52
9	15	9	3	16	4150	9.71	90		1825	2325	43.98	56.02
6	9	9	3	16	4149	9.71	91		1807	2342	43.55	56.45
7	7	9	3	17	4149	9.71	92		1935	2214	46.64	53.36
7	10	9	6	17	4149	9.71	93		2149	2000	51.8	48.2
12	2	9	4	16	4149	9.71	94		1822	2327	43.91	56.09
10	14	9	4	17	4148	9.7	95		2169	1979	52.29	47.71
7	17	9	6	16	4146	9.7	96		1926	2220	46.45	53.55
7	30	9	5	17	4146	9.7	97		2004	2142	48.34	51.66
8	27	9	5	16	4146	9.7	98		1819	2327	43.87	56.13
7	22	9	4	16	4144	9.69	99		1743	2401	42.06	57.94
8	21	9	6	17	4144	9.69	100		2181	1963	52.63	47.37
9	23	9	4	17	4144	9.69	101	42748	2055	2089	49.59	50.41
10	28	9	4	16	4144	9.69	102		1728	2416	41.7	58.3
6	17	9	4	16	4143	9.69	103		1791	2352	43.23	56.77
8	7	9	6	16	4142	9.69	104		1917	2225	46.28	53.72
12	9	9	4	17	4142	9.69	105		1996	2146	48.19	51.81
8	25	9	3	16	4138	9.68	106		1776	2362	42.92	57.08
11	13	9	6	16	4138	9.68	107		1870	2268	45.19	54.81
9	16	9	4	16	4134	9.67	108		1822	2312	44.07	55.93
6	17	9	4	17	4133	9.67	109		1992	2141	48.2	51.8
8	13	9	5	16	4133	9.67	110		1820	2313	44.04	55.96
11	3	9	3	17	4131	9.66	111		2020	2111	48.9	51.1
8	13	9	5	17	4128	9.66	112		1954	2174	47.34	52.66
9	22	9	3	16	4125	9.65	113		1790	2335	43.39	56.61
9	4	9	6	17	4124	9.65	114		2120	2004	51.41	48.59
7	23	9	5	17	4123	9.64	115		2033	2090	49.31	50.69
10	23	9	6	17	4123	9.64	116		2150	1973	52.15	47.85
9	2	9	4	16	4121	9.64	117		1813	2308	43.99	56.01
9	17	9	5	16	4117	9.63	118		1803	2314	43.79	56.21
11	19	9	5	17	4117	9.63	119		2016	2101	48.97	51.03
6	11	9	5	16	4116	9.63	120		1821	2295	44.24	55.76
9	8	9	3	16	4114	9.62	121	42748	1795	2319	43.63	56.37

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
6	9	9	3	17	4113	9.62	122		2000	2113	48.63	51.37
7	8	9	4	17	4112	9.62	123		2039	2073	49.59	50.41
10	27	9	3	16	4112	9.62	124		1840	2272	44.75	55.25
4	30	9	5	17	4111	9.62	125		2016	2095	49.04	50.96
12	16	9	4	17	4111	9.62	126		2014	2097	48.99	51.01
6	8	9	2	17	4109	9.61	127		1958	2151	47.65	52.35
10	1	9	5	16	4109	9.61	128		1768	2341	43.03	56.97
9	9	9	4	16	4108	9.61	129		1750	2358	42.6	57.4
7	21	9	3	17	4107	9.61	130		2006	2101	48.84	51.16
8	17	9	2	17	4107	9.61	131		2064	2043	50.26	49.74
8	18	9	3	16	4105	9.6	132		1790	2315	43.61	56.39
6	11	9	5	17	4104	9.6	133		2092	2012	50.97	49.03
7	24	9	6	16	4104	9.6	134		2041	2063	49.73	50.27
8	14	9	6	16	4103	9.6	135		1923	2180	46.87	53.13
12	4	9	6	16	4103	9.6	136		1818	2285	44.31	55.69
6	5	9	6	17	4102	9.6	137		2099	2003	51.17	48.83
11	2	9	2	17	4100	9.59	138		1970	2130	48.05	51.95
11	3	9	3	16	4099	9.59	139		1779	2320	43.4	56.6
6	16	9	3	16	4097	9.58	140		1784	2313	43.54	56.46
11	12	9	5	16	4095	9.58	141	42748	1703	2392	41.59	58.41
12	11	9	6	17	4093	9.57	142		2177	1916	53.19	46.81
4	28	9	3	17	4092	9.57	143		2017	2075	49.29	50.71
6	4	9	5	16	4092	9.57	144		1699	2393	41.52	58.48
2	12	9	5	17	4087	9.56	145		1968	2119	48.15	51.85
8	24	9	2	17	4087	9.56	146		2027	2060	49.6	50.4
8	19	9	4	16	4085	9.56	147		1832	2253	44.85	55.15
8	28	9	6	16	4084	9.55	148		1881	2203	46.06	53.94
6	4	9	5	17	4083	9.55	149		1998	2085	48.93	51.07
6	23	9	3	17	4083	9.55	150		2035	2048	49.84	50.16
9	14	9	2	17	4080	9.54	151		2000	2080	49.02	50.98
12	11	9	6	16	4080	9.54	152		1881	2199	46.1	53.9
6	18	9	5	16	4079	9.54	153		1707	2372	41.85	58.15
4	29	9	4	16	4078	9.54	154		1749	2329	42.89	57.11
10	19	9	2	17	4076	9.53	155		2105	1971	51.64	48.36
10	6	9	3	16	4074	9.53	156		1833	2241	44.99	55.01
8	28	9	6	17	4073	9.53	157		2117	1956	51.98	48.02
2	20	9	6	17	4072	9.53	158		1999	2073	49.09	50.91
4	15	9	4	17	4072	9.53	159		1982	2090	48.67	51.33
10	16	9	6	17	4071	9.52	160		2163	1908	53.13	46.87
11	6	9	6	16	4071	9.52	161	42748	1915	2156	47.04	52.96
8	4	9	3	16	4070	9.52	162		1727	2343	42.43	57.57
10	2	9	6	16	4070	9.52	163		1931	2139	47.44	52.56
10	22	9	5	16	4070	9.52	164		1804	2266	44.32	55.68
7	9	9	5	16	4069	9.52	165		1852	2217	45.51	54.49
12	17	9	5	17	4069	9.52	166		2017	2052	49.57	50.43
12	22	9	3	16	4069	9.52	167		1810	2259	44.48	55.52
6	25	9	5	17	4068	9.52	168		1955	2113	48.06	51.94
11	20	9	6	17	4067	9.51	169		2109	1958	51.86	48.14
6	19	9	6	16	4065	9.51	170		1880	2185	46.25	53.75
7	23	9	5	16	4065	9.51	171		1806	2259	44.43	55.57
8	10	9	2	17	4065	9.51	172		1980	2085	48.71	51.29
4	27	9	2	17	4063	9.5	173		1995	2068	49.1	50.9

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	3	9	2	17	4063	9.5	174		2014	2049	49.57	50.43
9	18	9	6	16	4060	9.5	175		1996	2064	49.16	50.84
12	8	9	3	16	4059	9.5	176		1721	2338	42.4	57.6
12	10	9	5	16	4059	9.5	177		1691	2368	41.66	58.34
4	21	9	3	16	4058	9.49	178		1717	2341	42.31	57.69
8	12	9	4	16	4058	9.49	179		1761	2297	43.4	56.6
10	16	9	6	16	4057	9.49	180		1830	2227	45.11	54.89
7	1	9	4	16	4056	9.49	181	42748	1755	2301	43.27	56.73
8	21	9	6	16	4055	9.49	182		1930	2125	47.6	52.4
10	9	9	6	17	4055	9.49	183		2090	1965	51.54	48.46
12	23	9	4	16	4055	9.49	184		1809	2246	44.61	55.39
7	30	9	5	16	4054	9.48	185		1814	2240	44.75	55.25
8	7	9	6	17	4051	9.48	186		2086	1965	51.49	48.51
11	30	9	2	17	4049	9.47	187		1973	2076	48.73	51.27
11	23	9	2	17	4048	9.47	188		1938	2110	47.88	52.12
6	8	9	2	16	4046	9.46	189		1789	2257	44.22	55.78
4	24	9	6	17	4045	9.46	190		2047	1998	50.61	49.39
7	21	9	3	16	4044	9.46	191		1802	2242	44.56	55.44
11	10	9	3	16	4044	9.46	192		1808	2236	44.71	55.29
6	19	9	6	17	4043	9.46	193		2077	1966	51.37	48.63

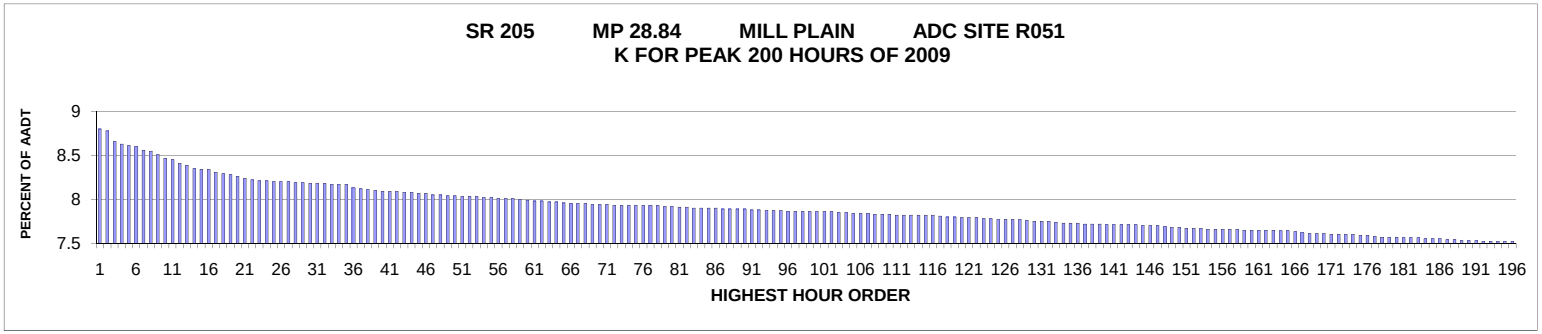

AADT= 107856 **K 30 FACTOR=** 8.18 **K 100 FACTOR=** 7.86 **K 200 FACTOR=** 7.5 **D FACTOR=** 54.39

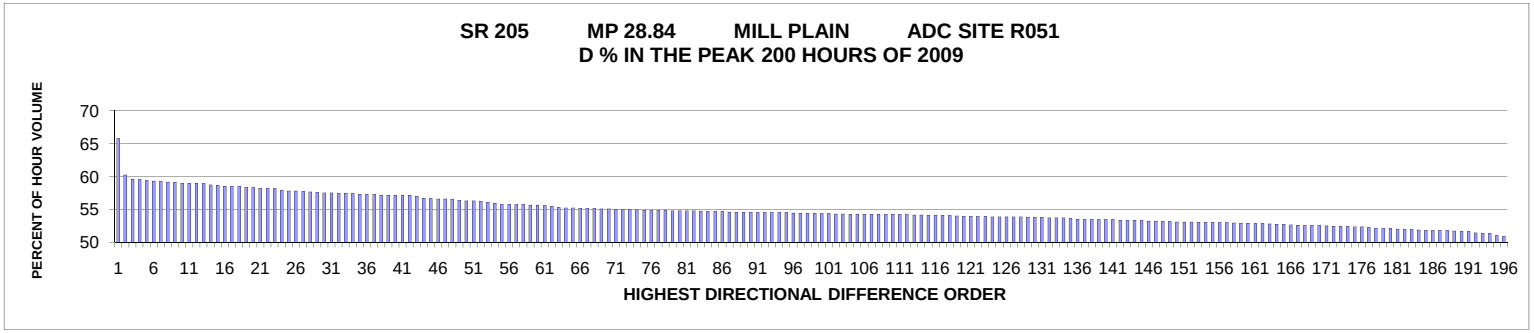

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
1	16	9	6	17	9489	8.8	1	107856	5428	4061	57.2	42.8
1	23	9	6	17	9470	8.78	2		5424	4046	57.28	42.72
1	30	9	6	17	9336	8.66	3		5341	3995	57.21	42.79
1	23	9	6	16	9304	8.63	4		5343	3961	57.43	42.57
1	30	9	6	16	9283	8.61	5		5255	4028	56.61	43.39
1	16	9	6	16	9271	8.6	6		5218	4053	56.28	43.72
1	16	9	6	18	9236	8.56	7		5086	4150	55.07	44.93
1	30	9	6	18	9223	8.55	8		5136	4087	55.69	44.31
1	9	9	6	17	9178	8.51	9		5192	3986	56.57	43.43
1	22	9	5	17	9131	8.47	10		5406	3725	59.2	40.8
8	14	9	6	18	9114	8.45	11		4720	4394	51.79	48.21
1	14	9	4	17	9076	8.41	12		5365	3711	59.11	40.89
8	14	9	6	16	9053	8.39	13		4865	4188	53.74	46.26
8	14	9	6	17	9008	8.35	14		4879	4129	54.16	45.84
6	12	9	6	17	8998	8.34	15		4692	4306	52.14	47.86
1	20	9	3	18	8991	8.34	16		5298	3693	58.93	41.07
5	15	9	6	17	8960	8.31	17		4639	4321	51.77	48.23

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
4	24	9	6	17	8943	8.29	18		4660	4283	52.11	47.89
6	26	9	6	18	8931	8.28	19		4592	4339	51.42	48.58
1	15	9	5	17	8908	8.26	20		5216	3692	58.55	41.45
5	22	9	6	16	8888	8.24	21	107856	4510	4378	50.74	49.26
4	10	9	6	17	8866	8.22	22		4716	4150	53.19	46.81
1	9	9	6	16	8857	8.21	23		4988	3869	56.32	43.68
1	13	9	3	18	8853	8.21	24		5089	3764	57.48	42.52
1	20	9	3	17	8845	8.2	25		5242	3603	59.27	40.73
5	15	9	6	16	8844	8.2	26		4598	4246	51.99	48.01
1	14	9	4	18	8840	8.2	27		5086	3754	57.53	42.47
1	21	9	4	17	8832	8.19	28		5211	3621	59	41
1	13	9	3	17	8830	8.19	29		5240	3590	59.34	40.66
8	13	9	5	18	8823	8.18	30		4770	4053	54.06	45.94
5	8	9	6	17	8822	8.18	31		4590	4232	52.03	47.97
4	10	9	6	16	8820	8.18	32		4597	4223	52.12	47.88
6	12	9	6	16	8816	8.17	33		4571	4245	51.85	48.15
1	28	9	4	18	8815	8.17	34		5095	3720	57.8	42.2
5	1	9	6	17	8813	8.17	35		4716	4097	53.51	46.49
8	26	9	4	17	8765	8.13	36		4770	3995	54.42	45.58
8	27	9	5	18	8757	8.12	37		4751	4006	54.25	45.75
4	24	9	6	16	8744	8.11	38		4643	4101	53.1	46.9
8	26	9	4	18	8740	8.1	39		4692	4048	53.68	46.32
8	25	9	3	18	8730	8.09	40		4785	3945	54.81	45.19
5	22	9	6	17	8729	8.09	41	107856	4575	4154	52.41	47.59
1	29	9	5	17	8723	8.09	42		5144	3579	58.97	41.03
5	8	9	6	16	8711	8.08	43		4512	4199	51.8	48.2
8	20	9	5	17	8711	8.08	44		4782	3929	54.9	45.1
1	21	9	4	18	8706	8.07	45		5072	3634	58.26	41.74
8	27	9	5	17	8705	8.07	46		4607	4098	52.92	47.08
6	17	9	4	18	8687	8.05	47		4731	3956	54.46	45.54
1	7	9	4	17	8680	8.05	48		4971	3709	57.27	42.73
6	25	9	5	18	8674	8.04	49		4727	3947	54.5	45.5
1	19	9	2	18	8670	8.04	50		5075	3595	58.54	41.46
1	29	9	5	18	8662	8.03	51		4909	3753	56.67	43.33
8	21	9	6	17	8660	8.03	52		4622	4038	53.37	46.63
1	22	9	5	16	8659	8.03	53		4985	3674	57.57	42.43
4	17	9	6	17	8655	8.02	54		4491	4164	51.89	48.11
6	12	9	6	18	8647	8.02	55		4585	4062	53.02	46.98
1	2	9	6	16	8644	8.01	56		4693	3951	54.29	45.71
1	22	9	5	18	8638	8.01	57		4811	3827	55.7	44.3
8	25	9	3	17	8637	8.01	58		4683	3954	54.22	45.78
6	18	9	5	18	8626	8	59		4684	3942	54.3	45.7
8	21	9	6	16	8616	7.99	60		4515	4101	52.4	47.6
5	8	9	6	18	8607	7.98	61	107856	4475	4132	51.99	48.01
6	17	9	4	17	8602	7.98	62		4746	3856	55.17	44.83
1	26	9	2	17	8597	7.97	63		5181	3416	60.27	39.73
1	19	9	2	16	8596	7.97	64		4998	3598	58.14	41.86
4	23	9	5	18	8584	7.96	65		4553	4031	53.04	46.96
6	16	9	3	17	8578	7.95	66		4703	3875	54.83	45.17
6	18	9	5	17	8578	7.95	67		4529	4049	52.8	47.2
5	21	9	5	18	8575	7.95	68		4507	4068	52.56	47.44
8	28	9	6	18	8563	7.94	69		4675	3888	54.6	45.4

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
1	15	9	5	16	8562	7.94	70		4847	3715	56.61	43.39
7	1	9	4	17	8562	7.94	71		4648	3914	54.29	45.71
5	1	9	6	16	8557	7.93	72		4422	4135	51.68	48.32
4	15	9	4	17	8555	7.93	73		4689	3866	54.81	45.19
4	17	9	6	18	8554	7.93	74		4553	4001	53.23	46.77
1	19	9	2	17	8553	7.93	75		5046	3507	59	41
1	12	9	2	17	8552	7.93	76		5098	3454	59.61	40.39
5	15	9	6	18	8551	7.93	77		4398	4153	51.43	48.57
1	23	9	6	18	8550	7.93	78		4547	4003	53.18	46.82
1	2	9	6	17	8546	7.92	79		4665	3881	54.59	45.41
1	5	9	2	17	8541	7.92	80		4914	3627	57.53	42.47
1	26	9	2	18	8534	7.91	81	107856	4974	3560	58.28	41.72
4	10	9	6	18	8534	7.91	82		4492	4042	52.64	47.36
5	14	9	5	17	8525	7.9	83		4665	3860	54.72	45.28
6	25	9	5	17	8524	7.9	84		4557	3967	53.46	46.54
5	22	9	6	15	8520	7.9	85		4147	4373	48.67	51.33
8	31	9	2	18	8516	7.9	86		4668	3848	54.81	45.19
7	10	9	6	18	8512	7.89	87		4699	3813	55.2	44.8
1	12	9	2	18	8507	7.89	88		4996	3511	58.73	41.27
7	9	9	5	18	8506	7.89	89		4618	3888	54.29	45.71
1	8	9	5	17	8505	7.89	90		5049	3456	59.37	40.63
5	14	9	5	18	8502	7.88	91		4547	3955	53.48	46.52
1	6	9	3	17	8495	7.88	92		5057	3438	59.53	40.47
8	21	9	6	18	8491	7.87	93		4395	4096	51.76	48.24
5	7	9	5	17	8489	7.87	94		4731	3758	55.73	44.27
4	17	9	6	16	8488	7.87	95		4447	4041	52.39	47.61
5	7	9	5	18	8481	7.86	96		4567	3914	53.85	46.15
4	24	9	6	18	8480	7.86	97		4435	4045	52.3	47.7
4	30	9	5	18	8480	7.86	98		4570	3910	53.89	46.11
5	21	9	5	17	8477	7.86	99		4482	3995	52.87	47.13
8	13	9	5	17	8477	7.86	100		4456	4021	52.57	47.43
1	28	9	4	17	8475	7.86	101	107856	4940	3535	58.29	41.71
4	23	9	5	17	8474	7.86	102		4600	3874	54.28	45.72
5	21	9	5	16	8469	7.85	103		4589	3880	54.19	45.81
6	23	9	3	18	8462	7.85	104		4717	3745	55.74	44.26
4	30	9	5	17	8460	7.84	105		4665	3795	55.14	44.86
6	23	9	3	17	8454	7.84	106		4660	3794	55.12	44.88
4	16	9	5	17	8451	7.84	107		4605	3846	54.49	45.51
8	20	9	5	16	8445	7.83	108		4551	3894	53.89	46.11
4	16	9	5	18	8443	7.83	109		4548	3895	53.87	46.13
7	10	9	6	17	8441	7.83	110		4452	3989	52.74	47.26
7	10	9	6	16	8439	7.82	111		4421	4018	52.39	47.61
5	20	9	4	17	8437	7.82	112		4600	3837	54.52	45.48
4	29	9	4	17	8436	7.82	113		4704	3732	55.76	44.24
5	1	9	6	18	8434	7.82	114		4444	3990	52.69	47.31
8	13	9	5	16	8431	7.82	115		4640	3791	55.03	44.97
8	18	9	3	18	8430	7.82	116		4472	3958	53.05	46.95
8	27	9	5	16	8423	7.81	117		4465	3958	53.01	46.99
1	29	9	5	16	8412	7.8	118		4800	3612	57.06	42.94
8	19	9	4	17	8409	7.8	119		4675	3734	55.6	44.4
7	2	9	5	16	8404	7.79	120		4415	3989	52.53	47.47
7	13	9	2	18	8401	7.79	121	107856	4580	3821	54.52	45.48

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	2	9	5	17	8399	7.79	122		4564	3835	54.34	45.66
8	17	9	2	18	8394	7.78	123		4594	3800	54.73	45.27
1	13	9	3	16	8391	7.78	124		4910	3481	58.52	41.48
5	20	9	4	18	8381	7.77	125		4524	3857	53.98	46.02
8	19	9	4	18	8380	7.77	126		4480	3900	53.46	46.54
8	24	9	2	18	8379	7.77	127		4580	3799	54.66	45.34
6	26	9	6	17	8377	7.77	128		4535	3842	54.14	45.86
7	13	9	2	17	8373	7.76	129		4624	3749	55.23	44.77
8	31	9	2	17	8364	7.75	130		4598	3766	54.97	45.03
5	19	9	3	17	8358	7.75	131		4596	3762	54.99	45.01
6	15	9	2	18	8356	7.75	132		4585	3771	54.87	45.13
7	1	9	4	18	8343	7.74	133		4416	3927	52.93	47.07
4	15	9	4	18	8340	7.73	134		4448	3892	53.33	46.67
4	22	9	4	17	8337	7.73	135		4568	3769	54.79	45.21
8	14	9	6	15	8337	7.73	136		4241	4096	50.87	49.13
1	14	9	4	16	8330	7.72	137		4810	3520	57.74	42.26
1	5	9	2	18	8326	7.72	138		4814	3512	57.82	42.18
6	16	9	3	18	8322	7.72	139		4586	3736	55.11	44.89
4	21	9	3	17	8321	7.71	140		4528	3793	54.42	45.58
8	20	9	5	18	8321	7.71	141	107856	4448	3873	53.46	46.54
4	22	9	4	18	8319	7.71	142		4486	3833	53.92	46.08
1	20	9	3	16	8318	7.71	143		4854	3464	58.36	41.64
6	22	9	2	17	8311	7.71	144		4529	3782	54.49	45.51
4	28	9	3	17	8310	7.7	145		4539	3771	54.62	45.38
1	7	9	4	18	8308	7.7	146		4750	3558	57.17	42.83
1	6	9	3	18	8307	7.7	147		4773	3534	57.46	42.54
8	24	9	2	17	8289	7.69	148		4477	3812	54.01	45.99
1	7	9	4	16	8282	7.68	149		4670	3612	56.39	43.61
6	24	9	4	17	8282	7.68	150		4410	3872	53.25	46.75
1	9	9	6	18	8277	7.67	151		4432	3845	53.55	46.45
1	8	9	5	18	8273	7.67	152		4857	3416	58.71	41.29
4	14	9	3	17	8273	7.67	153		4573	3700	55.28	44.72
5	12	9	3	17	8267	7.66	154		4588	3679	55.5	44.5
8	17	9	2	17	8265	7.66	155		4456	3809	53.91	46.09
6	24	9	4	18	8259	7.66	156		4447	3812	53.84	46.16
7	7	9	3	17	8258	7.66	157		4605	3653	55.76	44.24
4	27	9	2	17	8257	7.66	158		4455	3802	53.95	46.05
5	14	9	5	16	8256	7.65	159		4489	3767	54.37	45.63
1	5	9	2	16	8255	7.65	160		4731	3524	57.31	42.69
5	12	9	3	18	8253	7.65	161	107856	4527	3726	54.85	45.15
5	6	9	4	17	8252	7.65	162		4631	3621	56.12	43.88
5	6	9	4	18	8246	7.65	163		4438	3808	53.82	46.18
7	9	9	5	17	8245	7.64	164		4470	3775	54.21	45.79
8	26	9	4	16	8242	7.64	165		4441	3801	53.88	46.12
1	15	9	5	18	8231	7.63	166		4451	3780	54.08	45.92
4	20	9	2	17	8223	7.62	167		4500	3723	54.72	45.28
8	21	9	6	15	8213	7.61	168		4153	4060	50.57	49.43
6	22	9	2	18	8207	7.61	169		4454	3753	54.27	45.73
8	18	9	3	17	8206	7.61	170		4481	3725	54.61	45.39
4	21	9	3	18	8200	7.6	171		4371	3829	53.3	46.7
5	22	9	6	18	8196	7.6	172		4182	4014	51.02	48.98
5	19	9	3	18	8192	7.6	173		4433	3759	54.11	45.89

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	28	9	6	15	8192	7.6	174		4135	4057	50.48	49.52
5	13	9	4	17	8189	7.59	175		4454	3735	54.39	45.61
1	16	9	6	15	8186	7.59	176		4398	3788	53.73	46.27
6	19	9	6	16	8176	7.58	177		4097	4079	50.11	49.89
6	26	9	6	16	8169	7.57	178		4400	3769	53.86	46.14
7	1	9	4	16	8164	7.57	179		4317	3847	52.88	47.12
5	18	9	2	17	8161	7.57	180		4597	3564	56.33	43.67
4	14	9	3	18	8157	7.56	181	107856	4425	3732	54.25	45.75
1	21	9	4	16	8155	7.56	182		4703	3452	57.67	42.33
1	28	9	4	16	8155	7.56	183		4724	3431	57.93	42.07
8	24	9	2	16	8147	7.55	184		4284	3863	52.58	47.42
1	6	9	3	16	8143	7.55	185		4656	3487	57.18	42.82
5	11	9	2	17	8138	7.55	186		4556	3582	55.98	44.02
7	10	9	6	15	8135	7.54	187		3932	4203	48.33	51.67
4	23	9	5	16	8132	7.54	188		4315	3817	53.06	46.94
7	2	9	5	18	8123	7.53	189		4367	3756	53.76	46.24
1	23	9	6	15	8119	7.53	190		4420	3699	54.44	45.56
1	13	9	3	8	8117	7.53	191		2777	5340	34.21	65.79
6	18	9	5	16	8116	7.52	192		4284	3832	52.78	47.22
4	30	9	5	16	8115	7.52	193		4257	3858	52.46	47.54
4	13	9	2	17	8110	7.52	194		4478	3632	55.22	44.78
1	26	9	2	16	8108	7.52	195		4636	3472	57.18	42.82
7	7	9	3	18	8107	7.52	196		4303	3804	53.08	46.92
1	2	9	6	18	8099	7.51	197		4594	3505	56.72	43.28
4	28	9	3	18	8096	7.51	198		4322	3774	53.38	46.62
7	14	9	3	18	8095	7.51	199		4287	3808	52.96	47.04
7	8	9	4	18	8093	7.5	200		4296	3797	53.08	46.92

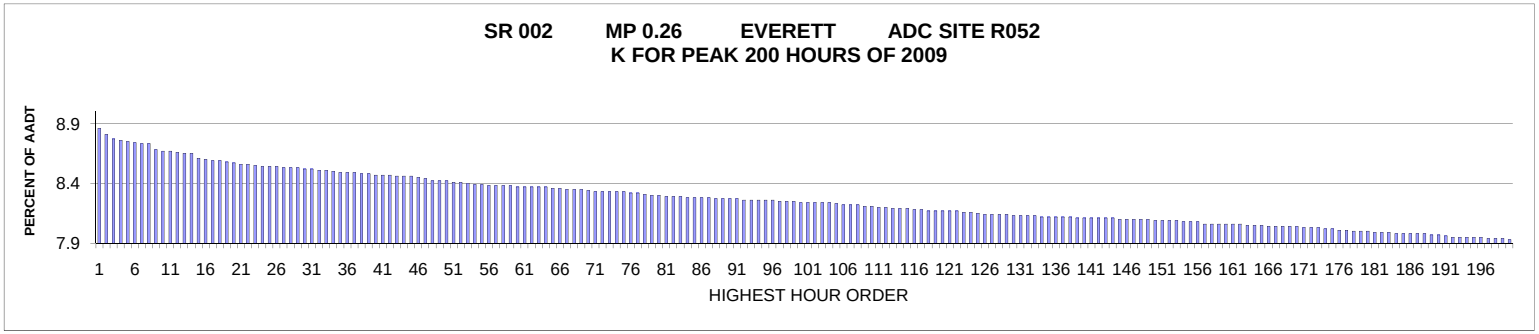

AADT= 71855 **K 30 FACTOR=** 8.52 **K 100 FACTOR=** 8.24 **K 200 FACTOR=** 7.93 **D FACTOR=** 64.88

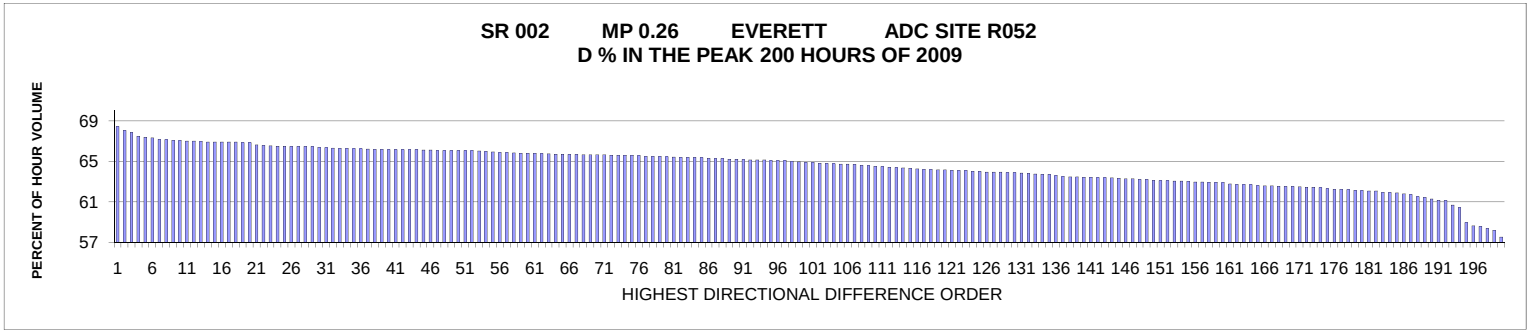

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
10	9	9	6	17	6363	8.86	1	71855	4111	2252	64.61	35.39
10	28	9	4	17	6328	8.81	2		4140	2188	65.42	34.58
9	3	9	5	17	6303	8.77	3		4143	2160	65.73	34.27
10	27	9	3	17	6296	8.76	4		4118	2178	65.41	34.59
9	22	9	3	17	6286	8.75	5		4152	2134	66.05	33.95
10	30	9	6	17	6278	8.74	6		4147	2131	66.06	33.94
8	27	9	5	17	6274	8.73	7		4076	2198	64.97	35.03
8	31	9	2	17	6270	8.73	8		4089	2181	65.22	34.78
11	3	9	3	17	6235	8.68	9		4173	2062	66.93	33.07
10	22	9	5	17	6229	8.67	10		4099	2130	65.81	34.19
9	1	9	3	17	6228	8.67	11		4227	2001	67.87	32.13
11	12	9	5	17	6221	8.66	12		4027	2194	64.73	35.27
9	2	9	4	17	6219	8.65	13		4135	2084	66.49	33.51
9	25	9	6	17	6214	8.65	14		4041	2173	65.03	34.97
9	9	9	4	17	6186	8.61	15		4117	2069	66.55	33.45
10	8	9	5	17	6178	8.6	16		4108	2070	66.49	33.51
10	2	9	6	16	6170	8.59	17		3901	2269	63.23	36.77

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
11	18	9	4	17	6170	8.59	18		4048	2122	65.61	34.39
9	17	9	5	17	6162	8.58	19		4088	2074	66.34	33.66
11	24	9	3	17	6158	8.57	20		4064	2094	66	34
10	19	9	2	17	6154	8.56	21	71855	4072	2082	66.17	33.83
11	4	9	4	18	6154	8.56	22		4053	2101	65.86	34.14
8	12	9	4	17	6142	8.55	23		3979	2163	64.78	35.22
9	15	9	3	17	6137	8.54	24		4085	2052	66.56	33.44
10	20	9	3	17	6137	8.54	25		3998	2139	65.15	34.85
10	9	9	6	16	6136	8.54	26		3761	2375	61.29	38.71
11	20	9	6	17	6132	8.53	27		3946	2186	64.35	35.65
11	4	9	4	17	6129	8.53	28		4009	2120	65.41	34.59
10	21	9	4	17	6126	8.53	29		3987	2139	65.08	34.92
8	28	9	6	17	6122	8.52	30		3929	2193	64.18	35.82
10	6	9	3	17	6120	8.52	31		4027	2093	65.8	34.2
10	13	9	3	17	6117	8.51	32		4068	2049	66.5	33.5
9	10	9	5	17	6112	8.51	33		4002	2110	65.48	34.52
9	11	9	6	17	6105	8.5	34		3897	2208	63.83	36.17
10	28	9	4	18	6101	8.49	35		4031	2070	66.07	33.93
11	6	9	6	17	6101	8.49	36		4006	2095	65.66	34.34
10	15	9	5	17	6099	8.49	37		3957	2142	64.88	35.12
9	30	9	4	17	6096	8.48	38		4028	2068	66.08	33.92
10	2	9	6	17	6091	8.48	39		3952	2139	64.88	35.12
9	21	9	2	17	6089	8.47	40		3969	2120	65.18	34.82
10	1	9	5	17	6089	8.47	41	71855	4022	2067	66.05	33.95
9	1	9	3	18	6084	8.47	42		4086	1998	67.16	32.84
10	5	9	2	17	6082	8.46	43		4023	2059	66.15	33.85
10	13	9	3	18	6080	8.46	44		4021	2059	66.13	33.87
9	28	9	2	17	6079	8.46	45		4040	2039	66.46	33.54
9	3	9	5	18	6073	8.45	46		3894	2179	64.12	35.88
9	16	9	4	18	6061	8.44	47		3891	2170	64.2	35.8
10	9	9	6	18	6053	8.42	48		3820	2233	63.11	36.89
8	25	9	3	17	6052	8.42	49		4025	2027	66.51	33.49
10	12	9	2	17	6049	8.42	50		3938	2111	65.1	34.9
8	27	9	5	18	6046	8.41	51		3913	2133	64.72	35.28
9	24	9	5	17	6041	8.41	52		3996	2045	66.15	33.85
9	22	9	3	18	6034	8.4	53		3877	2157	64.25	35.75
9	17	9	5	18	6031	8.39	54		3850	2181	63.84	36.16
8	26	9	4	17	6026	8.39	55		4005	2021	66.46	33.54
11	17	9	3	17	6025	8.38	56		3995	2030	66.31	33.69
9	3	9	5	16	6024	8.38	57		3779	2245	62.73	37.27
11	6	9	6	16	6023	8.38	58		3812	2211	63.29	36.71
9	23	9	4	17	6021	8.38	59		3931	2090	65.29	34.71
11	20	9	6	16	6017	8.37	60		3715	2302	61.74	38.26
9	16	9	4	17	6015	8.37	61	71855	3977	2038	66.12	33.88
9	14	9	2	17	6014	8.37	62		4024	1990	66.91	33.09
10	26	9	2	17	6014	8.37	63		4116	1898	68.44	31.56
11	30	9	2	17	6011	8.37	64		3982	2029	66.25	33.75
9	1	9	3	16	6008	8.36	65		3757	2251	62.53	37.47
9	8	9	3	17	6005	8.36	66		3966	2039	66.04	33.96
11	10	9	3	17	6000	8.35	67		3909	2091	65.15	34.85
9	9	9	4	18	5998	8.35	68		3929	2069	65.51	34.49
9	18	9	6	17	5998	8.35	69		3859	2139	64.34	35.66

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
9	24	9	5	18	5992	8.34	70		3879	2113	64.74	35.26
10	20	9	3	18	5989	8.33	71		3967	2022	66.24	33.76
11	2	9	2	17	5988	8.33	72		4011	1977	66.98	33.02
9	2	9	4	18	5985	8.33	73		3913	2072	65.38	34.62
11	23	9	2	17	5985	8.33	74		3968	2017	66.3	33.7
11	9	9	2	17	5982	8.33	75		4037	1945	67.49	32.51
10	14	9	4	17	5979	8.32	76		4026	1953	67.34	32.66
9	11	9	6	18	5976	8.32	77		3735	2241	62.5	37.5
8	11	9	3	17	5969	8.31	78		4000	1969	67.01	32.99
9	30	9	4	16	5967	8.3	79		3717	2250	62.29	37.71
11	5	9	5	17	5965	8.3	80		4020	1945	67.39	32.61
10	22	9	5	18	5959	8.29	81	71855	3891	2068	65.3	34.7
10	1	9	5	16	5957	8.29	82		3730	2227	62.62	37.38
10	8	9	5	18	5955	8.29	83		3985	1970	66.92	33.08
10	27	9	3	18	5953	8.28	84		3907	2046	65.63	34.37
9	11	9	6	16	5952	8.28	85		3766	2186	63.27	36.73
8	31	9	2	16	5947	8.28	86		3637	2310	61.16	38.84
11	13	9	6	16	5947	8.28	87		3694	2253	62.12	37.88
2	6	9	6	16	5944	8.27	88		3695	2249	62.16	37.84
10	30	9	6	15	5942	8.27	89		3418	2524	57.52	42.48
10	15	9	5	18	5939	8.27	90		3793	2146	63.87	36.13
11	25	9	4	16	5939	8.27	91		3714	2225	62.54	37.46
8	28	9	6	16	5935	8.26	92		3767	2168	63.47	36.53
11	3	9	3	18	5934	8.26	93		3980	1954	67.07	32.93
9	21	9	2	16	5933	8.26	94		3706	2227	62.46	37.54
10	8	9	5	16	5932	8.26	95		3736	2196	62.98	37.02
10	29	9	5	17	5932	8.26	96		3898	2034	65.71	34.29
9	23	9	4	16	5928	8.25	97		3642	2286	61.44	38.56
2	27	9	6	16	5927	8.25	98		3583	2344	60.45	39.55
9	25	9	6	18	5926	8.25	99		3798	2128	64.09	35.91
8	24	9	2	17	5923	8.24	100		3961	1962	66.87	33.13
10	15	9	5	16	5921	8.24	101	71855	3792	2129	64.04	35.96
2	4	9	4	17	5920	8.24	102		3876	2044	65.47	34.53
9	29	9	3	17	5920	8.24	103		3930	1990	66.39	33.61
9	2	9	4	16	5919	8.24	104		3704	2215	62.58	37.42
9	10	9	5	18	5917	8.23	105		3816	2101	64.49	35.51
10	6	9	3	18	5910	8.22	106		3912	1998	66.19	33.81
11	19	9	5	17	5908	8.22	107		3937	1971	66.64	33.36
9	24	9	5	16	5907	8.22	108		3791	2116	64.18	35.82
9	8	9	3	18	5900	8.21	109		3945	1955	66.86	33.14
2	5	9	5	17	5899	8.21	110		3825	2074	64.84	35.16
10	22	9	5	16	5895	8.2	111		3678	2217	62.39	37.61
9	30	9	4	18	5892	8.2	112		3853	2039	65.39	34.61
9	17	9	5	16	5887	8.19	113		3764	2123	63.94	36.06
10	30	9	6	16	5885	8.19	114		3663	2222	62.24	37.76
9	25	9	6	16	5883	8.19	115		3690	2193	62.72	37.28
11	20	9	6	18	5880	8.18	116		3643	2237	61.96	38.04
10	20	9	3	16	5876	8.18	117		3678	2198	62.59	37.41
8	12	9	4	18	5874	8.17	118		3827	2047	65.15	34.85
8	31	9	2	18	5872	8.17	119		3847	2025	65.51	34.49
8	10	9	2	17	5870	8.17	120		3855	2015	65.67	34.33
9	29	9	3	16	5869	8.17	121	71855	3684	2185	62.77	37.23

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
9	18	9	6	18	5867	8.17	122		3724	2143	63.47	36.53
9	4	9	6	16	5866	8.16	123		3762	2104	64.13	35.87
10	23	9	6	17	5866	8.16	124		3828	2038	65.26	34.74
8	27	9	5	16	5854	8.15	125		3663	2191	62.57	37.43
10	28	9	4	16	5852	8.14	126		3684	2168	62.95	37.05
10	1	9	5	18	5849	8.14	127		3871	1978	66.18	33.82
10	29	9	5	18	5849	8.14	128		3874	1975	66.23	33.77
9	15	9	3	16	5846	8.14	129		3637	2209	62.21	37.79
2	3	9	3	17	5844	8.13	130		3838	2006	65.67	34.33
10	14	9	4	18	5841	8.13	131		3841	2000	65.76	34.24
11	10	9	3	18	5840	8.13	132		3917	1923	67.07	32.93
10	21	9	4	18	5839	8.13	133		3843	1996	65.82	34.18
8	11	9	3	18	5836	8.12	134		3861	1975	66.16	33.84
11	24	9	3	16	5836	8.12	135		3702	2134	63.43	36.57
2	6	9	6	17	5833	8.12	136		3797	2036	65.1	34.9
8	25	9	3	16	5833	8.12	137		3758	2075	64.43	35.57
9	22	9	3	16	5832	8.12	138		3703	2129	63.49	36.51
9	23	9	4	18	5831	8.11	139		3732	2099	64	36
10	30	9	6	18	5829	8.11	140		3707	2122	63.6	36.4
8	17	9	2	17	5828	8.11	141	71855	3823	2005	65.6	34.4
11	6	9	6	18	5828	8.11	142		3676	2152	63.07	36.93
11	17	9	3	18	5824	8.11	143		3963	1861	68.05	31.95
11	25	9	4	15	5824	8.11	144		3415	2409	58.64	41.36
11	10	9	3	16	5823	8.1	145		3724	2099	63.95	36.05
9	15	9	3	18	5821	8.1	146		3832	1989	65.83	34.17
10	5	9	2	18	5819	8.1	147		3837	1982	65.94	34.06
11	12	9	5	16	5819	8.1	148		3649	2170	62.71	37.29
9	21	9	2	18	5818	8.1	149		3820	1998	65.66	34.34
8	28	9	6	18	5816	8.09	150		3715	2101	63.88	36.12
11	4	9	4	16	5814	8.09	151		3631	2183	62.45	37.55
9	10	9	5	16	5811	8.09	152		3592	2219	61.81	38.19
8	26	9	4	18	5810	8.09	153		3815	1995	65.66	34.34
10	13	9	3	16	5806	8.08	154		3729	2077	64.23	35.77
11	3	9	3	16	5806	8.08	155		3681	2125	63.4	36.6
11	13	9	6	17	5805	8.08	156		3681	2124	63.41	36.59
10	12	9	2	18	5794	8.06	157		3834	1960	66.17	33.83
9	9	9	4	16	5793	8.06	158		3675	2118	63.44	36.56
11	23	9	2	16	5791	8.06	159		3644	2147	62.93	37.07
8	26	9	4	16	5790	8.06	160		3585	2205	61.92	38.08
9	16	9	4	16	5790	8.06	161	71855	3703	2087	63.96	36.04
8	12	9	4	16	5788	8.06	162		3538	2250	61.13	38.87
10	5	9	2	16	5787	8.05	163		3667	2120	63.37	36.63
8	21	9	6	18	5783	8.05	164		3748	2035	64.81	35.19
11	18	9	4	16	5783	8.05	165		3637	2146	62.89	37.11
11	5	9	5	16	5780	8.04	166		3598	2182	62.25	37.75
9	8	9	3	16	5778	8.04	167		3642	2136	63.03	36.97
9	18	9	6	16	5777	8.04	168		3553	2224	61.5	38.5
9	14	9	2	18	5775	8.04	169		3829	1946	66.3	33.7
2	4	9	4	16	5774	8.04	170		3651	2123	63.23	36.77
10	21	9	4	16	5773	8.03	171		3643	2130	63.1	36.9
11	30	9	2	16	5772	8.03	172		3678	2094	63.72	36.28
11	18	9	4	18	5771	8.03	173		3802	1969	65.88	34.12

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
11	16	9	2	17	5766	8.02	174		3809	1957	66.06	33.94
10	19	9	2	18	5764	8.02	175		3857	1907	66.92	33.08
2	2	9	2	17	5753	8.01	176		3785	1968	65.79	34.21
10	6	9	3	16	5753	8.01	177		3645	2108	63.36	36.64
10	2	9	6	18	5751	8	178		3629	2122	63.1	36.9
11	20	9	6	15	5750	8	179		3391	2359	58.97	41.03
10	16	9	6	17	5749	8	180		3712	2037	64.57	35.43
10	9	9	6	15	5741	7.99	181	71855	3363	2378	58.58	41.42
2	11	9	4	17	5738	7.99	182		3702	2036	64.52	35.48
11	13	9	6	18	5738	7.99	183		3613	2125	62.97	37.03
2	27	9	6	17	5737	7.98	184		3561	2176	62.07	37.93
11	12	9	5	18	5736	7.98	185		3658	2078	63.77	36.23
9	4	9	6	15	5734	7.98	186		3338	2396	58.21	41.79
2	9	9	2	17	5733	7.98	187		3762	1971	65.62	34.38
8	25	9	3	18	5731	7.98	188		3738	1993	65.22	34.78
2	27	9	6	18	5730	7.97	189		3546	2184	61.88	38.12
11	9	9	2	18	5727	7.97	190		3832	1895	66.91	33.09
2	26	9	5	16	5723	7.96	191		3552	2171	62.07	37.93
2	11	9	4	16	5715	7.95	192		3680	2035	64.39	35.61
9	28	9	2	16	5715	7.95	193		3604	2111	63.06	36.94
2	26	9	5	17	5712	7.95	194		3827	1885	67	33
10	16	9	6	16	5712	7.95	195		3640	2072	63.73	36.27
10	2	9	6	15	5710	7.95	196		3465	2245	60.68	39.32
9	29	9	3	18	5707	7.94	197		3832	1875	67.15	32.85
8	10	9	2	18	5704	7.94	198		3745	1959	65.66	34.34
8	28	9	6	15	5702	7.94	199		3330	2372	58.4	41.6
9	28	9	2	18	5701	7.93	200		3741	1960	65.62	34.38

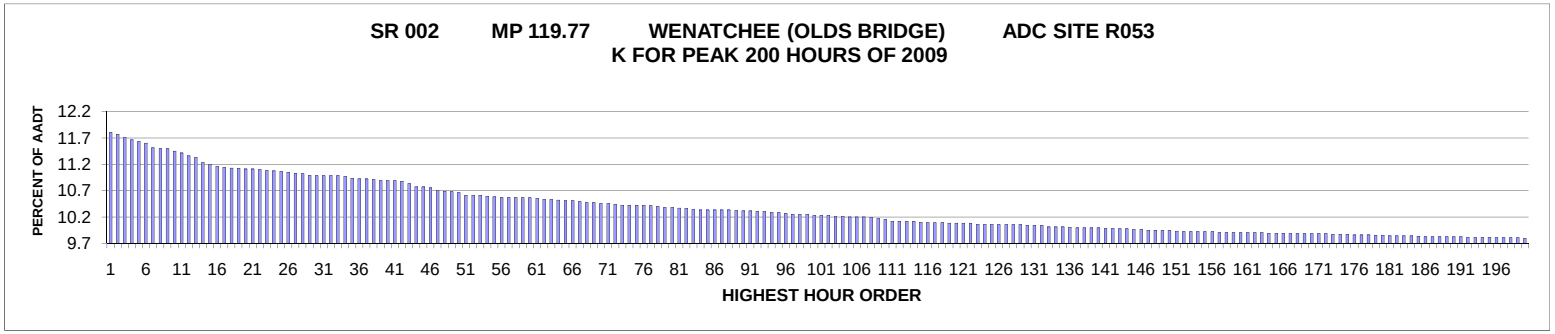

AADT= 20326 **K 30 FACTOR=** 10.98 **K 100 FACTOR=** 10.23 **K 200 FACTOR=** 9.79 **D FACTOR=** 56.44

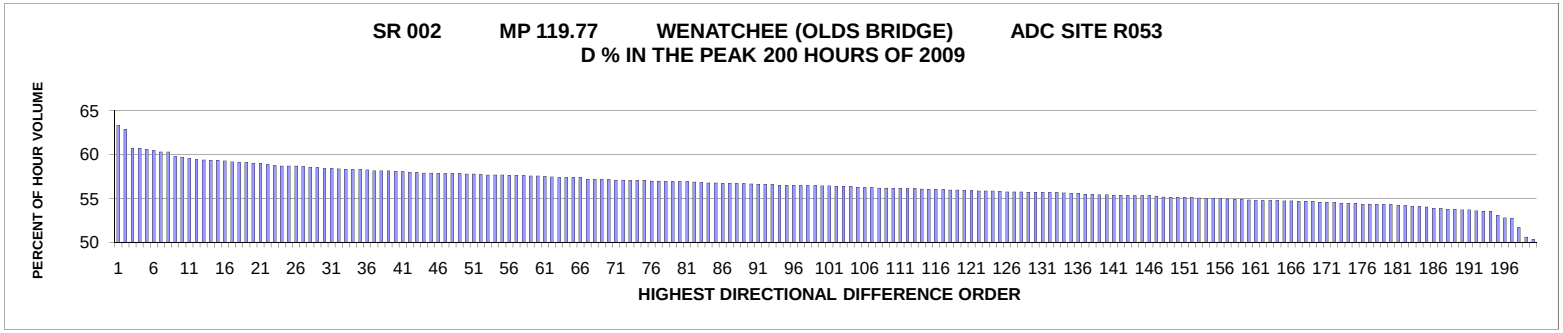

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	5	9	4	17	2401	11.81	1	20326	1521	880	63.35	36.65
7	10	9	6	17	2393	11.77	2		1314	1079	54.91	45.09
5	22	9	6	16	2381	11.71	3		1446	935	60.73	39.27
6	19	9	6	17	2369	11.66	4		1369	1000	57.79	42.21
7	1	9	4	17	2364	11.63	5		1318	1046	55.75	44.25
7	2	9	5	18	2357	11.6	6		1385	972	58.76	41.24
8	28	9	6	16	2339	11.51	7		1314	1025	56.18	43.82
5	22	9	6	17	2338	11.5	8		1371	967	58.64	41.36
6	5	9	6	18	2335	11.49	9		1182	1153	50.62	49.38
7	2	9	5	17	2328	11.45	10		1342	986	57.65	42.35
6	26	9	6	17	2319	11.41	11		1324	995	57.09	42.91
10	15	9	5	17	2310	11.36	12		1305	1005	56.49	43.51
6	26	9	6	16	2302	11.33	13		1250	1052	54.3	45.7
6	30	9	3	18	2282	11.23	14		1282	1000	56.18	43.82
7	10	9	6	16	2276	11.2	15		1237	1039	54.35	45.65
7	9	9	5	17	2268	11.16	16		1295	973	57.1	42.9
7	24	9	6	18	2264	11.14	17		1315	949	58.08	41.92

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	14	9	6	16	2262	11.13	18		1223	1039	54.07	45.93
7	2	9	5	16	2260	11.12	19		1292	968	57.17	42.83
6	26	9	6	18	2258	11.11	20		1247	1011	55.23	44.77
10	16	9	6	17	2258	11.11	21	20326	1267	991	56.11	43.89
7	16	9	5	18	2256	11.1	22		1341	915	59.44	40.56
7	1	9	4	18	2253	11.08	23		1255	998	55.7	44.3
6	25	9	5	17	2251	11.07	24		1278	973	56.77	43.23
9	4	9	6	17	2249	11.06	25		1280	969	56.91	43.09
7	10	9	6	18	2246	11.05	26		1302	944	57.97	42.03
7	7	9	3	18	2241	11.03	27		1288	953	57.47	42.53
10	8	9	5	17	2240	11.02	28		1278	962	57.05	42.95
5	1	9	6	17	2234	10.99	29		1354	880	60.61	39.39
8	21	9	6	16	2232	10.98	30		1244	988	55.73	44.27
6	19	9	6	18	2231	10.98	31		1293	938	57.96	42.04
7	17	9	6	18	2231	10.98	32		1259	972	56.43	43.57
9	18	9	6	16	2231	10.98	33		1215	1016	54.46	45.54
9	11	9	6	16	2230	10.97	34		1275	955	57.17	42.83
10	2	9	6	17	2221	10.93	35		1202	1019	54.12	45.88
7	9	9	5	18	2219	10.92	36		1264	955	56.96	43.04
7	31	9	6	17	2219	10.92	37		1279	940	57.64	42.36
10	16	9	6	16	2217	10.91	38		1257	960	56.7	43.3
6	5	9	6	17	2214	10.89	39		1189	1025	53.7	46.3
7	8	9	4	17	2213	10.89	40		1210	1003	54.68	45.32
8	28	9	6	17	2213	10.89	41	20326	1290	923	58.29	41.71
7	15	9	4	18	2211	10.88	42		1279	932	57.85	42.15
8	7	9	6	17	2201	10.83	43		1253	948	56.93	43.07
10	9	9	6	17	2190	10.77	44		1214	976	55.43	44.57
10	9	9	6	16	2189	10.77	45		1156	1033	52.81	47.19
6	29	9	2	17	2185	10.75	46		1198	987	54.83	45.17
4	24	9	6	16	2174	10.7	47		1231	943	56.62	43.38
6	19	9	6	16	2172	10.69	48		1178	994	54.24	45.76
6	24	9	4	17	2170	10.68	49		1213	957	55.9	44.1
6	18	9	5	17	2167	10.66	50		1251	916	57.73	42.27
5	15	9	6	16	2156	10.61	51		1179	977	54.68	45.32
8	7	9	6	16	2156	10.61	52		1181	975	54.78	45.22
9	9	9	4	17	2156	10.61	53		1177	979	54.59	45.41
7	24	9	6	17	2152	10.59	54		1210	942	56.23	43.77
7	7	9	3	17	2151	10.58	55		1178	973	54.77	45.23
7	6	9	2	17	2148	10.57	56		1164	984	54.19	45.81
7	6	9	2	18	2148	10.57	57		1198	950	55.77	44.23
9	25	9	6	17	2148	10.57	58		1182	966	55.03	44.97
6	23	9	3	17	2147	10.56	59		1219	928	56.78	43.22
8	26	9	4	17	2147	10.56	60		1199	948	55.85	44.15
9	4	9	6	16	2144	10.55	61	20326	1239	905	57.79	42.21
6	5	9	6	16	2141	10.53	62		1224	917	57.17	42.83
8	27	9	5	17	2140	10.53	63		1242	898	58.04	41.96
5	15	9	6	17	2139	10.52	64		1183	956	55.31	44.69
7	20	9	2	18	2137	10.51	65		1243	894	58.17	41.83
7	31	9	6	16	2137	10.51	66		1135	1002	53.11	46.89
7	14	9	3	18	2133	10.49	67		1216	917	57.01	42.99
6	29	9	2	18	2129	10.47	68		1255	874	58.95	41.05
7	17	9	6	17	2128	10.47	69		1193	935	56.06	43.94

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
6	30	9	3	17	2125	10.45	70		1200	925	56.47	43.53
9	17	9	5	17	2125	10.45	71		1239	886	58.31	41.69
8	14	9	6	17	2122	10.44	72		1120	1002	52.78	47.22
9	25	9	6	16	2118	10.42	73		1195	923	56.42	43.58
10	7	9	4	17	2118	10.42	74		1153	965	54.44	45.56
5	1	9	6	16	2117	10.42	75		1246	871	58.86	41.14
7	8	9	4	18	2117	10.42	76		1236	881	58.38	41.62
9	11	9	6	17	2116	10.41	77		1137	979	53.73	46.27
7	3	9	6	17	2113	10.4	78		1237	876	58.54	41.46
5	1	9	6	18	2110	10.38	79		1327	783	62.89	37.11
9	17	9	5	16	2109	10.38	80		1155	954	54.77	45.23
5	22	9	6	15	2108	10.37	81	20326	1226	882	58.16	41.84
4	24	9	6	17	2105	10.36	82		1204	901	57.2	42.8
7	15	9	4	17	2101	10.34	83		1206	895	57.4	42.6
9	10	9	5	17	2100	10.33	84		1187	913	56.52	43.48
7	13	9	2	18	2099	10.33	85		1223	876	58.27	41.73
7	30	9	5	17	2099	10.33	86		1266	833	60.31	39.69
9	8	9	3	17	2099	10.33	87		1188	911	56.6	43.4
10	2	9	6	16	2099	10.33	88		1148	951	54.69	45.31
5	29	9	6	16	2097	10.32	89		1153	944	54.98	45.02
8	13	9	5	17	2096	10.31	90		1176	920	56.11	43.89
7	23	9	5	18	2095	10.31	91		1206	889	57.57	42.43
7	22	9	4	17	2094	10.3	92		1222	872	58.36	41.64
9	30	9	4	17	2094	10.3	93		1169	925	55.83	44.17
10	1	9	5	17	2092	10.29	94		1169	923	55.88	44.12
8	14	9	6	18	2090	10.28	95		1151	939	55.07	44.93
8	7	9	6	18	2088	10.27	96		1259	829	60.3	39.7
5	14	9	5	17	2084	10.25	97		1189	895	57.05	42.95
6	25	9	5	18	2084	10.25	98		1238	846	59.4	40.6
7	31	9	6	18	2084	10.25	99		1188	896	57.01	42.99
8	21	9	6	18	2080	10.23	100		1204	876	57.88	42.12
7	16	9	5	17	2079	10.23	101	20326	1186	893	57.05	42.95
9	18	9	6	17	2079	10.23	102		1156	923	55.6	44.4
7	20	9	2	17	2076	10.21	103		1155	921	55.64	44.36
8	31	9	2	17	2075	10.21	104		1175	900	56.63	43.37
5	22	9	6	18	2074	10.2	105		1254	820	60.46	39.54
6	4	9	5	16	2074	10.2	106		1148	926	55.35	44.65
6	16	9	3	17	2074	10.2	107		1195	879	57.62	42.38
7	3	9	6	18	2071	10.19	108		1159	912	55.96	44.04
9	3	9	5	17	2067	10.17	109		1157	910	55.97	44.03
8	26	9	4	16	2063	10.15	110		1112	951	53.9	46.1
6	22	9	2	17	2058	10.12	111		1205	853	58.55	41.45
6	24	9	4	18	2058	10.12	112		1190	868	57.82	42.18
8	21	9	6	17	2058	10.12	113		1163	895	56.51	43.49
11	25	9	4	16	2058	10.12	114		1222	836	59.38	40.62
7	22	9	4	18	2053	10.1	115		1151	902	56.06	43.94
6	12	9	6	16	2051	10.09	116		1115	936	54.36	45.64
6	12	9	6	18	2050	10.09	117		1192	858	58.15	41.85
7	21	9	3	18	2050	10.09	118		1130	920	55.12	44.88
7	29	9	4	17	2049	10.08	119		1203	846	58.71	41.29
8	20	9	5	17	2049	10.08	120		1176	873	57.39	42.61
9	24	9	5	17	2049	10.08	121	20326	1182	867	57.69	42.31

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
10	9	9	6	18	2048	10.08	122		1142	906	55.76	44.24
5	8	9	6	17	2045	10.06	123		1184	861	57.9	42.1
5	14	9	5	16	2045	10.06	124		1137	908	55.6	44.4
6	25	9	5	16	2044	10.06	125		1115	929	54.55	45.45
6	23	9	3	18	2043	10.05	126		1206	837	59.03	40.97
8	20	9	5	16	2043	10.05	127		1130	913	55.31	44.69
9	22	9	3	17	2043	10.05	128		1159	884	56.73	43.27
10	20	9	3	17	2042	10.05	129		1094	948	53.57	46.43
6	12	9	6	17	2041	10.04	130		1240	801	60.75	39.25
8	31	9	2	16	2041	10.04	131		1098	943	53.8	46.2
12	23	9	4	17	2041	10.04	132		1149	892	56.3	43.7
9	3	9	5	16	2034	10.01	133		1139	895	56	44
9	21	9	2	17	2034	10.01	134		1173	861	57.67	42.33
10	16	9	6	18	2034	10.01	135		1215	819	59.73	40.27
6	17	9	4	18	2032	10	136		1205	827	59.3	40.7
8	6	9	5	16	2031	9.99	137		1139	892	56.08	43.92
8	10	9	2	17	2031	9.99	138		1126	905	55.44	44.56
5	8	9	6	16	2030	9.99	139		1131	899	55.71	44.29
7	14	9	3	17	2030	9.99	140		1150	880	56.65	43.35
7	31	9	6	15	2029	9.98	141	20326	1116	913	55	45
9	11	9	6	18	2029	9.98	142		1087	942	53.57	46.43
8	3	9	2	17	2027	9.97	143		1132	895	55.85	44.15
7	30	9	5	16	2026	9.97	144		1109	917	54.74	45.26
7	17	9	6	15	2025	9.96	145		1117	908	55.16	44.84
6	17	9	4	17	2024	9.96	146		1205	819	59.54	40.46
8	27	9	5	16	2022	9.95	147		1119	903	55.34	44.66
9	10	9	5	18	2022	9.95	148		1195	827	59.1	40.9
7	6	9	2	16	2021	9.94	149		1044	977	51.66	48.34
8	10	9	2	16	2021	9.94	150		1110	911	54.92	45.08
8	25	9	3	17	2018	9.93	151		1145	873	56.74	43.26
9	8	9	3	16	2017	9.92	152		1104	913	54.73	45.27
10	2	9	6	18	2017	9.92	153		1087	930	53.89	46.11
7	10	9	6	14	2016	9.92	154		1015	1001	50.35	49.65
8	24	9	2	17	2016	9.92	155		1166	850	57.84	42.16
8	28	9	6	18	2016	9.92	156		1193	823	59.18	40.82
4	30	9	5	17	2013	9.9	157		1146	867	56.93	43.07
5	27	9	4	16	2013	9.9	158		1109	904	55.09	44.91
7	13	9	2	17	2013	9.9	159		1110	903	55.14	44.86
8	6	9	5	17	2013	9.9	160		1155	858	57.38	42.62
8	11	9	3	16	2013	9.9	161	20326	1126	887	55.94	44.06
9	23	9	4	17	2013	9.9	162		1130	883	56.14	43.86
11	10	9	3	17	2013	9.9	163		1195	818	59.36	40.64
7	9	9	5	16	2011	9.89	164		1129	882	56.14	43.86
10	22	9	5	17	2011	9.89	165		1175	836	58.43	41.57
8	27	9	5	18	2010	9.89	166		1180	830	58.71	41.29
4	22	9	4	16	2009	9.88	167		1097	912	54.6	45.4
8	12	9	4	17	2008	9.88	168		1155	853	57.52	42.48
9	1	9	3	16	2008	9.88	169		1107	901	55.13	44.87
9	25	9	6	18	2008	9.88	170		1139	869	56.72	43.28
10	1	9	5	16	2008	9.88	171		1092	916	54.38	45.62
10	23	9	6	17	2008	9.88	172		1129	879	56.23	43.77
8	13	9	5	16	2007	9.87	173		1110	897	55.31	44.69

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
9	30	9	4	16	2006	9.87	174		1134	872	56.53	43.47
10	19	9	2	17	2006	9.87	175		1093	913	54.49	45.51
7	24	9	6	16	2005	9.86	176		1117	888	55.71	44.29
7	23	9	5	17	2004	9.86	177		1112	892	55.49	44.51
9	28	9	2	17	2004	9.86	178		1171	833	58.43	41.57
4	23	9	5	16	2003	9.85	179		1138	865	56.81	43.19
9	16	9	4	16	2003	9.85	180		1108	895	55.32	44.68
7	23	9	5	16	2001	9.84	181	20326	1076	925	53.77	46.23
8	24	9	2	16	2001	9.84	182		1100	901	54.97	45.03
11	20	9	6	16	2001	9.84	183		1110	891	55.47	44.53
6	18	9	5	16	2000	9.84	184		1114	886	55.7	44.3
8	17	9	2	17	1999	9.83	185		1127	872	56.38	43.62
4	24	9	6	18	1996	9.82	186		1146	850	57.41	42.59
5	29	9	6	17	1996	9.82	187		1126	870	56.41	43.59
5	7	9	5	17	1995	9.82	188		1126	869	56.44	43.56
7	27	9	2	17	1995	9.82	189		1155	840	57.89	42.11
10	5	9	2	17	1995	9.82	190		1084	911	54.34	45.66
11	17	9	3	17	1995	9.82	191		1192	803	59.75	40.25
4	17	9	6	16	1994	9.81	192		1134	860	56.87	43.13
7	1	9	4	16	1993	9.81	193		1126	867	56.5	43.5
9	10	9	5	16	1993	9.81	194		1150	843	57.7	42.3
11	24	9	3	17	1993	9.81	195		1170	823	58.71	41.29
5	28	9	5	16	1992	9.8	196		1147	845	57.58	42.42
10	6	9	3	17	1992	9.8	197		1091	901	54.77	45.23
4	30	9	5	16	1991	9.8	198		1076	915	54.04	45.96
12	23	9	4	16	1991	9.8	199		1067	924	53.59	46.41
8	5	9	4	18	1990	9.79	200		1176	814	59.1	40.9

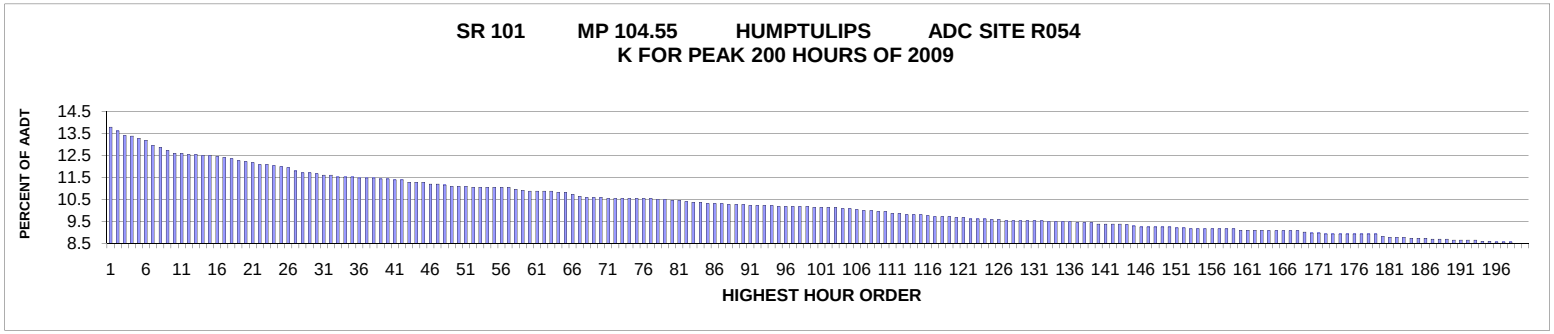

AADT= 2153 **K 30 FACTOR=** 11.66 **K 100 FACTOR=** 10.13 **K 200 FACTOR=** 8.5 **D FACTOR=** 54.66

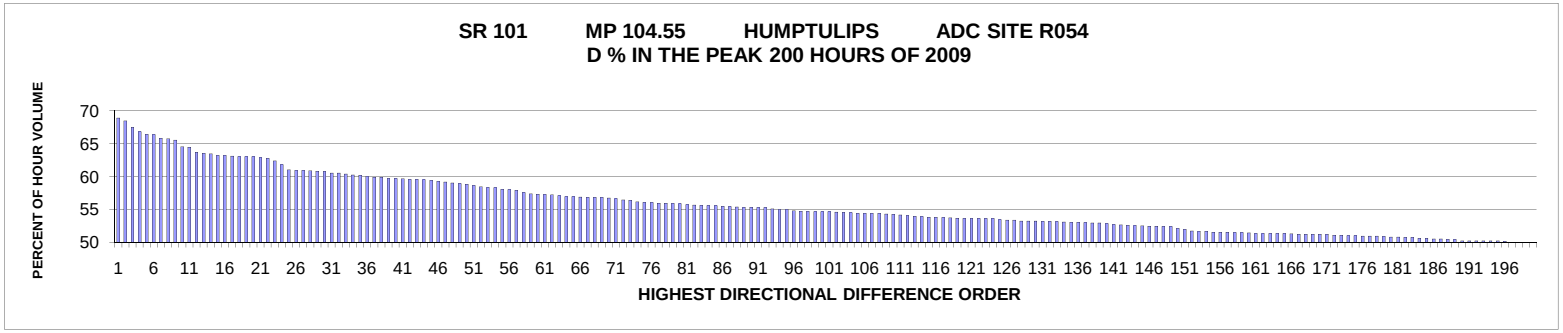

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	28	9	6	16	297	13.79	1	2153	148	149	49.83	50.17
8	16	9	1	14	293	13.61	2		116	177	39.59	60.41
8	23	9	1	14	289	13.42	3		114	175	39.45	60.55
8	14	9	6	17	288	13.38	4		139	149	48.26	51.74
8	23	9	1	16	286	13.28	5		96	190	33.57	66.43
8	28	9	6	14	284	13.19	6		142	142	50	50
8	23	9	1	17	279	12.96	7		105	174	37.63	62.37
8	30	9	1	14	277	12.87	8		112	165	40.43	59.57
8	23	9	1	15	274	12.73	9		101	173	36.86	63.14
8	9	9	1	14	271	12.59	10		110	161	40.59	59.41
8	23	9	1	13	271	12.59	11		117	154	43.17	56.83
8	1	9	7	15	270	12.54	12		142	128	52.59	47.41
8	2	9	1	13	270	12.54	13		125	145	46.3	53.7
8	1	9	7	12	269	12.49	14		171	98	63.57	36.43
8	14	9	6	16	269	12.49	15		141	128	52.42	47.58
8	21	9	6	17	268	12.45	16		108	160	40.3	59.7
8	2	9	1	14	267	12.4	17		123	144	46.07	53.93

8	19	9	4	14	266	12.35	18		137	129	51.5	48.5
8	9	9	1	13	264	12.26	19		105	159	39.77	60.23
8	19	9	4	17	263	12.22	20		114	149	43.35	56.65
8	21	9	6	18	262	12.17	21	2153	124	138	47.33	52.67
8	2	9	1	16	260	12.08	22		108	152	41.54	58.46
8	21	9	6	15	260	12.08	23		120	140	46.15	53.85
8	14	9	6	18	259	12.03	24		132	127	50.97	49.03
8	20	9	5	13	258	11.98	25		118	140	45.74	54.26
8	21	9	6	13	257	11.94	26		131	126	50.97	49.03
8	16	9	1	16	254	11.8	27		87	167	34.25	65.75
8	16	9	1	15	252	11.7	28		102	150	40.48	59.52
8	28	9	6	12	252	11.7	29		112	140	44.44	55.56
8	28	9	6	17	251	11.66	30		138	113	54.98	45.02
8	14	9	6	15	250	11.61	31		133	117	53.2	46.8
8	16	9	1	13	250	11.61	32		100	150	40	60
8	2	9	1	17	248	11.52	33		92	156	37.1	62.9
8	8	9	7	13	248	11.52	34		122	126	49.19	50.81
8	27	9	5	16	248	11.52	35		106	142	42.74	57.26
8	23	9	1	12	247	11.47	36		135	112	54.66	45.34
8	24	9	2	16	247	11.47	37		109	138	44.13	55.87
8	28	9	6	18	247	11.47	38		135	112	54.66	45.34
8	2	9	1	12	246	11.43	39		125	121	50.81	49.19
8	21	9	6	12	246	11.43	40		110	136	44.72	55.28
8	12	9	4	15	245	11.38	41	2153	115	130	46.94	53.06
8	28	9	6	15	245	11.38	42		121	124	49.39	50.61
8	1	9	7	17	243	11.29	43		133	110	54.73	45.27
8	5	9	4	12	243	11.29	44		119	124	48.97	51.03
8	27	9	5	17	243	11.29	45		102	141	41.98	58.02
8	9	9	1	15	241	11.19	46		99	142	41.08	58.92
8	25	9	3	16	241	11.19	47		83	158	34.44	65.56
8	27	9	5	15	240	11.15	48		117	123	48.75	51.25
8	2	9	1	15	239	11.1	49		106	133	44.35	55.65
8	14	9	6	14	239	11.1	50		129	110	53.97	46.03
8	20	9	5	16	239	11.1	51		118	121	49.37	50.63
8	16	9	1	12	238	11.05	52		108	130	45.38	54.62
8	16	9	1	17	238	11.05	53		74	164	31.09	68.91
8	19	9	4	15	238	11.05	54		128	110	53.78	46.22
8	19	9	4	18	238	11.05	55		88	150	36.97	63.03
8	21	9	6	16	238	11.05	56		113	125	47.48	52.52
8	26	9	4	17	238	11.05	57		93	145	39.08	60.92
8	20	9	5	17	236	10.96	58		92	144	38.98	61.02
8	1	9	7	16	235	10.92	59		103	132	43.83	56.17
8	1	9	7	13	234	10.87	60		124	110	52.99	47.01
8	5	9	4	14	234	10.87	61	2153	121	113	51.71	48.29
8	11	9	3	16	234	10.87	62		103	131	44.02	55.98
8	19	9	4	16	234	10.87	63		112	122	47.86	52.14
8	9	9	1	12	233	10.82	64		97	136	41.63	58.37
8	26	9	4	15	233	10.82	65		107	126	45.92	54.08
8	28	9	6	13	231	10.73	66		115	116	49.78	50.22
8	6	9	5	13	229	10.64	67		120	109	52.4	47.6
8	8	9	7	15	228	10.59	68		107	121	46.93	53.07
8	15	9	7	15	228	10.59	69		136	92	59.65	40.35
8	21	9	6	11	228	10.59	70		117	111	51.32	48.68
8	2	9	1	18	227	10.54	71		84	143	37	63
8	5	9	4	17	227	10.54	72		101	126	44.49	55.51
8	9	9	1	16	227	10.54	73		89	138	39.21	60.79
8	10	9	2	13	227	10.54	74		114	113	50.22	49.78

8	13	9	5	17	227	10.54	75		110	117	48.46	51.54
8	15	9	7	13	227	10.54	76		130	97	57.27	42.73
8	15	9	7	14	227	10.54	77		144	83	63.44	36.56
8	10	9	2	12	226	10.5	78		116	110	51.33	48.67
8	19	9	4	12	226	10.5	79		125	101	55.31	44.69
8	8	9	7	16	225	10.45	80		91	134	40.44	59.56
8	30	9	1	13	225	10.45	81	2153	88	137	39.11	60.89
8	20	9	5	18	224	10.4	82		95	129	42.41	57.59
8	1	9	7	14	223	10.36	83		141	82	63.23	36.77
8	24	9	2	17	223	10.36	84		96	127	43.05	56.95
8	15	9	7	16	222	10.31	85		104	118	46.85	53.15
8	18	9	3	17	222	10.31	86		110	112	49.55	50.45
8	30	9	1	16	222	10.31	87		89	133	40.09	59.91
8	6	9	5	17	221	10.26	88		93	128	42.08	57.92
8	14	9	6	12	221	10.26	89		117	104	52.94	47.06
8	17	9	2	15	221	10.26	90		108	113	48.87	51.13
8	5	9	4	16	220	10.22	91		97	123	44.09	55.91
8	13	9	5	16	220	10.22	92		107	113	48.64	51.36
8	17	9	2	13	220	10.22	93		122	98	55.45	44.55
8	24	9	2	18	220	10.22	94		102	118	46.36	53.64
8	6	9	5	12	219	10.17	95		94	125	42.92	57.08
8	17	9	2	17	219	10.17	96		102	117	46.58	53.42
8	21	9	6	19	219	10.17	97		122	97	55.71	44.29
8	24	9	2	14	219	10.17	98		103	116	47.03	52.97
8	27	9	5	18	219	10.17	99		109	110	49.77	50.23
8	6	9	5	16	218	10.13	100		93	125	42.66	57.34
8	14	9	6	13	218	10.13	101	2153	123	95	56.42	43.58
8	26	9	4	16	218	10.13	102		102	116	46.79	53.21
8	26	9	4	18	218	10.13	103		96	122	44.04	55.96
8	15	9	7	12	217	10.08	104		132	85	60.83	39.17
8	30	9	1	18	217	10.08	105		72	145	33.18	66.82
8	19	9	4	13	216	10.03	106		130	86	60.19	39.81
8	9	9	1	17	215	9.99	107		96	119	44.65	55.35
8	17	9	2	14	215	9.99	108		117	98	54.42	45.58
8	16	9	1	18	214	9.94	109		72	142	33.64	66.36
8	21	9	6	14	214	9.94	110		105	109	49.07	50.93
8	6	9	5	14	212	9.85	111		118	94	55.66	44.34
8	30	9	1	15	212	9.85	112		85	127	40.09	59.91
8	10	9	2	15	211	9.8	113		88	123	41.71	58.29
8	13	9	5	14	211	9.8	114		126	85	59.72	40.28
8	17	9	2	12	211	9.8	115		120	91	56.87	43.13
8	18	9	3	16	210	9.75	116		86	124	40.95	59.05
8	1	9	7	18	209	9.71	117		94	115	44.98	55.02
8	13	9	5	15	209	9.71	118		98	111	46.89	53.11
8	20	9	5	14	209	9.71	119		95	114	45.45	54.55
8	10	9	2	16	208	9.66	120		98	110	47.12	52.88
8	18	9	3	18	208	9.66	121	2153	103	105	49.52	50.48
8	25	9	3	13	207	9.61	122		96	111	46.38	53.62
8	29	9	7	12	207	9.61	123		104	103	50.24	49.76
8	30	9	1	12	207	9.61	124		77	130	37.2	62.8
8	18	9	3	14	206	9.57	125		110	96	53.4	46.6
8	30	9	1	17	206	9.57	126		67	139	32.52	67.48
1	8	9	5	17	205	9.52	127		102	103	49.76	50.24
8	5	9	4	15	205	9.52	128		86	119	41.95	58.05
8	11	9	3	13	205	9.52	129		103	102	50.24	49.76
8	20	9	5	15	205	9.52	130		99	106	48.29	51.71
8	31	9	2	15	205	9.52	131		94	111	45.85	54.15

8	31	9	2	18	205	9.52	132		95	110	46.34	53.66
8	6	9	5	18	204	9.48	133		105	99	51.47	48.53
8	8	9	7	14	204	9.48	134		104	100	50.98	49.02
8	31	9	2	16	204	9.48	135		93	111	45.59	54.41
11	6	9	6	16	204	9.48	136		97	107	47.55	52.45
8	18	9	3	13	203	9.43	137		92	111	45.32	54.68
8	28	9	6	19	203	9.43	138		131	72	64.53	35.47
11	13	9	6	17	203	9.43	139		96	107	47.29	52.71
8	10	9	2	14	202	9.38	140		87	115	43.07	56.93
8	11	9	3	17	202	9.38	141	2153	114	88	56.44	43.56
8	18	9	3	15	202	9.38	142		105	97	51.98	48.02
8	20	9	5	11	202	9.38	143		104	98	51.49	48.51
8	16	9	1	19	201	9.34	144		73	128	36.32	63.68
8	26	9	4	12	200	9.29	145		109	91	54.5	45.5
1	8	9	5	16	199	9.24	146		102	97	51.26	48.74
8	2	9	1	19	199	9.24	147		68	131	34.17	65.83
8	12	9	4	17	199	9.24	148		98	101	49.25	50.75
8	13	9	5	13	199	9.24	149		106	93	53.27	46.73
12	3	9	5	16	199	9.24	150		81	118	40.7	59.3
1	8	9	5	18	198	9.2	151		88	110	44.44	55.56
8	20	9	5	12	198	9.2	152		101	97	51.01	48.99
8	1	9	7	19	197	9.15	153		70	127	35.53	64.47
8	5	9	4	18	197	9.15	154		101	96	51.27	48.73
8	8	9	7	12	197	9.15	155		89	108	45.18	54.82
8	17	9	2	16	197	9.15	156		85	112	43.15	56.85
8	19	9	4	19	197	9.15	157		77	120	39.09	60.91
8	27	9	5	14	197	9.15	158		109	88	55.33	44.67
8	28	9	6	11	197	9.15	159		84	113	42.64	57.36
8	14	9	6	19	196	9.1	160		108	88	55.1	44.9
8	15	9	7	17	196	9.1	161	2153	81	115	41.33	58.67
8	24	9	2	19	196	9.1	162		99	97	50.51	49.49
8	27	9	5	13	196	9.1	163		116	80	59.18	40.82
1	8	9	5	15	195	9.06	164		108	87	55.38	44.62
8	31	9	2	13	195	9.06	165		96	99	49.23	50.77
8	31	9	2	17	195	9.06	166		95	100	48.72	51.28
11	4	9	4	16	195	9.06	167		90	105	46.15	53.85
11	25	9	4	15	195	9.06	168		100	95	51.28	48.72
1	23	9	6	17	194	9.01	169		94	100	48.45	51.55
8	10	9	2	17	193	8.96	170		105	88	54.4	45.6
8	19	9	4	11	193	8.96	171		105	88	54.4	45.6
8	2	9	1	11	192	8.92	172		83	109	43.23	56.77
8	8	9	7	17	192	8.92	173		79	113	41.15	58.85
8	12	9	4	16	192	8.92	174		89	103	46.35	53.65
8	15	9	7	18	192	8.92	175		71	121	36.98	63.02
8	24	9	2	13	192	8.92	176		96	96	50	50
8	26	9	4	14	192	8.92	177		93	99	48.44	51.56
12	4	9	6	17	192	8.92	178		91	101	47.4	52.6
12	28	9	2	17	192	8.92	179		89	103	46.35	53.65
8	5	9	4	11	190	8.82	180		104	86	54.74	45.26
8	17	9	2	11	189	8.78	181	2153	88	101	46.56	53.44
8	25	9	3	17	189	8.78	182		83	106	43.92	56.08
12	3	9	5	17	189	8.78	183		83	106	43.92	56.08
8	9	9	1	11	188	8.73	184		94	94	50	50
8	10	9	2	11	188	8.73	185		93	95	49.47	50.53
8	12	9	4	12	188	8.73	186		107	81	56.91	43.09
8	6	9	5	11	187	8.69	187		96	91	51.34	48.66
8	23	9	1	18	187	8.69	188		59	128	31.55	68.45

8	25	9	3	18	187	8.69	189	96	91	51.34	48.66
8	12	9	4	13	186	8.64	190	85	101	45.7	54.3
8	25	9	3	14	186	8.64	191	86	100	46.24	53.76
11	3	9	3	16	186	8.64	192	71	115	38.17	61.83
12	26	9	7	13	186	8.64	193	93	93	50	50
8	24	9	2	15	185	8.59	194	112	73	60.54	39.46
12	4	9	6	16	185	8.59	195	68	117	36.76	63.24
8	6	9	5	15	184	8.55	196	86	98	46.74	53.26
8	24	9	2	12	184	8.55	197	90	94	48.91	51.09
12	2	9	4	16	184	8.55	198	86	98	46.74	53.26
8	8	9	7	11	183	8.5	199	96	87	52.46	47.54
8	11	9	3	15	183	8.5	200	94	89	51.37	48.63

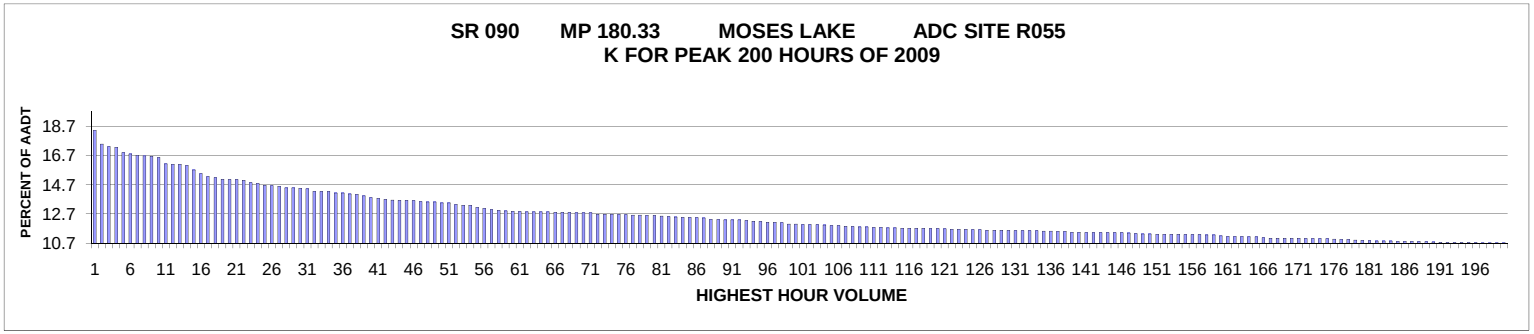

AADT= 10714 **K 30 FACTOR=** 14.46 **K 100 FACTOR=** 12 **K 200 FACTOR=** 10.71 **D FACTOR=** 53.27

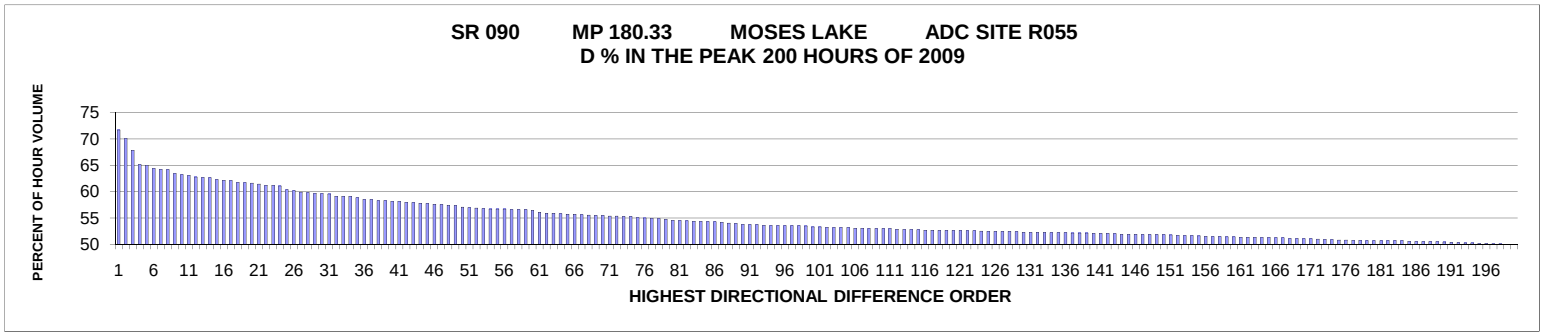

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	7	9	6	15	1973	18.42	1	10714	791	1182	40.09	59.91
6	26	9	6	15	1873	17.48	2		1175	698	62.73	37.27
8	16	9	1	15	1853	17.3	3		860	993	46.41	53.59
8	9	9	1	15	1850	17.27	4		887	963	47.95	52.05
6	26	9	6	16	1810	16.89	5		1179	631	65.14	34.86
8	9	9	1	14	1800	16.8	6		809	991	44.94	55.06
6	28	9	1	15	1791	16.72	7		725	1066	40.48	59.52
6	28	9	1	17	1785	16.66	8		636	1149	35.63	64.37
6	28	9	1	16	1784	16.65	9		676	1108	37.89	62.11
8	16	9	1	16	1774	16.56	10		845	929	47.63	52.37
8	9	9	1	16	1727	16.12	11		819	908	47.42	52.58
6	28	9	1	18	1725	16.1	12		554	1171	32.12	67.88
8	16	9	1	14	1725	16.1	13		787	938	45.62	54.38
8	16	9	1	17	1716	16.02	14		820	896	47.79	52.21
8	9	9	1	13	1682	15.7	15		759	923	45.12	54.88
6	26	9	6	14	1655	15.45	16		987	668	59.64	40.36
6	26	9	6	17	1634	15.25	17		1023	611	62.61	37.39

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	2	9	1	16	1626	15.18	18		706	920	43.42	56.58
5	22	9	6	16	1616	15.08	19		842	774	52.1	47.9
8	2	9	1	15	1614	15.06	20		703	911	43.56	56.44
8	9	9	1	17	1612	15.05	21	10714	767	845	47.58	52.42
6	28	9	1	14	1608	15.01	22		667	941	41.48	58.52
8	14	9	6	14	1590	14.84	23		847	743	53.27	46.73
8	14	9	6	15	1585	14.79	24		805	780	50.79	49.21
5	22	9	6	17	1570	14.65	25		766	804	48.79	51.21
8	16	9	1	13	1569	14.64	26		689	880	43.91	56.09
8	2	9	1	14	1562	14.58	27		648	914	41.49	58.51
8	7	9	6	16	1552	14.49	28		802	750	51.68	48.32
5	25	9	2	16	1551	14.48	29		736	815	47.45	52.55
5	22	9	6	14	1549	14.46	30		866	683	55.91	44.09
8	16	9	1	18	1545	14.42	31		760	785	49.19	50.81
8	14	9	6	16	1527	14.25	32		809	718	52.98	47.02
6	14	9	1	15	1526	14.24	33		676	850	44.3	55.7
8	9	9	1	12	1526	14.24	34		721	805	47.25	52.75
6	28	9	1	19	1515	14.14	35		453	1062	29.9	70.1
5	22	9	6	15	1514	14.13	36		810	704	53.5	46.5
5	3	9	1	17	1506	14.06	37		539	967	35.79	64.21
6	28	9	1	13	1505	14.05	38		581	924	38.6	61.4
8	14	9	6	13	1493	13.94	39		695	798	46.55	53.45
8	7	9	6	13	1479	13.8	40		692	787	46.79	53.21
8	15	9	7	12	1477	13.79	41	10714	687	790	46.51	53.49
6	14	9	1	16	1468	13.7	42		736	732	50.14	49.86
8	2	9	1	13	1462	13.65	43		612	850	41.86	58.14
6	26	9	6	13	1459	13.62	44		767	692	52.57	47.43
8	14	9	6	17	1459	13.62	45		716	743	49.07	50.93
5	25	9	2	14	1457	13.6	46		657	800	45.09	54.91
6	21	9	1	16	1450	13.53	47		710	740	48.97	51.03
8	7	9	6	17	1449	13.52	48		728	721	50.24	49.76
6	12	9	6	15	1447	13.51	49		839	608	57.98	42.02
5	3	9	1	16	1442	13.46	50		505	937	35.02	64.98
6	21	9	1	15	1442	13.46	51		668	774	46.32	53.68
8	2	9	1	17	1430	13.35	52		599	831	41.89	58.11
5	25	9	2	15	1425	13.3	53		670	755	47.02	52.98
8	14	9	6	12	1425	13.3	54		602	823	42.25	57.75
4	19	9	1	20	1408	13.14	55		399	1009	28.34	71.66
8	9	9	1	18	1401	13.08	56		607	794	43.33	56.67
6	12	9	6	14	1392	12.99	57		724	668	52.01	47.99
6	14	9	1	14	1389	12.96	58		625	764	45	55
8	7	9	6	12	1382	12.9	59		577	805	41.75	58.25
3	29	9	1	15	1380	12.88	60		673	707	48.77	51.23
6	26	9	6	18	1379	12.87	61	10714	871	508	63.16	36.84
5	10	9	1	17	1377	12.85	62		549	828	39.87	60.13
5	25	9	2	18	1377	12.85	63		666	711	48.37	51.63
12	27	9	1	14	1377	12.85	64		554	823	40.23	59.77
12	27	9	1	15	1376	12.84	65		636	740	46.22	53.78
6	21	9	1	14	1373	12.82	66		651	722	47.41	52.59
8	16	9	1	12	1373	12.82	67		662	711	48.22	51.78
5	25	9	2	17	1371	12.8	68		647	724	47.19	52.81
3	29	9	1	16	1369	12.78	69		667	702	48.72	51.28

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	7	9	6	18	1368	12.77	70		702	666	51.32	48.68
8	14	9	6	18	1368	12.77	71		684	684	50	50
5	22	9	6	18	1360	12.69	72		507	853	37.28	62.72
4	5	9	1	17	1359	12.68	73		681	678	50.11	49.89
5	8	9	6	15	1358	12.68	74		722	636	53.17	46.83
8	8	9	7	13	1356	12.66	75		638	718	47.05	52.95
8	2	9	1	18	1354	12.64	76		554	800	40.92	59.08
6	19	9	6	17	1352	12.62	77		714	638	52.81	47.19
6	21	9	1	17	1352	12.62	78		640	712	47.34	52.66
4	5	9	1	16	1350	12.6	79		669	681	49.56	50.44
6	14	9	1	17	1349	12.59	80		636	713	47.15	52.85
6	12	9	6	17	1345	12.55	81	10714	736	609	54.72	45.28
6	12	9	6	16	1341	12.52	82		776	565	57.87	42.13
4	5	9	1	15	1339	12.5	83		698	641	52.13	47.87
5	17	9	1	16	1335	12.46	84		643	692	48.16	51.84
8	15	9	7	11	1335	12.46	85		596	739	44.64	55.36
6	7	9	1	16	1333	12.44	86		613	720	45.99	54.01
6	19	9	6	16	1332	12.43	87		713	619	53.53	46.47
5	25	9	2	13	1322	12.34	88		561	761	42.44	57.56
5	3	9	1	15	1320	12.32	89		488	832	36.97	63.03
5	15	9	6	15	1318	12.3	90		658	660	49.92	50.08
6	19	9	6	15	1318	12.3	91		705	613	53.49	46.51
6	14	9	1	13	1317	12.29	92		504	813	38.27	61.73
12	27	9	1	13	1312	12.25	93		530	782	40.4	59.6
6	19	9	6	18	1308	12.21	94		742	566	56.73	43.27
8	2	9	1	12	1306	12.19	95		555	751	42.5	57.5
6	26	9	6	12	1302	12.15	96		630	672	48.39	51.61
5	3	9	1	18	1301	12.14	97		466	835	35.82	64.18
6	19	9	6	13	1295	12.09	98		656	639	50.66	49.34
5	17	9	1	15	1288	12.02	99		617	671	47.9	52.1
6	19	9	6	14	1286	12	100		685	601	53.27	46.73
8	14	9	6	11	1282	11.97	101	10714	547	735	42.67	57.33
5	22	9	6	19	1281	11.96	102		524	757	40.91	59.09
8	10	9	2	15	1281	11.96	103		668	613	52.15	47.85
5	15	9	6	17	1280	11.95	104		622	658	48.59	51.41
8	15	9	7	13	1276	11.91	105		639	637	50.08	49.92
8	16	9	1	19	1275	11.9	106		621	654	48.71	51.29
3	29	9	1	14	1270	11.85	107		523	747	41.18	58.82
8	7	9	6	14	1269	11.84	108		775	494	61.07	38.93
5	10	9	1	18	1265	11.81	109		491	774	38.81	61.19
5	17	9	1	14	1265	11.81	110		615	650	48.62	51.38
3	29	9	1	17	1264	11.8	111		626	638	49.53	50.47
5	10	9	1	16	1263	11.79	112		484	779	38.32	61.68
5	22	9	6	13	1259	11.75	113		655	604	52.03	47.97
6	21	9	1	13	1258	11.74	114		596	662	47.38	52.62
4	5	9	1	14	1257	11.73	115		598	659	47.57	52.43
8	1	9	7	13	1257	11.73	116		620	637	49.32	50.68
8	1	9	7	14	1257	11.73	117		651	606	51.79	48.21
5	17	9	1	17	1256	11.72	118		608	648	48.41	51.59
8	1	9	7	12	1254	11.7	119		673	581	53.67	46.33
8	15	9	7	15	1254	11.7	120		639	615	50.96	49.04
8	8	9	7	15	1251	11.68	121	10714	615	636	49.16	50.84

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
4	12	9	1	18	1248	11.65	122		618	630	49.52	50.48
6	12	9	6	18	1248	11.65	123		647	601	51.84	48.16
6	14	9	1	18	1248	11.65	124		593	655	47.52	52.48
6	28	9	1	12	1245	11.62	125		556	689	44.66	55.34
8	6	9	5	15	1245	11.62	126		631	614	50.68	49.32
6	7	9	1	15	1242	11.59	127		535	707	43.08	56.92
6	26	9	6	19	1242	11.59	128		772	470	62.16	37.84
8	8	9	7	14	1242	11.59	129		651	591	52.42	47.58
12	27	9	1	16	1240	11.57	130		597	643	48.15	51.85
5	8	9	6	16	1239	11.56	131		702	537	56.66	43.34
5	15	9	6	16	1238	11.55	132		646	592	52.18	47.82
8	8	9	7	12	1238	11.55	133		586	652	47.33	52.67
6	7	9	1	17	1236	11.54	134		565	671	45.71	54.29
6	7	9	1	14	1235	11.53	135		562	673	45.51	54.49
8	1	9	7	11	1234	11.52	136		666	568	53.97	46.03
3	27	9	6	17	1232	11.5	137		643	589	52.19	47.81
6	12	9	6	13	1232	11.5	138		612	620	49.68	50.32
4	19	9	1	17	1226	11.44	139		619	607	50.49	49.51
6	21	9	1	18	1226	11.44	140		609	617	49.67	50.33
8	8	9	7	11	1224	11.42	141	10714	582	642	47.55	52.45
4	17	9	6	16	1223	11.41	142		692	531	56.58	43.42
5	8	9	6	17	1223	11.41	143		650	573	53.15	46.85
3	22	9	1	17	1222	11.41	144		584	638	47.79	52.21
8	6	9	5	18	1222	11.41	145		697	525	57.04	42.96
8	15	9	7	14	1222	11.41	146		627	595	51.31	48.69
6	5	9	6	16	1221	11.4	147		675	546	55.28	44.72
8	9	9	1	11	1216	11.35	148		592	624	48.68	51.32
4	17	9	6	15	1215	11.34	149		674	541	55.47	44.53
5	15	9	6	18	1214	11.33	150		552	662	45.47	54.53
3	27	9	6	16	1213	11.32	151		598	615	49.3	50.7
5	10	9	1	15	1213	11.32	152		458	755	37.76	62.24
4	19	9	1	16	1212	11.31	153		600	612	49.5	50.5
5	17	9	1	18	1211	11.3	154		587	624	48.47	51.53
5	22	9	6	12	1210	11.29	155		578	632	47.77	52.23
8	7	9	6	11	1210	11.29	156		512	698	42.31	57.69
8	13	9	5	16	1210	11.29	157		597	613	49.34	50.66
2	16	9	2	16	1208	11.27	158		626	582	51.82	48.18
6	12	9	6	12	1207	11.27	159		540	667	44.74	55.26
3	22	9	1	16	1199	11.19	160		533	666	44.45	55.55
5	8	9	6	18	1195	11.15	161	10714	634	561	53.05	46.95
5	25	9	2	12	1195	11.15	162		459	736	38.41	61.59
8	3	9	2	14	1195	11.15	163		635	560	53.14	46.86
6	5	9	6	15	1194	11.14	164		639	555	53.52	46.48
8	13	9	5	15	1192	11.13	165		618	574	51.85	48.15
8	16	9	1	11	1186	11.07	166		585	601	49.33	50.67
4	3	9	6	18	1184	11.05	167		751	433	63.43	36.57
4	24	9	6	16	1184	11.05	168		671	513	56.67	43.33
8	13	9	5	14	1184	11.05	169		584	600	49.32	50.68
4	19	9	1	15	1183	11.04	170		522	661	44.13	55.87
8	13	9	5	17	1183	11.04	171		604	579	51.06	48.94
5	17	9	1	13	1182	11.03	172		604	578	51.1	48.9
5	23	9	7	12	1181	11.02	173		560	621	47.42	52.58

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
6	14	9	1	12	1180	11.01	174		458	722	38.81	61.19
5	23	9	7	11	1179	11	175		583	596	49.45	50.55
8	17	9	2	13	1178	10.99	176		565	613	47.96	52.04
5	8	9	6	14	1174	10.96	177		638	536	54.34	45.66
8	10	9	2	13	1174	10.96	178		520	654	44.29	55.71
8	3	9	2	15	1170	10.92	179		620	550	52.99	47.01
6	7	9	1	18	1168	10.9	180		478	690	40.92	59.08
3	27	9	6	15	1166	10.88	181	10714	583	583	50	50
4	26	9	1	16	1164	10.86	182		565	599	48.54	51.46
4	12	9	1	17	1162	10.85	183		559	603	48.11	51.89
4	17	9	6	17	1162	10.85	184		667	495	57.4	42.6
6	5	9	6	14	1160	10.83	185		615	545	53.02	46.98
4	3	9	6	16	1159	10.82	186		699	460	60.31	39.69
8	9	9	1	19	1159	10.82	187		563	596	48.58	51.42
4	5	9	1	13	1158	10.81	188		503	655	43.44	56.56
5	25	9	2	19	1157	10.8	189		576	581	49.78	50.22
5	1	9	6	17	1155	10.78	190		644	511	55.76	44.24
4	24	9	6	17	1154	10.77	191		640	514	55.46	44.54
6	5	9	6	13	1151	10.74	192		550	601	47.78	52.22
2	13	9	6	17	1150	10.73	193		624	526	54.26	45.74
8	2	9	1	19	1150	10.73	194		527	623	45.83	54.17
8	6	9	5	14	1150	10.73	195		567	583	49.3	50.7
8	17	9	2	16	1150	10.73	196		563	587	48.96	51.04
6	19	9	6	12	1149	10.72	197		524	625	45.6	54.4
6	21	9	1	12	1148	10.71	198		510	638	44.43	55.57
5	1	9	6	16	1147	10.71	199		668	479	58.24	41.76
8	13	9	5	12	1147	10.71	200		495	652	43.16	56.84

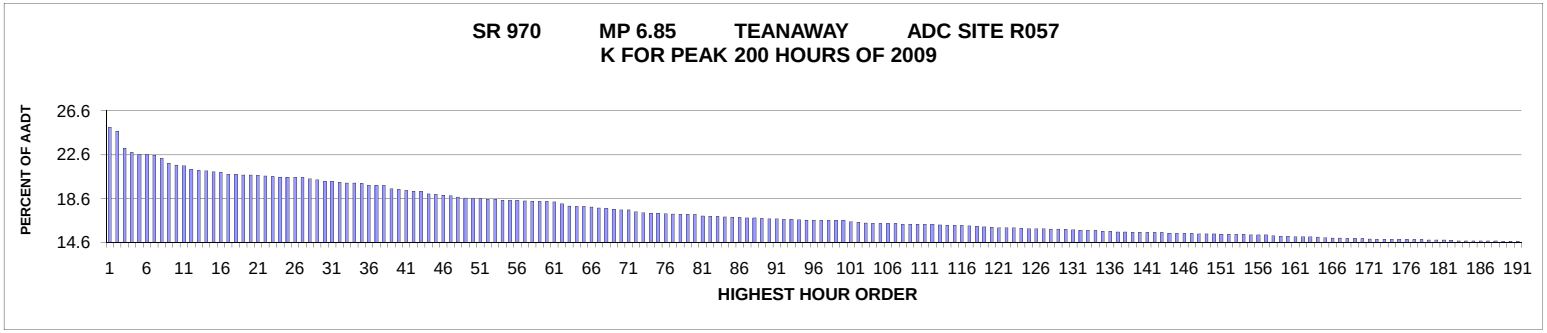

AADT= 4123 **K 30 FACTOR=** 20.16 **K 100 FACTOR=** 16.74 **K 200 FACTOR=** 14.7 **D FACTOR=** 67.97

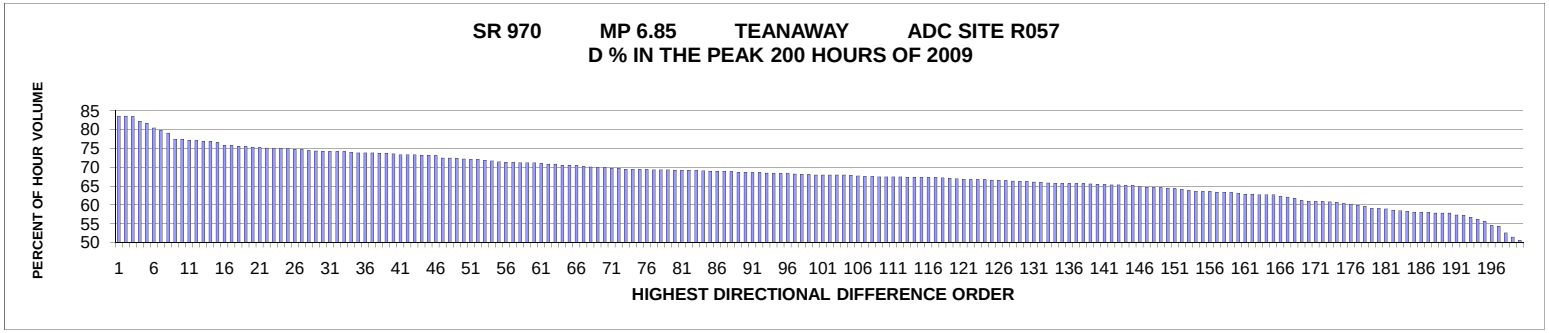

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
5	25	9	2	13	1035	25.1	1	4123	170	865	16.43	83.57
5	25	9	2	12	1020	24.74	2		167	853	16.37	83.63
5	25	9	2	14	956	23.19	3		170	786	17.78	82.22
8	9	9	1	15	940	22.8	4		299	641	31.81	68.19
8	9	9	1	13	933	22.63	5		320	613	34.3	65.7
8	30	9	1	17	933	22.63	6		391	542	41.91	58.09
6	28	9	1	15	930	22.56	7		236	694	25.38	74.62
8	9	9	1	14	918	22.27	8		294	624	32.03	67.97
8	30	9	1	16	900	21.83	9		369	531	41	59
8	16	9	1	16	893	21.66	10		273	620	30.57	69.43
8	9	9	1	18	891	21.61	11		274	617	30.75	69.25
8	23	9	1	14	876	21.25	12		269	607	30.71	69.29
8	9	9	1	16	873	21.17	13		286	587	32.76	67.24
6	28	9	1	16	871	21.13	14		217	654	24.91	75.09
8	16	9	1	14	868	21.05	15		291	577	33.53	66.47
8	9	9	1	17	865	20.98	16		251	614	29.02	70.98
8	2	9	1	13	858	20.81	17		289	569	33.68	66.32

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	23	9	1	16	858	20.81	18		217	641	25.29	74.71
6	28	9	1	17	855	20.74	19		193	662	22.57	77.43
9	7	9	2	14	855	20.74	20		198	657	23.16	76.84
9	7	9	2	13	854	20.71	21	4123	195	659	22.83	77.17
8	23	9	1	15	852	20.66	22		258	594	30.28	69.72
7	19	9	1	15	849	20.59	23		277	572	32.63	67.37
7	19	9	1	13	847	20.54	24		287	560	33.88	66.12
8	16	9	1	17	847	20.54	25		293	554	34.59	65.41
8	23	9	1	17	847	20.54	26		261	586	30.81	69.19
7	19	9	1	14	846	20.52	27		282	564	33.33	66.67
8	16	9	1	15	841	20.4	28		299	542	35.55	64.45
8	23	9	1	13	837	20.3	29		292	545	34.89	65.11
7	12	9	1	14	831	20.16	30		249	582	29.96	70.04
8	30	9	1	15	831	20.16	31		271	560	32.61	67.39
5	25	9	2	11	828	20.08	32		137	691	16.55	83.45
5	22	9	6	15	825	20.01	33		658	167	79.76	20.24
7	12	9	1	13	825	20.01	34		241	584	29.21	70.79
6	21	9	1	14	824	19.99	35		222	602	26.94	73.06
8	16	9	1	13	817	19.82	36		305	512	37.33	62.67
6	21	9	1	15	816	19.79	37		211	605	25.86	74.14
7	19	9	1	17	816	19.79	38		270	546	33.09	66.91
6	21	9	1	16	804	19.5	39		186	618	23.13	76.87
7	12	9	1	15	802	19.45	40		280	522	34.91	65.09
7	3	9	6	16	796	19.31	41	4123	568	228	71.36	28.64
6	21	9	1	17	794	19.26	42		210	584	26.45	73.55
7	3	9	6	14	794	19.26	43		589	205	74.18	25.82
5	25	9	2	15	785	19.04	44		144	641	18.34	81.66
7	19	9	1	16	782	18.97	45		200	582	25.58	74.42
6	21	9	1	13	780	18.92	46		251	529	32.18	67.82
8	30	9	1	14	777	18.85	47		214	563	27.54	72.46
8	8	9	7	13	773	18.75	48		465	308	60.16	39.84
7	26	9	1	15	769	18.65	49		273	496	35.5	64.5
7	26	9	1	17	767	18.6	50		246	521	32.07	67.93
9	7	9	2	12	766	18.58	51		180	586	23.5	76.5
7	3	9	6	15	764	18.53	52		574	190	75.13	24.87
8	30	9	1	18	764	18.53	53		331	433	43.32	56.68
7	12	9	1	16	761	18.46	54		244	517	32.06	67.94
5	23	9	7	14	759	18.41	55		564	195	74.31	25.69
8	16	9	1	18	759	18.41	56		238	521	31.36	68.64
6	28	9	1	13	758	18.38	57		276	482	36.41	63.59
8	23	9	1	18	757	18.36	58		235	522	31.04	68.96
7	26	9	1	13	756	18.34	59		267	489	35.32	64.68
7	26	9	1	14	756	18.34	60		244	512	32.28	67.72
6	14	9	1	16	755	18.31	61	4123	182	573	24.11	75.89
8	7	9	6	15	747	18.12	62		482	265	64.52	35.48
5	23	9	7	11	739	17.92	63		526	213	71.18	28.82
8	2	9	1	14	736	17.85	64		247	489	33.56	66.44
8	9	9	1	12	736	17.85	65		278	458	37.77	62.23
8	30	9	1	13	735	17.83	66		210	525	28.57	71.43
8	23	9	1	12	732	17.75	67		273	459	37.3	62.7
9	4	9	6	18	729	17.68	68		504	225	69.14	30.86
8	2	9	1	16	727	17.63	69		252	475	34.66	65.34

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	12	9	1	12	724	17.56	70		231	493	31.91	68.09
8	14	9	6	15	724	17.56	71		415	309	57.32	42.68
6	7	9	1	15	718	17.41	72		180	538	25.07	74.93
8	8	9	7	14	714	17.32	73		401	313	56.16	43.84
7	19	9	1	18	712	17.27	74		224	488	31.46	68.54
5	23	9	7	12	711	17.24	75		525	186	73.84	26.16
5	23	9	7	13	710	17.22	76		506	204	71.27	28.73
6	28	9	1	18	709	17.2	77		160	549	22.57	77.43
6	7	9	1	16	707	17.15	78		186	521	26.31	73.69
8	7	9	6	18	707	17.15	79		467	240	66.05	33.95
7	17	9	6	15	706	17.12	80		483	223	68.41	31.59
8	9	9	1	19	702	17.03	81	4123	228	474	32.48	67.52
9	7	9	2	15	700	16.98	82		175	525	25	75
7	12	9	1	18	699	16.95	83		195	504	27.9	72.1
7	26	9	1	16	698	16.93	84		223	475	31.95	68.05
6	19	9	6	17	697	16.91	85		496	201	71.16	28.84
8	7	9	6	16	695	16.86	86		455	240	65.47	34.53
6	19	9	6	16	694	16.83	87		501	193	72.19	27.81
7	19	9	1	12	694	16.83	88		258	436	37.18	62.82
5	22	9	6	16	692	16.78	89		533	159	77.02	22.98
6	14	9	1	17	690	16.74	90		181	509	26.23	73.77
8	7	9	6	14	690	16.74	91		422	268	61.16	38.84
8	14	9	6	17	689	16.71	92		436	253	63.28	36.72
8	14	9	6	16	688	16.69	93		424	264	61.63	38.37
8	7	9	6	17	687	16.66	94		459	228	66.81	33.19
5	17	9	1	15	686	16.64	95		184	502	26.82	73.18
5	25	9	2	17	686	16.64	96		168	518	24.49	75.51
5	22	9	6	14	685	16.61	97		507	178	74.01	25.99
6	26	9	6	15	685	16.61	98		451	234	65.84	34.16
7	12	9	1	17	685	16.61	99		180	505	26.28	73.72
7	26	9	1	18	685	16.61	100		202	483	29.49	70.51
8	16	9	1	19	680	16.49	101	4123	233	447	34.26	65.74
8	2	9	1	15	678	16.44	102		272	406	40.12	59.88
8	21	9	6	16	675	16.37	103		447	228	66.22	33.78
6	19	9	6	18	674	16.35	104		494	180	73.29	26.71
6	14	9	1	13	673	16.32	105		232	441	34.47	65.53
8	14	9	6	14	673	16.32	106		394	279	58.54	41.46
10	11	9	1	17	673	16.32	107		141	532	20.95	79.05
8	16	9	1	12	671	16.27	108		245	426	36.51	63.49
9	4	9	6	19	671	16.27	109		492	179	73.32	26.68
9	5	9	7	13	671	16.27	110		465	206	69.3	30.7
5	17	9	1	16	670	16.25	111		210	460	31.34	68.66
7	3	9	6	13	670	16.25	112		458	212	68.36	31.64
8	8	9	7	12	668	16.2	113		423	245	63.32	36.68
7	18	9	7	13	667	16.18	114		406	261	60.87	39.13
8	21	9	6	13	667	16.18	115		389	278	58.32	41.68
8	7	9	6	19	665	16.13	116		481	184	72.33	27.67
7	26	9	1	12	664	16.1	117		280	384	42.17	57.83
7	17	9	6	16	662	16.06	118		458	204	69.18	30.82
6	26	9	6	16	661	16.03	119		446	215	67.47	32.53
9	5	9	7	12	660	16.01	120		433	227	65.61	34.39
6	7	9	1	17	657	15.93	121	4123	159	498	24.2	75.8

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
6	28	9	1	12	657	15.93	122		241	416	36.68	63.32
7	25	9	7	13	657	15.93	123		357	300	54.34	45.66
6	21	9	1	18	655	15.89	124		201	454	30.69	69.31
6	14	9	1	15	653	15.84	125		200	453	30.63	69.37
6	21	9	1	12	653	15.84	126		214	439	32.77	67.23
9	4	9	6	15	653	15.84	127		478	175	73.2	26.8
5	24	9	1	13	652	15.81	128		322	330	49.39	50.61
8	23	9	1	19	652	15.81	129		226	426	34.66	65.34
9	4	9	6	17	651	15.79	130		449	202	68.97	31.03
8	21	9	6	15	650	15.77	131		433	217	66.62	33.38
7	17	9	6	14	647	15.69	132		415	232	64.14	35.86
9	7	9	2	16	647	15.69	133		162	485	25.04	74.96
7	31	9	6	15	646	15.67	134		375	271	58.05	41.95
7	10	9	6	15	644	15.62	135		391	253	60.71	39.29
8	7	9	6	13	644	15.62	136		358	286	55.59	44.41
8	14	9	6	18	642	15.57	137		408	234	63.55	36.45
6	14	9	1	14	641	15.55	138		193	448	30.11	69.89
8	14	9	6	13	640	15.52	139		349	291	54.53	45.47
10	11	9	1	13	640	15.52	140		214	426	33.44	66.56
7	3	9	6	11	639	15.5	141	4123	463	176	72.46	27.54
8	2	9	1	12	639	15.5	142		258	381	40.38	59.62
8	2	9	1	17	639	15.5	143		208	431	32.55	67.45
12	26	9	7	14	637	15.45	144		387	250	60.75	39.25
8	21	9	6	17	635	15.4	145		438	197	68.98	31.02
9	6	9	1	16	635	15.4	146		198	437	31.18	68.82
10	18	9	1	13	635	15.4	147		194	441	30.55	69.45
5	23	9	7	15	634	15.38	148		449	185	70.82	29.18
6	26	9	6	12	634	15.38	149		416	218	65.62	34.38
12	27	9	1	15	634	15.38	150		308	326	48.58	51.42
5	25	9	2	16	633	15.35	151		124	509	19.59	80.41
8	21	9	6	19	633	15.35	152		454	179	71.72	28.28
5	17	9	1	14	632	15.33	153		182	450	28.8	71.2
7	24	9	6	16	632	15.33	154		426	206	67.41	32.59
6	28	9	1	14	631	15.3	155		270	361	42.79	57.21
7	2	9	5	16	631	15.3	156		441	190	69.89	30.11
10	11	9	1	14	631	15.3	157		193	438	30.59	69.41
9	4	9	6	16	627	15.21	158		463	164	73.84	26.16
10	11	9	1	15	626	15.18	159		176	450	28.12	71.88
10	16	9	6	17	626	15.18	160		459	167	73.32	26.68
5	22	9	6	18	624	15.13	161	4123	450	174	72.12	27.88
7	10	9	6	13	623	15.11	162		360	263	57.78	42.22
12	26	9	7	13	623	15.11	163		367	256	58.91	41.09
5	23	9	7	10	622	15.09	164		438	184	70.42	29.58
8	9	9	1	20	620	15.04	165		199	421	32.1	67.9
7	17	9	6	18	619	15.01	166		423	196	68.34	31.66
9	5	9	7	14	619	15.01	167		398	221	64.3	35.7
8	28	9	6	17	617	14.96	168		400	217	64.83	35.17
9	13	9	1	14	617	14.96	169		194	423	31.44	68.56
10	18	9	1	15	617	14.96	170		182	435	29.5	70.5
6	19	9	6	19	615	14.92	171		429	186	69.76	30.24
6	26	9	6	18	614	14.89	172		424	190	69.06	30.94
7	2	9	5	19	614	14.89	173		417	197	67.92	32.08

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	15	9	7	13	614	14.89	174		356	258	57.98	42.02
9	6	9	1	15	614	14.89	175		233	381	37.95	62.05
5	25	9	2	18	613	14.87	176		150	463	24.47	75.53
9	13	9	1	15	613	14.87	177		200	413	32.63	67.37
9	13	9	1	18	613	14.87	178		202	411	32.95	67.05
8	21	9	6	14	612	14.84	179		373	239	60.95	39.05
8	28	9	6	18	612	14.84	180		413	199	67.48	32.52
7	10	9	6	14	611	14.82	181	4123	372	239	60.88	39.12
7	17	9	6	17	610	14.8	182		410	200	67.21	32.79
6	26	9	6	14	608	14.75	183		382	226	62.83	37.17
6	27	9	7	12	608	14.75	184		383	225	62.99	37.01

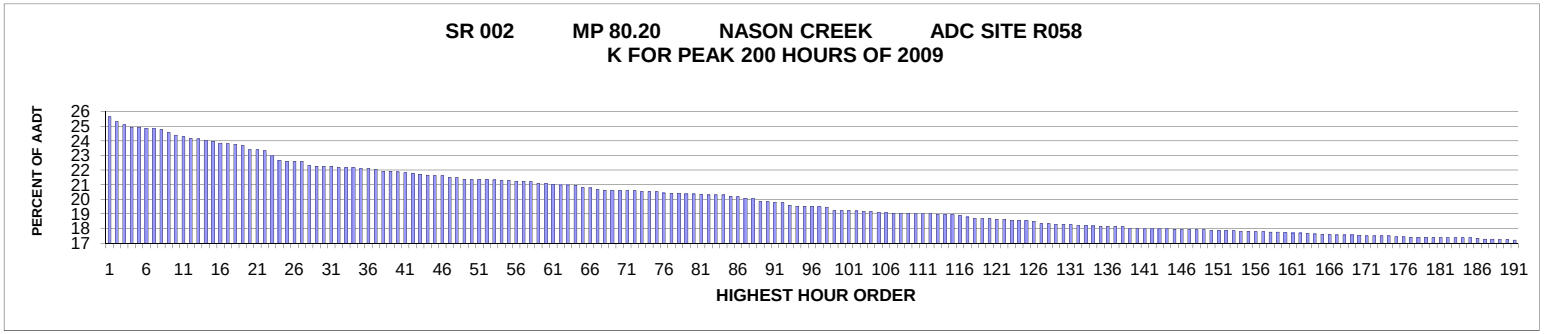

AADT= 4037 K 30 FACTOR= 22.27 K 100 FACTOR= 19.79 K 200 FACTOR= 17.22 D FACTOR= 70.36

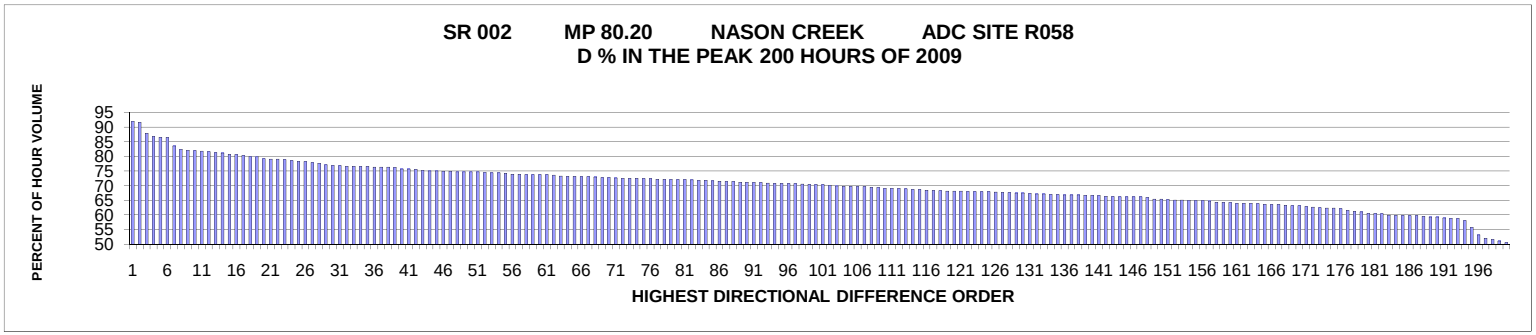

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
5	25	9	2	12	1035	25.64	1	4037	207	828	20	80
10	11	9	1	12	1022	25.32	2		385	637	37.67	62.33
8	9	9	1	14	1013	25.09	3		353	660	34.85	65.15
10	11	9	1	13	1007	24.94	4		405	602	40.22	59.78
10	11	9	1	17	1007	24.94	5		258	749	25.62	74.38
10	11	9	1	16	1003	24.85	6		265	738	26.42	73.58
8	16	9	1	14	1002	24.82	7		367	635	36.63	63.37
8	23	9	1	13	1000	24.77	8		357	643	35.7	64.3
10	11	9	1	15	992	24.57	9		304	688	30.65	69.35
8	23	9	1	14	985	24.4	10		324	661	32.89	67.11
8	16	9	1	16	980	24.28	11		319	661	32.55	67.45
5	25	9	2	13	976	24.18	12		210	766	21.52	78.48
10	11	9	1	14	974	24.13	13		351	623	36.04	63.96
5	25	9	2	11	971	24.05	14		131	840	13.49	86.51
8	23	9	1	15	968	23.98	15		319	649	32.95	67.05
7	19	9	1	13	963	23.85	16		363	600	37.69	62.31
8	9	9	1	13	961	23.8	17		369	592	38.4	61.6

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	16	9	1	15	959	23.76	18		324	635	33.79	66.21
7	19	9	1	15	956	23.68	19		323	633	33.79	66.21
7	19	9	1	14	944	23.38	20		306	638	32.42	67.58
10	4	9	1	13	944	23.38	21	4037	284	660	30.08	69.92
8	9	9	1	15	942	23.33	22		300	642	31.85	68.15
8	2	9	1	14	927	22.96	23		371	556	40.02	59.98
10	4	9	1	14	915	22.67	24		254	661	27.76	72.24
8	2	9	1	15	912	22.59	25		320	592	35.09	64.91
8	9	9	1	12	912	22.59	26		315	597	34.54	65.46
8	16	9	1	17	912	22.59	27		252	660	27.63	72.37
10	4	9	1	16	901	22.32	28		235	666	26.08	73.92
8	9	9	1	16	899	22.27	29		298	601	33.15	66.85
8	9	9	1	17	899	22.27	30		283	616	31.48	68.52
8	16	9	1	13	899	22.27	31		324	575	36.04	63.96
7	5	9	1	12	896	22.19	32		241	655	26.9	73.1
8	23	9	1	16	895	22.17	33		276	619	30.84	69.16
7	12	9	1	13	894	22.15	34		314	580	35.12	64.88
8	2	9	1	13	893	22.12	35		352	541	39.42	60.58
9	20	9	1	16	893	22.12	36		243	650	27.21	72.79
9	7	9	2	12	890	22.05	37		185	705	20.79	79.21
7	26	9	1	15	885	21.92	38		309	576	34.92	65.08
9	20	9	1	15	885	21.92	39		236	649	26.67	73.33
4	5	9	1	18	883	21.87	40		162	721	18.35	81.65
7	5	9	1	13	881	21.82	41	4037	251	630	28.49	71.51
7	26	9	1	16	879	21.77	42		295	584	33.56	66.44
7	26	9	1	14	877	21.72	43		316	561	36.03	63.97
8	23	9	1	12	874	21.65	44		280	594	32.04	67.96
6	21	9	1	14	873	21.62	45		248	625	28.41	71.59
8	30	9	1	16	873	21.62	46		254	619	29.1	70.9
6	28	9	1	15	868	21.5	47		255	613	29.38	70.62
6	21	9	1	15	867	21.48	48		228	639	26.3	73.7
7	12	9	1	14	863	21.38	49		287	576	33.26	66.74
5	25	9	2	15	862	21.35	50		161	701	18.68	81.32
6	28	9	1	14	862	21.35	51		248	614	28.77	71.23
9	27	9	1	16	862	21.35	52		218	644	25.29	74.71
9	20	9	1	14	861	21.33	53		242	619	28.11	71.89
8	9	9	1	18	859	21.28	54		209	650	24.33	75.67
10	4	9	1	15	859	21.28	55		217	642	25.26	74.74
8	16	9	1	12	857	21.23	56		344	513	40.14	59.86
10	4	9	1	12	857	21.23	57		239	618	27.89	72.11
9	7	9	2	13	856	21.2	58		209	647	24.42	75.58
4	5	9	1	19	851	21.08	59		112	739	13.16	86.84
9	27	9	1	14	850	21.06	60		263	587	30.94	69.06
4	5	9	1	20	849	21.03	61	4037	114	735	13.43	86.57
7	5	9	1	14	847	20.98	62		283	564	33.41	66.59
7	12	9	1	15	847	20.98	63		272	575	32.11	67.89
9	27	9	1	13	846	20.96	64		318	528	37.59	62.41
7	19	9	1	16	840	20.81	65		300	540	35.71	64.29
6	21	9	1	13	839	20.78	66		251	588	29.92	70.08
8	30	9	1	15	835	20.68	67		248	587	29.7	70.3
7	26	9	1	12	832	20.61	68		303	529	36.42	63.58
8	30	9	1	18	832	20.61	69		161	671	19.35	80.65

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
5	25	9	2	14	831	20.58	70		176	655	21.18	78.82
7	5	9	1	15	831	20.58	71		291	540	35.02	64.98
8	30	9	1	17	831	20.58	72		194	637	23.35	76.65
8	30	9	1	14	829	20.54	73		237	592	28.59	71.41
6	28	9	1	12	828	20.51	74		289	539	34.9	65.1
9	7	9	2	14	828	20.51	75		211	617	25.48	74.52
9	20	9	1	17	825	20.44	76		217	608	26.3	73.7
6	28	9	1	16	824	20.41	77		226	598	27.43	72.57
7	19	9	1	12	824	20.41	78		321	503	38.96	61.04
9	27	9	1	15	822	20.36	79		221	601	26.89	73.11
10	10	9	7	12	822	20.36	80		675	147	82.12	17.88
7	26	9	1	13	821	20.34	81	4037	334	487	40.68	59.32
10	18	9	1	12	820	20.31	82		229	591	27.93	72.07
8	2	9	1	12	819	20.29	83		330	489	40.29	59.71
10	18	9	1	13	819	20.29	84		256	563	31.26	68.74
6	28	9	1	13	816	20.21	85		271	545	33.21	66.79
9	27	9	1	17	814	20.16	86		238	576	29.24	70.76
4	5	9	1	17	811	20.09	87		203	608	25.03	74.97
10	10	9	7	13	809	20.04	88		618	191	76.39	23.61
6	20	9	7	14	801	19.84	89		633	168	79.03	20.97
7	12	9	1	16	801	19.84	90		282	519	35.21	64.79
6	21	9	1	12	799	19.79	91		230	569	28.79	71.21
10	10	9	7	16	798	19.77	92		395	403	49.5	50.5
9	27	9	1	18	791	19.59	93		217	574	27.43	72.57
7	19	9	1	17	789	19.54	94		252	537	31.94	68.06
8	8	9	7	12	789	19.54	95		534	255	67.68	32.32
8	30	9	1	12	789	19.54	96		228	561	28.9	71.1
10	4	9	1	17	787	19.49	97		191	596	24.27	75.73
7	3	9	6	13	786	19.47	98		554	232	70.48	29.52
5	17	9	1	15	776	19.22	99		222	554	28.61	71.39
9	13	9	1	14	776	19.22	100		237	539	30.54	69.46
10	18	9	1	14	776	19.22	101	4037	230	546	29.64	70.36
8	23	9	1	17	775	19.2	102		204	571	26.32	73.68
8	16	9	1	18	774	19.17	103		224	550	28.94	71.06
12	26	9	7	14	774	19.17	104		522	252	67.44	32.56
8	30	9	1	13	771	19.1	105		253	518	32.81	67.19
8	8	9	7	13	770	19.07	106		519	251	67.4	32.6
7	3	9	6	12	769	19.05	107		569	200	73.99	26.01
7	12	9	1	12	769	19.05	108		262	507	34.07	65.93
9	20	9	1	18	769	19.05	109		202	567	26.27	73.73
12	27	9	1	13	768	19.02	110		451	317	58.72	41.28
9	20	9	1	13	767	19	111		246	521	32.07	67.93
10	10	9	7	14	767	19	112		534	233	69.62	30.38
6	21	9	1	16	766	18.97	113		238	528	31.07	68.93
9	13	9	1	12	765	18.95	114		279	486	36.47	63.53
12	27	9	1	15	765	18.95	115		398	367	52.03	47.97
8	30	9	1	19	762	18.88	116		150	612	19.69	80.31
12	26	9	7	13	758	18.78	117		517	241	68.21	31.79
12	27	9	1	14	755	18.7	118		390	365	51.66	48.34
6	14	9	1	15	754	18.68	119		211	543	27.98	72.02
8	2	9	1	16	754	18.68	120		233	521	30.9	69.1
5	25	9	2	16	752	18.63	121	4037	145	607	19.28	80.72

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	3	9	6	16	752	18.63	122		514	238	68.35	31.65
7	5	9	1	11	750	18.58	123		176	574	23.47	76.53
8	22	9	7	14	749	18.55	124		473	276	63.15	36.85
10	11	9	1	18	749	18.55	125		174	575	23.23	76.77
6	14	9	1	14	747	18.5	126		205	542	27.44	72.56
5	22	9	6	17	740	18.33	127		575	165	77.7	22.3
6	20	9	7	15	740	18.33	128		490	250	66.22	33.78
5	24	9	1	14	738	18.28	129		346	392	46.88	53.12
7	3	9	6	15	738	18.28	130		503	235	68.16	31.84
9	20	9	1	12	737	18.26	131		268	469	36.36	63.64
9	27	9	1	12	735	18.21	132		285	450	38.78	61.22
10	10	9	7	15	735	18.21	133		472	263	64.22	35.78
5	22	9	6	15	734	18.18	134		574	160	78.2	21.8
5	24	9	1	13	733	18.16	135		409	324	55.8	44.2
6	28	9	1	17	733	18.16	136		168	565	22.92	77.08
7	5	9	1	16	733	18.16	137		242	491	33.02	66.98
9	7	9	2	15	732	18.13	138		174	558	23.77	76.23
5	24	9	1	17	727	18.01	139		170	557	23.38	76.62
6	7	9	1	15	727	18.01	140		172	555	23.66	76.34
5	17	9	1	14	726	17.98	141	4037	184	542	25.34	74.66
7	3	9	6	11	726	17.98	142		545	181	75.07	24.93
8	14	9	6	15	726	17.98	143		438	288	60.33	39.67
8	14	9	6	16	726	17.98	144		432	294	59.5	40.5
5	22	9	6	14	725	17.96	145		594	131	81.93	18.07
4	5	9	1	21	724	17.93	146		58	666	8.01	91.99
9	5	9	7	14	724	17.93	147		530	194	73.2	26.8
5	22	9	6	20	723	17.91	148		636	87	87.97	12.03
10	9	9	6	15	723	17.91	149		426	297	58.92	41.08
5	22	9	6	19	722	17.88	150		603	119	83.52	16.48
8	22	9	7	12	722	17.88	151		461	261	63.85	36.15
12	27	9	1	16	722	17.88	152		353	369	48.89	51.11
8	8	9	7	14	720	17.84	153		418	302	58.06	41.94
5	22	9	6	21	719	17.81	154		659	60	91.66	8.34
9	4	9	6	16	719	17.81	155		521	198	72.46	27.54
9	13	9	1	15	718	17.79	156		229	489	31.89	68.11
10	18	9	1	16	718	17.79	157		159	559	22.14	77.86
5	22	9	6	18	717	17.76	158		582	135	81.17	18.83
8	2	9	1	17	717	17.76	159		217	500	30.26	69.74
7	17	9	6	15	715	17.71	160		451	264	63.08	36.92
5	17	9	1	16	714	17.69	161	4037	167	547	23.39	76.61
12	26	9	7	16	714	17.69	162		432	282	60.5	39.5
9	26	9	7	12	713	17.66	163		504	209	70.69	29.31
9	5	9	7	13	712	17.64	164		517	195	72.61	27.39
5	23	9	7	12	711	17.61	165		586	125	82.42	17.58
10	18	9	1	15	710	17.59	166		177	533	24.93	75.07
5	22	9	6	16	709	17.56	167		580	129	81.81	18.19
6	14	9	1	12	709	17.56	168		209	500	29.48	70.52
8	1	9	7	12	709	17.56	169		446	263	62.91	37.09
8	22	9	7	13	708	17.54	170		494	214	69.77	30.23
6	7	9	1	13	707	17.51	171		190	517	26.87	73.13
9	4	9	6	15	707	17.51	172		532	175	75.25	24.75
10	3	9	7	13	707	17.51	173		525	182	74.26	25.74

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
12	26	9	7	15	706	17.49	174		467	239	66.15	33.85
9	13	9	1	13	704	17.44	175		263	441	37.36	62.64
10	4	9	1	18	704	17.44	176		180	524	25.57	74.43
6	7	9	1	16	703	17.41	177		142	561	20.2	79.8
7	12	9	1	17	703	17.41	178		213	490	30.3	69.7
12	27	9	1	18	703	17.41	179		513	190	72.97	27.03
5	17	9	1	13	702	17.39	180		243	459	34.62	65.38
8	21	9	6	14	702	17.39	181	4037	413	289	58.83	41.17
6	14	9	1	16	701	17.36	182		177	524	25.25	74.75
6	19	9	6	16	701	17.36	183		510	191	72.75	27.25
8	7	9	6	15	701	17.36	184		465	236	66.33	33.67
9	5	9	7	12	701	17.36	185		504	197	71.9	28.1
10	18	9	1	17	700	17.34	186		162	538	23.14	76.86
6	14	9	1	13	698	17.29	187		232	466	33.24	66.76
8	21	9	6	15	698	17.29	188		473	225	67.77	32.23
5	23	9	7	14	697	17.27	189		546	151	78.34	21.66
8	14	9	6	14	697	17.27	190		433	264	62.12	37.88
7	26	9	1	17	695	17.22	191		193	502	27.77	72.23
7	5	9	1	17	694	17.19	192		223	471	32.13	67.87
7	24	9	6	16	694	17.19	193		455	239	65.56	34.44

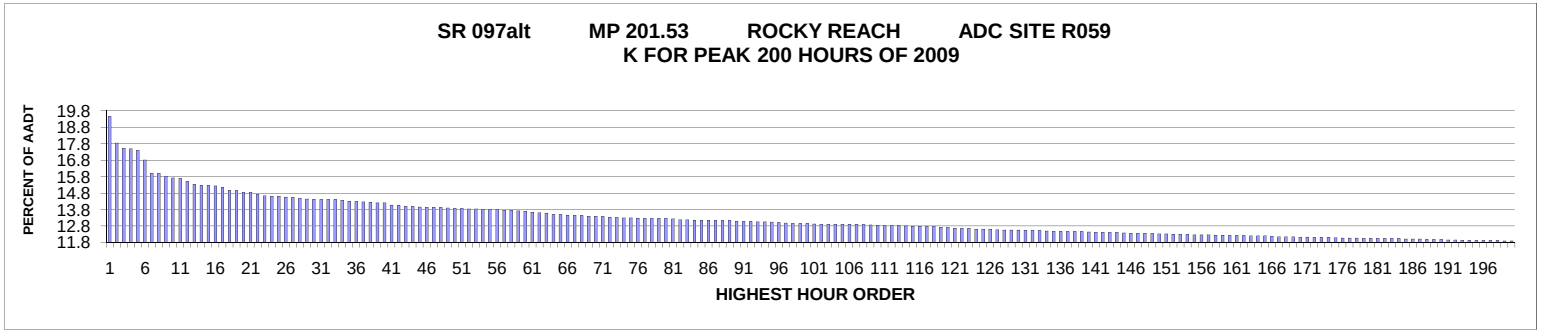

AADT= 6870 **K 30 FACTOR=** 14.43 **K 100 FACTOR=** 12.94 **K 200 FACTOR=** 11.89 **D FACTOR=** 59.35

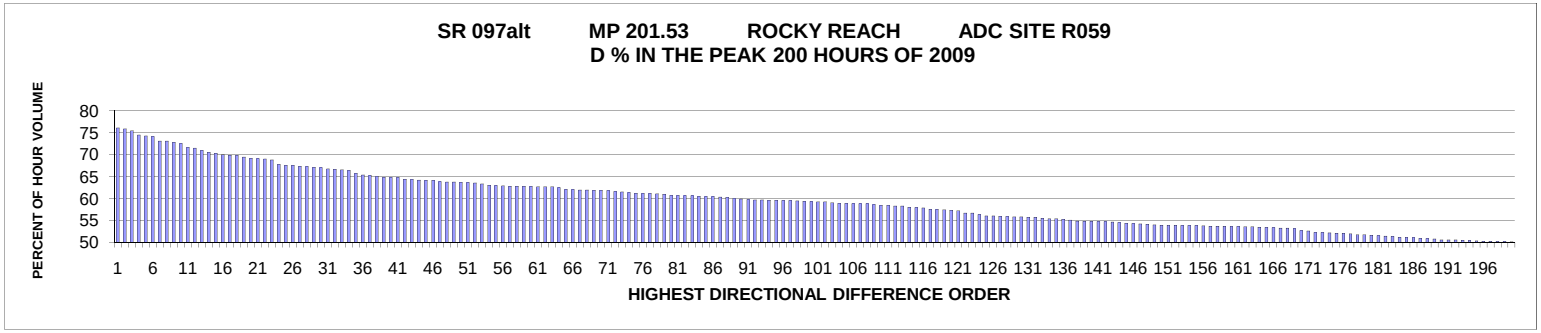

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
9	4	9	6	17	1336	19.45	1	6870	851	485	63.7	36.3
9	7	9	2	14	1226	17.85	2		369	857	30.1	69.9
9	7	9	2	12	1204	17.53	3		296	908	24.58	75.42
9	7	9	2	13	1202	17.5	4		309	893	25.71	74.29
9	4	9	6	18	1195	17.39	5		807	388	67.53	32.47
9	4	9	6	16	1155	16.81	6		696	459	60.26	39.74
9	11	9	6	17	1100	16.01	7		638	462	58	42
9	4	9	6	15	1099	16	8		708	391	64.42	35.58
9	11	9	6	16	1087	15.82	9		601	486	55.29	44.71
9	18	9	6	17	1080	15.72	10		665	415	61.57	38.43
9	12	9	7	16	1077	15.68	11		426	651	39.55	60.45
9	5	9	7	12	1066	15.52	12		570	496	53.47	46.53
9	7	9	2	15	1054	15.34	13		344	710	32.64	67.36
5	25	9	2	12	1050	15.28	14		251	799	23.9	76.1
9	25	9	6	17	1049	15.27	15		627	422	59.77	40.23
9	3	9	5	17	1047	15.24	16		515	532	49.19	50.81
5	22	9	6	17	1040	15.14	17		757	283	72.79	27.21

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
9	18	9	6	18	1028	14.96	18		690	338	67.12	32.88
9	18	9	6	16	1027	14.95	19		566	461	55.11	44.89
9	5	9	7	15	1020	14.85	20		606	414	59.41	40.59
9	7	9	2	16	1020	14.85	21	6870	315	705	30.88	69.12
5	22	9	6	16	1011	14.72	22		713	298	70.52	29.48
9	13	9	1	12	1006	14.64	23		381	625	37.87	62.13
9	5	9	7	13	1004	14.61	24		587	417	58.47	41.53
9	25	9	6	16	1004	14.61	25		547	457	54.48	45.52
9	10	9	5	17	1000	14.56	26		479	521	47.9	52.1
9	11	9	6	18	999	14.54	27		590	409	59.06	40.94
9	4	9	6	14	995	14.48	28		624	371	62.71	37.29
9	6	9	1	15	992	14.44	29		385	607	38.81	61.19
9	11	9	6	15	991	14.43	30		553	438	55.8	44.2
5	25	9	2	11	990	14.41	31		239	751	24.14	75.86
7	5	9	1	12	990	14.41	32		287	703	28.99	71.01
9	13	9	1	15	989	14.4	33		399	590	40.34	59.66
7	19	9	1	14	987	14.37	34		458	529	46.4	53.6
9	13	9	1	16	983	14.31	35		358	625	36.42	63.58
7	5	9	1	14	982	14.29	36		365	617	37.17	62.83
7	2	9	5	16	980	14.26	37		621	359	63.37	36.63
9	25	9	6	18	979	14.25	38		607	372	62	38
7	19	9	1	13	976	14.21	39		432	544	44.26	55.74
9	25	9	6	15	976	14.21	40		562	414	57.58	42.42
5	25	9	2	13	967	14.08	41	6870	274	693	28.34	71.66
7	17	9	6	16	965	14.05	42		606	359	62.8	37.2
9	10	9	5	16	961	13.99	43		501	460	52.13	47.87
9	13	9	1	14	960	13.97	44		366	594	38.13	61.88
9	17	9	5	17	959	13.96	45		458	501	47.76	52.24
7	17	9	6	17	957	13.93	46		609	348	63.64	36.36
9	6	9	1	14	957	13.93	47		437	520	45.66	54.34
9	6	9	1	16	956	13.92	48		356	600	37.24	62.76
8	9	9	1	12	954	13.89	49		424	530	44.44	55.56
8	28	9	6	16	952	13.86	50		565	387	59.35	40.65
9	4	9	6	19	952	13.86	51		666	286	69.96	30.04
9	6	9	1	13	951	13.84	52		440	511	46.27	53.73
9	18	9	6	15	950	13.83	53		500	450	52.63	47.37
9	5	9	7	14	949	13.81	54		559	390	58.9	41.1
9	8	9	3	16	949	13.81	55		439	510	46.26	53.74
9	1	9	3	16	948	13.8	56		437	511	46.1	53.9
9	3	9	5	16	945	13.76	57		493	452	52.17	47.83
9	13	9	1	13	945	13.76	58		364	581	38.52	61.48
9	13	9	1	17	943	13.73	59		368	575	39.02	60.98
9	27	9	1	16	941	13.7	60		331	610	35.18	64.82
7	2	9	5	17	937	13.64	61	6870	568	369	60.62	39.38
9	27	9	1	13	935	13.61	62		325	610	34.76	65.24
8	9	9	1	14	933	13.58	63		422	511	45.23	54.77
7	12	9	1	13	927	13.49	64		344	583	37.11	62.89
7	5	9	1	13	926	13.48	65		305	621	32.94	67.06
7	19	9	1	12	924	13.45	66		406	518	43.94	56.06
9	2	9	4	17	924	13.45	67		448	476	48.48	51.52
9	24	9	5	17	923	13.44	68		456	467	49.4	50.6
9	3	9	5	18	920	13.39	69		558	362	60.65	39.35

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
9	17	9	5	16	920	13.39	70		463	457	50.33	49.67
7	17	9	6	15	919	13.38	71		558	361	60.72	39.28
9	20	9	1	17	916	13.33	72		350	566	38.21	61.79
9	20	9	1	14	915	13.32	73		326	589	35.63	64.37
9	12	9	7	12	914	13.3	74		491	423	53.72	46.28
9	25	9	6	14	913	13.29	75		491	422	53.78	46.22
8	7	9	6	16	912	13.28	76		532	380	58.33	41.67
7	3	9	6	12	911	13.26	77		585	326	64.22	35.78
7	10	9	6	16	910	13.25	78		522	388	57.36	42.64
9	7	9	2	11	910	13.25	79		245	665	26.92	73.08
9	24	9	5	16	910	13.25	80		470	440	51.65	48.35
8	14	9	6	16	909	13.23	81	6870	556	353	61.17	38.83
7	3	9	6	17	905	13.17	82		567	338	62.65	37.35
9	4	9	6	13	905	13.17	83		507	398	56.02	43.98
7	19	9	1	15	904	13.16	84		400	504	44.25	55.75
9	12	9	7	17	904	13.16	85		398	506	44.03	55.97
9	27	9	1	17	904	13.16	86		324	580	35.84	64.16
9	13	9	1	18	903	13.14	87		365	538	40.42	59.58
7	3	9	6	16	902	13.13	88		593	309	65.74	34.26
8	23	9	1	16	902	13.13	89		327	575	36.25	63.75
9	20	9	1	13	900	13.1	90		281	619	31.22	68.78
8	2	9	1	13	899	13.09	91		465	434	51.72	48.28
8	7	9	6	17	899	13.09	92		574	325	63.85	36.15
8	23	9	1	13	898	13.07	93		370	528	41.2	58.8
9	11	9	6	14	898	13.07	94		497	401	55.35	44.65
9	7	9	2	17	896	13.04	95		321	575	35.83	64.17
9	16	9	4	17	893	13	96		434	459	48.6	51.4
9	1	9	3	17	892	12.98	97		414	478	46.41	53.59
7	3	9	6	13	891	12.97	98		604	287	67.79	32.21
9	6	9	1	17	889	12.94	99		360	529	40.49	59.51
9	16	9	4	16	889	12.94	100		415	474	46.68	53.32
8	14	9	6	17	888	12.93	101	6870	576	312	64.86	35.14
7	26	9	1	13	887	12.91	102		478	409	53.89	46.11
9	5	9	7	16	887	12.91	103		532	355	59.98	40.02
9	8	9	3	17	887	12.91	104		411	476	46.34	53.66
9	20	9	1	16	887	12.91	105		331	556	37.32	62.68
7	17	9	6	14	886	12.9	106		574	312	64.79	35.21
9	21	9	2	17	886	12.9	107		444	442	50.11	49.89
8	2	9	1	14	885	12.88	108		458	427	51.75	48.25
8	21	9	6	16	884	12.87	109		524	360	59.28	40.72
6	26	9	6	16	883	12.85	110		516	367	58.44	41.56
8	9	9	1	13	881	12.82	111		371	510	42.11	57.89
9	9	9	4	16	881	12.82	112		399	482	45.29	54.71
9	23	9	4	16	881	12.82	113		405	476	45.97	54.03
7	2	9	5	18	880	12.81	114		575	305	65.34	34.66
6	26	9	6	17	879	12.79	115		517	362	58.82	41.18
9	15	9	3	16	879	12.79	116		437	442	49.72	50.28
9	19	9	7	13	877	12.77	117		443	434	50.51	49.49
9	20	9	1	15	877	12.77	118		347	530	39.57	60.43
7	3	9	6	15	875	12.74	119		640	235	73.14	26.86
9	4	9	6	20	874	12.72	120		648	226	74.14	25.86
7	31	9	6	16	871	12.68	121	6870	532	339	61.08	38.92

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
9	2	9	4	16	869	12.65	122		407	462	46.84	53.16
9	5	9	7	17	869	12.65	123		464	405	53.39	46.61
9	26	9	7	16	867	12.62	124		424	443	48.9	51.1
8	8	9	7	13	866	12.61	125		475	391	54.85	45.15
9	10	9	5	18	866	12.61	126		484	382	55.89	44.11
8	16	9	1	15	864	12.58	127		329	535	38.08	61.92
9	22	9	3	17	863	12.56	128		401	462	46.47	53.53
9	3	9	5	15	862	12.55	129		436	426	50.58	49.42
9	24	9	5	15	862	12.55	130		459	403	53.25	46.75
8	1	9	7	13	861	12.53	131		573	288	66.55	33.45
9	18	9	6	14	861	12.53	132		472	389	54.82	45.18
8	23	9	1	14	860	12.52	133		368	492	42.79	57.21
7	26	9	1	15	858	12.49	134		392	466	45.69	54.31
7	26	9	1	16	857	12.47	135		355	502	41.42	58.58
8	23	9	1	15	857	12.47	136		326	531	38.04	61.96
6	28	9	1	14	856	12.46	137		382	474	44.63	55.37
9	12	9	7	13	856	12.46	138		482	374	56.31	43.69
9	14	9	2	16	855	12.45	139		394	461	46.08	53.92
5	22	9	6	18	854	12.43	140		636	218	74.47	25.53
7	3	9	6	18	853	12.42	141	6870	536	317	62.84	37.16
9	27	9	1	15	853	12.42	142		309	544	36.23	63.77
6	19	9	6	17	852	12.4	143		514	338	60.33	39.67
9	17	9	5	18	852	12.4	144		507	345	59.51	40.49
5	25	9	2	14	851	12.39	145		276	575	32.43	67.57
6	19	9	6	16	850	12.37	146		516	334	60.71	39.29
8	16	9	1	16	850	12.37	147		319	531	37.53	62.47
7	24	9	6	17	849	12.36	148		566	283	66.67	33.33
8	9	9	1	16	848	12.34	149		367	481	43.28	56.72
9	14	9	2	17	847	12.33	150		391	456	46.16	53.84
9	17	9	5	15	847	12.33	151		426	421	50.3	49.7
9	10	9	5	15	846	12.31	152		421	425	49.76	50.24
8	9	9	1	15	845	12.3	153		387	458	45.8	54.2
9	11	9	6	13	844	12.29	154		414	430	49.05	50.95
8	9	9	1	17	843	12.27	155		280	563	33.21	66.79
9	9	9	4	17	843	12.27	156		409	434	48.52	51.48
9	8	9	3	15	842	12.26	157		402	440	47.74	52.26
8	16	9	1	13	841	12.24	158		358	483	42.57	57.43
9	21	9	2	16	841	12.24	159		416	425	49.46	50.54
7	19	9	1	16	840	12.23	160		337	503	40.12	59.88
9	25	9	6	12	840	12.23	161	6870	413	427	49.17	50.83
9	25	9	6	19	840	12.23	162		529	311	62.98	37.02
6	21	9	1	13	839	12.21	163		260	579	30.99	69.01
9	15	9	3	17	839	12.21	164		387	452	46.13	53.87
8	21	9	6	17	838	12.2	165		507	331	60.5	39.5
7	18	9	7	12	837	12.18	166		485	352	57.95	42.05
9	8	9	3	18	835	12.15	167		427	408	51.14	48.86
7	25	9	7	12	834	12.14	168		516	318	61.87	38.13
9	20	9	1	12	834	12.14	169		308	526	36.93	63.07
7	25	9	7	13	833	12.13	170		490	343	58.82	41.18
9	15	9	3	15	833	12.13	171		413	420	49.58	50.42
7	10	9	6	17	832	12.11	172		490	342	58.89	41.11
8	20	9	5	16	832	12.11	173		443	389	53.25	46.75

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	1	9	7	12	831	12.1	174		494	337	59.45	40.55
9	27	9	1	14	830	12.08	175		335	495	40.36	59.64
7	12	9	1	14	829	12.07	176		322	507	38.84	61.16
7	26	9	1	14	829	12.07	177		416	413	50.18	49.82
7	26	9	1	17	829	12.07	178		253	576	30.52	69.48
5	22	9	6	15	828	12.05	179		592	236	71.5	28.5
7	5	9	1	15	828	12.05	180		334	494	40.34	59.66
8	23	9	1	12	828	12.05	181	6870	271	557	32.73	67.27
9	24	9	5	18	828	12.05	182		448	380	54.11	45.89
9	6	9	1	12	827	12.04	183		375	452	45.34	54.66
9	26	9	7	17	827	12.04	184		404	423	48.85	51.15
8	16	9	1	14	826	12.02	185		365	461	44.19	55.81
9	25	9	6	13	826	12.02	186		435	391	52.66	47.34
7	17	9	6	18	825	12.01	187		537	288	65.09	34.91
5	23	9	7	15	823	11.98	188		579	244	70.35	29.65
7	18	9	7	15	823	11.98	189		480	343	58.32	41.68
8	13	9	5	16	823	11.98	190		444	379	53.95	46.05
6	28	9	1	13	821	11.95	191		349	472	42.51	57.49
7	3	9	6	14	821	11.95	192		573	248	69.79	30.21
8	30	9	1	13	820	11.94	193		334	486	40.73	59.27
7	5	9	1	18	819	11.92	194		225	594	27.47	72.53
8	1	9	7	14	818	11.91	195		543	275	66.38	33.62
8	2	9	1	16	818	11.91	196		354	464	43.28	56.72
8	16	9	1	12	818	11.91	197		316	502	38.63	61.37
9	23	9	4	17	818	11.91	198		393	425	48.04	51.96
8	1	9	7	16	817	11.89	199		447	370	54.71	45.29
8	7	9	6	18	817	11.89	200		565	252	69.16	30.84

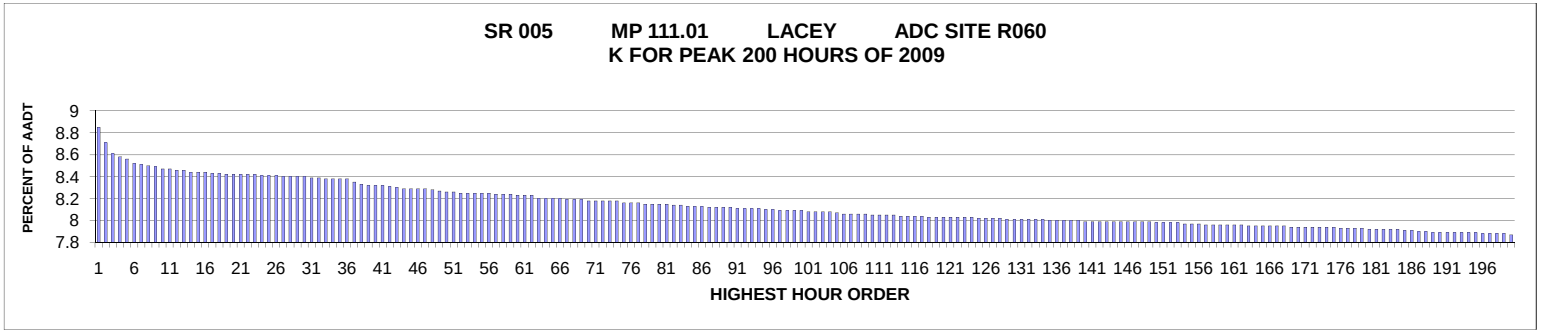

AADT= 113492 **K 30 FACTOR=** 8.4 **K 100 FACTOR=** 8.09 **K 200 FACTOR=** 7.87 **D FACTOR=** 51.87

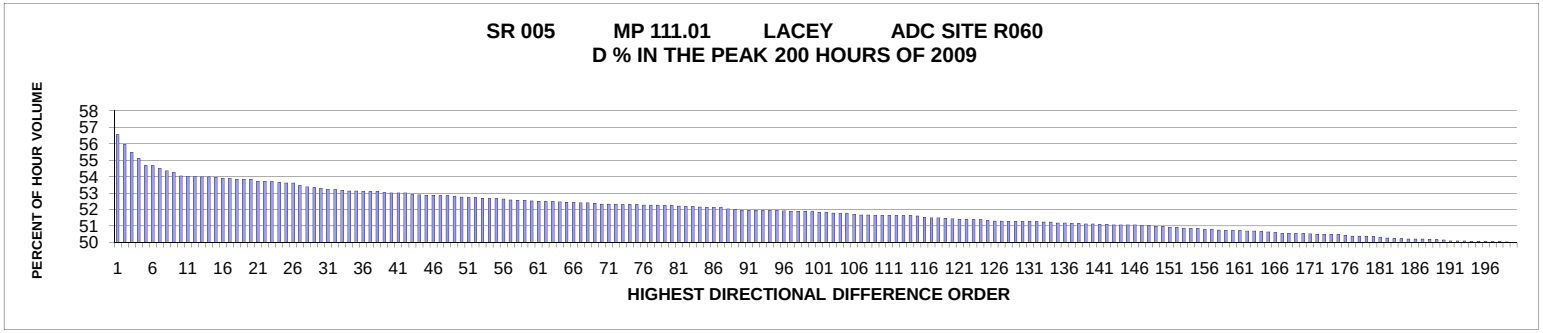

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
3	27	9	6	16	10042	8.85	1	113492	4794	5248	47.74	52.26
8	23	9	1	14	9880	8.71	2		5326	4554	53.91	46.09
8	14	9	6	16	9774	8.61	3		5132	4642	52.51	47.49
8	14	9	6	15	9743	8.58	4		5062	4681	51.96	48.04
8	28	9	6	16	9711	8.56	5		4807	4904	49.5	50.5
8	28	9	6	15	9668	8.52	6		4895	4773	50.63	49.37
2	27	9	6	17	9661	8.51	7		4644	5017	48.07	51.93
2	13	9	6	17	9642	8.5	8		4611	5031	47.82	52.18
5	1	9	6	16	9632	8.49	9		4690	4942	48.69	51.31
4	10	9	6	17	9612	8.47	10		4536	5076	47.19	52.81
8	13	9	5	16	9611	8.47	11		4704	4907	48.94	51.06
4	17	9	6	16	9603	8.46	12		4577	5026	47.66	52.34
8	21	9	6	16	9596	8.46	13		4789	4807	49.91	50.09
5	15	9	6	17	9576	8.44	14		4693	4883	49.01	50.99
5	8	9	6	16	9575	8.44	15		4552	5023	47.54	52.46
8	15	9	7	13	9575	8.44	16		4836	4739	50.51	49.49
8	5	9	4	17	9573	8.43	17		4905	4668	51.24	48.76

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
5	15	9	6	15	9571	8.43	18		4645	4926	48.53	51.47
8	14	9	6	14	9560	8.42	19		4758	4802	49.77	50.23
8	22	9	7	12	9560	8.42	20		4506	5054	47.13	52.87
8	14	9	6	13	9559	8.42	21	113492	4713	4846	49.3	50.7
8	15	9	7	12	9552	8.42	22		4556	4996	47.7	52.3
8	16	9	1	14	9551	8.42	23		4963	4588	51.96	48.04
8	14	9	6	17	9549	8.41	24		4797	4752	50.24	49.76
8	6	9	5	17	9548	8.41	25		4769	4779	49.95	50.05
8	21	9	6	17	9545	8.41	26		4614	4931	48.34	51.66
4	17	9	6	17	9537	8.4	27		4666	4871	48.93	51.07
5	1	9	6	17	9532	8.4	28		4600	4932	48.26	51.74
8	21	9	6	14	9532	8.4	29		4691	4841	49.21	50.79
8	28	9	6	14	9532	8.4	30		4631	4901	48.58	51.42
9	4	9	6	13	9523	8.39	31		4396	5127	46.16	53.84
3	27	9	6	15	9519	8.39	32		4382	5137	46.03	53.97
8	7	9	6	15	9511	8.38	33		4946	4565	52	48
8	12	9	4	17	9511	8.38	34		4634	4877	48.72	51.28
8	28	9	6	17	9510	8.38	35		4533	4977	47.67	52.33
5	15	9	6	16	9505	8.38	36		4680	4825	49.24	50.76
3	13	9	6	16	9474	8.35	37		4584	4890	48.39	51.61
8	22	9	7	13	9458	8.33	38		4461	4997	47.17	52.83
8	6	9	5	18	9445	8.32	39		4726	4719	50.04	49.96
5	8	9	6	15	9444	8.32	40		4378	5066	46.36	53.64
9	3	9	5	17	9437	8.32	41	113492	4596	4841	48.7	51.3
9	3	9	5	16	9427	8.31	42		4733	4694	50.21	49.79
4	3	9	6	16	9425	8.3	43		4687	4738	49.73	50.27
8	6	9	5	16	9410	8.29	44		4657	4753	49.49	50.51
10	30	9	6	16	9410	8.29	45		4403	5007	46.79	53.21
4	3	9	6	17	9408	8.29	46		4585	4823	48.74	51.26
9	4	9	6	15	9404	8.29	47		4530	4874	48.17	51.83
9	4	9	6	16	9401	8.28	48		4518	4883	48.06	51.94
8	21	9	6	13	9387	8.27	49		4480	4907	47.73	52.27
3	19	9	5	17	9371	8.26	50		4494	4877	47.96	52.04
8	11	9	3	17	9370	8.26	51		4564	4806	48.71	51.29
8	23	9	1	13	9368	8.25	52		5048	4320	53.89	46.11
4	10	9	6	16	9361	8.25	53		4392	4969	46.92	53.08
2	20	9	6	16	9360	8.25	54		4397	4963	46.98	53.02
9	4	9	6	14	9360	8.25	55		4497	4863	48.04	51.96
3	27	9	6	17	9359	8.25	56		4526	4833	48.36	51.64
4	17	9	6	18	9352	8.24	57		4494	4858	48.05	51.95
9	11	9	6	16	9351	8.24	58		4383	4968	46.87	53.13
8	14	9	6	12	9350	8.24	59		4302	5048	46.01	53.99
4	3	9	6	18	9345	8.23	60		4518	4827	48.35	51.65
2	13	9	6	18	9340	8.23	61	113492	4554	4786	48.76	51.24
8	26	9	4	17	9340	8.23	62		4676	4664	50.06	49.94
2	20	9	6	17	9311	8.2	63		4620	4691	49.62	50.38
8	21	9	6	18	9305	8.2	64		4399	4906	47.28	52.72
4	3	9	6	15	9302	8.2	65		4387	4915	47.16	52.84
8	14	9	6	18	9302	8.2	66		4590	4712	49.34	50.66
1	16	9	6	16	9298	8.19	67		4344	4954	46.72	53.28
3	20	9	6	18	9298	8.19	68		4539	4759	48.82	51.18
8	21	9	6	15	9297	8.19	69		4640	4657	49.91	50.09

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	7	9	6	13	9289	8.18	70		4783	4506	51.49	48.51
8	7	9	6	12	9285	8.18	71		4404	4881	47.43	52.57
5	1	9	6	18	9284	8.18	72		4395	4889	47.34	52.66
8	7	9	6	16	9284	8.18	73		4710	4574	50.73	49.27
8	28	9	6	13	9284	8.18	74		4441	4843	47.83	52.17
1	30	9	6	16	9266	8.16	75		4410	4856	47.59	52.41
4	24	9	6	17	9264	8.16	76		4297	4967	46.38	53.62
2	27	9	6	18	9261	8.16	77		4418	4843	47.71	52.29
4	30	9	5	17	9254	8.15	78		4417	4837	47.73	52.27
5	22	9	6	14	9253	8.15	79		4545	4708	49.12	50.88
8	13	9	5	17	9248	8.15	80		4916	4332	53.16	46.84
5	21	9	5	17	9246	8.15	81	113492	4603	4643	49.78	50.22
5	7	9	5	17	9240	8.14	82		4369	4871	47.28	52.72
4	10	9	6	18	9233	8.14	83		4454	4779	48.24	51.76
8	27	9	5	18	9231	8.13	84		4527	4704	49.04	50.96
8	22	9	7	14	9230	8.13	85		4370	4860	47.35	52.65
5	22	9	6	13	9225	8.13	86		4211	5014	45.65	54.35
3	6	9	6	16	9219	8.12	87		4239	4980	45.98	54.02
2	13	9	6	15	9215	8.12	88		4195	5020	45.52	54.48
8	2	9	1	14	9212	8.12	89		4818	4394	52.3	47.7
1	16	9	6	17	9211	8.12	90		4504	4707	48.9	51.1
5	22	9	6	16	9208	8.11	91		4611	4597	50.08	49.92
5	8	9	6	17	9206	8.11	92		4409	4797	47.89	52.11
4	2	9	5	18	9202	8.11	93		4593	4609	49.91	50.09
3	26	9	5	18	9199	8.11	94		4585	4614	49.84	50.16
8	4	9	3	17	9192	8.1	95		4469	4723	48.62	51.38
8	25	9	3	17	9191	8.1	96		4478	4713	48.72	51.28
8	8	9	7	13	9185	8.09	97		4239	4946	46.15	53.85
4	2	9	5	17	9183	8.09	98		4364	4819	47.52	52.48
1	30	9	6	17	9179	8.09	99		4448	4731	48.46	51.54
9	3	9	5	18	9177	8.09	100		4589	4588	50.01	49.99
9	5	9	7	12	9172	8.08	101	113492	4245	4927	46.28	53.72
8	1	9	7	12	9169	8.08	102		4434	4735	48.36	51.64
8	16	9	1	13	9169	8.08	103		4793	4376	52.27	47.73
1	22	9	5	17	9166	8.08	104		4242	4924	46.28	53.72
9	10	9	5	17	9163	8.07	105		4478	4685	48.87	51.13
9	11	9	6	17	9151	8.06	106		4313	4838	47.13	52.87
9	5	9	7	13	9148	8.06	107		4403	4745	48.13	51.87
8	5	9	4	18	9147	8.06	108		4594	4553	50.22	49.78
8	7	9	6	18	9144	8.06	109		4606	4538	50.37	49.63
8	29	9	7	12	9138	8.05	110		4238	4900	46.38	53.62
9	10	9	5	18	9136	8.05	111		4552	4584	49.82	50.18
8	31	9	2	17	9132	8.05	112		4660	4472	51.03	48.97
4	24	9	6	18	9131	8.05	113		4139	4992	45.33	54.67
3	29	9	1	16	9130	8.04	114		5065	4065	55.48	44.52
8	18	9	3	17	9125	8.04	115		4444	4681	48.7	51.3
5	20	9	4	17	9121	8.04	116		4366	4755	47.87	52.13
8	26	9	4	18	9121	8.04	117		4662	4459	51.11	48.89
9	2	9	4	17	9118	8.03	118		4338	4780	47.58	52.42
8	10	9	2	17	9117	8.03	119		4523	4594	49.61	50.39
4	15	9	4	17	9116	8.03	120		4461	4655	48.94	51.06
8	1	9	7	13	9113	8.03	121	113492	4505	4608	49.43	50.57

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
4	24	9	6	15	9111	8.03	122		4091	5020	44.9	55.1
9	1	9	3	17	9111	8.03	123		4492	4619	49.3	50.7
8	24	9	2	17	9109	8.03	124		4403	4706	48.34	51.66
10	20	9	3	17	9107	8.02	125		4278	4829	46.97	53.03
8	27	9	5	16	9106	8.02	126		4428	4678	48.63	51.37
5	21	9	5	18	9101	8.02	127		4444	4657	48.83	51.17
8	30	9	1	14	9097	8.02	128		5144	3953	56.55	43.45
8	2	9	1	13	9095	8.01	129		4742	4353	52.14	47.86
4	16	9	5	17	9093	8.01	130		4335	4758	47.67	52.33
10	15	9	5	18	9092	8.01	131		4438	4654	48.81	51.19
2	6	9	6	17	9091	8.01	132		4350	4741	47.85	52.15
8	21	9	6	12	9088	8.01	133		4394	4694	48.35	51.65
1	23	9	6	16	9087	8.01	134		4195	4892	46.16	53.84
2	27	9	6	16	9080	8	135		4308	4772	47.44	52.56
1	23	9	6	17	9079	8	136		4311	4768	47.48	52.52
3	20	9	6	17	9078	8	137		4643	4435	51.15	48.85
10	15	9	5	17	9077	8	138		4276	4801	47.11	52.89
4	9	9	5	18	9075	8	139		4621	4454	50.92	49.08
3	18	9	4	17	9073	7.99	140		4202	4871	46.31	53.69
3	29	9	1	15	9073	7.99	141	113492	4817	4256	53.09	46.91
8	5	9	4	16	9072	7.99	142		4486	4586	49.45	50.55
2	19	9	5	17	9070	7.99	143		4362	4708	48.09	51.91
9	8	9	3	17	9069	7.99	144		4372	4697	48.21	51.79
9	4	9	6	12	9067	7.99	145		4111	4956	45.34	54.66
4	17	9	6	15	9065	7.99	146		4314	4751	47.59	52.41
4	23	9	5	18	9064	7.99	147		4439	4625	48.97	51.03
8	23	9	1	15	9064	7.99	148		4838	4226	53.38	46.62
8	13	9	5	15	9063	7.99	149		4454	4609	49.14	50.86
3	27	9	6	18	9062	7.98	150		4288	4774	47.32	52.68
5	15	9	6	14	9059	7.98	151		4144	4915	45.74	54.26
3	20	9	6	16	9058	7.98	152		4462	4596	49.26	50.74
5	18	9	2	18	9053	7.98	153		4674	4379	51.63	48.37
8	12	9	4	16	9049	7.97	154		4348	4701	48.05	51.95
8	17	9	2	16	9043	7.97	155		4398	4645	48.63	51.37
3	26	9	5	17	9041	7.97	156		4373	4668	48.37	51.63
5	1	9	6	15	9038	7.96	157		4365	4673	48.3	51.7
9	9	9	4	17	9037	7.96	158		4315	4722	47.75	52.25
4	23	9	5	17	9035	7.96	159		4293	4742	47.52	52.48
5	22	9	6	17	9035	7.96	160		4353	4682	48.18	51.82
8	2	9	1	15	9031	7.96	161	113492	4878	4153	54.01	45.99
10	22	9	5	17	9031	7.96	162		4294	4737	47.55	52.45
3	13	9	6	15	9027	7.95	163		4251	4776	47.09	52.91
8	16	9	1	15	9026	7.95	164		4563	4463	50.55	49.45
3	13	9	6	17	9022	7.95	165		4552	4470	50.45	49.55
4	1	9	4	17	9018	7.95	166		4431	4587	49.14	50.86
5	22	9	6	15	9018	7.95	167		4455	4563	49.4	50.6
8	24	9	2	16	9017	7.95	168		4424	4593	49.06	50.94
3	6	9	6	18	9013	7.94	169		4551	4462	50.49	49.51
3	18	9	4	18	9013	7.94	170		4472	4541	49.62	50.38
2	6	9	6	18	9011	7.94	171		4370	4641	48.5	51.5
9	15	9	3	17	9011	7.94	172		4441	4570	49.28	50.72
8	8	9	7	12	9009	7.94	173		4289	4720	47.61	52.39

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	20	9	5	18	9008	7.94	174		4576	4432	50.8	49.2
10	29	9	5	17	9008	7.94	175		4233	4775	46.99	53.01
5	22	9	6	12	9005	7.93	176		3967	5038	44.05	55.95
8	3	9	2	17	9001	7.93	177		4526	4475	50.28	49.72
8	15	9	7	16	8999	7.93	178		4771	4228	53.02	46.98
4	24	9	6	16	8998	7.93	179		4328	4670	48.1	51.9
2	6	9	6	16	8994	7.92	180		4265	4729	47.42	52.58
8	10	9	2	16	8992	7.92	181	113492	4394	4598	48.87	51.13
10	23	9	6	18	8989	7.92	182		4398	4591	48.93	51.07
4	7	9	3	17	8988	7.92	183		4214	4774	46.88	53.12
5	23	9	7	12	8983	7.92	184		4293	4690	47.79	52.21
2	12	9	5	18	8982	7.91	185		4620	4362	51.44	48.56
8	15	9	7	11	8977	7.91	186		4126	4851	45.96	54.04
4	9	9	5	17	8967	7.9	187		4598	4369	51.28	48.72
2	12	9	5	17	8962	7.9	188		4431	4531	49.44	50.56
2	19	9	5	18	8960	7.89	189		4485	4475	50.06	49.94
8	17	9	2	17	8960	7.89	190		4433	4527	49.48	50.52
3	30	9	2	17	8959	7.89	191		4182	4777	46.68	53.32
8	13	9	5	18	8959	7.89	192		4726	4233	52.75	47.25
5	7	9	5	18	8955	7.89	193		4307	4648	48.1	51.9
8	16	9	1	12	8953	7.89	194		4755	4198	53.11	46.89
8	28	9	6	12	8949	7.89	195		4165	4784	46.54	53.46
5	12	9	3	17	8947	7.88	196		4185	4762	46.78	53.22
3	25	9	4	17	8945	7.88	197		4234	4711	47.33	52.67
4	1	9	4	18	8941	7.88	198		4453	4488	49.8	50.2
5	17	9	1	18	8938	7.88	199		4475	4463	50.07	49.93
10	30	9	6	17	8937	7.87	200		4112	4825	46.01	53.99

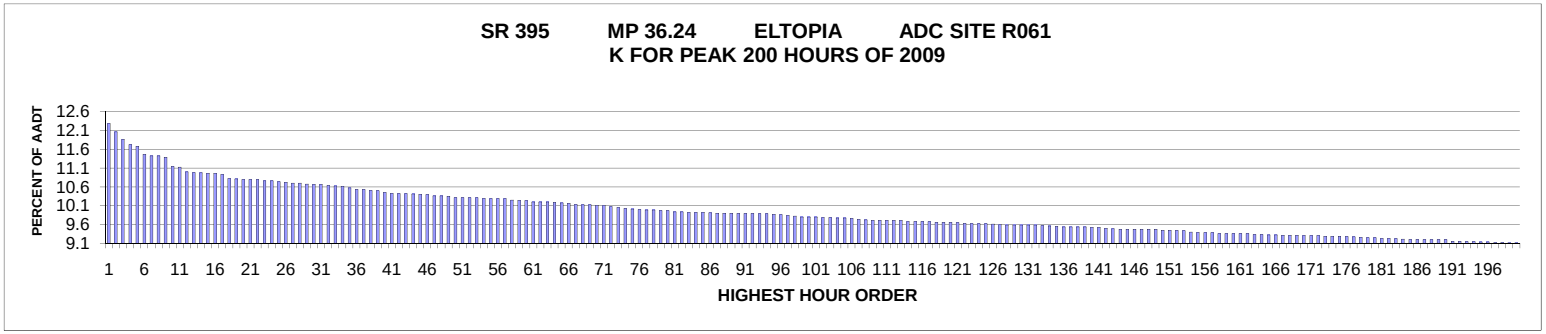

AADT= 13342 **K 30 FACTOR=** 10.66 **K 100 FACTOR=** 9.8 **K 200 FACTOR=** 9.11 **D FACTOR=** 52.41

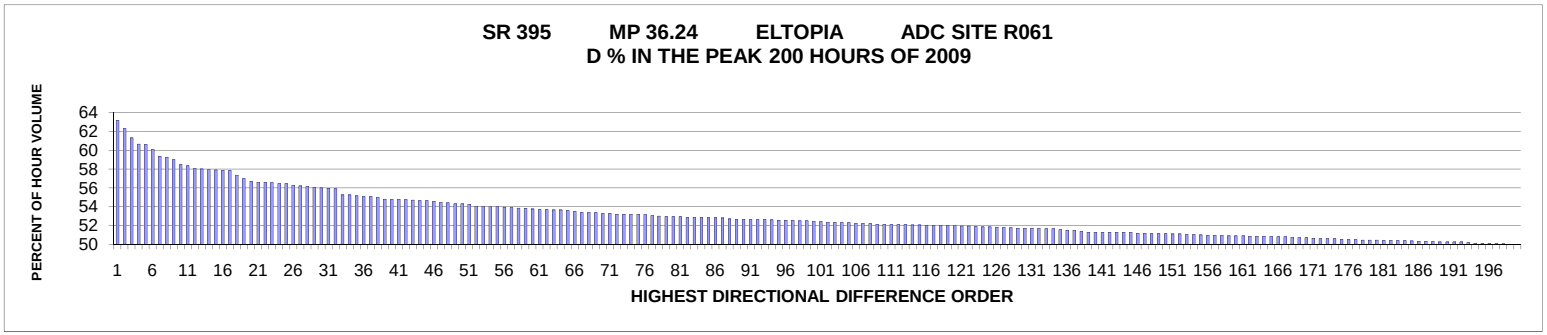

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	9	9	1	18	1638	12.28	1	13342	1020	618	62.27	37.73
7	5	9	1	16	1609	12.06	2		676	933	42.01	57.99
8	16	9	1	17	1582	11.86	3		871	711	55.06	44.94
7	5	9	1	15	1564	11.72	4		636	928	40.66	59.34
7	5	9	1	14	1558	11.68	5		622	936	39.92	60.08
8	16	9	1	18	1529	11.46	6		937	592	61.28	38.72
8	2	9	1	17	1524	11.42	7		792	732	51.97	48.03
8	2	9	1	18	1524	11.42	8		889	635	58.33	41.67
8	16	9	1	16	1520	11.39	9		769	751	50.59	49.41
8	9	9	1	16	1486	11.14	10		733	753	49.33	50.67
8	7	9	6	16	1483	11.12	11		738	745	49.76	50.24
8	13	9	5	16	1467	11	12		711	756	48.47	51.53
8	23	9	1	15	1465	10.98	13		721	744	49.22	50.78
6	26	9	6	15	1463	10.97	14		798	665	54.55	45.45
5	22	9	6	16	1462	10.96	15		714	748	48.84	51.16
7	24	9	6	17	1462	10.96	16		721	741	49.32	50.68
8	9	9	1	17	1458	10.93	17		864	594	59.26	40.74

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	31	9	6	17	1443	10.82	18		709	734	49.13	50.87
5	22	9	6	17	1442	10.81	19		763	679	52.91	47.09
5	22	9	6	18	1440	10.79	20		750	690	52.08	47.92
8	14	9	6	16	1440	10.79	21	13342	767	673	53.26	46.74
8	16	9	1	15	1439	10.79	22		663	776	46.07	53.93
8	9	9	1	15	1436	10.76	23		681	755	47.42	52.58
7	2	9	5	17	1435	10.76	24		781	654	54.43	45.57
6	26	9	6	17	1431	10.73	25		789	642	55.14	44.86
7	5	9	1	17	1430	10.72	26		630	800	44.06	55.94
7	5	9	1	13	1428	10.7	27		526	902	36.83	63.17
8	23	9	1	14	1427	10.7	28		601	826	42.12	57.88
6	19	9	6	17	1424	10.67	29		700	724	49.16	50.84
8	14	9	6	17	1422	10.66	30		703	719	49.44	50.56
8	23	9	1	16	1422	10.66	31		705	717	49.58	50.42
8	9	9	1	14	1419	10.64	32		681	738	47.99	52.01
6	26	9	6	16	1417	10.62	33		746	671	52.65	47.35
8	6	9	5	17	1415	10.61	34		680	735	48.06	51.94
7	24	9	6	16	1410	10.57	35		705	705	50	50
5	22	9	6	15	1405	10.53	36		745	660	53.02	46.98
8	7	9	6	17	1405	10.53	37		733	672	52.17	47.83
6	21	9	1	16	1401	10.5	38		783	618	55.89	44.11
8	7	9	6	15	1400	10.49	39		684	716	48.86	51.14
6	19	9	6	16	1394	10.45	40		690	704	49.5	50.5
7	31	9	6	15	1391	10.43	41	13342	755	636	54.28	45.72
6	5	9	6	16	1390	10.42	42		722	668	51.94	48.06
8	21	9	6	17	1390	10.42	43		698	692	50.22	49.78
7	2	9	5	16	1389	10.41	44		728	661	52.41	47.59
7	24	9	6	15	1388	10.4	45		689	699	49.64	50.36
5	15	9	6	17	1386	10.39	46		712	674	51.37	48.63
5	8	9	6	16	1382	10.36	47		716	666	51.81	48.19
8	13	9	5	17	1382	10.36	48		647	735	46.82	53.18
8	2	9	1	14	1381	10.35	49		602	779	43.59	56.41
5	8	9	6	17	1376	10.31	50		700	676	50.87	49.13
6	26	9	6	18	1375	10.31	51		753	622	54.76	45.24
7	10	9	6	17	1375	10.31	52		699	676	50.84	49.16
7	19	9	1	15	1375	10.31	53		694	681	50.47	49.53
7	31	9	6	18	1373	10.29	54		717	656	52.22	47.78
7	12	9	1	16	1371	10.28	55		684	687	49.89	50.11
7	17	9	6	16	1371	10.28	56		738	633	53.83	46.17
8	16	9	1	13	1371	10.28	57		577	794	42.09	57.91
8	6	9	5	16	1367	10.25	58		601	766	43.96	56.04
6	5	9	6	18	1366	10.24	59		677	689	49.56	50.44
8	21	9	6	15	1365	10.23	60		754	611	55.24	44.76
6	28	9	1	16	1361	10.2	61	13342	666	695	48.93	51.07
7	12	9	1	15	1361	10.2	62		632	729	46.44	53.56
8	9	9	1	13	1361	10.2	63		591	770	43.42	56.58
7	10	9	6	18	1360	10.19	64		704	656	51.76	48.24
7	2	9	5	15	1357	10.17	65		690	667	50.85	49.15
7	17	9	6	14	1356	10.16	66		677	679	49.93	50.07
7	24	9	6	14	1351	10.13	67		681	670	50.41	49.59
5	25	9	2	15	1350	10.12	68		566	784	41.93	58.07
7	10	9	6	16	1350	10.12	69		705	645	52.22	47.78

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	31	9	6	16	1349	10.11	70		713	636	52.85	47.15
6	19	9	6	15	1347	10.1	71		669	678	49.67	50.33
7	12	9	1	14	1343	10.07	72		583	760	43.41	56.59
8	16	9	1	14	1341	10.05	73		648	693	48.32	51.68
5	15	9	6	16	1338	10.03	74		642	696	47.98	52.02
7	17	9	6	15	1335	10.01	75		710	625	53.18	46.82
8	7	9	6	14	1333	9.99	76		640	693	48.01	51.99
6	19	9	6	18	1332	9.98	77		688	644	51.65	48.35
7	31	9	6	14	1331	9.98	78		719	612	54.02	45.98
6	12	9	6	17	1330	9.97	79		704	626	52.93	47.07
8	21	9	6	16	1330	9.97	80		710	620	53.38	46.62
6	26	9	6	14	1325	9.93	81	13342	755	570	56.98	43.02
8	6	9	5	18	1325	9.93	82		628	697	47.4	52.6
6	21	9	1	17	1324	9.92	83		747	577	56.42	43.58
7	3	9	6	12	1323	9.92	84		678	645	51.25	48.75
7	10	9	6	15	1323	9.92	85		684	639	51.7	48.3
7	2	9	5	18	1322	9.91	86		685	637	51.82	48.18
6	14	9	1	15	1321	9.9	87		647	674	48.98	51.02
7	5	9	1	18	1321	9.9	88		687	634	52.01	47.99
7	26	9	1	16	1321	9.9	89		668	653	50.57	49.43
7	30	9	5	17	1320	9.89	90		602	718	45.61	54.39
8	14	9	6	14	1319	9.89	91		699	620	52.99	47.01
8	23	9	1	18	1319	9.89	92		638	681	48.37	51.63
7	30	9	5	16	1318	9.88	93		629	689	47.72	52.28
8	14	9	6	18	1318	9.88	94		700	618	53.11	46.89
6	5	9	6	17	1317	9.87	95		695	622	52.77	47.23
6	12	9	6	16	1315	9.86	96		692	623	52.62	47.38
7	19	9	1	14	1313	9.84	97		594	719	45.24	54.76
5	25	9	2	16	1310	9.82	98		590	720	45.04	54.96
7	26	9	1	15	1308	9.8	99		623	685	47.63	52.37
7	17	9	6	17	1307	9.8	100		691	616	52.87	47.13
8	2	9	1	15	1307	9.8	101	13342	611	696	46.75	53.25
5	10	9	1	18	1305	9.78	102		666	639	51.03	48.97
6	21	9	1	15	1305	9.78	103		665	640	50.96	49.04
5	8	9	6	18	1304	9.77	104		642	662	49.23	50.77
7	19	9	1	16	1303	9.77	105		635	668	48.73	51.27
6	12	9	6	14	1302	9.76	106		681	621	52.3	47.7
5	22	9	6	14	1300	9.74	107		711	589	54.69	45.31
8	7	9	6	13	1297	9.72	108		616	681	47.49	52.51
6	21	9	1	14	1296	9.71	109		621	675	47.92	52.08
7	12	9	1	13	1296	9.71	110		510	786	39.35	60.65
8	14	9	6	12	1296	9.71	111		615	681	47.45	52.55
8	14	9	6	15	1296	9.71	112		670	626	51.7	48.3
8	23	9	1	17	1296	9.71	113		691	605	53.32	46.68
7	10	9	6	14	1292	9.68	114		630	662	48.76	51.24
5	15	9	6	18	1291	9.68	115		622	669	48.18	51.82
8	30	9	1	15	1291	9.68	116		623	668	48.26	51.74
7	26	9	1	17	1290	9.67	117		661	629	51.24	48.76
6	12	9	6	18	1288	9.65	118		644	644	50	50
6	28	9	1	18	1288	9.65	119		620	668	48.14	51.86
7	24	9	6	18	1288	9.65	120		640	648	49.69	50.31
6	12	9	6	15	1286	9.64	121	13342	694	592	53.97	46.03

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	28	9	6	17	1285	9.63	122		628	657	48.87	51.13
7	26	9	1	14	1284	9.62	123		646	638	50.31	49.69
8	7	9	6	18	1284	9.62	124		658	626	51.25	48.75
7	26	9	1	13	1283	9.62	125		595	688	46.38	53.62
8	23	9	1	13	1282	9.61	126		526	756	41.03	58.97
7	3	9	6	14	1280	9.59	127		699	581	54.61	45.39
5	25	9	2	17	1278	9.58	128		638	640	49.92	50.08
6	7	9	1	17	1278	9.58	129		686	592	53.68	46.32
8	7	9	6	12	1278	9.58	130		623	655	48.75	51.25
8	28	9	6	16	1278	9.58	131		666	612	52.11	47.89
12	27	9	1	15	1278	9.58	132		612	666	47.89	52.11
7	19	9	1	13	1277	9.57	133		538	739	42.13	57.87
7	2	9	5	14	1276	9.56	134		697	579	54.62	45.38
7	30	9	5	18	1274	9.55	135		576	698	45.21	54.79
5	3	9	1	16	1272	9.53	136		582	690	45.75	54.25
6	28	9	1	15	1272	9.53	137		627	645	49.29	50.71
6	21	9	1	13	1271	9.53	138		609	662	47.92	52.08
6	28	9	1	14	1271	9.53	139		569	702	44.77	55.23
8	2	9	1	16	1270	9.52	140		616	654	48.5	51.5
8	21	9	6	14	1270	9.52	141	13342	679	591	53.46	46.54
8	6	9	5	15	1267	9.5	142		591	676	46.65	53.35
5	10	9	1	16	1265	9.48	143		638	627	50.43	49.57
5	15	9	6	15	1264	9.47	144		618	646	48.89	51.11
8	2	9	1	13	1264	9.47	145		539	725	42.64	57.36
8	14	9	6	13	1264	9.47	146		595	669	47.07	52.93
8	13	9	5	15	1263	9.47	147		626	637	49.56	50.44
8	20	9	5	17	1263	9.47	148		661	602	52.34	47.66
12	23	9	4	15	1263	9.47	149		600	663	47.51	52.49
6	14	9	1	14	1261	9.45	150		597	664	47.34	52.66
6	14	9	1	16	1261	9.45	151		656	605	52.02	47.98
8	28	9	6	15	1260	9.44	152		646	614	51.27	48.73
6	19	9	6	14	1258	9.43	153		618	640	49.13	50.87
8	9	9	1	12	1254	9.4	154		494	760	39.39	60.61
7	12	9	1	18	1253	9.39	155		677	576	54.03	45.97
5	3	9	1	17	1251	9.38	156		549	702	43.88	56.12
7	6	9	2	17	1251	9.38	157		548	703	43.8	56.2
5	29	9	6	17	1248	9.35	158		625	623	50.08	49.92
8	20	9	5	16	1248	9.35	159		610	638	48.88	51.12
8	21	9	6	13	1248	9.35	160		634	614	50.8	49.2
8	30	9	1	16	1248	9.35	161	13342	621	627	49.76	50.24
7	3	9	6	13	1247	9.35	162		705	542	56.54	43.46
7	16	9	5	15	1245	9.33	163		619	626	49.72	50.28
7	24	9	6	13	1245	9.33	164		590	655	47.39	52.61
6	28	9	1	17	1244	9.32	165		616	628	49.52	50.48
7	31	9	6	12	1244	9.32	166		634	610	50.96	49.04
7	3	9	6	11	1242	9.31	167		684	558	55.07	44.93
7	10	9	6	13	1242	9.31	168		576	666	46.38	53.62
8	21	9	6	12	1242	9.31	169		613	629	49.36	50.64
8	13	9	5	14	1241	9.3	170		574	667	46.25	53.75
8	13	9	5	18	1241	9.3	171		562	679	45.29	54.71
8	16	9	1	19	1241	9.3	172		695	546	56	44
8	9	9	1	19	1240	9.29	173		725	515	58.47	41.53

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	14	9	6	11	1240	9.29	174		617	623	49.76	50.24
12	18	9	6	16	1240	9.29	175		573	667	46.21	53.79
8	21	9	6	18	1238	9.28	176		654	584	52.83	47.17
6	5	9	6	15	1237	9.27	177		649	588	52.47	47.53
7	3	9	6	15	1236	9.26	178		667	569	53.96	46.04
5	29	9	6	16	1233	9.24	179		617	616	50.04	49.96
7	6	9	2	15	1233	9.24	180		577	656	46.8	53.2
8	5	9	4	17	1232	9.23	181	13342	581	651	47.16	52.84
5	8	9	6	15	1231	9.23	182		647	584	52.56	47.44
12	23	9	4	16	1230	9.22	183		613	617	49.84	50.16
7	9	9	5	16	1229	9.21	184		590	639	48.01	51.99
7	31	9	6	13	1228	9.2	185		626	602	50.98	49.02
7	12	9	1	17	1227	9.2	186		618	609	50.37	49.63
5	22	9	6	13	1226	9.19	187		658	568	53.67	46.33
5	25	9	2	14	1226	9.19	188		531	695	43.31	56.69
6	7	9	1	14	1226	9.19	189		593	633	48.37	51.63
7	2	9	5	12	1226	9.19	190		646	580	52.69	47.31
5	8	9	6	14	1221	9.15	191		658	563	53.89	46.11
7	19	9	1	12	1221	9.15	192		534	687	43.73	56.27
7	9	9	5	17	1219	9.14	193		598	621	49.06	50.94
7	30	9	5	15	1219	9.14	194		575	644	47.17	52.83
5	22	9	6	19	1218	9.13	195		627	591	51.48	48.52
8	1	9	7	12	1218	9.13	196		596	622	48.93	51.07
6	12	9	6	13	1217	9.12	197		636	581	52.26	47.74
8	10	9	2	16	1217	9.12	198		570	647	46.84	53.16
6	21	9	1	18	1216	9.11	199		703	513	57.81	42.19
7	17	9	6	18	1216	9.11	200		660	556	54.28	45.72

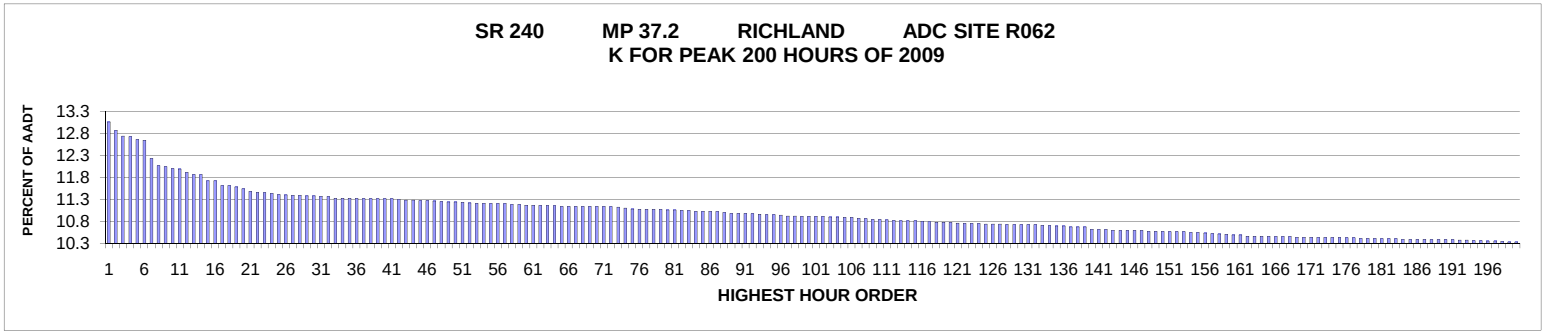

AADT= 64399 **K 30 FACTOR=** 11.38 **K 100 FACTOR=** 10.91 **K 200 FACTOR=** 10.33 **D FACTOR=** 60.2

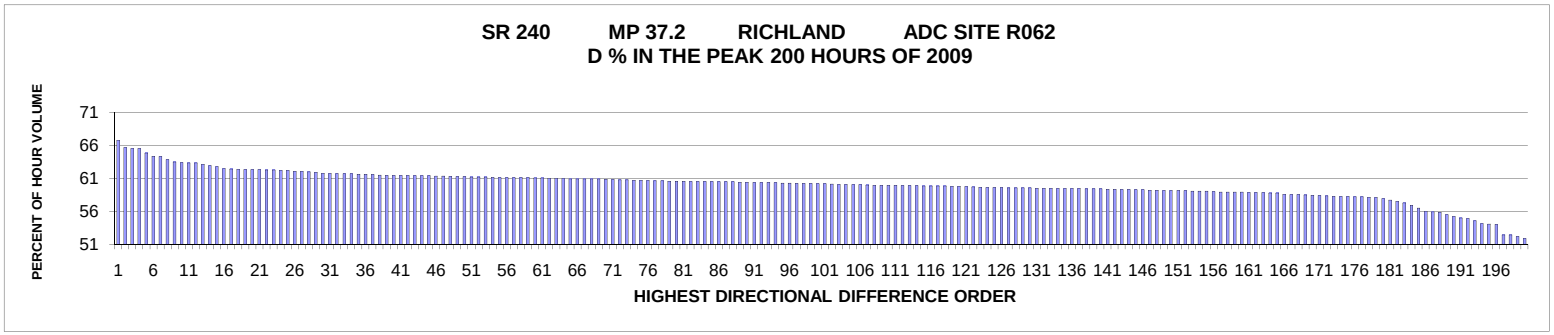

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
10	1	9	5	18	8412	13.06	1	64399	4551	3861	54.1	45.9
9	30	9	4	18	8285	12.87	2		4556	3729	54.99	45.01
9	17	9	5	18	8205	12.74	3		5239	2966	63.85	36.15
9	15	9	3	18	8197	12.73	4		5275	2922	64.35	35.65
9	29	9	3	18	8151	12.66	5		4270	3881	52.39	47.61
9	16	9	4	18	8144	12.65	6		5237	2907	64.31	35.69
9	28	9	2	18	7873	12.23	7		4295	3578	54.55	45.45
9	14	9	2	18	7768	12.06	8		5039	2729	64.87	35.13
10	15	9	5	18	7752	12.04	9		4672	3080	60.27	39.73
10	8	9	5	18	7730	12	10		4792	2938	61.99	38.01
10	1	9	5	17	7720	11.99	11		4282	3438	55.47	44.53
10	7	9	4	18	7679	11.92	12		4703	2976	61.24	38.76
10	6	9	3	18	7642	11.87	13		4692	2950	61.4	38.6
9	22	9	3	18	7636	11.86	14		4716	2920	61.76	38.24
9	17	9	5	17	7550	11.72	15		4948	2602	65.54	34.46
10	28	9	4	18	7547	11.72	16		4437	3110	58.79	41.21
9	29	9	3	17	7477	11.61	17		4104	3373	54.89	45.11

9	30	9	4	17	7474	11.61	18		4127	3347	55.22	44.78
5	20	9	4	18	7460	11.58	19		4443	3017	59.56	40.44
9	1	9	3	18	7430	11.54	20		4504	2926	60.62	39.38
10	21	9	4	18	7393	11.48	21	64399	4537	2856	61.37	38.63
7	15	9	4	18	7383	11.46	22		4417	2966	59.83	40.17
9	10	9	5	18	7376	11.45	23		4504	2872	61.06	38.94
9	16	9	4	17	7369	11.44	24		4840	2529	65.68	34.32
5	27	9	4	18	7351	11.41	25		4255	3096	57.88	42.12
5	28	9	5	18	7339	11.4	26		4264	3075	58.1	41.9
8	25	9	3	18	7337	11.39	27		4466	2871	60.87	39.13
5	19	9	3	18	7333	11.39	28		4349	2984	59.31	40.69
6	25	9	5	18	7331	11.38	29		4106	3225	56.01	43.99
9	8	9	3	18	7331	11.38	30		4388	2943	59.86	40.14
11	3	9	3	18	7323	11.37	31		4496	2827	61.4	38.6
12	17	9	5	18	7318	11.36	32		4429	2889	60.52	39.48
8	17	9	2	18	7299	11.33	33		4394	2905	60.2	39.8
11	10	9	3	18	7294	11.33	34		4457	2837	61.11	38.89
12	22	9	3	17	7294	11.33	35		4261	3033	58.42	41.58
12	9	9	4	18	7287	11.32	36		4427	2860	60.75	39.25
9	15	9	3	17	7286	11.31	37		4866	2420	66.79	33.21
12	2	9	4	18	7286	11.31	38		4409	2877	60.51	39.49
5	14	9	5	18	7285	11.31	39		4308	2977	59.14	40.86
8	24	9	2	18	7284	11.31	40		4401	2883	60.42	39.58
9	23	9	4	18	7283	11.31	41	64399	4350	2933	59.73	40.27
6	3	9	4	18	7278	11.3	42		4394	2884	60.37	39.63
9	9	9	4	18	7267	11.28	43		4395	2872	60.48	39.52
9	2	9	4	18	7266	11.28	44		4411	2855	60.71	39.29
10	14	9	4	18	7259	11.27	45		4360	2899	60.06	39.94
11	12	9	5	18	7259	11.27	46		4306	2953	59.32	40.68
11	19	9	5	18	7249	11.26	47		4315	2934	59.53	40.47
5	26	9	3	18	7247	11.25	48		4273	2974	58.96	41.04
10	27	9	3	18	7238	11.24	49		4401	2837	60.8	39.2
5	21	9	5	18	7237	11.24	50		4304	2933	59.47	40.53
6	9	9	3	18	7230	11.23	51		4377	2853	60.54	39.46
12	1	9	3	18	7226	11.22	52		4328	2898	59.89	40.11
6	10	9	4	18	7219	11.21	53		4450	2769	61.64	38.36
12	10	9	5	18	7217	11.21	54		4251	2966	58.9	41.1
6	30	9	3	18	7212	11.2	55		4222	2990	58.54	41.46
7	14	9	3	18	7212	11.2	56		4316	2896	59.84	40.16
9	21	9	2	18	7211	11.2	57		4393	2818	60.92	39.08
12	4	9	6	17	7203	11.18	58		4254	2949	59.06	40.94
12	7	9	2	18	7203	11.18	59		4402	2801	61.11	38.89
7	16	9	5	18	7194	11.17	60		4199	2995	58.37	41.63
8	20	9	5	18	7193	11.17	61	64399	4185	3008	58.18	41.82
8	26	9	4	18	7184	11.16	62		4429	2755	61.65	38.35
11	4	9	4	18	7184	11.16	63		4329	2855	60.26	39.74
9	28	9	2	17	7183	11.15	64		4058	3125	56.49	43.51
6	16	9	3	18	7176	11.14	65		4393	2783	61.22	38.78
12	3	9	5	18	7176	11.14	66		4409	2767	61.44	38.56
8	19	9	4	18	7175	11.14	67		4289	2886	59.78	40.22
10	2	9	6	17	7174	11.14	68		3416	3758	47.62	52.38
12	8	9	3	18	7173	11.14	69		4295	2878	59.88	40.12
10	15	9	5	17	7172	11.14	70		4547	2625	63.4	36.6
10	20	9	3	18	7171	11.14	71		4319	2852	60.23	39.77
12	18	9	6	17	7168	11.13	72		4235	2933	59.08	40.92
8	31	9	2	18	7164	11.12	73		4369	2795	60.99	39.01
7	8	9	4	18	7150	11.1	74		4253	2897	59.48	40.52

6	8	9	2	18	7136	11.08	75		4348	2788	60.93	39.07
8	18	9	3	18	7128	11.07	76		4240	2888	59.48	40.52
10	22	9	5	18	7128	11.07	77		4238	2890	59.46	40.54
6	2	9	3	18	7126	11.07	78		4346	2780	60.99	39.01
7	30	9	5	18	7126	11.07	79		4211	2915	59.09	40.91
6	18	9	5	18	7125	11.06	80		4151	2974	58.26	41.74
11	18	9	4	18	7121	11.06	81	64399	4323	2798	60.71	39.29
10	29	9	5	18	7119	11.05	82		4188	2931	58.83	41.17
8	27	9	5	18	7118	11.05	83		4345	2773	61.04	38.96
9	3	9	5	18	7106	11.03	84		4188	2918	58.94	41.06
7	22	9	4	18	7105	11.03	85		4156	2949	58.49	41.51
12	21	9	2	18	7105	11.03	86		4242	2863	59.7	40.3
10	13	9	3	18	7098	11.02	87		4286	2812	60.38	39.62
5	27	9	4	17	7081	11	88		4215	2866	59.53	40.47
9	24	9	5	18	7074	10.98	89		4190	2884	59.23	40.77
10	8	9	5	17	7074	10.98	90		4410	2664	62.34	37.66
8	5	9	4	18	7073	10.98	91		4257	2816	60.19	39.81
8	13	9	5	18	7066	10.97	92		4173	2893	59.06	40.94
11	5	9	5	18	7061	10.96	93		4185	2876	59.27	40.73
6	17	9	4	18	7053	10.95	94		4201	2852	59.56	40.44
8	11	9	3	18	7053	10.95	95		4247	2806	60.22	39.78
9	18	9	6	17	7044	10.94	96		4328	2716	61.44	38.56
10	5	9	2	18	7033	10.92	97		4099	2934	58.28	41.72
6	23	9	3	18	7031	10.92	98		4189	2842	59.58	40.42
6	4	9	5	18	7029	10.91	99		4282	2747	60.92	39.08
5	18	9	2	18	7024	10.91	100		4170	2854	59.37	40.63
7	9	9	5	18	7024	10.91	101	64399	4176	2848	59.45	40.55
10	19	9	2	18	7023	10.91	102		4187	2836	59.62	40.38
6	15	9	2	18	7020	10.9	103		4266	2754	60.77	39.23
12	14	9	2	18	7018	10.9	104		4290	2728	61.13	38.87
5	13	9	4	18	7015	10.89	105		4130	2885	58.87	41.13
12	10	9	5	17	7015	10.89	106		4244	2771	60.5	39.5
7	13	9	2	18	6997	10.87	107		4222	2775	60.34	39.66
8	6	9	5	18	6991	10.86	108		4109	2882	58.78	41.22
6	11	9	5	18	6980	10.84	109		3903	3077	55.92	44.08
7	21	9	3	18	6980	10.84	110		4204	2776	60.23	39.77
6	24	9	4	18	6977	10.83	111		4128	2849	59.17	40.83
8	10	9	2	18	6971	10.82	112		4188	2783	60.08	39.92
8	12	9	4	18	6963	10.81	113		4004	2959	57.5	42.5
11	30	9	2	18	6963	10.81	114		4296	2667	61.7	38.3
11	17	9	3	18	6960	10.81	115		4334	2626	62.27	37.73
6	22	9	2	18	6953	10.8	116		4168	2785	59.95	40.05
11	2	9	2	18	6946	10.79	117		4245	2701	61.11	38.89
6	11	9	5	17	6943	10.78	118		3876	3067	55.83	44.17
8	4	9	3	18	6941	10.78	119		4161	2780	59.95	40.05
10	29	9	5	17	6938	10.77	120		4298	2640	61.95	38.05
7	1	9	4	18	6929	10.76	121	64399	4059	2870	58.58	41.42
6	29	9	2	18	6926	10.75	122		4119	2807	59.47	40.53
7	28	9	3	18	6926	10.75	123		4220	2706	60.93	39.07
10	12	9	2	18	6920	10.75	124		4075	2845	58.89	41.11
12	2	9	4	17	6916	10.74	125		4239	2677	61.29	38.71
6	1	9	2	18	6915	10.74	126		4310	2605	62.33	37.67
10	26	9	2	18	6914	10.74	127		4187	2727	60.56	39.44
7	23	9	5	18	6906	10.72	128		4042	2864	58.53	41.47
12	18	9	6	16	6906	10.72	129		4023	2883	58.25	41.75
5	28	9	5	17	6905	10.72	130		4101	2804	59.39	40.61
3	4	9	4	18	6901	10.72	131		4090	2811	59.27	40.73

11	12	9	5	17	6901	10.72	132		4223	2678	61.19	38.81
9	14	9	2	17	6897	10.71	133		4518	2379	65.51	34.49
12	9	9	4	17	6892	10.7	134		4234	2658	61.43	38.57
12	1	9	3	17	6885	10.69	135		4248	2637	61.7	38.3
12	3	9	5	17	6883	10.69	136		4299	2584	62.46	37.54
3	12	9	5	18	6874	10.67	137		4101	2773	59.66	40.34
12	17	9	5	17	6871	10.67	138		4123	2748	60.01	39.99
12	21	9	2	17	6869	10.67	139		3965	2904	57.72	42.28
2	12	9	5	18	6837	10.62	140		4105	2732	60.04	39.96
11	6	9	6	17	6832	10.61	141	64399	4057	2775	59.38	40.62
7	29	9	4	18	6831	10.61	142		4089	2742	59.86	40.14
10	28	9	4	17	6827	10.6	143		4194	2633	61.43	38.57
9	3	9	5	17	6822	10.59	144		4322	2500	63.35	36.65
3	3	9	3	18	6818	10.59	145		4118	2700	60.4	39.6
11	20	9	6	17	6818	10.59	146		4050	2768	59.4	40.6
3	11	9	4	18	6817	10.59	147		4087	2730	59.95	40.05
9	18	9	6	18	6808	10.57	148		3876	2932	56.93	43.07
10	7	9	4	17	6806	10.57	149		4245	2561	62.37	37.63
11	24	9	3	17	6804	10.57	150		4168	2636	61.26	38.74
7	20	9	2	18	6803	10.56	151		4182	2621	61.47	38.53
11	11	9	4	18	6802	10.56	152		4075	2727	59.91	40.09
2	27	9	6	17	6798	10.56	153		4195	2603	61.71	38.29
12	8	9	3	17	6797	10.55	154		4153	2644	61.1	38.9
10	9	9	6	17	6791	10.55	155		4030	2761	59.34	40.66
2	25	9	4	18	6781	10.53	156		3883	2898	57.26	42.74
11	4	9	4	17	6772	10.52	157		4212	2560	62.2	37.8
10	2	9	6	18	6770	10.51	158		3112	3658	45.97	54.03
11	9	9	2	17	6764	10.5	159		4006	2758	59.23	40.77
2	18	9	4	18	6757	10.49	160		3929	2828	58.15	41.85
11	23	9	2	18	6753	10.49	161	64399	4055	2698	60.05	39.95
11	17	9	3	17	6739	10.46	162		4125	2614	61.21	38.79
8	3	9	2	18	6738	10.46	163		4040	2698	59.96	40.04
5	14	9	5	17	6735	10.46	164		4133	2602	61.37	38.63
5	19	9	3	17	6733	10.46	165		4066	2667	60.39	39.61
7	27	9	2	18	6730	10.45	166		4068	2662	60.45	39.55
2	24	9	3	18	6729	10.45	167		3914	2815	58.17	41.83
12	4	9	6	16	6728	10.45	168		4004	2724	59.51	40.49
11	5	9	5	17	6726	10.44	169		4099	2627	60.94	39.06
8	26	9	4	17	6723	10.44	170		4173	2550	62.07	37.93
6	3	9	4	17	6722	10.44	171		4229	2493	62.91	37.09
9	8	9	3	17	6719	10.43	172		4188	2531	62.33	37.67
10	22	9	5	17	6719	10.43	173		4152	2567	61.79	38.21
10	6	9	3	17	6715	10.43	174		4264	2451	63.5	36.5
10	21	9	4	17	6714	10.43	175		4251	2463	63.32	36.68
12	23	9	4	16	6712	10.42	176		3480	3232	51.85	48.15
12	22	9	3	18	6708	10.42	177		3625	3083	54.04	45.96
2	17	9	3	18	6706	10.41	178		4032	2674	60.13	39.87
11	10	9	3	17	6705	10.41	179		4235	2470	63.16	36.84
11	9	9	2	18	6704	10.41	180		3949	2755	58.91	41.09
9	10	9	5	17	6700	10.4	181	64399	4173	2527	62.28	37.72
11	19	9	5	17	6699	10.4	182		4065	2634	60.68	39.32
10	23	9	6	17	6698	10.4	183		4057	2641	60.57	39.43
12	7	9	2	17	6694	10.39	184		4180	2514	62.44	37.56
2	3	9	3	18	6692	10.39	185		3943	2749	58.92	41.08
8	28	9	6	17	6692	10.39	186		4047	2645	60.48	39.52
9	25	9	6	17	6688	10.39	187		3958	2730	59.18	40.82
6	18	9	5	17	6687	10.38	188		4049	2638	60.55	39.45

10	2	9	6	16	6685	10.38	189	3198	3487	47.84	52.16
8	12	9	4	17	6683	10.38	190	3899	2784	58.34	41.66
8	18	9	3	17	6682	10.38	191	4117	2565	61.61	38.39
11	18	9	4	17	6678	10.37	192	4067	2611	60.9	39.1
9	9	9	4	17	6677	10.37	193	4191	2486	62.77	37.23
8	19	9	4	17	6673	10.36	194	4151	2522	62.21	37.79
8	20	9	5	17	6672	10.36	195	4043	2629	60.6	39.4
11	16	9	2	18	6668	10.35	196	4074	2594	61.1	38.9
2	5	9	5	18	6664	10.35	197	3971	2693	59.59	40.41
5	20	9	4	17	6657	10.34	198	3980	2677	59.79	40.21
12	14	9	2	17	6654	10.33	199	4085	2569	61.39	38.61
5	21	9	5	17	6652	10.33	200	4129	2523	62.07	37.93

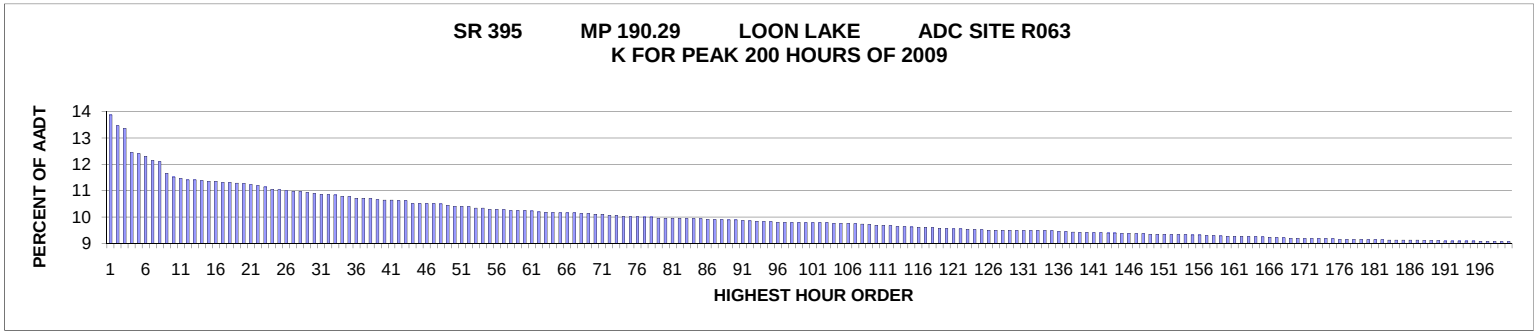

AADT= 8171 **K 30 FACTOR=** 10.89 **K 100 FACTOR=** 9.78 **K 200 FACTOR=** 9.06 **D FACTOR=** 56.63

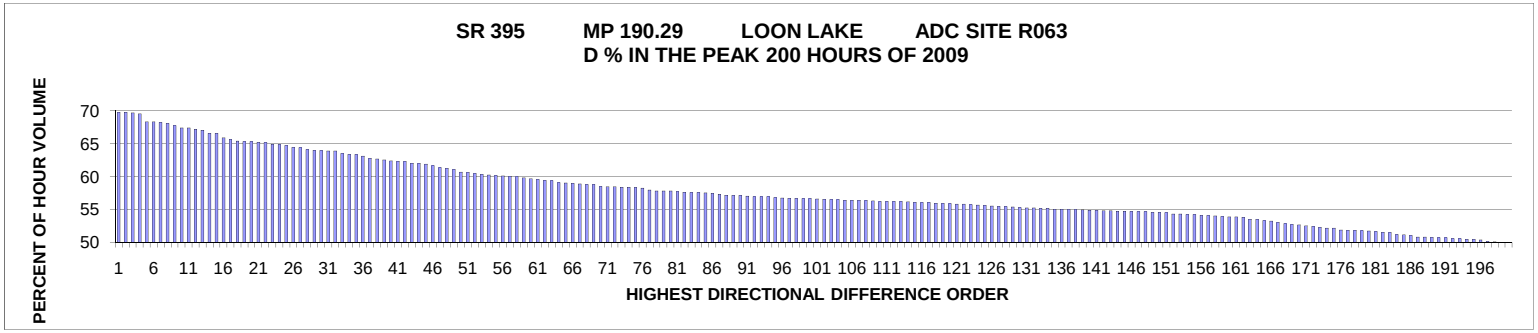

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	3	9	6	14	1133	13.87	1	8171	706	427	62.31	37.69
7	3	9	6	13	1100	13.46	2		688	412	62.55	37.45
7	3	9	6	12	1092	13.36	3		642	450	58.79	41.21
7	3	9	6	16	1017	12.45	4		650	367	63.91	36.09
7	3	9	6	15	1013	12.4	5		683	330	67.42	32.58
7	10	9	6	18	1006	12.31	6		663	343	65.9	34.1
7	4	9	7	12	992	12.14	7		602	390	60.69	39.31
10	16	9	6	17	989	12.1	8		590	399	59.66	40.34
7	4	9	7	13	953	11.66	9		614	339	64.43	35.57
7	2	9	5	16	941	11.52	10		569	372	60.47	39.53
7	11	9	7	13	936	11.46	11		541	395	57.8	42.2
10	9	9	6	18	932	11.41	12		600	332	64.38	35.62
10	16	9	6	18	932	11.41	13		605	327	64.91	35.09
7	11	9	7	14	930	11.38	14		512	418	55.05	44.95
7	5	9	1	13	928	11.36	15		335	593	36.1	63.9
7	17	9	6	17	927	11.35	16		581	346	62.68	37.32
7	10	9	6	17	924	11.31	17		566	358	61.26	38.74

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	1	9	7	13	924	11.31	18		515	409	55.74	44.26
7	10	9	6	15	922	11.28	19		521	401	56.51	43.49
7	5	9	1	15	921	11.27	20		302	619	32.79	67.21
7	10	9	6	16	917	11.22	21	8171	508	409	55.4	44.6
7	3	9	6	17	914	11.19	22		619	295	67.72	32.28
7	11	9	7	12	910	11.14	23		532	378	58.46	41.54
7	2	9	5	18	903	11.05	24		601	302	66.56	33.44
7	31	9	6	17	901	11.03	25		541	360	60.04	39.96
7	3	9	6	11	898	10.99	26		486	412	54.12	45.88
7	5	9	1	14	896	10.97	27		273	623	30.47	69.53
10	9	9	6	17	896	10.97	28		523	373	58.37	41.63
7	10	9	6	19	893	10.93	29		609	284	68.2	31.8
7	31	9	6	18	890	10.89	30		582	308	65.39	34.61
8	1	9	7	12	887	10.86	31		492	395	55.47	44.53
7	5	9	1	16	886	10.84	32		289	597	32.62	67.38
8	1	9	7	14	885	10.83	33		489	396	55.25	44.75
7	4	9	7	14	882	10.79	34		550	332	62.36	37.64
7	17	9	6	16	880	10.77	35		530	350	60.23	39.77
7	12	9	1	14	875	10.71	36		371	504	42.4	57.6
7	24	9	6	16	875	10.71	37		526	349	60.11	39.89
7	17	9	6	18	874	10.7	38		571	303	65.33	34.67
7	25	9	7	12	870	10.65	39		492	378	56.55	43.45
7	2	9	5	15	869	10.64	40		485	384	55.81	44.19
7	2	9	5	17	869	10.64	41	8171	557	312	64.1	35.9
10	9	9	6	16	868	10.62	42		475	393	54.72	45.28
10	16	9	6	16	867	10.61	43		492	375	56.75	43.25
4	3	9	6	17	859	10.51	44		430	429	50.06	49.94
7	18	9	7	13	859	10.51	45		489	370	56.93	43.07
7	18	9	7	14	859	10.51	46		477	382	55.53	44.47
8	7	9	6	16	859	10.51	47		502	357	58.44	41.56
7	3	9	6	18	857	10.49	48		559	298	65.23	34.77
7	11	9	7	17	854	10.45	49		412	442	48.24	51.76
2	27	9	6	17	851	10.41	50		470	381	55.23	44.77
7	31	9	6	16	851	10.41	51		497	354	58.4	41.6
7	5	9	1	12	849	10.39	52		269	580	31.68	68.32
10	2	9	6	16	845	10.34	53		455	390	53.85	46.15
7	26	9	1	13	844	10.33	54		326	518	38.63	61.37
7	10	9	6	14	841	10.29	55		461	380	54.82	45.18
7	24	9	6	18	841	10.29	56		560	281	66.59	33.41
7	12	9	1	13	839	10.27	57		368	471	43.86	56.14
7	2	9	5	14	837	10.24	58		460	377	54.96	45.04
7	24	9	6	17	837	10.24	59		518	319	61.89	38.11
8	14	9	6	18	837	10.24	60		584	253	69.77	30.23
7	10	9	6	13	836	10.23	61	8171	427	409	51.08	48.92
8	2	9	1	14	833	10.19	62		384	449	46.1	53.9
7	25	9	7	13	832	10.18	63		481	351	57.81	42.19
10	2	9	6	18	830	10.16	64		545	285	65.66	34.34
7	1	9	4	16	829	10.15	65		465	364	56.09	43.91
7	17	9	6	15	829	10.15	66		483	346	58.26	41.74
7	31	9	6	15	829	10.15	67		473	356	57.06	42.94
7	11	9	7	16	828	10.13	68		429	399	51.81	48.19
8	8	9	7	12	828	10.13	69		418	410	50.48	49.52

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	18	9	7	12	826	10.11	70		468	358	56.66	43.34
7	5	9	1	17	825	10.1	71		286	539	34.67	65.33
7	12	9	1	15	821	10.05	72		373	448	45.43	54.57
7	26	9	1	14	821	10.05	73		360	461	43.85	56.15
7	19	9	1	13	819	10.02	74		400	419	48.84	51.16
3	13	9	6	17	818	10.01	75		460	358	56.23	43.77
4	10	9	6	17	818	10.01	76		486	332	59.41	40.59
7	24	9	6	15	817	10	77		451	366	55.2	44.8
7	24	9	6	14	816	9.99	78		423	393	51.84	48.16
7	1	9	4	17	813	9.95	79		457	356	56.21	43.79
7	17	9	6	12	813	9.95	80		366	447	45.02	54.98
8	9	9	1	16	813	9.95	81	8171	375	438	46.13	53.87
10	21	9	4	17	813	9.95	82		427	386	52.52	47.48
8	9	9	1	14	812	9.94	83		369	443	45.44	54.56
4	3	9	6	16	811	9.93	84		390	421	48.09	51.91
8	7	9	6	17	811	9.93	85		503	308	62.02	37.98
4	3	9	6	18	810	9.91	86		449	361	55.43	44.57
7	16	9	5	17	809	9.9	87		467	342	57.73	42.27
11	6	9	6	17	809	9.9	88		469	340	57.97	42.03
8	7	9	6	18	808	9.89	89		564	244	69.8	30.2
10	2	9	6	17	808	9.89	90		475	333	58.79	41.21
7	4	9	7	11	806	9.86	91		480	326	59.55	40.45
7	6	9	2	13	805	9.85	92		341	464	42.36	57.64
10	23	9	6	17	804	9.84	93		465	339	57.84	42.16
8	2	9	1	13	803	9.83	94		369	434	45.95	54.05
7	17	9	6	14	802	9.82	95		429	373	53.49	46.51
7	11	9	7	11	801	9.8	96		456	345	56.93	43.07
7	24	9	6	12	801	9.8	97		346	455	43.2	56.8
7	9	9	5	17	800	9.79	98		460	340	57.5	42.5
7	11	9	7	15	800	9.79	99		403	397	50.38	49.63
7	7	9	3	17	799	9.78	100		440	359	55.07	44.93
7	11	9	7	10	798	9.77	101	8171	484	314	60.65	39.35
7	17	9	6	19	798	9.77	102		545	253	68.3	31.7
8	2	9	1	16	798	9.77	103		362	436	45.36	54.64
7	10	9	6	12	797	9.75	104		411	386	51.57	48.43
7	21	9	3	17	797	9.75	105		470	327	58.97	41.03
7	24	9	6	11	797	9.75	106		374	423	46.93	53.07
1	30	9	6	17	796	9.74	107		437	359	54.9	45.1
8	2	9	1	17	795	9.73	108		379	416	47.67	52.33
7	26	9	1	17	794	9.72	109		347	447	43.7	56.3
7	2	9	5	13	791	9.68	110		402	389	50.82	49.18
7	8	9	4	17	791	9.68	111		473	318	59.8	40.2
3	27	9	6	16	790	9.67	112		414	376	52.41	47.59
10	9	9	6	15	787	9.63	113		440	347	55.91	44.09
10	16	9	6	15	787	9.63	114		465	322	59.09	40.91
10	16	9	6	19	786	9.62	115		527	259	67.05	32.95
7	2	9	5	19	785	9.61	116		547	238	69.68	30.32
7	20	9	2	17	785	9.61	117		447	338	56.94	43.06
11	6	9	6	18	784	9.59	118		511	273	65.18	34.82
7	19	9	1	15	782	9.57	119		378	404	48.34	51.66
3	27	9	6	17	781	9.56	120		461	320	59.03	40.97
7	11	9	7	18	780	9.55	121	8171	407	373	52.18	47.82

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
10	15	9	5	17	780	9.55	122		427	353	54.74	45.26
7	25	9	7	16	779	9.53	123		448	331	57.51	42.49
12	4	9	6	17	778	9.52	124		441	337	56.68	43.32
7	31	9	6	19	777	9.51	125		529	248	68.08	31.92
7	5	9	1	18	776	9.5	126		283	493	36.47	63.53
7	12	9	1	17	776	9.5	127		323	453	41.62	58.38
7	19	9	1	14	776	9.5	128		371	405	47.81	52.19
8	1	9	7	16	776	9.5	129		409	367	52.71	47.29
3	13	9	6	16	775	9.48	130		388	387	50.06	49.94
3	13	9	6	18	775	9.48	131		489	286	63.1	36.9
7	9	9	5	16	775	9.48	132		431	344	55.61	44.39
7	31	9	6	13	775	9.48	133		399	376	51.48	48.52
8	1	9	7	11	775	9.48	134		383	392	49.42	50.58
7	25	9	7	11	774	9.47	135		381	393	49.22	50.78
7	30	9	5	18	772	9.45	136		479	293	62.05	37.95
8	1	9	7	17	771	9.44	137		380	391	49.29	50.71
3	20	9	6	17	770	9.42	138		434	336	56.36	43.64
2	20	9	6	17	769	9.41	139		389	380	50.59	49.41
8	2	9	1	15	769	9.41	140		346	423	44.99	55.01
7	25	9	7	14	768	9.4	141	8171	434	334	56.51	43.49
8	9	9	1	13	768	9.4	142		329	439	42.84	57.16
7	1	9	4	15	767	9.39	143		389	378	50.72	49.28
11	20	9	6	16	767	9.39	144		424	343	55.28	44.72
7	6	9	2	12	766	9.37	145		269	497	35.12	64.88
10	30	9	6	16	766	9.37	146		432	334	56.4	43.6
2	13	9	6	17	765	9.36	147		459	306	60	40
7	18	9	7	11	765	9.36	148		403	362	52.68	47.32
7	24	9	6	19	763	9.34	149		466	297	61.07	38.93
8	1	9	7	15	763	9.34	150		432	331	56.62	43.38
8	6	9	5	17	763	9.34	151		427	336	55.96	44.04
2	16	9	2	17	762	9.33	152		412	350	54.07	45.93
4	10	9	6	16	762	9.33	153		414	348	54.33	45.67
11	6	9	6	16	762	9.33	154		411	351	53.94	46.06
7	6	9	2	17	761	9.31	155		445	316	58.48	41.52
10	22	9	5	17	761	9.31	156		415	346	54.53	45.47
7	15	9	4	17	759	9.29	157		415	344	54.68	45.32
7	31	9	6	14	759	9.29	158		383	376	50.46	49.54
7	17	9	6	13	758	9.28	159		393	365	51.85	48.15
7	1	9	4	18	757	9.26	160		490	267	64.73	35.27
7	14	9	3	17	757	9.26	161	8171	436	321	57.6	42.4
8	14	9	6	16	757	9.26	162		484	273	63.94	36.06
7	18	9	7	15	756	9.25	163		425	331	56.22	43.78
7	26	9	1	15	756	9.25	164		332	424	43.92	56.08
7	4	9	7	15	755	9.24	165		483	272	63.97	36.03
10	7	9	4	17	754	9.23	166		427	327	56.63	43.37
7	6	9	2	11	753	9.22	167		276	477	36.65	63.35
10	1	9	5	17	752	9.2	168		412	340	54.79	45.21
8	15	9	7	12	751	9.19	169		349	402	46.47	53.53
8	15	9	7	14	751	9.19	170		376	375	50.07	49.93
1	17	9	7	16	750	9.18	171		468	282	62.4	37.6
3	6	9	6	17	750	9.18	172		419	331	55.87	44.13
7	25	9	7	15	750	9.18	173		423	327	56.4	43.6

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	26	9	1	12	750	9.18	174		299	451	39.87	60.13
7	25	9	7	17	749	9.17	175		396	353	52.87	47.13
11	25	9	4	16	748	9.15	176		424	324	56.68	43.32
7	19	9	1	16	747	9.14	177		278	469	37.22	62.78
8	15	9	7	17	747	9.14	178		405	342	54.22	45.78
10	11	9	1	16	747	9.14	179		296	451	39.63	60.37
4	3	9	6	15	746	9.13	180		382	364	51.21	48.79
12	24	9	5	16	746	9.13	181	8171	460	286	61.66	38.34
12	26	9	7	16	746	9.13	182		421	325	56.43	43.57
7	26	9	1	18	745	9.12	183		319	426	42.82	57.18
8	7	9	6	15	745	9.12	184		404	341	54.23	45.77
10	9	9	6	14	745	9.12	185		408	337	54.77	45.23
10	9	9	6	19	745	9.12	186		472	273	63.36	36.64
11	20	9	6	17	745	9.12	187		397	348	53.29	46.71
7	10	9	6	11	744	9.11	188		340	404	45.7	54.3
10	9	9	6	12	744	9.11	189		371	373	49.87	50.13
11	10	9	3	17	744	9.11	190		408	336	54.84	45.16
7	1	9	4	12	742	9.08	191		347	395	46.77	53.23
7	1	9	4	14	742	9.08	192		377	365	50.81	49.19
7	19	9	1	18	742	9.08	193		318	424	42.86	57.14
7	23	9	5	18	742	9.08	194		437	305	58.89	41.11
8	8	9	7	14	742	9.08	195		417	325	56.2	43.8
7	9	9	5	18	741	9.07	196		440	301	59.38	40.62
7	14	9	3	16	741	9.07	197		409	332	55.2	44.8
7	26	9	1	16	741	9.07	198		316	425	42.65	57.35
7	6	9	2	14	740	9.06	199		327	413	44.19	55.81
7	12	9	1	16	740	9.06	200		328	412	44.32	55.68

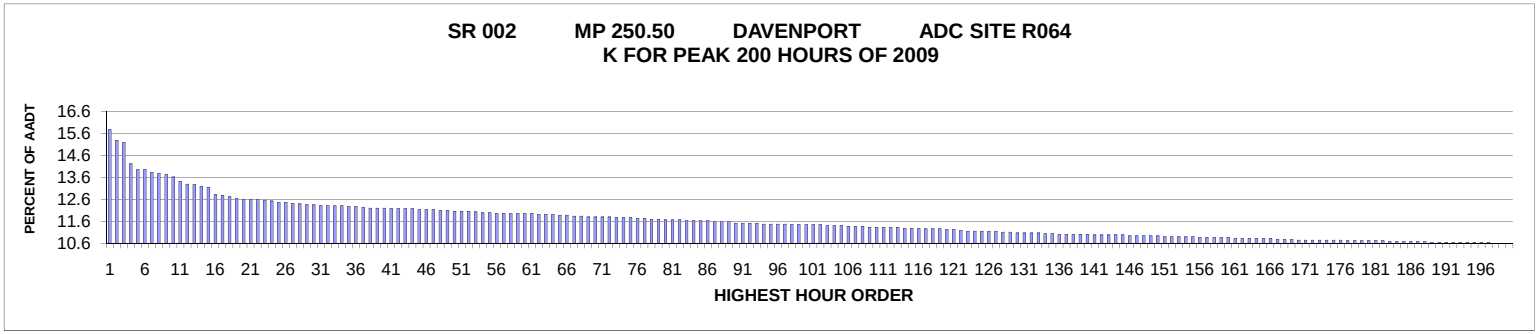

AADT= 2745 **K 30 FACTOR=** 12.35 **K 100 FACTOR=** 11.44 **K 200 FACTOR=** 10.6 **D FACTOR=** 55.22

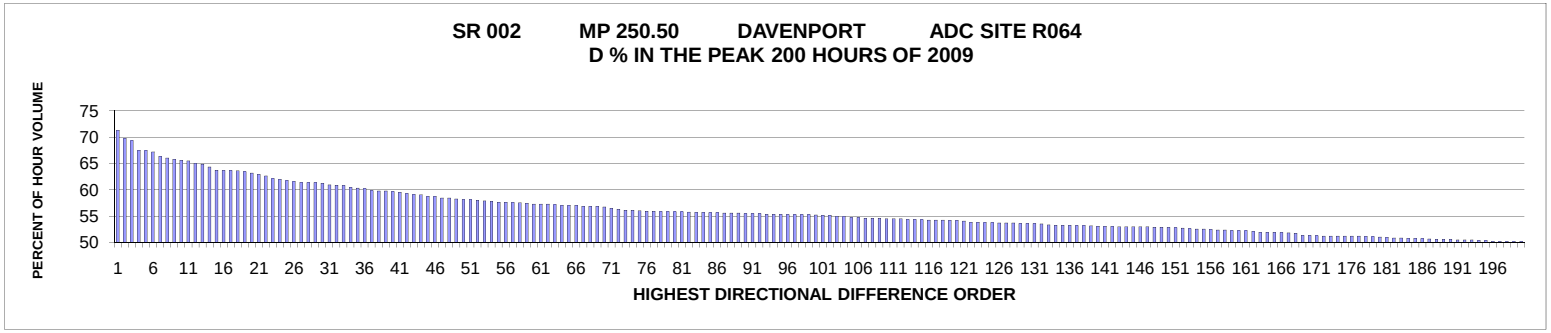

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
10	4	9	1	15	433	15.77	1	2745	192	241	44.34	55.66
5	22	9	6	18	420	15.3	2		127	293	30.24	69.76
10	4	9	1	16	417	15.19	3		193	224	46.28	53.72
10	4	9	1	17	390	14.21	4		194	196	49.74	50.26
5	22	9	6	16	383	13.95	5		154	229	40.21	59.79
8	7	9	6	15	383	13.95	6		154	229	40.21	59.79
7	5	9	1	15	380	13.84	7		241	139	63.42	36.58
5	25	9	2	16	378	13.77	8		262	116	69.31	30.69
8	7	9	6	16	377	13.73	9		170	207	45.09	54.91
5	22	9	6	17	374	13.62	10		126	248	33.69	66.31
6	19	9	6	16	368	13.41	11		154	214	41.85	58.15
6	26	9	6	16	365	13.3	12		209	156	57.26	42.74
7	5	9	1	14	364	13.26	13		220	144	60.44	39.56
7	17	9	6	15	362	13.19	14		144	218	39.78	60.22
7	3	9	6	12	361	13.15	15		172	189	47.65	52.35
5	22	9	6	15	352	12.82	16		138	214	39.2	60.8
7	5	9	1	13	351	12.79	17		215	136	61.25	38.75

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
5	23	9	7	11	349	12.71	18		143	206	40.97	59.03
5	22	9	6	14	347	12.64	19		142	205	40.92	59.08
5	25	9	2	15	346	12.6	20		227	119	65.61	34.39
7	3	9	6	14	346	12.6	21	2745	131	215	37.86	62.14
10	4	9	1	18	346	12.6	22		193	153	55.78	44.22
6	28	9	1	16	345	12.57	23		158	187	45.8	54.2
8	7	9	6	17	344	12.53	24		133	211	38.66	61.34
6	5	9	6	16	342	12.46	25		165	177	48.25	51.75
8	7	9	6	14	342	12.46	26		163	179	47.66	52.34
8	27	9	5	16	341	12.42	27		190	151	55.72	44.28
7	31	9	6	15	340	12.39	28		166	174	48.82	51.18
8	7	9	6	18	339	12.35	29		144	195	42.48	57.52
9	4	9	6	18	339	12.35	30		152	187	44.84	55.16
7	19	9	1	13	338	12.31	31		180	158	53.25	46.75
7	19	9	1	14	338	12.31	32		180	158	53.25	46.75
8	28	9	6	17	338	12.31	33		159	179	47.04	52.96
10	9	9	6	16	338	12.31	34		153	185	45.27	54.73
7	17	9	6	14	337	12.28	35		154	183	45.7	54.3
7	26	9	1	15	337	12.28	36		178	159	52.82	47.18
7	12	9	1	15	336	12.24	37		170	166	50.6	49.4
7	24	9	6	15	335	12.2	38		160	175	47.76	52.24
7	24	9	6	18	335	12.2	39		157	178	46.87	53.13
8	29	9	7	13	335	12.2	40		191	144	57.01	42.99
8	7	9	6	11	334	12.17	41	2745	157	177	47.01	52.99
8	9	9	1	13	334	12.17	42		182	152	54.49	45.51
8	9	9	1	14	334	12.17	43		177	157	52.99	47.01
8	30	9	1	16	334	12.17	44		187	147	55.99	44.01
6	12	9	6	17	333	12.13	45		148	185	44.44	55.56
7	31	9	6	17	333	12.13	46		164	169	49.25	50.75
11	25	9	4	16	333	12.13	47		163	170	48.95	51.05
7	17	9	6	17	332	12.09	48		139	193	41.87	58.13
10	9	9	6	14	332	12.09	49		162	170	48.8	51.2
6	28	9	1	17	331	12.06	50		153	178	46.22	53.78
7	26	9	1	16	331	12.06	51		180	151	54.38	45.62
10	9	9	6	18	331	12.06	52		147	184	44.41	55.59
5	25	9	2	17	330	12.02	53		210	120	63.64	36.36
6	12	9	6	15	329	11.99	54		165	164	50.15	49.85
9	11	9	6	16	329	11.99	55		142	187	43.16	56.84
6	26	9	6	14	328	11.95	56		189	139	57.62	42.38
6	26	9	6	15	328	11.95	57		154	174	46.95	53.05
7	3	9	6	13	328	11.95	58		144	184	43.9	56.1
7	16	9	5	15	328	11.95	59		162	166	49.39	50.61
7	17	9	6	13	328	11.95	60		146	182	44.51	55.49
7	19	9	1	15	328	11.95	61	2745	171	157	52.13	47.87
6	26	9	6	17	327	11.91	62		164	163	50.15	49.85
8	28	9	6	16	327	11.91	63		136	191	41.59	58.41
10	16	9	6	16	327	11.91	64		125	202	38.23	61.77
5	8	9	6	16	326	11.88	65		140	186	42.94	57.06
5	22	9	6	19	326	11.88	66		106	220	32.52	67.48
7	26	9	1	14	325	11.84	67		159	166	48.92	51.08
8	8	9	7	11	325	11.84	68		153	172	47.08	52.92
5	25	9	2	18	324	11.8	69		231	93	71.3	28.7

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	3	9	6	11	324	11.8	70		132	192	40.74	59.26
7	3	9	6	15	324	11.8	71		143	181	44.14	55.86
10	9	9	6	15	324	11.8	72		143	181	44.14	55.86
7	5	9	1	17	323	11.77	73		210	113	65.02	34.98
7	12	9	1	14	323	11.77	74		164	159	50.77	49.23
7	17	9	6	12	323	11.77	75		159	164	49.23	50.77
7	24	9	6	14	322	11.73	76		159	163	49.38	50.62
7	31	9	6	16	322	11.73	77		153	169	47.52	52.48
8	9	9	1	15	321	11.69	78		185	136	57.63	42.37
8	9	9	1	18	321	11.69	79		201	120	62.62	37.38
7	24	9	6	16	320	11.66	80		141	179	44.06	55.94
8	1	9	7	12	320	11.66	81	2745	177	143	55.31	44.69
9	18	9	6	16	320	11.66	82		143	177	44.69	55.31
5	15	9	6	18	319	11.62	83		146	173	45.77	54.23
6	12	9	6	16	319	11.62	84		160	159	50.16	49.84
8	29	9	7	12	319	11.62	85		178	141	55.8	44.2
8	30	9	1	15	319	11.62	86		173	146	54.23	45.77
5	23	9	7	12	318	11.58	87		153	165	48.11	51.89
7	25	9	7	12	318	11.58	88		177	141	55.66	44.34
9	7	9	2	13	318	11.58	89		178	140	55.97	44.03
7	2	9	5	16	316	11.51	90		127	189	40.19	59.81
8	9	9	1	17	316	11.51	91		181	135	57.28	42.72
8	30	9	1	17	316	11.51	92		165	151	52.22	47.78
10	2	9	6	17	316	11.51	93		150	166	47.47	52.53
9	4	9	6	16	315	11.48	94		136	179	43.17	56.83
9	4	9	6	19	315	11.48	95		121	194	38.41	61.59
9	7	9	2	14	315	11.48	96		188	127	59.68	40.32
9	7	9	2	15	315	11.48	97		168	147	53.33	46.67
7	10	9	6	14	314	11.44	98		151	163	48.09	51.91
7	19	9	1	16	314	11.44	99		169	145	53.82	46.18
8	29	9	7	14	314	11.44	100		175	139	55.73	44.27
9	5	9	7	11	314	11.44	101	2745	161	153	51.27	48.73
10	16	9	6	17	314	11.44	102		114	200	36.31	63.69
7	10	9	6	13	313	11.4	103		165	148	52.72	47.28
7	10	9	6	17	313	11.4	104		121	192	38.66	61.34
9	18	9	6	18	313	11.4	105		140	173	44.73	55.27
7	5	9	1	16	312	11.37	106		206	106	66.03	33.97
7	24	9	6	13	312	11.37	107		150	162	48.08	51.92
9	4	9	6	17	312	11.37	108		145	167	46.47	53.53
6	18	9	5	16	311	11.33	109		154	157	49.52	50.48
6	21	9	1	14	311	11.33	110		191	120	61.41	38.59
7	2	9	5	17	311	11.33	111		111	200	35.69	64.31
7	9	9	5	15	311	11.33	112		169	142	54.34	45.66
9	25	9	6	17	311	11.33	113		102	209	32.8	67.2
8	7	9	6	13	310	11.29	114		138	172	44.52	55.48
8	9	9	1	16	310	11.29	115		203	107	65.48	34.52
6	19	9	6	15	309	11.26	116		135	174	43.69	56.31
6	28	9	1	14	309	11.26	117		132	177	42.72	57.28
7	17	9	6	18	309	11.26	118		129	180	41.75	58.25
9	25	9	6	16	309	11.26	119		131	178	42.39	57.61
8	30	9	1	13	308	11.22	120		160	148	51.95	48.05
9	7	9	2	12	308	11.22	121	2745	163	145	52.92	47.08

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	31	9	6	12	307	11.18	122		162	145	52.77	47.23
4	17	9	6	18	306	11.15	123		132	174	43.14	56.86
7	31	9	6	14	306	11.15	124		164	142	53.59	46.41
8	7	9	6	12	306	11.15	125		140	166	45.75	54.25
8	27	9	5	14	306	11.15	126		139	167	45.42	54.58
11	25	9	4	15	306	11.15	127		142	164	46.41	53.59
6	19	9	6	14	305	11.11	128		132	173	43.28	56.72
6	21	9	1	13	305	11.11	129		194	111	63.61	36.39
5	29	9	6	17	304	11.07	130		144	160	47.37	52.63
7	19	9	1	17	304	11.07	131		192	112	63.16	36.84
7	31	9	6	13	304	11.07	132		162	142	53.29	46.71
8	9	9	1	19	304	11.07	133		205	99	67.43	32.57
7	30	9	5	14	303	11.04	134		146	157	48.18	51.82
8	28	9	6	12	303	11.04	135		148	155	48.84	51.16
6	12	9	6	18	302	11	136		148	154	49.01	50.99
7	16	9	5	14	302	11	137		160	142	52.98	47.02
7	18	9	7	11	302	11	138		167	135	55.3	44.7
9	25	9	6	15	302	11	139		153	149	50.66	49.34
10	9	9	6	17	302	11	140		142	160	47.02	52.98
5	25	9	2	12	301	10.97	141	2745	164	137	54.49	45.51
6	28	9	1	18	301	10.97	142		139	162	46.18	53.82
7	12	9	1	13	301	10.97	143		164	137	54.49	45.51
8	8	9	7	13	301	10.97	144		152	149	50.5	49.5
8	28	9	6	18	301	10.97	145		153	148	50.83	49.17
4	10	9	6	17	300	10.93	146		114	186	38	62
6	28	9	1	15	300	10.93	147		146	154	48.67	51.33
7	18	9	7	12	300	10.93	148		134	166	44.67	55.33
7	30	9	5	16	300	10.93	149		149	151	49.67	50.33
11	25	9	4	17	300	10.93	150		135	165	45	55
6	26	9	6	18	299	10.89	151		151	148	50.5	49.5
7	16	9	5	11	299	10.89	152		152	147	50.84	49.16
9	18	9	6	17	299	10.89	153		117	182	39.13	60.87
9	25	9	6	18	299	10.89	154		121	178	40.47	59.53
10	16	9	6	18	299	10.89	155		134	165	44.82	55.18
6	25	9	5	17	298	10.86	156		123	175	41.28	58.72
7	5	9	1	12	298	10.86	157		175	123	58.72	41.28
7	19	9	1	18	298	10.86	158		196	102	65.77	34.23
8	2	9	1	17	298	10.86	159		160	138	53.69	46.31
8	6	9	5	12	298	10.86	160		128	170	42.95	57.05
4	24	9	6	18	297	10.82	161	2745	149	148	50.17	49.83
5	15	9	6	17	297	10.82	162		136	161	45.79	54.21
5	22	9	6	12	297	10.82	163		133	164	44.78	55.22
6	12	9	6	14	297	10.82	164		139	158	46.8	53.2
8	28	9	6	19	297	10.82	165		158	139	53.2	46.8
10	11	9	1	17	297	10.82	166		181	116	60.94	39.06
6	28	9	1	13	296	10.78	167		134	162	45.27	54.73
7	24	9	6	12	296	10.78	168		144	152	48.65	51.35
7	25	9	7	14	296	10.78	169		159	137	53.72	46.28
6	26	9	6	12	295	10.75	170		161	134	54.58	45.42
7	3	9	6	16	295	10.75	171		131	164	44.41	55.59
7	6	9	2	15	295	10.75	172		155	140	52.54	47.46
7	25	9	7	13	295	10.75	173		151	144	51.19	48.81

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
9	11	9	6	18	295	10.75	174		132	163	44.75	55.25
10	4	9	1	14	295	10.75	175		134	161	45.42	54.58
10	16	9	6	14	295	10.75	176		117	178	39.66	60.34
5	8	9	6	17	294	10.71	177		109	185	37.07	62.93
6	21	9	1	15	294	10.71	178		169	125	57.48	42.52
7	2	9	5	15	294	10.71	179		126	168	42.86	57.14
7	17	9	6	16	294	10.71	180		135	159	45.92	54.08
9	7	9	2	16	294	10.71	181	2745	170	124	57.82	42.18
10	9	9	6	11	294	10.71	182		129	165	43.88	56.12
6	5	9	6	17	293	10.67	183		123	170	41.98	58.02
7	10	9	6	12	293	10.67	184		162	131	55.29	44.71
7	10	9	6	15	293	10.67	185		143	150	48.81	51.19
7	24	9	6	11	293	10.67	186		136	157	46.42	53.58
8	28	9	6	13	293	10.67	187		153	140	52.22	47.78
10	11	9	1	16	293	10.67	188		190	103	64.85	35.15
4	24	9	6	17	292	10.64	189		147	145	50.34	49.66
5	10	9	1	17	292	10.64	190		155	137	53.08	46.92
5	23	9	7	13	292	10.64	191		123	169	42.12	57.88
6	5	9	6	18	292	10.64	192		135	157	46.23	53.77
7	16	9	5	12	292	10.64	193		137	155	46.92	53.08
7	26	9	1	17	292	10.64	194		186	106	63.7	36.3
8	3	9	2	12	292	10.64	195		163	129	55.82	44.18
8	8	9	7	12	292	10.64	196		130	162	44.52	55.48
10	2	9	6	15	292	10.64	197		127	165	43.49	56.51
7	2	9	5	12	291	10.6	198		142	149	48.8	51.2
7	24	9	6	17	291	10.6	199		121	170	41.58	58.42
8	2	9	1	13	291	10.6	200		149	142	51.2	48.8

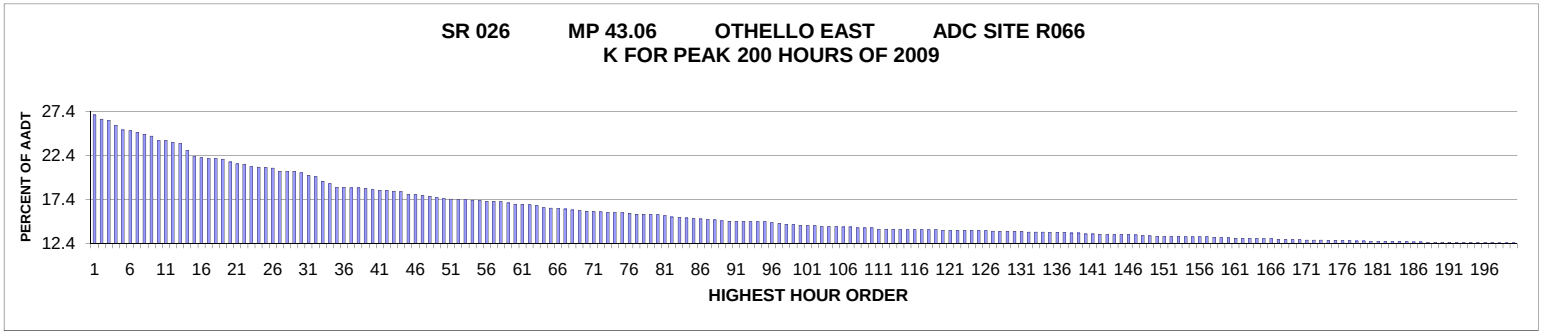

AADT= 2576 **K 30 FACTOR=** 20.42 **K 100 FACTOR=** 14.44 **K 200 FACTOR=** 12.42 **D FACTOR=** 62.65

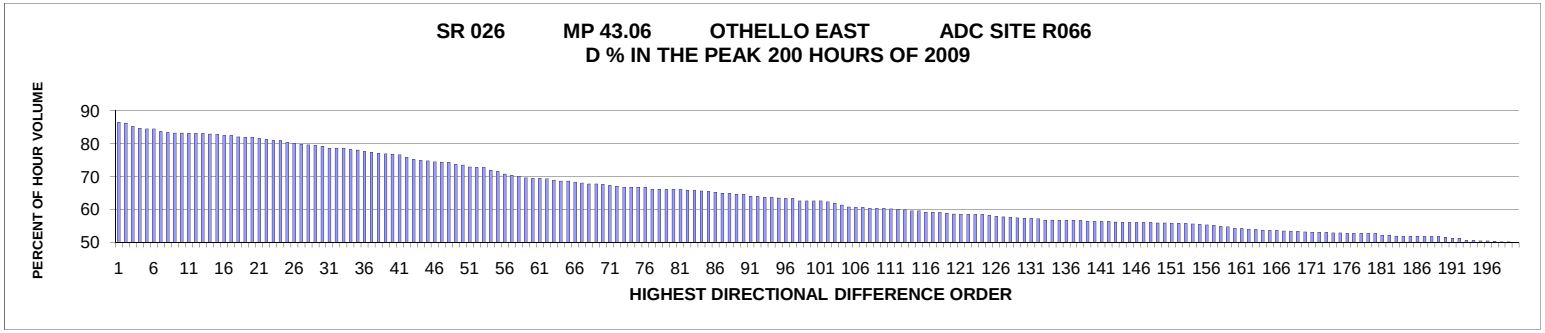

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
10	4	9	1	14	696	27.02	1	2576	222	474	31.9	68.1
10	4	9	1	17	684	26.55	2		338	346	49.42	50.58
4	5	9	1	15	680	26.4	3		122	558	17.94	82.06
3	22	9	1	16	666	25.85	4		552	114	82.88	17.12
3	22	9	1	17	652	25.31	5		545	107	83.59	16.41
10	4	9	1	16	650	25.23	6		281	369	43.23	56.77
10	4	9	1	18	645	25.04	7		392	253	60.78	39.22
5	8	9	6	15	639	24.81	8		429	210	67.14	32.86
5	8	9	6	16	634	24.61	9		382	252	60.25	39.75
4	3	9	6	16	621	24.11	10		452	169	72.79	27.21
10	4	9	1	19	621	24.11	11		356	265	57.33	42.67
4	5	9	1	16	615	23.87	12		139	476	22.6	77.4
5	8	9	6	17	612	23.76	13		343	269	56.05	43.95
9	4	9	6	17	592	22.98	14		223	369	37.67	62.33
4	5	9	1	14	574	22.28	15		89	485	15.51	84.49
3	22	9	1	18	570	22.13	16		483	87	84.74	15.26
4	3	9	6	14	568	22.05	17		456	112	80.28	19.72

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
10	4	9	1	15	568	22.05	18		255	313	44.89	55.11
9	11	9	6	18	566	21.97	19		121	445	21.38	78.62
3	13	9	6	16	558	21.66	20		94	464	16.85	83.15
3	13	9	6	17	552	21.43	21	2576	103	449	18.66	81.34
4	3	9	6	15	551	21.39	22		438	113	79.49	20.51
9	4	9	6	18	544	21.12	23		185	359	34.01	65.99
5	8	9	6	19	543	21.08	24		281	262	51.75	48.25
5	8	9	6	18	542	21.04	25		238	304	43.91	56.09
3	13	9	6	15	540	20.96	26		90	450	16.67	83.33
5	8	9	6	14	531	20.61	27		366	165	68.93	31.07
9	11	9	6	17	531	20.61	28		128	403	24.11	75.89
10	4	9	1	13	531	20.61	29		134	397	25.24	74.76
3	22	9	1	15	526	20.42	30		414	112	78.71	21.29
4	3	9	6	17	518	20.11	31		336	182	64.86	35.14
3	13	9	6	18	515	19.99	32		88	427	17.09	82.91
5	10	9	1	15	501	19.45	33		88	413	17.56	82.44
5	10	9	1	14	494	19.18	34		84	410	17	83
4	5	9	1	13	484	18.79	35		75	409	15.5	84.5
12	18	9	6	15	484	18.79	36		81	403	16.74	83.26
3	22	9	1	14	482	18.71	37		386	96	80.08	19.92
10	9	9	6	18	482	18.71	38		247	235	51.24	48.76
5	9	9	7	15	480	18.63	39		84	396	17.5	82.5
12	18	9	6	14	476	18.48	40		97	379	20.38	79.62
9	13	9	1	17	475	18.44	41	2576	371	104	78.11	21.89
5	10	9	1	13	474	18.4	42		80	394	16.88	83.12
9	4	9	6	15	472	18.32	43		200	272	42.37	57.63
9	4	9	6	19	471	18.28	44		152	319	32.27	67.73
10	9	9	6	17	463	17.97	45		276	187	59.61	40.39
3	13	9	6	14	462	17.93	46		107	355	23.16	76.84
5	9	9	7	16	459	17.82	47		63	396	13.73	86.27
9	11	9	6	16	457	17.74	48		124	333	27.13	72.87
4	3	9	6	13	454	17.62	49		349	105	76.87	23.13
9	4	9	6	16	451	17.51	50		195	256	43.24	56.76
9	7	9	2	18	449	17.43	51		285	164	63.47	36.53
4	5	9	1	17	448	17.39	52		131	317	29.24	70.76
5	9	9	7	17	447	17.35	53		66	381	14.77	85.23
2	13	9	6	17	446	17.31	54		140	306	31.39	68.61
10	9	9	6	16	445	17.27	55		237	208	53.26	46.74
9	7	9	2	16	442	17.16	56		259	183	58.6	41.4
9	13	9	1	18	442	17.16	57		329	113	74.43	25.57
10	11	9	1	15	441	17.12	58		135	306	30.61	69.39
4	3	9	6	18	438	17	59		283	155	64.61	35.39
5	8	9	6	13	434	16.85	60		284	150	65.44	34.56
8	16	9	1	15	434	16.85	61	2576	225	209	51.84	48.16
9	13	9	1	16	432	16.77	62		321	111	74.31	25.69
9	7	9	2	17	430	16.69	63		283	147	65.81	34.19
12	18	9	6	16	424	16.46	64		86	338	20.28	79.72
10	16	9	6	16	423	16.42	65		209	214	49.41	50.59
10	9	9	6	15	422	16.38	66		244	178	57.82	42.18
10	4	9	1	12	420	16.3	67		98	322	23.33	76.67
10	2	9	6	16	417	16.19	68		191	226	45.8	54.2
2	16	9	2	16	415	16.11	69		285	130	68.67	31.33

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	16	9	1	17	413	16.03	70		194	219	46.97	53.03
10	16	9	6	15	412	15.99	71		179	233	43.45	56.55
8	21	9	6	15	411	15.95	72		245	166	59.61	40.39
2	16	9	2	17	409	15.88	73		273	136	66.75	33.25
5	10	9	1	16	409	15.88	74		94	315	22.98	77.02
10	4	9	1	20	409	15.88	75		229	180	55.99	44.01
8	16	9	1	16	408	15.84	76		203	205	49.75	50.25
5	9	9	7	18	405	15.72	77		55	350	13.58	86.42
10	16	9	6	17	405	15.72	78		179	226	44.2	55.8
10	23	9	6	16	404	15.68	79		175	229	43.32	56.68
9	11	9	6	19	403	15.64	80		88	315	21.84	78.16
5	9	9	7	14	400	15.53	81	2576	106	294	26.5	73.5
10	11	9	1	13	396	15.37	82		73	323	18.43	81.57
10	2	9	6	17	395	15.33	83		164	231	41.52	58.48
10	23	9	6	17	393	15.26	84		156	237	39.69	60.31
5	8	9	6	20	392	15.22	85		191	201	48.72	51.28
10	11	9	1	14	391	15.18	86		103	288	26.34	73.66
9	13	9	1	15	389	15.1	87		260	129	66.84	33.16
10	2	9	6	18	388	15.06	88		154	234	39.69	60.31
5	9	9	7	13	385	14.95	89		117	268	30.39	69.61
8	21	9	6	17	384	14.91	90		203	181	52.86	47.14
8	16	9	1	14	383	14.87	91		202	181	52.74	47.26
8	16	9	1	19	383	14.87	92		143	240	37.34	62.66
3	22	9	1	19	382	14.83	93		313	69	81.94	18.06
5	8	9	6	12	382	14.83	94		244	138	63.87	36.13
5	10	9	1	12	382	14.83	95		69	313	18.06	81.94
8	20	9	5	16	379	14.71	96		198	181	52.24	47.76
10	9	9	6	19	378	14.67	97		213	165	56.35	43.65
6	19	9	6	18	375	14.56	98		153	222	40.8	59.2
8	21	9	6	16	374	14.52	99		198	176	52.94	47.06
2	13	9	6	16	372	14.44	100		120	252	32.26	67.74
8	16	9	1	18	371	14.4	101	2576	171	200	46.09	53.91
9	13	9	1	19	371	14.4	102		267	104	71.97	28.03
4	10	9	6	16	368	14.29	103		145	223	39.4	60.6
8	18	9	3	16	368	14.29	104		200	168	54.35	45.65
10	16	9	6	18	368	14.29	105		176	192	47.83	52.17
8	16	9	1	13	367	14.25	106		227	140	61.85	38.15
10	18	9	1	16	367	14.25	107		164	203	44.69	55.31
9	7	9	2	14	364	14.13	108		208	156	57.14	42.86
10	9	9	6	14	364	14.13	109		245	119	67.31	32.69
10	23	9	6	18	364	14.13	110		151	213	41.48	58.52
5	9	9	7	12	361	14.01	111		175	186	48.48	51.52
8	23	9	1	15	361	14.01	112		181	180	50.14	49.86
9	11	9	6	15	361	14.01	113		77	284	21.33	78.67
10	23	9	6	15	360	13.98	114		152	208	42.22	57.78
2	13	9	6	15	359	13.94	115		127	232	35.38	64.62
5	22	9	6	16	359	13.94	116		157	202	43.73	56.27
8	21	9	6	13	359	13.94	117		236	123	65.74	34.26
9	25	9	6	16	359	13.94	118		158	201	44.01	55.99
10	25	9	1	17	359	13.94	119		192	167	53.48	46.52
8	20	9	5	13	358	13.9	120		212	146	59.22	40.78
7	31	9	6	17	357	13.86	121	2576	130	227	36.41	63.59

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	17	9	2	13	357	13.86	122		201	156	56.3	43.7
8	19	9	4	16	357	13.86	123		188	169	52.66	47.34
9	7	9	2	15	357	13.86	124		188	169	52.66	47.34
12	18	9	6	17	357	13.86	125		91	266	25.49	74.51
4	5	9	1	12	356	13.82	126		68	288	19.1	80.9
2	16	9	2	15	355	13.78	127		237	118	66.76	33.24
3	13	9	6	13	354	13.74	128		89	265	25.14	74.86
6	19	9	6	17	354	13.74	129		130	224	36.72	63.28
8	23	9	1	16	354	13.74	130		164	190	46.33	53.67
10	11	9	1	16	354	13.74	131		120	234	33.9	66.1
2	13	9	6	18	352	13.66	132		117	235	33.24	66.76
10	18	9	1	17	352	13.66	133		159	193	45.17	54.83
10	25	9	1	15	352	13.66	134		155	197	44.03	55.97
5	10	9	1	17	351	13.63	135		104	247	29.63	70.37
8	17	9	2	14	351	13.63	136		199	152	56.7	43.3
12	18	9	6	13	351	13.63	137		67	284	19.09	80.91
9	4	9	6	14	349	13.55	138		173	176	49.57	50.43
9	25	9	6	18	349	13.55	139		143	206	40.97	59.03
4	10	9	6	17	347	13.47	140		134	213	38.62	61.38
8	20	9	5	14	347	13.47	141	2576	229	118	65.99	34.01
4	3	9	6	12	346	13.43	142		260	86	75.14	24.86
1	11	9	1	15	345	13.39	143		242	103	70.14	29.86
5	15	9	6	17	345	13.39	144		151	194	43.77	56.23
8	16	9	1	12	345	13.39	145		233	112	67.54	32.46
8	21	9	6	14	345	13.39	146		228	117	66.09	33.91
10	2	9	6	15	344	13.35	147		149	195	43.31	56.69
9	7	9	2	19	342	13.28	148		218	124	63.74	36.26
1	11	9	1	14	341	13.24	149		270	71	79.18	20.82
7	31	9	6	18	340	13.2	150		118	222	34.71	65.29
4	17	9	6	16	339	13.16	151		168	171	49.56	50.44
9	25	9	6	17	339	13.16	152		136	203	40.12	59.88
10	25	9	1	16	339	13.16	153		159	180	46.9	53.1
5	22	9	6	17	338	13.12	154		149	189	44.08	55.92
8	21	9	6	18	338	13.12	155		178	160	52.66	47.34
10	4	9	1	21	338	13.12	156		181	157	53.55	46.45
10	30	9	6	17	338	13.12	157		188	150	55.62	44.38
9	5	9	7	11	337	13.08	158		234	103	69.44	30.56
5	22	9	6	15	335	13	159		174	161	51.94	48.06
10	18	9	1	18	335	13	160		197	138	58.81	41.19
4	5	9	1	18	334	12.97	161	2576	117	217	35.03	64.97
2	16	9	2	18	333	12.93	162		243	90	72.97	27.03
4	26	9	1	16	333	12.93	163		120	213	36.04	63.96
10	30	9	6	16	333	12.93	164		177	156	53.15	46.85
4	19	9	1	15	332	12.89	165		124	208	37.35	62.65
4	24	9	6	15	332	12.89	166		177	155	53.31	46.69
8	17	9	2	15	331	12.85	167		199	132	60.12	39.88
8	17	9	2	16	330	12.81	168		174	156	52.73	47.27
8	19	9	4	17	330	12.81	169		171	159	51.82	48.18
10	30	9	6	18	330	12.81	170		183	147	55.45	44.55
4	12	9	1	18	329	12.77	171		206	123	62.61	37.39
8	19	9	4	13	329	12.77	172		198	131	60.18	39.82
9	20	9	1	13	329	12.77	173		94	235	28.57	71.43

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
4	24	9	6	17	328	12.73	174		174	154	53.05	46.95
7	2	9	5	18	328	12.73	175		151	177	46.04	53.96
4	10	9	6	18	327	12.69	176		136	191	41.59	58.41
6	5	9	6	16	327	12.69	177		148	179	45.26	54.74
5	8	9	6	11	326	12.66	178		214	112	65.64	34.36
9	4	9	6	20	326	12.66	179		142	184	43.56	56.44
5	9	9	7	11	325	12.62	180		181	144	55.69	44.31
7	17	9	6	17	325	12.62	181	2576	135	190	41.54	58.46
8	19	9	4	14	325	12.62	182		222	103	68.31	31.69
10	11	9	1	17	325	12.62	183		128	197	39.38	60.62
6	19	9	6	16	324	12.58	184		121	203	37.35	62.65
8	23	9	1	17	324	12.58	185		168	156	51.85	48.15
1	10	9	7	15	323	12.54	186		269	54	83.28	16.72
5	22	9	6	18	323	12.54	187		135	188	41.8	58.2
1	10	9	7	14	322	12.5	188		250	72	77.64	22.36
5	7	9	5	17	322	12.5	189		137	185	42.55	57.45
6	26	9	6	16	322	12.5	190		161	161	50	50
8	15	9	7	16	322	12.5	191		204	118	63.35	36.65
2	16	9	2	14	321	12.46	192		179	142	55.76	44.24
4	17	9	6	17	321	12.46	193		155	166	48.29	51.71
8	21	9	6	12	321	12.46	194		184	137	57.32	42.68
9	11	9	6	14	321	12.46	195		109	212	33.96	66.04
10	18	9	1	15	321	12.46	196		149	172	46.42	53.58
10	23	9	6	14	321	12.46	197		160	161	49.84	50.16
4	24	9	6	16	320	12.42	198		166	154	51.88	48.13
4	26	9	1	15	320	12.42	199		98	222	30.63	69.38
8	20	9	5	17	320	12.42	200		179	141	55.94	44.06

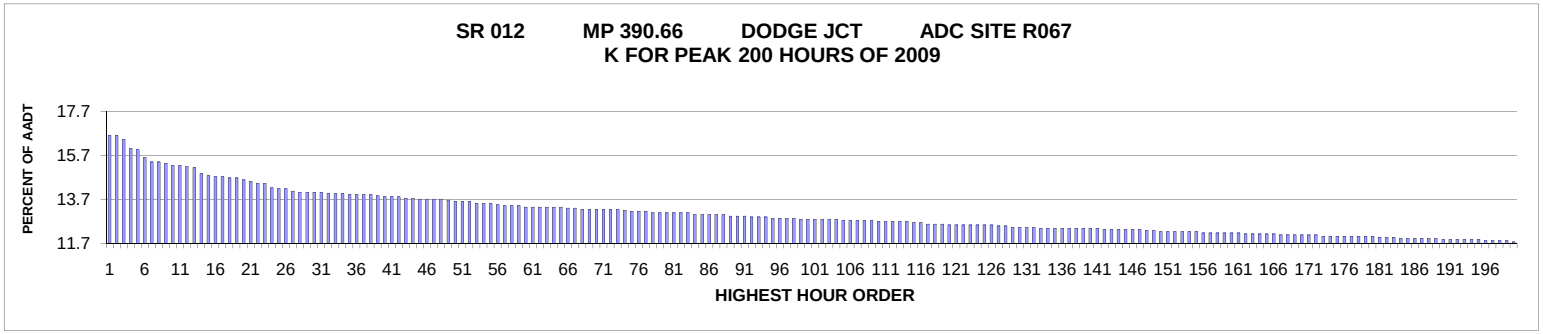

AADT= 1955 **K 30 FACTOR=** 14.02 **K 100 FACTOR=** 12.79 **K 200 FACTOR=** 11.76 **D FACTOR=** 55.64

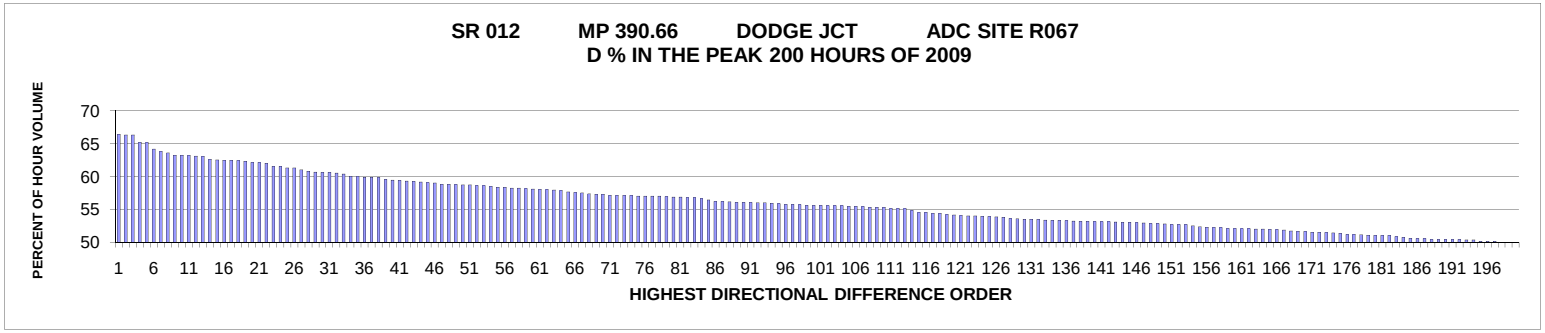

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
5	25	9	2	15	325	16.62	1	1955	130	195	40	60
11	29	9	1	16	325	16.62	2		174	151	53.54	46.46
5	9	9	7	11	321	16.42	3		205	116	63.86	36.14
5	25	9	2	13	313	16.01	4		115	198	36.74	63.26
11	29	9	1	15	312	15.96	5		144	168	46.15	53.85
7	5	9	1	14	305	15.6	6		120	185	39.34	60.66
5	22	9	6	17	301	15.4	7		166	135	55.15	44.85
5	25	9	2	16	301	15.4	8		141	160	46.84	53.16
11	25	9	4	16	300	15.35	9		172	128	57.33	42.67
7	5	9	1	15	298	15.24	10		121	177	40.6	59.4
11	25	9	4	15	298	15.24	11		161	137	54.03	45.97
5	22	9	6	16	297	15.19	12		176	121	59.26	40.74
9	4	9	6	17	296	15.14	13		155	141	52.36	47.64
5	25	9	2	12	291	14.88	14		98	193	33.68	66.32
11	25	9	4	17	289	14.78	15		162	127	56.06	43.94
5	25	9	2	14	288	14.73	16		108	180	37.5	62.5
9	7	9	2	15	288	14.73	17		132	156	45.83	54.17

7	3	9	6	12	287	14.68	18		163	124	56.79	43.21
7	5	9	1	17	287	14.68	19		127	160	44.25	55.75
8	9	9	1	16	285	14.58	20		133	152	46.67	53.33
9	7	9	2	13	284	14.53	21	1955	125	159	44.01	55.99
7	5	9	1	13	282	14.42	22		95	187	33.69	66.31
9	7	9	2	16	282	14.42	23		130	152	46.1	53.9
9	4	9	6	16	278	14.22	24		157	121	56.47	43.53
8	16	9	1	16	277	14.17	25		130	147	46.93	53.07
10	16	9	6	16	277	14.17	26		166	111	59.93	40.07
8	16	9	1	15	275	14.07	27		122	153	44.36	55.64
5	22	9	6	18	274	14.02	28		168	106	61.31	38.69
9	4	9	6	18	274	14.02	29		156	118	56.93	43.07
9	7	9	2	14	274	14.02	30		104	170	37.96	62.04
11	29	9	1	14	274	14.02	31		120	154	43.8	56.2
8	9	9	1	19	273	13.96	32		164	109	60.07	39.93
8	16	9	1	17	273	13.96	33		141	132	51.65	48.35
9	20	9	1	16	273	13.96	34		155	118	56.78	43.22
7	12	9	1	16	272	13.91	35		133	139	48.9	51.1
7	19	9	1	14	272	13.91	36		107	165	39.34	60.66
10	16	9	6	17	272	13.91	37		169	103	62.13	37.87
11	29	9	1	17	272	13.91	38		162	110	59.56	40.44
9	25	9	6	16	271	13.86	39		147	124	54.24	45.76
5	23	9	7	12	270	13.81	40		127	143	47.04	52.96
6	19	9	6	17	270	13.81	41	1955	154	116	57.04	42.96
8	23	9	1	15	270	13.81	42		116	154	42.96	57.04
6	19	9	6	14	269	13.76	43		143	126	53.16	46.84
6	28	9	1	16	269	13.76	44		130	139	48.33	51.67
7	5	9	1	16	268	13.71	45		90	178	33.58	66.42
7	26	9	1	16	268	13.71	46		119	149	44.4	55.6
9	20	9	1	15	268	13.71	47		125	143	46.64	53.36
9	20	9	1	17	268	13.71	48		136	132	50.75	49.25
7	26	9	1	15	267	13.66	49		100	167	37.45	62.55
7	19	9	1	15	266	13.61	50		133	133	50	50
8	9	9	1	18	266	13.61	51		138	128	51.88	48.12
8	14	9	6	17	266	13.61	52		161	105	60.53	39.47
9	4	9	6	14	264	13.5	53		138	126	52.27	47.73
9	18	9	6	16	264	13.5	54		140	124	53.03	46.97
9	18	9	6	18	264	13.5	55		152	112	57.58	42.42
5	22	9	6	19	263	13.45	56		154	109	58.56	41.44
8	14	9	6	15	262	13.4	57		145	117	55.34	44.66
8	21	9	6	15	262	13.4	58		153	109	58.4	41.6
10	16	9	6	15	262	13.4	59		137	125	52.29	47.71
4	5	9	1	17	261	13.35	60		139	122	53.26	46.74
4	5	9	1	18	261	13.35	61	1955	166	95	63.6	36.4
6	19	9	6	15	261	13.35	62		144	117	55.17	44.83
6	21	9	1	17	261	13.35	63		138	123	52.87	47.13
6	28	9	1	15	261	13.35	64		109	152	41.76	58.24
8	23	9	1	14	261	13.35	65		101	160	38.7	61.3
8	16	9	1	14	260	13.3	66		126	134	48.46	51.54
8	23	9	1	16	260	13.3	67		122	138	46.92	53.08
5	23	9	7	11	259	13.25	68		148	111	57.14	42.86
5	25	9	2	17	259	13.25	69		118	141	45.56	54.44
9	4	9	6	15	259	13.25	70		141	118	54.44	45.56
9	7	9	2	17	259	13.25	71		121	138	46.72	53.28
9	7	9	2	18	259	13.25	72		134	125	51.74	48.26
9	20	9	1	18	259	13.25	73		110	149	42.47	57.53
5	22	9	6	15	258	13.2	74		150	108	58.14	41.86

8	7	9	6	15	257	13.15	75		143	114	55.64	44.36
9	25	9	6	17	257	13.15	76		156	101	60.7	39.3
9	27	9	1	17	257	13.15	77		114	143	44.36	55.64
5	10	9	1	15	256	13.09	78		113	143	44.14	55.86
6	12	9	6	15	256	13.09	79		131	125	51.17	48.83
6	12	9	6	17	256	13.09	80		135	121	52.73	47.27
7	5	9	1	12	256	13.09	81	1955	89	167	34.77	65.23
7	10	9	6	15	256	13.09	82		127	129	49.61	50.39
8	9	9	1	17	256	13.09	83		124	132	48.44	51.56
6	12	9	6	14	254	12.99	84		141	113	55.51	44.49
7	3	9	6	13	254	12.99	85		148	106	58.27	41.73
7	3	9	6	15	254	12.99	86		135	119	53.15	46.85
9	5	9	7	12	254	12.99	87		147	107	57.87	42.13
11	29	9	1	13	254	12.99	88		103	151	40.55	59.45
4	19	9	1	17	253	12.94	89		147	106	58.1	41.9
5	10	9	1	17	253	12.94	90		128	125	50.59	49.41
7	12	9	1	15	253	12.94	91		115	138	45.45	54.55
4	24	9	6	16	252	12.89	92		148	104	58.73	41.27
9	19	9	7	12	252	12.89	93		159	93	63.1	36.9
9	25	9	6	18	252	12.89	94		144	108	57.14	42.86
6	28	9	1	14	251	12.84	95		110	141	43.82	56.18
7	24	9	6	15	251	12.84	96		129	122	51.39	48.61
9	13	9	1	16	251	12.84	97		127	124	50.6	49.4
9	18	9	6	17	251	12.84	98		140	111	55.78	44.22
6	19	9	6	16	250	12.79	99		145	105	58	42
7	2	9	5	18	250	12.79	100		151	99	60.4	39.6
8	2	9	1	15	250	12.79	101	1955	117	133	46.8	53.2
8	21	9	6	14	250	12.79	102		140	110	56	44
9	27	9	1	18	250	12.79	103		103	147	41.2	58.8
11	25	9	4	14	250	12.79	104		130	120	52	48
5	10	9	1	18	249	12.74	105		124	125	49.8	50.2
5	23	9	7	10	249	12.74	106		156	93	62.65	37.35
7	31	9	6	15	249	12.74	107		146	103	58.63	41.37
9	11	9	6	18	249	12.74	108		149	100	59.84	40.16
10	4	9	1	15	249	12.74	109		103	146	41.37	58.63
6	7	9	1	15	248	12.69	110		117	131	47.18	52.82
7	10	9	6	12	248	12.69	111		125	123	50.4	49.6
8	16	9	1	18	248	12.69	112		121	127	48.79	51.21
10	2	9	6	15	248	12.69	113		136	112	54.84	45.16
10	23	9	6	17	248	12.69	114		143	105	57.66	42.34
2	27	9	6	18	247	12.63	115		99	148	40.08	59.92
9	7	9	2	11	247	12.63	116		93	154	37.65	62.35
6	28	9	1	17	246	12.58	117		130	116	52.85	47.15
7	19	9	1	16	246	12.58	118		128	118	52.03	47.97
9	11	9	6	16	246	12.58	119		120	126	48.78	51.22
5	22	9	6	14	245	12.53	120		140	105	57.14	42.86
6	14	9	1	17	245	12.53	121	1955	126	119	51.43	48.57
6	21	9	1	13	245	12.53	122		105	140	42.86	57.14
9	18	9	6	15	245	12.53	123		130	115	53.06	46.94
9	27	9	1	15	245	12.53	124		100	145	40.82	59.18
10	18	9	1	15	245	12.53	125		103	142	42.04	57.96
10	23	9	6	18	245	12.53	126		136	109	55.51	44.49
5	8	9	6	15	244	12.48	127		132	112	54.1	45.9
6	14	9	1	13	244	12.48	128		127	117	52.05	47.95
3	21	9	7	17	243	12.43	129		112	131	46.09	53.91
4	10	9	6	17	243	12.43	130		151	92	62.14	37.86
8	23	9	1	12	243	12.43	131		87	156	35.8	64.2

9	11	9	6	15	243	12.43	132		113	130	46.5	53.5
5	8	9	6	17	242	12.38	133		138	104	57.02	42.98
5	25	9	2	11	242	12.38	134		93	149	38.43	61.57
6	28	9	1	18	242	12.38	135		121	121	50	50
7	12	9	1	12	242	12.38	136		89	153	36.78	63.22
7	17	9	6	11	242	12.38	137		126	116	52.07	47.93
8	23	9	1	17	242	12.38	138		93	149	38.43	61.57
10	9	9	6	15	242	12.38	139		126	116	52.07	47.93
10	9	9	6	18	242	12.38	140		122	120	50.41	49.59
10	18	9	1	16	242	12.38	141	1955	107	135	44.21	55.79
5	8	9	6	16	241	12.33	142		157	84	65.15	34.85
6	5	9	6	14	241	12.33	143		121	120	50.21	49.79
6	21	9	1	14	241	12.33	144		118	123	48.96	51.04
7	17	9	6	15	241	12.33	145		129	112	53.53	46.47
9	20	9	1	11	241	12.33	146		107	134	44.4	55.6
10	23	9	6	16	241	12.33	147		114	127	47.3	52.7
6	26	9	6	16	240	12.28	148		136	104	56.67	43.33
10	16	9	6	18	240	12.28	149		150	90	62.5	37.5
4	26	9	1	17	239	12.23	150		103	136	43.1	56.9
5	15	9	6	17	239	12.23	151		129	110	53.97	46.03
5	17	9	1	17	239	12.23	152		103	136	43.1	56.9
6	7	9	1	16	239	12.23	153		134	105	56.07	43.93
8	2	9	1	14	239	12.23	154		113	126	47.28	52.72
9	13	9	1	18	239	12.23	155		121	118	50.63	49.37
6	28	9	1	11	238	12.17	156		99	139	41.6	58.4
7	2	9	5	12	238	12.17	157		120	118	50.42	49.58
7	26	9	1	13	238	12.17	158		98	140	41.18	58.82
8	9	9	1	14	238	12.17	159		98	140	41.18	58.82
9	27	9	1	16	238	12.17	160		106	132	44.54	55.46
11	26	9	5	11	238	12.17	161	1955	125	113	52.52	47.48
5	1	9	6	17	237	12.12	162		136	101	57.38	42.62
7	24	9	6	16	237	12.12	163		109	128	45.99	54.01
7	31	9	6	16	237	12.12	164		148	89	62.45	37.55
8	2	9	1	16	237	12.12	165		110	127	46.41	53.59
10	16	9	6	14	237	12.12	166		140	97	59.07	40.93
6	5	9	6	16	236	12.07	167		119	117	50.42	49.58
7	10	9	6	14	236	12.07	168		123	113	52.12	47.88
7	24	9	6	13	236	12.07	169		126	110	53.39	46.61
7	26	9	1	18	236	12.07	170		118	118	50	50
7	31	9	6	11	236	12.07	171		113	123	47.88	52.12
10	11	9	1	13	236	12.07	172		99	137	41.95	58.05
6	14	9	1	16	235	12.02	173		117	118	49.79	50.21
6	21	9	1	12	235	12.02	174		123	112	52.34	47.66
6	26	9	6	17	235	12.02	175		134	101	57.02	42.98
7	5	9	1	18	235	12.02	176		109	126	46.38	53.62
7	6	9	2	12	235	12.02	177		97	138	41.28	58.72
8	21	9	6	16	235	12.02	178		130	105	55.32	44.68
8	23	9	1	18	235	12.02	179		110	125	46.81	53.19
10	9	9	6	16	235	12.02	180		143	92	60.85	39.15
7	2	9	5	14	234	11.97	181	1955	148	86	63.25	36.75
9	11	9	6	17	234	11.97	182		119	115	50.85	49.15
9	13	9	1	14	234	11.97	183		118	116	50.43	49.57
6	7	9	1	17	233	11.92	184		129	104	55.36	44.64
6	14	9	1	15	233	11.92	185		119	114	51.07	48.93
7	12	9	1	17	233	11.92	186		113	120	48.5	51.5
8	2	9	1	12	233	11.92	187		114	119	48.93	51.07
10	11	9	1	16	233	11.92	188		102	131	43.78	56.22

11	29	9	1	12	233	11.92	189	86	147	36.91	63.09
6	5	9	6	15	232	11.87	190	128	104	55.17	44.83
6	19	9	6	18	232	11.87	191	117	115	50.43	49.57
7	12	9	1	13	232	11.87	192	99	133	42.67	57.33
7	17	9	6	16	232	11.87	193	130	102	56.03	43.97
7	26	9	1	17	232	11.87	194	103	129	44.4	55.6
10	2	9	6	18	232	11.87	195	137	95	59.05	40.95
4	5	9	1	15	231	11.82	196	120	111	51.95	48.05
6	26	9	6	12	231	11.82	197	126	105	54.55	45.45
8	9	9	1	12	231	11.82	198	94	137	40.69	59.31
8	21	9	6	13	231	11.82	199	141	90	61.04	38.96
6	20	9	7	11	230	11.76	200	101	129	43.91	56.09

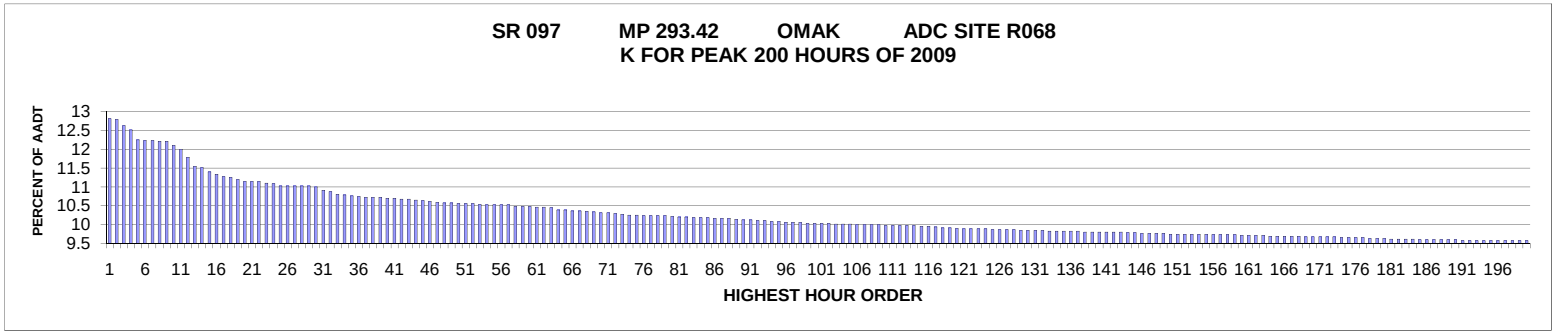

AADT= 5316 **K 30 FACTOR=** 11 **K 100 FACTOR=** 10.03 **K 200 FACTOR=** 9.57 **D FACTOR=** 57.27

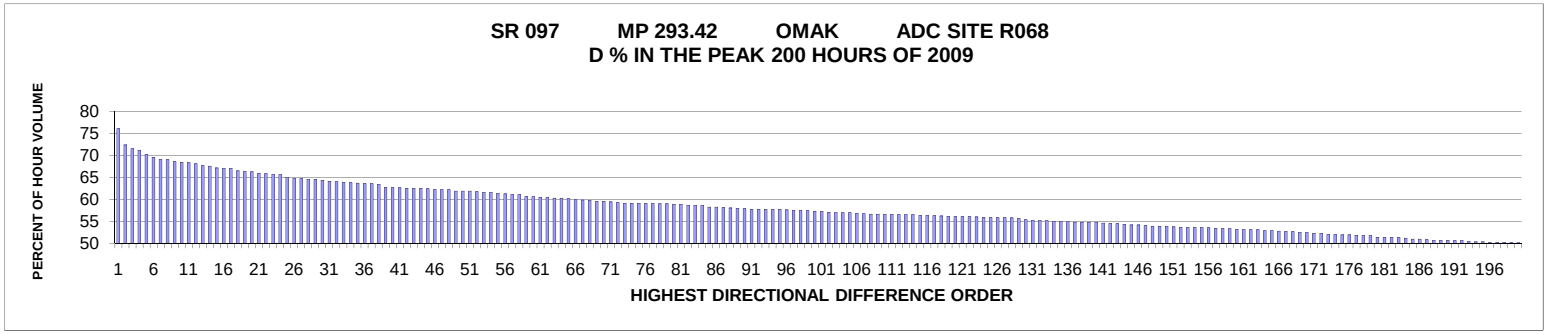

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
5	22	9	6	16	681	12.81	1	5316	474	207	69.6	30.4
10	9	9	6	17	680	12.79	2		435	245	63.97	36.03
5	22	9	6	17	671	12.62	3		420	251	62.59	37.41
10	9	9	6	16	665	12.51	4		441	224	66.32	33.68
8	9	9	1	13	651	12.25	5		267	384	41.01	58.99
10	9	9	6	14	650	12.23	6		384	266	59.08	40.92
10	16	9	6	13	650	12.23	7		413	237	63.54	36.46
5	22	9	6	15	649	12.21	8		413	236	63.64	36.36
10	16	9	6	14	649	12.21	9		422	227	65.02	34.98
10	11	9	1	14	643	12.1	10		185	458	28.77	71.23
5	16	9	7	13	638	12	11		400	238	62.7	37.3
10	16	9	6	17	627	11.79	12		440	187	70.18	29.82
10	16	9	6	15	614	11.55	13		375	239	61.07	38.93
10	9	9	6	18	612	11.51	14		411	201	67.16	32.84
8	7	9	6	18	606	11.4	15		302	304	49.83	50.17
8	9	9	1	12	603	11.34	16		228	375	37.81	62.19
7	6	9	2	14	599	11.27	17		237	362	39.57	60.43

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	9	9	1	14	598	11.25	18		261	337	43.65	56.35
10	11	9	1	13	595	11.19	19		184	411	30.92	69.08
8	14	9	6	16	592	11.14	20		335	257	56.59	43.41
9	7	9	2	13	592	11.14	21	5316	211	381	35.64	64.36
10	10	9	7	12	592	11.14	22		280	312	47.3	52.7
10	16	9	6	16	590	11.1	23		391	199	66.27	33.73
10	11	9	1	16	589	11.08	24		188	401	31.92	68.08
5	22	9	6	18	586	11.02	25		402	184	68.6	31.4
5	25	9	2	12	586	11.02	26		140	446	23.89	76.11
8	7	9	6	15	586	11.02	27		321	265	54.78	45.22
8	14	9	6	15	586	11.02	28		331	255	56.48	43.52
8	14	9	6	17	586	11.02	29		331	255	56.48	43.52
8	6	9	5	18	585	11	30		312	273	53.33	46.67
5	16	9	7	16	580	10.91	31		218	362	37.59	62.41
7	6	9	2	13	578	10.87	32		247	331	42.73	57.27
10	9	9	6	13	574	10.8	33		317	257	55.23	44.77
7	6	9	2	15	573	10.78	34		279	294	48.69	51.31
7	25	9	7	13	572	10.76	35		299	273	52.27	47.73
8	14	9	6	14	571	10.74	36		265	306	46.41	53.59
7	5	9	1	13	570	10.72	37		201	369	35.26	64.74
8	14	9	6	13	570	10.72	38		249	321	43.68	56.32
10	9	9	6	15	570	10.72	39		337	233	59.12	40.88
5	25	9	2	13	569	10.7	40		162	407	28.47	71.53
8	9	9	1	15	569	10.7	41	5316	264	305	46.4	53.6
7	2	9	5	15	567	10.67	42		308	259	54.32	45.68
7	2	9	5	17	567	10.67	43		380	187	67.02	32.98
10	16	9	6	12	566	10.65	44		332	234	58.66	41.34
8	7	9	6	17	565	10.63	45		311	254	55.04	44.96
9	25	9	6	17	564	10.61	46		332	232	58.87	41.13
8	7	9	6	14	563	10.59	47		253	310	44.94	55.06
8	20	9	5	17	562	10.57	48		323	239	57.47	42.53
10	16	9	6	18	562	10.57	49		388	174	69.04	30.96
8	6	9	5	17	561	10.55	50		303	258	54.01	45.99
8	21	9	6	14	561	10.55	51		302	259	53.83	46.17
9	4	9	6	15	561	10.55	52		282	279	50.27	49.73
7	31	9	6	16	560	10.53	53		303	257	54.11	45.89
8	13	9	5	16	559	10.52	54		318	241	56.89	43.11
9	4	9	6	18	559	10.52	55		367	192	65.65	34.35
10	8	9	5	17	559	10.52	56		339	220	60.64	39.36
10	10	9	7	13	559	10.52	57		287	272	51.34	48.66
8	7	9	6	16	557	10.48	58		291	266	52.24	47.76
8	11	9	3	17	557	10.48	59		312	245	56.01	43.99
10	11	9	1	15	557	10.48	60		154	403	27.65	72.35
7	2	9	5	16	556	10.46	61	5316	331	225	59.53	40.47
10	11	9	1	17	556	10.46	62		202	354	36.33	63.67
7	3	9	6	14	555	10.44	63		311	244	56.04	43.96
5	22	9	6	12	552	10.38	64		277	275	50.18	49.82
9	4	9	6	16	552	10.38	65		324	228	58.7	41.3
5	1	9	6	16	551	10.36	66		317	234	57.53	42.47
5	23	9	7	12	551	10.36	67		295	256	53.54	46.46
8	5	9	4	17	550	10.35	68		333	217	60.55	39.45
8	21	9	6	15	549	10.33	69		279	270	50.82	49.18

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	31	9	6	17	548	10.31	70		310	238	56.57	43.43
9	6	9	1	13	548	10.31	71		253	295	46.17	53.83
10	16	9	6	11	547	10.29	72		288	259	52.65	47.35
7	10	9	6	16	546	10.27	73		307	239	56.23	43.77
7	3	9	6	13	545	10.25	74		283	262	51.93	48.07
7	5	9	1	14	545	10.25	75		193	352	35.41	64.59
5	22	9	6	13	544	10.23	76		297	247	54.6	45.4
7	2	9	5	18	544	10.23	77		359	185	65.99	34.01
7	3	9	6	12	544	10.23	78		277	267	50.92	49.08
9	4	9	6	17	544	10.23	79		327	217	60.11	39.89
9	8	9	3	17	543	10.21	80		316	227	58.2	41.8
7	9	9	5	17	542	10.2	81	5316	339	203	62.55	37.45
7	17	9	6	16	542	10.2	82		290	252	53.51	46.49
5	25	9	2	14	541	10.18	83		171	370	31.61	68.39
7	31	9	6	14	541	10.18	84		267	274	49.35	50.65
8	31	9	2	13	541	10.18	85		215	326	39.74	60.26
7	6	9	2	12	540	10.16	86		181	359	33.52	66.48
7	10	9	6	17	540	10.16	87		313	227	57.96	42.04
7	30	9	5	17	540	10.16	88		308	232	57.04	42.96
10	23	9	6	17	539	10.14	89		323	216	59.93	40.07
7	10	9	6	14	538	10.12	90		279	259	51.86	48.14
10	15	9	5	15	538	10.12	91		330	208	61.34	38.66
8	8	9	7	14	537	10.1	92		251	286	46.74	53.26
10	15	9	5	17	537	10.1	93		360	177	67.04	32.96
7	10	9	6	13	536	10.08	94		249	287	46.46	53.54
8	7	9	6	12	536	10.08	95		226	310	42.16	57.84
5	22	9	6	14	535	10.06	96		317	218	59.25	40.75
7	16	9	5	18	535	10.06	97		343	192	64.11	35.89
8	1	9	7	13	534	10.05	98		264	270	49.44	50.56
7	3	9	6	15	533	10.03	99		329	204	61.73	38.27
8	5	9	4	15	533	10.03	100		290	243	54.41	45.59
8	14	9	6	12	533	10.03	101	5316	203	330	38.09	61.91
9	24	9	5	17	533	10.03	102		303	230	56.85	43.15
7	2	9	5	13	532	10.01	103		268	264	50.38	49.62
7	9	9	5	18	532	10.01	104		360	172	67.67	32.33
10	9	9	6	12	532	10.01	105		265	267	49.81	50.19
7	24	9	6	15	531	9.99	106		293	238	55.18	44.82
7	31	9	6	13	531	9.99	107		251	280	47.27	52.73
10	2	9	6	17	531	9.99	108		316	215	59.51	40.49
10	9	9	6	11	531	9.99	109		240	291	45.2	54.8
5	26	9	3	17	530	9.97	110		338	192	63.77	36.23
8	8	9	7	19	530	9.97	111		202	328	38.11	61.89
8	13	9	5	15	530	9.97	112		275	255	51.89	48.11
9	23	9	4	17	530	9.97	113		336	194	63.4	36.6
10	23	9	6	15	530	9.97	114		278	252	52.45	47.55
9	18	9	6	17	529	9.95	115		264	265	49.91	50.09
10	9	9	6	19	529	9.95	116		347	182	65.6	34.4
7	6	9	2	17	528	9.93	117		311	217	58.9	41.1
7	17	9	6	15	527	9.91	118		276	251	52.37	47.63
8	3	9	2	13	527	9.91	119		253	274	48.01	51.99
10	23	9	6	13	526	9.89	120		224	302	42.59	57.41
7	24	9	6	17	525	9.88	121	5316	303	222	57.71	42.29

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	7	9	6	13	525	9.88	122		215	310	40.95	59.05
8	28	9	6	17	525	9.88	123		312	213	59.43	40.57
9	3	9	5	14	525	9.88	124		266	259	50.67	49.33
7	20	9	2	14	524	9.86	125		268	256	51.15	48.85
8	16	9	1	13	524	9.86	126		215	309	41.03	58.97
8	20	9	5	15	524	9.86	127		278	246	53.05	46.95
9	17	9	5	17	524	9.86	128		313	211	59.73	40.27
8	8	9	7	13	523	9.84	129		221	302	42.26	57.74
8	8	9	7	17	523	9.84	130		201	322	38.43	61.57
8	10	9	2	16	523	9.84	131		293	230	56.02	43.98
9	4	9	6	14	523	9.84	132		292	231	55.83	44.17
7	1	9	4	15	522	9.82	133		291	231	55.75	44.25
7	2	9	5	14	522	9.82	134		262	260	50.19	49.81
8	3	9	2	16	522	9.82	135		293	229	56.13	43.87
8	11	9	3	14	522	9.82	136		268	254	51.34	48.66
8	28	9	6	14	522	9.82	137		264	258	50.57	49.43
5	6	9	4	17	521	9.8	138		297	224	57.01	42.99
7	12	9	1	14	521	9.8	139		213	308	40.88	59.12
8	2	9	1	14	521	9.8	140		239	282	45.87	54.13
8	3	9	2	15	521	9.8	141	5316	284	237	54.51	45.49
8	8	9	7	16	521	9.8	142		230	291	44.15	55.85
8	9	9	1	17	521	9.8	143		270	251	51.82	48.18
7	25	9	7	14	520	9.78	144		234	286	45	55
9	9	9	4	16	520	9.78	145		269	251	51.73	48.27
7	1	9	4	18	519	9.76	146		323	196	62.24	37.76
7	23	9	5	18	519	9.76	147		304	215	58.57	41.43
8	4	9	3	17	519	9.76	148		301	218	58	42
9	11	9	6	16	519	9.76	149		302	217	58.19	41.81
7	1	9	4	17	518	9.74	150		325	193	62.74	37.26
7	31	9	6	15	518	9.74	151		279	239	53.86	46.14
8	8	9	7	18	518	9.74	152		199	319	38.42	61.58
8	24	9	2	15	518	9.74	153		264	254	50.97	49.03
8	28	9	6	12	518	9.74	154		228	290	44.02	55.98
9	3	9	5	15	518	9.74	155		295	223	56.95	43.05
7	5	9	1	15	517	9.73	156		197	320	38.1	61.9
9	7	9	2	12	517	9.73	157		163	354	31.53	68.47
10	2	9	6	15	517	9.73	158		286	231	55.32	44.68
10	12	9	2	15	517	9.73	159		244	273	47.2	52.8
5	13	9	4	17	516	9.71	160		297	219	57.56	42.44
8	3	9	2	17	516	9.71	161	5316	298	218	57.75	42.25
9	11	9	6	17	516	9.71	162		292	224	56.59	43.41
9	18	9	6	18	516	9.71	163		298	218	57.75	42.25
4	22	9	4	17	515	9.69	164		291	224	56.5	43.5
5	22	9	6	19	515	9.69	165		348	167	67.57	32.43
7	8	9	4	18	515	9.69	166		322	193	62.52	37.48
7	26	9	1	13	515	9.69	167		227	288	44.08	55.92
9	9	9	4	17	515	9.69	168		304	211	59.03	40.97
5	15	9	6	17	514	9.67	169		250	264	48.64	51.36
7	3	9	6	16	514	9.67	170		332	182	64.59	35.41
8	31	9	2	15	514	9.67	171		238	276	46.3	53.7
9	1	9	3	15	514	9.67	172		241	273	46.89	53.11
9	7	9	2	14	514	9.67	173		203	311	39.49	60.51

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	1	9	7	15	513	9.65	174		274	239	53.41	46.59
9	9	9	4	13	513	9.65	175		217	296	42.3	57.7
10	2	9	6	18	513	9.65	176		314	199	61.21	38.79
10	23	9	6	12	513	9.65	177		181	332	35.28	64.72
8	1	9	7	12	512	9.63	178		214	298	41.8	58.2
9	11	9	6	15	512	9.63	179		281	231	54.88	45.12
9	24	9	5	16	512	9.63	180		285	227	55.66	44.34
5	15	9	6	16	511	9.61	181	5316	259	252	50.68	49.32
5	26	9	3	13	511	9.61	182		239	272	46.77	53.23
7	13	9	2	13	511	9.61	183		231	280	45.21	54.79
8	27	9	5	18	511	9.61	184		308	203	60.27	39.73
5	23	9	7	13	510	9.59	185		305	205	59.8	40.2
5	29	9	6	16	510	9.59	186		292	218	57.25	42.75
7	8	9	4	17	510	9.59	187		319	191	62.55	37.45
8	27	9	5	17	510	9.59	188		317	193	62.16	37.84
8	31	9	2	14	510	9.59	189		221	289	43.33	56.67
10	1	9	5	16	510	9.59	190		264	246	51.76	48.24
5	1	9	6	15	509	9.57	191		284	225	55.8	44.2
5	26	9	3	14	509	9.57	192		239	270	46.95	53.05
7	17	9	6	12	509	9.57	193		221	288	43.42	56.58
7	17	9	6	17	509	9.57	194		311	198	61.1	38.9
8	1	9	7	14	509	9.57	195		256	253	50.29	49.71
8	15	9	7	12	509	9.57	196		223	286	43.81	56.19
8	21	9	6	13	509	9.57	197		240	269	47.15	52.85
10	8	9	5	18	509	9.57	198		335	174	65.82	34.18
10	12	9	2	14	509	9.57	199		230	279	45.19	54.81
10	19	9	2	12	509	9.57	200		184	325	36.15	63.85

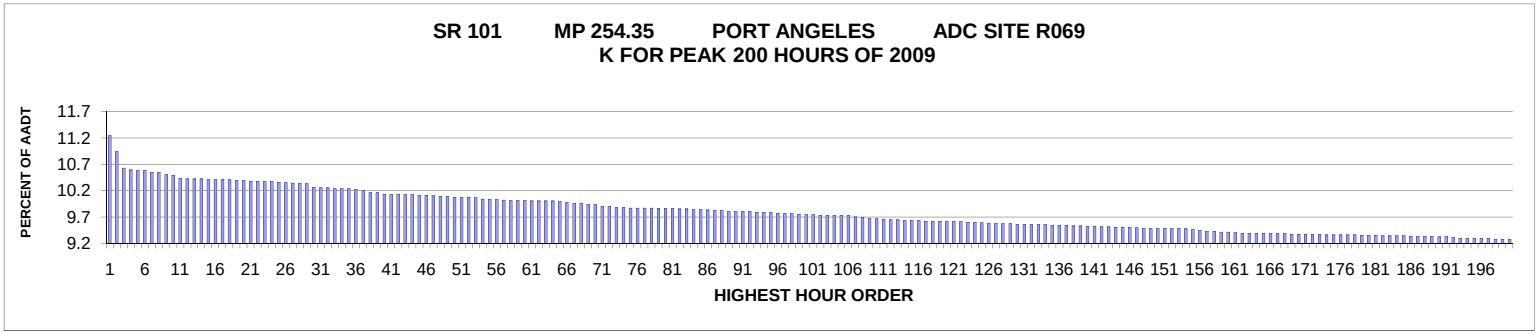

AADT= 21919 **K 30 FACTOR=** 10.26 **K 100 FACTOR=** 9.74 **K 200 FACTOR=** 9.28 **D FACTOR=** 54.42

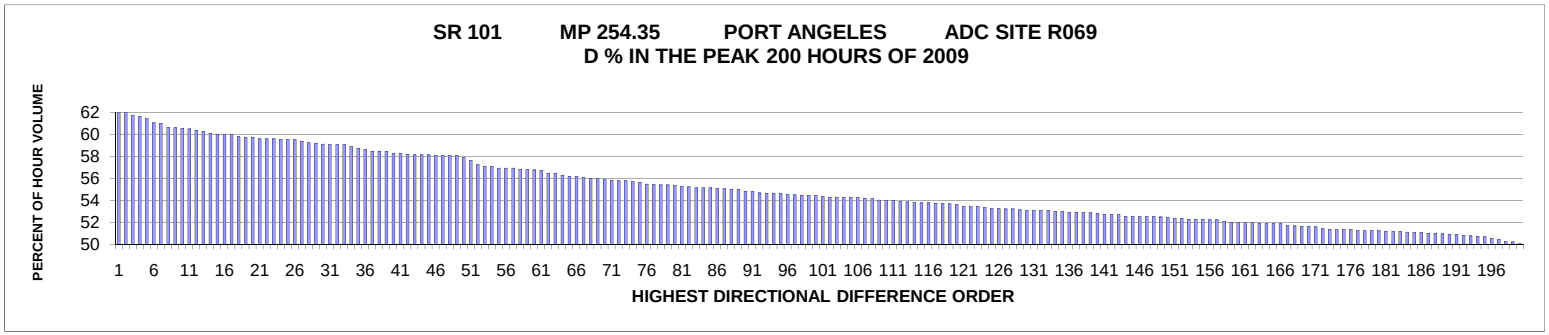

EAST IS INCREASING MP DIRECTION

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	21	9	6	17	2463	11.24	1	21919	1273	1190	51.68	48.32
7	15	9	4	17	2397	10.94	2		1281	1116	53.44	46.56
8	14	9	6	17	2331	10.63	3		1184	1147	50.79	49.21
7	24	9	6	17	2321	10.59	4		1182	1139	50.93	49.07
8	27	9	5	17	2320	10.58	5		1234	1086	53.19	46.81
7	17	9	6	17	2318	10.58	6		1139	1179	49.14	50.86
8	19	9	4	18	2312	10.55	7		1387	925	59.99	40.01
7	31	9	6	18	2310	10.54	8		1262	1048	54.63	45.37
7	31	9	6	16	2301	10.5	9		1177	1124	51.15	48.85
8	6	9	5	17	2300	10.49	10		1275	1025	55.43	44.57
7	16	9	5	18	2286	10.43	11		1371	915	59.97	40.03
7	1	9	4	17	2284	10.42	12		1228	1056	53.77	46.23
8	18	9	3	17	2284	10.42	13		1255	1029	54.95	45.05
9	25	9	6	17	2283	10.42	14		1300	983	56.94	43.06
7	24	9	6	18	2281	10.41	15		1334	947	58.48	41.52
8	20	9	5	18	2280	10.4	16		1391	889	61.01	38.99
8	17	9	2	17	2279	10.4	17		1286	993	56.43	43.57

EAST IS INCREASING MP DIRECTION

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
9	4	9	6	17	2279	10.4	18		1206	1073	52.92	47.08
7	3	9	6	13	2277	10.39	19		1060	1217	46.55	53.45
7	16	9	5	17	2277	10.39	20		1220	1057	53.58	46.42
8	7	9	6	17	2276	10.38	21	21919	1166	1110	51.23	48.77
8	7	9	6	18	2274	10.37	22		1295	979	56.95	43.05
7	31	9	6	17	2273	10.37	23		1168	1105	51.39	48.61
7	30	9	5	17	2272	10.37	24		1197	1075	52.68	47.32
7	22	9	4	17	2271	10.36	25		1209	1062	53.24	46.76
8	5	9	4	18	2269	10.35	26		1344	925	59.23	40.77
8	28	9	6	17	2267	10.34	27		1156	1111	50.99	49.01
7	2	9	5	17	2266	10.34	28		1190	1076	52.52	47.48
9	11	9	6	17	2264	10.33	29		1250	1014	55.21	44.79
8	19	9	4	17	2249	10.26	30		1211	1038	53.85	46.15
7	24	9	6	16	2247	10.25	31		1173	1074	52.2	47.8
8	20	9	5	17	2247	10.25	32		1219	1028	54.25	45.75
8	5	9	4	17	2245	10.24	33		1278	967	56.93	43.07
8	3	9	2	17	2244	10.24	34		1218	1026	54.28	45.72
8	21	9	6	18	2243	10.23	35		1260	983	56.17	43.83
9	24	9	5	17	2240	10.22	36		1219	1021	54.42	45.58
9	11	9	6	16	2236	10.2	37		1155	1081	51.65	48.35
7	10	9	6	17	2227	10.16	38		1000	1227	44.9	55.1
9	1	9	3	17	2227	10.16	39		1228	999	55.14	44.86
7	3	9	6	15	2221	10.13	40		984	1237	44.3	55.7
10	9	9	6	17	2221	10.13	41	21919	1180	1041	53.13	46.87
6	26	9	6	17	2220	10.13	42		1145	1075	51.58	48.42
7	1	9	4	18	2219	10.12	43		1289	930	58.09	41.91
7	10	9	6	18	2219	10.12	44		1121	1098	50.52	49.48
8	20	9	5	16	2217	10.11	45		1113	1104	50.2	49.8
7	22	9	4	18	2216	10.11	46		1291	925	58.26	41.74
8	4	9	3	17	2214	10.1	47		1196	1018	54.02	45.98
9	18	9	6	17	2212	10.09	48		1202	1010	54.34	45.66
8	28	9	6	16	2210	10.08	49		1063	1147	48.1	51.9
7	23	9	5	17	2208	10.07	50		1175	1033	53.22	46.78
8	26	9	4	18	2207	10.07	51		1360	847	61.62	38.38
9	10	9	5	17	2207	10.07	52		1228	979	55.64	44.36
7	31	9	6	15	2204	10.06	53		1052	1152	47.73	52.27
10	2	9	6	17	2201	10.04	54		1243	958	56.47	43.53
8	6	9	5	18	2200	10.04	55		1282	918	58.27	41.73
8	21	9	6	16	2199	10.03	56		1126	1073	51.21	48.79
8	10	9	2	17	2196	10.02	57		1144	1052	52.09	47.91
8	28	9	6	18	2195	10.01	58		1306	889	59.5	40.5
7	14	9	3	17	2193	10.01	59		1209	984	55.13	44.87
9	10	9	5	18	2193	10.01	60		1354	839	61.74	38.26
8	13	9	5	17	2192	10	61	21919	1189	1003	54.24	45.76
7	9	9	5	17	2191	10	62		1171	1020	53.45	46.55
9	2	9	4	17	2191	10	63		1163	1028	53.08	46.92
9	11	9	6	18	2191	10	64		1254	937	57.23	42.77
8	14	9	6	18	2189	9.99	65		1272	917	58.11	41.89
8	11	9	3	17	2185	9.97	66		1180	1005	54	46
8	18	9	3	18	2182	9.95	67		1323	859	60.63	39.37
9	23	9	4	17	2180	9.95	68		1266	914	58.07	41.93
8	12	9	4	18	2179	9.94	69		1313	866	60.26	39.74

EAST IS INCREASING MP DIRECTION

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	29	9	4	17	2177	9.93	70		1169	1008	53.7	46.3
8	24	9	2	17	2171	9.9	71		1197	974	55.14	44.86
9	4	9	6	16	2170	9.9	72		1139	1031	52.49	47.51
8	25	9	3	18	2165	9.88	73		1286	879	59.4	40.6
10	8	9	5	17	2165	9.88	74		1212	953	55.98	44.02
7	2	9	5	18	2164	9.87	75		1265	899	58.46	41.54
7	3	9	6	12	2163	9.87	76		884	1279	40.87	59.13
8	14	9	6	16	2163	9.87	77		1022	1141	47.25	52.75
10	9	9	6	16	2163	9.87	78		1122	1041	51.87	48.13
8	12	9	4	17	2162	9.86	79		1148	1014	53.1	46.9
7	2	9	5	16	2161	9.86	80		1128	1033	52.2	47.8
8	26	9	4	17	2161	9.86	81	21919	1178	983	54.51	45.49
7	10	9	6	16	2158	9.85	82		1030	1128	47.73	52.27
7	17	9	6	18	2158	9.85	83		1183	975	54.82	45.18
7	17	9	6	16	2157	9.84	84		1063	1094	49.28	50.72
8	11	9	3	18	2157	9.84	85		1271	886	58.92	41.08
7	20	9	2	17	2154	9.83	86		1193	961	55.39	44.61
7	28	9	3	17	2153	9.82	87		1167	986	54.2	45.8
8	13	9	5	18	2153	9.82	88		1253	900	58.2	41.8
9	9	9	4	17	2149	9.8	89		1174	975	54.63	45.37
7	15	9	4	18	2148	9.8	90		1283	865	59.73	40.27
8	14	9	6	15	2147	9.8	91		1127	1020	52.49	47.51
9	22	9	3	17	2147	9.8	92		1169	978	54.45	45.55
6	30	9	3	17	2146	9.79	93		1155	991	53.82	46.18
9	17	9	5	17	2145	9.79	94		1151	994	53.66	46.34
9	3	9	5	17	2143	9.78	95		1143	1000	53.34	46.66
7	16	9	5	16	2142	9.77	96		1096	1046	51.17	48.83
7	3	9	6	16	2140	9.76	97		1016	1124	47.48	52.52
7	31	9	6	14	2140	9.76	98		1093	1047	51.07	48.93
7	23	9	5	18	2137	9.75	99		1242	895	58.12	41.88
7	9	9	5	18	2136	9.74	100		1273	863	59.6	40.4
8	25	9	3	17	2136	9.74	101	21919	1220	916	57.12	42.88
9	4	9	6	18	2133	9.73	102		1260	873	59.07	40.93
6	30	9	3	18	2132	9.73	103		1275	857	59.8	40.2
7	10	9	6	15	2132	9.73	104		1013	1119	47.51	52.49
9	15	9	3	17	2131	9.72	105		1228	903	57.63	42.37
9	25	9	6	16	2131	9.72	106		1156	975	54.25	45.75
6	26	9	6	18	2127	9.7	107		1207	920	56.75	43.25
8	27	9	5	18	2123	9.69	108		1282	841	60.39	39.61
8	20	9	5	15	2120	9.67	109		1050	1070	49.53	50.47
8	21	9	6	15	2118	9.66	110		991	1127	46.79	53.21
7	21	9	3	17	2116	9.65	111		1208	908	57.09	42.91
7	8	9	4	17	2113	9.64	112		1136	977	53.76	46.24
10	7	9	4	17	2112	9.64	113		1184	928	56.06	43.94
6	18	9	5	18	2110	9.63	114		1308	802	61.99	38.01
8	1	9	7	14	2110	9.63	115		1027	1083	48.67	51.33
10	9	9	6	18	2110	9.63	116		1221	889	57.87	42.13
8	22	9	7	13	2109	9.62	117		948	1161	44.95	55.05
8	31	9	2	18	2108	9.62	118		1295	813	61.43	38.57
9	10	9	5	16	2108	9.62	119		1079	1029	51.19	48.81
6	19	9	6	18	2106	9.61	120		1244	862	59.07	40.93
7	3	9	6	17	2106	9.61	121	21919	1030	1076	48.91	51.09

EAST IS INCREASING MP DIRECTION

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	3	9	2	16	2106	9.61	122		1118	988	53.09	46.91
7	7	9	3	17	2104	9.6	123		1150	954	54.66	45.34
9	17	9	5	18	2104	9.6	124		1222	882	58.08	41.92
7	27	9	2	17	2102	9.59	125		1166	936	55.47	44.53
7	10	9	6	14	2099	9.58	126		1070	1029	50.98	49.02
7	21	9	3	18	2099	9.58	127		1262	837	60.12	39.88
7	24	9	6	15	2098	9.57	128		997	1101	47.52	52.48
8	3	9	2	18	2098	9.57	129		1242	856	59.2	40.8
10	6	9	3	17	2096	9.56	130		1180	916	56.3	43.7
7	31	9	6	13	2095	9.56	131		1095	1000	52.27	47.73
8	17	9	2	18	2093	9.55	132		1247	846	59.58	40.42
9	18	9	6	18	2093	9.55	133		1224	869	58.48	41.52
12	22	9	3	17	2093	9.55	134		1172	921	56	44
6	29	9	2	17	2092	9.54	135		1107	985	52.92	47.08
7	29	9	4	18	2092	9.54	136		1267	825	60.56	39.44
10	1	9	5	17	2092	9.54	137		1168	924	55.83	44.17
7	25	9	7	13	2089	9.53	138		924	1165	44.23	55.77
9	2	9	4	18	2089	9.53	139		1248	841	59.74	40.26
6	24	9	4	18	2087	9.52	140		1243	844	59.56	40.44
10	10	9	7	15	2087	9.52	141	21919	1044	1043	50.02	49.98
7	3	9	6	14	2085	9.51	142		985	1100	47.24	52.76
8	4	9	3	18	2085	9.51	143		1241	844	59.52	40.48
6	18	9	5	17	2082	9.5	144		1134	948	54.47	45.53
8	7	9	6	16	2082	9.5	145		1055	1027	50.67	49.33
9	1	9	3	18	2082	9.5	146		1262	820	60.61	39.39
8	7	9	6	15	2081	9.49	147		1007	1074	48.39	51.61
7	1	9	4	16	2079	9.48	148		1017	1062	48.92	51.08
7	30	9	5	15	2079	9.48	149		1011	1068	48.63	51.37
11	24	9	3	17	2079	9.48	150		1168	911	56.18	43.82
8	21	9	6	14	2078	9.48	151		1011	1067	48.65	51.35
8	6	9	5	16	2077	9.48	152		1095	982	52.72	47.28
10	10	9	7	14	2077	9.48	153		977	1100	47.04	52.96
9	25	9	6	18	2076	9.47	154		1237	839	59.59	40.41
9	12	9	7	13	2073	9.46	155		1021	1052	49.25	50.75
11	20	9	6	17	2071	9.45	156		1155	916	55.77	44.23
9	8	9	3	17	2068	9.43	157		1156	912	55.9	44.1
9	4	9	6	15	2067	9.43	158		1052	1015	50.9	49.1
7	2	9	5	14	2062	9.41	159		991	1071	48.06	51.94
9	9	9	4	18	2062	9.41	160		1238	824	60.04	39.96
10	30	9	6	17	2061	9.4	161	21919	1169	892	56.72	43.28
8	17	9	2	15	2059	9.39	162		970	1089	47.11	52.89
11	13	9	6	17	2059	9.39	163		1128	931	54.78	45.22
9	18	9	6	16	2058	9.39	164		1090	968	52.96	47.04
6	19	9	6	17	2056	9.38	165		1066	990	51.85	48.15
7	13	9	2	17	2056	9.38	166		1138	918	55.35	44.65
9	23	9	4	18	2056	9.38	167		1195	861	58.12	41.88
8	7	9	6	13	2055	9.38	168		1076	979	52.36	47.64
6	25	9	5	17	2054	9.37	169		1112	942	54.14	45.86
7	24	9	6	14	2054	9.37	170		964	1090	46.93	53.07
7	23	9	5	16	2053	9.37	171		1052	1001	51.24	48.76
8	28	9	6	15	2053	9.37	172		986	1067	48.03	51.97
10	2	9	6	16	2053	9.37	173		1121	932	54.6	45.4

EAST IS INCREASING MP DIRECTION

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	30	9	5	18	2052	9.36	174		1212	840	59.06	40.94
8	19	9	4	16	2052	9.36	175		1051	1001	51.22	48.78
9	21	9	2	17	2052	9.36	176		1134	918	55.26	44.74
8	24	9	2	18	2051	9.36	177		1241	810	60.51	39.49
10	9	9	6	15	2051	9.36	178		1076	975	52.46	47.54
7	2	9	5	15	2050	9.35	179		1065	985	51.95	48.05
7	21	9	3	16	2050	9.35	180		1063	987	51.85	48.15
12	3	9	5	17	2049	9.35	181	21919	1106	943	53.98	46.02
8	28	9	6	14	2048	9.34	182		1019	1029	49.76	50.24
9	24	9	5	16	2048	9.34	183		1116	932	54.49	45.51
7	26	9	1	13	2047	9.34	184		996	1051	48.66	51.34
10	23	9	6	17	2047	9.34	185		1134	913	55.4	44.6
6	23	9	3	17	2045	9.33	186		1099	946	53.74	46.26
9	22	9	3	18	2044	9.33	187		1267	777	61.99	38.01
9	24	9	5	18	2044	9.33	188		1198	846	58.61	41.39
12	23	9	4	17	2044	9.33	189		1080	964	52.84	47.16
9	30	9	4	17	2043	9.32	190		1161	882	56.83	43.17
7	17	9	6	15	2042	9.32	191		942	1100	46.13	53.87
7	25	9	7	12	2039	9.3	192		841	1198	41.25	58.75
6	24	9	4	17	2037	9.29	193		1105	932	54.25	45.75
8	17	9	2	16	2037	9.29	194		1052	985	51.64	48.36
7	28	9	3	18	2036	9.29	195		1243	793	61.05	38.95
9	14	9	2	17	2036	9.29	196		1156	880	56.78	43.22
10	7	9	4	16	2036	9.29	197		1120	916	55.01	44.99
9	4	9	6	14	2035	9.28	198		970	1065	47.67	52.33
10	10	9	7	13	2035	9.28	199		852	1183	41.87	58.13
8	26	9	4	16	2034	9.28	200		1058	976	52.02	47.98

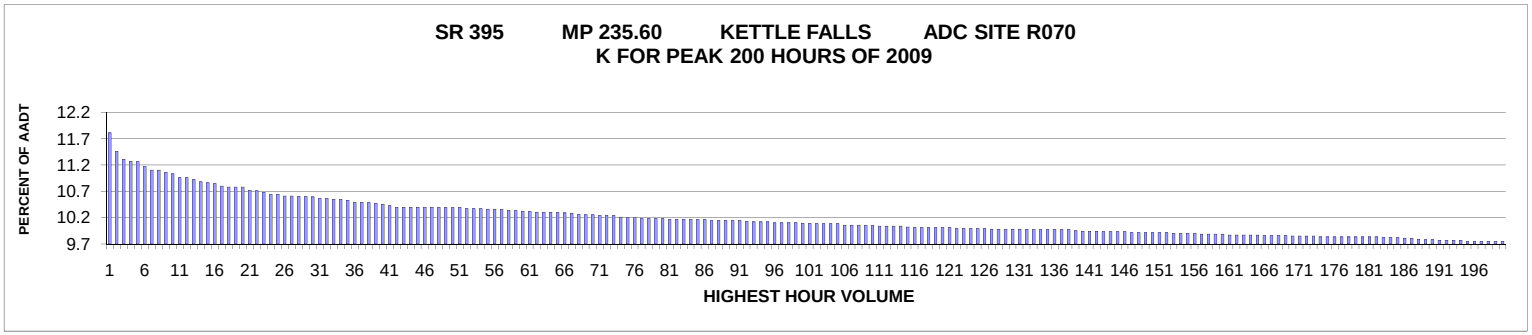

AADT= 7424 **K 30 FACTOR=** 10.59 **K 100 FACTOR=** 10.09 **K 200 FACTOR=** 9.75 **D FACTOR=** 53.63

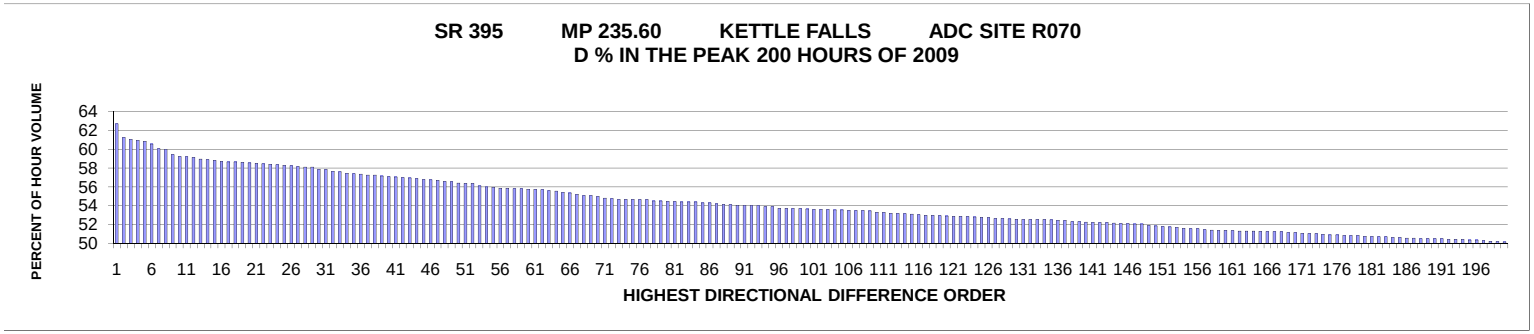

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	3	9	6	13	877	11.81	1	7424	502	375	57.24	42.76
7	3	9	6	12	851	11.46	2		424	427	49.82	50.18
7	3	9	6	15	840	11.31	3		490	350	58.33	41.67
5	22	9	6	15	837	11.27	4		480	357	57.35	42.65
7	2	9	5	15	836	11.26	5		447	389	53.47	46.53
7	1	9	4	17	829	11.17	6		462	367	55.73	44.27
5	22	9	6	16	824	11.1	7		461	363	55.95	44.05
7	3	9	6	16	824	11.1	8		479	345	58.13	41.87
10	9	9	6	15	821	11.06	9		443	378	53.96	46.04
7	1	9	4	15	819	11.03	10		425	394	51.89	48.11
9	3	9	5	16	814	10.96	11		398	416	48.89	51.11
9	4	9	6	16	814	10.96	12		435	379	53.44	46.56
7	2	9	5	17	811	10.92	13		478	333	58.94	41.06
7	8	9	4	15	808	10.88	14		433	375	53.59	46.41
7	2	9	5	16	806	10.86	15		441	365	54.71	45.29
7	31	9	6	16	805	10.84	16		411	394	51.06	48.94
5	8	9	6	16	802	10.8	17		393	409	49	51

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	3	9	6	14	800	10.78	18		469	331	58.63	41.38
7	17	9	6	13	800	10.78	19		393	407	49.13	50.88
9	8	9	3	16	800	10.78	20		455	345	56.88	43.13
10	9	9	6	16	796	10.72	21	7424	421	375	52.89	47.11
7	31	9	6	15	795	10.71	22		448	347	56.35	43.65
7	17	9	6	16	793	10.68	23		454	339	57.25	42.75
6	19	9	6	15	790	10.64	24		419	371	53.04	46.96
8	20	9	5	16	790	10.64	25		402	388	50.89	49.11
6	3	9	4	17	788	10.61	26		444	344	56.35	43.65
10	15	9	5	17	788	10.61	27		481	307	61.04	38.96
6	3	9	4	16	787	10.6	28		401	386	50.95	49.05
8	12	9	4	15	787	10.6	29		384	403	48.79	51.21
7	24	9	6	15	786	10.59	30		425	361	54.07	45.93
7	1	9	4	16	784	10.56	31		409	375	52.17	47.83
9	2	9	4	16	784	10.56	32		408	376	52.04	47.96
4	24	9	6	15	783	10.55	33		397	386	50.7	49.3
6	5	9	6	16	783	10.55	34		428	355	54.66	45.34
9	4	9	6	13	782	10.53	35		401	381	51.28	48.72
6	4	9	5	16	779	10.49	36		391	388	50.19	49.81
7	2	9	5	14	779	10.49	37		400	379	51.35	48.65
10	16	9	6	16	778	10.48	38		423	355	54.37	45.63
7	1	9	4	18	777	10.47	39		476	301	61.26	38.74
7	16	9	5	15	776	10.45	40		420	356	54.12	45.88
5	29	9	6	15	774	10.43	41	7424	417	357	53.88	46.12
6	6	9	7	11	772	10.4	42		430	342	55.7	44.3
6	30	9	3	17	772	10.4	43		445	327	57.64	42.36
7	2	9	5	18	772	10.4	44		484	288	62.69	37.31
7	24	9	6	16	772	10.4	45		420	352	54.4	45.6
8	21	9	6	15	772	10.4	46		423	349	54.79	45.21
9	4	9	6	17	772	10.4	47		450	322	58.29	41.71
5	1	9	6	15	771	10.39	48		403	368	52.27	47.73
5	22	9	6	17	771	10.39	49		470	301	60.96	39.04
8	21	9	6	14	771	10.39	50		399	372	51.75	48.25
9	11	9	6	16	771	10.39	51		411	360	53.31	46.69
7	17	9	6	15	770	10.37	52		425	345	55.19	44.81
8	11	9	3	15	770	10.37	53		416	354	54.03	45.97
10	15	9	5	16	770	10.37	54		407	363	52.86	47.14
4	10	9	6	15	769	10.36	55		429	340	55.79	44.21
9	4	9	6	15	769	10.36	56		411	358	53.45	46.55
10	2	9	6	15	769	10.36	57		404	365	52.54	47.46
10	16	9	6	15	768	10.34	58		422	346	54.95	45.05
8	19	9	4	17	767	10.33	59		437	330	56.98	43.02
8	3	9	2	15	766	10.32	60		432	334	56.4	43.6
8	28	9	6	16	766	10.32	61	7424	411	355	53.66	46.34
5	8	9	6	15	765	10.3	62		405	360	52.94	47.06
6	4	9	5	17	765	10.3	63		453	312	59.22	40.78
9	3	9	5	17	765	10.3	64		434	331	56.73	43.27
10	16	9	6	17	765	10.3	65		439	326	57.39	42.61
8	12	9	4	16	764	10.29	66		401	363	52.49	47.51
6	19	9	6	14	763	10.28	67		412	351	54	46
8	12	9	4	17	762	10.26	68		457	305	59.97	40.03
7	7	9	3	16	761	10.25	69		384	377	50.46	49.54

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
10	2	9	6	16	761	10.25	70		411	350	54.01	45.99
6	25	9	5	15	760	10.24	71		396	364	52.11	47.89
7	22	9	4	15	760	10.24	72		431	329	56.71	43.29
8	7	9	6	16	760	10.24	73		399	361	52.5	47.5
6	12	9	6	15	758	10.21	74		374	384	49.34	50.66
7	21	9	3	16	757	10.2	75		406	351	53.63	46.37
9	10	9	5	16	757	10.2	76		394	363	52.05	47.95
7	3	9	6	11	756	10.18	77		368	388	48.68	51.32
7	15	9	4	16	756	10.18	78		400	356	52.91	47.09
7	17	9	6	17	756	10.18	79		460	296	60.85	39.15
8	28	9	6	15	756	10.18	80		443	313	58.6	41.4
7	8	9	4	16	755	10.17	81	7424	387	368	51.26	48.74
7	10	9	6	15	755	10.17	82		382	373	50.6	49.4
8	5	9	4	16	755	10.17	83		389	366	51.52	48.48
10	8	9	5	16	755	10.17	84		381	374	50.46	49.54
5	20	9	4	17	754	10.16	85		444	310	58.89	41.11
5	21	9	5	16	754	10.16	86		410	344	54.38	45.62
6	25	9	5	16	753	10.14	87		392	361	52.06	47.94
6	26	9	6	15	753	10.14	88		410	343	54.45	45.55
8	7	9	6	15	753	10.14	89		400	353	53.12	46.88
8	27	9	5	15	753	10.14	90		420	333	55.78	44.22
9	8	9	3	15	753	10.14	91		374	379	49.67	50.33
8	4	9	3	16	752	10.13	92		388	364	51.6	48.4
6	6	9	7	13	751	10.12	93		307	444	40.88	59.12
7	1	9	4	14	751	10.12	94		407	344	54.19	45.81
10	9	9	6	17	751	10.12	95		441	310	58.72	41.28
5	27	9	4	17	750	10.1	96		420	330	56	44
7	28	9	3	16	750	10.1	97		399	351	53.2	46.8
9	3	9	5	15	750	10.1	98		407	343	54.27	45.73
10	6	9	3	17	750	10.1	99		424	326	56.53	43.47
5	26	9	3	16	749	10.09	100		366	383	48.87	51.13
9	1	9	3	17	749	10.09	101	7424	428	321	57.14	42.86
6	26	9	6	17	748	10.08	102		375	373	50.13	49.87
7	14	9	3	16	748	10.08	103		387	361	51.74	48.26
7	30	9	5	17	748	10.08	104		426	322	56.95	43.05
8	6	9	5	17	748	10.08	105		437	311	58.42	41.58
6	30	9	3	16	747	10.06	106		398	349	53.28	46.72
7	30	9	5	16	747	10.06	107		407	340	54.48	45.52
8	3	9	2	17	747	10.06	108		434	313	58.1	41.9
5	21	9	5	15	746	10.05	109		395	351	52.95	47.05
9	2	9	4	15	746	10.05	110		379	367	50.8	49.2
6	18	9	5	17	745	10.04	111		407	338	54.63	45.37
7	7	9	3	15	745	10.04	112		406	339	54.5	45.5
7	9	9	5	14	745	10.04	113		384	361	51.54	48.46
8	27	9	5	16	745	10.04	114		399	346	53.56	46.44
7	16	9	5	16	744	10.02	115		398	346	53.49	46.51
5	15	9	6	15	743	10.01	116		367	376	49.39	50.61
6	30	9	3	15	743	10.01	117		388	355	52.22	47.78
7	22	9	4	16	743	10.01	118		391	352	52.62	47.38
8	6	9	5	16	743	10.01	119		409	334	55.05	44.95
8	14	9	6	16	743	10.01	120		391	352	52.62	47.38
10	8	9	5	17	743	10.01	121	7424	437	306	58.82	41.18

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
6	10	9	4	17	742	9.99	122		429	313	57.82	42.18
7	6	9	2	17	742	9.99	123		431	311	58.09	41.91
7	10	9	6	14	742	9.99	124		392	350	52.83	47.17
8	14	9	6	15	742	9.99	125		388	354	52.29	47.71
9	25	9	6	16	742	9.99	126		361	381	48.65	51.35
5	28	9	5	15	741	9.98	127		387	354	52.23	47.77
5	28	9	5	16	741	9.98	128		384	357	51.82	48.18
7	31	9	6	17	741	9.98	129		445	296	60.05	39.95
8	3	9	2	16	741	9.98	130		405	336	54.66	45.34
10	7	9	4	16	741	9.98	131		391	350	52.77	47.23
11	10	9	3	16	741	9.98	132		389	352	52.5	47.5
5	20	9	4	16	740	9.97	133		376	364	50.81	49.19
6	4	9	5	15	740	9.97	134		386	354	52.16	47.84
7	9	9	5	17	740	9.97	135		415	325	56.08	43.92
8	31	9	2	17	740	9.97	136		422	318	57.03	42.97
9	18	9	6	15	740	9.97	137		411	329	55.54	44.46
9	30	9	4	17	740	9.97	138		431	309	58.24	41.76
6	5	9	6	15	739	9.95	139		375	364	50.74	49.26
5	22	9	6	14	738	9.94	140		395	343	53.52	46.48
7	31	9	6	13	738	9.94	141	7424	366	372	49.59	50.41
8	6	9	5	15	738	9.94	142		387	351	52.44	47.56
6	5	9	6	17	737	9.93	143		400	337	54.27	45.73
7	31	9	6	12	737	9.93	144		371	366	50.34	49.66
8	17	9	2	17	737	9.93	145		438	299	59.43	40.57
9	17	9	5	16	737	9.93	146		378	359	51.29	48.71
7	2	9	5	13	736	9.91	147		371	365	50.41	49.59
7	10	9	6	17	736	9.91	148		395	341	53.67	46.33
8	27	9	5	17	736	9.91	149		411	325	55.84	44.16
8	31	9	2	16	736	9.91	150		363	373	49.32	50.68
9	9	9	4	16	736	9.91	151		389	347	52.85	47.15
12	18	9	6	16	736	9.91	152		387	349	52.58	47.42
5	22	9	6	13	735	9.9	153		371	364	50.48	49.52
5	26	9	3	17	735	9.9	154		435	300	59.18	40.82
6	3	9	4	15	735	9.9	155		377	358	51.29	48.71
6	11	9	5	17	735	9.9	156		430	305	58.5	41.5
6	25	9	5	17	734	9.89	157		401	333	54.63	45.37
7	1	9	4	13	734	9.89	158		371	363	50.54	49.46
7	9	9	5	16	734	9.89	159		358	376	48.77	51.23
8	11	9	3	16	734	9.89	160		373	361	50.82	49.18
5	27	9	4	16	733	9.87	161	7424	385	348	52.52	47.48
5	29	9	6	16	733	9.87	162		377	356	51.43	48.57
7	14	9	3	17	733	9.87	163		424	309	57.84	42.16
9	16	9	4	17	733	9.87	164		429	304	58.53	41.47
10	3	9	7	12	733	9.87	165		334	399	45.57	54.43
5	18	9	2	16	732	9.86	166		386	346	52.73	47.27
8	11	9	3	17	732	9.86	167		414	318	56.56	43.44
8	21	9	6	16	732	9.86	168		392	340	53.55	46.45
10	1	9	5	16	732	9.86	169		370	362	50.55	49.45
6	24	9	4	16	731	9.85	170		384	347	52.53	47.47
7	2	9	5	12	731	9.85	171		362	369	49.52	50.48
8	1	9	7	12	731	9.85	172		353	378	48.29	51.71
9	11	9	6	15	731	9.85	173		388	343	53.08	46.92

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
5	1	9	6	16	730	9.83	174		399	331	54.66	45.34
5	14	9	5	16	730	9.83	175		374	356	51.23	48.77
7	27	9	2	17	730	9.83	176		428	302	58.63	41.37
8	18	9	3	16	730	9.83	177		402	328	55.07	44.93
9	4	9	6	12	730	9.83	178		363	367	49.73	50.27
9	17	9	5	15	730	9.83	179		388	342	53.15	46.85
10	2	9	6	14	730	9.83	180		368	362	50.41	49.59
10	9	9	6	13	730	9.83	181	7424	404	326	55.34	44.66
10	9	9	6	14	730	9.83	182		385	345	52.74	47.26
7	17	9	6	14	729	9.82	183		405	324	55.56	44.44
8	28	9	6	17	729	9.82	184		416	313	57.06	42.94
11	5	9	5	16	729	9.82	185		406	323	55.69	44.31
6	2	9	3	16	728	9.81	186		391	337	53.71	46.29
9	24	9	5	16	728	9.81	187		391	337	53.71	46.29
5	19	9	3	17	727	9.79	188		406	321	55.85	44.15
5	8	9	6	17	726	9.78	189		424	302	58.4	41.6
11	3	9	3	17	726	9.78	190		418	308	57.58	42.42
4	24	9	6	16	725	9.77	191		378	347	52.14	47.86
5	15	9	6	16	725	9.77	192		355	370	48.97	51.03
5	21	9	5	17	725	9.77	193		439	286	60.55	39.45
6	1	9	2	16	725	9.77	194		380	345	52.41	47.59
5	28	9	5	17	724	9.75	195		401	323	55.39	44.61
7	30	9	5	14	724	9.75	196		390	334	53.87	46.13
8	17	9	2	16	724	9.75	197		372	352	51.38	48.62
9	2	9	4	17	724	9.75	198		411	313	56.77	43.23
9	22	9	3	17	724	9.75	199		416	308	57.46	42.54
9	28	9	2	16	724	9.75	200		388	336	53.59	46.41

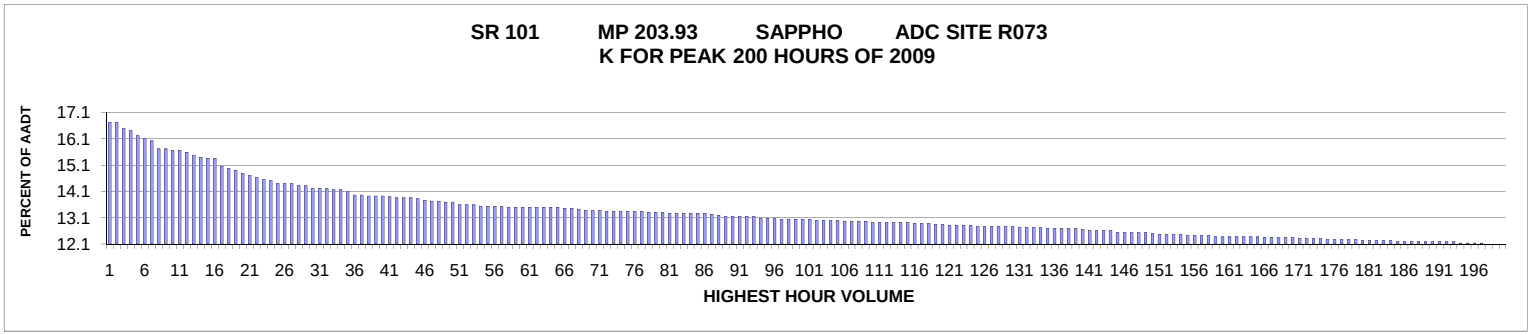

AADT= 2578 **K 30 FACTOR=** 14.2 **K 100 FACTOR=** 13.03 **K 200 FACTOR=** 12.1 **D FACTOR=** 55.56

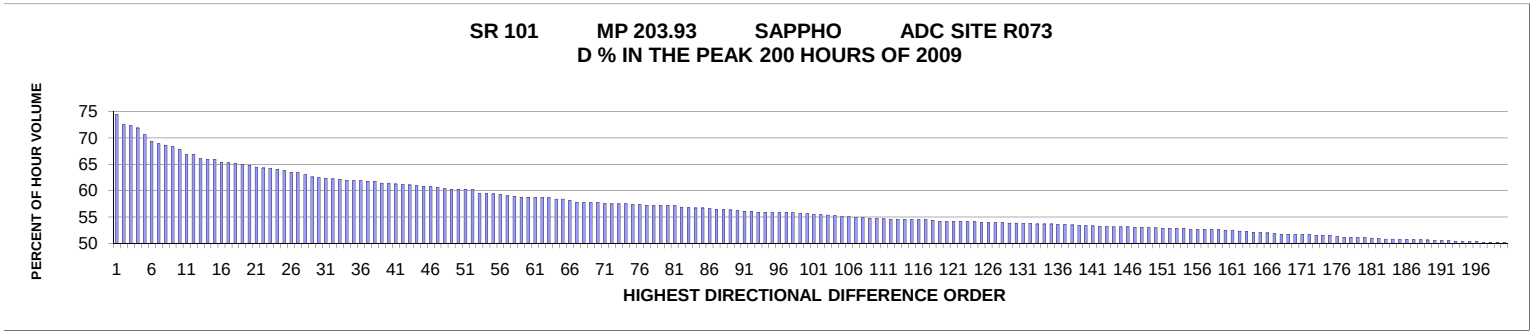

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	2	9	1	13	431	16.72	1	2578	276	155	64.04	35.96
8	16	9	1	14	431	16.72	2		246	185	57.08	42.92
8	23	9	1	15	425	16.49	3		261	164	61.41	38.59
7	5	9	1	12	423	16.41	4		290	133	68.56	31.44
8	2	9	1	14	418	16.21	5		225	193	53.83	46.17
7	5	9	1	13	415	16.1	6		309	106	74.46	25.54
8	16	9	1	13	413	16.02	7		234	179	56.66	43.34
7	26	9	1	13	405	15.71	8		215	190	53.09	46.91
8	1	9	7	12	405	15.71	9		176	229	43.46	56.54
7	5	9	1	14	404	15.67	10		270	134	66.83	33.17
7	26	9	1	15	404	15.67	11		256	148	63.37	36.63
8	16	9	1	15	402	15.59	12		236	166	58.71	41.29
7	3	9	6	16	399	15.48	13		188	211	47.12	52.88
8	2	9	1	15	397	15.4	14		247	150	62.22	37.78
7	3	9	6	15	396	15.36	15		156	240	39.39	60.61
9	12	9	7	16	396	15.36	16		213	183	53.79	46.21
8	16	9	1	16	388	15.05	17		237	151	61.08	38.92

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	5	9	1	16	386	14.97	18		266	120	68.91	31.09
8	1	9	7	15	384	14.9	19		172	212	44.79	55.21
8	2	9	1	16	381	14.78	20		245	136	64.3	35.7
8	30	9	1	17	379	14.7	21	2578	259	120	68.34	31.66
9	20	9	1	17	377	14.62	22		271	106	71.88	28.12
8	15	9	7	14	375	14.55	23		169	206	45.07	54.93
7	19	9	1	15	374	14.51	24		222	152	59.36	40.64
8	6	9	5	12	371	14.39	25		159	212	42.86	57.14
8	14	9	6	16	371	14.39	26		209	162	56.33	43.67
8	16	9	1	12	371	14.39	27		195	176	52.56	47.44
8	21	9	6	17	369	14.31	28		190	179	51.49	48.51
8	23	9	1	14	369	14.31	29		230	139	62.33	37.67
7	3	9	6	12	366	14.2	30		140	226	38.25	61.75
7	31	9	6	15	366	14.2	31		174	192	47.54	52.46
9	12	9	7	15	366	14.2	32		177	189	48.36	51.64
8	15	9	7	12	365	14.16	33		139	226	38.08	61.92
8	22	9	7	17	365	14.16	34		213	152	58.36	41.64
7	26	9	1	16	363	14.08	35		222	141	61.16	38.84
7	3	9	6	14	360	13.96	36		137	223	38.06	61.94
8	2	9	1	12	360	13.96	37		217	143	60.28	39.72
8	1	9	7	13	359	13.93	38		130	229	36.21	63.79
8	19	9	4	15	359	13.93	39		185	174	51.53	48.47
8	30	9	1	16	359	13.93	40		240	119	66.85	33.15
8	19	9	4	16	358	13.89	41	2578	209	149	58.38	41.62
7	4	9	7	12	357	13.85	42		105	252	29.41	70.59
7	5	9	1	15	357	13.85	43		230	127	64.43	35.57
7	26	9	1	14	357	13.85	44		204	153	57.14	42.86
9	13	9	1	16	356	13.81	45		235	121	66.01	33.99
7	3	9	6	17	355	13.77	46		151	204	42.54	57.46
7	12	9	1	12	354	13.73	47		208	146	58.76	41.24
8	9	9	1	13	354	13.73	48		208	146	58.76	41.24
8	30	9	1	12	353	13.69	49		191	162	54.11	45.89
8	30	9	1	18	353	13.69	50		256	97	72.52	27.48
7	25	9	7	17	350	13.58	51		179	171	51.14	48.86
8	1	9	7	16	350	13.58	52		177	173	50.57	49.43
8	22	9	7	16	350	13.58	53		174	176	49.71	50.29
7	31	9	6	16	349	13.54	54		166	183	47.56	52.44
8	1	9	7	14	349	13.54	55		152	197	43.55	56.45
8	15	9	7	17	349	13.54	56		198	151	56.73	43.27
8	18	9	3	16	349	13.54	57		191	158	54.73	45.27
7	3	9	6	13	348	13.5	58		122	226	35.06	64.94
7	11	9	7	17	348	13.5	59		213	135	61.21	38.79
7	25	9	7	12	348	13.5	60		147	201	42.24	57.76
7	26	9	1	12	348	13.5	61	2578	180	168	51.72	48.28
7	31	9	6	17	348	13.5	62		186	162	53.45	46.55
8	18	9	3	17	348	13.5	63		202	146	58.05	41.95
8	19	9	4	14	348	13.5	64		187	161	53.74	46.26
8	22	9	7	14	348	13.5	65		154	194	44.25	55.75
8	2	9	1	17	347	13.46	66		193	154	55.62	44.38
8	7	9	6	17	347	13.46	67		191	156	55.04	44.96
8	15	9	7	16	346	13.42	68		187	159	54.05	45.95
7	21	9	3	17	345	13.38	69		188	157	54.49	45.51

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	24	9	6	12	345	13.38	70		160	185	46.38	53.62
8	21	9	6	16	345	13.38	71		183	162	53.04	46.96
7	19	9	1	14	344	13.34	72		207	137	60.17	39.83
8	9	9	1	16	344	13.34	73		221	123	64.24	35.76
8	14	9	6	13	344	13.34	74		158	186	45.93	54.07
8	17	9	2	17	344	13.34	75		203	141	59.01	40.99
8	28	9	6	12	344	13.34	76		163	181	47.38	52.62
8	28	9	6	17	344	13.34	77		164	180	47.67	52.33
7	5	9	1	17	343	13.3	78		238	105	69.39	30.61
7	24	9	6	17	343	13.3	79		161	182	46.94	53.06
7	31	9	6	12	343	13.3	80		156	187	45.48	54.52
8	8	9	7	16	342	13.27	81	2578	175	167	51.17	48.83
8	14	9	6	17	342	13.27	82		183	159	53.51	46.49
8	21	9	6	15	342	13.27	83		174	168	50.88	49.12
8	22	9	7	13	342	13.27	84		146	196	42.69	57.31
8	23	9	1	13	342	13.27	85		210	132	61.4	38.6
8	30	9	1	13	342	13.27	86		208	134	60.82	39.18
7	3	9	6	18	341	13.23	87		141	200	41.35	58.65
8	14	9	6	12	340	13.19	88		156	184	45.88	54.12
7	4	9	7	11	339	13.15	89		94	245	27.73	72.27
7	17	9	6	16	339	13.15	90		177	162	52.21	47.79
7	25	9	7	14	339	13.15	91		151	188	44.54	55.46
8	6	9	5	15	339	13.15	92		185	154	54.57	45.43
8	14	9	6	14	339	13.15	93		170	169	50.15	49.85
8	1	9	7	18	337	13.07	94		178	159	52.82	47.18
8	6	9	5	13	337	13.07	95		158	179	46.88	53.12
8	18	9	3	14	337	13.07	96		146	191	43.32	56.68
7	11	9	7	16	336	13.03	97		184	152	54.76	45.24
7	27	9	2	16	336	13.03	98		193	143	57.44	42.56
8	13	9	5	16	336	13.03	99		181	155	53.87	46.13
8	19	9	4	12	336	13.03	100		153	183	45.54	54.46
8	22	9	7	15	336	13.03	101	2578	153	183	45.54	54.46
7	23	9	5	17	335	12.99	102		187	148	55.82	44.18
7	24	9	6	15	335	12.99	103		157	178	46.87	53.13
8	15	9	7	15	335	12.99	104		161	174	48.06	51.94
9	13	9	1	15	335	12.99	105		207	128	61.79	38.21
7	20	9	2	17	334	12.96	106		177	157	52.99	47.01
8	14	9	6	15	334	12.96	107		172	162	51.5	48.5
8	30	9	1	15	334	12.96	108		212	122	63.47	36.53
9	11	9	6	17	334	12.96	109		180	154	53.89	46.11
7	21	9	3	15	333	12.92	110		172	161	51.65	48.35
7	27	9	2	15	333	12.92	111		165	168	49.55	50.45
8	6	9	5	16	333	12.92	112		186	147	55.86	44.14
8	7	9	6	16	333	12.92	113		166	167	49.85	50.15
8	17	9	2	15	333	12.92	114		164	169	49.25	50.75
9	12	9	7	17	333	12.92	115		177	156	53.15	46.85
7	18	9	7	16	332	12.88	116		155	177	46.69	53.31
7	19	9	1	12	332	12.88	117		195	137	58.73	41.27
8	17	9	2	16	332	12.88	118		184	148	55.42	44.58
7	25	9	7	16	331	12.84	119		180	151	54.38	45.62
8	23	9	1	16	331	12.84	120		216	115	65.26	34.74
7	12	9	1	15	330	12.8	121	2578	215	115	65.15	34.85

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	8	9	7	13	330	12.8	122		134	196	40.61	59.39
8	15	9	7	13	330	12.8	123		124	206	37.58	62.42
8	17	9	2	12	330	12.8	124		159	171	48.18	51.82
7	12	9	1	16	329	12.76	125		215	114	65.35	34.65
8	1	9	7	17	329	12.76	126		158	171	48.02	51.98
8	5	9	4	16	329	12.76	127		189	140	57.45	42.55
8	18	9	3	15	329	12.76	128		173	156	52.58	47.42
9	6	9	1	14	329	12.76	129		161	168	48.94	51.06
9	20	9	1	15	329	12.76	130		213	116	64.74	35.26
7	30	9	5	15	328	12.72	131		154	174	46.95	53.05
7	31	9	6	13	328	12.72	132		151	177	46.04	53.96
8	6	9	5	14	328	12.72	133		176	152	53.66	46.34
9	4	9	6	17	328	12.72	134		179	149	54.57	45.43
8	7	9	6	12	327	12.68	135		152	175	46.48	53.52
8	16	9	1	17	327	12.68	136		197	130	60.24	39.76
8	20	9	5	16	327	12.68	137		164	163	50.15	49.85
8	21	9	6	12	327	12.68	138		161	166	49.24	50.76
8	29	9	7	15	327	12.68	139		169	158	51.68	48.32
7	10	9	6	17	326	12.65	140		152	174	46.63	53.37
7	19	9	1	16	325	12.61	141	2578	202	123	62.15	37.85
7	26	9	1	17	325	12.61	142		201	124	61.85	38.15
8	1	9	7	19	325	12.61	143		186	139	57.23	42.77
8	3	9	2	12	325	12.61	144		149	176	45.85	54.15
7	24	9	6	14	323	12.53	145		153	170	47.37	52.63
7	29	9	4	16	323	12.53	146		174	149	53.87	46.13
8	2	9	1	11	323	12.53	147		181	142	56.04	43.96
8	8	9	7	14	323	12.53	148		131	192	40.56	59.44
8	23	9	1	12	323	12.53	149		182	141	56.35	43.65
8	20	9	5	15	322	12.49	150		181	141	56.21	43.79
7	12	9	1	13	321	12.45	151		195	126	60.75	39.25
7	16	9	5	17	321	12.45	152		164	157	51.09	48.91
7	18	9	7	17	321	12.45	153		171	150	53.27	46.73
8	21	9	6	14	321	12.45	154		176	145	54.83	45.17
7	22	9	4	16	320	12.41	155		172	148	53.75	46.25
7	23	9	5	16	320	12.41	156		162	158	50.63	49.38
7	24	9	6	16	320	12.41	157		156	164	48.75	51.25
8	7	9	6	18	320	12.41	158		183	137	57.19	42.81
7	11	9	7	13	319	12.37	159		131	188	41.07	58.93
7	26	9	1	11	319	12.37	160		154	165	48.28	51.72
7	26	9	1	18	319	12.37	161	2578	201	118	63.01	36.99
8	7	9	6	14	319	12.37	162		141	178	44.2	55.8
8	16	9	1	11	319	12.37	163		158	161	49.53	50.47
9	20	9	1	14	319	12.37	164		184	135	57.68	42.32
9	20	9	1	16	319	12.37	165		216	103	67.71	32.29
8	3	9	2	13	318	12.34	166		150	168	47.17	52.83
8	8	9	7	17	318	12.34	167		183	135	57.55	42.45
8	9	9	1	14	318	12.34	168		176	142	55.35	44.65
8	20	9	5	17	318	12.34	169		192	126	60.38	39.62
9	6	9	1	15	318	12.34	170		158	160	49.69	50.31
8	7	9	6	11	317	12.3	171		140	177	44.16	55.84
8	8	9	7	12	317	12.3	172		134	183	42.27	57.73
8	14	9	6	18	317	12.3	173		158	159	49.84	50.16

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	15	9	7	18	317	12.3	174		191	126	60.25	39.75
7	16	9	5	16	316	12.26	175		160	156	50.63	49.37
7	20	9	2	14	316	12.26	176		159	157	50.32	49.68
7	22	9	4	17	316	12.26	177		174	142	55.06	44.94
7	29	9	4	17	316	12.26	178		167	149	52.85	47.15
8	10	9	2	12	316	12.26	179		156	160	49.37	50.63
7	20	9	2	16	315	12.22	180		156	159	49.52	50.48
7	23	9	5	15	315	12.22	181	2578	176	139	55.87	44.13
8	4	9	3	13	315	12.22	182		146	169	46.35	53.65
8	10	9	2	15	315	12.22	183		175	140	55.56	44.44
8	19	9	4	17	315	12.22	184		197	118	62.54	37.46
6	27	9	7	17	314	12.18	185		176	138	56.05	43.95
7	1	9	4	15	314	12.18	186		166	148	52.87	47.13
7	11	9	7	12	314	12.18	187		107	207	34.08	65.92
7	17	9	6	18	314	12.18	188		144	170	45.86	54.14
8	2	9	1	18	314	12.18	189		207	107	65.92	34.08
8	6	9	5	18	314	12.18	190		180	134	57.32	42.68
8	17	9	2	14	314	12.18	191		154	160	49.04	50.96
8	28	9	6	15	314	12.18	192		165	149	52.55	47.45
9	6	9	1	16	314	12.18	193		186	128	59.24	40.76
7	6	9	2	16	313	12.14	194		178	135	56.87	43.13
7	27	9	2	12	313	12.14	195		142	171	45.37	54.63
8	20	9	5	12	313	12.14	196		150	163	47.92	52.08
9	4	9	6	16	313	12.14	197		159	154	50.8	49.2
7	19	9	1	13	312	12.1	198		190	122	60.9	39.1
7	30	9	5	18	312	12.1	199		180	132	57.69	42.31
8	3	9	2	16	312	12.1	200		157	155	50.32	49.68

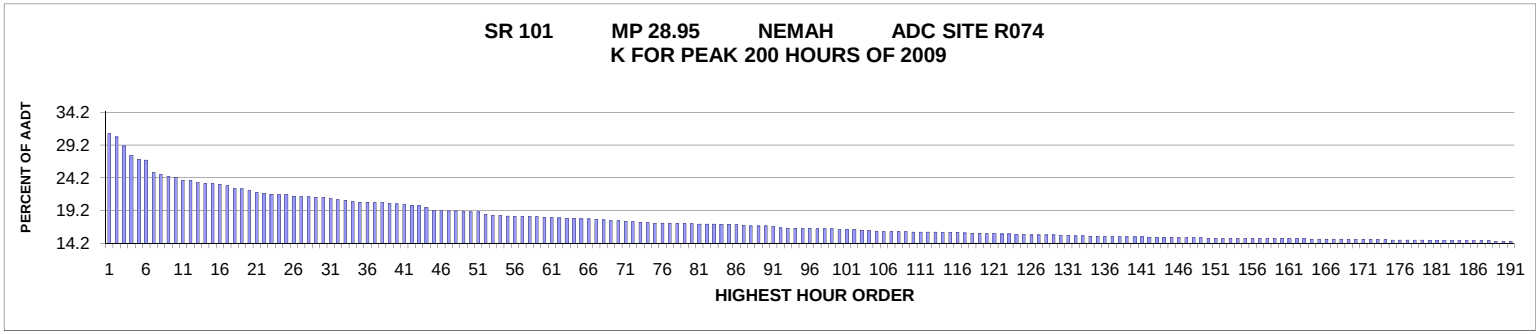

AADT= 2267 **K 30 FACTOR=** 21.97 **K 100 FACTOR=** 16.76 **K 200 FACTOR=** 14.47 **D FACTOR=** 61.04

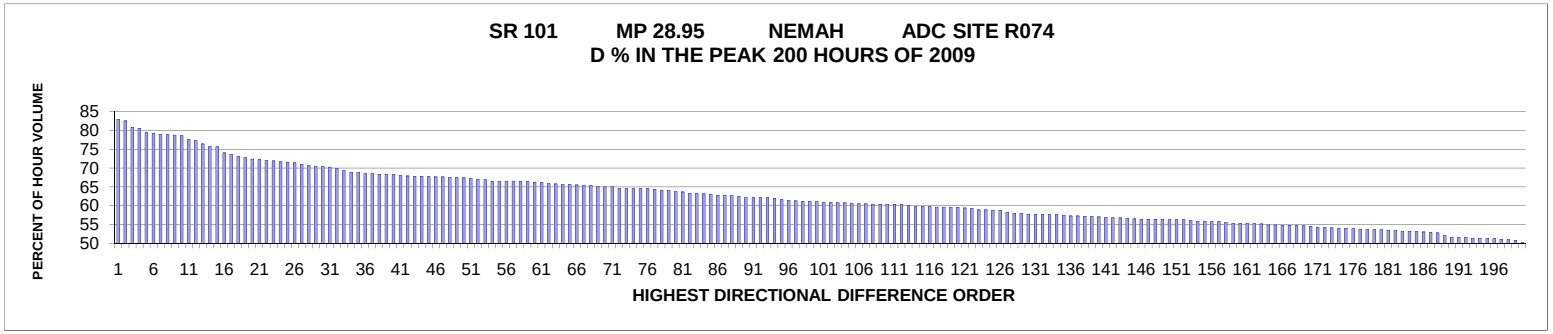

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	5	9	1	14	701	30.92	1	2267	551	150	78.6	21.4
7	5	9	1	13	689	30.39	2		555	134	80.55	19.45
7	5	9	1	15	658	29.03	3		476	182	72.34	27.66
8	23	9	1	15	625	27.57	4		411	214	65.76	34.24
7	5	9	1	12	612	27	5		505	107	82.52	17.48
8	23	9	1	13	610	26.91	6		405	205	66.39	33.61
8	23	9	1	14	566	24.97	7		353	213	62.37	37.63
8	23	9	1	16	560	24.7	8		374	186	66.79	33.21
7	3	9	6	13	553	24.39	9		151	402	27.31	72.69
5	25	9	2	13	550	24.26	10		425	125	77.27	22.73
7	19	9	1	15	540	23.82	11		366	174	67.78	32.22
8	23	9	1	12	539	23.78	12		358	181	66.42	33.58
7	26	9	1	14	532	23.47	13		294	238	55.26	44.74
7	5	9	1	16	529	23.33	14		380	149	71.83	28.17
8	2	9	1	13	528	23.29	15		315	213	59.66	40.34
5	25	9	2	12	525	23.16	16		414	111	78.86	21.14
7	26	9	1	15	521	22.98	17		279	242	53.55	46.45

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	16	9	1	16	511	22.54	18		317	194	62.04	37.96
8	16	9	1	15	510	22.5	19		289	221	56.67	43.33
8	2	9	1	12	503	22.19	20		315	188	62.62	37.38
7	26	9	1	12	498	21.97	21	2267	350	148	70.28	29.72
7	19	9	1	13	493	21.75	22		350	143	70.99	29.01
7	26	9	1	13	491	21.66	23		271	220	55.19	44.81
8	2	9	1	15	490	21.61	24		276	214	56.33	43.67
8	9	9	1	14	490	21.61	25		276	214	56.33	43.67
7	3	9	6	14	485	21.39	26		149	336	30.72	69.28
7	3	9	6	15	483	21.31	27		155	328	32.09	67.91
8	16	9	1	13	482	21.26	28		279	203	57.88	42.12
7	5	9	1	11	481	21.22	29		399	82	82.95	17.05
8	16	9	1	14	480	21.17	30		277	203	57.71	42.29
5	25	9	2	14	476	21	31		369	107	77.52	22.48
8	2	9	1	16	472	20.82	32		281	191	59.53	40.47
8	23	9	1	17	470	20.73	33		346	124	73.62	26.38
8	9	9	1	15	466	20.56	34		266	200	57.08	42.92
7	3	9	6	12	464	20.47	35		125	339	26.94	73.06
8	2	9	1	14	464	20.47	36		253	211	54.53	45.47
7	3	9	6	17	462	20.38	37		164	298	35.5	64.5
7	19	9	1	14	462	20.38	38		292	170	63.2	36.8
8	9	9	1	13	459	20.25	39		285	174	62.09	37.91
8	16	9	1	12	458	20.2	40		289	169	63.1	36.9
7	3	9	6	16	456	20.11	41	2267	144	312	31.58	68.42
7	5	9	1	17	454	20.03	42		336	118	74.01	25.99
7	19	9	1	12	451	19.89	43		291	160	64.52	35.48
8	1	9	7	13	446	19.67	44		184	262	41.26	58.74
8	22	9	7	13	436	19.23	45		142	294	32.57	67.43
5	25	9	2	15	435	19.19	46		332	103	76.32	23.68
8	21	9	6	15	434	19.14	47		179	255	41.24	58.76
8	30	9	1	16	434	19.14	48		284	150	65.44	34.56
7	26	9	1	16	430	18.97	49		253	177	58.84	41.16
7	26	9	1	17	430	18.97	50		277	153	64.42	35.58
8	21	9	6	14	430	18.97	51		169	261	39.3	60.7
8	20	9	5	15	422	18.61	52		170	252	40.28	59.72
8	9	9	1	16	419	18.48	53		253	166	60.38	39.62
8	30	9	1	13	418	18.44	54		272	146	65.07	34.93
8	1	9	7	14	416	18.35	55		161	255	38.7	61.3
5	23	9	7	13	415	18.31	56		101	314	24.34	75.66
7	19	9	1	16	415	18.31	57		272	143	65.54	34.46
8	23	9	1	11	415	18.31	58		296	119	71.33	28.67
5	25	9	2	16	414	18.26	59		313	101	75.6	24.4
7	25	9	7	14	412	18.17	60		142	270	34.47	65.53
7	18	9	7	13	411	18.13	61	2267	144	267	35.04	64.96
7	31	9	6	15	409	18.04	62		192	217	46.94	53.06
8	23	9	1	18	408	18	63		292	116	71.57	28.43
7	25	9	7	13	407	17.95	64		160	247	39.31	60.69
8	16	9	1	18	406	17.91	65		269	137	66.26	33.74
8	22	9	7	14	406	17.91	66		161	245	39.66	60.34
7	6	9	2	12	405	17.87	67		269	136	66.42	33.58
7	18	9	7	12	403	17.78	68		150	253	37.22	62.78
7	18	9	7	14	399	17.6	69		134	265	33.58	66.42

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	15	9	7	13	399	17.6	70		158	241	39.6	60.4
8	14	9	6	15	398	17.56	71		180	218	45.23	54.77
7	2	9	5	16	396	17.47	72		133	263	33.59	66.41
8	9	9	1	12	395	17.42	73		267	128	67.59	32.41
8	14	9	6	16	393	17.34	74		154	239	39.19	60.81
7	12	9	1	12	392	17.29	75		270	122	68.88	31.12
8	30	9	1	15	392	17.29	76		248	144	63.27	36.73
7	31	9	6	14	391	17.25	77		173	218	44.25	55.75
7	24	9	6	14	390	17.2	78		177	213	45.38	54.62
8	14	9	6	13	390	17.2	79		199	191	51.03	48.97
8	30	9	1	14	389	17.16	80		264	125	67.87	32.13
8	20	9	5	14	388	17.12	81	2267	157	231	40.46	59.54
8	21	9	6	17	388	17.12	82		172	216	44.33	55.67
8	22	9	7	12	388	17.12	83		147	241	37.89	62.11
6	28	9	1	15	387	17.07	84		234	153	60.47	39.53
7	27	9	2	16	387	17.07	85		158	229	40.83	59.17
8	2	9	1	17	386	17.03	86		252	134	65.28	34.72
8	17	9	2	16	384	16.94	87		167	217	43.49	56.51
7	2	9	5	15	382	16.85	88		123	259	32.2	67.8
8	22	9	7	17	382	16.85	89		246	136	64.4	35.6
8	30	9	1	12	382	16.85	90		273	109	71.47	28.53
8	21	9	6	16	380	16.76	91		176	204	46.32	53.68
6	21	9	1	15	375	16.54	92		227	148	60.53	39.47
8	14	9	6	14	374	16.5	93		193	181	51.6	48.4
8	19	9	4	15	374	16.5	94		133	241	35.56	64.44
7	24	9	6	13	373	16.45	95		191	182	51.21	48.79
8	17	9	2	14	373	16.45	96		158	215	42.36	57.64
8	16	9	1	17	372	16.41	97		237	135	63.71	36.29
8	14	9	6	17	371	16.37	98		135	236	36.39	63.61
8	28	9	6	16	371	16.37	99		168	203	45.28	54.72
8	1	9	7	15	368	16.23	100		165	203	44.84	55.16
8	15	9	7	12	368	16.23	101	2267	169	199	45.92	54.08
8	17	9	2	12	368	16.23	102		197	171	53.53	46.47
7	19	9	1	17	367	16.19	103		247	120	67.3	32.7
8	15	9	7	15	365	16.1	104		156	209	42.74	57.26
7	31	9	6	18	364	16.06	105		152	212	41.76	58.24
6	21	9	1	14	362	15.97	106		220	142	60.77	39.23
7	12	9	1	13	362	15.97	107		235	127	64.92	35.08
7	12	9	1	15	362	15.97	108		204	158	56.35	43.65
8	21	9	6	13	362	15.97	109		144	218	39.78	60.22
8	9	9	1	17	361	15.92	110		208	153	57.62	42.38
7	6	9	2	13	360	15.88	111		237	123	65.83	34.17
8	17	9	2	15	360	15.88	112		157	203	43.61	56.39
8	28	9	6	15	360	15.88	113		155	205	43.06	56.94
5	25	9	2	11	359	15.84	114		290	69	80.78	19.22
7	30	9	5	13	359	15.84	115		167	192	46.52	53.48
7	31	9	6	13	359	15.84	116		169	190	47.08	52.92
5	23	9	7	12	357	15.75	117		76	281	21.29	78.71
8	19	9	4	14	356	15.7	118		156	200	43.82	56.18
8	20	9	5	13	356	15.7	119		154	202	43.26	56.74
7	12	9	1	14	355	15.66	120		220	135	61.97	38.03
8	24	9	2	13	355	15.66	121	2267	204	151	57.46	42.54

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
4	26	9	1	14	354	15.62	122		249	105	70.34	29.66
8	14	9	6	12	354	15.62	123		190	164	53.67	46.33
7	6	9	2	15	352	15.53	124		195	157	55.4	44.6
8	3	9	2	14	352	15.53	125		156	196	44.32	55.68
7	6	9	2	11	351	15.48	126		232	119	66.1	33.9
7	24	9	6	15	351	15.48	127		136	215	38.75	61.25
7	31	9	6	12	351	15.48	128		185	166	52.71	47.29
7	31	9	6	17	350	15.44	129		141	209	40.29	59.71
8	20	9	5	16	349	15.39	130		156	193	44.7	55.3
8	22	9	7	15	348	15.35	131		167	181	47.99	52.01
8	17	9	2	13	347	15.31	132		147	200	42.36	57.64
8	30	9	1	17	347	15.31	133		227	120	65.42	34.58
7	2	9	5	14	346	15.26	134		113	233	32.66	67.34
7	5	9	1	18	346	15.26	135		249	97	71.97	28.03
7	18	9	7	15	345	15.22	136		128	217	37.1	62.9
8	1	9	7	16	345	15.22	137		149	196	43.19	56.81
6	28	9	1	16	344	15.17	138		205	139	59.59	40.41
7	3	9	6	18	344	15.17	139		107	237	31.1	68.9
7	24	9	6	17	344	15.17	140		128	216	37.21	62.79
8	2	9	1	11	344	15.17	141	2267	235	109	68.31	31.69
5	23	9	7	14	343	15.13	142		95	248	27.7	72.3
7	31	9	6	16	343	15.13	143		145	198	42.27	57.73
8	1	9	7	12	343	15.13	144		122	221	35.57	64.43
6	28	9	1	14	342	15.09	145		234	108	68.42	31.58
6	28	9	1	17	342	15.09	146		227	115	66.37	33.63
8	29	9	7	13	341	15.04	147		146	195	42.82	57.18
7	3	9	6	11	340	15	148		129	211	37.94	62.06
7	27	9	2	12	340	15	149		180	160	52.94	47.06
5	17	9	1	14	339	14.95	150		205	134	60.47	39.53
7	3	9	6	19	339	14.95	151		122	217	35.99	64.01
7	6	9	2	14	339	14.95	152		227	112	66.96	33.04
7	30	9	5	15	339	14.95	153		132	207	38.94	61.06
8	15	9	7	16	339	14.95	154		153	186	45.13	54.87
8	19	9	4	16	339	14.95	155		170	169	50.15	49.85
5	22	9	6	15	338	14.91	156		107	231	31.66	68.34
5	24	9	1	12	338	14.91	157		142	196	42.01	57.99
7	2	9	5	17	338	14.91	158		110	228	32.54	67.46
8	15	9	7	14	338	14.91	159		135	203	39.94	60.06
8	20	9	5	12	338	14.91	160		166	172	49.11	50.89
3	29	9	1	14	337	14.87	161	2267	201	136	59.64	40.36
5	25	9	2	17	337	14.87	162		266	71	78.93	21.07
7	18	9	7	16	337	14.87	163		164	173	48.66	51.34
5	23	9	7	15	336	14.82	164		109	227	32.44	67.56
7	25	9	7	12	336	14.82	165		144	192	42.86	57.14
7	27	9	2	14	336	14.82	166		147	189	43.75	56.25
8	8	9	7	15	336	14.82	167		154	182	45.83	54.17
8	20	9	5	17	336	14.82	168		173	163	51.49	48.51
7	30	9	5	17	335	14.78	169		138	197	41.19	58.81
8	5	9	4	14	335	14.78	170		163	172	48.66	51.34
8	10	9	2	15	335	14.78	171		170	165	50.75	49.25
8	21	9	6	18	335	14.78	172		147	188	43.88	56.12
8	22	9	7	16	335	14.78	173		179	156	53.43	46.57

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	24	9	2	15	334	14.73	174		181	153	54.19	45.81
5	22	9	6	17	333	14.69	175		99	234	29.73	70.27
7	30	9	5	16	333	14.69	176		145	188	43.54	56.46
8	2	9	1	18	333	14.69	177		201	132	60.36	39.64
8	3	9	2	15	333	14.69	178		177	156	53.15	46.85
8	6	9	5	13	333	14.69	179		156	177	46.85	53.15
7	19	9	1	11	332	14.64	180		232	100	69.88	30.12
11	29	9	1	12	332	14.64	181	2267	263	69	79.22	20.78
5	23	9	7	16	331	14.6	182		150	181	45.32	54.68
5	24	9	1	13	331	14.6	183		153	178	46.22	53.78
6	14	9	1	15	331	14.6	184		224	107	67.67	32.33
7	29	9	4	16	331	14.6	185		146	185	44.11	55.89
5	22	9	6	16	330	14.56	186		97	233	29.39	70.61
6	28	9	1	12	330	14.56	187		203	127	61.52	38.48
8	28	9	6	14	330	14.56	188		149	181	45.15	54.85
8	3	9	2	13	329	14.51	189		185	144	56.23	43.77
4	5	9	1	15	328	14.47	190		210	118	64.02	35.98
7	30	9	5	14	328	14.47	191		159	169	48.48	51.52
8	8	9	7	14	327	14.42	192		147	180	44.95	55.05
6	28	9	1	13	326	14.38	193		199	127	61.04	38.96

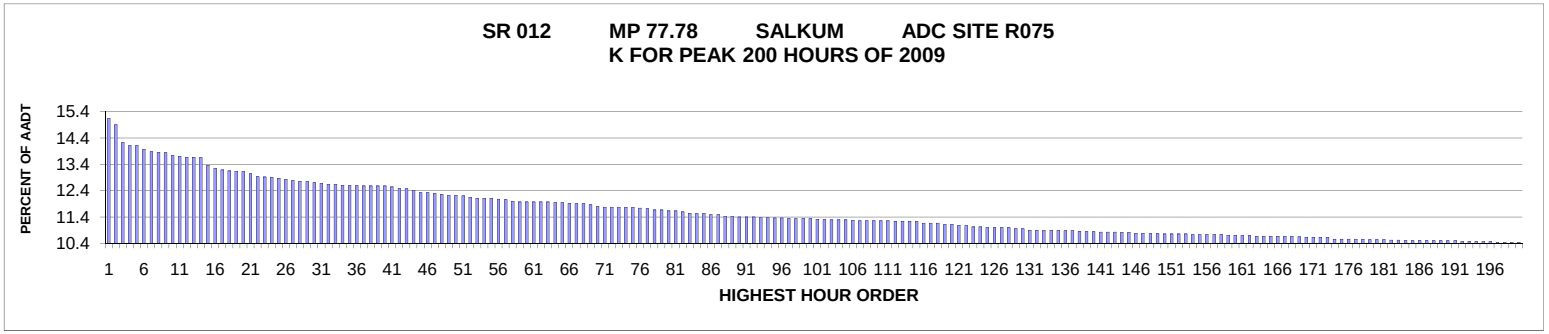

AADT= 6541 **K 30 FACTOR=** 12.7 **K 100 FACTOR=** 11.34 **K 200 FACTOR=** 10.43 **D FACTOR=** 56.87

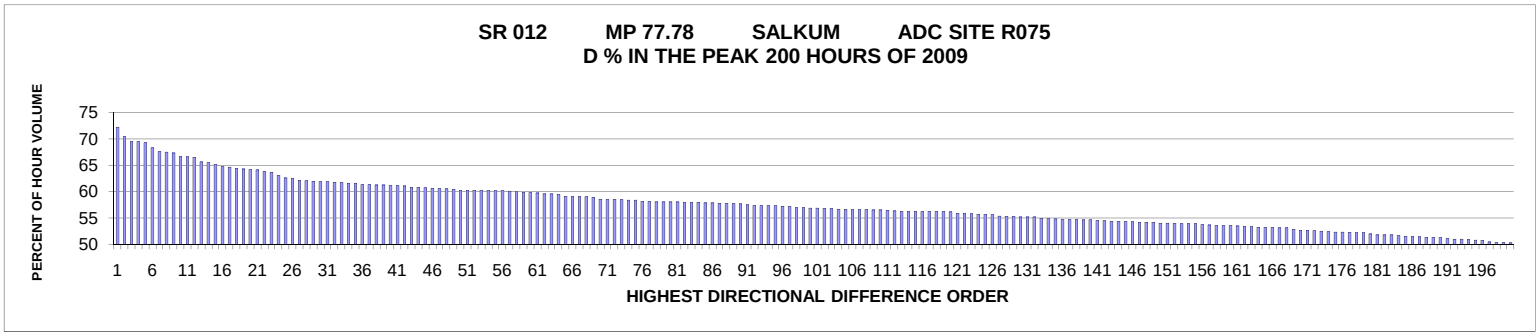

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	2	9	1	14	990	15.14	1	6541	472	518	47.68	52.32
7	19	9	1	13	974	14.89	2		382	592	39.22	60.78
7	26	9	1	13	930	14.22	3		429	501	46.13	53.87
9	4	9	6	18	922	14.1	4		570	352	61.82	38.18
9	7	9	2	14	922	14.1	5		281	641	30.48	69.52
8	9	9	1	13	914	13.97	6		361	553	39.5	60.5
7	26	9	1	14	907	13.87	7		447	460	49.28	50.72
7	19	9	1	14	906	13.85	8		397	509	43.82	56.18
8	2	9	1	13	905	13.84	9		419	486	46.3	53.7
7	26	9	1	16	898	13.73	10		413	485	45.99	54.01
7	26	9	1	12	897	13.71	11		411	486	45.82	54.18
7	5	9	1	14	894	13.67	12		389	505	43.51	56.49
8	9	9	1	14	894	13.67	13		357	537	39.93	60.07
8	16	9	1	14	893	13.65	14		382	511	42.78	57.22
7	19	9	1	15	874	13.36	15		420	454	48.05	51.95
8	23	9	1	14	866	13.24	16		324	542	37.41	62.59
7	31	9	6	15	862	13.18	17		471	391	54.64	45.36

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	5	9	1	13	860	13.15	18		297	563	34.53	65.47
8	2	9	1	15	859	13.13	19		421	438	49.01	50.99
7	26	9	1	15	858	13.12	20		414	444	48.25	51.75
7	26	9	1	17	853	13.04	21	6541	364	489	42.67	57.33
9	7	9	2	13	846	12.93	22		260	586	30.73	69.27
9	4	9	6	19	845	12.92	23		533	312	63.08	36.92
8	16	9	1	13	844	12.9	24		328	516	38.86	61.14
7	24	9	6	18	842	12.87	25		512	330	60.81	39.19
7	17	9	6	17	839	12.83	26		463	376	55.18	44.82
8	14	9	6	16	836	12.78	27		467	369	55.86	44.14
7	24	9	6	17	834	12.75	28		465	369	55.76	44.24
8	16	9	1	15	833	12.74	29		353	480	42.38	57.62
8	9	9	1	16	831	12.7	30		330	501	39.71	60.29
8	9	9	1	15	829	12.67	31		379	450	45.72	54.28
7	17	9	6	16	827	12.64	32		456	371	55.14	44.86
8	1	9	7	17	826	12.63	33		362	464	43.83	56.17
8	2	9	1	12	824	12.6	34		379	445	46	54
9	4	9	6	16	824	12.6	35		493	331	59.83	40.17
7	3	9	6	16	823	12.58	36		477	346	57.96	42.04
7	5	9	1	15	822	12.57	37		402	420	48.91	51.09
7	17	9	6	15	822	12.57	38		504	318	61.31	38.69
7	31	9	6	16	822	12.57	39		502	320	61.07	38.93
9	4	9	6	17	822	12.57	40		489	333	59.49	40.51
8	7	9	6	17	820	12.54	41	6541	494	326	60.24	39.76
8	1	9	7	12	816	12.48	42		493	323	60.42	39.58
7	26	9	1	18	815	12.46	43		295	520	36.2	63.8
8	7	9	6	16	811	12.4	44		437	374	53.88	46.12
8	1	9	7	14	806	12.32	45		465	341	57.69	42.31
8	23	9	1	13	806	12.32	46		288	518	35.73	64.27
7	31	9	6	17	804	12.29	47		482	322	59.95	40.05
8	9	9	1	12	802	12.26	48		347	455	43.27	56.73
7	17	9	6	14	799	12.22	49		468	331	58.57	41.43
8	8	9	7	14	799	12.22	50		438	361	54.82	45.18
8	16	9	1	16	798	12.2	51		327	471	40.98	59.02
9	4	9	6	15	795	12.15	52		478	317	60.13	39.87
5	22	9	6	18	792	12.11	53		490	302	61.87	38.13
7	3	9	6	13	792	12.11	54		448	344	56.57	43.43
8	14	9	6	17	792	12.11	55		437	355	55.18	44.82
5	25	9	2	13	790	12.08	56		264	526	33.42	66.58
9	7	9	2	12	788	12.05	57		219	569	27.79	72.21
6	26	9	6	16	784	11.99	58		441	343	56.25	43.75
7	3	9	6	12	783	11.97	59		428	355	54.66	45.34
7	11	9	7	13	783	11.97	60		472	311	60.28	39.72
7	19	9	1	16	783	11.97	61	6541	369	414	47.13	52.87
8	2	9	1	17	782	11.96	62		315	467	40.28	59.72
9	11	9	6	16	782	11.96	63		412	370	52.69	47.31
7	10	9	6	16	781	11.94	64		418	363	53.52	46.48
8	21	9	6	16	781	11.94	65		423	358	54.16	45.84
5	25	9	2	14	779	11.91	66		260	519	33.38	66.62
7	2	9	5	16	779	11.91	67		423	356	54.3	45.7
8	1	9	7	16	779	11.91	68		362	417	46.47	53.53
7	31	9	6	18	776	11.86	69		467	309	60.18	39.82

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	5	9	1	12	771	11.79	70		265	506	34.37	65.63
7	5	9	1	16	770	11.77	71		361	409	46.88	53.12
8	1	9	7	13	770	11.77	72		477	293	61.95	38.05
8	21	9	6	17	770	11.77	73		402	368	52.21	47.79
7	3	9	6	14	769	11.76	74		447	322	58.13	41.87
8	7	9	6	14	769	11.76	75		437	332	56.83	43.17
8	7	9	6	15	767	11.73	76		410	357	53.46	46.54
8	8	9	7	11	766	11.71	77		456	310	59.53	40.47
5	25	9	2	15	763	11.66	78		296	467	38.79	61.21
8	9	9	1	17	763	11.66	79		326	437	42.73	57.27
8	14	9	6	15	761	11.63	80		416	345	54.66	45.34
8	28	9	6	17	761	11.63	81	6541	418	343	54.93	45.07
7	3	9	6	17	758	11.59	82		414	344	54.62	45.38
5	23	9	7	13	755	11.54	83		466	289	61.72	38.28
5	25	9	2	17	754	11.53	84		223	531	29.58	70.42
7	10	9	6	15	754	11.53	85		437	317	57.96	42.04
7	17	9	6	18	751	11.48	86		430	321	57.26	42.74
9	4	9	6	14	751	11.48	87		402	349	53.53	46.47
7	24	9	6	14	747	11.42	88		406	341	54.35	45.65
7	25	9	7	12	747	11.42	89		408	339	54.62	45.38
8	7	9	6	18	746	11.4	90		482	264	64.61	35.39
8	2	9	1	18	745	11.39	91		289	456	38.79	61.21
8	14	9	6	14	745	11.39	92		421	324	56.51	43.49
7	18	9	7	15	744	11.37	93		396	348	53.23	46.77
8	1	9	7	15	744	11.37	94		356	388	47.85	52.15
7	2	9	5	17	743	11.36	95		405	338	54.51	45.49
8	23	9	1	15	743	11.36	96		312	431	41.99	58.01
6	21	9	1	14	742	11.34	97		322	420	43.4	56.6
7	16	9	5	16	742	11.34	98		368	374	49.6	50.4
7	31	9	6	14	742	11.34	99		407	335	54.85	45.15
8	8	9	7	13	742	11.34	100		433	309	58.36	41.64
7	17	9	6	13	740	11.31	101	6541	386	354	52.16	47.84
7	12	9	1	16	739	11.3	102		312	427	42.22	57.78
8	2	9	1	16	738	11.28	103		350	388	47.43	52.57
8	30	9	1	14	738	11.28	104		314	424	42.55	57.45
9	5	9	7	12	738	11.28	105		441	297	59.76	40.24
7	24	9	6	15	737	11.27	106		397	340	53.87	46.13
7	12	9	1	15	736	11.25	107		318	418	43.21	56.79
8	14	9	6	18	736	11.25	108		451	285	61.28	38.72
8	21	9	6	15	736	11.25	109		407	329	55.3	44.7
9	5	9	7	14	736	11.25	110		399	337	54.21	45.79
9	11	9	6	17	736	11.25	111		419	317	56.93	43.07
7	25	9	7	11	735	11.24	112		418	317	56.87	43.13
8	16	9	1	17	735	11.24	113		293	442	39.86	60.14
9	11	9	6	18	735	11.24	114		449	286	61.09	38.91
5	25	9	2	16	734	11.22	115		233	501	31.74	68.26
6	21	9	1	13	730	11.16	116		299	431	40.96	59.04
7	25	9	7	13	730	11.16	117		406	324	55.62	44.38
9	13	9	1	17	730	11.16	118		277	453	37.95	62.05
7	1	9	4	17	727	11.11	119		390	337	53.65	46.35
8	16	9	1	18	727	11.11	120		278	449	38.24	61.76
7	10	9	6	17	725	11.08	121	6541	405	320	55.86	44.14

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
6	28	9	1	13	724	11.07	122		285	439	39.36	60.64
5	22	9	6	17	721	11.02	123		426	295	59.08	40.92
5	23	9	7	12	721	11.02	124		462	259	64.08	35.92
5	23	9	7	14	719	10.99	125		443	276	61.61	38.39
6	26	9	6	15	719	10.99	126		369	350	51.32	48.68
7	18	9	7	12	719	10.99	127		411	308	57.16	42.84
9	7	9	2	15	719	10.99	128		258	461	35.88	64.12
8	28	9	6	16	717	10.96	129		419	298	58.44	41.56
8	13	9	5	17	716	10.95	130		360	356	50.28	49.72
5	22	9	6	16	713	10.9	131		443	270	62.13	37.87
7	31	9	6	13	713	10.9	132		365	348	51.19	48.81
8	7	9	6	13	713	10.9	133		344	369	48.25	51.75
8	23	9	1	16	713	10.9	134		293	420	41.09	58.91
6	26	9	6	17	712	10.89	135		365	347	51.26	48.74
7	19	9	1	12	711	10.87	136		299	412	42.05	57.95
8	2	9	1	19	711	10.87	137		238	473	33.47	66.53
7	19	9	1	17	710	10.85	138		306	404	43.1	56.9
8	16	9	1	12	709	10.84	139		311	398	43.86	56.14
8	28	9	6	15	709	10.84	140		348	361	49.08	50.92
6	12	9	6	17	708	10.82	141	6541	384	324	54.24	45.76
9	7	9	2	17	708	10.82	142		252	456	35.59	64.41
9	25	9	6	17	708	10.82	143		382	326	53.95	46.05
6	12	9	6	16	707	10.81	144		370	337	52.33	47.67
7	5	9	1	17	707	10.81	145		314	393	44.41	55.59
6	5	9	6	17	705	10.78	146		370	335	52.48	47.52
9	4	9	6	13	705	10.78	147		369	336	52.34	47.66
6	28	9	1	14	704	10.76	148		285	419	40.48	59.52
7	30	9	5	15	704	10.76	149		389	315	55.26	44.74
5	23	9	7	11	703	10.75	150		475	228	67.57	32.43
7	16	9	5	17	703	10.75	151		363	340	51.64	48.36
7	18	9	7	16	703	10.75	152		364	339	51.78	48.22
8	23	9	1	17	703	10.75	153		305	398	43.39	56.61
7	2	9	5	18	702	10.73	154		397	305	56.55	43.45
7	12	9	1	14	702	10.73	155		277	425	39.46	60.54
7	16	9	5	18	702	10.73	156		395	307	56.27	43.73
7	23	9	5	17	702	10.73	157		373	329	53.13	46.87
8	6	9	5	16	702	10.73	158		373	329	53.13	46.87
7	3	9	6	11	700	10.7	159		381	319	54.43	45.57
7	30	9	5	16	700	10.7	160		405	295	57.86	42.14
7	12	9	1	13	699	10.69	161	6541	262	437	37.48	62.52
9	5	9	7	13	699	10.69	162		409	290	58.51	41.49
7	19	9	1	18	698	10.67	163		268	430	38.4	61.6
7	25	9	7	18	698	10.67	164		306	392	43.84	56.16
8	7	9	6	19	698	10.67	165		470	228	67.34	32.66
7	31	9	6	19	697	10.66	166		451	246	64.71	35.29
8	8	9	7	15	697	10.66	167		350	347	50.22	49.78
8	21	9	6	18	697	10.66	168		411	286	58.97	41.03
6	19	9	6	17	696	10.64	169		404	292	58.05	41.95
5	22	9	6	15	695	10.63	170		398	297	57.27	42.73
7	10	9	6	14	695	10.63	171		393	302	56.55	43.45
8	21	9	6	13	695	10.63	172		329	366	47.34	52.66
9	25	9	6	18	695	10.63	173		402	293	57.84	42.16

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	25	9	7	17	691	10.56	174		324	367	46.89	53.11
8	8	9	7	12	691	10.56	175		440	251	63.68	36.32
8	8	9	7	17	691	10.56	176		287	404	41.53	58.47
9	18	9	6	17	691	10.56	177		369	322	53.4	46.6
7	17	9	6	12	690	10.55	178		347	343	50.29	49.71
5	22	9	6	19	689	10.53	179		465	224	67.49	32.51
7	2	9	5	14	689	10.53	180		355	334	51.52	48.48
9	4	9	6	12	689	10.53	181	6541	402	287	58.35	41.65
8	15	9	7	12	688	10.52	182		399	289	57.99	42.01
8	30	9	1	13	688	10.52	183		274	414	39.83	60.17
5	25	9	2	18	687	10.5	184		210	477	30.57	69.43
7	11	9	7	12	687	10.5	185		386	301	56.19	43.81
7	29	9	4	18	687	10.5	186		353	334	51.38	48.62
7	2	9	5	13	686	10.49	187		387	299	56.41	43.59
7	18	9	7	14	686	10.49	188		386	300	56.27	43.73
7	26	9	1	11	686	10.49	189		304	382	44.31	55.69
7	26	9	1	19	686	10.49	190		239	447	34.84	65.16
8	27	9	5	16	686	10.49	191		320	366	46.65	53.35
8	27	9	5	17	685	10.47	192		336	349	49.05	50.95
7	18	9	7	13	684	10.46	193		397	287	58.04	41.96
7	23	9	5	16	684	10.46	194		352	332	51.46	48.54
8	30	9	1	16	684	10.46	195		287	397	41.96	58.04
9	6	9	1	13	684	10.46	196		269	415	39.33	60.67
6	26	9	6	13	683	10.44	197		378	305	55.34	44.66
8	6	9	5	18	683	10.44	198		394	289	57.69	42.31
8	14	9	6	13	683	10.44	199		347	336	50.81	49.19
7	12	9	1	17	682	10.43	200		298	384	43.7	56.3

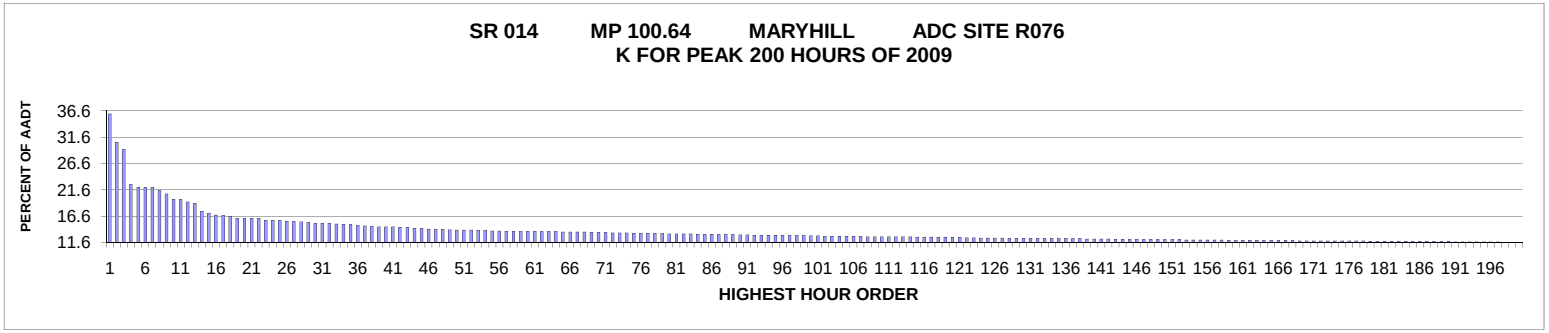

AADT= 2022 **K 30 FACTOR=** 15.23 **K 100 FACTOR=** 12.86 **K 200 FACTOR=** 11.67 **D FACTOR=** 54.51

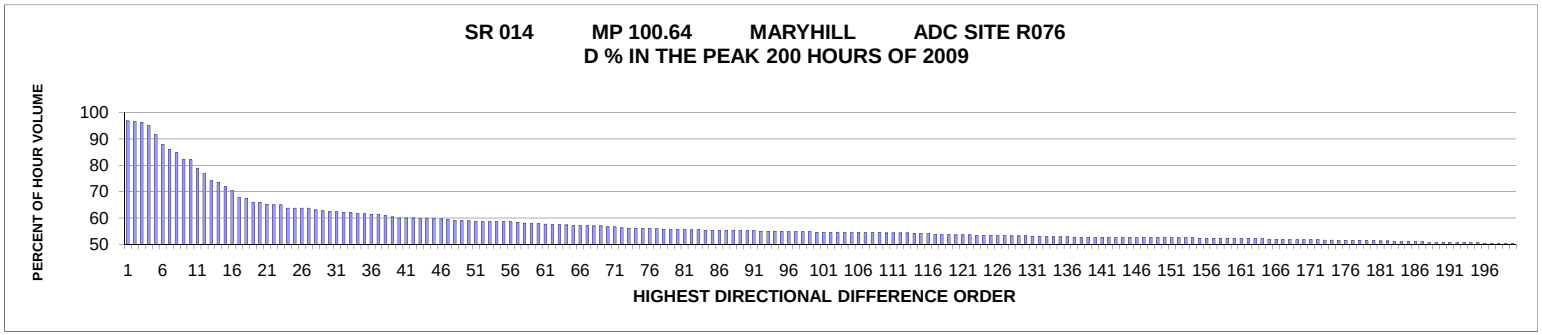

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	22	9	7	23	728	36	1	2022	701	27	96.29	3.71
7	17	9	6	24	619	30.61	2		599	20	96.77	3.23
8	22	9	7	18	592	29.28	3		125	467	21.11	78.89
8	29	9	7	23	457	22.6	4		434	23	94.97	5.03
8	22	9	7	19	447	22.11	5		80	367	17.9	82.1
7	2	9	5	16	446	22.06	6		116	330	26.01	73.99
8	22	9	7	17	446	22.06	7		172	274	38.57	61.43
8	29	9	7	18	434	21.46	8		115	319	26.5	73.5
8	29	9	7	19	421	20.82	9		64	357	15.2	84.8
7	17	9	6	20	400	19.78	10		56	344	14	86
5	11	9	2	17	399	19.73	11		93	306	23.31	76.69
7	17	9	6	19	390	19.29	12		69	321	17.69	82.31
7	2	9	5	17	385	19.04	13		114	271	29.61	70.39
7	2	9	5	15	355	17.56	14		121	234	34.08	65.92
8	29	9	7	17	348	17.21	15		131	217	37.64	62.36
8	16	9	1	14	340	16.82	16		153	187	45	55
5	11	9	2	16	337	16.67	17		95	242	28.19	71.81

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	16	9	1	13	335	16.57	18		144	191	42.99	57.01
8	22	9	7	16	327	16.17	19		153	174	46.79	53.21
9	26	9	7	14	327	16.17	20		172	155	52.6	47.4
8	16	9	1	16	326	16.12	21	2022	171	155	52.45	47.55
8	23	9	1	14	326	16.12	22		171	155	52.45	47.55
8	15	9	7	14	320	15.83	23		154	166	48.13	51.88
9	26	9	7	16	320	15.83	24		204	116	63.75	36.25
8	22	9	7	14	319	15.78	25		179	140	56.11	43.89
8	22	9	7	15	317	15.68	26		167	150	52.68	47.32
9	5	9	7	15	316	15.63	27		166	150	52.53	47.47
8	15	9	7	16	314	15.53	28		181	133	57.64	42.36
5	25	9	2	14	310	15.33	29		129	181	41.61	58.39
8	23	9	1	13	308	15.23	30		162	146	52.6	47.4
9	6	9	1	15	308	15.23	31		170	138	55.19	44.81
9	7	9	2	15	308	15.23	32		159	149	51.62	48.38
8	16	9	1	15	306	15.13	33		169	137	55.23	44.77
8	15	9	7	15	304	15.03	34		155	149	50.99	49.01
8	29	9	7	16	303	14.99	35		147	156	48.51	51.49
9	6	9	1	16	300	14.84	36		160	140	53.33	46.67
9	26	9	7	13	298	14.74	37		139	159	46.64	53.36
9	6	9	1	14	296	14.64	38		135	161	45.61	54.39
8	15	9	7	13	295	14.59	39		117	178	39.66	60.34
9	7	9	2	14	295	14.59	40		121	174	41.02	58.98
8	21	9	6	14	294	14.54	41	2022	172	122	58.5	41.5
5	25	9	2	15	293	14.49	42		139	154	47.44	52.56
7	17	9	6	18	292	14.44	43		106	186	36.3	63.7
7	17	9	6	17	289	14.29	44		131	158	45.33	54.67
5	24	9	1	16	288	14.24	45		138	150	47.92	52.08
8	9	9	1	14	286	14.14	46		135	151	47.2	52.8
8	16	9	1	17	285	14.09	47		193	92	67.72	32.28
9	7	9	2	16	285	14.09	48		150	135	52.63	47.37
9	4	9	6	16	284	14.05	49		162	122	57.04	42.96
5	23	9	7	14	282	13.95	50		116	166	41.13	58.87
7	3	9	6	12	282	13.95	51		153	129	54.26	45.74
8	29	9	7	15	282	13.95	52		136	146	48.23	51.77
8	30	9	1	13	281	13.9	53		140	141	49.82	50.18
9	26	9	7	12	281	13.9	54		98	183	34.88	65.12
8	21	9	6	15	279	13.8	55		156	123	55.91	44.09
9	26	9	7	17	279	13.8	56		166	113	59.5	40.5
5	17	9	1	14	277	13.7	57		124	153	44.77	55.23
5	25	9	2	16	277	13.7	58		158	119	57.04	42.96
8	7	9	6	14	277	13.7	59		139	138	50.18	49.82
8	29	9	7	13	277	13.7	60		172	105	62.09	37.91
9	26	9	7	15	277	13.7	61	2022	141	136	50.9	49.1
7	2	9	5	18	276	13.65	62		102	174	36.96	63.04
7	8	9	4	16	276	13.65	63		176	100	63.77	36.23
8	29	9	7	14	276	13.65	64		151	125	54.71	45.29
7	17	9	6	13	275	13.6	65		149	126	54.18	45.82
7	18	9	7	15	275	13.6	66		139	136	50.55	49.45
8	7	9	6	16	275	13.6	67		144	131	52.36	47.64
9	7	9	2	17	275	13.6	68		135	140	49.09	50.91
9	5	9	7	14	274	13.55	69		133	141	48.54	51.46

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	29	9	7	12	273	13.5	70		141	132	51.65	48.35
5	22	9	6	15	272	13.45	71		163	109	59.93	40.07
5	24	9	1	13	271	13.4	72		104	167	38.38	61.62
5	24	9	1	15	271	13.4	73		150	121	55.35	44.65
7	31	9	6	14	271	13.4	74		140	131	51.66	48.34
8	14	9	6	15	270	13.35	75		129	141	47.78	52.22
8	21	9	6	17	270	13.35	76		140	130	51.85	48.15
8	23	9	1	16	270	13.35	77		150	120	55.56	44.44
8	15	9	7	12	269	13.3	78		102	167	37.92	62.08
8	22	9	7	13	269	13.3	79		133	136	49.44	50.56
7	19	9	1	15	268	13.25	80		140	128	52.24	47.76
8	15	9	7	17	268	13.25	81	2022	174	94	64.93	35.07
8	23	9	1	15	268	13.25	82		149	119	55.6	44.4
9	4	9	6	15	268	13.25	83		160	108	59.7	40.3
6	19	9	6	15	267	13.2	84		145	122	54.31	45.69
8	29	9	7	24	267	13.2	85		258	9	96.63	3.37
9	26	9	7	18	267	13.2	86		170	97	63.67	36.33
5	17	9	1	15	265	13.11	87		142	123	53.58	46.42
8	25	9	3	16	265	13.11	88		133	132	50.19	49.81
9	18	9	6	16	265	13.11	89		144	121	54.34	45.66
7	17	9	6	15	264	13.06	90		121	143	45.83	54.17
7	19	9	1	13	264	13.06	91		109	155	41.29	58.71
7	10	9	6	15	263	13.01	92		130	133	49.43	50.57
8	14	9	6	16	263	13.01	93		135	128	51.33	48.67
6	19	9	6	13	262	12.96	94		125	137	47.71	52.29
9	13	9	1	14	262	12.96	95		132	130	50.38	49.62
7	23	9	5	17	261	12.91	96		151	110	57.85	42.15
7	24	9	6	14	261	12.91	97		125	136	47.89	52.11
8	22	9	7	22	261	12.91	98		229	32	87.74	12.26
9	10	9	5	16	261	12.91	99		132	129	50.57	49.43
7	3	9	6	14	260	12.86	100		141	119	54.23	45.77
9	20	9	1	14	260	12.86	101	2022	121	139	46.54	53.46
5	25	9	2	13	259	12.81	102		118	141	45.56	54.44
8	7	9	6	17	259	12.81	103		126	133	48.65	51.35
8	20	9	5	14	259	12.81	104		124	135	47.88	52.12
8	20	9	5	16	259	12.81	105		123	136	47.49	52.51
8	23	9	1	17	259	12.81	106		142	117	54.83	45.17
8	9	9	1	16	258	12.76	107		151	107	58.53	41.47
8	6	9	5	14	257	12.71	108		128	129	49.81	50.19
8	7	9	6	15	257	12.71	109		137	120	53.31	46.69
8	23	9	1	12	257	12.71	110		123	134	47.86	52.14
5	22	9	6	17	256	12.66	111		136	120	53.13	46.88
7	17	9	6	16	256	12.66	112		121	135	47.27	52.73
7	24	9	6	15	256	12.66	113		122	134	47.66	52.34
8	9	9	1	15	256	12.66	114		136	120	53.13	46.88
7	8	9	4	14	255	12.61	115		155	100	60.78	39.22
8	28	9	6	15	255	12.61	116		129	126	50.59	49.41
9	4	9	6	14	255	12.61	117		135	120	52.94	47.06
9	5	9	7	13	255	12.61	118		121	134	47.45	52.55
9	6	9	1	13	255	12.61	119		106	149	41.57	58.43
9	25	9	6	16	255	12.61	120		136	119	53.33	46.67
9	4	9	6	17	254	12.56	121	2022	138	116	54.33	45.67

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	16	9	1	12	253	12.51	122		102	151	40.32	59.68
9	18	9	6	13	253	12.51	123		105	148	41.5	58.5
5	11	9	2	18	252	12.46	124		86	166	34.13	65.87
8	14	9	6	14	252	12.46	125		130	122	51.59	48.41
9	25	9	6	15	252	12.46	126		115	137	45.63	54.37
9	25	9	6	17	252	12.46	127		121	131	48.02	51.98
5	24	9	1	14	251	12.41	128		119	132	47.41	52.59
7	17	9	6	14	251	12.41	129		119	132	47.41	52.59
8	7	9	6	13	251	12.41	130		127	124	50.6	49.4
8	28	9	6	16	251	12.41	131		144	107	57.37	42.63
8	30	9	1	15	251	12.41	132		128	123	51	49
7	26	9	1	14	250	12.36	133		140	110	56	44
8	7	9	6	12	250	12.36	134		112	138	44.8	55.2
8	21	9	6	16	250	12.36	135		117	133	46.8	53.2
9	18	9	6	12	250	12.36	136		132	118	52.8	47.2
7	9	9	5	15	249	12.31	137		127	122	51	49
8	8	9	7	14	249	12.31	138		123	126	49.4	50.6
6	21	9	1	14	248	12.27	139		115	133	46.37	53.63
7	3	9	6	15	248	12.27	140		121	127	48.79	51.21
7	31	9	6	15	248	12.27	141	2022	133	115	53.63	46.37
9	18	9	6	15	248	12.27	142		142	106	57.26	42.74
6	7	9	1	15	247	12.22	143		137	110	55.47	44.53
6	19	9	6	14	247	12.22	144		134	113	54.25	45.75
6	19	9	6	16	246	12.17	145		136	110	55.28	44.72
7	12	9	1	15	246	12.17	146		139	107	56.5	43.5
7	3	9	6	13	245	12.12	147		109	136	44.49	55.51
7	31	9	6	16	245	12.12	148		115	130	46.94	53.06
9	11	9	6	13	245	12.12	149		124	121	50.61	49.39
9	13	9	1	15	245	12.12	150		146	99	59.59	40.41
9	14	9	2	13	245	12.12	151		129	116	52.65	47.35
9	20	9	1	15	245	12.12	152		126	119	51.43	48.57
5	15	9	6	15	244	12.07	153		139	105	56.97	43.03
5	23	9	7	13	244	12.07	154		103	141	42.21	57.79
6	20	9	7	15	244	12.07	155		150	94	61.48	38.52
6	27	9	7	14	244	12.07	156		116	128	47.54	52.46
7	12	9	1	13	244	12.07	157		92	152	37.7	62.3
7	12	9	1	16	244	12.07	158		133	111	54.51	45.49
5	25	9	2	17	243	12.02	159		130	113	53.5	46.5
7	2	9	5	13	243	12.02	160		127	116	52.26	47.74
8	8	9	7	16	243	12.02	161	2022	133	110	54.73	45.27
9	7	9	2	13	243	12.02	162		107	136	44.03	55.97
9	17	9	5	15	243	12.02	163		143	100	58.85	41.15
5	24	9	1	17	242	11.97	164		157	85	64.88	35.12
6	14	9	1	15	242	11.97	165		107	135	44.21	55.79
8	10	9	2	15	242	11.97	166		127	115	52.48	47.52
8	30	9	1	14	242	11.97	167		127	115	52.48	47.52
9	20	9	1	13	242	11.97	168		97	145	40.08	59.92
8	17	9	2	15	241	11.92	169		127	114	52.7	47.3
9	10	9	5	15	241	11.92	170		141	100	58.51	41.49
9	17	9	5	16	241	11.92	171		132	109	54.77	45.23
5	23	9	7	16	240	11.87	172		162	78	67.5	32.5
6	26	9	6	17	240	11.87	173		132	108	55	45

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	8	9	4	12	240	11.87	174		144	96	60	40
7	26	9	1	13	240	11.87	175		132	108	55	45
8	6	9	5	15	240	11.87	176		130	110	54.17	45.83
8	12	9	4	15	240	11.87	177		123	117	51.25	48.75
9	5	9	7	16	240	11.87	178		147	93	61.25	38.75
5	16	9	7	15	239	11.82	179		123	116	51.46	48.54
5	17	9	1	16	239	11.82	180		109	130	45.61	54.39
7	24	9	6	16	239	11.82	181	2022	111	128	46.44	53.56
7	26	9	1	15	239	11.82	182		130	109	54.39	45.61
8	28	9	6	13	239	11.82	183		129	110	53.97	46.03
9	13	9	1	13	239	11.82	184		125	114	52.3	47.7
6	28	9	1	14	238	11.77	185		123	115	51.68	48.32
7	4	9	7	23	238	11.77	186		218	20	91.6	8.4
7	5	9	1	13	238	11.77	187		123	115	51.68	48.32
8	16	9	1	18	238	11.77	188		149	89	62.61	37.39
8	20	9	5	13	238	11.77	189		131	107	55.04	44.96
9	27	9	1	15	238	11.77	190		96	142	40.34	59.66
5	22	9	6	16	237	11.72	191		125	112	52.74	47.26
6	28	9	1	15	237	11.72	192		103	134	43.46	56.54
6	28	9	1	17	237	11.72	193		129	108	54.43	45.57
8	20	9	5	12	237	11.72	194		105	132	44.3	55.7
9	4	9	6	12	237	11.72	195		104	133	43.88	56.12
9	5	9	7	12	237	11.72	196		102	135	43.04	56.96
9	11	9	6	15	237	11.72	197		136	101	57.38	42.62
5	24	9	1	12	236	11.67	198		99	137	41.95	58.05
6	14	9	1	13	236	11.67	199		106	130	44.92	55.08
7	10	9	6	16	236	11.67	200		131	105	55.51	44.49

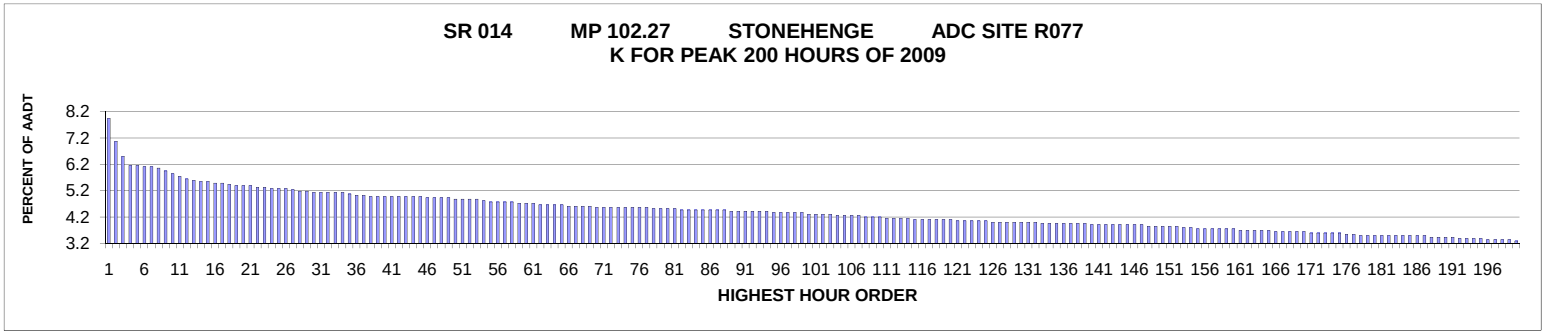

AADT= 1951 **K 30 FACTOR=** 5.13 **K 100 FACTOR=** 4.31 **K 200 FACTOR=** 3.28 **D FACTOR=** 56.25

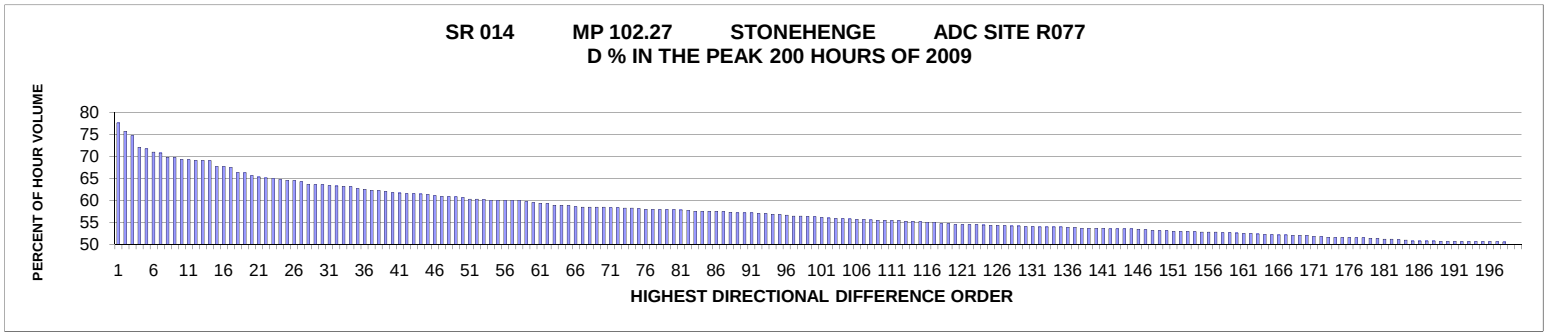

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
1	7	9	4	17	155	7.94	1	1951	50	105	32.26	67.74
1	8	9	5	15	138	7.07	2		68	70	49.28	50.72
1	9	9	6	15	127	6.51	3		50	77	39.37	60.63
1	4	9	1	15	120	6.15	4		63	57	52.5	47.5
1	30	9	6	16	120	6.15	5		55	65	45.83	54.17
1	9	9	6	13	119	6.1	6		62	57	52.1	47.9
1	26	9	2	16	119	6.1	7		36	83	30.25	69.75
1	30	9	6	15	118	6.05	8		44	74	37.29	62.71
1	7	9	4	16	116	5.95	9		47	69	40.52	59.48
1	11	9	1	16	114	5.84	10		62	52	54.39	45.61
1	23	9	6	16	112	5.74	11		51	61	45.54	54.46
1	16	9	6	14	110	5.64	12		53	57	48.18	51.82
1	9	9	6	16	109	5.59	13		46	63	42.2	57.8
1	21	9	4	16	108	5.54	14		46	62	42.59	57.41
1	27	9	3	16	108	5.54	15		44	64	40.74	59.26
1	13	9	3	17	107	5.48	16		39	68	36.45	63.55
1	22	9	5	16	107	5.48	17		45	62	42.06	57.94

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
1	2	9	6	13	106	5.43	18		46	60	43.4	56.6
1	12	9	2	16	105	5.38	19		48	57	45.71	54.29
1	16	9	6	17	105	5.38	20		45	60	42.86	57.14
1	19	9	2	16	105	5.38	21	1951	47	58	44.76	55.24
1	12	9	2	14	104	5.33	22		51	53	49.04	50.96
1	15	9	5	16	104	5.33	23		46	58	44.23	55.77
1	16	9	6	18	103	5.28	24		36	67	34.95	65.05
1	19	9	2	15	103	5.28	25		50	53	48.54	51.46
1	30	9	6	12	103	5.28	26		44	59	42.72	57.28
1	26	9	2	17	102	5.23	27		45	57	44.12	55.88
1	3	9	7	15	101	5.18	28		51	50	50.5	49.5
1	29	9	5	16	101	5.18	29		44	57	43.56	56.44
1	2	9	6	14	100	5.13	30		49	51	49	51
1	8	9	5	17	100	5.13	31		48	52	48	52
1	11	9	1	15	100	5.13	32		46	54	46	54
1	23	9	6	14	100	5.13	33		40	60	40	60
1	29	9	5	18	100	5.13	34		29	71	29	71
1	8	9	5	16	99	5.07	35		52	47	52.53	47.47
1	8	9	5	13	98	5.02	36		37	61	37.76	62.24
1	23	9	6	15	98	5.02	37		43	55	43.88	56.12
1	5	9	2	16	97	4.97	38		46	51	47.42	52.58
1	6	9	3	13	97	4.97	39		52	45	53.61	46.39
1	7	9	4	15	97	4.97	40		38	59	39.18	60.82
1	8	9	5	14	97	4.97	41	1951	52	45	53.61	46.39
1	16	9	6	16	97	4.97	42		34	63	35.05	64.95
1	22	9	5	18	97	4.97	43		30	67	30.93	69.07
1	28	9	4	15	97	4.97	44		44	53	45.36	54.64
1	29	9	5	15	97	4.97	45		50	47	51.55	48.45
1	20	9	3	14	96	4.92	46		61	35	63.54	36.46
1	26	9	2	15	96	4.92	47		52	44	54.17	45.83
1	28	9	4	16	96	4.92	48		29	67	30.21	69.79
1	30	9	6	18	96	4.92	49		34	62	35.42	64.58
1	6	9	3	15	95	4.87	50		49	46	51.58	48.42
1	7	9	4	14	95	4.87	51		45	50	47.37	52.63
1	12	9	2	17	95	4.87	52		40	55	42.11	57.89
1	23	9	6	18	95	4.87	53		32	63	33.68	66.32
1	7	9	4	12	94	4.82	54		53	41	56.38	43.62
1	5	9	2	13	93	4.77	55		54	39	58.06	41.94
1	14	9	4	17	93	4.77	56		32	61	34.41	65.59
1	19	9	2	17	93	4.77	57		37	56	39.78	60.22
1	21	9	4	18	93	4.77	58		30	63	32.26	67.74
1	6	9	3	14	92	4.72	59		41	51	44.57	55.43
1	16	9	6	15	92	4.72	60		41	51	44.57	55.43
1	20	9	3	18	92	4.72	61	1951	26	66	28.26	71.74
1	4	9	1	14	91	4.66	62		52	39	57.14	42.86
1	12	9	2	18	91	4.66	63		23	68	25.27	74.73
1	17	9	7	13	91	4.66	64		38	53	41.76	58.24
1	21	9	4	14	91	4.66	65		53	38	58.24	41.76
1	3	9	7	13	90	4.61	66		49	41	54.44	45.56
1	13	9	3	11	90	4.61	67		47	43	52.22	47.78
1	29	9	5	17	90	4.61	68		37	53	41.11	58.89
1	31	9	7	14	90	4.61	69		33	57	36.67	63.33

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
1	12	9	2	15	89	4.56	70		44	45	49.44	50.56
1	15	9	5	15	89	4.56	71		42	47	47.19	52.81
1	15	9	5	18	89	4.56	72		37	52	41.57	58.43
1	19	9	2	14	89	4.56	73		44	45	49.44	50.56
1	20	9	3	15	89	4.56	74		44	45	49.44	50.56
1	20	9	3	16	89	4.56	75		37	52	41.57	58.43
1	30	9	6	19	89	4.56	76		37	52	41.57	58.43
1	31	9	7	17	89	4.56	77		26	63	29.21	70.79
1	2	9	6	12	88	4.51	78		51	37	57.95	42.05
1	23	9	6	17	88	4.51	79		41	47	46.59	53.41
1	27	9	3	17	88	4.51	80		27	61	30.68	69.32
1	28	9	4	13	88	4.51	81	1951	50	38	56.82	43.18
1	4	9	1	17	87	4.46	82		43	44	49.43	50.57
1	13	9	3	16	87	4.46	83		38	49	43.68	56.32
1	14	9	4	13	87	4.46	84		44	43	50.57	49.43
1	23	9	6	12	87	4.46	85		34	53	39.08	60.92
1	29	9	5	14	87	4.46	86		47	40	54.02	45.98
1	30	9	6	14	87	4.46	87		43	44	49.43	50.57
1	30	9	6	17	87	4.46	88		32	55	36.78	63.22
1	7	9	4	13	86	4.41	89		39	47	45.35	54.65
1	7	9	4	18	86	4.41	90		35	51	40.7	59.3
1	13	9	3	12	86	4.41	91		42	44	48.84	51.16
1	22	9	5	14	86	4.41	92		46	40	53.49	46.51
1	23	9	6	13	86	4.41	93		37	49	43.02	56.98
1	26	9	2	18	86	4.41	94		33	53	38.37	61.63
1	9	9	6	12	85	4.36	95		51	34	60	40
1	9	9	6	17	85	4.36	96		44	41	51.76	48.24
1	18	9	1	15	85	4.36	97		34	51	40	60
1	18	9	1	16	85	4.36	98		34	51	40	60
1	19	9	2	13	85	4.36	99		40	45	47.06	52.94
1	6	9	3	16	84	4.31	100		35	49	41.67	58.33
1	13	9	3	15	84	4.31	101	1951	35	49	41.67	58.33
1	13	9	3	18	84	4.31	102		26	58	30.95	69.05
1	30	9	6	13	84	4.31	103		43	41	51.19	48.81
1	2	9	6	15	83	4.25	104		46	37	55.42	44.58
1	2	9	6	16	83	4.25	105		38	45	45.78	54.22
1	12	9	2	13	83	4.25	106		33	50	39.76	60.24
1	27	9	3	18	83	4.25	107		46	37	55.42	44.58
1	6	9	3	12	82	4.2	108		44	38	53.66	46.34
1	18	9	1	14	82	4.2	109		39	43	47.56	52.44
1	21	9	4	15	82	4.2	110		34	48	41.46	58.54
1	9	9	6	14	81	4.15	111		43	38	53.09	46.91
1	10	9	7	15	81	4.15	112		31	50	38.27	61.73
1	11	9	1	17	81	4.15	113		36	45	44.44	55.56
1	20	9	3	17	81	4.15	114		35	46	43.21	56.79
1	5	9	2	14	80	4.1	115		30	50	37.5	62.5
1	11	9	1	14	80	4.1	116		26	54	32.5	67.5
1	14	9	4	16	80	4.1	117		34	46	42.5	57.5
1	15	9	5	13	80	4.1	118		36	44	45	55
1	22	9	5	17	80	4.1	119		27	53	33.75	66.25
1	28	9	4	14	80	4.1	120		36	44	45	55
1	4	9	1	13	79	4.05	121	1951	45	34	56.96	43.04

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
1	7	9	4	11	79	4.05	122		35	44	44.3	55.7
1	7	9	4	19	79	4.05	123		31	48	39.24	60.76
1	16	9	6	13	79	4.05	124		35	44	44.3	55.7
1	28	9	4	18	79	4.05	125		30	49	37.97	62.03
1	8	9	5	18	78	4	126		30	48	38.46	61.54
1	14	9	4	12	78	4	127		45	33	57.69	42.31
1	19	9	2	18	78	4	128		30	48	38.46	61.54
1	21	9	4	13	78	4	129		38	40	48.72	51.28
1	21	9	4	17	78	4	130		24	54	30.77	69.23
1	22	9	5	12	78	4	131		36	42	46.15	53.85
1	22	9	5	15	78	4	132		35	43	44.87	55.13
1	3	9	7	16	77	3.95	133		28	49	36.36	63.64
1	8	9	5	12	77	3.95	134		47	30	61.04	38.96
1	9	9	6	11	77	3.95	135		41	36	53.25	46.75
1	10	9	7	14	77	3.95	136		33	44	42.86	57.14
1	14	9	4	11	77	3.95	137		29	48	37.66	62.34
1	16	9	6	21	77	3.95	138		43	34	55.84	44.16
1	17	9	7	14	77	3.95	139		38	39	49.35	50.65
1	6	9	3	18	76	3.9	140		17	59	22.37	77.63
1	10	9	7	13	76	3.9	141	1951	35	41	46.05	53.95
1	10	9	7	17	76	3.9	142		27	49	35.53	64.47
1	15	9	5	11	76	3.9	143		35	41	46.05	53.95
1	20	9	3	13	76	3.9	144		32	44	42.11	57.89
1	22	9	5	13	76	3.9	145		41	35	53.95	46.05
1	28	9	4	12	76	3.9	146		41	35	53.95	46.05
1	28	9	4	17	76	3.9	147		32	44	42.11	57.89
1	1	9	5	14	75	3.84	148		33	42	44	56
1	5	9	2	18	75	3.84	149		36	39	48	52
1	6	9	3	17	75	3.84	150		26	49	34.67	65.33
1	25	9	1	15	75	3.84	151		29	46	38.67	61.33
1	26	9	2	13	75	3.84	152		36	39	48	52
1	15	9	5	12	74	3.79	153		37	37	50	50
1	29	9	5	12	74	3.79	154		38	36	51.35	48.65
1	3	9	7	14	73	3.74	155		36	37	49.32	50.68
1	13	9	3	13	73	3.74	156		31	42	42.47	57.53
1	13	9	3	14	73	3.74	157		31	42	42.47	57.53
1	14	9	4	14	73	3.74	158		42	31	57.53	42.47
1	15	9	5	14	73	3.74	159		37	36	50.68	49.32
1	16	9	6	22	73	3.74	160		43	30	58.9	41.1
1	12	9	2	11	72	3.69	161	1951	38	34	52.78	47.22
1	17	9	7	12	72	3.69	162		38	34	52.78	47.22
1	17	9	7	16	72	3.69	163		34	38	47.22	52.78
1	19	9	2	12	72	3.69	164		36	36	50	50
1	23	9	6	11	72	3.69	165		43	29	59.72	40.28
1	5	9	2	15	71	3.64	166		37	34	52.11	47.89
1	14	9	4	15	71	3.64	167		33	38	46.48	53.52
1	15	9	5	17	71	3.64	168		36	35	50.7	49.3
1	25	9	1	16	71	3.64	169		33	38	46.48	53.52
1	26	9	2	12	71	3.64	170		38	33	53.52	46.48
1	4	9	1	12	70	3.59	171		34	36	48.57	51.43
1	5	9	2	17	70	3.59	172		28	42	40	60
1	8	9	5	11	70	3.59	173		32	38	45.71	54.29

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
1	13	9	3	8	70	3.59	174		17	53	24.29	75.71
1	31	9	7	13	70	3.59	175		27	43	38.57	61.43
1	18	9	1	17	69	3.54	176		37	32	53.62	46.38
1	31	9	7	15	69	3.54	177		33	36	47.83	52.17
1	1	9	5	17	68	3.49	178		41	27	60.29	39.71
1	2	9	6	17	68	3.49	179		28	40	41.18	58.82
1	4	9	1	16	68	3.49	180		37	31	54.41	45.59
1	8	9	5	10	68	3.49	181	1951	32	36	47.06	52.94
1	9	9	6	18	68	3.49	182		21	47	30.88	69.12
1	10	9	7	11	68	3.49	183		32	36	47.06	52.94
1	15	9	5	8	68	3.49	184		24	44	35.29	64.71
1	17	9	7	18	68	3.49	185		19	49	27.94	72.06
1	29	9	5	13	68	3.49	186		31	37	45.59	54.41
1	31	9	7	12	68	3.49	187		25	43	36.76	63.24
1	16	9	6	12	67	3.43	188		30	37	44.78	55.22
1	16	9	6	19	67	3.43	189		24	43	35.82	64.18
1	21	9	4	11	67	3.43	190		34	33	50.75	49.25
1	21	9	4	12	67	3.43	191		34	33	50.75	49.25
1	4	9	1	18	66	3.38	192		31	35	46.97	53.03
1	9	9	6	20	66	3.38	193		35	31	53.03	46.97
1	24	9	7	16	66	3.38	194		34	32	51.52	48.48
1	29	9	5	10	66	3.38	195		34	32	51.52	48.48
1	17	9	7	15	65	3.33	196		24	41	36.92	63.08
1	20	9	3	12	65	3.33	197		31	34	47.69	52.31
1	22	9	5	11	65	3.33	198		30	35	46.15	53.85
1	27	9	3	15	65	3.33	199		38	27	58.46	41.54
1	2	9	6	11	64	3.28	200		36	28	56.25	43.75

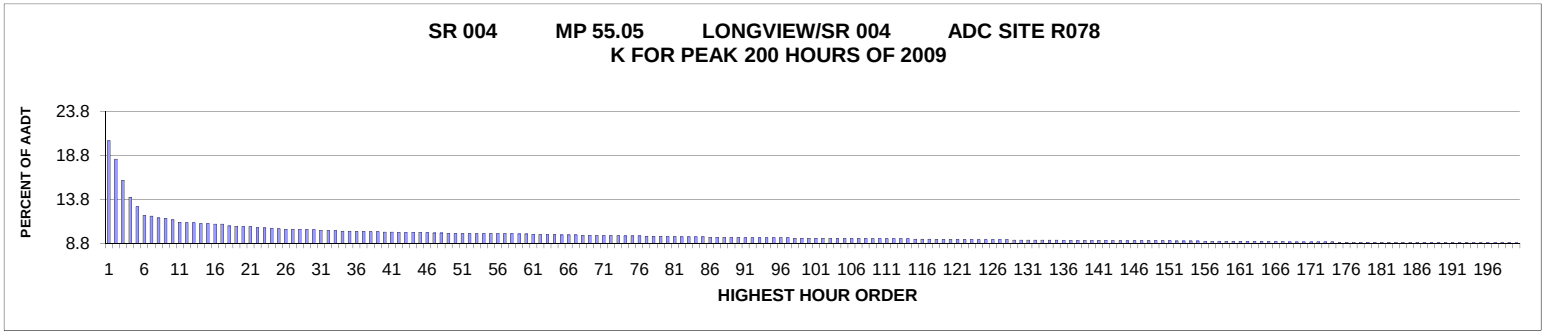

AADT= 5083 **K 30 FACTOR=** 10.31 **K 100 FACTOR=** 9.38 **K 200 FACTOR=** 8.83 **D FACTOR=** 56.92

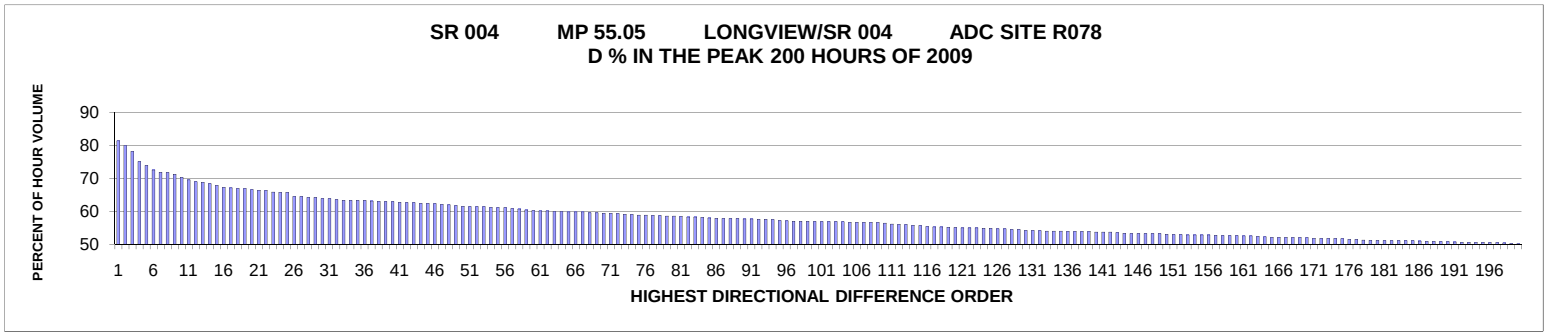

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	5	9	1	15	1041	20.48	1	5083	814	227	78.19	21.81
7	5	9	1	16	934	18.37	2		760	174	81.37	18.63
7	5	9	1	14	811	15.96	3		609	202	75.09	24.91
7	5	9	1	17	714	14.05	4		571	143	79.97	20.03
7	5	9	1	13	659	12.96	5		473	186	71.78	28.22
7	3	9	6	15	608	11.96	6		201	407	33.06	66.94
9	13	9	1	16	604	11.88	7		438	166	72.52	27.48
3	26	9	5	16	594	11.69	8		328	266	55.22	44.78
7	3	9	6	14	592	11.65	9		198	394	33.45	66.55
9	13	9	1	14	582	11.45	10		401	181	68.9	31.1
7	5	9	1	18	570	11.21	11		421	149	73.86	26.14
9	13	9	1	15	566	11.14	12		381	185	67.31	32.69
9	11	9	6	18	565	11.12	13		213	352	37.7	62.3
7	3	9	6	16	560	11.02	14		177	383	31.61	68.39
9	13	9	1	13	560	11.02	15		361	199	64.46	35.54
3	26	9	5	17	559	11	16		292	267	52.24	47.76
9	13	9	1	17	558	10.98	17		388	170	69.53	30.47

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	5	9	1	12	548	10.78	18		377	171	68.8	31.2
7	19	9	1	14	545	10.72	19		284	261	52.11	47.89
5	22	9	6	17	543	10.68	20		225	318	41.44	58.56
9	11	9	6	17	543	10.68	21	5083	245	298	45.12	54.88
7	17	9	6	17	538	10.58	22		266	272	49.44	50.56
7	2	9	5	16	537	10.56	23		224	313	41.71	58.29
7	24	9	6	18	534	10.51	24		214	320	40.07	59.93
5	28	9	5	17	531	10.45	25		286	245	53.86	46.14
7	3	9	6	12	529	10.41	26		228	301	43.1	56.9
3	26	9	5	9	528	10.39	27		227	301	42.99	57.01
7	2	9	5	15	528	10.39	28		214	314	40.53	59.47
3	26	9	5	15	527	10.37	29		299	228	56.74	43.26
10	2	9	6	17	524	10.31	30		236	288	45.04	54.96
10	2	9	6	16	523	10.29	31		232	291	44.36	55.64
3	27	9	6	17	522	10.27	32		203	319	38.89	61.11
9	13	9	1	18	522	10.27	33		367	155	70.31	29.69
7	17	9	6	16	517	10.17	34		245	272	47.39	52.61
9	11	9	6	16	517	10.17	35		224	293	43.33	56.67
5	25	9	2	14	516	10.15	36		339	177	65.7	34.3
9	4	9	6	17	516	10.15	37		185	331	35.85	64.15
9	11	9	6	15	514	10.11	38		234	280	45.53	54.47
5	25	9	2	15	513	10.09	39		325	188	63.35	36.65
9	4	9	6	16	512	10.07	40		216	296	42.19	57.81
10	15	9	5	17	512	10.07	41	5083	259	253	50.59	49.41
4	24	9	6	17	511	10.05	42		191	320	37.38	62.62
5	22	9	6	15	511	10.05	43		209	302	40.9	59.1
6	19	9	6	17	510	10.03	44		220	290	43.14	56.86
7	3	9	6	17	510	10.03	45		187	323	36.67	63.33
4	26	9	1	14	509	10.01	46		335	174	65.82	34.18
5	10	9	1	13	506	9.95	47		284	222	56.13	43.87
7	1	9	4	17	506	9.95	48		238	268	47.04	52.96
7	2	9	5	18	505	9.94	49		181	324	35.84	64.16
7	24	9	6	17	504	9.92	50		201	303	39.88	60.12
3	27	9	6	18	503	9.9	51		182	321	36.18	63.82
6	26	9	6	15	503	9.9	52		256	247	50.89	49.11
6	26	9	6	16	503	9.9	53		235	268	46.72	53.28
5	8	9	6	17	502	9.88	54		217	285	43.23	56.77
9	4	9	6	15	502	9.88	55		211	291	42.03	57.97
9	12	9	7	13	502	9.88	56		203	299	40.44	59.56
9	18	9	6	17	502	9.88	57		224	278	44.62	55.38
9	25	9	6	17	502	9.88	58		230	272	45.82	54.18
7	19	9	1	13	501	9.86	59		318	183	63.47	36.53
9	10	9	5	18	501	9.86	60		204	297	40.72	59.28
7	21	9	3	16	498	9.8	61	5083	293	205	58.84	41.16
3	26	9	5	18	497	9.78	62		231	266	46.48	53.52
3	27	9	6	16	497	9.78	63		200	297	40.24	59.76
7	2	9	5	17	497	9.78	64		219	278	44.06	55.94
7	17	9	6	14	496	9.76	65		232	264	46.77	53.23
7	24	9	6	16	496	9.76	66		203	293	40.93	59.07
2	7	9	7	13	495	9.74	67		192	303	38.79	61.21
10	9	9	6	16	494	9.72	68		251	243	50.81	49.19
5	25	9	2	13	493	9.7	69		318	175	64.5	35.5

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
4	24	9	6	18	492	9.68	70		158	334	32.11	67.89
7	15	9	4	17	492	9.68	71		272	220	55.28	44.72
5	25	9	2	16	491	9.66	72		313	178	63.75	36.25
5	27	9	4	17	491	9.66	73		243	248	49.49	50.51
4	24	9	6	16	490	9.64	74		197	293	40.2	59.8
7	3	9	6	13	489	9.62	75		186	303	38.04	61.96
10	9	9	6	14	489	9.62	76		255	234	52.15	47.85
9	7	9	2	15	488	9.6	77		307	181	62.91	37.09
10	2	9	6	14	488	9.6	78		237	251	48.57	51.43
9	7	9	2	14	487	9.58	79		304	183	62.42	37.58
5	22	9	6	18	486	9.56	80		188	298	38.68	61.32
9	3	9	5	17	486	9.56	81	5083	235	251	48.35	51.65
5	1	9	6	17	485	9.54	82		208	277	42.89	57.11
9	11	9	6	14	485	9.54	83		230	255	47.42	52.58
7	2	9	5	13	484	9.52	84		230	254	47.52	52.48
7	19	9	1	16	484	9.52	85		299	185	61.78	38.22
2	13	9	6	17	483	9.5	86		208	275	43.06	56.94
7	3	9	6	11	483	9.5	87		226	257	46.79	53.21
5	30	9	7	18	481	9.46	88		277	204	57.59	42.41
6	30	9	3	17	481	9.46	89		225	256	46.78	53.22
9	12	9	7	12	481	9.46	90		178	303	37.01	62.99
2	27	9	6	17	479	9.42	91		222	257	46.35	53.65
5	26	9	3	17	479	9.42	92		235	244	49.06	50.94
5	29	9	6	17	479	9.42	93		245	234	51.15	48.85
7	1	9	4	16	479	9.42	94		231	248	48.23	51.77
7	17	9	6	15	479	9.42	95		198	281	41.34	58.66
7	20	9	2	18	479	9.42	96		227	252	47.39	52.61
7	20	9	2	17	478	9.4	97		233	245	48.74	51.26
6	3	9	4	16	477	9.38	98		236	241	49.48	50.52
7	2	9	5	11	477	9.38	99		272	205	57.02	42.98
9	7	9	2	16	477	9.38	100		302	175	63.31	36.69
5	25	9	2	17	476	9.36	101	5083	342	134	71.85	28.15
9	25	9	6	18	476	9.36	102		202	274	42.44	57.56
5	15	9	6	17	475	9.34	103		220	255	46.32	53.68
6	5	9	6	16	475	9.34	104		219	256	46.11	53.89
10	9	9	6	17	475	9.34	105		218	257	45.89	54.11
6	25	9	5	17	474	9.33	106		198	276	41.77	58.23
9	7	9	2	13	474	9.33	107		318	156	67.09	32.91
9	14	9	2	17	474	9.33	108		218	256	45.99	54.01
3	13	9	6	17	473	9.31	109		217	256	45.88	54.12
6	18	9	5	16	473	9.31	110		228	245	48.2	51.8
7	24	9	6	15	473	9.31	111		237	236	50.11	49.89
9	18	9	6	18	473	9.31	112		177	296	37.42	62.58
3	13	9	6	16	472	9.29	113		221	251	46.82	53.18
3	29	9	1	14	472	9.29	114		316	156	66.95	33.05
1	16	9	6	17	471	9.27	115		203	268	43.1	56.9
5	22	9	6	16	471	9.27	116		182	289	38.64	61.36
6	26	9	6	17	471	9.27	117		226	245	47.98	52.02
9	9	9	4	17	470	9.25	118		213	257	45.32	54.68
10	19	9	2	17	470	9.25	119		230	240	48.94	51.06
5	21	9	5	17	469	9.23	120		216	253	46.06	53.94
10	9	9	6	15	469	9.23	121	5083	203	266	43.28	56.72

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
10	9	9	6	18	469	9.23	122		201	268	42.86	57.14
11	30	9	2	17	469	9.23	123		232	237	49.47	50.53
5	29	9	6	16	468	9.21	124		213	255	45.51	54.49
6	12	9	6	17	468	9.21	125		196	272	41.88	58.12
7	2	9	5	14	468	9.21	126		211	257	45.09	54.91
9	10	9	5	17	468	9.21	127		199	269	42.52	57.48
11	6	9	6	16	467	9.19	128		186	281	39.83	60.17
4	12	9	1	13	466	9.17	129		294	172	63.09	36.91
5	8	9	6	16	466	9.17	130		186	280	39.91	60.09
6	29	9	2	17	466	9.17	131		228	238	48.93	51.07
7	2	9	5	12	466	9.17	132		202	264	43.35	56.65
11	4	9	4	16	466	9.17	133		216	250	46.35	53.65
4	27	9	2	14	465	9.15	134		309	156	66.45	33.55
9	10	9	5	16	465	9.15	135		206	259	44.3	55.7
5	8	9	6	18	464	9.13	136		159	305	34.27	65.73
7	15	9	4	18	464	9.13	137		196	268	42.24	57.76
9	8	9	3	16	464	9.13	138		227	237	48.92	51.08
9	11	9	6	12	464	9.13	139		193	271	41.59	58.41
10	21	9	4	17	464	9.13	140		227	237	48.92	51.08
5	21	9	5	18	463	9.11	141	5083	196	267	42.33	57.67
9	9	9	4	18	463	9.11	142		195	268	42.12	57.88
3	27	9	6	14	462	9.09	143		213	249	46.1	53.9
3	27	9	6	15	462	9.09	144		208	254	45.02	54.98
6	26	9	6	14	462	9.09	145		249	213	53.9	46.1
7	3	9	6	18	462	9.09	146		190	272	41.13	58.87
7	19	9	1	15	462	9.09	147		267	195	57.79	42.21
4	24	9	6	15	461	9.07	148		171	290	37.09	62.91
5	10	9	1	14	461	9.07	149		266	195	57.7	42.3
9	12	9	7	14	461	9.07	150		187	274	40.56	59.44
10	20	9	3	17	461	9.07	151		200	261	43.38	56.62
3	26	9	5	11	460	9.05	152		253	207	55	45
3	29	9	1	15	460	9.05	153		328	132	71.3	28.7
5	20	9	4	17	460	9.05	154		225	235	48.91	51.09
7	1	9	4	13	460	9.05	155		239	221	51.96	48.04
4	10	9	6	17	459	9.03	156		184	275	40.09	59.91
5	15	9	6	16	459	9.03	157		202	257	44.01	55.99
6	28	9	1	17	459	9.03	158		279	180	60.78	39.22
7	1	9	4	15	459	9.03	159		220	239	47.93	52.07
1	7	9	4	16	458	9.01	160		172	286	37.55	62.45
4	16	9	5	17	458	9.01	161	5083	221	237	48.25	51.75
6	11	9	5	17	458	9.01	162		211	247	46.07	53.93
6	12	9	6	18	458	9.01	163		177	281	38.65	61.35
9	17	9	5	17	458	9.01	164		218	240	47.6	52.4
1	23	9	6	17	457	8.99	165		216	241	47.26	52.74
6	29	9	2	16	456	8.97	166		215	241	47.15	52.85
9	25	9	6	16	456	8.97	167		215	241	47.15	52.85
1	30	9	6	17	455	8.95	168		226	229	49.67	50.33
6	5	9	6	17	455	8.95	169		196	259	43.08	56.92
7	17	9	6	18	455	8.95	170		177	278	38.9	61.1
11	6	9	6	13	455	8.95	171		224	231	49.23	50.77
3	26	9	5	13	454	8.93	172		228	226	50.22	49.78
4	15	9	4	17	454	8.93	173		224	230	49.34	50.66

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
4	29	9	4	17	454	8.93	174		240	214	52.86	47.14
3	25	9	4	16	453	8.91	175		214	239	47.24	52.76
5	22	9	6	14	453	8.91	176		178	275	39.29	60.71
6	12	9	6	16	453	8.91	177		188	265	41.5	58.5
7	1	9	4	18	453	8.91	178		174	279	38.41	61.59
7	23	9	5	14	453	8.91	179		271	182	59.82	40.18
9	9	9	4	16	453	8.91	180		215	238	47.46	52.54
9	24	9	5	17	453	8.91	181	5083	212	241	46.8	53.2
9	30	9	4	16	453	8.91	182		214	239	47.24	52.76
2	20	9	6	18	452	8.89	183		179	273	39.6	60.4
4	10	9	6	18	452	8.89	184		166	286	36.73	63.27
4	17	9	6	17	452	8.89	185		197	255	43.58	56.42
9	23	9	4	18	452	8.89	186		221	231	48.89	51.11
10	16	9	6	17	452	8.89	187		204	248	45.13	54.87
3	29	9	1	13	451	8.87	188		299	152	66.3	33.7
5	23	9	7	12	451	8.87	189		168	283	37.25	62.75
6	4	9	5	18	451	8.87	190		186	265	41.24	58.76
9	11	9	6	13	451	8.87	191		216	235	47.89	52.11
9	17	9	5	16	451	8.87	192		223	228	49.45	50.55
11	6	9	6	18	451	8.87	193		183	268	40.58	59.42
12	2	9	4	17	451	8.87	194		219	232	48.56	51.44
6	28	9	1	14	450	8.85	195		248	202	55.11	44.89
7	1	9	4	12	450	8.85	196		233	217	51.78	48.22
7	24	9	6	14	450	8.85	197		246	204	54.67	45.33
9	1	9	3	14	450	8.85	198		229	221	50.89	49.11
10	2	9	6	13	450	8.85	199		238	212	52.89	47.11
5	10	9	1	16	449	8.83	200		279	170	62.14	37.86

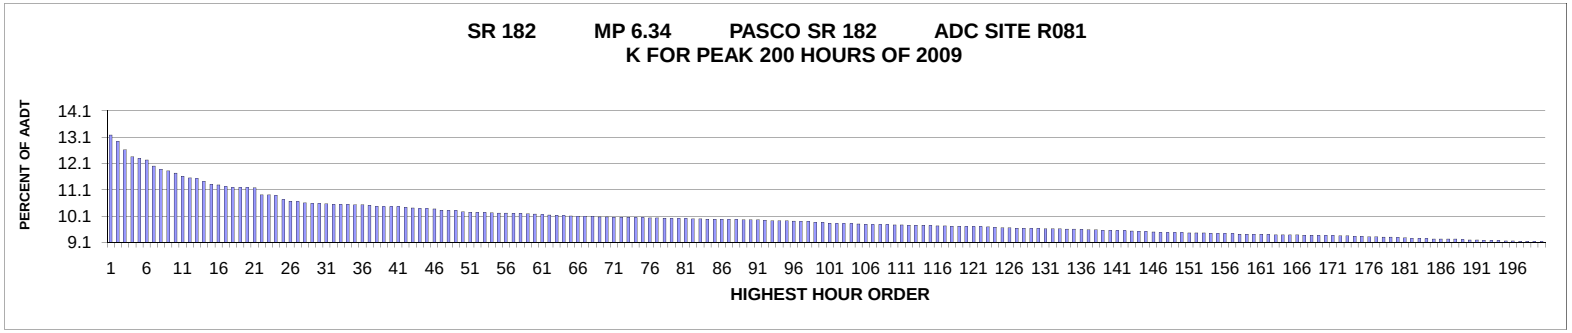

AADT= 53828 **K 30 FACTOR=** 10.58 **K 100 FACTOR=** 9.86 **K 200 FACTOR=** 9.13 **D FACTOR=** 58.31

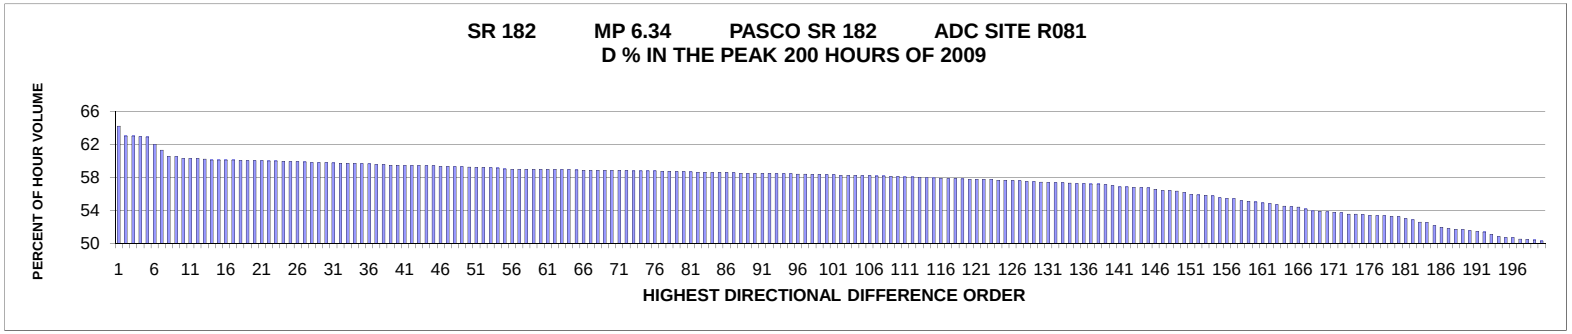

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
10	1	9	5	18	7092	13.18	1	53828	4295	2797	60.56	39.44
9	17	9	5	18	6968	12.94	2		3361	3607	48.23	51.77
9	30	9	4	18	6792	12.62	3		4213	2579	62.03	37.97
9	16	9	4	18	6654	12.36	4		3301	3353	49.61	50.39
9	29	9	3	18	6620	12.3	5		4253	2367	64.24	35.76
9	15	9	3	18	6583	12.23	6		3309	3274	50.27	49.73
10	1	9	5	17	6460	12	7		3891	2569	60.23	39.77
10	8	9	5	18	6396	11.88	8		3604	2792	56.35	43.65
9	28	9	2	18	6365	11.82	9		4012	2353	63.03	36.97
10	15	9	5	18	6313	11.73	10		3478	2835	55.09	44.91
9	14	9	2	18	6256	11.62	11		3212	3044	51.34	48.66
10	2	9	6	17	6215	11.55	12		3661	2554	58.91	41.09
9	18	9	6	17	6209	11.53	13		2635	3574	42.44	57.56
10	6	9	3	18	6146	11.42	14		3493	2653	56.83	43.17
9	17	9	5	17	6087	11.31	15		2942	3145	48.33	51.67
9	18	9	6	18	6076	11.29	16		2573	3503	42.35	57.65
10	2	9	6	18	6042	11.22	17		3495	2547	57.85	42.15

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
9	15	9	3	17	6023	11.19	18		2895	3128	48.07	51.93
9	29	9	3	17	6023	11.19	19		3796	2227	63.03	36.97
10	7	9	4	18	6023	11.19	20		3416	2607	56.72	43.28
9	30	9	4	17	6017	11.18	21	53828	3788	2229	62.95	37.05
9	16	9	4	17	5874	10.91	22		2977	2897	50.68	49.32
9	28	9	2	17	5873	10.91	23		3695	2178	62.92	37.08
10	22	9	5	18	5860	10.89	24		3491	2369	59.57	40.43
10	21	9	4	18	5778	10.73	25		3260	2518	56.42	43.58
9	24	9	5	18	5743	10.67	26		3413	2330	59.43	40.57
10	15	9	5	17	5731	10.65	27		3133	2598	54.67	45.33
10	8	9	5	17	5706	10.6	28		3133	2573	54.91	45.09
10	9	9	6	17	5696	10.58	29		3009	2687	52.83	47.17
9	10	9	5	18	5693	10.58	30		3373	2320	59.25	40.75
10	28	9	4	18	5691	10.57	31		3401	2290	59.76	40.24
9	21	9	2	18	5678	10.55	32		3343	2335	58.88	41.12
10	16	9	6	17	5675	10.54	33		2740	2935	48.28	51.72
9	8	9	3	18	5673	10.54	34		3335	2338	58.79	41.21
10	20	9	3	18	5669	10.53	35		3314	2355	58.46	41.54
9	1	9	3	18	5667	10.53	36		3341	2326	58.96	41.04
7	15	9	4	18	5656	10.51	37		3215	2441	56.84	43.16
9	14	9	2	17	5634	10.47	38		2897	2737	51.42	48.58
9	3	9	5	18	5632	10.46	39		3222	2410	57.21	42.79
10	2	9	6	16	5630	10.46	40		3367	2263	59.8	40.2
11	10	9	3	18	5628	10.46	41	53828	3372	2256	59.91	40.09
10	1	9	5	16	5618	10.44	42		3258	2360	57.99	42.01
9	23	9	4	18	5606	10.41	43		3300	2306	58.87	41.13
11	12	9	5	18	5595	10.39	44		3294	2301	58.87	41.13
10	7	9	4	17	5592	10.39	45		3118	2474	55.76	44.24
10	19	9	2	18	5584	10.37	46		3311	2273	59.29	40.71
8	17	9	2	18	5558	10.33	47		3271	2287	58.85	41.15
11	19	9	5	18	5549	10.31	48		3290	2259	59.29	40.71
9	18	9	6	16	5547	10.31	49		2496	3051	45	55
10	14	9	4	18	5523	10.26	50		3257	2266	58.97	41.03
8	27	9	5	18	5517	10.25	51		3251	2266	58.93	41.07
10	28	9	4	17	5514	10.24	52		3309	2205	60.01	39.99
10	29	9	5	18	5512	10.24	53		3184	2328	57.76	42.24
11	4	9	4	18	5507	10.23	54		3218	2289	58.43	41.57
8	10	9	2	18	5500	10.22	55		3305	2195	60.09	39.91
10	27	9	3	18	5499	10.22	56		3238	2261	58.88	41.12
7	23	9	5	18	5496	10.21	57		3154	2342	57.39	42.61
10	22	9	5	17	5496	10.21	58		3273	2223	59.55	40.45
8	24	9	2	18	5485	10.19	59		3295	2190	60.07	39.93
9	9	9	4	18	5477	10.18	60		3187	2290	58.19	41.81
11	3	9	3	18	5461	10.15	61	53828	3218	2243	58.93	41.07
8	19	9	4	18	5460	10.14	62		3192	2268	58.46	41.54
10	12	9	2	18	5452	10.13	63		3209	2243	58.86	41.14
8	25	9	3	18	5447	10.12	64		3241	2206	59.5	40.5
9	17	9	5	16	5440	10.11	65		2545	2895	46.78	53.22
8	6	9	5	18	5438	10.1	66		3208	2230	58.99	41.01
7	30	9	5	18	5434	10.1	67		3250	2184	59.81	40.19
10	13	9	3	18	5432	10.09	68		3261	2171	60.03	39.97
9	2	9	4	18	5423	10.07	69		3162	2261	58.31	41.69

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
12	1	9	3	18	5421	10.07	70		3258	2163	60.1	39.9
7	28	9	3	18	5415	10.06	71		3255	2160	60.11	39.89
7	16	9	5	18	5414	10.06	72		3159	2255	58.35	41.65
7	29	9	4	18	5413	10.06	73		3203	2210	59.17	40.83
11	6	9	6	17	5412	10.05	74		2911	2501	53.79	46.21
10	21	9	4	17	5410	10.05	75		3089	2321	57.1	42.9
8	18	9	3	18	5403	10.04	76		3171	2232	58.69	41.31
7	8	9	4	18	5398	10.03	77		3211	2187	59.48	40.52
8	31	9	2	18	5393	10.02	78		3144	2249	58.3	41.7
8	13	9	5	18	5390	10.01	79		3138	2252	58.22	41.78
11	5	9	5	18	5390	10.01	80		3114	2276	57.77	42.23
8	4	9	3	18	5388	10.01	81	53828	3112	2276	57.76	42.24
8	12	9	4	18	5385	10	82		3118	2267	57.9	42.1
10	29	9	5	17	5382	10	83		3152	2230	58.57	41.43
11	2	9	2	18	5380	9.99	84		3162	2218	58.77	41.23
11	5	9	5	17	5375	9.99	85		3127	2248	58.18	41.82
12	3	9	5	18	5371	9.98	86		3186	2185	59.32	40.68
11	12	9	5	17	5368	9.97	87		3105	2263	57.84	42.16
7	9	9	5	18	5364	9.97	88		3186	2178	59.4	40.6
7	20	9	2	18	5361	9.96	89		3121	2240	58.22	41.78
10	6	9	3	17	5361	9.96	90		3012	2349	56.18	43.82
7	22	9	4	18	5359	9.96	91		3197	2162	59.66	40.34
7	7	9	3	18	5358	9.95	92		3199	2159	59.71	40.29
7	14	9	3	18	5345	9.93	93		3177	2168	59.44	40.56
10	16	9	6	18	5341	9.92	94		2644	2697	49.5	50.5
9	25	9	6	17	5339	9.92	95		2946	2393	55.18	44.82
8	5	9	4	18	5337	9.91	96		3116	2221	58.38	41.62
8	11	9	3	18	5328	9.9	97		3150	2178	59.12	40.88
9	24	9	5	17	5328	9.9	98		3078	2250	57.77	42.23
12	3	9	5	17	5310	9.86	99		3093	2217	58.25	41.75
7	1	9	4	18	5308	9.86	100		3058	2250	57.61	42.39
8	26	9	4	18	5289	9.83	101	53828	3072	2217	58.08	41.92
7	13	9	2	18	5286	9.82	102		3130	2156	59.21	40.79
8	4	9	3	17	5280	9.81	103		2826	2454	53.52	46.48
10	26	9	2	18	5280	9.81	104		3127	2153	59.22	40.78
12	1	9	3	17	5277	9.8	105		3035	2242	57.51	42.49
12	9	9	4	18	5268	9.79	106		3176	2092	60.29	39.71
11	19	9	5	17	5266	9.78	107		3131	2135	59.46	40.54
10	23	9	6	17	5265	9.78	108		2819	2446	53.54	46.46
11	10	9	3	17	5262	9.78	109		3011	2251	57.22	42.78
9	10	9	5	17	5261	9.77	110		3076	2185	58.47	41.53
8	20	9	5	18	5260	9.77	111		3090	2170	58.75	41.25
10	20	9	3	17	5251	9.76	112		3047	2204	58.03	41.97
8	3	9	2	18	5249	9.75	113		3130	2119	59.63	40.37
11	20	9	6	17	5249	9.75	114		3011	2238	57.36	42.64
7	21	9	3	18	5245	9.74	115		3216	2029	61.32	38.68
12	4	9	6	17	5236	9.73	116		2929	2307	55.94	44.06
9	11	9	6	17	5235	9.73	117		2848	2387	54.4	45.6
12	10	9	5	17	5234	9.72	118		2984	2250	57.01	42.99
10	12	9	2	17	5231	9.72	119		3060	2171	58.5	41.5
11	18	9	4	18	5226	9.71	120		3085	2141	59.03	40.97
7	9	9	5	17	5224	9.7	121	53828	2916	2308	55.82	44.18

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
9	29	9	3	8	5219	9.7	122		2805	2414	53.75	46.25
8	6	9	5	17	5216	9.69	123		2963	2253	56.81	43.19
9	23	9	4	17	5210	9.68	124		3053	2157	58.6	41.4
10	16	9	6	16	5202	9.66	125		2577	2625	49.54	50.46
9	11	9	6	18	5198	9.66	126		2880	2318	55.41	44.59
10	9	9	6	18	5195	9.65	127		2633	2562	50.68	49.32
10	1	9	5	8	5192	9.65	128		2777	2415	53.49	46.51
12	10	9	5	18	5186	9.63	129		3042	2144	58.66	41.34
10	19	9	2	17	5185	9.63	130		3026	2159	58.36	41.64
9	8	9	3	17	5178	9.62	131		2985	2193	57.65	42.35
9	29	9	3	16	5177	9.62	132		2974	2203	57.45	42.55
11	24	9	3	17	5176	9.62	133		3011	2165	58.17	41.83
7	6	9	2	18	5175	9.61	134		3052	2123	58.98	41.02
10	27	9	3	17	5172	9.61	135		3042	2130	58.82	41.18
7	27	9	2	18	5168	9.6	136		3117	2051	60.31	39.69
9	30	9	4	8	5157	9.58	137		2811	2346	54.51	45.49
11	24	9	3	18	5156	9.58	138		2917	2239	56.57	43.43
12	2	9	4	17	5145	9.56	139		3072	2073	59.71	40.29
12	8	9	3	18	5144	9.56	140		3092	2052	60.11	39.89
9	16	9	4	16	5140	9.55	141	53828	2381	2759	46.32	53.68
9	21	9	2	17	5139	9.55	142		3006	2133	58.49	41.51
10	9	9	6	16	5135	9.54	143		2814	2321	54.8	45.2
9	3	9	5	17	5126	9.52	144		3006	2120	58.64	41.36
11	6	9	6	16	5119	9.51	145		2773	2346	54.17	45.83
11	4	9	4	17	5114	9.5	146		3066	2048	59.95	40.05
9	22	9	3	17	5105	9.48	147		2981	2124	58.39	41.61
12	18	9	6	17	5104	9.48	148		2834	2270	55.53	44.47
11	30	9	2	18	5101	9.48	149		3061	2040	60.01	39.99
11	23	9	2	18	5099	9.47	150		3025	2074	59.33	40.67
8	28	9	6	17	5094	9.46	151		2716	2378	53.32	46.68
12	2	9	4	18	5094	9.46	152		3052	2042	59.91	40.09
9	30	9	4	16	5091	9.46	153		2918	2173	57.32	42.68
11	11	9	4	18	5085	9.45	154		3050	2035	59.98	40.02
9	11	9	6	16	5084	9.44	155		2766	2318	54.41	45.59
12	17	9	5	18	5083	9.44	156		3065	2018	60.3	39.7
9	15	9	3	16	5080	9.44	157		2341	2739	46.08	53.92
10	23	9	6	18	5072	9.42	158		2706	2366	53.35	46.65
12	22	9	3	17	5071	9.42	159		2912	2159	57.42	42.58
10	13	9	3	17	5066	9.41	160		2898	2168	57.2	42.8
11	16	9	2	18	5066	9.41	161	53828	3067	1999	60.54	39.46
11	17	9	3	18	5059	9.4	162		3034	2025	59.97	40.03
12	9	9	4	17	5057	9.39	163		3027	2030	59.86	40.14
7	1	9	4	17	5056	9.39	164		2923	2133	57.81	42.19
11	18	9	4	17	5055	9.39	165		3019	2036	59.72	40.28
10	14	9	4	17	5053	9.39	166		2962	2091	58.62	41.38
12	11	9	6	17	5050	9.38	167		2632	2418	52.12	47.88
8	13	9	5	17	5047	9.38	168		2933	2114	58.11	41.89
11	2	9	2	17	5046	9.37	169		2966	2080	58.78	41.22
12	21	9	2	18	5044	9.37	170		2966	2078	58.8	41.2
11	30	9	2	17	5043	9.37	171		2975	2068	58.99	41.01
11	3	9	3	17	5032	9.35	172		3009	2023	59.8	40.2
9	25	9	6	16	5031	9.35	173		2885	2146	57.34	42.66

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	12	9	4	17	5026	9.34	174		2918	2108	58.06	41.94
12	17	9	5	17	5025	9.34	175		2808	2217	55.88	44.12
10	2	9	6	15	5019	9.32	176		2981	2038	59.39	40.61
7	2	9	5	17	5017	9.32	177		2868	2149	57.17	42.83
10	30	9	6	18	5006	9.3	178		2631	2375	52.56	47.44
11	23	9	2	17	5004	9.3	179		2951	2053	58.97	41.03
7	2	9	5	18	4999	9.29	180		2838	2161	56.77	43.23
8	26	9	4	17	4993	9.28	181	53828	2892	2101	57.92	42.08
7	16	9	5	17	4986	9.26	182		2940	2046	58.97	41.03
9	2	9	4	17	4985	9.26	183		2927	2058	58.72	41.28
10	8	9	5	16	4979	9.25	184		2531	2448	50.83	49.17
7	6	9	2	17	4971	9.23	185		2921	2050	58.76	41.24
8	11	9	3	17	4971	9.23	186		2881	2090	57.96	42.04
11	6	9	6	18	4969	9.23	187		2560	2409	51.52	48.48
12	8	9	3	17	4968	9.23	188		2892	2076	58.21	41.79
9	28	9	2	16	4959	9.21	189		2750	2209	55.45	44.55
7	29	9	4	17	4950	9.2	190		2793	2157	56.42	43.58
12	7	9	2	18	4947	9.19	191		2896	2051	58.54	41.46
7	13	9	2	17	4944	9.18	192		2889	2055	58.43	41.57
10	30	9	6	17	4936	9.17	193		2592	2344	52.51	47.49
9	4	9	6	17	4934	9.17	194		2520	2414	51.07	48.93
9	25	9	6	18	4932	9.16	195		2627	2305	53.26	46.74
7	30	9	5	17	4928	9.16	196		2880	2048	58.44	41.56
9	14	9	2	16	4927	9.15	197		2297	2630	46.62	53.38
9	18	9	6	15	4926	9.15	198		2271	2655	46.1	53.9
11	20	9	6	18	4917	9.13	199		2606	2311	53	47
7	8	9	4	17	4914	9.13	200		2878	2036	58.57	41.43

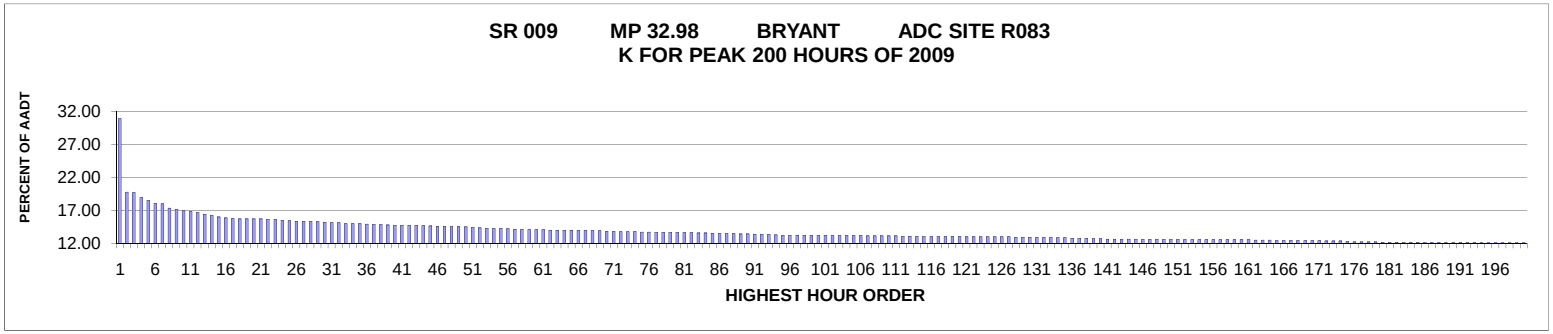

AADT= 1965 **K 30 FACTOR=** 15.22 **K 100 FACTOR=** 13.18 **K 200 FACTOR=** 12.01 **D FACTOR=** 59.07

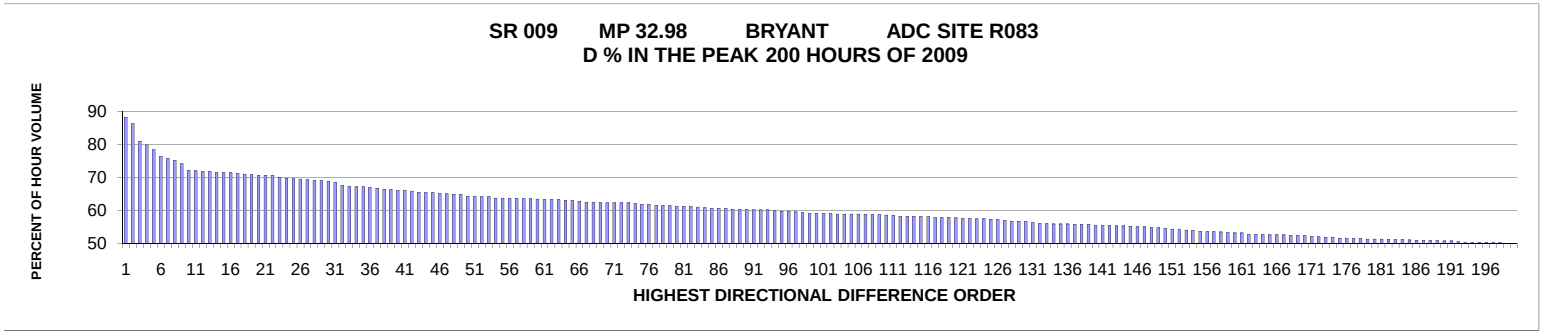

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
9	27	9	1	11	607	30.89	1	1965	536	71	88.30	11.70
9	27	9	1	12	388	19.75	2		304	84	78.35	21.65
7	3	9	6	17	387	19.69	3		266	121	68.73	31.27
9	27	9	1	10	371	18.88	4		320	51	86.25	13.75
9	27	9	1	17	364	18.52	5		69	295	18.96	81.04
9	27	9	1	16	354	18.02	6		86	268	24.29	75.71
7	3	9	6	16	353	17.96	7		252	101	71.39	28.61
5	17	9	1	15	341	17.35	8		169	172	49.56	50.44
7	3	9	6	18	337	17.15	9		226	111	67.06	32.94
7	18	9	7	13	333	16.95	10		235	98	70.57	29.43
7	4	9	7	13	330	16.79	11		231	99	70.00	30.00
9	27	9	1	18	327	16.64	12		66	261	20.18	79.82
4	26	9	1	17	323	16.44	13		129	194	39.94	60.06
6	27	9	7	16	319	16.23	14		195	124	61.13	38.87
7	4	9	7	15	314	15.98	15		173	141	55.10	44.90
7	18	9	7	14	311	15.83	16		222	89	71.38	28.62
7	3	9	6	15	309	15.73	17		214	95	69.26	30.74

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	5	9	1	13	308	15.67	18		136	172	44.16	55.84
7	5	9	1	17	308	15.67	19		88	220	28.57	71.43
8	16	9	1	16	308	15.67	20		124	184	40.26	59.74
9	27	9	1	13	308	15.67	21	1965	195	113	63.31	36.69
4	26	9	1	14	307	15.62	22		174	133	56.68	43.32
4	26	9	1	15	307	15.62	23		156	151	50.81	49.19
4	26	9	1	16	304	15.47	24		159	145	52.30	47.70
9	13	9	1	14	303	15.42	25		149	154	49.17	50.83
7	3	9	6	14	302	15.37	26		227	75	75.17	24.83
8	23	9	1	14	302	15.37	27		136	166	45.03	54.97
8	1	9	7	13	301	15.32	28		164	137	54.49	45.51
9	27	9	1	14	300	15.27	29		142	158	47.33	52.67
7	4	9	7	14	299	15.22	30		194	105	64.88	35.12
5	17	9	1	14	297	15.11	31		154	143	51.85	48.15
7	26	9	1	16	297	15.11	32		118	179	39.73	60.27
5	25	9	2	15	294	14.96	33		123	171	41.84	58.16
7	5	9	1	15	294	14.96	34		122	172	41.50	58.50
8	1	9	7	14	294	14.96	35		183	111	62.24	37.76
7	26	9	1	14	293	14.91	36		159	134	54.27	45.73
5	25	9	2	14	292	14.86	37		134	158	45.89	54.11
7	3	9	6	12	291	14.81	38		187	104	64.26	35.74
5	17	9	1	16	290	14.76	39		136	154	46.90	53.10
5	17	9	1	13	289	14.71	40		160	129	55.36	44.64
7	5	9	1	16	289	14.71	41	1965	100	189	34.60	65.40
8	2	9	1	13	289	14.71	42		170	119	58.82	41.18
9	13	9	1	13	289	14.71	43		145	144	50.17	49.83
8	16	9	1	14	288	14.66	44		161	127	55.90	44.10
8	2	9	1	15	287	14.61	45		136	151	47.39	52.61
7	3	9	6	13	286	14.55	46		192	94	67.13	32.87
7	5	9	1	14	286	14.55	47		129	157	45.10	54.90
5	25	9	2	16	285	14.50	48		82	203	28.77	71.23
7	19	9	1	15	285	14.50	49		136	149	47.72	52.28
6	27	9	7	12	284	14.45	50		201	83	70.77	29.23
6	27	9	7	17	283	14.40	51		151	132	53.36	46.64
6	14	9	1	15	282	14.35	52		154	128	54.61	45.39
9	27	9	1	15	281	14.30	53		106	175	37.72	62.28
8	9	9	1	15	280	14.25	54		125	155	44.64	55.36
8	16	9	1	15	280	14.25	55		124	156	44.29	55.71
7	18	9	7	15	279	14.20	56		161	118	57.71	42.29
8	1	9	7	16	278	14.15	57		166	112	59.71	40.29
5	24	9	1	14	277	14.10	58		176	101	63.54	36.46
4	26	9	1	13	276	14.05	59		141	135	51.09	48.91
5	23	9	7	14	276	14.05	60		183	93	66.30	33.70
8	2	9	1	16	276	14.05	61	1965	122	154	44.20	55.80
5	30	9	7	11	275	13.99	62		156	119	56.73	43.27
7	11	9	7	13	275	13.99	63		173	102	62.91	37.09
8	16	9	1	17	275	13.99	64		91	184	33.09	66.91
8	23	9	1	15	275	13.99	65		106	169	38.55	61.45
5	25	9	2	13	274	13.94	66		126	148	45.99	54.01
5	30	9	7	14	274	13.94	67		166	108	60.58	39.42
7	26	9	1	13	274	13.94	68		185	89	67.52	32.48
5	24	9	1	16	273	13.89	69		133	140	48.72	51.28

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
5	24	9	1	13	271	13.79	70		169	102	62.36	37.64
5	29	9	6	18	271	13.79	71		159	112	58.67	41.33
6	13	9	7	14	270	13.74	72		171	99	63.33	36.67
7	18	9	7	12	270	13.74	73		179	91	66.30	33.70
7	26	9	1	17	270	13.74	74		98	172	36.30	63.70
5	31	9	1	14	269	13.69	75		144	125	53.53	46.47
7	5	9	1	12	269	13.69	76		110	159	40.89	59.11
5	31	9	1	15	268	13.64	77		107	161	39.93	60.07
7	11	9	7	14	268	13.64	78		148	120	55.22	44.78
7	19	9	1	13	268	13.64	79		106	162	39.55	60.45
9	13	9	1	16	268	13.64	80		101	167	37.69	62.31
6	14	9	1	16	267	13.59	81	1965	110	157	41.20	58.80
7	16	9	5	17	267	13.59	82		142	125	53.18	46.82
5	16	9	7	12	266	13.54	83		136	130	51.13	48.87
8	2	9	1	14	266	13.54	84		133	133	50.00	50.00
7	18	9	7	17	265	13.49	85		142	123	53.58	46.42
7	4	9	7	16	264	13.44	86		148	116	56.06	43.94
7	26	9	1	15	264	13.44	87		127	137	48.11	51.89
8	1	9	7	12	264	13.44	88		159	105	60.23	39.77
7	5	9	1	18	263	13.38	89		68	195	25.86	74.14
7	11	9	7	16	263	13.38	90		132	131	50.19	49.81
6	27	9	7	14	262	13.33	91		167	95	63.74	36.26
7	19	9	1	14	262	13.33	92		139	123	53.05	46.95
9	12	9	7	16	262	13.33	93		138	124	52.67	47.33
4	26	9	1	18	261	13.28	94		81	180	31.03	68.97
5	17	9	1	12	260	13.23	95		151	109	58.08	41.92
5	23	9	7	15	260	13.23	96		162	98	62.31	37.69
7	11	9	7	15	260	13.23	97		158	102	60.77	39.23
8	16	9	1	18	260	13.23	98		101	159	38.85	61.15
8	30	9	1	14	260	13.23	99		142	118	54.62	45.38
7	4	9	7	17	259	13.18	100		129	130	49.81	50.19
7	5	9	1	19	259	13.18	101	1965	72	187	27.80	72.20
7	26	9	1	19	259	13.18	102		79	180	30.50	69.50
7	31	9	6	18	259	13.18	103		156	103	60.23	39.77
8	9	9	1	14	259	13.18	104		127	132	49.03	50.97
8	16	9	1	13	259	13.18	105		157	102	60.62	39.38
11	26	9	5	14	259	13.18	106		186	73	71.81	28.19
5	16	9	7	14	258	13.13	107		152	106	58.91	41.09
5	31	9	1	17	258	13.13	108		80	178	31.01	68.99
6	13	9	7	17	258	13.13	109		129	129	50.00	50.00
7	17	9	6	17	258	13.13	110		150	108	58.14	41.86
8	30	9	1	15	258	13.13	111		125	133	48.45	51.55
5	23	9	7	12	257	13.08	112		176	81	68.48	31.52
7	31	9	6	16	257	13.08	113		158	99	61.48	38.52
4	19	9	1	16	256	13.03	114		109	147	42.58	57.42
5	29	9	6	17	256	13.03	115		143	113	55.86	44.14
5	31	9	1	16	256	13.03	116		92	164	35.94	64.06
7	17	9	6	18	256	13.03	117		169	87	66.02	33.98
7	25	9	7	14	256	13.03	118		149	107	58.20	41.80
8	15	9	7	16	256	13.03	119		138	118	53.91	46.09
9	26	9	7	16	256	13.03	120		137	119	53.52	46.48
5	10	9	1	14	255	12.98	121	1965	148	107	58.04	41.96

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
5	25	9	2	18	255	12.98	122		60	195	23.53	76.47
7	18	9	7	16	255	12.98	123		134	121	52.55	47.45
7	25	9	7	13	255	12.98	124		166	89	65.10	34.90
8	22	9	7	16	255	12.98	125		128	127	50.20	49.80
9	13	9	1	15	255	12.98	126		121	134	47.45	52.55
9	26	9	7	18	255	12.98	127		121	134	47.45	52.55
6	7	9	1	16	254	12.93	128		88	166	34.65	65.35
8	22	9	7	12	254	12.93	129		158	96	62.20	37.80
8	22	9	7	14	254	12.93	130		149	105	58.66	41.34
5	17	9	1	18	253	12.88	131		83	170	32.81	67.19
7	4	9	7	12	253	12.88	132		182	71	71.94	28.06
9	12	9	7	15	253	12.88	133		140	113	55.34	44.66
5	23	9	7	13	252	12.82	134		178	74	70.63	29.37
7	31	9	6	19	252	12.82	135		175	77	69.44	30.56
5	9	9	7	12	251	12.77	136		145	106	57.77	42.23
6	13	9	7	15	251	12.77	137		144	107	57.37	42.63
6	13	9	7	16	250	12.72	138		138	112	55.20	44.80
7	25	9	7	16	249	12.67	139		140	109	56.22	43.78
9	13	9	1	12	249	12.67	140		128	121	51.41	48.59
5	22	9	6	16	248	12.62	141	1965	162	86	65.32	34.68
5	24	9	1	12	248	12.62	142		175	73	70.56	29.44
6	7	9	1	14	248	12.62	143		126	122	50.81	49.19
8	7	9	6	17	248	12.62	144		145	103	58.47	41.53
11	26	9	5	13	248	12.62	145		173	75	69.76	30.24
4	19	9	1	15	247	12.57	146		105	142	42.51	57.49
5	17	9	1	17	247	12.57	147		90	157	36.44	63.56
7	31	9	6	17	247	12.57	148		163	84	65.99	34.01
8	9	9	1	13	247	12.57	149		127	120	51.42	48.58
9	11	9	6	18	247	12.57	150		148	99	59.92	40.08
9	12	9	7	14	247	12.57	151		157	90	63.56	36.44
5	9	9	7	17	246	12.52	152		137	109	55.69	44.31
5	16	9	7	15	246	12.52	153		129	117	52.44	47.56
7	10	9	6	17	246	12.52	154		162	84	65.85	34.15
7	11	9	7	17	246	12.52	155		100	146	40.65	59.35
7	19	9	1	17	246	12.52	156		93	153	37.80	62.20
7	25	9	7	12	246	12.52	157		156	90	63.41	36.59
8	1	9	7	15	246	12.52	158		140	106	56.91	43.09
8	23	9	1	16	246	12.52	159		91	155	36.99	63.01
8	30	9	1	17	246	12.52	160		96	150	39.02	60.98
9	12	9	7	17	246	12.52	161	1965	128	118	52.03	47.97
8	18	9	3	17	245	12.47	162		123	122	50.20	49.80
8	22	9	7	13	245	12.47	163		157	88	64.08	35.92
10	4	9	1	17	245	12.47	164		93	152	37.96	62.04
4	19	9	1	13	244	12.42	165		153	91	62.70	37.30
5	30	9	7	15	244	12.42	166		125	119	51.23	48.77
8	21	9	6	18	244	12.42	167		155	89	63.52	36.48
5	16	9	7	18	243	12.37	168		94	149	38.68	61.32
5	24	9	1	15	243	12.37	169		125	118	51.44	48.56
8	15	9	7	13	243	12.37	170		143	100	58.85	41.15
8	23	9	1	17	243	12.37	171		100	143	41.15	58.85
7	2	9	5	16	242	12.32	172		137	105	56.61	43.39
7	19	9	1	18	242	12.32	173		85	157	35.12	64.88

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	22	9	7	15	242	12.32	174		144	98	59.50	40.50
6	28	9	1	15	241	12.26	175		120	121	49.79	50.21
6	7	9	1	15	240	12.21	176		102	138	42.50	57.50
6	12	9	6	17	240	12.21	177		154	86	64.17	35.83
8	21	9	6	16	240	12.21	178		141	99	58.75	41.25
10	10	9	7	16	240	12.21	179		117	123	48.75	51.25
5	9	9	7	14	239	12.16	180		141	98	59.00	41.00
5	30	9	7	12	239	12.16	181	1965	146	93	61.09	38.91
6	7	9	1	13	239	12.16	182		118	121	49.37	50.63
6	26	9	6	17	239	12.16	183		138	101	57.74	42.26
7	3	9	6	19	239	12.16	184		151	88	63.18	36.82
7	16	9	5	18	239	12.16	185		137	102	57.32	42.68
8	30	9	1	16	239	12.16	186		101	138	42.26	57.74
9	26	9	7	15	239	12.16	187		121	118	50.63	49.37
5	1	9	6	17	238	12.11	188		147	91	61.76	38.24
5	16	9	7	16	238	12.11	189		117	121	49.16	50.84
5	24	9	1	17	238	12.11	190		91	147	38.24	61.76
8	30	9	1	18	238	12.11	191		69	169	28.99	71.01
9	12	9	7	18	238	12.11	192		102	136	42.86	57.14
9	26	9	7	13	238	12.11	193		143	95	60.08	39.92
5	16	9	7	17	237	12.06	194		121	116	51.05	48.95
5	31	9	1	12	237	12.06	195		132	105	55.70	44.30
7	26	9	1	18	237	12.06	196		67	170	28.27	71.73
7	29	9	4	18	237	12.06	197		154	83	64.98	35.02
8	2	9	1	17	237	12.06	198		79	158	33.33	66.67
9	11	9	6	16	237	12.06	199		140	97	59.07	40.93
5	23	9	7	18	236	12.01	200		122	114	51.69	48.31

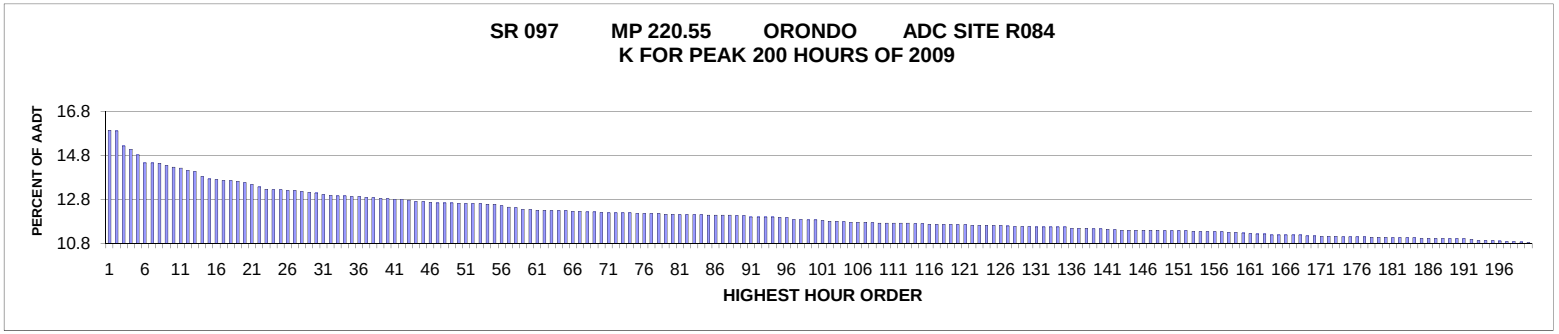

AADT= 4065 **K 30 FACTOR=** 13.09 **K 100 FACTOR=** 11.86 **K 200 FACTOR=** 10.82 **D FACTOR=** 59.87

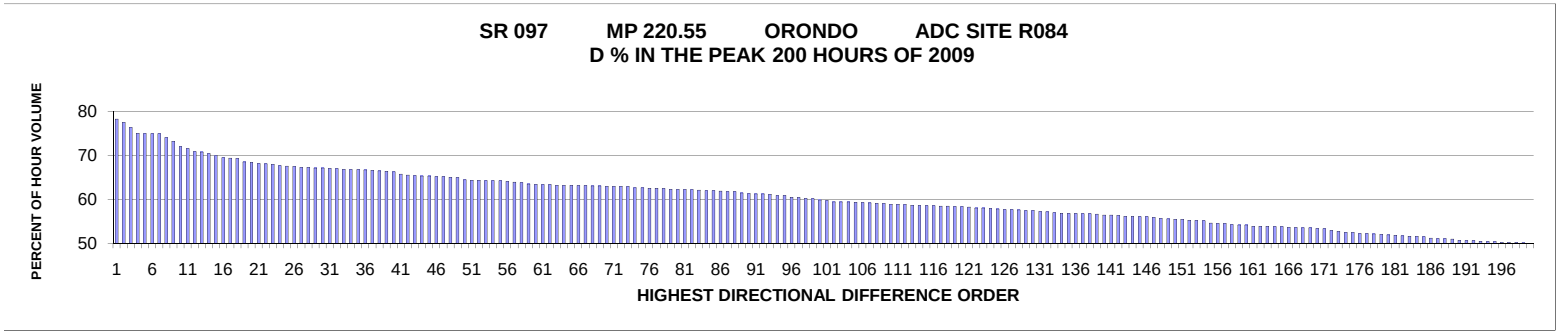

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
5	22	9	6	17	648	15.94	1	4065	423	225	65.28	34.72
5	22	9	6	16	647	15.92	2		430	217	66.46	33.54
5	25	9	2	12	619	15.23	3		139	480	22.46	77.54
8	9	9	1	14	613	15.08	4		227	386	37.03	62.97
5	22	9	6	15	603	14.83	5		395	208	65.51	34.49
4	24	9	6	16	588	14.46	6		278	310	47.28	52.72
5	22	9	6	19	588	14.46	7		421	167	71.6	28.4
7	5	9	1	14	587	14.44	8		224	363	38.16	61.84
7	5	9	1	12	583	14.34	9		163	420	27.96	72.04
7	5	9	1	13	580	14.27	10		169	411	29.14	70.86
8	23	9	1	13	578	14.22	11		206	372	35.64	64.36
8	9	9	1	16	574	14.12	12		149	425	25.96	74.04
8	9	9	1	15	572	14.07	13		191	381	33.39	66.61
5	25	9	2	13	563	13.85	14		141	422	25.04	74.96
8	9	9	1	13	558	13.73	15		217	341	38.89	61.11
8	7	9	6	16	557	13.7	16		330	227	59.25	40.75
7	5	9	1	16	555	13.65	17		185	370	33.33	66.67

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	14	9	6	17	555	13.65	18		334	221	60.18	39.82
7	19	9	1	15	554	13.63	19		215	339	38.81	61.19
7	3	9	6	16	551	13.55	20		342	209	62.07	37.93
8	7	9	6	15	548	13.48	21	4065	316	232	57.66	42.34
7	26	9	1	17	543	13.36	22		200	343	36.83	63.17
5	22	9	6	18	539	13.26	23		367	172	68.09	31.91
7	10	9	6	17	538	13.23	24		305	233	56.69	43.31
7	19	9	1	13	538	13.23	25		176	362	32.71	67.29
8	9	9	1	12	537	13.21	26		210	327	39.11	60.89
8	16	9	1	14	537	13.21	27		208	329	38.73	61.27
8	28	9	6	15	535	13.16	28		267	268	49.91	50.09
7	5	9	1	15	533	13.11	29		177	356	33.21	66.79
10	9	9	6	16	532	13.09	30		288	244	54.14	45.86
7	19	9	1	12	529	13.01	31		190	339	35.92	64.08
7	3	9	6	13	528	12.99	32		309	219	58.52	41.48
5	25	9	2	14	527	12.96	33		132	395	25.05	74.95
7	17	9	6	17	527	12.96	34		291	236	55.22	44.78
5	25	9	2	11	525	12.92	35		114	411	21.71	78.29
6	21	9	1	14	525	12.92	36		161	364	30.67	69.33
5	22	9	6	14	524	12.89	37		335	189	63.93	36.07
7	17	9	6	16	523	12.87	38		305	218	58.32	41.68
7	3	9	6	15	522	12.84	39		327	195	62.64	37.36
8	22	9	7	12	521	12.82	40		227	294	43.57	56.43
7	17	9	6	15	520	12.79	41	4065	292	228	56.15	43.85
8	16	9	1	15	520	12.79	42		193	327	37.12	62.88
8	7	9	6	17	519	12.77	43		337	182	64.93	35.07
4	24	9	6	17	516	12.69	44		291	225	56.4	43.6
8	7	9	6	18	516	12.69	45		349	167	67.64	32.36
8	23	9	1	15	515	12.67	46		197	318	38.25	61.75
7	6	9	2	14	514	12.64	47		194	320	37.74	62.26
7	19	9	1	14	514	12.64	48		193	321	37.55	62.45
8	2	9	1	13	514	12.64	49		226	288	43.97	56.03
8	23	9	1	16	513	12.62	50		212	301	41.33	58.67
5	1	9	6	16	512	12.6	51		233	279	45.51	54.49
5	25	9	2	16	512	12.6	52		128	384	25	75
8	14	9	6	16	512	12.6	53		284	228	55.47	44.53
7	3	9	6	14	511	12.57	54		305	206	59.69	40.31
7	10	9	6	16	511	12.57	55		268	243	52.45	47.55
6	26	9	6	15	508	12.5	56		293	215	57.68	42.32
4	26	9	1	15	506	12.45	57		152	354	30.04	69.96
8	14	9	6	12	505	12.42	58		212	293	41.98	58.02
8	9	9	1	19	502	12.35	59		160	342	31.87	68.13
10	9	9	6	17	502	12.35	60		254	248	50.6	49.4
7	10	9	6	14	500	12.3	61	4065	260	240	52	48
8	7	9	6	14	500	12.3	62		296	204	59.2	40.8
7	2	9	5	17	499	12.28	63		311	188	62.32	37.68
7	3	9	6	12	499	12.28	64		325	174	65.13	34.87
7	19	9	1	16	499	12.28	65		183	316	36.67	63.33
5	22	9	6	13	498	12.25	66		316	182	63.45	36.55
6	28	9	1	16	498	12.25	67		197	301	39.56	60.44
5	23	9	7	12	497	12.23	68		345	152	69.42	30.58
8	23	9	1	12	497	12.23	69		164	333	33	67

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
6	21	9	1	15	496	12.2	70		170	326	34.27	65.73
7	3	9	6	17	495	12.18	71		290	205	58.59	41.41
7	31	9	6	16	495	12.18	72		258	237	52.12	47.88
8	9	9	1	17	495	12.18	73		176	319	35.56	64.44
8	9	9	1	18	495	12.18	74		151	344	30.51	69.49
6	28	9	1	14	494	12.15	75		182	312	36.84	63.16
7	2	9	5	18	494	12.15	76		328	166	66.4	33.6
7	26	9	1	13	494	12.15	77		201	293	40.69	59.31
8	2	9	1	12	494	12.15	78		171	323	34.62	65.38
7	12	9	1	13	493	12.13	79		171	322	34.69	65.31
7	24	9	6	16	493	12.13	80		283	210	57.4	42.6
7	5	9	1	17	492	12.1	81	4065	176	316	35.77	64.23
7	12	9	1	14	492	12.1	82		184	308	37.4	62.6
8	23	9	1	14	492	12.1	83		176	316	35.77	64.23
8	30	9	1	13	492	12.1	84		166	326	33.74	66.26
5	23	9	7	14	491	12.08	85		328	163	66.8	33.2
7	10	9	6	18	491	12.08	86		311	180	63.34	36.66
7	24	9	6	17	491	12.08	87		286	205	58.25	41.75
7	26	9	1	16	491	12.08	88		204	287	41.55	58.45
6	5	9	6	16	490	12.05	89		273	217	55.71	44.29
7	10	9	6	15	490	12.05	90		240	250	48.98	51.02
7	26	9	1	15	488	12	91		191	297	39.14	60.86
8	21	9	6	15	488	12	92		277	211	56.76	43.24
8	21	9	6	17	488	12	93		281	207	57.58	42.42
8	23	9	1	17	488	12	94		183	305	37.5	62.5
8	16	9	1	13	487	11.98	95		160	327	32.85	67.15
6	19	9	6	15	486	11.96	96		268	218	55.14	44.86
7	24	9	6	15	483	11.88	97		246	237	50.93	49.07
8	28	9	6	17	483	11.88	98		274	209	56.73	43.27
5	23	9	7	13	482	11.86	99		295	187	61.2	38.8
7	5	9	1	11	482	11.86	100		152	330	31.54	68.46
6	26	9	6	16	481	11.83	101	4065	248	233	51.56	48.44
7	2	9	5	16	480	11.81	102		285	195	59.38	40.63
10	11	9	1	17	480	11.81	103		156	324	32.5	67.5
5	23	9	7	11	479	11.78	104		282	197	58.87	41.13
8	7	9	6	13	478	11.76	105		261	217	54.6	45.4
8	8	9	7	15	478	11.76	106		277	201	57.95	42.05
8	21	9	6	16	478	11.76	107		247	231	51.67	48.33
7	31	9	6	17	477	11.73	108		270	207	56.6	43.4
5	24	9	1	13	476	11.71	109		210	266	44.12	55.88
6	26	9	6	17	476	11.71	110		280	196	58.82	41.18
7	6	9	2	16	476	11.71	111		191	285	40.13	59.87
8	7	9	6	19	476	11.71	112		335	141	70.38	29.62
10	11	9	1	16	476	11.71	113		157	319	32.98	67.02
7	12	9	1	16	475	11.69	114		197	278	41.47	58.53
7	31	9	6	15	475	11.69	115		245	230	51.58	48.42
5	25	9	2	15	474	11.66	116		118	356	24.89	75.11
7	2	9	5	14	474	11.66	117		279	195	58.86	41.14
7	17	9	6	13	474	11.66	118		240	234	50.63	49.37
10	11	9	1	15	474	11.66	119		165	309	34.81	65.19
8	14	9	6	15	473	11.64	120		238	235	50.32	49.68
8	30	9	1	14	473	11.64	121	4065	174	299	36.79	63.21

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
6	5	9	6	17	472	11.61	122		265	207	56.14	43.86
6	21	9	1	13	472	11.61	123		138	334	29.24	70.76
7	2	9	5	15	472	11.61	124		279	193	59.11	40.89
8	16	9	1	16	472	11.61	125		169	303	35.81	64.19
8	16	9	1	18	472	11.61	126		193	279	40.89	59.11
8	16	9	1	12	471	11.59	127		154	317	32.7	67.3
6	21	9	1	12	470	11.56	128		148	322	31.49	68.51
7	19	9	1	17	470	11.56	129		200	270	42.55	57.45
8	28	9	6	16	470	11.56	130		244	226	51.91	48.09
4	30	9	5	16	469	11.54	131		177	292	37.74	62.26
6	28	9	1	15	469	11.54	132		181	288	38.59	61.41
7	6	9	2	13	469	11.54	133		170	299	36.25	63.75
7	17	9	6	14	469	11.54	134		251	218	53.52	46.48
8	2	9	1	15	469	11.54	135		195	274	41.58	58.42
5	16	9	7	11	467	11.49	136		253	214	54.18	45.82
7	3	9	6	11	467	11.49	137		265	202	56.75	43.25
7	30	9	5	16	467	11.49	138		242	225	51.82	48.18
6	19	9	6	17	466	11.46	139		294	172	63.09	36.91
8	16	9	1	17	466	11.46	140		194	272	41.63	58.37
8	14	9	6	14	465	11.44	141	4065	249	216	53.55	46.45
7	24	9	6	14	464	11.41	142		242	222	52.16	47.84
5	23	9	7	16	463	11.39	143		301	162	65.01	34.99
7	12	9	1	12	463	11.39	144		188	275	40.6	59.4
7	17	9	6	12	463	11.39	145		265	198	57.24	42.76
7	25	9	7	13	463	11.39	146		226	237	48.81	51.19
8	22	9	7	13	463	11.39	147		220	243	47.52	52.48
8	28	9	6	14	463	11.39	148		212	251	45.79	54.21
5	1	9	6	17	462	11.37	149		241	221	52.16	47.84
5	24	9	1	14	462	11.37	150		232	230	50.22	49.78
7	17	9	6	18	462	11.37	151		291	171	62.99	37.01
8	8	9	7	12	462	11.37	152		259	203	56.06	43.94
8	8	9	7	13	461	11.34	153		248	213	53.8	46.2
5	22	9	6	12	460	11.32	154		267	193	58.04	41.96
7	12	9	1	15	460	11.32	155		174	286	37.83	62.17
7	23	9	5	16	460	11.32	156		232	228	50.43	49.57
8	14	9	6	18	460	11.32	157		290	170	63.04	36.96
7	18	9	7	13	459	11.29	158		223	236	48.58	51.42
8	29	9	7	14	459	11.29	159		228	231	49.67	50.33
5	22	9	6	20	458	11.27	160		350	108	76.42	23.58
7	11	9	7	13	457	11.24	161	4065	197	260	43.11	56.89
4	17	9	6	17	456	11.22	162		257	199	56.36	43.64
7	2	9	5	13	456	11.22	163		243	213	53.29	46.71
6	14	9	1	13	454	11.17	164		168	286	37	63
6	14	9	1	16	454	11.17	165		202	252	44.49	55.51
7	11	9	7	14	454	11.17	166		243	211	53.52	46.48
7	18	9	7	14	454	11.17	167		226	228	49.78	50.22
8	21	9	6	18	454	11.17	168		288	166	63.44	36.56
7	19	9	1	18	453	11.14	169		184	269	40.62	59.38
8	2	9	1	14	453	11.14	170		194	259	42.83	57.17
6	28	9	1	13	452	11.12	171		172	280	38.05	61.95
7	9	9	5	17	452	11.12	172		226	226	50	50
7	26	9	1	14	452	11.12	173		195	257	43.14	56.86

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
4	23	9	5	16	451	11.09	174		208	243	46.12	53.88
4	29	9	4	16	451	11.09	175		180	271	39.91	60.09
5	8	9	6	17	451	11.09	176		243	208	53.88	46.12
7	9	9	5	16	451	11.09	177		228	223	50.55	49.45
6	7	9	1	16	450	11.07	178		166	284	36.89	63.11
6	19	9	6	18	450	11.07	179		306	144	68	32
8	14	9	6	13	450	11.07	180		240	210	53.33	46.67
6	19	9	6	16	449	11.05	181	4065	241	208	53.67	46.33
7	2	9	5	19	449	11.05	182		329	120	73.27	26.73
7	24	9	6	18	449	11.05	183		283	166	63.03	36.97
8	2	9	1	18	449	11.05	184		160	289	35.63	64.37
5	21	9	5	17	448	11.02	185		247	201	55.13	44.87
5	24	9	1	16	448	11.02	186		177	271	39.51	60.49
6	28	9	1	17	448	11.02	187		168	280	37.5	62.5
8	21	9	6	14	448	11.02	188		237	211	52.9	47.1
6	21	9	1	16	447	11	189		171	276	38.26	61.74
8	6	9	5	15	447	11	190		219	228	48.99	51.01
8	30	9	1	12	447	11	191		145	302	32.44	67.56
7	31	9	6	14	446	10.97	192		240	206	53.81	46.19
7	6	9	2	15	444	10.92	193		169	275	38.06	61.94
7	25	9	7	12	444	10.92	194		205	239	46.17	53.83
8	8	9	7	16	444	10.92	195		242	202	54.5	45.5
8	15	9	7	13	443	10.9	196		187	256	42.21	57.79
6	7	9	1	14	442	10.87	197		147	295	33.26	66.74
8	8	9	7	11	442	10.87	198		220	222	49.77	50.23
6	7	9	1	15	441	10.85	199		145	296	32.88	67.12
6	5	9	6	15	440	10.82	200		244	196	55.45	44.55

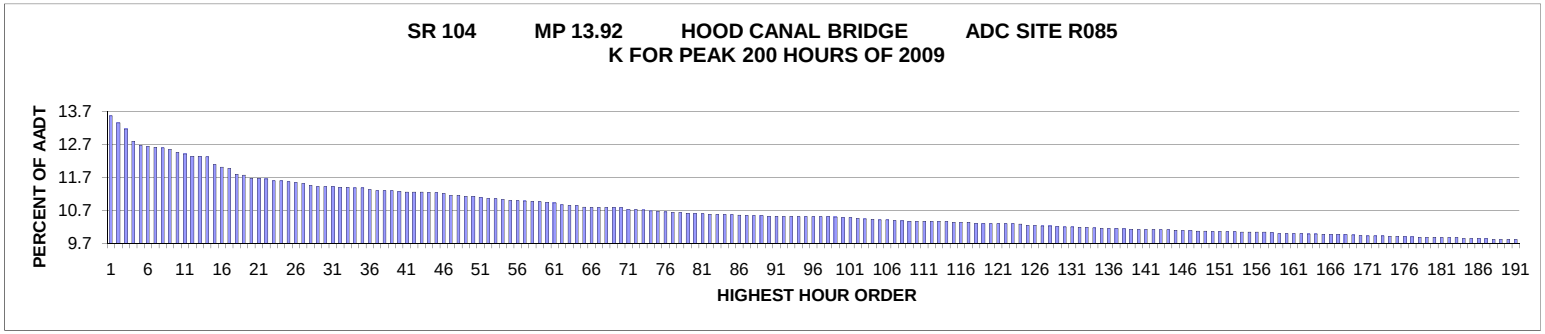

AADT= 16011 **K 30 FACTOR=** 11.67 **K 100 FACTOR=** 10.52 **K 200 FACTOR=** 9.82 **D FACTOR=** 56.8

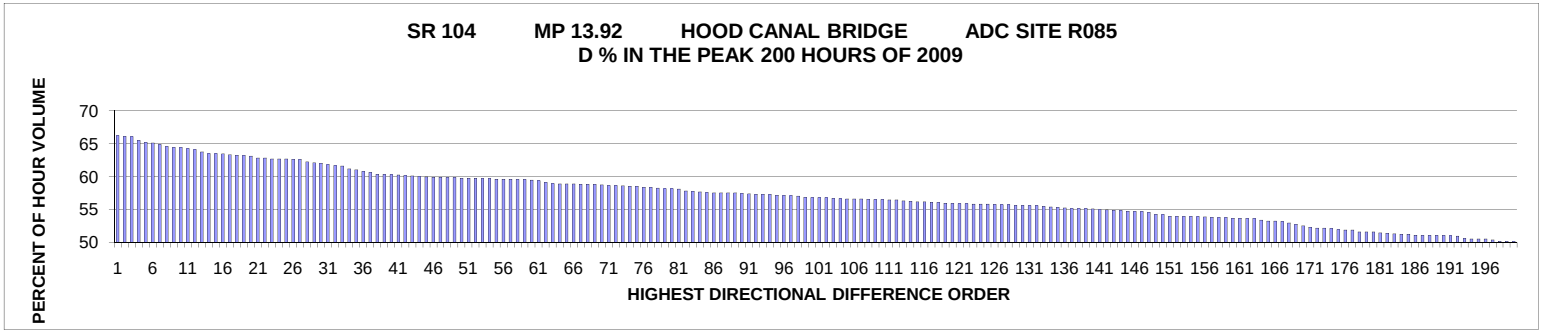

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	18	9	7	17	2173	13.57	1	16011	1157	1016	53.24	46.76
7	19	9	1	12	2137	13.35	2		1096	1041	51.29	48.71
7	19	9	1	13	2109	13.17	3		978	1131	46.37	53.63
7	17	9	6	18	2049	12.8	4		1004	1045	49	51
8	9	9	1	14	2029	12.67	5		1128	901	55.59	44.41
7	26	9	1	16	2023	12.64	6		1022	1001	50.52	49.48
7	25	9	7	11	2021	12.62	7		879	1142	43.49	56.51
9	18	9	6	19	2017	12.6	8		864	1153	42.84	57.16
4	30	9	5	18	2011	12.56	9		1080	931	53.7	46.3
7	3	9	6	18	1995	12.46	10		893	1102	44.76	55.24
7	19	9	1	14	1987	12.41	11		1015	972	51.08	48.92
11	6	9	6	17	1976	12.34	12		951	1025	48.13	51.87
4	26	9	1	17	1975	12.34	13		1115	860	56.46	43.54
8	14	9	6	15	1972	12.32	14		871	1101	44.17	55.83
7	30	9	5	16	1936	12.09	15		926	1010	47.83	52.17
7	26	9	1	12	1923	12.01	16		992	931	51.59	48.41
12	29	9	3	13	1916	11.97	17		948	968	49.48	50.52

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	2	9	1	14	1890	11.8	18		1020	870	53.97	46.03
7	18	9	7	12	1884	11.77	19		700	1184	37.15	62.85
7	31	9	6	17	1868	11.67	20		697	1171	37.31	62.69
9	18	9	6	17	1868	11.67	21	16011	938	930	50.21	49.79
7	26	9	1	13	1865	11.65	22		1029	836	55.17	44.83
7	17	9	6	16	1856	11.59	23		821	1035	44.23	55.77
8	1	9	7	13	1856	11.59	24		802	1054	43.21	56.79
7	18	9	7	13	1853	11.57	25		645	1208	34.81	65.19
7	26	9	1	17	1849	11.55	26		1044	805	56.46	43.54
7	18	9	7	15	1845	11.52	27		784	1061	42.49	57.51
9	11	9	6	15	1835	11.46	28		810	1025	44.14	55.86
8	15	9	7	12	1828	11.42	29		766	1062	41.9	58.1
8	23	9	1	15	1828	11.42	30		1111	717	60.78	39.22
11	27	9	6	14	1828	11.42	31		801	1027	43.82	56.18
8	2	9	1	16	1826	11.4	32		1088	738	59.58	40.42
8	23	9	1	16	1825	11.4	33		1132	693	62.03	37.97
7	18	9	7	14	1822	11.38	34		645	1177	35.4	64.6
9	26	9	7	12	1822	11.38	35		789	1033	43.3	56.7
9	12	9	7	12	1814	11.33	36		658	1156	36.27	63.73
7	5	9	1	12	1808	11.29	37		976	832	53.98	46.02
7	5	9	1	13	1807	11.29	38		1073	734	59.38	40.62
7	18	9	7	11	1807	11.29	39		623	1184	34.48	65.52
8	9	9	1	15	1805	11.27	40		1063	742	58.89	41.11
8	16	9	1	14	1802	11.25	41	16011	912	890	50.61	49.39
8	16	9	1	17	1802	11.25	42		1076	726	59.71	40.29
7	24	9	6	18	1801	11.25	43		702	1099	38.98	61.02
7	18	9	7	18	1799	11.24	44		1137	662	63.2	36.8
11	25	9	4	16	1798	11.23	45		681	1117	37.88	62.12
8	23	9	1	17	1797	11.22	46		1152	645	64.11	35.89
7	19	9	1	16	1787	11.16	47		865	922	48.41	51.59
8	23	9	1	13	1787	11.16	48		985	802	55.12	44.88
7	19	9	1	17	1782	11.13	49		1038	744	58.25	41.75
8	1	9	7	12	1782	11.13	50		785	997	44.05	55.95
8	28	9	6	15	1776	11.09	51		706	1070	39.75	60.25
8	21	9	6	15	1771	11.06	52		728	1043	41.11	58.89
10	13	9	3	16	1770	11.05	53		756	1014	42.71	57.29
7	12	9	1	15	1766	11.03	54		1034	732	58.55	41.45
8	22	9	7	12	1762	11	55		709	1053	40.24	59.76
8	2	9	1	17	1760	10.99	56		1036	724	58.86	41.14
8	2	9	1	13	1758	10.98	57		966	792	54.95	45.05
7	3	9	6	14	1756	10.97	58		625	1131	35.59	64.41
6	28	9	1	17	1755	10.96	59		972	783	55.38	44.62
7	17	9	6	19	1751	10.94	60		819	932	46.77	53.23
7	10	9	6	13	1749	10.92	61	16011	841	908	48.08	51.92
8	16	9	1	12	1740	10.87	62		933	807	53.62	46.38
7	17	9	6	11	1737	10.85	63		738	999	42.49	57.51
8	16	9	1	13	1737	10.85	64		893	844	51.41	48.59
7	31	9	6	18	1729	10.8	65		646	1083	37.36	62.64
7	5	9	1	14	1728	10.79	66		1033	695	59.78	40.22
8	2	9	1	12	1728	10.79	67		948	780	54.86	45.14
8	8	9	7	12	1728	10.79	68		768	960	44.44	55.56
7	3	9	6	12	1727	10.79	69		630	1097	36.48	63.52

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
6	5	9	6	16	1726	10.78	70		722	1004	41.83	58.17
7	28	9	3	17	1717	10.72	71		762	955	44.38	55.62
8	22	9	7	17	1716	10.72	72		876	840	51.05	48.95
8	30	9	1	16	1714	10.71	73		987	727	57.58	42.42
8	14	9	6	16	1710	10.68	74		685	1025	40.06	59.94
8	30	9	1	14	1709	10.67	75		1019	690	59.63	40.37
7	25	9	7	12	1705	10.65	76		740	965	43.4	56.6
7	3	9	6	15	1704	10.64	77		662	1042	38.85	61.15
7	17	9	6	15	1702	10.63	78		748	954	43.95	56.05
4	29	9	4	16	1699	10.61	79		795	904	46.79	53.21
6	25	9	5	15	1697	10.6	80		765	932	45.08	54.92
8	30	9	1	13	1696	10.59	81	16011	981	715	57.84	42.16
12	11	9	6	17	1694	10.58	82		680	1014	40.14	59.86
8	16	9	1	18	1692	10.57	83		1090	602	64.42	35.58
12	26	9	7	11	1692	10.57	84		864	828	51.06	48.94
4	30	9	5	14	1691	10.56	85		885	806	52.34	47.66
7	5	9	1	15	1689	10.55	86		1051	638	62.23	37.77
4	30	9	5	13	1688	10.54	87		924	764	54.74	45.26
7	10	9	6	14	1686	10.53	88		629	1057	37.31	62.69
8	2	9	1	18	1686	10.53	89		1056	630	62.63	37.37
7	24	9	6	15	1685	10.52	90		756	929	44.87	55.13
9	7	9	2	17	1685	10.52	91		1038	647	61.6	38.4
7	25	9	7	15	1684	10.52	92		675	1009	40.08	59.92
8	30	9	1	15	1684	10.52	93		1013	671	60.15	39.85
7	3	9	6	16	1683	10.51	94		691	992	41.06	58.94
7	2	9	5	15	1682	10.51	95		717	965	42.63	57.37
7	5	9	1	16	1682	10.51	96		1062	620	63.14	36.86
8	30	9	1	17	1682	10.51	97		1040	642	61.83	38.17
11	26	9	5	12	1682	10.51	98		723	959	42.98	57.02
8	1	9	7	15	1681	10.5	99		717	964	42.65	57.35
8	9	9	1	13	1678	10.48	100		860	818	51.25	48.75
11	1	9	1	18	1678	10.48	101	16011	855	823	50.95	49.05
6	21	9	1	14	1675	10.46	102		964	711	57.55	42.45
8	1	9	7	14	1671	10.44	103		695	976	41.59	58.41
8	28	9	6	16	1670	10.43	104		677	993	40.54	59.46
7	25	9	7	14	1667	10.41	105		689	978	41.33	58.67
4	26	9	1	18	1666	10.41	106		1101	565	66.09	33.91
8	23	9	1	12	1664	10.39	107		927	737	55.71	44.29
8	16	9	1	16	1662	10.38	108		979	683	58.9	41.1
8	24	9	2	12	1661	10.37	109		894	767	53.82	46.18
7	12	9	1	13	1660	10.37	110		932	728	56.14	43.86
8	9	9	1	16	1660	10.37	111		955	705	57.53	42.47
9	11	9	6	16	1660	10.37	112		767	893	46.2	53.8
9	11	9	6	17	1660	10.37	113		752	908	45.3	54.7
4	24	9	6	14	1659	10.36	114		708	951	42.68	57.32
7	17	9	6	12	1656	10.34	115		669	987	40.4	59.6
8	15	9	7	16	1656	10.34	116		782	874	47.22	52.78
8	16	9	1	15	1655	10.34	117		897	758	54.2	45.8
8	17	9	2	14	1649	10.3	118		723	926	43.84	56.16
4	24	9	6	17	1648	10.29	119		654	994	39.68	60.32
7	31	9	6	16	1648	10.29	120		845	803	51.27	48.73
8	22	9	7	13	1648	10.29	121	16011	716	932	43.45	56.55

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
9	4	9	6	17	1648	10.29	122		632	1016	38.35	61.65
7	19	9	1	18	1647	10.29	123		1042	605	63.27	36.73
8	1	9	7	11	1646	10.28	124		761	885	46.23	53.77
6	19	9	6	18	1640	10.24	125		650	990	39.63	60.37
8	15	9	7	13	1639	10.24	126		711	928	43.38	56.62
7	2	9	5	16	1637	10.22	127		655	982	40.01	59.99
7	11	9	7	14	1637	10.22	128		656	981	40.07	59.93
6	28	9	1	13	1633	10.2	129		847	786	51.87	48.13
3	21	9	7	12	1631	10.19	130		818	813	50.15	49.85
7	17	9	6	14	1631	10.19	131		708	923	43.41	56.59
8	9	9	1	17	1630	10.18	132		976	654	59.88	40.12
9	5	9	7	12	1630	10.18	133		741	889	45.46	54.54
11	13	9	6	16	1628	10.17	134		706	922	43.37	56.63
7	24	9	6	16	1626	10.16	135		687	939	42.25	57.75
7	26	9	1	11	1625	10.15	136		847	778	52.12	47.88
8	15	9	7	14	1625	10.15	137		726	899	44.68	55.32
8	28	9	6	17	1623	10.14	138		663	960	40.85	59.15
8	7	9	6	17	1622	10.13	139		647	975	39.89	60.11
4	30	9	5	19	1620	10.12	140		670	950	41.36	58.64
8	14	9	6	17	1620	10.12	141	16011	674	946	41.6	58.4
11	25	9	4	18	1620	10.12	142		642	978	39.63	60.37
9	13	9	1	17	1618	10.11	143		1050	568	64.89	35.11
11	27	9	6	17	1618	10.11	144		699	919	43.2	56.8
8	21	9	6	18	1617	10.1	145		651	966	40.26	59.74
7	18	9	7	10	1616	10.09	146		676	940	41.83	58.17
9	7	9	2	13	1615	10.09	147		965	650	59.75	40.25
7	10	9	6	16	1613	10.07	148		683	930	42.34	57.66
8	10	9	2	16	1613	10.07	149		692	921	42.9	57.1
8	22	9	7	14	1611	10.06	150		696	915	43.2	56.8
4	5	9	1	16	1610	10.06	151		896	714	55.65	44.35
7	12	9	1	16	1609	10.05	152		906	703	56.31	43.69
9	5	9	7	13	1609	10.05	153		684	925	42.51	57.49
8	8	9	7	13	1608	10.04	154		699	909	43.47	56.53
6	21	9	1	13	1607	10.04	155		851	756	52.96	47.04
9	13	9	1	14	1607	10.04	156		879	728	54.7	45.3
11	27	9	6	12	1607	10.04	157		786	821	48.91	51.09
8	7	9	6	15	1605	10.02	158		779	826	48.54	51.46
8	2	9	1	15	1600	9.99	159		880	720	55	45
8	8	9	7	14	1600	9.99	160		736	864	46	54
6	21	9	1	15	1599	9.99	161	16011	868	731	54.28	45.72
9	13	9	1	18	1599	9.99	162		1015	584	63.48	36.52
7	11	9	7	12	1598	9.98	163		645	953	40.36	59.64
8	21	9	6	17	1598	9.98	164		684	914	42.8	57.2
8	22	9	7	11	1597	9.97	165		707	890	44.27	55.73
8	23	9	1	18	1597	9.97	166		1040	557	65.12	34.88
6	16	9	3	16	1596	9.97	167		705	891	44.17	55.83
4	25	9	7	12	1594	9.96	168		738	856	46.3	53.7
8	7	9	6	16	1593	9.95	169		703	890	44.13	55.87
4	30	9	5	17	1590	9.93	170		801	789	50.38	49.62
6	27	9	7	16	1588	9.92	171		707	881	44.52	55.48
7	26	9	1	19	1588	9.92	172		1005	583	63.29	36.71
8	29	9	7	12	1588	9.92	173		732	856	46.1	53.9

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
9	4	9	6	15	1587	9.91	174		658	929	41.46	58.54
8	29	9	7	16	1586	9.91	175		653	933	41.17	58.83
10	11	9	1	17	1585	9.9	176		1018	567	64.23	35.77
4	26	9	1	15	1583	9.89	177		1005	578	63.49	36.51
8	21	9	6	16	1582	9.88	178		651	931	41.15	58.85
8	22	9	7	16	1582	9.88	179		751	831	47.47	52.53
8	30	9	1	18	1582	9.88	180		929	653	58.72	41.28
9	12	9	7	11	1581	9.87	181	16011	622	959	39.34	60.66
9	12	9	7	13	1581	9.87	182		639	942	40.42	59.58
8	1	9	7	17	1580	9.87	183		773	807	48.92	51.08
7	19	9	1	19	1575	9.84	184		1043	532	66.22	33.78
7	31	9	6	14	1575	9.84	185		680	895	43.17	56.83
10	10	9	7	11	1575	9.84	186		652	923	41.4	58.6
7	11	9	7	11	1574	9.83	187		694	880	44.09	55.91
7	5	9	1	18	1573	9.82	188		1040	533	66.12	33.88
9	12	9	7	17	1573	9.82	189		848	725	53.91	46.09
10	10	9	7	12	1573	9.82	190		688	885	43.74	56.26
11	25	9	4	15	1573	9.82	191		840	733	53.4	46.6
12	10	9	5	16	1573	9.82	192		684	889	43.48	56.52
4	26	9	1	14	1572	9.82	193		866	706	55.09	44.91

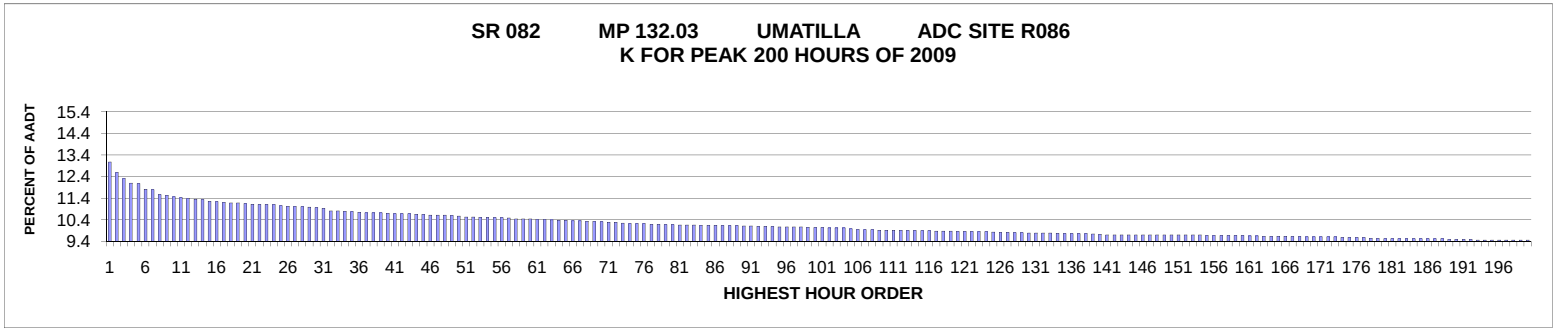

AADT= 17158 **K 30 FACTOR=** 10.96 **K 100 FACTOR=** 10.04 **K 200 FACTOR=** 9.45 **D FACTOR=** 52.04

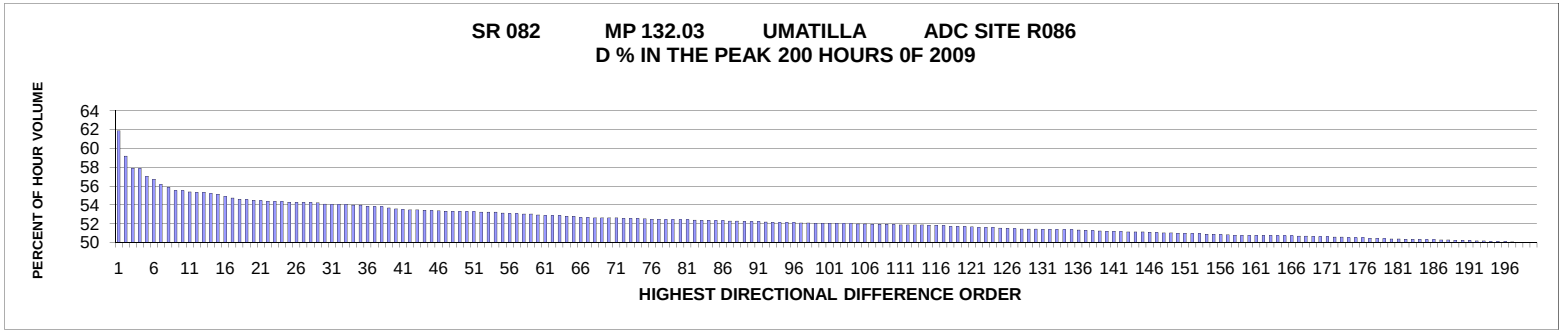

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
11	29	9	1	15	2243	13.07	1	17158	1005	1238	44.81	55.19
11	29	9	1	16	2160	12.59	2		961	1199	44.49	55.51
11	29	9	1	14	2113	12.31	3		970	1143	45.91	54.09
11	25	9	4	17	2075	12.09	4		1092	983	52.63	47.37
11	25	9	4	16	2069	12.06	5		1048	1021	50.65	49.35
11	29	9	1	13	2028	11.82	6		944	1084	46.55	53.45
9	7	9	2	16	2023	11.79	7		1008	1015	49.83	50.17
7	5	9	1	15	1986	11.57	8		1045	941	52.62	47.38
7	5	9	1	17	1978	11.53	9		944	1034	47.72	52.28
7	5	9	1	16	1966	11.46	10		1011	955	51.42	48.58
9	4	9	6	17	1959	11.42	11		1027	932	52.42	47.58
9	4	9	6	16	1955	11.39	12		1042	913	53.3	46.7
6	26	9	6	17	1947	11.35	13		1012	935	51.98	48.02
8	9	9	1	14	1942	11.32	14		952	990	49.02	50.98
8	14	9	6	17	1930	11.25	15		1047	883	54.25	45.75
8	9	9	1	15	1928	11.24	16		886	1042	45.95	54.05
8	9	9	1	17	1921	11.2	17		944	977	49.14	50.86

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	9	9	1	16	1919	11.18	18		893	1026	46.53	53.47
7	10	9	6	17	1917	11.17	19		1110	807	57.9	42.1
9	7	9	2	15	1912	11.14	20		961	951	50.26	49.74
8	16	9	1	17	1908	11.12	21	17158	980	928	51.36	48.64
8	16	9	1	15	1907	11.11	22		878	1029	46.04	53.96
8	16	9	1	16	1906	11.11	23		935	971	49.06	50.94
9	7	9	2	17	1904	11.1	24		912	992	47.9	52.1
11	29	9	1	17	1896	11.05	25		855	1041	45.09	54.91
5	22	9	6	17	1892	11.03	26		1030	862	54.44	45.56
8	7	9	6	16	1889	11.01	27		1002	887	53.04	46.96
7	2	9	5	17	1888	11	28		976	912	51.69	48.31
8	23	9	1	15	1885	10.99	29		866	1019	45.94	54.06
8	7	9	6	15	1880	10.96	30		978	902	52.02	47.98
8	7	9	6	17	1876	10.93	31		974	902	51.92	48.08
7	10	9	6	16	1855	10.81	32		967	888	52.13	47.87
7	2	9	5	16	1853	10.8	33		958	895	51.7	48.3
8	13	9	5	17	1852	10.79	34		924	928	49.89	50.11
7	5	9	1	14	1850	10.78	35		985	865	53.24	46.76
11	25	9	4	18	1843	10.74	36		992	851	53.83	46.17
6	28	9	1	15	1839	10.72	37		901	938	48.99	51.01
7	3	9	6	13	1838	10.71	38		890	948	48.42	51.58
9	7	9	2	14	1837	10.71	39		905	932	49.27	50.73
9	4	9	6	15	1836	10.7	40		915	921	49.84	50.16
11	25	9	4	13	1832	10.68	41	17158	1000	832	54.59	45.41
8	14	9	6	16	1830	10.67	42		958	872	52.35	47.65
8	21	9	6	17	1830	10.67	43		950	880	51.91	48.09
6	19	9	6	16	1829	10.66	44		977	852	53.42	46.58
8	16	9	1	18	1827	10.65	45		1026	801	56.16	43.84
6	19	9	6	17	1820	10.61	46		989	831	54.34	45.66
8	21	9	6	16	1820	10.61	47		906	914	49.78	50.22
9	4	9	6	18	1820	10.61	48		989	831	54.34	45.66
6	26	9	6	16	1818	10.6	49		935	883	51.43	48.57
11	25	9	4	15	1813	10.57	50		965	848	53.23	46.77
8	9	9	1	13	1807	10.53	51		889	918	49.2	50.8
7	19	9	1	16	1805	10.52	52		806	999	44.65	55.35
7	3	9	6	14	1804	10.51	53		932	872	51.66	48.34
4	3	9	6	17	1803	10.51	54		843	960	46.76	53.24
11	25	9	4	14	1801	10.5	55		929	872	51.58	48.42
8	6	9	5	16	1800	10.49	56		867	933	48.17	51.83
7	17	9	6	15	1799	10.48	57		971	828	53.97	46.03
8	9	9	1	18	1792	10.44	58		885	907	49.39	50.61
7	24	9	6	16	1790	10.43	59		946	844	52.85	47.15
3	27	9	6	17	1789	10.43	60		1107	682	61.88	38.12
8	7	9	6	18	1784	10.4	61	17158	925	859	51.85	48.15
8	14	9	6	14	1784	10.4	62		900	884	50.45	49.55
7	24	9	6	17	1783	10.39	63		905	878	50.76	49.24
7	2	9	5	18	1779	10.37	64		888	891	49.92	50.08
8	14	9	6	18	1779	10.37	65		965	814	54.24	45.76
5	22	9	6	16	1776	10.35	66		931	845	52.42	47.58
5	22	9	6	18	1776	10.35	67		901	875	50.73	49.27
7	31	9	6	13	1773	10.33	68		908	865	51.21	48.79
8	6	9	5	18	1769	10.31	69		878	891	49.63	50.37

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	24	9	6	15	1768	10.3	70		931	837	52.66	47.34
5	25	9	2	15	1766	10.29	71		820	946	46.43	53.57
8	23	9	1	14	1764	10.28	72		805	959	45.63	54.37
8	6	9	5	17	1759	10.25	73		822	937	46.73	53.27
7	12	9	1	16	1754	10.22	74		836	918	47.66	52.34
7	31	9	6	17	1752	10.21	75		951	801	54.28	45.72
8	14	9	6	15	1751	10.21	76		958	793	54.71	45.29
6	26	9	6	18	1748	10.19	77		909	839	52	48
5	25	9	2	16	1747	10.18	78		819	928	46.88	53.12
6	26	9	6	15	1745	10.17	79		917	828	52.55	47.45
7	24	9	6	14	1745	10.17	80		873	872	50.03	49.97
7	2	9	5	15	1744	10.16	81	17158	889	855	50.97	49.03
4	5	9	1	16	1742	10.15	82		778	964	44.66	55.34
8	21	9	6	15	1741	10.15	83		1007	734	57.84	42.16
7	19	9	1	15	1740	10.14	84		848	892	48.74	51.26
6	21	9	1	16	1739	10.14	85		813	926	46.75	53.25
8	28	9	6	17	1739	10.14	86		899	840	51.7	48.3
8	23	9	1	16	1738	10.13	87		831	907	47.81	52.19
7	31	9	6	18	1737	10.12	88		888	849	51.12	48.88
7	2	9	5	14	1736	10.12	89		896	840	51.61	48.39
8	16	9	1	14	1734	10.11	90		836	898	48.21	51.79
11	29	9	1	12	1734	10.11	91		862	872	49.71	50.29
8	16	9	1	13	1732	10.09	92		824	908	47.58	52.42
7	6	9	2	17	1731	10.09	93		865	866	49.97	50.03
7	31	9	6	14	1729	10.08	94		904	825	52.28	47.72
6	25	9	5	18	1728	10.07	95		832	896	48.15	51.85
10	9	9	6	17	1728	10.07	96		943	785	54.57	45.43
4	5	9	1	17	1727	10.07	97		867	860	50.2	49.8
7	17	9	6	14	1727	10.07	98		936	791	54.2	45.8
6	12	9	6	16	1725	10.05	99		882	843	51.13	48.87
7	6	9	2	16	1723	10.04	100		850	873	49.33	50.67
7	31	9	6	16	1723	10.04	101	17158	896	827	52	48
8	21	9	6	14	1720	10.02	102		883	837	51.34	48.66
5	25	9	2	17	1719	10.02	103		794	925	46.19	53.81
7	10	9	6	14	1719	10.02	104		899	820	52.3	47.7
7	17	9	6	17	1712	9.98	105		905	807	52.86	47.14
7	3	9	6	15	1705	9.94	106		888	817	52.08	47.92
9	4	9	6	14	1704	9.93	107		876	828	51.41	48.59
7	6	9	2	15	1703	9.93	108		860	843	50.5	49.5
6	25	9	5	17	1702	9.92	109		847	855	49.76	50.24
7	12	9	1	17	1701	9.91	110		731	970	42.97	57.03
9	11	9	6	17	1701	9.91	111		938	763	55.14	44.86
8	28	9	6	16	1700	9.91	112		862	838	50.71	49.29
6	19	9	6	18	1699	9.9	113		943	756	55.5	44.5
6	21	9	1	17	1698	9.9	114		818	880	48.17	51.83
7	6	9	2	18	1696	9.88	115		796	900	46.93	53.07
7	17	9	6	16	1696	9.88	116		900	796	53.07	46.93
7	26	9	1	15	1694	9.87	117		806	888	47.58	52.42
8	14	9	6	13	1693	9.87	118		878	815	51.86	48.14
8	30	9	1	15	1693	9.87	119		839	854	49.56	50.44
8	30	9	1	14	1692	9.86	120		836	856	49.41	50.59
7	9	9	5	16	1691	9.86	121	17158	871	820	51.51	48.49

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	31	9	6	15	1691	9.86	122		858	833	50.74	49.26
8	2	9	1	16	1689	9.84	123		812	877	48.08	51.92
8	7	9	6	14	1688	9.84	124		903	785	53.5	46.5
7	5	9	1	18	1686	9.83	125		853	833	50.59	49.41
3	29	9	1	16	1683	9.81	126		843	840	50.09	49.91
6	12	9	6	17	1683	9.81	127		917	766	54.49	45.51
7	24	9	6	13	1682	9.8	128		857	825	50.95	49.05
7	9	9	5	18	1681	9.8	129		846	835	50.33	49.67
7	12	9	1	14	1679	9.79	130		844	835	50.27	49.73
5	25	9	2	14	1678	9.78	131		808	870	48.15	51.85
7	26	9	1	16	1678	9.78	132		819	859	48.81	51.19
8	21	9	6	18	1678	9.78	133		832	846	49.58	50.42
6	19	9	6	15	1676	9.77	134		887	789	52.92	47.08
7	10	9	6	15	1675	9.76	135		882	793	52.66	47.34
8	20	9	5	18	1675	9.76	136		838	837	50.03	49.97
7	5	9	1	13	1673	9.75	137		878	795	52.48	47.52
8	30	9	1	16	1673	9.75	138		849	824	50.75	49.25
6	28	9	1	17	1671	9.74	139		774	897	46.32	53.68
7	3	9	6	16	1668	9.72	140		822	846	49.28	50.72
5	15	9	6	16	1665	9.7	141	17158	875	790	52.55	47.45
7	30	9	5	17	1665	9.7	142		824	841	49.49	50.51
8	7	9	6	13	1665	9.7	143		821	844	49.31	50.69
3	27	9	6	18	1664	9.7	144		985	679	59.19	40.81
3	29	9	1	15	1664	9.7	145		866	798	52.04	47.96
8	13	9	5	16	1664	9.7	146		813	851	48.86	51.14
8	23	9	1	17	1664	9.7	147		795	869	47.78	52.22
9	25	9	6	17	1664	9.7	148		874	790	52.52	47.48
6	12	9	6	14	1663	9.69	149		895	768	53.82	46.18
8	19	9	4	18	1663	9.69	150		781	882	46.96	53.04
9	18	9	6	18	1663	9.69	151		899	764	54.06	45.94
7	24	9	6	18	1662	9.69	152		863	799	51.93	48.07
8	2	9	1	17	1662	9.69	153		821	841	49.4	50.6
10	16	9	6	17	1662	9.69	154		877	785	52.77	47.23
8	28	9	6	18	1660	9.67	155		835	825	50.3	49.7
6	5	9	6	17	1659	9.67	156		824	835	49.67	50.33
6	18	9	5	17	1659	9.67	157		873	786	52.62	47.38
7	9	9	5	17	1659	9.67	158		851	808	51.3	48.7
7	23	9	5	17	1658	9.66	159		812	846	48.97	51.03
7	2	9	5	13	1657	9.66	160		814	843	49.12	50.88
8	13	9	5	18	1656	9.65	161	17158	804	852	48.55	51.45
5	22	9	6	15	1655	9.65	162		883	772	53.35	46.65
5	8	9	6	17	1654	9.64	163		870	784	52.6	47.4
10	2	9	6	16	1654	9.64	164		924	730	55.86	44.14
7	16	9	5	17	1653	9.63	165		807	846	48.82	51.18
8	20	9	5	17	1653	9.63	166		809	844	48.94	51.06
8	14	9	6	12	1651	9.62	167		865	786	52.39	47.61
7	12	9	1	15	1650	9.62	168		802	848	48.61	51.39
6	26	9	6	14	1649	9.61	169		847	802	51.36	48.64
6	28	9	1	16	1649	9.61	170		792	857	48.03	51.97
9	18	9	6	16	1649	9.61	171		830	819	50.33	49.67
8	30	9	1	17	1648	9.6	172		783	865	47.51	52.49
7	3	9	6	12	1647	9.6	173		789	858	47.91	52.09

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	2	9	1	15	1643	9.58	174		836	807	50.88	49.12
9	4	9	6	13	1642	9.57	175		798	844	48.6	51.4
9	18	9	6	17	1642	9.57	176		839	803	51.1	48.9
11	25	9	4	12	1642	9.57	177		877	765	53.41	46.59
7	17	9	6	13	1638	9.55	178		857	781	52.32	47.68
7	19	9	1	17	1635	9.53	179		771	864	47.16	52.84
6	19	9	6	14	1634	9.52	180		850	784	52.02	47.98
7	1	9	4	17	1634	9.52	181	17158	811	823	49.63	50.37
10	16	9	6	18	1634	9.52	182		927	707	56.73	43.27
4	17	9	6	17	1633	9.52	183		886	747	54.26	45.74
8	2	9	1	14	1633	9.52	184		782	851	47.89	52.11
8	10	9	2	17	1633	9.52	185		850	783	52.05	47.95
8	13	9	5	15	1633	9.52	186		771	862	47.21	52.79
7	19	9	1	14	1631	9.51	187		834	797	51.13	48.87
10	9	9	6	18	1631	9.51	188		870	761	53.34	46.66
10	9	9	6	16	1629	9.49	189		856	773	52.55	47.45
8	12	9	4	17	1627	9.48	190		802	825	49.29	50.71
8	28	9	6	15	1627	9.48	191		847	780	52.06	47.94
8	27	9	5	17	1626	9.48	192		821	805	50.49	49.51
6	18	9	5	18	1624	9.46	193		788	836	48.52	51.48
6	21	9	1	15	1623	9.46	194		775	848	47.75	52.25
8	17	9	2	15	1623	9.46	195		813	810	50.09	49.91
6	14	9	1	15	1622	9.45	196		776	846	47.84	52.16
8	17	9	2	18	1622	9.45	197		757	865	46.67	53.33
10	23	9	6	17	1622	9.45	198		898	724	55.36	44.64
7	23	9	5	15	1621	9.45	199		798	823	49.23	50.77
7	26	9	1	14	1621	9.45	200		789	832	48.67	51.33

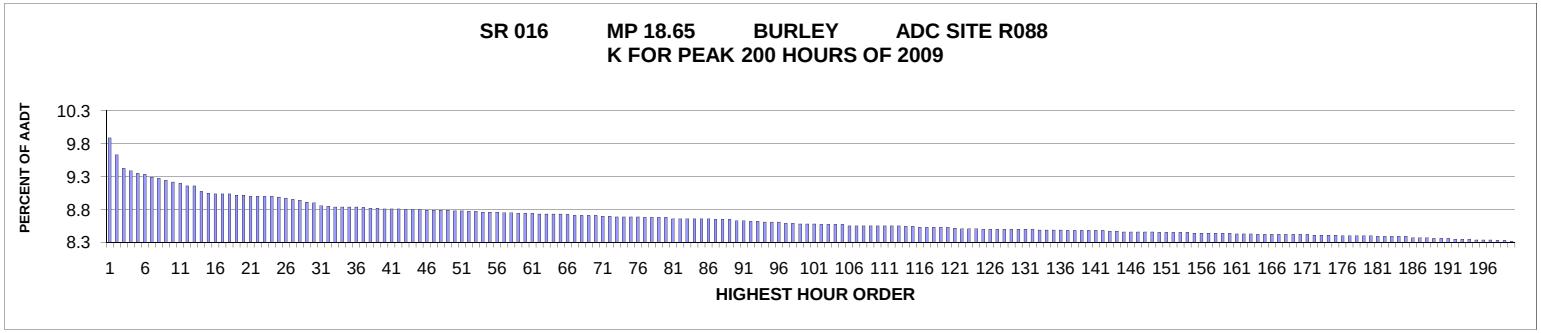

AADT= 42310 **K 30 FACTOR=** 8.9 **K 100 FACTOR=** 8.58 **K 200 FACTOR=** 8.32 **D FACTOR=** 53.22

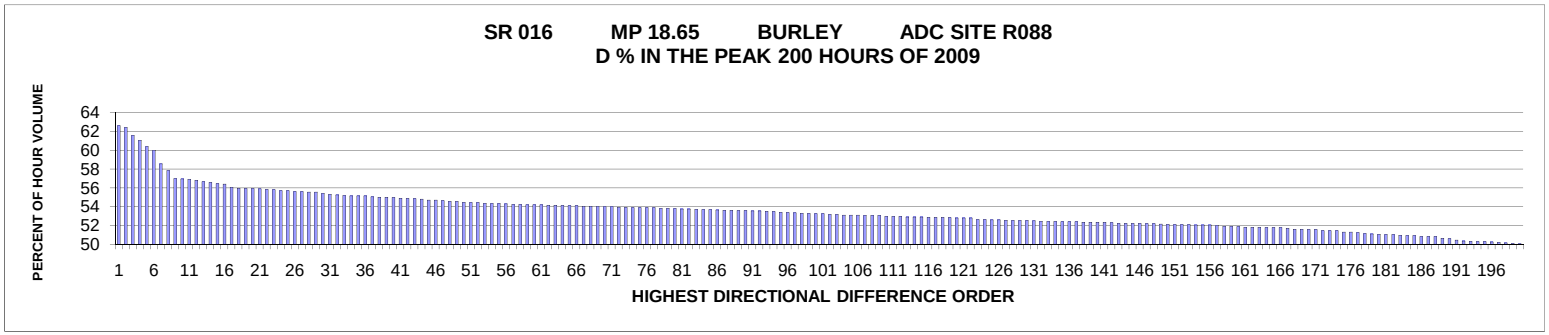

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
6	5	9	6	18	4186	9.89	1	42310	2266	1920	54.13	45.87
6	5	9	6	17	4074	9.63	2		2032	2042	49.88	50.12
11	26	9	5	13	3987	9.42	3		1839	2148	46.12	53.88
7	24	9	6	17	3974	9.39	4		1711	2263	43.05	56.95
8	14	9	6	17	3954	9.35	5		1819	2135	46	54
12	18	9	6	17	3948	9.33	6		1849	2099	46.83	53.17
8	21	9	6	17	3932	9.29	7		1734	2198	44.1	55.9
6	19	9	6	17	3922	9.27	8		1862	2060	47.48	52.52
10	30	9	6	17	3910	9.24	9		1785	2125	45.65	54.35
10	9	9	6	17	3900	9.22	10		1834	2066	47.03	52.97
7	24	9	6	16	3891	9.2	11		1774	2117	45.59	54.41
11	12	9	5	17	3876	9.16	12		1811	2065	46.72	53.28
12	11	9	6	17	3874	9.16	13		1863	2011	48.09	51.91
11	26	9	5	14	3839	9.07	14		1740	2099	45.32	54.68
10	22	9	5	17	3830	9.05	15		1830	2000	47.78	52.22
7	2	9	5	16	3826	9.04	16		1763	2063	46.08	53.92
12	3	9	5	17	3825	9.04	17		1818	2007	47.53	52.47

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
11	13	9	6	17	3823	9.04	18		1781	2042	46.59	53.41
4	24	9	6	17	3817	9.02	19		1821	1996	47.71	52.29
11	20	9	6	17	3815	9.02	20		1830	1985	47.97	52.03
9	11	9	6	17	3809	9	21	42310	1809	2000	47.49	52.51
12	22	9	3	17	3809	9	22		1806	2003	47.41	52.59
10	23	9	6	17	3808	9	23		1835	1973	48.19	51.81
11	25	9	4	17	3806	9	24		1692	2114	44.46	55.54
8	28	9	6	17	3803	8.99	25		1706	2097	44.86	55.14
7	17	9	6	17	3794	8.97	26		1760	2034	46.39	53.61
11	24	9	3	17	3788	8.95	27		1785	2003	47.12	52.88
10	2	9	6	17	3782	8.94	28		1860	1922	49.18	50.82
11	26	9	5	12	3770	8.91	29		1697	2073	45.01	54.99
5	15	9	6	17	3765	8.9	30		1804	1961	47.92	52.08
9	4	9	6	17	3749	8.86	31		1699	2050	45.32	54.68
11	25	9	4	16	3743	8.85	32		1711	2032	45.71	54.29
12	4	9	6	17	3742	8.84	33		1764	1978	47.14	52.86
2	27	9	6	17	3741	8.84	34		1760	1981	47.05	52.95
8	20	9	5	17	3739	8.84	35		1834	1905	49.05	50.95
12	21	9	2	17	3739	8.84	36		1729	2010	46.24	53.76
10	9	9	6	18	3738	8.83	37		1790	1948	47.89	52.11
8	14	9	6	18	3733	8.82	38		1645	2088	44.07	55.93
8	21	9	6	16	3730	8.82	39		1718	2012	46.06	53.94
8	28	9	6	16	3729	8.81	40		1731	1998	46.42	53.58
10	8	9	5	17	3729	8.81	41	42310	1720	2009	46.12	53.88
10	15	9	5	17	3727	8.81	42		1713	2014	45.96	54.04
6	12	9	6	17	3724	8.8	43		1723	2001	46.27	53.73
6	11	9	5	17	3722	8.8	44		1839	1883	49.41	50.59
10	2	9	6	16	3722	8.8	45		1704	2018	45.78	54.22
1	16	9	6	17	3720	8.79	46		1766	1954	47.47	52.53
8	28	9	6	18	3720	8.79	47		1649	2071	44.33	55.67
8	7	9	6	17	3717	8.79	48		1800	1917	48.43	51.57
12	23	9	4	17	3717	8.79	49		1717	2000	46.19	53.81
6	5	9	6	16	3714	8.78	50		1706	2008	45.93	54.07
12	24	9	5	14	3713	8.78	51		1719	1994	46.3	53.7
4	17	9	6	17	3711	8.77	52		1817	1894	48.96	51.04
7	10	9	6	17	3710	8.77	53		1741	1969	46.93	53.07
12	4	9	6	18	3708	8.76	54		1730	1978	46.66	53.34
4	10	9	6	17	3707	8.76	55		1663	2044	44.86	55.14
12	18	9	6	16	3706	8.76	56		1698	2008	45.82	54.18
9	10	9	5	17	3703	8.75	57		1849	1854	49.93	50.07
12	18	9	6	18	3702	8.75	58		1763	1939	47.62	52.38
6	26	9	6	17	3700	8.74	59		1714	1986	46.32	53.68
7	9	9	5	17	3698	8.74	60		1837	1861	49.68	50.32
9	11	9	6	18	3698	8.74	61	42310	1759	1939	47.57	52.43
6	12	9	6	16	3695	8.73	62		1716	1979	46.44	53.56
8	11	9	3	17	3695	8.73	63		1731	1964	46.85	53.15
9	3	9	5	17	3695	8.73	64		1818	1877	49.2	50.8
2	13	9	6	17	3693	8.73	65		1759	1934	47.63	52.37
7	2	9	5	17	3689	8.72	66		1690	1999	45.81	54.19
12	10	9	5	17	3687	8.71	67		1756	1931	47.63	52.37
6	19	9	6	16	3686	8.71	68		1767	1919	47.94	52.06
12	17	9	5	17	3685	8.71	69		1773	1912	48.11	51.89

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	14	9	6	16	3684	8.71	70		1657	2027	44.98	55.02
9	25	9	6	18	3683	8.7	71		1693	1990	45.97	54.03
10	29	9	5	17	3681	8.7	72		1752	1929	47.6	52.4
10	27	9	3	17	3678	8.69	73		1736	1942	47.2	52.8
11	12	9	5	18	3677	8.69	74		1744	1933	47.43	52.57
8	7	9	6	16	3675	8.69	75		1708	1967	46.48	53.52
10	28	9	4	17	3675	8.69	76		1771	1904	48.19	51.81
8	12	9	4	17	3672	8.68	77		1734	1938	47.22	52.78
9	17	9	5	17	3672	8.68	78		1763	1909	48.01	51.99
7	3	9	6	14	3671	8.68	79		1468	2203	39.99	60.01
7	17	9	6	18	3671	8.68	80		1580	2091	43.04	56.96
10	16	9	6	17	3666	8.66	81	42310	1721	1945	46.94	53.06
12	24	9	5	15	3665	8.66	82		1634	2031	44.58	55.42
9	25	9	6	17	3664	8.66	83		1823	1841	49.75	50.25
6	30	9	3	17	3663	8.66	84		1746	1917	47.67	52.33
8	7	9	6	18	3663	8.66	85		1653	2010	45.13	54.87
8	21	9	6	18	3662	8.66	86		1588	2074	43.36	56.64
10	30	9	6	16	3661	8.65	87		1735	1926	47.39	52.61
10	9	9	6	16	3660	8.65	88		1717	1943	46.91	53.09
6	25	9	5	18	3658	8.65	89		1640	2018	44.83	55.17
10	5	9	2	17	3651	8.63	90		1833	1818	50.21	49.79
11	19	9	5	17	3650	8.63	91		1684	1966	46.14	53.86
12	16	9	4	17	3647	8.62	92		1748	1899	47.93	52.07
9	3	9	5	18	3646	8.62	93		1766	1880	48.44	51.56
1	9	9	6	17	3642	8.61	94		1699	1943	46.65	53.35
2	20	9	6	17	3642	8.61	95		1787	1855	49.07	50.93
8	31	9	2	17	3641	8.61	96		1709	1932	46.94	53.06
6	10	9	4	17	3633	8.59	97		1853	1780	51	49
8	31	9	2	18	3633	8.59	98		1721	1912	47.37	52.63
5	27	9	4	17	3631	8.58	99		1751	1880	48.22	51.78
12	23	9	4	16	3631	8.58	100		1655	1976	45.58	54.42
4	30	9	5	17	3629	8.58	101	42310	1734	1895	47.78	52.22
6	18	9	5	17	3628	8.57	102		1773	1855	48.87	51.13
7	17	9	6	16	3626	8.57	103		1682	1944	46.39	53.61
9	16	9	4	18	3626	8.57	104		1790	1836	49.37	50.63
11	2	9	2	17	3626	8.57	105		1633	1993	45.04	54.96
11	13	9	6	18	3619	8.55	106		1629	1990	45.01	54.99
8	26	9	4	17	3617	8.55	107		1769	1848	48.91	51.09
10	7	9	4	17	3617	8.55	108		1673	1944	46.25	53.75
10	13	9	3	17	3617	8.55	109		1661	1956	45.92	54.08
10	21	9	4	17	3617	8.55	110		1723	1894	47.64	52.36
4	17	9	6	16	3616	8.55	111		1730	1886	47.84	52.16
7	22	9	4	17	3616	8.55	112		1807	1809	49.97	50.03
7	24	9	6	18	3616	8.55	113		1562	2054	43.2	56.8
5	1	9	6	17	3615	8.54	114		1696	1919	46.92	53.08
5	8	9	6	17	3613	8.54	115		1690	1923	46.78	53.22
1	23	9	6	17	3611	8.53	116		1638	1973	45.36	54.64
8	7	9	6	15	3611	8.53	117		1744	1867	48.3	51.7
9	15	9	3	17	3611	8.53	118		1796	1815	49.74	50.26
12	29	9	3	17	3611	8.53	119		1569	2042	43.45	56.55
9	4	9	6	16	3610	8.53	120		1667	1943	46.18	53.82
7	23	9	5	17	3605	8.52	121	42310	1813	1792	50.29	49.71

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
9	24	9	5	17	3600	8.51	122		1737	1863	48.25	51.75
11	20	9	6	18	3600	8.51	123		1601	1999	44.47	55.53
5	21	9	5	17	3599	8.51	124		1770	1829	49.18	50.82
3	13	9	6	17	3598	8.5	125		1683	1915	46.78	53.22
6	25	9	5	17	3598	8.5	126		1766	1832	49.08	50.92
12	1	9	3	18	3597	8.5	127		1607	1990	44.68	55.32
12	15	9	3	17	3597	8.5	128		1643	1954	45.68	54.32
8	6	9	5	17	3596	8.5	129		1740	1856	48.39	51.61
12	24	9	5	13	3596	8.5	130		1706	1890	47.44	52.56
8	20	9	5	18	3595	8.5	131		1648	1947	45.84	54.16
12	1	9	3	17	3595	8.5	132		1718	1877	47.79	52.21
12	24	9	5	16	3593	8.49	133		1566	2027	43.58	56.42
9	30	9	4	17	3591	8.49	134		1744	1847	48.57	51.43
11	6	9	6	17	3591	8.49	135		1641	1950	45.7	54.3
12	2	9	4	17	3591	8.49	136		1644	1947	45.78	54.22
6	17	9	4	17	3589	8.48	137		1758	1831	48.98	51.02
9	1	9	3	18	3589	8.48	138		1622	1967	45.19	54.81
12	10	9	5	18	3589	8.48	139		1655	1934	46.11	53.89
5	22	9	6	16	3588	8.48	140		1644	1944	45.82	54.18
8	4	9	3	17	3588	8.48	141	42310	1716	1872	47.83	52.17
4	8	9	4	17	3587	8.48	142		1668	1919	46.5	53.5
7	3	9	6	15	3585	8.47	143		1378	2207	38.44	61.56
9	24	9	5	18	3583	8.47	144		1718	1865	47.95	52.05
6	26	9	6	16	3581	8.46	145		1744	1837	48.7	51.3
7	2	9	5	18	3581	8.46	146		1485	2096	41.47	58.53
8	27	9	5	17	3581	8.46	147		1739	1842	48.56	51.44
7	24	9	6	15	3580	8.46	148		1691	1889	47.23	52.77
10	23	9	6	18	3578	8.46	149		1602	1976	44.77	55.23
8	25	9	3	17	3577	8.45	150		1724	1853	48.2	51.8
7	3	9	6	13	3576	8.45	151		1392	2184	38.93	61.07
10	19	9	2	17	3575	8.45	152		1677	1898	46.91	53.09
10	26	9	2	17	3575	8.45	153		1612	1963	45.09	54.91
12	11	9	6	18	3575	8.45	154		1663	1912	46.52	53.48
7	7	9	3	17	3572	8.44	155		1720	1852	48.15	51.85
12	9	9	4	17	3572	8.44	156		1655	1917	46.33	53.67
1	30	9	6	17	3571	8.44	157		1707	1864	47.8	52.2
4	23	9	5	17	3570	8.44	158		1684	1886	47.17	52.83
12	30	9	4	17	3570	8.44	159		1557	2013	43.61	56.39
10	2	9	6	18	3569	8.44	160		1659	1910	46.48	53.52
9	16	9	4	17	3568	8.43	161	42310	1800	1768	50.45	49.55
10	1	9	5	17	3567	8.43	162		1700	1867	47.66	52.34
7	5	9	1	14	3565	8.43	163		2152	1413	60.36	39.64
11	4	9	4	17	3564	8.42	164		1738	1826	48.77	51.23
8	21	9	6	15	3563	8.42	165		1640	1923	46.03	53.97
11	18	9	4	18	3563	8.42	166		1503	2060	42.18	57.82
7	25	9	7	14	3562	8.42	167		1333	2229	37.42	62.58
8	3	9	2	17	3562	8.42	168		1735	1827	48.71	51.29
9	8	9	3	17	3562	8.42	169		1652	1910	46.38	53.62
6	12	9	6	18	3561	8.42	170		1634	1927	45.89	54.11
11	25	9	4	15	3561	8.42	171		1597	1964	44.85	55.15
7	3	9	6	16	3559	8.41	172		1338	2221	37.59	62.41
7	8	9	4	17	3558	8.41	173		1769	1789	49.72	50.28

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
2	27	9	6	18	3557	8.41	174		1617	1940	45.46	54.54
10	20	9	3	17	3557	8.41	175		1617	1940	45.46	54.54
3	6	9	6	17	3555	8.4	176		1675	1880	47.12	52.88
11	17	9	3	17	3555	8.4	177		1694	1861	47.65	52.35
5	15	9	6	16	3554	8.4	178		1721	1833	48.42	51.58
12	23	9	4	18	3553	8.4	179		1571	1982	44.22	55.78
8	5	9	4	17	3552	8.4	180		1690	1862	47.58	52.42
5	22	9	6	17	3551	8.39	181	42310	1635	1916	46.04	53.96
5	29	9	6	17	3550	8.39	182		1672	1878	47.1	52.9
7	10	9	6	16	3550	8.39	183		1699	1851	47.86	52.14
12	2	9	4	18	3549	8.39	184		1577	1972	44.44	55.56
10	16	9	6	18	3548	8.39	185		1565	1983	44.11	55.89
7	1	9	4	18	3543	8.37	186		1600	1943	45.16	54.84
10	6	9	3	17	3541	8.37	187		1669	1872	47.13	52.87
8	18	9	3	17	3540	8.37	188		1556	1984	43.95	56.05
6	26	9	6	18	3539	8.36	189		1563	1976	44.17	55.83
9	25	9	6	16	3537	8.36	190		1718	1819	48.57	51.43
8	24	9	2	17	3536	8.36	191		1705	1831	48.22	51.78
4	15	9	4	17	3535	8.35	192		1667	1868	47.16	52.84
5	15	9	6	18	3533	8.35	193		1566	1967	44.32	55.68
11	5	9	5	17	3532	8.35	194		1651	1881	46.74	53.26
7	2	9	5	15	3530	8.34	195		1568	1962	44.42	55.58
7	1	9	4	17	3529	8.34	196		1660	1869	47.04	52.96
10	15	9	5	18	3528	8.34	197		1520	2008	43.08	56.92
4	3	9	6	17	3525	8.33	198		1606	1919	45.56	54.44
6	16	9	3	17	3525	8.33	199		1691	1834	47.97	52.03
8	6	9	5	18	3521	8.32	200		1551	1970	44.05	55.95

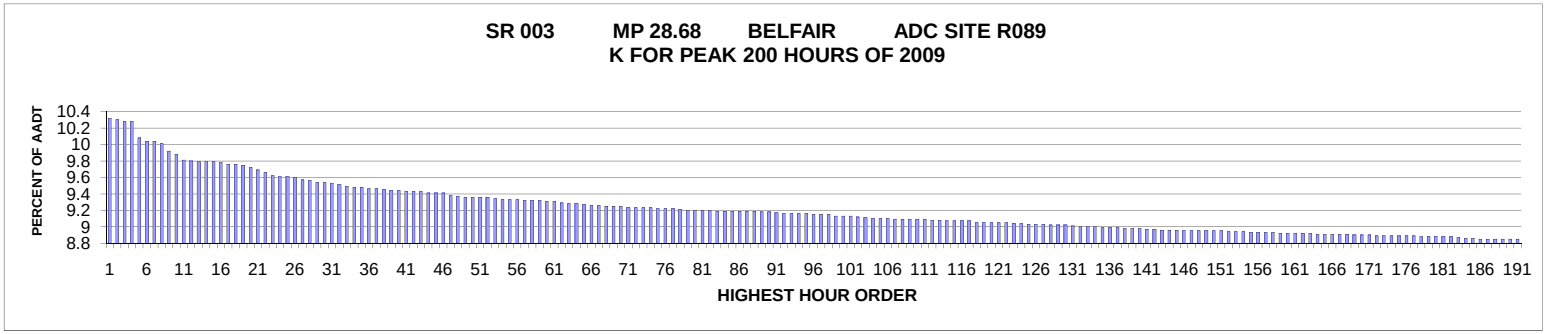

AADT= 17113 **K 30 FACTOR=** 9.54 **K 100 FACTOR=** 9.17 **K 200 FACTOR=** 8.85 **D FACTOR=** 61.63

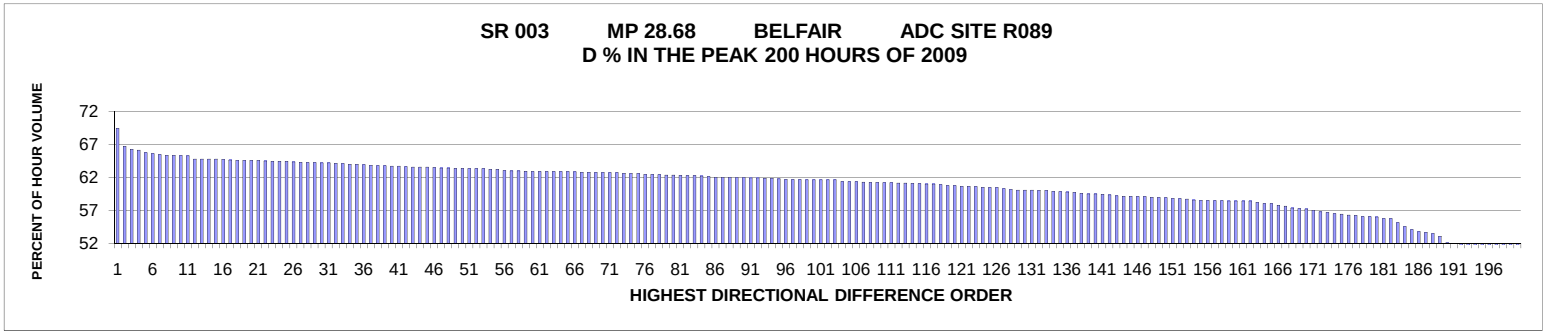

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	21	9	6	17	1766	10.32	1	17113	671	1095	38	62
5	1	9	6	17	1762	10.3	2		676	1086	38.37	61.63
5	1	9	6	16	1760	10.28	3		675	1085	38.35	61.65
5	15	9	6	17	1760	10.28	4		664	1096	37.73	62.27
8	14	9	6	17	1725	10.08	5		632	1093	36.64	63.36
5	8	9	6	18	1719	10.04	6		619	1100	36.01	63.99
5	15	9	6	16	1718	10.04	7		692	1026	40.28	59.72
3	13	9	6	17	1713	10.01	8		617	1096	36.02	63.98
5	8	9	6	17	1697	9.92	9		619	1078	36.48	63.52
8	28	9	6	17	1691	9.88	10		642	1049	37.97	62.03
7	24	9	6	17	1678	9.81	11		614	1064	36.59	63.41
8	28	9	6	16	1677	9.8	12		671	1006	40.01	59.99
4	24	9	6	17	1676	9.79	13		608	1068	36.28	63.72
5	8	9	6	16	1676	9.79	14		669	1007	39.92	60.08
5	29	9	6	16	1676	9.79	15		742	934	44.27	55.73
5	23	9	7	11	1674	9.78	16		593	1081	35.42	64.58
7	31	9	6	15	1671	9.76	17		686	985	41.05	58.95

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	21	9	6	16	1671	9.76	18		680	991	40.69	59.31
5	9	9	7	16	1668	9.75	19		820	848	49.16	50.84
5	1	9	6	18	1663	9.72	20		657	1006	39.51	60.49
8	1	9	7	13	1658	9.69	21	17113	730	928	44.03	55.97
7	31	9	6	16	1653	9.66	22		639	1014	38.66	61.34
8	7	9	6	16	1647	9.62	23		703	944	42.68	57.32
8	7	9	6	17	1645	9.61	24		612	1033	37.2	62.8
5	8	9	6	15	1644	9.61	25		748	896	45.5	54.5
8	14	9	6	16	1643	9.6	26		653	990	39.74	60.26
10	2	9	6	17	1637	9.57	27		607	1030	37.08	62.92
6	12	9	6	16	1636	9.56	28		669	967	40.89	59.11
5	15	9	6	15	1633	9.54	29		677	956	41.46	58.54
10	9	9	6	17	1632	9.54	30		626	1006	38.36	61.64
5	25	9	2	13	1631	9.53	31		976	655	59.84	40.16
7	10	9	6	17	1628	9.51	32		604	1024	37.1	62.9
7	17	9	6	16	1624	9.49	33		601	1023	37.01	62.99
4	10	9	6	16	1623	9.48	34		633	990	39	61
8	7	9	6	15	1622	9.48	35		673	949	41.49	58.51
1	16	9	6	17	1619	9.46	36		570	1049	35.21	64.79
4	17	9	6	17	1619	9.46	37		575	1044	35.52	64.48
8	21	9	6	15	1617	9.45	38		692	925	42.8	57.2
5	1	9	6	15	1616	9.44	39		675	941	41.77	58.23
5	20	9	4	17	1615	9.44	40		600	1015	37.15	62.85
9	25	9	6	17	1614	9.43	41	17113	610	1004	37.79	62.21
6	12	9	6	17	1613	9.43	42		575	1038	35.65	64.35
7	31	9	6	17	1613	9.43	43		577	1036	35.77	64.23
9	12	9	7	12	1611	9.41	44		786	825	48.79	51.21
2	13	9	6	17	1610	9.41	45		570	1040	35.4	64.6
6	15	9	2	17	1610	9.41	46		618	992	38.39	61.61
3	6	9	6	17	1606	9.38	47		583	1023	36.3	63.7
6	19	9	6	16	1603	9.37	48		677	926	42.23	57.77
4	10	9	6	17	1602	9.36	49		564	1038	35.21	64.79
5	12	9	3	17	1602	9.36	50		570	1032	35.58	64.42
5	25	9	2	14	1601	9.36	51		971	630	60.65	39.35
7	24	9	6	18	1601	9.36	52		609	992	38.04	61.96
1	9	9	6	17	1598	9.34	53		539	1059	33.73	66.27
6	19	9	6	17	1596	9.33	54		547	1049	34.27	65.73
7	15	9	4	17	1596	9.33	55		600	996	37.59	62.41
10	7	9	4	17	1596	9.33	56		609	987	38.16	61.84
5	14	9	5	17	1595	9.32	57		587	1008	36.8	63.2
7	10	9	6	16	1595	9.32	58		654	941	41	59
9	11	9	6	18	1595	9.32	59		585	1010	36.68	63.32
6	9	9	3	17	1594	9.31	60		606	988	38.02	61.98
8	20	9	5	17	1594	9.31	61	17113	621	973	38.96	61.04
4	24	9	6	16	1590	9.29	62		622	968	39.12	60.88
7	24	9	6	16	1588	9.28	63		655	933	41.25	58.75
7	31	9	6	14	1588	9.28	64		698	890	43.95	56.05
9	11	9	6	15	1586	9.27	65		666	920	41.99	58.01
9	4	9	6	16	1585	9.26	66		655	930	41.32	58.68
10	23	9	6	17	1585	9.26	67		591	994	37.29	62.71
6	5	9	6	16	1583	9.25	68		647	936	40.87	59.13
6	5	9	6	17	1583	9.25	69		624	959	39.42	60.58

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	26	9	4	17	1583	9.25	70		596	987	37.65	62.35
8	7	9	6	18	1580	9.23	71		616	964	38.99	61.01
9	11	9	6	17	1580	9.23	72		636	944	40.25	59.75
4	24	9	6	18	1579	9.23	73		543	1036	34.39	65.61
7	13	9	2	17	1579	9.23	74		586	993	37.11	62.89
5	9	9	7	17	1577	9.22	75		820	757	52	48
5	20	9	4	18	1577	9.22	76		577	1000	36.59	63.41
9	25	9	6	16	1577	9.22	77		631	946	40.01	59.99
5	16	9	7	14	1576	9.21	78		729	847	46.26	53.74
8	1	9	7	14	1575	9.2	79		689	886	43.75	56.25
9	30	9	4	17	1575	9.2	80		585	990	37.14	62.86
7	31	9	6	18	1574	9.2	81	17113	598	976	37.99	62.01
10	2	9	6	16	1574	9.2	82		643	931	40.85	59.15
5	15	9	6	18	1573	9.19	83		654	919	41.58	58.42
2	6	9	6	17	1572	9.19	84		568	1004	36.13	63.87
3	20	9	6	16	1572	9.19	85		610	962	38.8	61.2
5	18	9	2	17	1572	9.19	86		557	1015	35.43	64.57
5	21	9	5	16	1572	9.19	87		622	950	39.57	60.43
8	25	9	3	17	1572	9.19	88		588	984	37.4	62.6
4	17	9	6	16	1571	9.18	89		599	972	38.13	61.87
9	11	9	6	16	1571	9.18	90		684	887	43.54	56.46
7	14	9	3	17	1570	9.17	91		554	1016	35.29	64.71
1	16	9	6	16	1568	9.16	92		635	933	40.5	59.5
9	18	9	6	16	1568	9.16	93		651	917	41.52	58.48
5	29	9	6	15	1567	9.16	94		641	926	40.91	59.09
9	24	9	5	17	1567	9.16	95		609	958	38.86	61.14
10	9	9	6	18	1565	9.15	96		607	958	38.79	61.21
11	4	9	4	17	1565	9.15	97		581	984	37.12	62.88
11	6	9	6	17	1565	9.15	98		650	915	41.53	58.47
2	27	9	6	17	1562	9.13	99		569	993	36.43	63.57
4	7	9	3	17	1562	9.13	100		580	982	37.13	62.87
4	15	9	4	17	1562	9.13	101	17113	553	1009	35.4	64.6
6	10	9	4	17	1560	9.12	102		598	962	38.33	61.67
8	19	9	4	17	1559	9.11	103		594	965	38.1	61.9
4	20	9	2	17	1558	9.1	104		565	993	36.26	63.74
8	28	9	6	18	1558	9.1	105		556	1002	35.69	64.31
8	5	9	4	17	1557	9.1	106		581	976	37.32	62.68
3	27	9	6	17	1556	9.09	107		518	1038	33.29	66.71
5	24	9	1	13	1556	9.09	108		674	882	43.32	56.68
7	11	9	7	12	1556	9.09	109		665	891	42.74	57.26
5	11	9	2	17	1555	9.09	110		548	1007	35.24	64.76
8	6	9	5	17	1555	9.09	111		557	998	35.82	64.18
7	26	9	1	12	1554	9.08	112		759	795	48.84	51.16
8	27	9	5	18	1554	9.08	113		604	950	38.87	61.13
7	17	9	6	17	1553	9.07	114		575	978	37.03	62.97
9	23	9	4	17	1553	9.07	115		610	943	39.28	60.72
10	1	9	5	17	1553	9.07	116		569	984	36.64	63.36
2	13	9	6	16	1552	9.07	117		583	969	37.56	62.44
5	25	9	2	16	1549	9.05	118		1076	473	69.46	30.54
10	6	9	3	17	1549	9.05	119		619	930	39.96	60.04
10	8	9	5	17	1549	9.05	120		592	957	38.22	61.78
10	19	9	2	17	1549	9.05	121	17113	551	998	35.57	64.43

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
4	3	9	6	17	1548	9.05	122		577	971	37.27	62.73
5	10	9	1	13	1547	9.04	123		770	777	49.77	50.23
7	25	9	7	13	1547	9.04	124		621	926	40.14	59.86
7	24	9	6	15	1546	9.03	125		665	881	43.01	56.99
8	21	9	6	18	1546	9.03	126		578	968	37.39	62.61
5	13	9	4	17	1545	9.03	127		536	1009	34.69	65.31
8	14	9	6	15	1544	9.02	128		642	902	41.58	58.42
6	12	9	6	18	1543	9.02	129		648	895	42	58
8	17	9	2	17	1543	9.02	130		566	977	36.68	63.32
8	1	9	7	12	1542	9.01	131		724	818	46.95	53.05
5	14	9	5	16	1541	9	132		570	971	36.99	63.01
1	23	9	6	17	1540	9	133		535	1005	34.74	65.26
2	20	9	6	17	1540	9	134		573	967	37.21	62.79
9	3	9	5	17	1539	8.99	135		551	988	35.8	64.2
5	9	9	7	12	1538	8.99	136		713	825	46.36	53.64
11	24	9	3	17	1538	8.99	137		547	991	35.57	64.43
8	2	9	1	13	1536	8.98	138		749	787	48.76	51.24
8	27	9	5	17	1536	8.98	139		557	979	36.26	63.74
8	28	9	6	15	1536	8.98	140		639	897	41.6	58.4
5	27	9	4	18	1535	8.97	141	17113	607	928	39.54	60.46
6	9	9	3	18	1535	8.97	142		578	957	37.65	62.35
9	28	9	2	17	1534	8.96	143		550	984	35.85	64.15
7	11	9	7	14	1533	8.96	144		674	859	43.97	56.03
8	4	9	3	17	1533	8.96	145		548	985	35.75	64.25
8	15	9	7	12	1532	8.95	146		747	785	48.76	51.24
10	2	9	6	18	1532	8.95	147		593	939	38.71	61.29
10	22	9	5	17	1532	8.95	148		588	944	38.38	61.62
11	13	9	6	17	1532	8.95	149		603	929	39.36	60.64
1	30	9	6	17	1531	8.95	150		530	1001	34.62	65.38
6	2	9	3	17	1531	8.95	151		578	953	37.75	62.25
4	3	9	6	16	1530	8.94	152		563	967	36.8	63.2
5	28	9	5	16	1530	8.94	153		648	882	42.35	57.65
7	26	9	1	14	1530	8.94	154		759	771	49.61	50.39
9	18	9	6	17	1529	8.93	155		609	920	39.83	60.17
10	14	9	4	17	1529	8.93	156		595	934	38.91	61.09
3	20	9	6	17	1528	8.93	157		582	946	38.09	61.91
11	20	9	6	17	1528	8.93	158		567	961	37.11	62.89
3	13	9	6	16	1527	8.92	159		610	917	39.95	60.05
7	18	9	7	13	1527	8.92	160		660	867	43.22	56.78
7	24	9	6	14	1527	8.92	161	17113	676	851	44.27	55.73
2	5	9	5	17	1526	8.92	162		517	1009	33.88	66.12
10	15	9	5	17	1526	8.92	163		623	903	40.83	59.17
8	13	9	5	17	1525	8.91	164		556	969	36.46	63.54
9	10	9	5	17	1525	8.91	165		592	933	38.82	61.18
5	25	9	2	12	1524	8.91	166		890	634	58.4	41.6
8	20	9	5	18	1524	8.91	167		589	935	38.65	61.35
8	23	9	1	13	1524	8.91	168		860	664	56.43	43.57
5	14	9	5	18	1523	8.9	169		588	935	38.61	61.39
5	24	9	1	14	1523	8.9	170		684	839	44.91	55.09
9	4	9	6	15	1523	8.9	171		618	905	40.58	59.42
8	3	9	2	17	1522	8.89	172		574	948	37.71	62.29
5	16	9	7	15	1521	8.89	173		699	822	45.96	54.04

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
5	26	9	3	17	1521	8.89	174		615	906	40.43	59.57
7	26	9	1	13	1521	8.89	175		666	855	43.79	56.21
8	2	9	1	14	1521	8.89	176		754	767	49.57	50.43
9	8	9	3	17	1521	8.89	177		567	954	37.28	62.72
5	13	9	4	18	1520	8.88	178		535	985	35.2	64.8
7	23	9	5	17	1520	8.88	179		525	995	34.54	65.46
11	25	9	4	17	1520	8.88	180		538	982	35.39	64.61
5	16	9	7	16	1519	8.88	181	17113	751	768	49.44	50.56
7	10	9	6	15	1519	8.88	182		630	889	41.47	58.53
6	13	9	7	13	1518	8.87	183		707	811	46.57	53.43
1	9	9	6	16	1516	8.86	184		566	950	37.34	62.66
7	25	9	7	12	1516	8.86	185		623	893	41.09	58.91
5	28	9	5	18	1515	8.85	186		614	901	40.53	59.47
7	17	9	6	15	1515	8.85	187		624	891	41.19	58.81
7	22	9	4	17	1515	8.85	188		556	959	36.7	63.3
9	9	9	4	17	1515	8.85	189		544	971	35.91	64.09
10	29	9	5	17	1515	8.85	190		547	968	36.11	63.89
5	20	9	4	16	1514	8.85	191		587	927	38.77	61.23
3	6	9	6	16	1513	8.84	192		594	919	39.26	60.74
7	23	9	5	18	1513	8.84	193		551	962	36.42	63.58

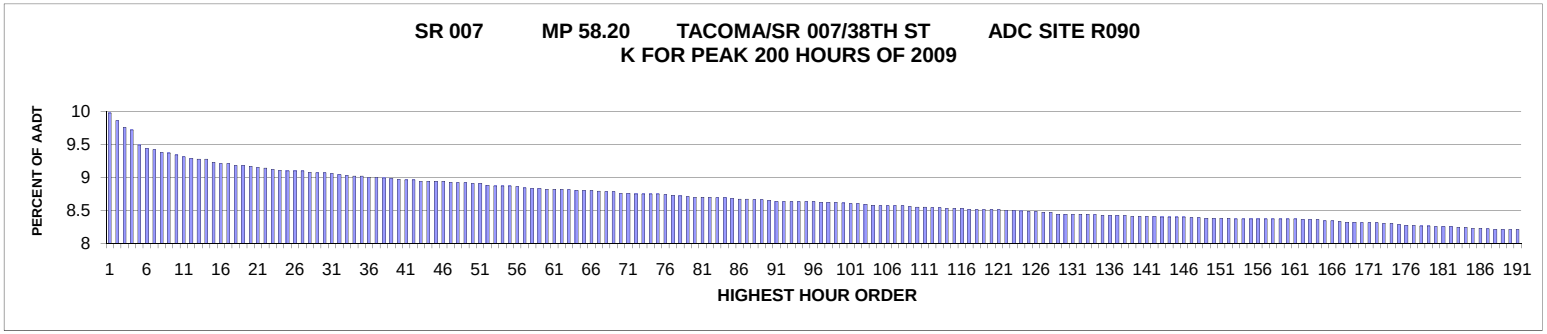

AADT= 23105 K 30 FACTOR= 9.15 K 100 FACTOR= 8.63 K 200 FACTOR= 8.21 D FACTOR= 61.91

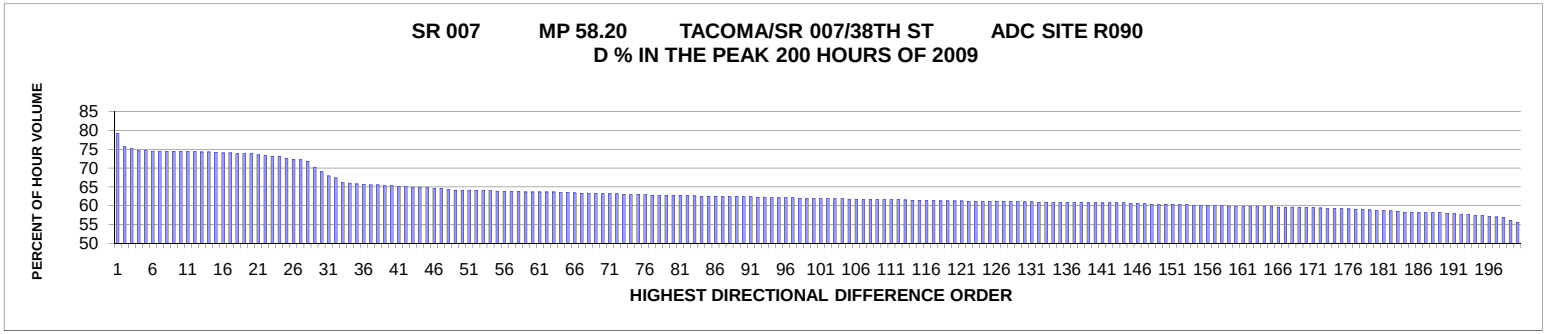

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
1	5	9	2	8	2306	9.98	1	23105	1717	589	74.46	25.54
2	20	9	6	17	2278	9.86	2		848	1430	37.23	62.77
2	27	9	6	17	2256	9.76	3		767	1489	34	66
11	6	9	6	17	2245	9.72	4		795	1450	35.41	64.59
1	9	9	6	17	2192	9.49	5		868	1324	39.6	60.4
2	26	9	5	17	2181	9.44	6		784	1397	35.95	64.05
1	16	9	6	17	2176	9.42	7		777	1399	35.71	64.29
10	22	9	5	18	2168	9.38	8		796	1372	36.72	63.28
10	16	9	6	17	2164	9.37	9		870	1294	40.2	59.8
2	20	9	6	18	2157	9.34	10		786	1371	36.44	63.56
1	5	9	2	17	2152	9.31	11		836	1316	38.85	61.15
11	24	9	3	17	2146	9.29	12		854	1292	39.79	60.21
11	6	9	6	16	2145	9.28	13		854	1291	39.81	60.19
2	12	9	5	17	2144	9.28	14		782	1362	36.47	63.53
1	30	9	6	17	2132	9.23	15		854	1278	40.06	59.94
10	20	9	3	18	2128	9.21	16		738	1390	34.68	65.32
10	22	9	5	17	2127	9.21	17		806	1321	37.89	62.11

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
2	12	9	5	18	2120	9.18	18		771	1349	36.37	63.63
12	8	9	3	17	2120	9.18	19		820	1300	38.68	61.32
10	23	9	6	17	2119	9.17	20		825	1294	38.93	61.07
2	18	9	4	18	2113	9.15	21	23105	747	1366	35.35	64.65
12	3	9	5	17	2112	9.14	22		793	1319	37.55	62.45
12	10	9	5	18	2107	9.12	23		791	1316	37.54	62.46
12	11	9	6	17	2105	9.11	24		807	1298	38.34	61.66
10	14	9	4	18	2103	9.1	25		788	1315	37.47	62.53
12	9	9	4	16	2103	9.1	26		907	1196	43.13	56.87
10	27	9	3	18	2102	9.1	27		762	1340	36.25	63.75
11	3	9	3	17	2098	9.08	28		829	1269	39.51	60.49
2	24	9	3	18	2095	9.07	29		813	1282	38.81	61.19
10	15	9	5	18	2095	9.07	30		763	1332	36.42	63.58
10	28	9	4	18	2094	9.06	31		776	1318	37.06	62.94
10	14	9	4	17	2089	9.04	32		801	1288	38.34	61.66
12	2	9	4	17	2087	9.03	33		846	1241	40.54	59.46
2	25	9	4	17	2083	9.02	34		838	1245	40.23	59.77
12	8	9	3	18	2083	9.02	35		853	1230	40.95	59.05
2	24	9	3	17	2080	9	36		790	1290	37.98	62.02
2	11	9	4	18	2079	9	37		766	1313	36.84	63.16
11	24	9	3	18	2077	8.99	38		787	1290	37.89	62.11
1	6	9	3	17	2074	8.98	39		757	1317	36.5	63.5
1	16	9	6	18	2072	8.97	40		772	1300	37.26	62.74
2	26	9	5	18	2071	8.96	41	23105	754	1317	36.41	63.59
11	17	9	3	17	2070	8.96	42		809	1261	39.08	60.92
2	23	9	2	17	2066	8.94	43		725	1341	35.09	64.91
1	15	9	5	17	2065	8.94	44		798	1267	38.64	61.36
1	22	9	5	18	2065	8.94	45		741	1324	35.88	64.12
2	19	9	5	17	2065	8.94	46		804	1261	38.93	61.07
2	11	9	4	17	2064	8.93	47		794	1270	38.47	61.53
2	18	9	4	17	2061	8.92	48		827	1234	40.13	59.87
11	2	9	2	17	2060	8.92	49		807	1253	39.17	60.83
1	22	9	5	17	2059	8.91	50		749	1310	36.38	63.62
10	20	9	3	17	2059	8.91	51		809	1250	39.29	60.71
10	21	9	4	17	2051	8.88	52		860	1191	41.93	58.07
11	3	9	3	18	2050	8.87	53		792	1258	38.63	61.37
10	2	9	6	18	2049	8.87	54		772	1277	37.68	62.32
12	11	9	6	16	2049	8.87	55		857	1192	41.83	58.17
10	29	9	5	18	2046	8.86	56		765	1281	37.39	62.61
12	16	9	4	18	2042	8.84	57		717	1325	35.11	64.89
11	24	9	3	16	2041	8.83	58		879	1162	43.07	56.93
10	30	9	6	17	2040	8.83	59		833	1207	40.83	59.17
2	19	9	5	18	2038	8.82	60		790	1248	38.76	61.24
2	27	9	6	16	2038	8.82	61	23105	832	1206	40.82	59.18
11	18	9	4	17	2038	8.82	62		802	1236	39.35	60.65
10	28	9	4	17	2035	8.81	63		800	1235	39.31	60.69
1	6	9	3	8	2033	8.8	64		1500	533	73.78	26.22
2	27	9	6	18	2033	8.8	65		730	1303	35.91	64.09
12	9	9	4	17	2033	8.8	66		753	1280	37.04	62.96
11	4	9	4	18	2032	8.79	67		774	1258	38.09	61.91
10	2	9	6	17	2029	8.78	68		819	1210	40.36	59.64
1	12	9	2	18	2028	8.78	69		689	1339	33.97	66.03

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
10	15	9	5	17	2025	8.76	70		810	1215	40	60
1	13	9	3	18	2024	8.76	71		696	1328	34.39	65.61
11	19	9	5	18	2022	8.75	72		710	1312	35.11	64.89
12	10	9	5	17	2022	8.75	73		793	1229	39.22	60.78
10	23	9	6	18	2021	8.75	74		819	1202	40.52	59.48
12	3	9	5	18	2021	8.75	75		693	1328	34.29	65.71
11	4	9	4	17	2020	8.74	76		773	1247	38.27	61.73
2	20	9	6	16	2016	8.73	77		837	1179	41.52	58.48
1	5	9	2	18	2015	8.72	78		658	1357	32.66	67.34
10	13	9	3	17	2012	8.71	79		798	1214	39.66	60.34
1	9	9	6	18	2011	8.7	80		725	1286	36.05	63.95
2	27	9	6	8	2011	8.7	81	23105	1412	599	70.21	29.79
1	16	9	6	16	2009	8.7	82		810	1199	40.32	59.68
10	21	9	4	18	2008	8.69	83		753	1255	37.5	62.5
11	6	9	6	18	2007	8.69	84		702	1305	34.98	65.02
1	12	9	2	17	2005	8.68	85		788	1217	39.3	60.7
1	21	9	4	17	2004	8.67	86		815	1189	40.67	59.33
12	9	9	4	18	2004	8.67	87		695	1309	34.68	65.32
10	19	9	2	17	2002	8.66	88		753	1249	37.61	62.39
1	30	9	6	18	2001	8.66	89		724	1277	36.18	63.82
2	17	9	3	17	1999	8.65	90		777	1222	38.87	61.13
1	7	9	4	17	1995	8.63	91		743	1252	37.24	62.76
1	29	9	5	18	1995	8.63	92		750	1245	37.59	62.41
11	5	9	5	18	1995	8.63	93		761	1234	38.15	61.85
11	17	9	3	18	1995	8.63	94		722	1273	36.19	63.81
1	23	9	6	17	1993	8.63	95		796	1197	39.94	60.06
12	16	9	4	17	1993	8.63	96		825	1168	41.39	58.61
1	13	9	3	17	1992	8.62	97		790	1202	39.66	60.34
10	16	9	6	18	1992	8.62	98		754	1238	37.85	62.15
1	20	9	3	17	1991	8.62	99		775	1216	38.93	61.07
10	27	9	3	17	1989	8.61	100		782	1207	39.32	60.68
12	2	9	4	18	1988	8.6	101	23105	693	1295	34.86	65.14
11	18	9	4	18	1987	8.6	102		760	1227	38.25	61.75
11	20	9	6	18	1985	8.59	103		749	1236	37.73	62.27
10	13	9	3	18	1983	8.58	104		770	1213	38.83	61.17
12	17	9	5	17	1981	8.57	105		831	1150	41.95	58.05
1	12	9	2	8	1980	8.57	106		1421	559	71.77	28.23
12	1	9	3	18	1980	8.57	107		711	1269	35.91	64.09
1	6	9	3	18	1979	8.57	108		613	1366	30.98	69.02
10	12	9	2	17	1978	8.56	109		776	1202	39.23	60.77
1	8	9	5	17	1976	8.55	110		765	1211	38.71	61.29
1	13	9	3	8	1975	8.55	111		1441	534	72.96	27.04
11	23	9	2	17	1974	8.54	112		797	1177	40.37	59.63
10	19	9	2	18	1973	8.54	113		681	1292	34.52	65.48
12	15	9	3	17	1971	8.53	114		750	1221	38.05	61.95
1	14	9	4	17	1970	8.53	115		794	1176	40.3	59.7
2	23	9	2	8	1970	8.53	116		1424	546	72.28	27.72
1	7	9	4	8	1967	8.51	117		1441	526	73.26	26.74
12	8	9	3	9	1967	8.51	118		1232	735	62.63	37.37
2	6	9	6	17	1966	8.51	119		813	1153	41.35	58.65
2	19	9	5	16	1966	8.51	120		834	1132	42.42	57.58
10	29	9	5	8	1966	8.51	121	23105	1445	521	73.5	26.5

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
1	14	9	4	18	1965	8.5	122		770	1195	39.19	60.81
2	13	9	6	17	1964	8.5	123		740	1224	37.68	62.32
1	29	9	5	17	1961	8.49	124		767	1194	39.11	60.89
12	23	9	4	17	1960	8.48	125		782	1178	39.9	60.1
11	3	9	3	8	1959	8.48	126		1455	504	74.27	25.73
2	25	9	4	8	1957	8.47	127		1412	545	72.15	27.85
11	5	9	5	8	1956	8.47	128		1444	512	73.82	26.18
12	11	9	6	18	1951	8.44	129		717	1234	36.75	63.25
2	23	9	2	18	1950	8.44	130		717	1233	36.77	63.23
11	19	9	5	17	1950	8.44	131		766	1184	39.28	60.72
12	8	9	3	16	1950	8.44	132		767	1183	39.33	60.67
2	5	9	5	18	1949	8.44	133		787	1162	40.38	59.62
1	12	9	2	16	1948	8.43	134		798	1150	40.97	59.03
12	17	9	5	18	1946	8.42	135		725	1221	37.26	62.74
2	24	9	3	8	1945	8.42	136		1461	484	75.12	24.88
11	4	9	4	16	1945	8.42	137		856	1089	44.01	55.99
11	19	9	5	8	1945	8.42	138		1421	524	73.06	26.94
11	18	9	4	8	1944	8.41	139		1447	497	74.43	25.57
10	27	9	3	16	1943	8.41	140		835	1108	42.97	57.03
11	17	9	3	8	1943	8.41	141	23105	1444	499	74.32	25.68
11	25	9	4	16	1943	8.41	142		719	1224	37	63
11	2	9	2	8	1941	8.4	143		1450	491	74.7	25.3
1	5	9	2	16	1940	8.4	144		741	1199	38.2	61.8
1	9	9	6	8	1940	8.4	145		1408	532	72.58	27.42
10	26	9	2	18	1940	8.4	146		703	1237	36.24	63.76
10	27	9	3	8	1938	8.39	147		1433	505	73.94	26.06
10	30	9	6	16	1938	8.39	148		826	1112	42.62	57.38
1	15	9	5	8	1937	8.38	149		1438	499	74.24	25.76
2	4	9	4	17	1937	8.38	150		814	1123	42.02	57.98
11	3	9	3	16	1937	8.38	151		810	1127	41.82	58.18
1	9	9	6	16	1936	8.38	152		738	1198	38.12	61.88
1	27	9	3	17	1935	8.37	153		780	1155	40.31	59.69
2	9	9	2	17	1935	8.37	154		824	1111	42.58	57.42
11	5	9	5	17	1935	8.37	155		778	1157	40.21	59.79
2	3	9	3	18	1934	8.37	156		744	1190	38.47	61.53
2	4	9	4	18	1934	8.37	157		723	1211	37.38	62.62
10	26	9	2	17	1934	8.37	158		750	1184	38.78	61.22
10	29	9	5	17	1934	8.37	159		793	1141	41	59
2	18	9	4	8	1933	8.37	160		1462	471	75.63	24.37
12	15	9	3	18	1933	8.37	161	23105	693	1240	35.85	64.15
11	2	9	2	18	1931	8.36	162		742	1189	38.43	61.57
11	4	9	4	8	1931	8.36	163		1436	495	74.37	25.63
12	22	9	3	17	1931	8.36	164		736	1195	38.11	61.89
12	1	9	3	17	1927	8.34	165		797	1130	41.36	58.64
1	5	9	2	9	1926	8.34	166		1307	619	67.86	32.14
1	29	9	5	16	1925	8.33	167		808	1117	41.97	58.03
10	14	9	4	8	1923	8.32	168		1432	491	74.47	25.53
10	22	9	5	8	1923	8.32	169		1429	494	74.31	25.69
10	2	9	6	16	1920	8.31	170		852	1068	44.38	55.63
11	20	9	6	17	1920	8.31	171		746	1174	38.85	61.15
2	25	9	4	18	1919	8.31	172		663	1256	34.55	65.45
1	27	9	3	18	1918	8.3	173		751	1167	39.16	60.84

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
11	18	9	4	16	1918	8.3	174		766	1152	39.94	60.06
1	21	9	4	18	1912	8.28	175		735	1177	38.44	61.56
2	5	9	5	17	1911	8.27	176		801	1110	41.92	58.08
1	8	9	5	18	1910	8.27	177		705	1205	36.91	63.09
2	6	9	6	18	1908	8.26	178		724	1184	37.95	62.05
2	17	9	3	18	1908	8.26	179		702	1206	36.79	63.21
1	6	9	3	16	1907	8.25	180		724	1183	37.97	62.03
1	15	9	5	18	1906	8.25	181	23105	747	1159	39.19	60.81
10	13	9	3	8	1906	8.25	182		1407	499	73.82	26.18
12	2	9	4	8	1905	8.24	183		1409	496	73.96	26.04
1	22	9	5	16	1904	8.24	184		754	1150	39.6	60.4
10	21	9	4	8	1902	8.23	185		1415	487	74.4	25.6
12	7	9	2	17	1902	8.23	186		706	1196	37.12	62.88
10	29	9	5	16	1899	8.22	187		806	1093	42.44	57.56
12	4	9	6	17	1897	8.21	188		737	1160	38.85	61.15
11	30	9	2	17	1896	8.21	189		736	1160	38.82	61.18
12	18	9	6	17	1896	8.21	190		748	1148	39.45	60.55
12	22	9	3	18	1896	8.21	191		730	1166	38.5	61.5
1	29	9	5	8	1895	8.2	192		1501	394	79.21	20.79

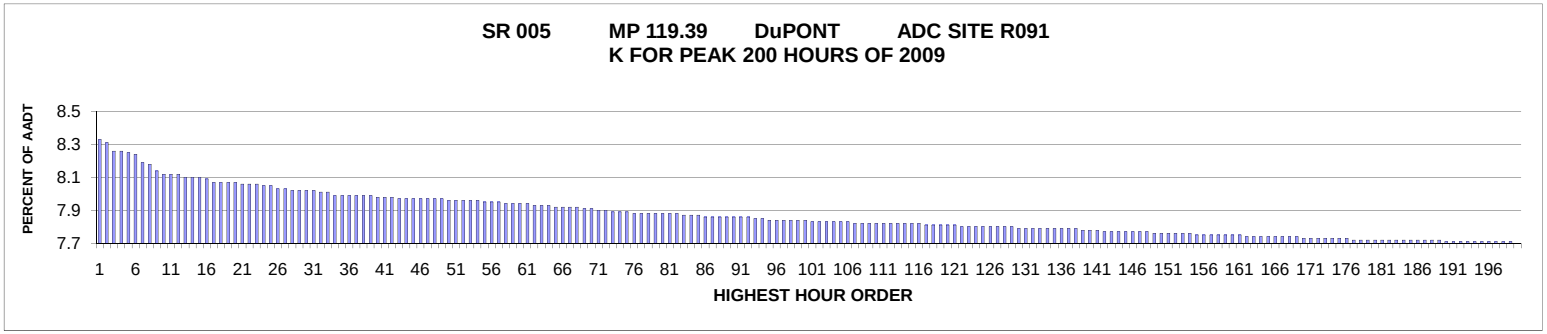

AADT= 118013 **K 30 FACTOR=** 8.02 **K 100 FACTOR=** 7.84 **K 200 FACTOR=** 7.7 **D FACTOR=** 54.49

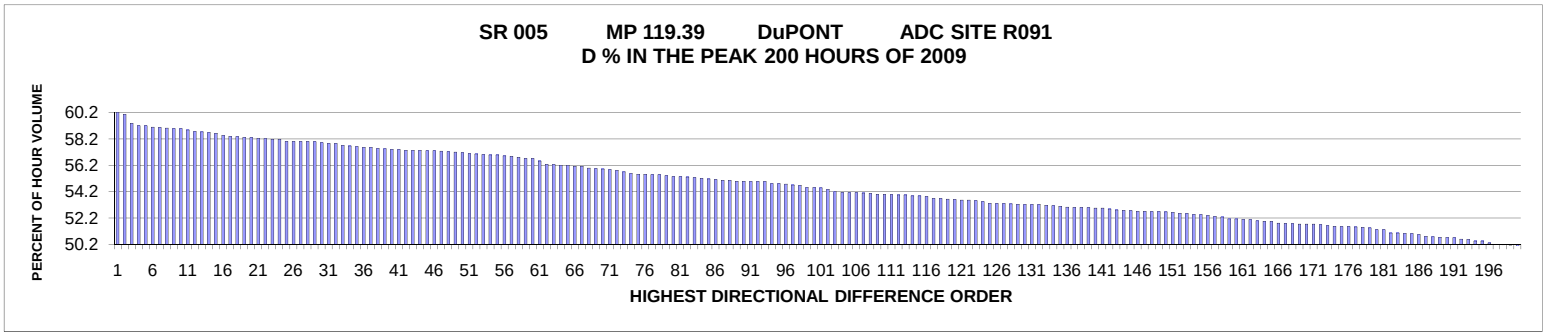

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	16	9	1	14	9829	8.33	1	118013	5060	4769	51.48	48.52
11	25	9	4	14	9812	8.31	2		4590	5222	46.78	53.22
10	9	9	6	16	9747	8.26	3		4474	5273	45.9	54.1
3	27	9	6	15	9746	8.26	4		4501	5245	46.18	53.82
3	19	9	5	17	9732	8.25	5		4145	5587	42.59	57.41
9	18	9	6	15	9721	8.24	6		4624	5097	47.57	52.43
8	23	9	1	14	9664	8.19	7		5089	4575	52.66	47.34
9	4	9	6	15	9658	8.18	8		4516	5142	46.76	53.24
8	13	9	5	16	9602	8.14	9		4513	5089	47	53
8	14	9	6	15	9588	8.12	10		4823	4765	50.3	49.7
8	8	9	7	12	9586	8.12	11		4446	5140	46.38	53.62
11	25	9	4	13	9578	8.12	12		4342	5236	45.33	54.67
6	5	9	6	15	9563	8.1	13		4494	5069	46.99	53.01
7	23	9	5	16	9560	8.1	14		4361	5199	45.62	54.38
8	15	9	7	13	9554	8.1	15		4844	4710	50.7	49.3
8	22	9	7	12	9549	8.09	16		4554	4995	47.69	52.31
6	21	9	1	14	9524	8.07	17		4911	4613	51.56	48.44

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
5	7	9	5	17	9523	8.07	18		3902	5621	40.97	59.03
3	27	9	6	16	9520	8.07	19		4089	5431	42.95	57.05
2	13	9	6	16	9519	8.07	20		4421	5098	46.44	53.56
5	8	9	6	15	9516	8.06	21	118013	4333	5183	45.53	54.47
4	2	9	5	17	9511	8.06	22		4099	5412	43.1	56.9
4	30	9	5	17	9506	8.06	23		3973	5533	41.79	58.21
6	26	9	6	13	9503	8.05	24		4456	5047	46.89	53.11
8	15	9	7	12	9502	8.05	25		4580	4922	48.2	51.8
12	18	9	6	16	9481	8.03	26		4270	5211	45.04	54.96
10	30	9	6	16	9477	8.03	27		4158	5319	43.87	56.13
12	23	9	4	15	9470	8.02	28		4478	4992	47.29	52.71
1	22	9	5	17	9466	8.02	29		3916	5550	41.37	58.63
3	6	9	6	16	9465	8.02	30		4167	5298	44.03	55.97
7	26	9	1	13	9463	8.02	31		4926	4537	52.06	47.94
8	11	9	3	17	9451	8.01	32		4046	5405	42.81	57.19
12	24	9	5	14	9447	8.01	33		4446	5001	47.06	52.94
8	14	9	6	14	9432	7.99	34		4640	4792	49.19	50.81
8	14	9	6	13	9431	7.99	35		4595	4836	48.72	51.28
8	16	9	1	13	9429	7.99	36		4858	4571	51.52	48.48
8	16	9	1	15	9427	7.99	37		4859	4568	51.54	48.46
4	10	9	6	16	9426	7.99	38		4270	5156	45.3	54.7
6	11	9	5	16	9424	7.99	39		4177	5247	44.32	55.68
8	7	9	6	14	9419	7.98	40		4765	4654	50.59	49.41
9	18	9	6	16	9416	7.98	41	118013	4320	5096	45.88	54.12
5	17	9	1	18	9414	7.98	42		4608	4806	48.95	51.05
9	3	9	5	16	9408	7.97	43		4154	5254	44.15	55.85
8	25	9	3	17	9407	7.97	44		3978	5429	42.29	57.71
2	17	9	3	17	9406	7.97	45		3927	5479	41.75	58.25
8	23	9	1	13	9406	7.97	46		4965	4441	52.79	47.21
8	17	9	2	16	9403	7.97	47		4279	5124	45.51	54.49
8	22	9	7	14	9402	7.97	48		4649	4753	49.45	50.55
6	12	9	6	15	9400	7.97	49		4488	4912	47.74	52.26
8	5	9	4	16	9395	7.96	50		4436	4959	47.22	52.78
12	18	9	6	15	9395	7.96	51		4197	5198	44.67	55.33
6	26	9	6	15	9390	7.96	52		4536	4854	48.31	51.69
6	25	9	5	16	9388	7.96	53		4215	5173	44.9	55.1
7	24	9	6	12	9388	7.96	54		4170	5218	44.42	55.58
10	8	9	5	17	9385	7.95	55		3951	5434	42.1	57.9
12	11	9	6	15	9385	7.95	56		4595	4790	48.96	51.04
7	10	9	6	14	9380	7.95	57		4556	4824	48.57	51.43
7	15	9	4	17	9374	7.94	58		3936	5438	41.99	58.01
1	16	9	6	16	9371	7.94	59		4237	5134	45.21	54.79
1	23	9	6	16	9366	7.94	60		4128	5238	44.07	55.93
9	24	9	5	17	9365	7.94	61	118013	4001	5364	42.72	57.28
8	7	9	6	13	9361	7.93	62		4514	4847	48.22	51.78
12	3	9	5	17	9359	7.93	63		3839	5520	41.02	58.98
6	29	9	2	17	9357	7.93	64		3915	5442	41.84	58.16
10	9	9	6	15	9352	7.92	65		4344	5008	46.45	53.55
8	12	9	4	16	9349	7.92	66		4202	5147	44.95	55.05
2	13	9	6	15	9346	7.92	67		4225	5121	45.21	54.79
6	24	9	4	17	9342	7.92	68		4161	5181	44.54	55.46
4	29	9	4	17	9336	7.91	69		3920	5416	41.99	58.01

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	12	9	4	17	9331	7.91	70		3920	5411	42.01	57.99
3	30	9	2	17	9327	7.9	71		3846	5481	41.24	58.76
3	26	9	5	17	9318	7.9	72		4052	5266	43.49	56.51
9	4	9	6	13	9316	7.89	73		4290	5026	46.05	53.95
9	17	9	5	16	9316	7.89	74		4149	5167	44.54	55.46
5	18	9	2	17	9306	7.89	75		3807	5499	40.91	59.09
12	26	9	7	13	9305	7.88	76		4400	4905	47.29	52.71
4	1	9	4	17	9304	7.88	77		3986	5318	42.84	57.16
8	22	9	7	13	9302	7.88	78		4422	4880	47.54	52.46
8	13	9	5	15	9299	7.88	79		4468	4831	48.05	51.95
9	4	9	6	14	9299	7.88	80		4363	4936	46.92	53.08
4	15	9	4	17	9295	7.88	81	118013	3957	5338	42.57	57.43
12	26	9	7	14	9294	7.88	82		4450	4844	47.88	52.12
9	11	9	6	16	9292	7.87	83		4262	5030	45.87	54.13
5	12	9	3	17	9284	7.87	84		3790	5494	40.82	59.18
8	6	9	5	16	9282	7.87	85		4180	5102	45.03	54.97
3	13	9	6	15	9280	7.86	86		4322	4958	46.57	53.43
3	18	9	4	17	9280	7.86	87		3872	5408	41.72	58.28
4	16	9	5	17	9280	7.86	88		3934	5346	42.39	57.61
9	8	9	3	17	9280	7.86	89		3900	5380	42.03	57.97
5	10	9	1	16	9276	7.86	90		4940	4336	53.26	46.74
8	4	9	3	17	9270	7.86	91		3949	5321	42.6	57.4
8	28	9	6	15	9270	7.86	92		4571	4699	49.31	50.69
7	1	9	4	16	9266	7.85	93		3957	5309	42.7	57.3
7	13	9	2	17	9259	7.85	94		4007	5252	43.28	56.72
7	10	9	6	13	9255	7.84	95		4558	4697	49.25	50.75
7	2	9	5	13	9254	7.84	96		4250	5004	45.93	54.07
6	12	9	6	14	9252	7.84	97		4360	4892	47.12	52.88
5	15	9	6	15	9251	7.84	98		4483	4768	48.46	51.54
2	16	9	2	16	9249	7.84	99		4643	4606	50.2	49.8
5	29	9	6	15	9247	7.84	100		4182	5065	45.23	54.77
6	18	9	5	16	9246	7.83	101	118013	4162	5084	45.01	54.99
3	11	9	4	17	9244	7.83	102		3974	5270	42.99	57.01
8	14	9	6	12	9237	7.83	103		4203	5034	45.5	54.5
5	1	9	6	15	9236	7.83	104		4458	4778	48.27	51.73
6	21	9	1	13	9236	7.83	105		4658	4578	50.43	49.57
6	21	9	1	15	9235	7.83	106		4914	4321	53.21	46.79
3	13	9	6	16	9234	7.82	107		4137	5097	44.8	55.2
4	3	9	6	15	9234	7.82	108		4293	4941	46.49	53.51
5	8	9	6	16	9231	7.82	109		4050	5181	43.87	56.13
3	6	9	6	15	9230	7.82	110		4247	4983	46.01	53.99
10	8	9	5	16	9229	7.82	111		3970	5259	43.02	56.98
1	21	9	4	17	9228	7.82	112		3776	5452	40.92	59.08
8	28	9	6	14	9228	7.82	113		4433	4795	48.04	51.96
6	2	9	3	17	9227	7.82	114		3841	5386	41.63	58.37
9	9	9	4	17	9225	7.82	115		3794	5431	41.13	58.87
9	18	9	6	14	9225	7.82	116		4377	4848	47.45	52.55
5	5	9	3	17	9222	7.81	117		3683	5539	39.94	60.06
8	21	9	6	13	9221	7.81	118		4463	4758	48.4	51.6
10	20	9	3	17	9219	7.81	119		3805	5414	41.27	58.73
10	22	9	5	17	9212	7.81	120		3840	5372	41.68	58.32
10	29	9	5	17	9212	7.81	121	118013	3929	5283	42.65	57.35

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
6	24	9	4	16	9208	7.8	122		4121	5087	44.75	55.25
8	24	9	2	16	9208	7.8	123		4218	4990	45.81	54.19
7	9	9	5	16	9204	7.8	124		4263	4941	46.32	53.68
5	22	9	6	15	9203	7.8	125		4510	4693	49.01	50.99
2	13	9	6	17	9202	7.8	126		4126	5076	44.84	55.16
4	7	9	3	17	9202	7.8	127		3896	5306	42.34	57.66
3	25	9	4	17	9201	7.8	128		3877	5324	42.14	57.86
7	24	9	6	14	9201	7.8	129		4368	4833	47.47	52.53
8	2	9	1	14	9197	7.79	130		4889	4308	53.16	46.84
8	10	9	2	17	9196	7.79	131		4029	5167	43.81	56.19
4	17	9	6	15	9195	7.79	132		4294	4901	46.7	53.3
4	8	9	4	17	9194	7.79	133		3911	5283	42.54	57.46
3	29	9	1	16	9192	7.79	134		4972	4220	54.09	45.91
8	15	9	7	16	9191	7.79	135		4775	4416	51.95	48.05
7	2	9	5	14	9190	7.79	136		4257	4933	46.32	53.68
9	25	9	6	15	9190	7.79	137		4140	5050	45.05	54.95
9	24	9	5	16	9188	7.79	138		4104	5084	44.67	55.33
9	13	9	1	18	9183	7.78	139		4318	4865	47.02	52.98
7	17	9	6	15	9182	7.78	140		4602	4580	50.12	49.88
4	21	9	3	17	9176	7.78	141	118013	3745	5431	40.81	59.19
6	23	9	3	17	9175	7.77	142		3957	5218	43.13	56.87
9	29	9	3	17	9173	7.77	143		3726	5447	40.62	59.38
9	11	9	6	15	9170	7.77	144		4256	4914	46.41	53.59
2	27	9	6	16	9169	7.77	145		4098	5071	44.69	55.31
4	22	9	4	17	9165	7.77	146		3833	5332	41.82	58.18
6	8	9	2	17	9165	7.77	147		3813	5352	41.6	58.4
9	22	9	3	17	9165	7.77	148		3889	5276	42.43	57.57
8	1	9	7	12	9161	7.76	149		4576	4585	49.95	50.05
9	1	9	3	17	9161	7.76	150		3889	5272	42.45	57.55
9	30	9	4	17	9161	7.76	151		3805	5356	41.53	58.47
6	26	9	6	14	9160	7.76	152		4361	4799	47.61	52.39
3	24	9	3	17	9155	7.76	153		3858	5297	42.14	57.86
11	5	9	5	17	9153	7.76	154		3783	5370	41.33	58.67
2	20	9	6	16	9151	7.75	155		3961	5190	43.28	56.72
8	18	9	3	17	9151	7.75	156		3916	5235	42.79	57.21
7	11	9	7	12	9150	7.75	157		4280	4870	46.78	53.22
8	30	9	1	14	9150	7.75	158		5031	4119	54.98	45.02
4	10	9	6	15	9147	7.75	159		4323	4824	47.26	52.74
7	11	9	7	13	9146	7.75	160		4333	4813	47.38	52.62
7	20	9	2	16	9144	7.75	161	118013	4078	5066	44.6	55.4
11	29	9	1	14	9140	7.74	162		4923	4217	53.86	46.14
7	24	9	6	13	9139	7.74	163		4410	4729	48.25	51.75
8	7	9	6	15	9139	7.74	164		4503	4636	49.27	50.73
9	21	9	2	17	9136	7.74	165		3902	5234	42.71	57.29
2	19	9	5	17	9135	7.74	166		4002	5133	43.81	56.19
10	15	9	5	17	9133	7.74	167		3895	5238	42.65	57.35
6	30	9	3	17	9132	7.74	168		3896	5236	42.66	57.34
8	10	9	2	16	9130	7.74	169		4212	4918	46.13	53.87
8	27	9	5	15	9126	7.73	170		4370	4756	47.89	52.11
6	19	9	6	15	9125	7.73	171		4479	4646	49.08	50.92
9	23	9	4	17	9120	7.73	172		3915	5205	42.93	57.07
4	27	9	2	17	9119	7.73	173		3741	5378	41.02	58.98

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
6	16	9	3	17	9118	7.73	174		3829	5289	41.99	58.01
4	16	9	5	16	9117	7.73	175		3987	5130	43.73	56.27
4	28	9	3	17	9117	7.73	176		3627	5490	39.78	60.22
4	9	9	5	16	9115	7.72	177		4193	4922	46	54
6	20	9	7	13	9115	7.72	178		4544	4571	49.85	50.15
8	9	9	1	14	9114	7.72	179		4516	4598	49.55	50.45
1	30	9	6	16	9113	7.72	180		3988	5125	43.76	56.24
2	20	9	6	15	9112	7.72	181	118013	4194	4918	46.03	53.97
6	17	9	4	17	9112	7.72	182		4053	5059	44.48	55.52
9	4	9	6	16	9112	7.72	183		4257	4855	46.72	53.28
6	12	9	6	13	9111	7.72	184		4311	4800	47.32	52.68
11	25	9	4	15	9111	7.72	185		4311	4800	47.32	52.68
4	17	9	6	16	9107	7.72	186		4094	5013	44.95	55.05
8	29	9	7	12	9107	7.72	187		4396	4711	48.27	51.73
5	20	9	4	8	9105	7.72	188		5189	3916	56.99	43.01
11	29	9	1	15	9105	7.72	189		4852	4253	53.29	46.71
6	20	9	7	12	9104	7.71	190		4361	4743	47.9	52.1
12	23	9	4	14	9104	7.71	191		4435	4669	48.71	51.29
4	10	9	6	17	9097	7.71	192		3930	5167	43.2	56.8
3	27	9	6	14	9095	7.71	193		4189	4906	46.06	53.94

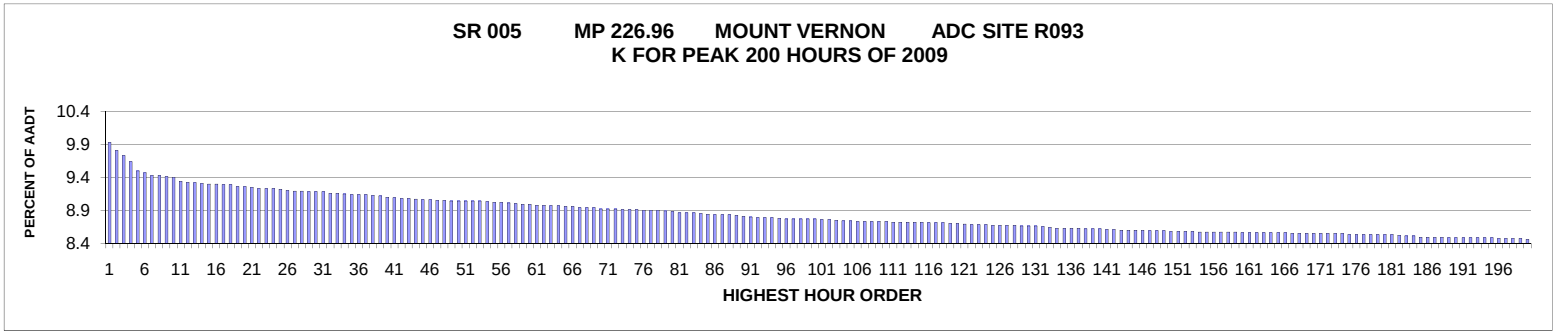

AADT= 66554 **K 30 FACTOR=** 9.18 **K 100 FACTOR=** 8.77 **K 200 FACTOR=** 8.46 **D FACTOR=** 51.91

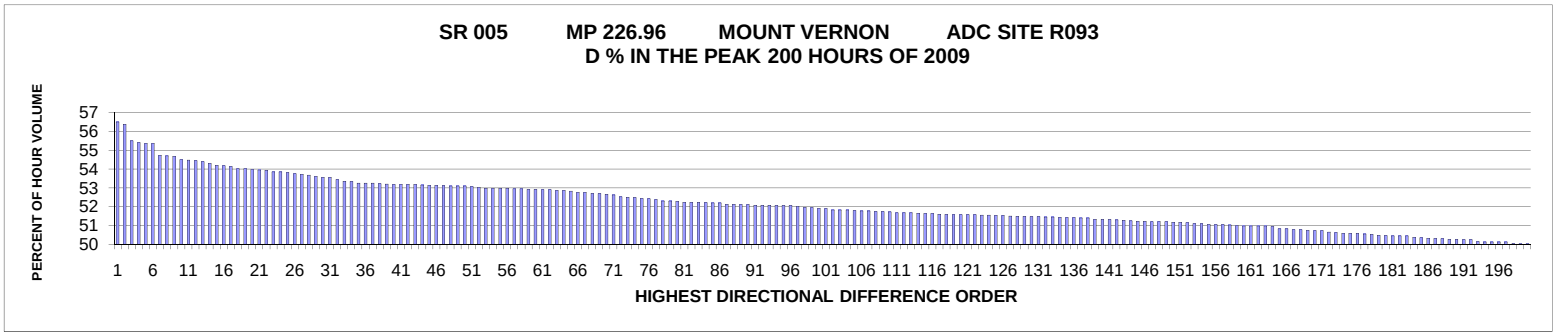

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	7	9	6	17	6606	9.93	1	66554	3427	3179	51.88	48.12
8	14	9	6	17	6529	9.81	2		3445	3084	52.76	47.24
8	14	9	6	16	6479	9.73	3		3232	3247	49.88	50.12
8	7	9	6	16	6416	9.64	4		3236	3180	50.44	49.56
8	14	9	6	15	6324	9.5	5		3227	3097	51.03	48.97
10	9	9	6	17	6303	9.47	6		3282	3021	52.07	47.93
8	14	9	6	18	6277	9.43	7		3199	3078	50.96	49.04
8	28	9	6	17	6277	9.43	8		3267	3010	52.05	47.95
7	24	9	6	17	6260	9.41	9		3465	2795	55.35	44.65
7	24	9	6	16	6259	9.4	10		3157	3102	50.44	49.56
8	21	9	6	16	6217	9.34	11		3199	3018	51.46	48.54
6	19	9	6	17	6212	9.33	12		3209	3003	51.66	48.34
11	25	9	4	14	6202	9.32	13		2904	3298	46.82	53.18
9	4	9	6	16	6196	9.31	14		3336	2860	53.84	46.16
10	2	9	6	17	6192	9.3	15		3081	3111	49.76	50.24
8	21	9	6	17	6188	9.3	16		3371	2817	54.48	45.52
8	28	9	6	16	6183	9.29	17		3173	3010	51.32	48.68

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
11	6	9	6	17	6180	9.29	18		3162	3018	51.17	48.83
8	7	9	6	14	6162	9.26	19		3259	2903	52.89	47.11
9	18	9	6	17	6161	9.26	20		3207	2954	52.05	47.95
10	9	9	6	18	6159	9.25	21	66554	3321	2838	53.92	46.08
10	9	9	6	16	6146	9.23	22		3170	2976	51.58	48.42
8	15	9	7	12	6145	9.23	23		3236	2909	52.66	47.34
7	31	9	6	16	6143	9.23	24		3071	3072	49.99	50.01
6	19	9	6	16	6137	9.22	25		3246	2891	52.89	47.11
11	13	9	6	17	6123	9.2	26		3188	2935	52.07	47.93
4	24	9	6	17	6119	9.19	27		3097	3022	50.61	49.39
8	15	9	7	13	6119	9.19	28		3052	3067	49.88	50.12
8	7	9	6	15	6109	9.18	29		3165	2944	51.81	48.19
8	14	9	6	14	6108	9.18	30		3206	2902	52.49	47.51
8	28	9	6	15	6108	9.18	31		3150	2958	51.57	48.43
11	29	9	1	16	6095	9.16	32		3280	2815	53.81	46.19
4	24	9	6	16	6094	9.16	33		3141	2953	51.54	48.46
9	25	9	6	16	6091	9.15	34		3179	2912	52.19	47.81
8	14	9	6	13	6084	9.14	35		3129	2955	51.43	48.57
8	1	9	7	12	6083	9.14	36		3129	2954	51.44	48.56
7	10	9	6	17	6081	9.14	37		3116	2965	51.24	48.76
9	25	9	6	17	6078	9.13	38		3148	2930	51.79	48.21
10	2	9	6	16	6067	9.12	39		3105	2962	51.18	48.82
8	21	9	6	18	6054	9.1	40		3200	2854	52.86	47.14
8	8	9	7	13	6053	9.09	41	66554	3127	2926	51.66	48.34
11	20	9	6	17	6045	9.08	42		3103	2942	51.33	48.67
8	22	9	7	12	6043	9.08	43		3224	2819	53.35	46.65
9	4	9	6	15	6037	9.07	44		3191	2846	52.86	47.14
7	24	9	6	15	6031	9.06	45		3023	3008	50.12	49.88
12	30	9	4	17	6030	9.06	46		3190	2840	52.9	47.1
11	25	9	4	15	6023	9.05	47		2940	3083	48.81	51.19
10	16	9	6	17	6020	9.05	48		3172	2848	52.69	47.31
11	29	9	1	17	6017	9.04	49		3215	2802	53.43	46.57
7	31	9	6	14	6015	9.04	50		3159	2856	52.52	47.48
8	21	9	6	15	6015	9.04	51		3135	2880	52.12	47.88
9	5	9	7	13	6015	9.04	52		3145	2870	52.29	47.71
9	5	9	7	12	6014	9.04	53		3189	2825	53.03	46.97
6	12	9	6	17	6009	9.03	54		2927	3082	48.71	51.29
8	28	9	6	18	6005	9.02	55		3194	2811	53.19	46.81
10	23	9	6	17	6000	9.02	56		2971	3029	49.52	50.48
2	20	9	6	17	5997	9.01	57		3136	2861	52.29	47.71
4	24	9	6	18	5993	9	58		3184	2809	53.13	46.87
9	18	9	6	16	5985	8.99	59		3086	2899	51.56	48.44
8	7	9	6	18	5984	8.99	60		3080	2904	51.47	48.53
8	7	9	6	13	5977	8.98	61	66554	3236	2741	54.14	45.86
8	15	9	7	14	5974	8.98	62		2942	3032	49.25	50.75
8	21	9	6	14	5973	8.97	63		3222	2751	53.94	46.06
7	24	9	6	18	5972	8.97	64		3201	2771	53.6	46.4
12	23	9	4	16	5966	8.96	65		3074	2892	51.53	48.47
2	13	9	6	17	5962	8.96	66		3040	2922	50.99	49.01
2	13	9	6	16	5952	8.94	67		3022	2930	50.77	49.23
7	31	9	6	17	5950	8.94	68		3042	2908	51.13	48.87
1	16	9	6	17	5947	8.94	69		3068	2879	51.59	48.41

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
4	26	9	1	17	5936	8.92	70		2911	3025	49.04	50.96
8	13	9	5	17	5935	8.92	71		3144	2791	52.97	47.03
8	16	9	1	14	5934	8.92	72		2911	3023	49.06	50.94
3	27	9	6	17	5931	8.91	73		3221	2710	54.31	45.69
6	26	9	6	17	5930	8.91	74		3080	2850	51.94	48.06
8	23	9	1	16	5928	8.91	75		2644	3284	44.6	55.4
9	11	9	6	17	5926	8.9	76		3095	2831	52.23	47.77
8	8	9	7	12	5921	8.9	77		3144	2777	53.1	46.9
7	31	9	6	15	5920	8.9	78		2977	2943	50.29	49.71
9	3	9	5	17	5914	8.89	79		3083	2831	52.13	47.87
7	17	9	6	17	5912	8.88	80		3047	2865	51.54	48.46
10	23	9	6	16	5898	8.86	81	66554	2931	2967	49.69	50.31
9	4	9	6	17	5897	8.86	82		3169	2728	53.74	46.26
2	13	9	6	18	5895	8.86	83		3123	2772	52.98	47.02
6	12	9	6	16	5893	8.85	84		2901	2992	49.23	50.77
7	5	9	1	15	5885	8.84	85		2567	3318	43.62	56.38
10	30	9	6	17	5877	8.83	86		3120	2757	53.09	46.91
8	23	9	1	15	5874	8.83	87		2752	3122	46.85	53.15
11	25	9	4	16	5874	8.83	88		3061	2813	52.11	47.89
12	11	9	6	17	5872	8.82	89		2998	2874	51.06	48.94
6	19	9	6	18	5863	8.81	90		3113	2750	53.1	46.9
7	17	9	6	18	5854	8.8	91		3115	2739	53.21	46.79
9	18	9	6	18	5852	8.79	92		3029	2823	51.76	48.24
9	25	9	6	18	5852	8.79	93		3001	2851	51.28	48.72
6	5	9	6	17	5850	8.79	94		2988	2862	51.08	48.92
8	21	9	6	13	5841	8.78	95		3166	2675	54.2	45.8
7	2	9	5	17	5840	8.77	96		3154	2686	54.01	45.99
8	29	9	7	16	5839	8.77	97		2848	2991	48.78	51.22
8	15	9	7	15	5837	8.77	98		2847	2990	48.78	51.22
8	16	9	1	16	5836	8.77	99		2710	3126	46.44	53.56
9	4	9	6	14	5835	8.77	100		3023	2812	51.81	48.19
7	17	9	6	14	5828	8.76	101	66554	3005	2823	51.56	48.44
12	18	9	6	17	5828	8.76	102		3095	2733	53.11	46.89
6	5	9	6	16	5822	8.75	103		3063	2759	52.61	47.39
2	13	9	6	15	5820	8.74	104		3040	2780	52.23	47.77
7	17	9	6	16	5815	8.74	105		2955	2860	50.82	49.18
7	31	9	6	13	5813	8.73	106		3001	2812	51.63	48.37
6	19	9	6	14	5812	8.73	107		3095	2717	53.25	46.75
8	15	9	7	16	5812	8.73	108		2837	2975	48.81	51.19
8	16	9	1	15	5810	8.73	109		2716	3094	46.75	53.25
9	4	9	6	18	5810	8.73	110		3094	2716	53.25	46.75
8	29	9	7	13	5806	8.72	111		2987	2819	51.45	48.55
12	29	9	3	17	5803	8.72	112		3019	2784	52.02	47.98
8	3	9	2	17	5802	8.72	113		3143	2659	54.17	45.83
8	1	9	7	14	5801	8.72	114		3033	2768	52.28	47.72
12	23	9	4	17	5801	8.72	115		3038	2763	52.37	47.63
8	8	9	7	14	5797	8.71	116		2993	2804	51.63	48.37
8	9	9	1	13	5797	8.71	117		2682	3115	46.27	53.73
8	20	9	5	17	5796	8.71	118		2980	2816	51.41	48.59
8	12	9	4	17	5788	8.7	119		3016	2772	52.11	47.89
8	16	9	1	13	5788	8.7	120		2623	3165	45.32	54.68
7	24	9	6	14	5786	8.69	121	66554	2988	2798	51.64	48.36

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
11	13	9	6	16	5779	8.68	122		3000	2779	51.91	48.09
6	19	9	6	15	5778	8.68	123		3066	2712	53.06	46.94
9	20	9	1	18	5777	8.68	124		2970	2807	51.41	48.59
3	13	9	6	18	5771	8.67	125		2884	2887	49.97	50.03
9	3	9	5	16	5770	8.67	126		2926	2844	50.71	49.29
8	25	9	3	17	5768	8.67	127		3113	2655	53.97	46.03
7	10	9	6	15	5767	8.67	128		2917	2850	50.58	49.42
1	23	9	6	17	5762	8.66	129		3073	2689	53.33	46.67
8	16	9	1	17	5762	8.66	130		2737	3025	47.5	52.5
6	12	9	6	15	5761	8.66	131		2881	2880	50.01	49.99
1	16	9	6	18	5755	8.65	132		2946	2809	51.19	48.81
7	10	9	6	18	5752	8.64	133		2988	2764	51.95	48.05
8	5	9	4	17	5746	8.63	134		2895	2851	50.38	49.62
1	30	9	6	17	5745	8.63	135		3103	2642	54.01	45.99
8	22	9	7	17	5745	8.63	136		2668	3077	46.44	53.56
7	5	9	1	13	5742	8.63	137		2498	3244	43.5	56.5
6	26	9	6	18	5735	8.62	138		2901	2834	50.58	49.42
8	29	9	7	12	5735	8.62	139		2861	2874	49.89	50.11
8	23	9	1	13	5734	8.62	140		2613	3121	45.57	54.43
9	27	9	1	18	5731	8.61	141	66554	2785	2946	48.6	51.4
8	3	9	2	16	5727	8.61	142		2962	2765	51.72	48.28
10	9	9	6	15	5726	8.6	143		2808	2918	49.04	50.96
3	20	9	6	16	5725	8.6	144		2881	2844	50.32	49.68
8	22	9	7	15	5721	8.6	145		2801	2920	48.96	51.04
8	28	9	6	14	5721	8.6	146		2940	2781	51.39	48.61
6	26	9	6	16	5716	8.59	147		2942	2774	51.47	48.53
8	9	9	1	16	5715	8.59	148		2589	3126	45.3	54.7
9	25	9	6	15	5714	8.59	149		2843	2871	49.75	50.25
4	24	9	6	15	5713	8.58	150		2889	2824	50.57	49.43
11	27	9	6	16	5712	8.58	151		3126	2586	54.73	45.27
3	27	9	6	16	5711	8.58	152		3112	2599	54.49	45.51
10	2	9	6	18	5710	8.58	153		2892	2818	50.65	49.35
9	11	9	6	18	5706	8.57	154		2894	2812	50.72	49.28
8	9	9	1	17	5705	8.57	155		2674	3031	46.87	53.13
8	8	9	7	15	5704	8.57	156		2883	2821	50.54	49.46
11	13	9	6	18	5704	8.57	157		2833	2871	49.67	50.33
12	26	9	7	14	5703	8.57	158		3019	2684	52.94	47.06
9	11	9	6	16	5702	8.57	159		3005	2697	52.7	47.3
12	4	9	6	17	5700	8.56	160		2975	2725	52.19	47.81
12	28	9	2	17	5699	8.56	161	66554	2935	2764	51.5	48.5
8	1	9	7	13	5698	8.56	162		2896	2802	50.82	49.18
9	26	9	7	12	5698	8.56	163		2967	2731	52.07	47.93
8	13	9	5	16	5696	8.56	164		2818	2878	49.47	50.53
10	30	9	6	16	5696	8.56	165		3005	2691	52.76	47.24
2	6	9	6	17	5694	8.56	166		2984	2710	52.41	47.59
7	19	9	1	16	5693	8.55	167		2637	3056	46.32	53.68
11	25	9	4	17	5693	8.55	168		2985	2708	52.43	47.57
2	20	9	6	16	5692	8.55	169		2784	2908	48.91	51.09
8	13	9	5	18	5691	8.55	170		2903	2788	51.01	48.99
12	22	9	3	17	5691	8.55	171		3013	2678	52.94	47.06
6	11	9	5	17	5689	8.55	172		3014	2675	52.98	47.02
7	26	9	1	16	5688	8.55	173		2595	3093	45.62	54.38

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
9	4	9	6	13	5688	8.55	174		2947	2741	51.81	48.19
9	3	9	5	18	5678	8.53	175		2926	2752	51.53	48.47
8	27	9	5	17	5677	8.53	176		2964	2713	52.21	47.79
9	18	9	6	15	5676	8.53	177		2739	2937	48.26	51.74
11	27	9	6	15	5676	8.53	178		3150	2526	55.5	44.5
9	2	9	4	17	5675	8.53	179		2911	2764	51.3	48.7
11	6	9	6	16	5675	8.53	180		2936	2739	51.74	48.26
3	13	9	6	17	5674	8.53	181	66554	3006	2668	52.98	47.02
9	20	9	1	17	5673	8.52	182		2656	3017	46.82	53.18
2	27	9	6	16	5664	8.51	183		2921	2743	51.57	48.43
2	27	9	6	17	5661	8.51	184		2995	2666	52.91	47.09
12	24	9	5	14	5653	8.49	185		2926	2727	51.76	48.24
3	20	9	6	18	5651	8.49	186		3005	2646	53.18	46.82
7	26	9	1	13	5649	8.49	187		2810	2839	49.74	50.26
8	22	9	7	13	5649	8.49	188		2850	2799	50.45	49.55
6	5	9	6	18	5647	8.48	189		2949	2698	52.22	47.78
7	31	9	6	18	5647	8.48	190		2983	2664	52.82	47.18
12	29	9	3	16	5647	8.48	191		2831	2816	50.13	49.87
8	30	9	1	14	5645	8.48	192		2683	2962	47.53	52.47
11	20	9	6	16	5644	8.48	193		2912	2732	51.59	48.41
12	4	9	6	16	5643	8.48	194		2826	2817	50.08	49.92
8	20	9	5	16	5641	8.48	195		2752	2889	48.79	51.21
7	26	9	1	15	5639	8.47	196		2682	2957	47.56	52.44
2	20	9	6	18	5637	8.47	197		2914	2723	51.69	48.31
6	12	9	6	18	5637	8.47	198		2988	2649	53.01	46.99
8	16	9	1	18	5636	8.47	199		2740	2896	48.62	51.38
9	27	9	1	17	5632	8.46	200		2515	3117	44.66	55.34

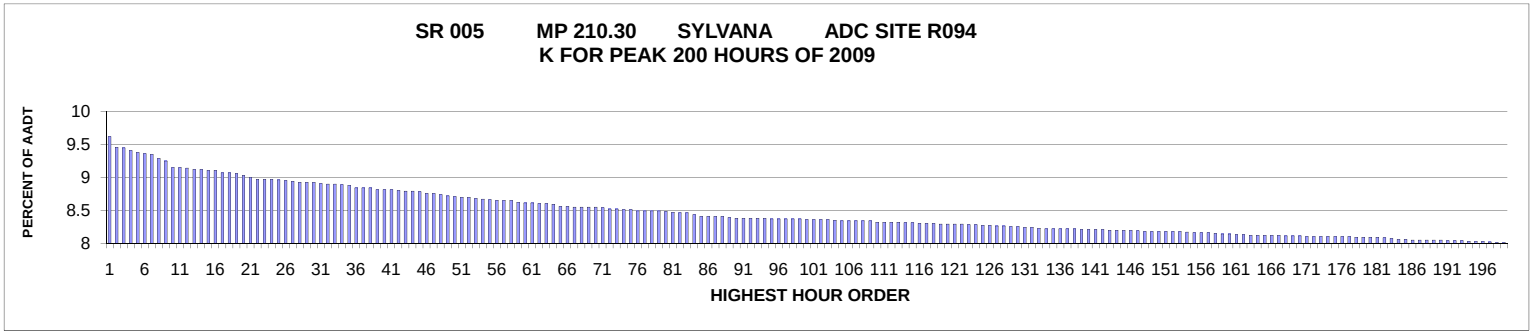

AADT= 71695 **K 30 FACTOR=** 8.93 **K 100 FACTOR=** 8.37 **K 200 FACTOR=** 8.01 **D FACTOR=** 53.71

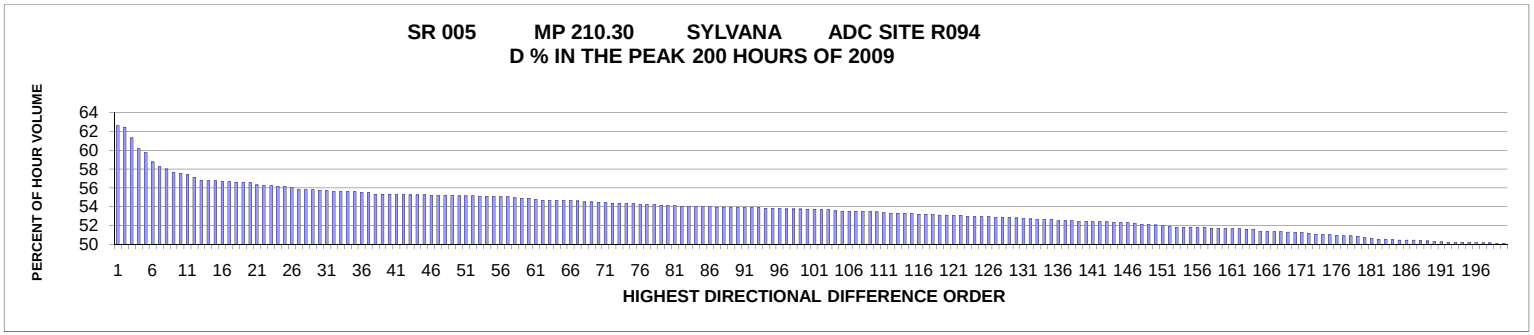

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
9	27	9	1	18	6964	9.71	1	71695	3102	3862	44.54	55.46
5	10	9	1	17	6894	9.62	2		3084	3810	44.73	55.27
11	26	9	5	14	6784	9.46	3		3934	2850	57.99	42.01
11	27	9	6	15	6772	9.45	4		4237	2535	62.57	37.43
4	18	9	7	12	6743	9.41	5		3816	2927	56.59	43.41
4	12	9	1	19	6726	9.38	6		3345	3381	49.73	50.27
4	19	9	1	17	6710	9.36	7		2674	4036	39.85	60.15
4	10	9	6	16	6704	9.35	8		3507	3197	52.31	47.69
5	8	9	6	17	6657	9.29	9		3441	3216	51.69	48.31
4	10	9	6	17	6634	9.25	10		3338	3296	50.32	49.68
5	10	9	1	18	6557	9.15	11		3021	3536	46.07	53.93
9	27	9	1	17	6557	9.15	12		2874	3683	43.83	56.17
4	18	9	7	17	6553	9.14	13		2778	3775	42.39	57.61
10	9	9	6	17	6541	9.12	14		3555	2986	54.35	45.65
11	29	9	1	16	6535	9.12	15		3497	3038	53.51	46.49
9	20	9	1	18	6534	9.11	16		3234	3300	49.49	50.51
4	18	9	7	13	6529	9.11	17		3597	2932	55.09	44.91

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
9	4	9	6	16	6505	9.07	18		3614	2891	55.56	44.44
10	2	9	6	17	6503	9.07	19		3337	3166	51.31	48.69
9	5	9	7	12	6496	9.06	20		3291	3205	50.66	49.34
4	17	9	6	17	6471	9.03	21	71695	3444	3027	53.22	46.78
4	10	9	6	15	6452	9	22		3491	2961	54.11	45.89
2	16	9	2	17	6431	8.97	23		3205	3226	49.84	50.16
5	8	9	6	18	6431	8.97	24		3422	3009	53.21	46.79
5	10	9	1	16	6430	8.97	25		2915	3515	45.33	54.67
4	12	9	1	18	6424	8.96	26		3045	3379	47.4	52.6
4	10	9	6	18	6419	8.95	27		3290	3129	51.25	48.75
4	18	9	7	15	6409	8.94	28		3196	3213	49.87	50.13
11	25	9	4	15	6404	8.93	29		3307	3097	51.64	48.36
4	18	9	7	14	6403	8.93	30		3474	2929	54.26	45.74
9	25	9	6	16	6399	8.93	31		3455	2944	53.99	46.01
11	29	9	1	17	6385	8.91	32		3323	3062	52.04	47.96
10	9	9	6	18	6381	8.9	33		3527	2854	55.27	44.73
9	18	9	6	17	6380	8.9	34		3519	2861	55.16	44.84
1	16	9	6	17	6377	8.89	35		3399	2978	53.3	46.7
4	18	9	7	16	6368	8.88	36		2931	3437	46.03	53.97
4	19	9	1	16	6341	8.84	37		2808	3533	44.28	55.72
10	9	9	6	16	6340	8.84	38		3405	2935	53.71	46.29
5	10	9	1	14	6336	8.84	39		3113	3223	49.13	50.87
4	19	9	1	14	6317	8.81	40		3315	3002	52.48	47.52
12	26	9	7	12	6317	8.81	41	71695	2691	3626	42.6	57.4
11	6	9	6	17	6313	8.81	42		3405	2908	53.94	46.06
11	25	9	4	14	6311	8.8	43		3042	3269	48.2	51.8
11	26	9	5	13	6305	8.79	44		2931	3374	46.49	53.51
9	5	9	7	13	6301	8.79	45		3179	3122	50.45	49.55
9	18	9	6	16	6296	8.78	46		3315	2981	52.65	47.35
9	4	9	6	15	6280	8.76	47		3491	2789	55.59	44.41
5	10	9	1	19	6279	8.76	48		2925	3354	46.58	53.42
4	17	9	6	18	6263	8.74	49		3430	2833	54.77	45.23
9	18	9	6	18	6252	8.72	50		3452	2800	55.21	44.79
9	25	9	6	17	6248	8.71	51		3450	2798	55.22	44.78
9	11	9	6	17	6240	8.7	52		3364	2876	53.91	46.09
10	16	9	6	17	6238	8.7	53		3477	2761	55.74	44.26
5	10	9	1	13	6220	8.68	54		3291	2929	52.91	47.09
9	4	9	6	18	6213	8.67	55		3480	2733	56.01	43.99
5	10	9	1	15	6210	8.66	56		3004	3206	48.37	51.63
5	8	9	6	16	6204	8.65	57		3294	2910	53.09	46.91
10	2	9	6	16	6204	8.65	58		3354	2850	54.06	45.94
4	18	9	7	18	6199	8.65	59		2586	3613	41.72	58.28
9	11	9	6	18	6183	8.62	60		3326	2857	53.79	46.21
3	6	9	6	17	6175	8.61	61	71695	3374	2801	54.64	45.36
10	11	9	1	18	6174	8.61	62		3430	2744	55.56	44.44
4	19	9	1	15	6169	8.6	63		3022	3147	48.99	51.01
9	20	9	1	17	6163	8.6	64		3050	3113	49.49	50.51
12	26	9	7	14	6158	8.59	65		3187	2971	51.75	48.25
9	27	9	1	19	6135	8.56	66		3095	3040	50.45	49.55
9	13	9	1	18	6134	8.56	67		3148	2986	51.32	48.68
9	20	9	1	16	6131	8.55	68		2895	3236	47.22	52.78
10	11	9	1	17	6129	8.55	69		2890	3239	47.15	52.85

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
9	25	9	6	18	6128	8.55	70		3348	2780	54.63	45.37
11	25	9	4	16	6127	8.55	71		3377	2750	55.12	44.88
10	23	9	6	17	6126	8.54	72		3115	3011	50.85	49.15
4	3	9	6	17	6111	8.52	73		3339	2772	54.64	45.36
9	26	9	7	17	6106	8.52	74		3198	2908	52.37	47.63
9	3	9	5	17	6101	8.51	75		3352	2749	54.94	45.06
11	29	9	1	15	6099	8.51	76		3295	2804	54.03	45.97
12	30	9	4	17	6090	8.49	77		3301	2789	54.2	45.8
2	6	9	6	17	6089	8.49	78		3425	2664	56.25	43.75
9	4	9	6	14	6089	8.49	79		3318	2771	54.49	45.51
9	7	9	2	16	6088	8.49	80		2765	3323	45.42	54.58
5	10	9	1	12	6081	8.48	81	71695	3254	2827	53.51	46.49
11	13	9	6	17	6073	8.47	82		3293	2780	54.22	45.78
11	20	9	6	17	6065	8.46	83		3355	2710	55.32	44.68
12	24	9	5	16	6064	8.46	84		3205	2859	52.85	47.15
3	13	9	6	18	6042	8.43	85		3258	2784	53.92	46.08
4	12	9	1	14	6031	8.41	86		2918	3113	48.38	51.62
5	9	9	7	17	6031	8.41	87		2916	3115	48.35	51.65
4	12	9	1	13	6030	8.41	88		3042	2988	50.45	49.55
9	12	9	7	12	6026	8.41	89		3008	3018	49.92	50.08
4	19	9	1	18	6016	8.39	90		2483	3533	41.27	58.73
3	13	9	6	17	6009	8.38	91		3232	2777	53.79	46.21
10	2	9	6	18	6008	8.38	92		3179	2829	52.91	47.09
11	6	9	6	16	6007	8.38	93		3284	2723	54.67	45.33
1	30	9	6	17	6006	8.38	94		3350	2656	55.78	44.22
9	26	9	7	12	6005	8.38	95		2975	3030	49.54	50.46
9	27	9	1	16	6000	8.37	96		2574	3426	42.9	57.1
9	19	9	7	14	5999	8.37	97		3149	2850	52.49	47.51
10	30	9	6	17	5999	8.37	98		3346	2653	55.78	44.22
12	24	9	5	14	5999	8.37	99		3234	2765	53.91	46.09
9	5	9	7	16	5998	8.37	100		3184	2814	53.08	46.92
9	11	9	6	16	5996	8.36	101	71695	3299	2697	55.02	44.98
9	3	9	5	16	5995	8.36	102		3146	2849	52.48	47.52
9	27	9	1	15	5995	8.36	103		2694	3301	44.94	55.06
9	7	9	2	15	5991	8.36	104		2805	3186	46.82	53.18
9	13	9	1	16	5990	8.35	105		2682	3308	44.77	55.23
10	10	9	7	14	5982	8.34	106		2828	3154	47.28	52.72
11	13	9	6	16	5979	8.34	107		3306	2673	55.29	44.71
11	28	9	7	14	5978	8.34	108		2755	3223	46.09	53.91
11	29	9	1	14	5977	8.34	109		3000	2977	50.19	49.81
9	12	9	7	11	5976	8.34	110		2777	3199	46.47	53.53
12	4	9	6	17	5967	8.32	111		3349	2618	56.13	43.87
1	23	9	6	17	5965	8.32	112		3358	2607	56.3	43.7
12	29	9	3	17	5965	8.32	113		3298	2667	55.29	44.71
9	12	9	7	13	5963	8.32	114		2970	2993	49.81	50.19
10	10	9	7	16	5956	8.31	115		2804	3152	47.08	52.92
10	16	9	6	18	5956	8.31	116		3184	2772	53.46	46.54
11	6	9	6	18	5953	8.3	117		3095	2858	51.99	48.01
1	19	9	2	17	5951	8.3	118		2900	3051	48.73	51.27
10	10	9	7	15	5950	8.3	119		2914	3036	48.97	51.03
5	9	9	7	12	5945	8.29	120		3215	2730	54.08	45.92
9	12	9	7	14	5945	8.29	121	71695	3097	2848	52.09	47.91

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
9	12	9	7	15	5945	8.29	122		3190	2755	53.66	46.34
12	11	9	6	17	5944	8.29	123		3276	2668	55.11	44.89
2	27	9	6	18	5939	8.28	124		3151	2788	53.06	46.94
9	20	9	1	15	5937	8.28	125		3031	2906	51.05	48.95
4	12	9	1	20	5932	8.27	126		2963	2969	49.95	50.05
1	16	9	6	18	5929	8.27	127		3159	2770	53.28	46.72
9	4	9	6	13	5925	8.26	128		3066	2859	51.75	48.25
4	19	9	1	13	5922	8.26	129		3406	2516	57.51	42.49
4	18	9	7	11	5915	8.25	130		3263	2652	55.16	44.84
2	27	9	6	17	5913	8.25	131		3246	2667	54.9	45.1
10	10	9	7	17	5910	8.24	132		2815	3095	47.63	52.37
9	5	9	7	14	5909	8.24	133		3142	2767	53.17	46.83
12	23	9	4	16	5901	8.23	134		3212	2689	54.43	45.57
12	26	9	7	15	5893	8.22	135		2998	2895	50.87	49.13
1	16	9	6	16	5891	8.22	136		3330	2561	56.53	43.47
12	27	9	1	17	5891	8.22	137		2713	3178	46.05	53.95
4	3	9	6	18	5890	8.22	138		3210	2680	54.5	45.5
9	3	9	5	18	5890	8.22	139		3190	2700	54.16	45.84
12	18	9	6	17	5886	8.21	140		3270	2616	55.56	44.44
9	4	9	6	19	5885	8.21	141	71695	3515	2370	59.73	40.27
4	12	9	1	16	5884	8.21	142		2811	3073	47.77	52.23
12	24	9	5	15	5884	8.21	143		3101	2783	52.7	47.3
10	10	9	7	12	5882	8.2	144		2832	3050	48.15	51.85
4	12	9	1	15	5880	8.2	145		3063	2817	52.09	47.91
9	19	9	7	12	5879	8.2	146		2903	2976	49.38	50.62
12	27	9	1	16	5877	8.2	147		2718	3159	46.25	53.75
4	17	9	6	16	5871	8.19	148		3077	2794	52.41	47.59
9	7	9	2	14	5867	8.18	149		2639	3228	44.98	55.02
9	25	9	6	15	5866	8.18	150		3138	2728	53.49	46.51
9	5	9	7	15	5865	8.18	151		3026	2839	51.59	48.41
10	23	9	6	16	5864	8.18	152		3128	2736	53.34	46.66
9	20	9	1	13	5862	8.18	153		2920	2942	49.81	50.19
10	9	9	6	15	5862	8.18	154		3008	2854	51.31	48.69
9	19	9	7	16	5854	8.17	155		3032	2822	51.79	48.21
4	3	9	6	16	5852	8.16	156		3001	2851	51.28	48.72
1	30	9	6	18	5849	8.16	157		3143	2706	53.74	46.26
9	4	9	6	17	5847	8.16	158		3174	2673	54.28	45.72
12	30	9	4	16	5843	8.15	159		3317	2526	56.77	43.23
1	30	9	6	16	5837	8.14	160		3311	2526	56.72	43.28
11	28	9	7	13	5834	8.14	161	71695	2525	3309	43.28	56.72
9	2	9	4	16	5827	8.13	162		3164	2663	54.3	45.7
10	16	9	6	16	5827	8.13	163		3232	2595	55.47	44.53
11	20	9	6	16	5824	8.12	164		3275	2549	56.23	43.77
5	8	9	6	15	5823	8.12	165		3104	2719	53.31	46.69
9	12	9	7	16	5821	8.12	166		3050	2771	52.4	47.6
11	13	9	6	18	5820	8.12	167		3015	2805	51.8	48.2
9	2	9	4	17	5819	8.12	168		3245	2574	55.77	44.23
9	19	9	7	15	5817	8.11	169		3086	2731	53.05	46.95
9	13	9	1	17	5814	8.11	170		2693	3121	46.32	53.68
12	28	9	2	17	5812	8.11	171		3191	2621	54.9	45.1
11	27	9	6	16	5810	8.1	172		3204	2606	55.15	44.85
12	23	9	4	17	5809	8.1	173		3161	2648	54.42	45.58

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
3	13	9	6	16	5808	8.1	174		3209	2599	55.25	44.75
4	12	9	1	17	5807	8.1	175		2825	2982	48.65	51.35
10	10	9	7	13	5807	8.1	176		2770	3037	47.7	52.3
5	9	9	7	16	5806	8.1	177		2896	2910	49.88	50.12
11	25	9	4	17	5805	8.1	178		3200	2605	55.12	44.88
10	23	9	6	18	5802	8.09	179		2968	2834	51.15	48.85
5	25	9	2	17	5801	8.09	180		2178	3623	37.55	62.45
1	23	9	6	16	5798	8.09	181	71695	3283	2515	56.62	43.38
4	19	9	1	12	5797	8.09	182		3279	2518	56.56	43.44
10	30	9	6	16	5792	8.08	183		3148	2644	54.35	45.65
10	11	9	1	16	5784	8.07	184		2674	3110	46.23	53.77
9	6	9	1	13	5779	8.06	185		2758	3021	47.72	52.28
10	4	9	1	17	5777	8.06	186		2875	2902	49.77	50.23
9	27	9	1	14	5774	8.05	187		2588	3186	44.82	55.18
9	19	9	7	13	5772	8.05	188		2897	2875	50.19	49.81
10	2	9	6	15	5772	8.05	189		3118	2654	54.02	45.98
12	28	9	2	16	5771	8.05	190		3101	2670	53.73	46.27
3	21	9	7	16	5768	8.05	191		2975	2793	51.58	48.42
2	6	9	6	18	5765	8.04	192		3264	2501	56.62	43.38
12	26	9	7	13	5765	8.04	193		2746	3019	47.63	52.37
11	26	9	5	15	5762	8.04	194		3532	2230	61.3	38.7
3	6	9	6	18	5760	8.03	195		3042	2718	52.81	47.19
5	9	9	7	14	5759	8.03	196		3049	2710	52.94	47.06
4	11	9	7	16	5757	8.03	197		2823	2934	49.04	50.96
9	11	9	6	15	5748	8.02	198		3086	2662	53.69	46.31
12	27	9	1	15	5746	8.01	199		2722	3024	47.37	52.63
12	26	9	7	16	5745	8.01	200		2896	2849	50.41	49.59

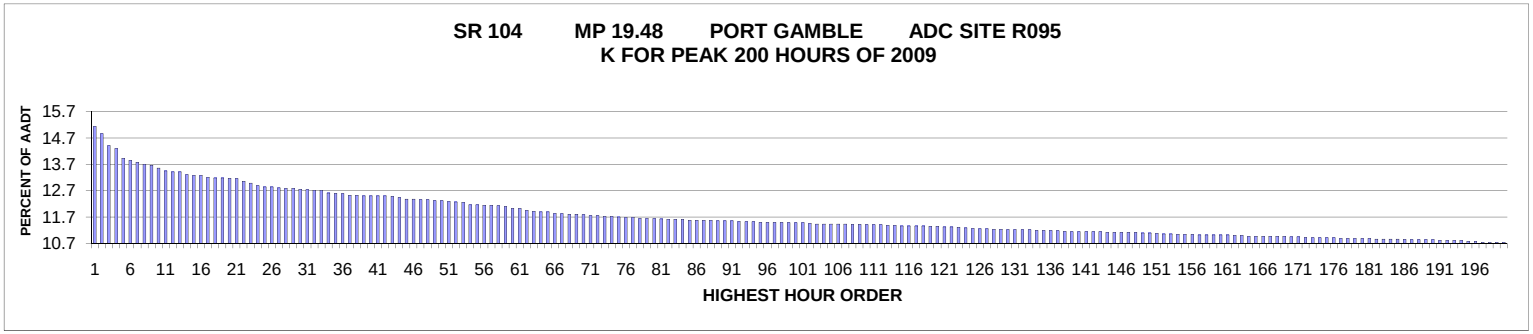

AADT= 5256 **K 30 FACTOR=** 12.75 **K 100 FACTOR=** 11.47 **K 200 FACTOR=** 10.73 **D FACTOR=** 55.57

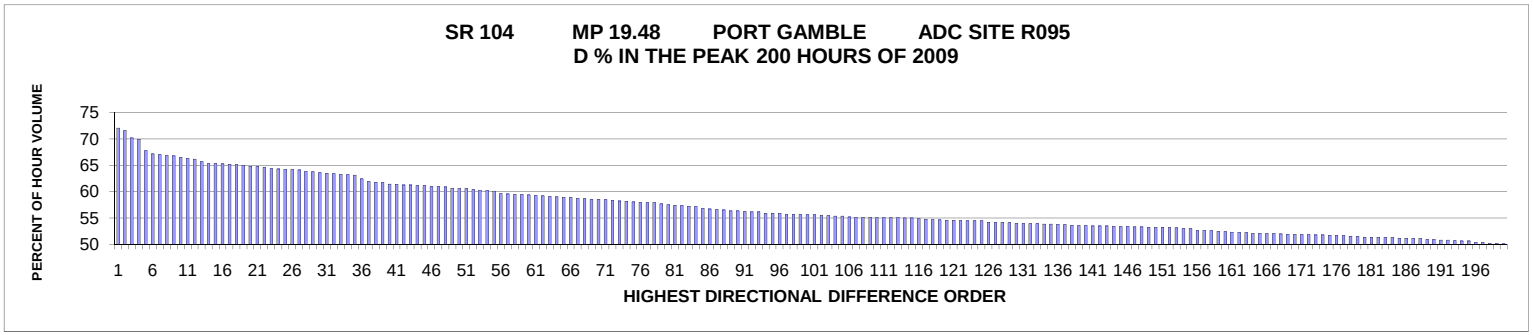

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
6	21	9	1	13	795	15.13	1	5256	423	372	53.21	46.79
8	1	9	7	14	781	14.86	2		355	426	45.45	54.55
8	2	9	1	13	757	14.4	3		387	370	51.12	48.88
8	2	9	1	14	751	14.29	4		389	362	51.8	48.2
8	2	9	1	12	732	13.93	5		411	321	56.15	43.85
9	26	9	7	16	728	13.85	6		351	377	48.21	51.79
9	26	9	7	13	724	13.77	7		239	485	33.01	66.99
8	2	9	1	16	720	13.7	8		428	292	59.44	40.56
8	1	9	7	12	718	13.66	9		347	371	48.33	51.67
8	16	9	1	13	712	13.55	10		364	348	51.12	48.88
8	23	9	1	13	707	13.45	11		360	347	50.92	49.08
7	5	9	1	13	705	13.41	12		388	317	55.04	44.96
9	26	9	7	17	705	13.41	13		420	285	59.57	40.43
8	9	9	1	13	699	13.3	14		361	338	51.65	48.35
6	7	9	1	16	698	13.28	15		432	266	61.89	38.11
7	26	9	1	12	698	13.28	16		390	308	55.87	44.13
9	27	9	1	16	694	13.2	17		419	275	60.37	39.63

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
4	5	9	1	16	693	13.18	18		404	289	58.3	41.7
7	19	9	1	13	693	13.18	19		314	379	45.31	54.69
7	25	9	7	14	692	13.17	20		295	397	42.63	57.37
7	26	9	1	13	691	13.15	21	5256	376	315	54.41	45.59
6	21	9	1	16	686	13.05	22		357	329	52.04	47.96
8	1	9	7	11	682	12.98	23		285	397	41.79	58.21
8	22	9	7	16	677	12.88	24		276	401	40.77	59.23
6	21	9	1	14	675	12.84	25		350	325	51.85	48.15
6	28	9	1	13	675	12.84	26		361	314	53.48	46.52
7	17	9	6	16	673	12.8	27		306	367	45.47	54.53
7	19	9	1	14	672	12.79	28		340	332	50.6	49.4
8	2	9	1	17	672	12.79	29		389	283	57.89	42.11
8	16	9	1	14	670	12.75	30		376	294	56.12	43.88
4	30	9	5	18	669	12.73	31		364	305	54.41	45.59
8	1	9	7	17	668	12.71	32		324	344	48.5	51.5
9	11	9	6	16	668	12.71	33		307	361	45.96	54.04
7	5	9	1	16	663	12.61	34		409	254	61.69	38.31
6	7	9	1	13	662	12.6	35		336	326	50.76	49.24
7	26	9	1	16	661	12.58	36		344	317	52.04	47.96
8	23	9	1	16	658	12.52	37		396	262	60.18	39.82
9	27	9	1	14	658	12.52	38		366	292	55.62	44.38
7	17	9	6	18	657	12.5	39		362	295	55.1	44.9
7	18	9	7	15	657	12.5	40		275	382	41.86	58.14
7	31	9	6	17	657	12.5	41	5256	267	390	40.64	59.36
9	27	9	1	15	657	12.5	42		415	242	63.17	36.83
7	19	9	1	12	656	12.48	43		377	279	57.47	42.53
9	27	9	1	13	654	12.44	44		310	344	47.4	52.6
7	17	9	6	19	650	12.37	45		348	302	53.54	46.46
9	26	9	7	14	650	12.37	46		254	396	39.08	60.92
8	30	9	1	16	649	12.35	47		356	293	54.85	45.15
9	26	9	7	15	649	12.35	48		341	308	52.54	47.46
6	20	9	7	12	647	12.31	49		255	392	39.41	60.59
8	30	9	1	13	647	12.31	50		366	281	56.57	43.43
7	18	9	7	17	646	12.29	51		361	285	55.88	44.12
7	26	9	1	17	645	12.27	52		396	249	61.4	38.6
8	1	9	7	13	644	12.25	53		301	343	46.74	53.26
4	26	9	1	13	639	12.16	54		340	299	53.21	46.79
9	18	9	6	19	639	12.16	55		335	304	52.43	47.57
4	26	9	1	17	638	12.14	56		423	215	66.3	33.7
6	7	9	1	14	638	12.14	57		413	225	64.73	35.27
8	30	9	1	14	637	12.12	58		390	247	61.22	38.78
9	18	9	6	17	636	12.1	59		325	311	51.1	48.9
7	12	9	1	13	632	12.02	60		325	307	51.42	48.58
9	26	9	7	18	632	12.02	61	5256	412	220	65.19	34.81
6	21	9	1	15	628	11.95	62		404	224	64.33	35.67
8	2	9	1	11	626	11.91	63		337	289	53.83	46.17
7	26	9	1	19	625	11.89	64		390	235	62.4	37.6
8	1	9	7	16	625	11.89	65		331	294	52.96	47.04
8	9	9	1	14	622	11.83	66		380	242	61.09	38.91
6	20	9	7	17	621	11.82	67		329	292	52.98	47.02
3	26	9	5	16	620	11.8	68		352	268	56.77	43.23
7	11	9	7	16	620	11.8	69		284	336	45.81	54.19

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	18	9	7	12	619	11.78	70		242	377	39.1	60.9
4	26	9	1	18	617	11.74	71		377	240	61.1	38.9
8	28	9	6	16	617	11.74	72		255	362	41.33	58.67
8	16	9	1	12	616	11.72	73		337	279	54.71	45.29
9	11	9	6	17	616	11.72	74		316	300	51.3	48.7
7	26	9	1	11	615	11.7	75		335	280	54.47	45.53
7	11	9	7	13	614	11.68	76		242	372	39.41	60.59
7	18	9	7	18	614	11.68	77		403	211	65.64	34.36
7	19	9	1	10	612	11.64	78		272	340	44.44	55.56
9	20	9	1	16	612	11.64	79		347	265	56.7	43.3
9	25	9	6	16	612	11.64	80		268	344	43.79	56.21
7	19	9	1	17	611	11.62	81	5256	317	294	51.88	48.12
7	10	9	6	16	610	11.61	82		256	354	41.97	58.03
8	30	9	1	18	610	11.61	83		361	249	59.18	40.82
9	27	9	1	18	610	11.61	84		428	182	70.16	29.84
6	14	9	1	13	608	11.57	85		329	279	54.11	45.89
7	3	9	6	18	608	11.57	86		328	280	53.95	46.05
9	13	9	1	13	608	11.57	87		320	288	52.63	47.37
9	27	9	1	17	608	11.57	88		412	196	67.76	32.24
4	5	9	1	13	607	11.55	89		318	289	52.39	47.61
7	24	9	6	13	607	11.55	90		271	336	44.65	55.35
10	9	9	6	16	607	11.55	91		273	334	44.98	55.02
7	3	9	6	13	606	11.53	92		220	386	36.3	63.7
8	1	9	7	15	605	11.51	93		279	326	46.12	53.88
9	26	9	7	12	605	11.51	94		251	354	41.49	58.51
6	21	9	1	12	604	11.49	95		326	278	53.97	46.03
8	9	9	1	12	604	11.49	96		348	256	57.62	42.38
8	14	9	6	16	604	11.49	97		294	310	48.68	51.32
8	21	9	6	16	604	11.49	98		254	350	42.05	57.95
8	2	9	1	18	603	11.47	99		401	202	66.5	33.5
8	9	9	1	15	603	11.47	100		382	221	63.35	36.65
10	11	9	1	18	603	11.47	101	5256	367	236	60.86	39.14
6	7	9	1	15	602	11.45	102		387	215	64.29	35.71
7	22	9	4	16	601	11.43	103		323	278	53.74	46.26
7	25	9	7	15	601	11.43	104		301	300	50.08	49.92
8	15	9	7	11	601	11.43	105		295	306	49.08	50.92
8	23	9	1	15	601	11.43	106		385	216	64.06	35.94
11	13	9	6	16	601	11.43	107		334	267	55.57	44.43
7	31	9	6	13	600	11.42	108		281	319	46.83	53.17
11	27	9	6	16	600	11.42	109		287	313	47.83	52.17
7	3	9	6	16	599	11.4	110		246	353	41.07	58.93
7	31	9	6	18	599	11.4	111		286	313	47.75	52.25
8	22	9	7	18	599	11.4	112		361	238	60.27	39.73
7	2	9	5	17	598	11.38	113		295	303	49.33	50.67
7	25	9	7	11	598	11.38	114		269	329	44.98	55.02
7	25	9	7	12	597	11.36	115		285	312	47.74	52.26
8	8	9	7	11	597	11.36	116		268	329	44.89	55.11
9	12	9	7	11	597	11.36	117		210	387	35.18	64.82
10	10	9	7	16	597	11.36	118		288	309	48.24	51.76
9	13	9	1	18	596	11.34	119		365	231	61.24	38.76
9	25	9	6	17	596	11.34	120		306	290	51.34	48.66
7	18	9	7	19	595	11.32	121	5256	416	179	69.92	30.08

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	24	9	6	18	595	11.32	122		302	293	50.76	49.24
6	28	9	1	17	594	11.3	123		357	237	60.1	39.9
8	9	9	1	16	593	11.28	124		286	307	48.23	51.77
7	30	9	5	16	592	11.26	125		315	277	53.21	46.79
4	5	9	1	17	591	11.24	126		391	200	66.16	33.84
7	26	9	1	18	591	11.24	127		395	196	66.84	33.16
4	30	9	5	17	590	11.23	128		265	325	44.92	55.08
6	5	9	6	16	590	11.23	129		285	305	48.31	51.69
8	8	9	7	14	589	11.21	130		252	337	42.78	57.22
8	16	9	1	17	589	11.21	131		374	215	63.5	36.5
8	30	9	1	15	589	11.21	132		364	225	61.8	38.2
9	6	9	1	13	589	11.21	133		274	315	46.52	53.48
4	5	9	1	15	588	11.19	134		371	217	63.1	36.9
7	19	9	1	18	588	11.19	135		384	204	65.31	34.69
9	13	9	1	14	588	11.19	136		347	241	59.01	40.99
6	21	9	1	17	587	11.17	137		392	195	66.78	33.22
8	23	9	1	12	586	11.15	138		349	237	59.56	40.44
4	19	9	1	13	585	11.13	139		315	270	53.85	46.15
6	20	9	7	14	585	11.13	140		272	313	46.5	53.5
8	7	9	6	13	585	11.13	141	5256	285	300	48.72	51.28
9	26	9	7	11	585	11.13	142		215	370	36.75	63.25
11	27	9	6	14	585	11.13	143		273	312	46.67	53.33
6	27	9	7	16	584	11.11	144		290	294	49.66	50.34
7	5	9	1	14	584	11.11	145		329	255	56.34	43.66
7	12	9	1	16	584	11.11	146		329	255	56.34	43.66
8	15	9	7	12	584	11.11	147		263	321	45.03	54.97
10	11	9	1	17	584	11.11	148		418	166	71.58	28.42
6	27	9	7	13	583	11.09	149		209	374	35.85	64.15
8	15	9	7	14	583	11.09	150		272	311	46.66	53.34
7	5	9	1	12	582	11.07	151		370	212	63.57	36.43
7	4	9	7	15	581	11.05	152		239	342	41.14	58.86
7	12	9	1	15	581	11.05	153		373	208	64.2	35.8
7	17	9	6	11	580	11.04	154		203	377	35	65
8	7	9	6	16	580	11.04	155		266	314	45.86	54.14
9	7	9	2	13	580	11.04	156		309	271	53.28	46.72
6	7	9	1	17	579	11.02	157		417	162	72.02	27.98
6	19	9	6	16	579	11.02	158		228	351	39.38	60.62
7	24	9	6	16	579	11.02	159		268	311	46.29	53.71
8	8	9	7	16	579	11.02	160		309	270	53.37	46.63
10	11	9	1	13	579	11.02	161	5256	283	296	48.88	51.12
7	10	9	6	13	578	11	162		267	311	46.19	53.81
8	1	9	7	19	578	11	163		377	201	65.22	34.78
2	15	9	1	16	576	10.96	164		342	234	59.38	40.63
2	16	9	2	16	576	10.96	165		319	257	55.38	44.62
7	26	9	1	10	576	10.96	166		268	308	46.53	53.47
8	16	9	1	16	576	10.96	167		317	259	55.03	44.97
8	30	9	1	12	576	10.96	168		322	254	55.9	44.1
8	30	9	1	17	576	10.96	169		376	200	65.28	34.72
8	15	9	7	13	575	10.94	170		262	313	45.57	54.43
8	22	9	7	13	575	10.94	171		239	336	41.57	58.43
8	22	9	7	14	574	10.92	172		285	289	49.65	50.35
6	14	9	1	16	573	10.9	173		318	255	55.5	44.5

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	2	9	1	15	573	10.9	174		315	258	54.97	45.03
8	23	9	1	17	573	10.9	175		373	200	65.1	34.9
9	12	9	7	13	573	10.9	176		244	329	42.58	57.42
4	26	9	1	15	572	10.88	177		384	188	67.13	32.87
6	6	9	7	16	572	10.88	178		287	285	50.17	49.83
7	17	9	6	15	572	10.88	179		254	318	44.41	55.59
7	29	9	4	18	572	10.88	180		351	221	61.36	38.64
9	27	9	1	19	572	10.88	181	5256	331	241	57.87	42.13
7	16	9	5	16	571	10.86	182		256	315	44.83	55.17
7	24	9	6	17	571	10.86	183		202	369	35.38	64.62
8	28	9	6	13	571	10.86	184		234	337	40.98	59.02
9	25	9	6	18	571	10.86	185		274	297	47.99	52.01
9	20	9	1	13	570	10.84	186		284	286	49.82	50.18
4	26	9	1	14	569	10.83	187		333	236	58.52	41.48
4	29	9	4	16	569	10.83	188		273	296	47.98	52.02
7	24	9	6	15	569	10.83	189		288	281	50.62	49.38
7	31	9	6	16	569	10.83	190		267	302	46.92	53.08
7	11	9	7	11	568	10.81	191		247	321	43.49	56.51
7	18	9	7	10	568	10.81	192		252	316	44.37	55.63
8	14	9	6	15	568	10.81	193		310	258	54.58	45.42
9	12	9	7	19	568	10.81	194		333	235	58.63	41.37
6	6	9	7	12	566	10.77	195		205	361	36.22	63.78
8	21	9	6	18	566	10.77	196		294	272	51.94	48.06
6	26	9	6	16	564	10.73	197		252	312	44.68	55.32
7	23	9	5	16	564	10.73	198		275	289	48.76	51.24
9	4	9	6	17	564	10.73	199		262	302	46.45	53.55
9	12	9	7	17	564	10.73	200		322	242	57.09	42.91

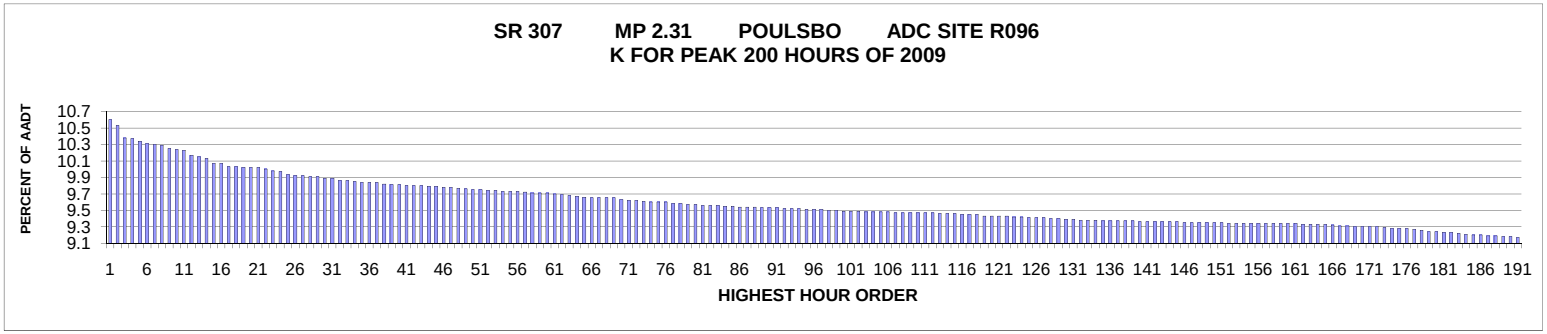

AADT= 15393 **K 30 FACTOR=** 10.02 **K 100 FACTOR=** 9.53 **K 200 FACTOR=** 9.17 **D FACTOR=** 58.12

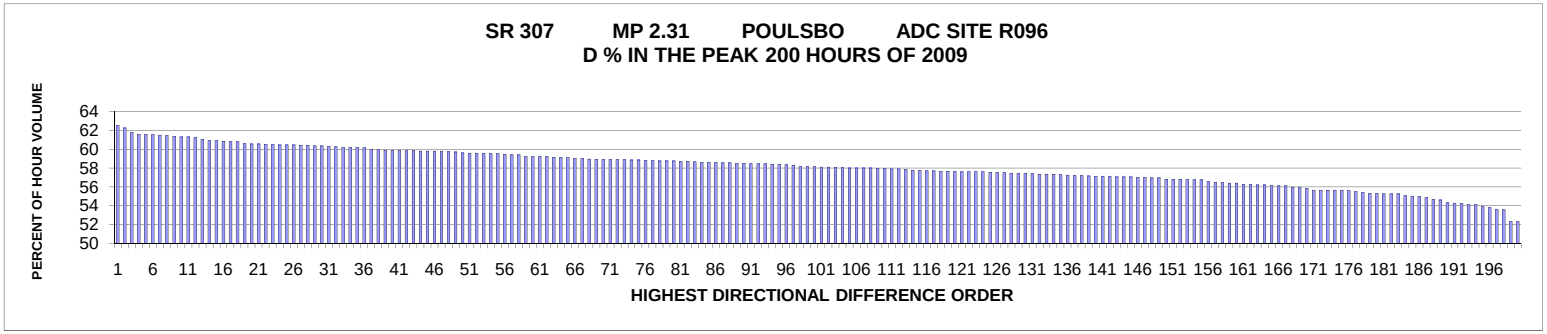

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
12	11	9	6	17	1631	10.6	1	15393	977	654	59.9	40.1
5	15	9	6	17	1621	10.53	2		889	732	54.84	45.16
6	12	9	6	17	1598	10.38	3		925	673	57.88	42.12
5	29	9	6	17	1596	10.37	4		865	731	54.2	45.8
12	1	9	3	17	1591	10.34	5		918	673	57.7	42.3
5	8	9	6	17	1587	10.31	6		932	655	58.73	41.27
5	15	9	6	16	1586	10.3	7		853	733	53.78	46.22
6	2	9	3	17	1584	10.29	8		933	651	58.9	41.1
5	1	9	6	16	1578	10.25	9		922	656	58.43	41.57
12	18	9	6	17	1576	10.24	10		967	609	61.36	38.64
6	17	9	4	17	1574	10.23	11		947	627	60.17	39.83
12	18	9	6	16	1566	10.17	12		899	667	57.41	42.59
11	6	9	6	17	1563	10.15	13		951	612	60.84	39.16
4	30	9	5	17	1559	10.13	14		942	617	60.42	39.58
5	1	9	6	17	1550	10.07	15		874	676	56.39	43.61
11	3	9	3	17	1550	10.07	16		926	624	59.74	40.26
5	8	9	6	16	1544	10.03	17		868	676	56.22	43.78

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
6	30	9	3	17	1544	10.03	18		910	634	58.94	41.06
4	24	9	6	17	1543	10.02	19		885	658	57.36	42.64
6	5	9	6	17	1543	10.02	20		905	638	58.65	41.35
4	21	9	3	17	1542	10.02	21	15393	852	690	55.25	44.75
4	28	9	3	17	1539	10	22		880	659	57.18	42.82
5	29	9	6	16	1536	9.98	23		876	660	57.03	42.97
10	2	9	6	17	1534	9.97	24		933	601	60.82	39.18
12	21	9	2	17	1529	9.93	25		892	637	58.34	41.66
10	7	9	4	17	1527	9.92	26		940	587	61.56	38.44
12	7	9	2	17	1527	9.92	27		919	608	60.18	39.82
4	10	9	6	17	1525	9.91	28		843	682	55.28	44.72
12	15	9	3	17	1525	9.91	29		939	586	61.57	38.43
6	15	9	2	17	1523	9.89	30		864	659	56.73	43.27
6	29	9	2	17	1522	9.89	31		868	654	57.03	42.97
6	10	9	4	17	1518	9.86	32		853	665	56.19	43.81
6	3	9	4	17	1517	9.86	33		891	626	58.73	41.27
6	8	9	2	17	1516	9.85	34		864	652	56.99	43.01
3	6	9	6	17	1515	9.84	35		875	640	57.76	42.24
12	9	9	4	17	1515	9.84	36		921	594	60.79	39.21
7	2	9	5	17	1514	9.84	37		832	682	54.95	45.05
11	24	9	3	17	1511	9.82	38		881	630	58.31	41.69
4	29	9	4	17	1510	9.81	39		903	607	59.8	40.2
6	16	9	3	17	1510	9.81	40		849	661	56.23	43.77
8	4	9	3	17	1509	9.8	41	15393	883	626	58.52	41.48
11	20	9	6	17	1509	9.8	42		871	638	57.72	42.28
12	2	9	4	17	1509	9.8	43		912	597	60.44	39.56
5	20	9	4	17	1507	9.79	44		855	652	56.74	43.26
9	8	9	3	17	1507	9.79	45		882	625	58.53	41.47
8	21	9	6	17	1506	9.78	46		909	597	60.36	39.64
8	5	9	4	17	1505	9.78	47		886	619	58.87	41.13
9	18	9	6	17	1504	9.77	48		922	582	61.3	38.7
5	1	9	6	18	1503	9.76	49		843	660	56.09	43.91
5	14	9	5	17	1501	9.75	50		839	662	55.9	44.1
9	10	9	5	17	1501	9.75	51		868	633	57.83	42.17
6	9	9	3	17	1500	9.74	52		886	614	59.07	40.93
8	18	9	3	17	1499	9.74	53		926	573	61.77	38.23
3	3	9	3	17	1497	9.73	54		861	636	57.52	42.48
5	21	9	5	17	1497	9.73	55		827	670	55.24	44.76
6	11	9	5	17	1497	9.73	56		845	652	56.45	43.55
6	4	9	5	17	1496	9.72	57		877	619	58.62	41.38
12	4	9	6	17	1495	9.71	58		900	595	60.2	39.8
6	18	9	5	17	1494	9.71	59		900	594	60.24	39.76
12	11	9	6	16	1494	9.71	60		868	626	58.1	41.9
10	5	9	2	17	1493	9.7	61	15393	893	600	59.81	40.19
7	14	9	3	17	1492	9.69	62		871	621	58.38	41.62
7	30	9	5	17	1490	9.68	63		820	670	55.03	44.97
7	6	9	2	17	1489	9.67	64		833	656	55.94	44.06
9	22	9	3	17	1487	9.66	65		890	597	59.85	40.15
7	15	9	4	17	1486	9.65	66		844	642	56.8	43.2
11	18	9	4	17	1486	9.65	67		905	581	60.9	39.1
5	13	9	4	17	1485	9.65	68		855	630	57.58	42.42
5	21	9	5	18	1485	9.65	69		855	630	57.58	42.42

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
10	23	9	6	16	1483	9.63	70		854	629	57.59	42.41
9	25	9	6	17	1481	9.62	71		861	620	58.14	41.86
11	6	9	6	16	1481	9.62	72		859	622	58	42
8	11	9	3	17	1480	9.61	73		909	571	61.42	38.58
10	13	9	3	17	1478	9.6	74		895	583	60.55	39.45
10	22	9	5	17	1478	9.6	75		885	593	59.88	40.12
4	17	9	6	16	1477	9.6	76		818	659	55.38	44.62
5	18	9	2	17	1475	9.58	77		821	654	55.66	44.34
5	26	9	3	17	1475	9.58	78		855	620	57.97	42.03
5	7	9	5	17	1473	9.57	79		826	647	56.08	43.92
12	3	9	5	17	1473	9.57	80		849	624	57.64	42.36
4	22	9	4	17	1471	9.56	81	15393	853	618	57.99	42.01
5	22	9	6	17	1471	9.56	82		862	609	58.6	41.4
5	28	9	5	17	1471	9.56	83		842	629	57.24	42.76
6	1	9	2	17	1470	9.55	84		831	639	56.53	43.47
10	9	9	6	17	1470	9.55	85		866	604	58.91	41.09
10	6	9	3	17	1469	9.54	86		877	592	59.7	40.3
11	5	9	5	17	1469	9.54	87		865	604	58.88	41.12
9	24	9	5	17	1468	9.54	88		828	640	56.4	43.6
9	17	9	5	17	1467	9.53	89		861	606	58.69	41.31
9	18	9	6	16	1467	9.53	90		888	579	60.53	39.47
10	8	9	5	17	1467	9.53	91		893	574	60.87	39.13
11	25	9	4	16	1466	9.52	92		895	571	61.05	38.95
6	5	9	6	16	1465	9.52	93		851	614	58.09	41.91
11	17	9	3	17	1465	9.52	94		876	589	59.8	40.2
6	12	9	6	16	1464	9.51	95		855	609	58.4	41.6
7	31	9	6	17	1464	9.51	96		862	602	58.88	41.12
10	23	9	6	17	1464	9.51	97		901	563	61.54	38.46
8	7	9	6	17	1463	9.5	98		833	630	56.94	43.06
8	31	9	2	17	1463	9.5	99		822	641	56.19	43.81
1	30	9	6	17	1461	9.49	100		838	623	57.36	42.64
5	22	9	6	16	1461	9.49	101	15393	764	697	52.29	47.71
11	13	9	6	16	1461	9.49	102		840	621	57.49	42.51
2	20	9	6	17	1460	9.48	103		838	622	57.4	42.6
12	22	9	3	17	1460	9.48	104		895	565	61.3	38.7
5	19	9	3	17	1459	9.48	105		846	613	57.98	42.02
11	13	9	6	17	1459	9.48	106		864	595	59.22	40.78
2	27	9	6	17	1458	9.47	107		837	621	57.41	42.59
10	20	9	3	17	1458	9.47	108		869	589	59.6	40.4
7	31	9	6	16	1457	9.47	109		896	561	61.5	38.5
8	25	9	3	17	1457	9.47	110		867	590	59.51	40.49
10	16	9	6	17	1457	9.47	111		879	578	60.33	39.67
12	16	9	4	17	1457	9.47	112		879	578	60.33	39.67
10	2	9	6	16	1456	9.46	113		835	621	57.35	42.65
10	28	9	4	17	1456	9.46	114		881	575	60.51	39.49
12	24	9	5	13	1456	9.46	115		761	695	52.27	47.73
10	19	9	2	17	1455	9.45	116		875	580	60.14	39.86
10	27	9	3	17	1455	9.45	117		856	599	58.83	41.17
8	17	9	2	17	1454	9.45	118		881	573	60.59	39.41
4	10	9	6	16	1452	9.43	119		865	587	59.57	40.43
4	30	9	5	16	1452	9.43	120		824	628	56.75	43.25
11	30	9	2	17	1452	9.43	121	15393	889	563	61.23	38.77

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
10	9	9	6	16	1451	9.43	122		824	627	56.79	43.21
4	15	9	4	17	1450	9.42	123		801	649	55.24	44.76
6	22	9	2	17	1450	9.42	124		869	581	59.93	40.07
4	7	9	3	17	1449	9.41	125		804	645	55.49	44.51
6	24	9	4	17	1448	9.41	126		831	617	57.39	42.61
7	7	9	3	17	1448	9.41	127		835	613	57.67	42.33
5	4	9	2	17	1447	9.4	128		841	606	58.12	41.88
11	23	9	2	17	1447	9.4	129		826	621	57.08	42.92
7	13	9	2	17	1446	9.39	130		874	572	60.44	39.56
11	2	9	2	17	1446	9.39	131		904	542	62.52	37.48
7	9	9	5	17	1444	9.38	132		811	633	56.16	43.84
9	1	9	3	17	1444	9.38	133		864	580	59.83	40.17
12	17	9	5	17	1444	9.38	134		899	545	62.26	37.74
6	16	9	3	16	1443	9.37	135		844	599	58.49	41.51
12	4	9	6	16	1443	9.37	136		854	589	59.18	40.82
12	8	9	3	17	1443	9.37	137		852	591	59.04	40.96
12	17	9	5	16	1443	9.37	138		859	584	59.53	40.47
5	5	9	3	17	1442	9.37	139		821	621	56.93	43.07
2	6	9	6	17	1441	9.36	140		823	618	57.11	42.89
4	16	9	5	17	1441	9.36	141	15393	802	639	55.66	44.34
6	23	9	3	17	1441	9.36	142		847	594	58.78	41.22
7	10	9	6	17	1441	9.36	143		822	619	57.04	42.96
10	15	9	5	17	1441	9.36	144		856	585	59.4	40.6
11	25	9	4	17	1441	9.36	145		853	588	59.2	40.8
3	6	9	6	16	1440	9.35	146		800	640	55.56	44.44
4	23	9	5	17	1440	9.35	147		818	622	56.81	43.19
5	15	9	6	18	1440	9.35	148		796	644	55.28	44.72
4	6	9	2	17	1439	9.35	149		778	661	54.07	45.93
5	7	9	5	18	1439	9.35	150		778	661	54.07	45.93
12	3	9	5	16	1439	9.35	151		863	576	59.97	40.03
2	5	9	5	17	1438	9.34	152		822	616	57.16	42.84
3	20	9	6	16	1438	9.34	153		785	653	54.59	45.41
5	11	9	2	17	1438	9.34	154		835	603	58.07	41.93
6	10	9	4	16	1438	9.34	155		786	652	54.66	45.34
8	26	9	4	17	1438	9.34	156		869	569	60.43	39.57
12	23	9	4	16	1438	9.34	157		812	626	56.47	43.53
5	8	9	6	18	1437	9.34	158		779	658	54.21	45.79
6	25	9	5	17	1437	9.34	159		823	614	57.27	42.73
8	20	9	5	17	1437	9.34	160		844	593	58.73	41.27
10	30	9	6	16	1437	9.34	161	15393	828	609	57.62	42.38
3	20	9	6	17	1436	9.33	162		845	591	58.84	41.16
5	12	9	3	17	1436	9.33	163		799	637	55.64	44.36
5	26	9	3	18	1436	9.33	164		802	634	55.85	44.15
6	18	9	5	18	1436	9.33	165		841	595	58.57	41.43
9	28	9	2	17	1434	9.32	166		867	567	60.46	39.54
3	18	9	4	17	1433	9.31	167		841	592	58.69	41.31
8	14	9	6	17	1433	9.31	168		847	586	59.11	40.89
3	13	9	6	17	1431	9.3	169		837	594	58.49	41.51
9	9	9	4	17	1431	9.3	170		851	580	59.47	40.53
9	11	9	6	16	1431	9.3	171		863	568	60.31	39.69
11	19	9	5	17	1431	9.3	172		836	595	58.42	41.58
6	12	9	6	18	1430	9.29	173		816	614	57.06	42.94

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
10	1	9	5	17	1429	9.28	174		824	605	57.66	42.34
1	23	9	6	17	1428	9.28	175		822	606	57.56	42.44
6	11	9	5	16	1428	9.28	176		785	643	54.97	45.03
1	30	9	6	16	1427	9.27	177		827	600	57.95	42.05
10	15	9	5	16	1426	9.26	178		821	605	57.57	42.43
4	9	9	5	17	1422	9.24	179		766	656	53.87	46.13
5	28	9	5	18	1422	9.24	180		761	661	53.52	46.48
2	17	9	3	17	1421	9.23	181	15393	826	595	58.13	41.87
11	10	9	3	17	1421	9.23	182		850	571	59.82	40.18
2	27	9	6	16	1420	9.22	183		790	630	55.63	44.37
1	16	9	6	16	1418	9.21	184		821	597	57.9	42.1
2	13	9	6	17	1416	9.2	185		788	628	55.65	44.35
8	27	9	5	17	1416	9.2	186		841	575	59.39	40.61
2	20	9	6	18	1415	9.19	187		842	573	59.51	40.49
9	15	9	3	17	1415	9.19	188		835	580	59.01	40.99
2	2	9	2	17	1413	9.18	189		767	646	54.28	45.72
7	1	9	4	17	1413	9.18	190		836	577	59.16	40.84
10	16	9	6	16	1412	9.17	191		805	607	57.01	42.99
5	16	9	7	13	1411	9.17	192		655	756	46.42	53.58
6	19	9	6	17	1411	9.17	193		835	576	59.18	40.82

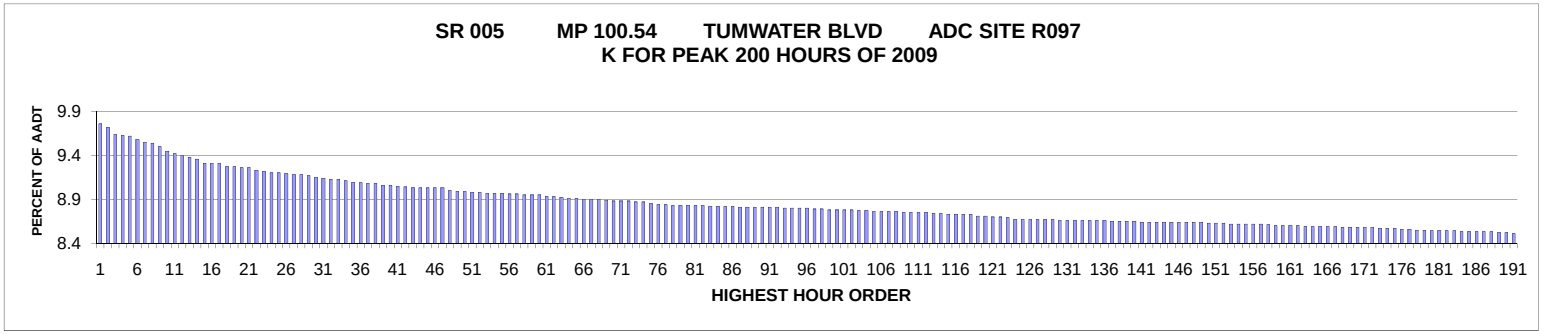

AADT= 68903 **K 30 FACTOR=** 9.26 **K 100 FACTOR=** 8.81 **K 200 FACTOR=** 8.51 **D FACTOR=** 52.55

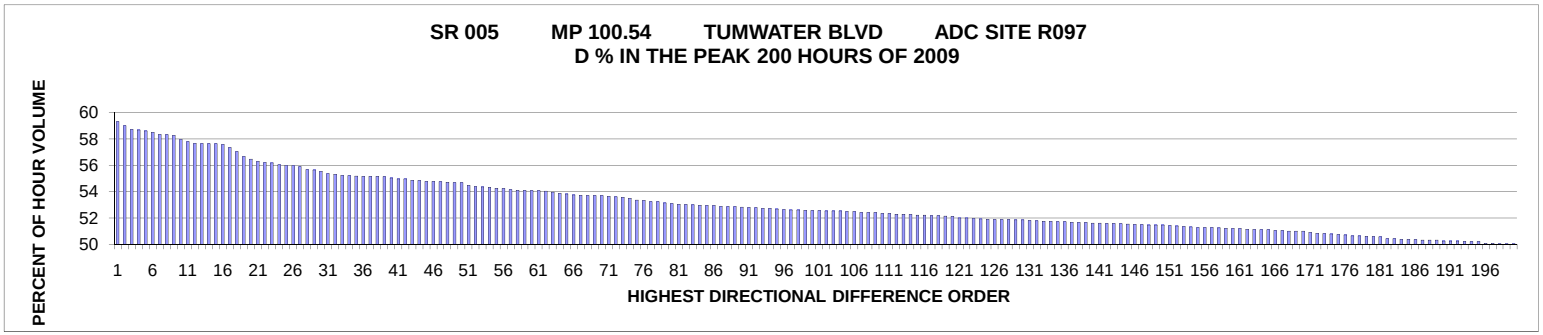

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
12	26	9	7	14	6722	9.76	1	68903	3200	3522	47.6	52.4
8	14	9	6	15	6695	9.72	2		3375	3320	50.41	49.59
12	26	9	7	13	6645	9.64	3		3226	3419	48.55	51.45
11	29	9	1	14	6634	9.63	4		3490	3144	52.61	47.39
11	29	9	1	15	6627	9.62	5		3561	3066	53.73	46.27
11	25	9	4	15	6602	9.58	6		3022	3580	45.77	54.23
11	25	9	4	16	6580	9.55	7		3122	3458	47.45	52.55
8	14	9	6	17	6574	9.54	8		3198	3376	48.65	51.35
11	25	9	4	14	6544	9.5	9		3161	3383	48.3	51.7
6	19	9	6	15	6509	9.45	10		3173	3336	48.75	51.25
8	16	9	1	15	6492	9.42	11		3318	3174	51.11	48.89
8	28	9	6	16	6477	9.4	12		3063	3414	47.29	52.71
8	7	9	6	15	6464	9.38	13		2958	3506	45.76	54.24
7	10	9	6	17	6451	9.36	14		2809	3642	43.54	56.46
11	26	9	5	11	6417	9.31	15		2846	3571	44.35	55.65
8	9	9	1	14	6412	9.31	16		3190	3222	49.75	50.25
8	14	9	6	16	6412	9.31	17		3111	3301	48.52	51.48

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	28	9	6	15	6387	9.27	18		3074	3313	48.13	51.87
8	15	9	7	13	6384	9.27	19		3275	3109	51.3	48.7
8	21	9	6	16	6380	9.26	20		3090	3290	48.43	51.57
8	7	9	6	18	6378	9.26	21	68903	3013	3365	47.24	52.76
8	16	9	1	16	6360	9.23	22		3160	3200	49.69	50.31
7	24	9	6	17	6351	9.22	23		3215	3136	50.62	49.38
8	15	9	7	12	6340	9.2	24		3053	3287	48.15	51.85
8	23	9	1	14	6336	9.2	25		3166	3170	49.97	50.03
12	27	9	1	15	6332	9.19	26		3387	2945	53.49	46.51
7	24	9	6	14	6328	9.18	27		3148	3180	49.75	50.25
11	25	9	4	17	6325	9.18	28		2861	3464	45.23	54.77
8	16	9	1	18	6316	9.17	29		3119	3197	49.38	50.62
8	7	9	6	17	6307	9.15	30		3010	3297	47.72	52.28
11	25	9	4	13	6295	9.14	31		3046	3249	48.39	51.61
7	31	9	6	16	6292	9.13	32		3054	3238	48.54	51.46
11	28	9	7	14	6290	9.13	33		3371	2919	53.59	46.41
5	15	9	6	17	6276	9.11	34		3025	3251	48.2	51.8
8	28	9	6	17	6266	9.09	35		2817	3449	44.96	55.04
7	17	9	6	16	6261	9.09	36		3040	3221	48.55	51.45
8	16	9	1	17	6256	9.08	37		3140	3116	50.19	49.81
6	12	9	6	16	6254	9.08	38		2965	3289	47.41	52.59
12	24	9	5	14	6246	9.06	39		2934	3312	46.97	53.03
7	17	9	6	15	6244	9.06	40		3071	3173	49.18	50.82
9	4	9	6	15	6239	9.05	41	68903	2818	3421	45.17	54.83
8	14	9	6	14	6228	9.04	42		3101	3127	49.79	50.21
8	21	9	6	17	6224	9.03	43		2842	3382	45.66	54.34
12	27	9	1	14	6223	9.03	44		3186	3037	51.2	48.8
11	27	9	6	14	6222	9.03	45		3033	3189	48.75	51.25
7	26	9	1	13	6220	9.03	46		3267	2953	52.52	47.48
7	31	9	6	15	6220	9.03	47		3022	3198	48.59	51.41
7	5	9	1	14	6204	9	48		3107	3097	50.08	49.92
8	8	9	7	13	6196	8.99	49		2872	3324	46.35	53.65
11	28	9	7	13	6195	8.99	50		3201	2994	51.67	48.33
11	29	9	1	16	6188	8.98	51		3253	2935	52.57	47.43
8	16	9	1	14	6187	8.98	52		3074	3113	49.68	50.32
6	26	9	6	16	6181	8.97	53		3023	3158	48.91	51.09
7	5	9	1	16	6181	8.97	54		3138	3043	50.77	49.23
7	10	9	6	16	6179	8.97	55		3065	3114	49.6	50.4
8	7	9	6	16	6177	8.96	56		2798	3379	45.3	54.7
8	23	9	1	13	6177	8.96	57		3137	3040	50.79	49.21
8	14	9	6	18	6169	8.95	58		2830	3339	45.87	54.13
11	28	9	7	15	6169	8.95	59		3312	2857	53.69	46.31
8	16	9	1	13	6164	8.95	60		2974	3190	48.25	51.75
12	24	9	5	13	6155	8.93	61	68903	2896	3259	47.05	52.95
8	9	9	1	15	6152	8.93	62		3075	3077	49.98	50.02
6	19	9	6	17	6143	8.92	63		2710	3433	44.12	55.88
8	7	9	6	14	6142	8.91	64		3251	2891	52.93	47.07
4	3	9	6	17	6141	8.91	65		2755	3386	44.86	55.14
8	23	9	1	16	6133	8.9	66		3045	3088	49.65	50.35
6	12	9	6	17	6131	8.9	67		2657	3474	43.34	56.66
8	21	9	6	18	6129	8.9	68		2554	3575	41.67	58.33
9	4	9	6	14	6126	8.89	69		2888	3238	47.14	52.86

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	16	9	1	19	6121	8.88	70		2985	3136	48.77	51.23
9	18	9	6	16	6117	8.88	71		2886	3231	47.18	52.82
8	9	9	1	13	6116	8.88	72		3102	3014	50.72	49.28
8	30	9	1	16	6113	8.87	73		3191	2922	52.2	47.8
8	22	9	7	13	6110	8.87	74		2896	3214	47.4	52.6
10	2	9	6	17	6095	8.85	75		2581	3514	42.35	57.65
7	24	9	6	18	6091	8.84	76		3025	3066	49.66	50.34
11	27	9	6	13	6089	8.84	77		2902	3187	47.66	52.34
8	14	9	6	12	6084	8.83	78		2864	3220	47.07	52.93
8	14	9	6	13	6084	8.83	79		3030	3054	49.8	50.2
6	21	9	1	17	6083	8.83	80		3102	2981	50.99	49.01
12	23	9	4	15	6082	8.83	81	68903	2879	3203	47.34	52.66
12	27	9	1	16	6082	8.83	82		3290	2792	54.09	45.91
8	8	9	7	12	6078	8.82	83		2886	3192	47.48	52.52
8	1	9	7	12	6077	8.82	84		3075	3002	50.6	49.4
8	21	9	6	14	6075	8.82	85		2940	3135	48.4	51.6
12	26	9	7	12	6075	8.82	86		2907	3168	47.85	52.15
4	10	9	6	18	6072	8.81	87		2471	3601	40.69	59.31
9	4	9	6	16	6071	8.81	88		2839	3232	46.76	53.24
7	26	9	1	14	6070	8.81	89		3141	2929	51.75	48.25
8	30	9	1	14	6068	8.81	90		3265	2803	53.81	46.19
7	17	9	6	14	6067	8.81	91		2930	3137	48.29	51.71
8	2	9	1	15	6067	8.81	92		3100	2967	51.1	48.9
8	28	9	6	14	6064	8.8	93		2918	3146	48.12	51.88
12	23	9	4	17	6064	8.8	94		2656	3408	43.8	56.2
5	22	9	6	16	6063	8.8	95		2877	3186	47.45	52.55
11	29	9	1	13	6062	8.8	96		3226	2836	53.22	46.78
12	24	9	5	15	6059	8.79	97		2717	3342	44.84	55.16
9	25	9	6	17	6058	8.79	98		2603	3455	42.97	57.03
12	26	9	7	15	6053	8.78	99		3140	2913	51.88	48.12
7	31	9	6	17	6050	8.78	100		2754	3296	45.52	54.48
6	26	9	6	15	6049	8.78	101	68903	2879	3170	47.59	52.41
5	22	9	6	17	6047	8.78	102		2735	3312	45.23	54.77
8	23	9	1	17	6045	8.77	103		3194	2851	52.84	47.16
7	10	9	6	14	6040	8.77	104		3001	3039	49.69	50.31
8	29	9	7	12	6039	8.76	105		2855	3184	47.28	52.72
11	26	9	5	12	6034	8.76	106		2954	3080	48.96	51.04
7	31	9	6	18	6033	8.76	107		2682	3351	44.46	55.54
8	9	9	1	18	6033	8.76	108		3110	2923	51.55	48.45
7	10	9	6	15	6032	8.75	109		3078	2954	51.03	48.97
8	23	9	1	15	6032	8.75	110		3087	2945	51.18	48.82
9	11	9	6	16	6027	8.75	111		2732	3295	45.33	54.67
8	15	9	7	14	6026	8.75	112		3150	2876	52.27	47.73
4	10	9	6	17	6024	8.74	113		2700	3324	44.82	55.18
7	26	9	1	15	6019	8.74	114		3120	2899	51.84	48.16
8	22	9	7	12	6017	8.73	115		2881	3136	47.88	52.12
8	21	9	6	13	6016	8.73	116		2872	3144	47.74	52.26
8	13	9	5	16	6014	8.73	117		2916	3098	48.49	51.51
8	30	9	1	17	6012	8.73	118		3173	2839	52.78	47.22
6	12	9	6	15	6004	8.71	119		2817	3187	46.92	53.08
7	31	9	6	14	6000	8.71	120		2966	3034	49.43	50.57
9	18	9	6	15	5998	8.7	121	68903	2819	3179	47	53

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	24	9	6	13	5993	8.7	122		2921	3072	48.74	51.26
8	28	9	6	18	5988	8.69	123		2499	3489	41.73	58.27
11	27	9	6	12	5977	8.67	124		2752	3225	46.04	53.96
4	17	9	6	17	5975	8.67	125		2788	3187	46.66	53.34
6	26	9	6	18	5972	8.67	126		2534	3438	42.43	57.57
7	10	9	6	13	5972	8.67	127		2799	3173	46.87	53.13
7	19	9	1	17	5972	8.67	128		3155	2817	52.83	47.17
10	2	9	6	16	5972	8.67	129		2680	3292	44.88	55.12
2	13	9	6	18	5968	8.66	130		2476	3492	41.49	58.51
7	5	9	1	15	5968	8.66	131		2986	2982	50.03	49.97
7	10	9	6	18	5967	8.66	132		2528	3439	42.37	57.63
8	30	9	1	15	5967	8.66	133		3320	2647	55.64	44.36
7	17	9	6	18	5965	8.66	134		2623	3342	43.97	56.03
8	21	9	6	15	5964	8.66	135		2762	3202	46.31	53.69
10	9	9	6	16	5964	8.66	136		2742	3222	45.98	54.02
5	22	9	6	15	5962	8.65	137		2882	3080	48.34	51.66
6	19	9	6	18	5959	8.65	138		2611	3348	43.82	56.18
12	27	9	1	13	5959	8.65	139		2975	2984	49.92	50.08
9	4	9	6	17	5958	8.65	140		2673	3285	44.86	55.14
2	13	9	6	17	5954	8.64	141	68903	2602	3352	43.7	56.3
9	25	9	6	16	5954	8.64	142		2699	3255	45.33	54.67
9	25	9	6	18	5953	8.64	143		2514	3439	42.23	57.77
7	19	9	1	16	5952	8.64	144		3067	2885	51.53	48.47
9	5	9	7	12	5952	8.64	145		2917	3035	49.01	50.99
2	27	9	6	17	5951	8.64	146		2686	3265	45.14	54.86
8	9	9	1	16	5951	8.64	147		2847	3104	47.84	52.16
10	9	9	6	18	5951	8.64	148		2441	3510	41.02	58.98
8	16	9	1	12	5950	8.64	149		3042	2908	51.13	48.87
11	25	9	4	18	5948	8.63	150		2463	3485	41.41	58.59
6	20	9	7	14	5945	8.63	151		2617	3328	44.02	55.98
10	2	9	6	15	5945	8.63	152		2731	3214	45.94	54.06
4	3	9	6	15	5941	8.62	153		2856	3085	48.07	51.93
9	13	9	1	18	5941	8.62	154		2956	2985	49.76	50.24
7	5	9	1	13	5940	8.62	155		2865	3075	48.23	51.77
9	25	9	6	15	5938	8.62	156		2675	3263	45.05	54.95
7	26	9	1	16	5937	8.62	157		3081	2856	51.89	48.11
7	24	9	6	15	5935	8.61	158		2657	3278	44.77	55.23
8	1	9	7	13	5928	8.6	159		3045	2883	51.37	48.63
4	3	9	6	18	5927	8.6	160		2512	3415	42.38	57.62
6	5	9	6	17	5926	8.6	161	68903	2669	3257	45.04	54.96
8	15	9	7	11	5923	8.6	162		2741	3182	46.28	53.72
12	26	9	7	16	5922	8.59	163		3020	2902	51	49
2	13	9	6	16	5921	8.59	164		2718	3203	45.9	54.1
6	12	9	6	18	5920	8.59	165		2447	3473	41.33	58.67
8	29	9	7	13	5920	8.59	166		2842	3078	48.01	51.99
11	27	9	6	15	5920	8.59	167		2981	2939	50.35	49.65
8	28	9	6	13	5914	8.58	168		2781	3133	47.02	52.98
9	18	9	6	17	5914	8.58	169		2728	3186	46.13	53.87
11	25	9	4	12	5912	8.58	170		2641	3271	44.67	55.33
8	8	9	7	14	5911	8.58	171		2809	3102	47.52	52.48
8	13	9	5	17	5910	8.58	172		2715	3195	45.94	54.06
8	30	9	1	13	5906	8.57	173		3095	2811	52.4	47.6

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	3	9	6	12	5903	8.57	174		3089	2814	52.33	47.67
10	2	9	6	18	5902	8.57	175		2482	3420	42.05	57.95
6	19	9	6	16	5898	8.56	176		2598	3300	44.05	55.95
8	2	9	1	14	5898	8.56	177		2879	3019	48.81	51.19
7	17	9	6	17	5892	8.55	178		2728	3164	46.3	53.7
6	21	9	1	14	5889	8.55	179		2977	2912	50.55	49.45
5	15	9	6	18	5884	8.54	180		2627	3257	44.65	55.35
6	19	9	6	14	5884	8.54	181	68903	2796	3088	47.52	52.48
4	3	9	6	16	5882	8.54	182		2792	3090	47.47	52.53
6	5	9	6	18	5882	8.54	183		2492	3390	42.37	57.63
6	18	9	5	17	5880	8.53	184		2634	3246	44.8	55.2

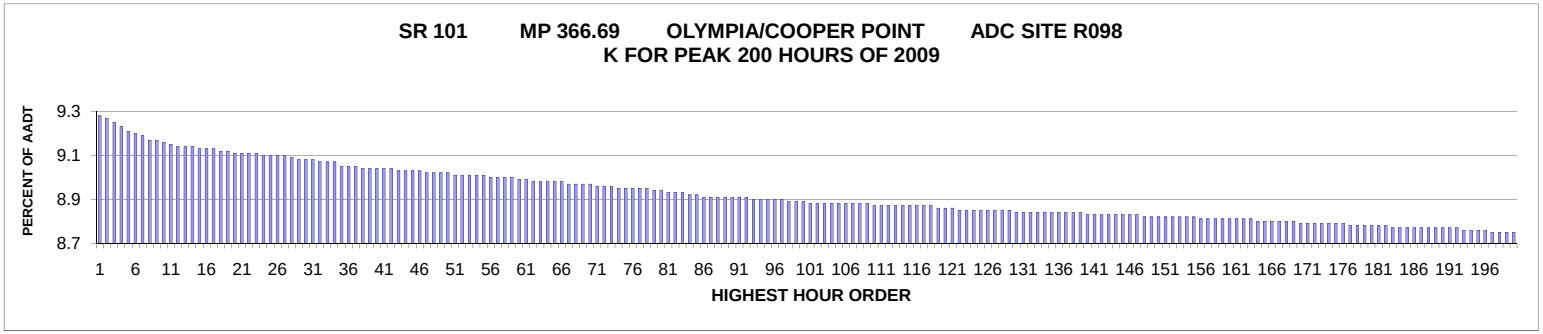

AADT= 96528 **K 30 FACTOR=** 9.08 **K 100 FACTOR=** 8.89 **K 200 FACTOR=** 8.75 **D FACTOR=** 52.99

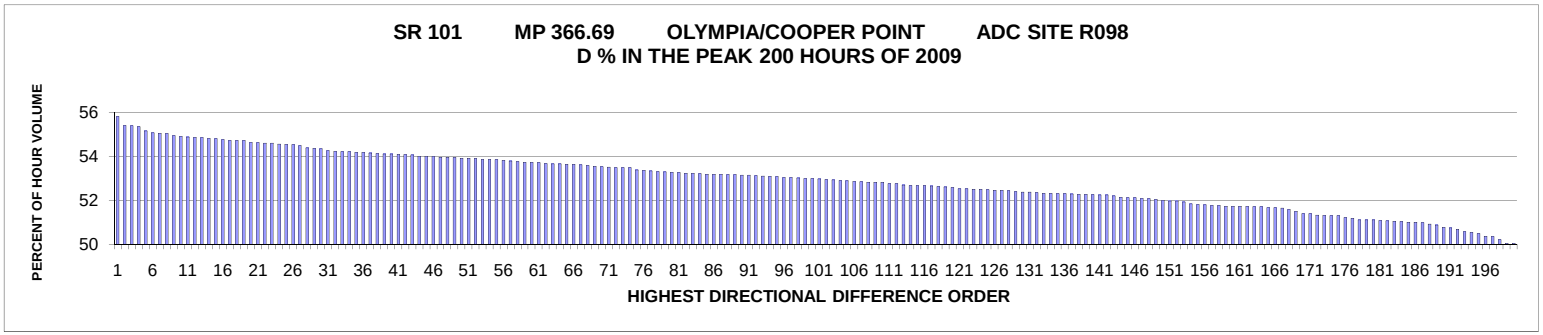

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
9	30	9	4	18	8959	9.28	1	96528	4047	4912	45.17	54.83
10	6	9	3	18	8944	9.27	2		4092	4852	45.75	54.25
9	24	9	5	18	8933	9.25	3		4247	4686	47.54	52.46
10	20	9	3	18	8908	9.23	4		4016	4892	45.08	54.92
9	29	9	3	18	8889	9.21	5		4005	4884	45.06	54.94
10	20	9	3	17	8878	9.2	6		4283	4595	48.24	51.76
9	15	9	3	18	8875	9.19	7		4172	4703	47.01	52.99
9	16	9	4	18	8853	9.17	8		4147	4706	46.84	53.16
9	22	9	3	17	8850	9.17	9		4242	4608	47.93	52.07
9	8	9	3	17	8844	9.16	10		4203	4641	47.52	52.48
9	25	9	6	17	8836	9.15	11		4330	4506	49	51
5	5	9	3	18	8827	9.14	12		4090	4737	46.34	53.66
9	15	9	3	17	8822	9.14	13		4330	4492	49.08	50.92
6	16	9	3	17	8821	9.14	14		4145	4676	46.99	53.01
9	22	9	3	18	8816	9.13	15		4116	4700	46.69	53.31
12	2	9	4	17	8815	9.13	16		4118	4697	46.72	53.28
10	8	9	5	18	8810	9.13	17		4057	4753	46.05	53.95

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
5	8	9	6	17	8808	9.12	18		4282	4526	48.61	51.39
11	3	9	3	18	8802	9.12	19		4083	4719	46.39	53.61
9	17	9	5	18	8798	9.11	20		4166	4632	47.35	52.65
9	30	9	4	17	8798	9.11	21	96528	4078	4720	46.35	53.65
6	11	9	5	17	8794	9.11	22		4175	4619	47.48	52.52
10	28	9	4	17	8790	9.11	23		4085	4705	46.47	53.53
9	3	9	5	17	8783	9.1	24		4331	4452	49.31	50.69
9	2	9	4	18	8782	9.1	25		4182	4600	47.62	52.38
9	10	9	5	18	8782	9.1	26		4121	4661	46.93	53.07
6	10	9	4	17	8781	9.1	27		4185	4596	47.66	52.34
2	27	9	6	17	8774	9.09	28		4139	4635	47.17	52.83
9	17	9	5	17	8767	9.08	29		4232	4535	48.27	51.73
9	21	9	2	17	8766	9.08	30		4262	4504	48.62	51.38
12	4	9	6	17	8764	9.08	31		4189	4575	47.8	52.2
9	24	9	5	17	8759	9.07	32		4287	4472	48.94	51.06
5	27	9	4	18	8758	9.07	33		4021	4737	45.91	54.09
6	11	9	5	18	8756	9.07	34		4082	4674	46.62	53.38
9	3	9	5	18	8739	9.05	35		4151	4588	47.5	52.5
5	21	9	5	18	8734	9.05	36		4001	4733	45.81	54.19
6	1	9	2	17	8733	9.05	37		4147	4586	47.49	52.51
4	28	9	3	18	8727	9.04	38		3944	4783	45.19	54.81
1	9	9	6	17	8725	9.04	39		4116	4609	47.17	52.83
9	9	9	4	17	8724	9.04	40		4129	4595	47.33	52.67
6	2	9	3	18	8722	9.04	41	96528	3993	4729	45.78	54.22
9	23	9	4	17	8722	9.04	42		4265	4457	48.9	51.1
9	21	9	2	18	8719	9.03	43		4026	4693	46.18	53.82
6	10	9	4	18	8717	9.03	44		4067	4650	46.66	53.34
9	29	9	3	17	8717	9.03	45		4055	4662	46.52	53.48
11	3	9	3	17	8713	9.03	46		4137	4576	47.48	52.52
10	2	9	6	17	8710	9.02	47		4308	4402	49.46	50.54
1	30	9	6	17	8708	9.02	48		4266	4442	48.99	51.01
9	10	9	5	17	8706	9.02	49		4237	4469	48.67	51.33
9	23	9	4	18	8705	9.02	50		4155	4550	47.73	52.27
4	15	9	4	18	8699	9.01	51		4015	4684	46.15	53.85
10	27	9	3	17	8698	9.01	52		3994	4704	45.92	54.08
5	27	9	4	17	8697	9.01	53		4124	4573	47.42	52.58
10	6	9	3	17	8697	9.01	54		4077	4620	46.88	53.12
9	9	9	4	18	8695	9.01	55		4135	4560	47.56	52.44
5	20	9	4	17	8692	9	56		4069	4623	46.81	53.19
4	29	9	4	18	8691	9	57		3923	4768	45.14	54.86
11	4	9	4	18	8688	9	58		3964	4724	45.63	54.37
9	2	9	4	17	8683	9	59		4245	4438	48.89	51.11
6	2	9	3	17	8677	8.99	60		4034	4643	46.49	53.51
1	23	9	6	17	8676	8.99	61	96528	4178	4498	48.16	51.84
10	15	9	5	18	8673	8.98	62		3934	4739	45.36	54.64
10	27	9	3	18	8671	8.98	63		3926	4745	45.28	54.72
10	9	9	6	17	8670	8.98	64		4305	4365	49.65	50.35
9	28	9	2	17	8667	8.98	65		4244	4423	48.97	51.03
5	18	9	2	18	8665	8.98	66		4016	4649	46.35	53.65
9	8	9	3	18	8661	8.97	67		4133	4528	47.72	52.28
2	20	9	6	17	8660	8.97	68		4130	4530	47.69	52.31
7	15	9	4	17	8660	8.97	69		4313	4347	49.8	50.2

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
10	13	9	3	17	8659	8.97	70		4085	4574	47.18	52.82
6	5	9	6	17	8652	8.96	71		4250	4402	49.12	50.88
6	16	9	3	18	8650	8.96	72		3963	4687	45.82	54.18
12	1	9	3	17	8648	8.96	73		4056	4592	46.9	53.1
6	3	9	4	18	8644	8.95	74		3958	4686	45.79	54.21
5	15	9	6	17	8643	8.95	75		4139	4504	47.89	52.11
3	4	9	4	18	8638	8.95	76		3873	4765	44.84	55.16
5	7	9	5	17	8638	8.95	77		4114	4524	47.63	52.37
6	12	9	6	17	8637	8.95	78		4432	4205	51.31	48.69
4	24	9	6	17	8630	8.94	79		4078	4552	47.25	52.75
4	15	9	4	17	8626	8.94	80		4041	4585	46.85	53.15
10	5	9	2	18	8623	8.93	81	96528	3947	4676	45.77	54.23
6	12	9	6	16	8620	8.93	82		4341	4279	50.36	49.64
3	10	9	3	18	8618	8.93	83		3912	4706	45.39	54.61
12	22	9	3	17	8614	8.92	84		4057	4557	47.1	52.9
5	20	9	4	18	8612	8.92	85		3908	4704	45.38	54.62
4	30	9	5	17	8605	8.91	86		4134	4471	48.04	51.96
4	27	9	2	17	8602	8.91	87		4135	4467	48.07	51.93
5	19	9	3	18	8602	8.91	88		3867	4735	44.95	55.05
6	17	9	4	18	8602	8.91	89		4027	4575	46.81	53.19
1	14	9	4	17	8601	8.91	90		4103	4498	47.7	52.3
11	4	9	4	17	8601	8.91	91		4075	4526	47.38	52.62
7	15	9	4	18	8599	8.91	92		3993	4606	46.44	53.56
10	8	9	5	17	8592	8.9	93		4091	4501	47.61	52.39
4	30	9	5	18	8591	8.9	94		3947	4644	45.94	54.06
3	11	9	4	18	8589	8.9	95		3830	4759	44.59	55.41
10	30	9	6	17	8588	8.9	96		4139	4449	48.2	51.8
11	2	9	2	17	8588	8.9	97		4057	4531	47.24	52.76
5	6	9	4	18	8580	8.89	98		3899	4681	45.44	54.56
6	3	9	4	17	8579	8.89	99		4092	4487	47.7	52.3
10	21	9	4	18	8577	8.89	100		3830	4747	44.65	55.35
6	17	9	4	17	8576	8.88	101	96528	4028	4548	46.97	53.03
7	16	9	5	18	8576	8.88	102		3989	4587	46.51	53.49
2	3	9	3	17	8575	8.88	103		4031	4544	47.01	52.99
1	13	9	3	17	8573	8.88	104		3998	4575	46.63	53.37
5	21	9	5	17	8572	8.88	105		4062	4510	47.39	52.61
10	28	9	4	18	8572	8.88	106		3951	4621	46.09	53.91
6	15	9	2	17	8570	8.88	107		4137	4433	48.27	51.73
4	22	9	4	17	8568	8.88	108		3966	4602	46.29	53.71
10	1	9	5	17	8568	8.88	109		4032	4536	47.06	52.94
2	13	9	6	17	8566	8.87	110		4085	4481	47.69	52.31
5	11	9	2	18	8564	8.87	111		3894	4670	45.47	54.53
4	17	9	6	17	8563	8.87	112		4012	4551	46.85	53.15
11	24	9	3	17	8563	8.87	113		4017	4546	46.91	53.09
3	18	9	4	18	8562	8.87	114		3783	4779	44.18	55.82
2	12	9	5	17	8561	8.87	115		3973	4588	46.41	53.59
5	26	9	3	18	8560	8.87	116		3967	4593	46.34	53.66
2	4	9	4	17	8558	8.87	117		3964	4594	46.32	53.68
3	12	9	5	18	8558	8.87	118		3861	4697	45.12	54.88
9	25	9	6	16	8554	8.86	119		4274	4280	49.96	50.04
1	21	9	4	17	8551	8.86	120		4003	4548	46.81	53.19
5	12	9	3	18	8549	8.86	121	96528	3870	4679	45.27	54.73

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
6	5	9	6	16	8545	8.85	122		4181	4364	48.93	51.07
5	12	9	3	17	8543	8.85	123		3937	4606	46.08	53.92
10	5	9	2	17	8543	8.85	124		3998	4545	46.8	53.2
4	23	9	5	18	8542	8.85	125		3811	4731	44.61	55.39
7	14	9	3	18	8541	8.85	126		3932	4609	46.04	53.96
3	13	9	6	17	8539	8.85	127		4027	4512	47.16	52.84
5	8	9	6	16	8538	8.85	128		4203	4335	49.23	50.77
10	21	9	4	17	8538	8.85	129		4059	4479	47.54	52.46
12	10	9	5	17	8537	8.84	130		4101	4436	48.04	51.96
4	3	9	6	17	8536	8.84	131		3987	4549	46.71	53.29
2	19	9	5	18	8535	8.84	132		3834	4701	44.92	55.08
5	7	9	5	18	8533	8.84	133		3916	4617	45.89	54.11
6	18	9	5	17	8533	8.84	134		4120	4413	48.28	51.72
10	15	9	5	17	8533	8.84	135		3991	4542	46.77	53.23
9	16	9	4	17	8532	8.84	136		4218	4314	49.44	50.56
4	28	9	3	17	8530	8.84	137		3942	4588	46.21	53.79
6	23	9	3	17	8530	8.84	138		4085	4445	47.89	52.11
4	16	9	5	18	8529	8.84	139		3858	4671	45.23	54.77
6	8	9	2	17	8527	8.83	140		4036	4491	47.33	52.67
7	6	9	2	17	8525	8.83	141	96528	4121	4404	48.34	51.66
9	11	9	6	17	8525	8.83	142		4114	4411	48.26	51.74
1	16	9	6	17	8523	8.83	143		4167	4356	48.89	51.11
5	11	9	2	17	8522	8.83	144		4017	4505	47.14	52.86
5	29	9	6	17	8519	8.83	145		4170	4349	48.95	51.05
7	8	9	4	18	8519	8.83	146		4013	4506	47.11	52.89
10	7	9	4	18	8519	8.83	147		3868	4651	45.4	54.6
10	1	9	5	18	8517	8.82	148		4081	4436	47.92	52.08
5	5	9	3	17	8515	8.82	149		3928	4587	46.13	53.87
4	22	9	4	18	8513	8.82	150		3842	4671	45.13	54.87
12	2	9	4	18	8513	8.82	151		3907	4606	45.89	54.11
10	22	9	5	18	8512	8.82	152		3882	4630	45.61	54.39
12	1	9	3	18	8512	8.82	153		3927	4585	46.13	53.87
4	8	9	4	18	8510	8.82	154		3853	4657	45.28	54.72
9	14	9	2	17	8510	8.82	155		4086	4424	48.01	51.99
3	3	9	3	17	8508	8.81	156		3937	4571	46.27	53.73
5	1	9	6	17	8508	8.81	157		4063	4445	47.76	52.24
10	12	9	2	17	8507	8.81	158		4126	4381	48.5	51.5
12	18	9	6	16	8507	8.81	159		4171	4336	49.03	50.97
5	26	9	3	17	8506	8.81	160		4058	4448	47.71	52.29
4	27	9	2	18	8504	8.81	161	96528	3911	4593	45.99	54.01
5	1	9	6	16	8500	8.81	162		4105	4395	48.29	51.71
9	18	9	6	18	8500	8.81	163		4187	4313	49.26	50.74
3	31	9	3	17	8497	8.8	164		3929	4568	46.24	53.76
9	18	9	6	17	8497	8.8	165		4096	4401	48.21	51.79
12	11	9	6	17	8495	8.8	166		4057	4438	47.76	52.24
11	20	9	6	17	8494	8.8	167		4137	4357	48.7	51.3
12	21	9	2	17	8493	8.8	168		4065	4428	47.86	52.14
2	18	9	4	17	8491	8.8	169		3905	4586	45.99	54.01
5	15	9	6	18	8489	8.79	170		3996	4493	47.07	52.93
10	30	9	6	16	8487	8.79	171		4103	4384	48.34	51.66
7	7	9	3	17	8485	8.79	172		4098	4387	48.3	51.7
6	23	9	3	18	8484	8.79	173		4050	4434	47.74	52.26

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
12	23	9	4	17	8484	8.79	174		4142	4342	48.82	51.18
2	3	9	3	18	8483	8.79	175		3812	4671	44.94	55.06
6	24	9	4	17	8483	8.79	176		3965	4518	46.74	53.26
4	24	9	6	18	8477	8.78	177		3899	4578	46	54
4	2	9	5	18	8476	8.78	178		3852	4624	45.45	54.55
6	30	9	3	18	8475	8.78	179		3942	4533	46.51	53.49
2	27	9	6	16	8474	8.78	180		4127	4347	48.7	51.3
12	3	9	5	17	8474	8.78	181	96528	3969	4505	46.84	53.16
2	12	9	5	18	8472	8.78	182		3868	4604	45.66	54.34
5	19	9	3	17	8470	8.77	183		4006	4464	47.3	52.7
10	12	9	2	18	8469	8.77	184		3854	4615	45.51	54.49
12	4	9	6	16	8469	8.77	185		4238	4231	50.04	49.96
4	13	9	2	18	8468	8.77	186		3918	4550	46.27	53.73
9	28	9	2	18	8468	8.77	187		3977	4491	46.97	53.03
6	4	9	5	17	8467	8.77	188		3982	4485	47.03	52.97
9	25	9	6	18	8466	8.77	189		4100	4366	48.43	51.57
2	6	9	6	17	8465	8.77	190		4060	4405	47.96	52.04
4	21	9	3	18	8465	8.77	191		3884	4581	45.88	54.12
12	7	9	2	17	8464	8.77	192		3900	4564	46.08	53.92
7	1	9	4	17	8457	8.76	193		4003	4454	47.33	52.67
10	9	9	6	18	8456	8.76	194		4089	4367	48.36	51.64
7	7	9	3	18	8455	8.76	195		3877	4578	45.85	54.15
1	9	9	6	18	8453	8.76	196		4078	4375	48.24	51.76
5	15	9	6	16	8449	8.75	197		4122	4327	48.79	51.21
7	1	9	4	18	8449	8.75	198		3952	4497	46.77	53.23
3	24	9	3	18	8448	8.75	199		3889	4559	46.03	53.97
9	18	9	6	16	8447	8.75	200		4183	4264	49.52	50.48

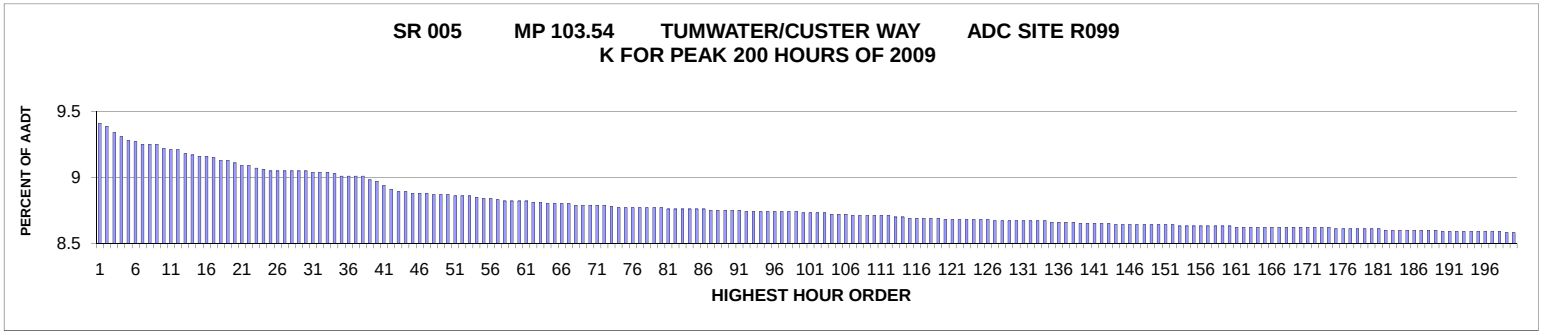

AADT= 95564 **K 30 FACTOR=** 9.05 **K 100 FACTOR=** 8.73 **K 200 FACTOR=** 8.58 **D FACTOR=** 51.35

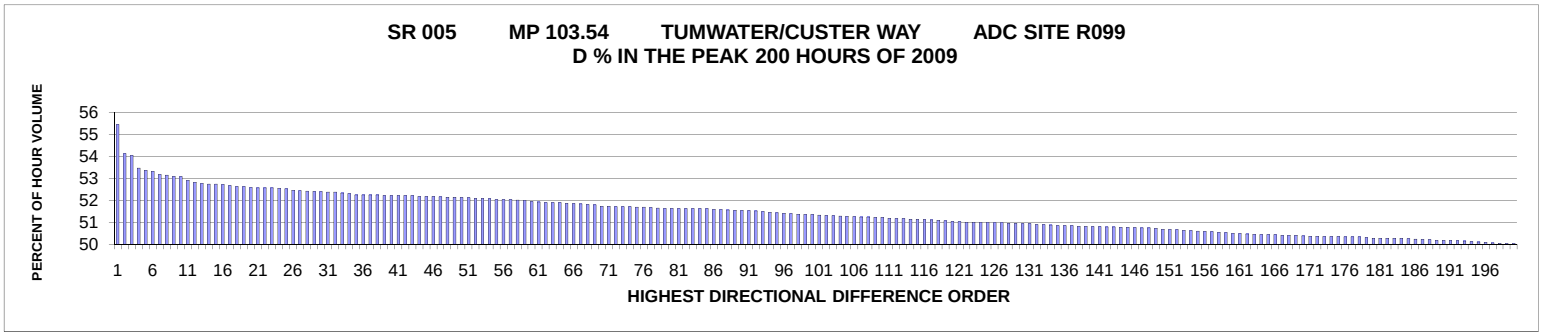

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
11	25	9	4	15	8996	9.41	1	95564	4235	4761	47.08	52.92
11	25	9	4	16	8973	9.39	2		4537	4436	50.56	49.44
8	14	9	6	17	8929	9.34	3		4610	4319	51.63	48.37
7	10	9	6	17	8895	9.31	4		4349	4546	48.89	51.11
8	7	9	6	17	8867	9.28	5		4521	4346	50.99	49.01
7	24	9	6	17	8856	9.27	6		4673	4183	52.77	47.23
6	12	9	6	17	8843	9.25	7		4234	4609	47.88	52.12
5	15	9	6	17	8842	9.25	8		4474	4368	50.6	49.4
6	12	9	6	16	8835	9.25	9		4388	4447	49.67	50.33
11	25	9	4	14	8810	9.22	10		4328	4482	49.13	50.87
4	3	9	6	17	8802	9.21	11		4323	4479	49.11	50.89
12	23	9	4	17	8798	9.21	12		4311	4487	49	51
6	18	9	5	17	8773	9.18	13		4385	4388	49.98	50.02
11	25	9	4	17	8765	9.17	14		4231	4534	48.27	51.73
11	25	9	4	13	8754	9.16	15		4243	4511	48.47	51.53
8	28	9	6	17	8753	9.16	16		4294	4459	49.06	50.94
2	13	9	6	17	8742	9.15	17		4229	4513	48.38	51.62

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	13	9	5	17	8726	9.13	18		4436	4290	50.84	49.16
4	10	9	6	17	8721	9.13	19		4224	4497	48.43	51.57
6	11	9	5	17	8703	9.11	20		4238	4465	48.7	51.3
4	17	9	6	17	8687	9.09	21	95564	4382	4305	50.44	49.56
6	19	9	6	17	8687	9.09	22		4237	4450	48.77	51.23
8	14	9	6	15	8672	9.07	23		4409	4263	50.84	49.16
10	2	9	6	17	8655	9.06	24		4126	4529	47.67	52.33
2	27	9	6	17	8653	9.05	25		4238	4415	48.98	51.02
8	14	9	6	16	8653	9.05	26		4477	4176	51.74	48.26
2	20	9	6	17	8649	9.05	27		4282	4367	49.51	50.49
6	19	9	6	15	8649	9.05	28		4334	4315	50.11	49.89
12	23	9	4	15	8646	9.05	29		4285	4361	49.56	50.44
9	3	9	5	17	8644	9.05	30		4230	4414	48.94	51.06
6	5	9	6	17	8639	9.04	31		4256	4383	49.26	50.74
7	23	9	5	17	8638	9.04	32		4281	4357	49.56	50.44
7	9	9	5	17	8637	9.04	33		4233	4404	49.01	50.99
9	25	9	6	17	8629	9.03	34		4079	4550	47.27	52.73
8	6	9	5	17	8615	9.01	35		4273	4342	49.6	50.4
1	16	9	6	17	8612	9.01	36		4089	4523	47.48	52.52
8	21	9	6	17	8610	9.01	37		4281	4329	49.72	50.28
8	28	9	6	16	8610	9.01	38		4236	4374	49.2	50.8
8	28	9	6	15	8582	8.98	39		4260	4322	49.64	50.36
6	26	9	6	16	8573	8.97	40		4310	4263	50.27	49.73
3	20	9	6	17	8547	8.94	41	95564	4135	4412	48.38	51.62
7	6	9	2	17	8513	8.91	42		4226	4287	49.64	50.36
3	6	9	6	18	8498	8.89	43		4226	4272	49.73	50.27
5	1	9	6	17	8498	8.89	44		4246	4252	49.96	50.04
8	21	9	6	16	8487	8.88	45		4230	4257	49.84	50.16
6	12	9	6	15	8486	8.88	46		4160	4326	49.02	50.98
5	8	9	6	17	8482	8.88	47		4040	4442	47.63	52.37
5	21	9	5	17	8474	8.87	48		4123	4351	48.65	51.35
6	17	9	4	17	8474	8.87	49		4158	4316	49.07	50.93
8	14	9	6	18	8474	8.87	50		4250	4224	50.15	49.85
3	13	9	6	17	8469	8.86	51		4126	4343	48.72	51.28
3	27	9	6	17	8468	8.86	52		4091	4377	48.31	51.69
4	10	9	6	18	8463	8.86	53		3882	4581	45.87	54.13
8	11	9	3	17	8462	8.85	54		4133	4329	48.84	51.16
7	13	9	2	17	8446	8.84	55		4128	4318	48.88	51.12
6	16	9	3	17	8445	8.84	56		4083	4362	48.35	51.65
4	16	9	5	17	8440	8.83	57		3999	4441	47.38	52.62
6	26	9	6	17	8433	8.82	58		4098	4335	48.59	51.41
10	15	9	5	17	8426	8.82	59		4032	4394	47.85	52.15
7	1	9	4	17	8424	8.82	60		4143	4281	49.18	50.82
8	31	9	2	17	8424	8.82	61	95564	4226	4198	50.17	49.83
7	17	9	6	16	8423	8.81	62		4275	4148	50.75	49.25
7	31	9	6	17	8417	8.81	63		4182	4235	49.69	50.31
3	20	9	6	18	8414	8.8	64		4102	4312	48.75	51.25
8	26	9	4	17	8414	8.8	65		4047	4367	48.1	51.9
7	16	9	5	17	8408	8.8	66		4126	4282	49.07	50.93
8	21	9	6	13	8407	8.8	67		4148	4259	49.34	50.66
2	13	9	6	18	8403	8.79	68		4058	4345	48.29	51.71
1	30	9	6	17	8402	8.79	69		4019	4383	47.83	52.17

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	8	9	4	17	8402	8.79	70		4134	4268	49.2	50.8
9	17	9	5	17	8401	8.79	71		4050	4351	48.21	51.79
6	10	9	4	17	8399	8.79	72		4113	4286	48.97	51.03
12	11	9	6	15	8388	8.78	73		4409	3979	52.56	47.44
9	4	9	6	15	8385	8.77	74		4005	4380	47.76	52.24
9	30	9	4	17	8384	8.77	75		4088	4296	48.76	51.24
3	27	9	6	16	8383	8.77	76		4061	4322	48.44	51.56
8	27	9	5	17	8383	8.77	77		4135	4248	49.33	50.67
7	31	9	6	16	8382	8.77	78		4205	4177	50.17	49.83
8	14	9	6	14	8382	8.77	79		4245	4137	50.64	49.36
10	9	9	6	16	8377	8.77	80		4020	4357	47.99	52.01
9	18	9	6	17	8376	8.76	81	95564	4192	4184	50.05	49.95
8	7	9	6	18	8374	8.76	82		4282	4092	51.13	48.87
8	7	9	6	15	8371	8.76	83		4134	4237	49.38	50.62
6	25	9	5	17	8368	8.76	84		4250	4118	50.79	49.21
9	18	9	6	15	8367	8.76	85		4152	4215	49.62	50.38
10	9	9	6	18	8367	8.76	86		3961	4406	47.34	52.66
6	5	9	6	18	8366	8.75	87		4040	4326	48.29	51.71
7	10	9	6	16	8365	8.75	88		4322	4043	51.67	48.33
4	30	9	5	17	8361	8.75	89		3993	4368	47.76	52.24
6	30	9	3	17	8358	8.75	90		4095	4263	48.99	51.01
7	24	9	6	13	8358	8.75	91		4150	4208	49.65	50.35
3	6	9	6	17	8357	8.74	92		4025	4332	48.16	51.84
6	11	9	5	18	8357	8.74	93		4145	4212	49.6	50.4
4	2	9	5	17	8354	8.74	94		4041	4313	48.37	51.63
4	3	9	6	18	8354	8.74	95		3985	4369	47.7	52.3
8	6	9	5	18	8350	8.74	96		4101	4249	49.11	50.89
8	14	9	6	13	8350	8.74	97		4194	4156	50.23	49.77
4	17	9	6	16	8348	8.74	98		4113	4235	49.27	50.73
8	25	9	3	17	8348	8.74	99		3969	4379	47.54	52.46
5	1	9	6	18	8347	8.73	100		3909	4438	46.83	53.17
10	30	9	6	16	8343	8.73	101	95564	3958	4385	47.44	52.56
9	9	9	4	17	8341	8.73	102		3997	4344	47.92	52.08
11	24	9	3	17	8339	8.73	103		4049	4290	48.55	51.45
10	2	9	6	16	8334	8.72	104		4001	4333	48.01	51.99
8	10	9	2	17	8330	8.72	105		4083	4247	49.02	50.98
10	8	9	5	17	8329	8.72	106		3980	4349	47.78	52.22
4	3	9	6	16	8328	8.71	107		4136	4192	49.66	50.34
9	15	9	3	17	8327	8.71	108		4014	4313	48.2	51.8
5	8	9	6	15	8326	8.71	109		3990	4336	47.92	52.08
3	19	9	5	17	8322	8.71	110		4000	4322	48.07	51.93
1	23	9	6	17	8321	8.71	111		3962	4359	47.61	52.39
5	7	9	5	17	8319	8.71	112		3959	4360	47.59	52.41
8	5	9	4	17	8314	8.7	113		4140	4174	49.8	50.2
7	24	9	6	14	8311	8.7	114		4185	4126	50.35	49.65
8	21	9	6	14	8309	8.69	115		4020	4289	48.38	51.62
9	24	9	5	17	8306	8.69	116		3973	4333	47.83	52.17
3	26	9	5	17	8304	8.69	117		4012	4292	48.31	51.69
10	16	9	6	17	8301	8.69	118		4025	4276	48.49	51.51
5	22	9	6	16	8300	8.69	119		4152	4148	50.02	49.98
9	11	9	6	17	8299	8.68	120		4105	4194	49.46	50.54
2	13	9	6	15	8298	8.68	121	95564	3869	4429	46.63	53.37

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
3	13	9	6	16	8298	8.68	122		4015	4283	48.39	51.61
7	31	9	6	15	8297	8.68	123		4213	4084	50.78	49.22
7	10	9	6	18	8296	8.68	124		3947	4349	47.58	52.42
10	9	9	6	17	8294	8.68	125		3886	4408	46.85	53.15
6	12	9	6	18	8291	8.68	126		3912	4379	47.18	52.82
3	27	9	6	15	8289	8.67	127		3976	4313	47.97	52.03
3	26	9	5	18	8288	8.67	128		3961	4327	47.79	52.21
8	20	9	5	18	8288	8.67	129		4116	4172	49.66	50.34
5	15	9	6	18	8287	8.67	130		4126	4161	49.79	50.21
5	21	9	5	18	8287	8.67	131		4026	4261	48.58	51.42
4	23	9	5	17	8286	8.67	132		3960	4326	47.79	52.21
7	31	9	6	14	8284	8.67	133		4128	4156	49.83	50.17
7	24	9	6	18	8282	8.67	134		4428	3854	53.47	46.53
6	19	9	6	18	8277	8.66	135		4060	4217	49.05	50.95
6	19	9	6	14	8275	8.66	136		4040	4235	48.82	51.18
9	25	9	6	16	8274	8.66	137		3953	4321	47.78	52.22
5	15	9	6	15	8273	8.66	138		4160	4113	50.28	49.72
12	18	9	6	16	8268	8.65	139		4007	4261	48.46	51.54
11	20	9	6	17	8265	8.65	140		3972	4293	48.06	51.94
5	15	9	6	16	8263	8.65	141	95564	4023	4240	48.69	51.31
10	30	9	6	17	8263	8.65	142		3905	4358	47.26	52.74
12	24	9	5	14	8263	8.65	143		3946	4317	47.76	52.24
8	14	9	6	12	8261	8.64	144		3945	4316	47.75	52.25
10	2	9	6	15	8260	8.64	145		3959	4301	47.93	52.07
6	19	9	6	16	8258	8.64	146		3916	4342	47.42	52.58
7	7	9	3	17	8258	8.64	147		4096	4162	49.6	50.4
10	1	9	5	17	8256	8.64	148		3927	4329	47.57	52.43
6	23	9	3	17	8255	8.64	149		3987	4268	48.3	51.7
8	26	9	4	18	8255	8.64	150		4090	4165	49.55	50.45
12	23	9	4	14	8255	8.64	151		4064	4191	49.23	50.77
5	8	9	6	18	8254	8.64	152		3950	4304	47.86	52.14
6	5	9	6	15	8247	8.63	153		3996	4251	48.45	51.55
9	4	9	6	17	8246	8.63	154		4062	4184	49.26	50.74
9	18	9	6	16	8246	8.63	155		3992	4254	48.41	51.59
7	23	9	5	18	8245	8.63	156		3989	4256	48.38	51.62
8	7	9	6	16	8245	8.63	157		3970	4275	48.15	51.85
8	12	9	4	18	8245	8.63	158		4075	4170	49.42	50.58
1	16	9	6	18	8244	8.63	159		3968	4276	48.13	51.87
8	12	9	4	17	8244	8.63	160		4093	4151	49.65	50.35
4	10	9	6	16	8242	8.62	161	95564	3954	4288	47.97	52.03
5	8	9	6	16	8242	8.62	162		4031	4211	48.91	51.09
6	24	9	4	17	8242	8.62	163		4099	4143	49.73	50.27
8	27	9	5	18	8241	8.62	164		4009	4232	48.65	51.35
12	24	9	5	13	8240	8.62	165		3867	4373	46.93	53.07
3	19	9	5	18	8239	8.62	166		3963	4276	48.1	51.9
5	1	9	6	16	8239	8.62	167		4111	4128	49.9	50.1
9	4	9	6	16	8237	8.62	168		4079	4158	49.52	50.48
6	4	9	5	17	8235	8.62	169		4051	4184	49.19	50.81
7	17	9	6	17	8235	8.62	170		4110	4125	49.91	50.09
9	10	9	5	17	8235	8.62	171		3961	4274	48.1	51.9
9	1	9	3	17	8233	8.62	172		4008	4225	48.68	51.32
10	23	9	6	17	8233	8.62	173		4159	4074	50.52	49.48

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
12	18	9	6	15	8233	8.62	174		4013	4220	48.74	51.26
5	27	9	4	17	8230	8.61	175		4013	4217	48.76	51.24
6	26	9	6	15	8230	8.61	176		4015	4215	48.78	51.22
7	15	9	4	17	8230	8.61	177		3948	4282	47.97	52.03
7	23	9	5	16	8230	8.61	178		4021	4209	48.86	51.14
7	10	9	6	13	8229	8.61	179		3941	4288	47.89	52.11
11	25	9	4	12	8229	8.61	180		3666	4563	44.55	55.45
3	18	9	4	17	8224	8.61	181	95564	3916	4308	47.62	52.38
11	6	9	6	17	8223	8.6	182		4016	4207	48.84	51.16
8	21	9	6	18	8222	8.6	183		3886	4336	47.26	52.74
9	22	9	3	17	8220	8.6	184		3928	4292	47.79	52.21
8	13	9	5	16	8219	8.6	185		3996	4223	48.62	51.38
3	27	9	6	18	8216	8.6	186		3898	4318	47.44	52.56
2	20	9	6	16	8215	8.6	187		3898	4317	47.45	52.55
12	22	9	3	17	8215	8.6	188		4070	4145	49.54	50.46
8	18	9	3	17	8214	8.6	189		4050	4164	49.31	50.69
7	9	9	5	18	8212	8.59	190		4036	4176	49.15	50.85
4	17	9	6	15	8211	8.59	191		3984	4227	48.52	51.48
7	10	9	6	14	8210	8.59	192		4085	4125	49.76	50.24
9	3	9	5	18	8210	8.59	193		3929	4281	47.86	52.14
4	3	9	6	15	8209	8.59	194		3992	4217	48.63	51.37
9	11	9	6	16	8209	8.59	195		3926	4283	47.83	52.17
3	12	9	5	17	8208	8.59	196		3850	4358	46.91	53.09
10	30	9	6	18	8207	8.59	197		3771	4436	45.95	54.05
8	28	9	6	18	8206	8.59	198		3830	4376	46.67	53.33
5	18	9	2	18	8203	8.58	199		4165	4038	50.77	49.23
9	2	9	4	17	8202	8.58	200		3886	4316	47.38	52.62

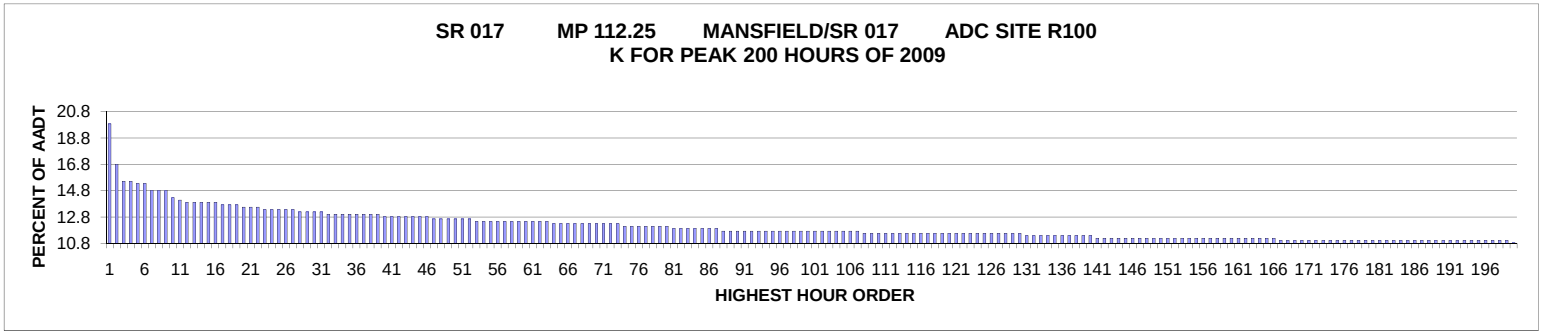

AADT= 554 **K 30 FACTOR=** 13.18 **K 100 FACTOR=** 11.73 **K 200 FACTOR=** 10.83 **D FACTOR=** 58.44

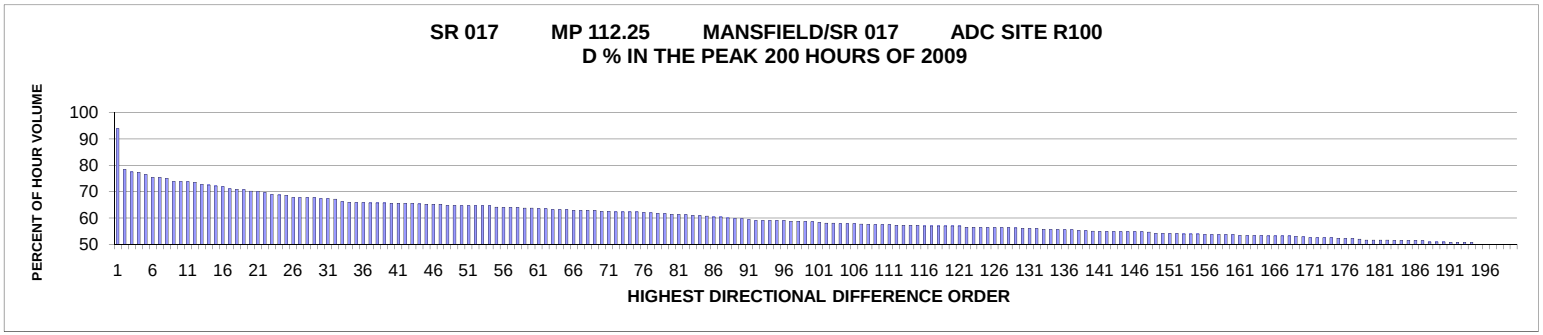

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	9	9	1	19	110	19.86	1	554	25	85	22.73	77.27
8	9	9	1	17	93	16.79	2		27	66	29.03	70.97
9	7	9	2	15	86	15.52	3		30	56	34.88	65.12
9	11	9	6	17	86	15.52	4		53	33	61.63	38.37
8	9	9	1	12	85	15.34	5		33	52	38.82	61.18
8	9	9	1	18	85	15.34	6		20	65	23.53	76.47
8	16	9	1	15	82	14.8	7		29	53	35.37	64.63
9	7	9	2	14	82	14.8	8		28	54	34.15	65.85
9	7	9	2	16	82	14.8	9		25	57	30.49	69.51
10	16	9	6	14	79	14.26	10		48	31	60.76	39.24
9	7	9	2	13	78	14.08	11		31	47	39.74	60.26
4	5	9	1	15	77	13.9	12		40	37	51.95	48.05
7	31	9	6	12	77	13.9	13		32	45	41.56	58.44
9	7	9	2	12	77	13.9	14		33	44	42.86	57.14
10	9	9	6	16	77	13.9	15		46	31	59.74	40.26
10	18	9	1	12	77	13.9	16		21	56	27.27	72.73
2	27	9	6	18	76	13.72	17		25	51	32.89	67.11

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	5	9	1	15	76	13.72	18		26	50	34.21	65.79
9	11	9	6	18	76	13.72	19		56	20	73.68	26.32
8	9	9	1	14	75	13.54	20		29	46	38.67	61.33
10	16	9	6	18	75	13.54	21	554	53	22	70.67	29.33
10	18	9	1	16	75	13.54	22		27	48	36	64
5	22	9	6	18	74	13.36	23		36	38	48.65	51.35
7	5	9	1	13	74	13.36	24		27	47	36.49	63.51
7	5	9	1	17	74	13.36	25		33	41	44.59	55.41
10	16	9	6	16	74	13.36	26		40	34	54.05	45.95
10	20	9	3	15	74	13.36	27		33	41	44.59	55.41
4	2	9	5	13	73	13.18	28		48	25	65.75	34.25
6	19	9	6	15	73	13.18	29		41	32	56.16	43.84
9	11	9	6	15	73	13.18	30		42	31	57.53	42.47
10	16	9	6	10	73	13.18	31		40	33	54.79	45.21
5	25	9	2	12	72	13	32		19	53	26.39	73.61
7	19	9	1	15	72	13	33		21	51	29.17	70.83
8	9	9	1	16	72	13	34		32	40	44.44	55.56
9	4	9	6	17	72	13	35		45	27	62.5	37.5
9	25	9	6	11	72	13	36		41	31	56.94	43.06
10	16	9	6	13	72	13	37		38	34	52.78	47.22
10	16	9	6	17	72	13	38		47	25	65.28	34.72
10	25	9	1	11	72	13	39		18	54	25	75
5	22	9	6	17	71	12.82	40		37	34	52.11	47.89
6	21	9	1	14	71	12.82	41	554	30	41	42.25	57.75
8	2	9	1	14	71	12.82	42		32	39	45.07	54.93
8	7	9	6	14	71	12.82	43		44	27	61.97	38.03
8	7	9	6	17	71	12.82	44		51	20	71.83	28.17
8	23	9	1	15	71	12.82	45		31	40	43.66	56.34
10	9	9	6	15	71	12.82	46		36	35	50.7	49.3
5	10	9	1	18	70	12.64	47		24	46	34.29	65.71
7	19	9	1	16	70	12.64	48		26	44	37.14	62.86
7	24	9	6	15	70	12.64	49		34	36	48.57	51.43
8	7	9	6	12	70	12.64	50		41	29	58.57	41.43
8	7	9	6	15	70	12.64	51		48	22	68.57	31.43
8	21	9	6	17	70	12.64	52		27	43	38.57	61.43
5	25	9	2	14	69	12.45	53		33	36	47.83	52.17
6	19	9	6	11	69	12.45	54		37	32	53.62	46.38
7	26	9	1	15	69	12.45	55		24	45	34.78	65.22
8	7	9	6	16	69	12.45	56		44	25	63.77	36.23
8	16	9	1	18	69	12.45	57		40	29	57.97	42.03
8	22	9	7	11	69	12.45	58		37	32	53.62	46.38
8	23	9	1	14	69	12.45	59		31	38	44.93	55.07
9	11	9	6	16	69	12.45	60		32	37	46.38	53.62
10	11	9	1	16	69	12.45	61	554	25	44	36.23	63.77
10	21	9	4	12	69	12.45	62		32	37	46.38	53.62
12	27	9	1	12	69	12.45	63		19	50	27.54	72.46
5	25	9	2	18	68	12.27	64		30	38	44.12	55.88
5	29	9	6	17	68	12.27	65		33	35	48.53	51.47
7	10	9	6	15	68	12.27	66		26	42	38.24	61.76
7	12	9	1	11	68	12.27	67		49	19	72.06	27.94
8	2	9	1	12	68	12.27	68		34	34	50	50
8	9	9	1	13	68	12.27	69		30	38	44.12	55.88

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	21	9	6	16	68	12.27	70		35	33	51.47	48.53
9	7	9	2	17	68	12.27	71		24	44	35.29	64.71
9	27	9	1	17	68	12.27	72		35	33	51.47	48.53
10	23	9	6	11	68	12.27	73		27	41	39.71	60.29
5	22	9	6	16	67	12.09	74		36	31	53.73	46.27
5	23	9	7	12	67	12.09	75		37	30	55.22	44.78
7	3	9	6	15	67	12.09	76		33	34	49.25	50.75
9	17	9	5	11	67	12.09	77		35	32	52.24	47.76
10	6	9	3	11	67	12.09	78		28	39	41.79	58.21
10	11	9	1	15	67	12.09	79		20	47	29.85	70.15
10	28	9	4	12	67	12.09	80		23	44	34.33	65.67
5	25	9	2	17	66	11.91	81	554	23	43	34.85	65.15
6	19	9	6	16	66	11.91	82		29	37	43.94	56.06
8	13	9	5	15	66	11.91	83		32	34	48.48	51.52
9	4	9	6	13	66	11.91	84		33	33	50	50
10	1	9	5	17	66	11.91	85		31	35	46.97	53.03
10	16	9	6	12	66	11.91	86		28	38	42.42	57.58
12	26	9	7	14	66	11.91	87		30	36	45.45	54.55
2	27	9	6	23	65	11.73	88		61	4	93.85	6.15
4	7	9	3	11	65	11.73	89		48	17	73.85	26.15
4	9	9	5	14	65	11.73	90		30	35	46.15	53.85
4	17	9	6	18	65	11.73	91		37	28	56.92	43.08
5	25	9	2	13	65	11.73	92		17	48	26.15	73.85
6	28	9	1	12	65	11.73	93		24	41	36.92	63.08
7	10	9	6	11	65	11.73	94		32	33	49.23	50.77
7	10	9	6	12	65	11.73	95		23	42	35.38	64.62
7	10	9	6	14	65	11.73	96		28	37	43.08	56.92
7	12	9	1	14	65	11.73	97		14	51	21.54	78.46
8	3	9	2	13	65	11.73	98		30	35	46.15	53.85
8	13	9	5	11	65	11.73	99		30	35	46.15	53.85
9	4	9	6	15	65	11.73	100		33	32	50.77	49.23
10	2	9	6	16	65	11.73	101	554	37	28	56.92	43.08
10	9	9	6	17	65	11.73	102		41	24	63.08	36.92
10	10	9	7	12	65	11.73	103		37	28	56.92	43.08
10	16	9	6	15	65	11.73	104		39	26	60	40
10	22	9	5	16	65	11.73	105		23	42	35.38	64.62
10	23	9	6	12	65	11.73	106		28	37	43.08	56.92
10	25	9	1	16	65	11.73	107		24	41	36.92	63.08
4	9	9	5	10	64	11.55	108		34	30	53.13	46.88
5	15	9	6	18	64	11.55	109		35	29	54.69	45.31
6	5	9	6	18	64	11.55	110		36	28	56.25	43.75
6	19	9	6	12	64	11.55	111		30	34	46.88	53.13
6	19	9	6	18	64	11.55	112		37	27	57.81	42.19
6	21	9	1	16	64	11.55	113		29	35	45.31	54.69
7	2	9	5	16	64	11.55	114		37	27	57.81	42.19
7	2	9	5	18	64	11.55	115		30	34	46.88	53.13
7	18	9	7	13	64	11.55	116		30	34	46.88	53.13
8	14	9	6	12	64	11.55	117		31	33	48.44	51.56
8	16	9	1	17	64	11.55	118		36	28	56.25	43.75
8	26	9	4	12	64	11.55	119		29	35	45.31	54.69
9	18	9	6	18	64	11.55	120		36	28	56.25	43.75
9	19	9	7	13	64	11.55	121	554	28	36	43.75	56.25

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
9	20	9	1	17	64	11.55	122		25	39	39.06	60.94
9	22	9	3	15	64	11.55	123		32	32	50	50
9	25	9	6	17	64	11.55	124		40	24	62.5	37.5
10	3	9	7	9	64	11.55	125		26	38	40.63	59.38
10	15	9	5	16	64	11.55	126		29	35	45.31	54.69
10	16	9	6	11	64	11.55	127		32	32	50	50
10	21	9	4	11	64	11.55	128		23	41	35.94	64.06
10	23	9	6	14	64	11.55	129		20	44	31.25	68.75
10	30	9	6	11	64	11.55	130		22	42	34.38	65.63
3	27	9	6	18	63	11.37	131		39	24	61.9	38.1
4	4	9	7	11	63	11.37	132		37	26	58.73	41.27
5	22	9	6	19	63	11.37	133		30	33	47.62	52.38
5	23	9	7	10	63	11.37	134		36	27	57.14	42.86
6	26	9	6	13	63	11.37	135		27	36	42.86	57.14
7	16	9	5	18	63	11.37	136		37	26	58.73	41.27
7	17	9	6	15	63	11.37	137		34	29	53.97	46.03
9	5	9	7	14	63	11.37	138		28	35	44.44	55.56
11	1	9	1	16	63	11.37	139		23	40	36.51	63.49
11	25	9	4	14	63	11.37	140		27	36	42.86	57.14
3	27	9	6	16	62	11.19	141	554	37	25	59.68	40.32
3	28	9	7	14	62	11.19	142		40	22	64.52	35.48
5	15	9	6	16	62	11.19	143		33	29	53.23	46.77
5	29	9	6	16	62	11.19	144		29	33	46.77	53.23
6	21	9	1	12	62	11.19	145		22	40	35.48	64.52
6	21	9	1	17	62	11.19	146		32	30	51.61	48.39
6	28	9	1	15	62	11.19	147		32	30	51.61	48.39
6	28	9	1	17	62	11.19	148		28	34	45.16	54.84
6	28	9	1	18	62	11.19	149		33	29	53.23	46.77
7	3	9	6	12	62	11.19	150		41	21	66.13	33.87
7	5	9	1	14	62	11.19	151		27	35	43.55	56.45
7	6	9	2	11	62	11.19	152		26	36	41.94	58.06
7	6	9	2	12	62	11.19	153		22	40	35.48	64.52
8	6	9	5	14	62	11.19	154		33	29	53.23	46.77
8	9	9	1	11	62	11.19	155		23	39	37.1	62.9
8	13	9	5	13	62	11.19	156		27	35	43.55	56.45
8	21	9	6	12	62	11.19	157		31	31	50	50
9	4	9	6	18	62	11.19	158		42	20	67.74	32.26
9	17	9	5	17	62	11.19	159		20	42	32.26	67.74
9	25	9	6	16	62	11.19	160		42	20	67.74	32.26
10	3	9	7	11	62	11.19	161	554	39	23	62.9	37.1
10	15	9	5	12	62	11.19	162		28	34	45.16	54.84
10	25	9	1	13	62	11.19	163		14	48	22.58	77.42
10	26	9	2	16	62	11.19	164		23	39	37.1	62.9
11	25	9	4	16	62	11.19	165		31	31	50	50
11	28	9	7	12	62	11.19	166		20	42	32.26	67.74
3	27	9	6	12	61	11.01	167		46	15	75.41	24.59
4	9	9	5	15	61	11.01	168		38	23	62.3	37.7
4	18	9	7	13	61	11.01	169		36	25	59.02	40.98
5	8	9	6	16	61	11.01	170		36	25	59.02	40.98
5	21	9	5	18	61	11.01	171		39	22	63.93	36.07
5	22	9	6	14	61	11.01	172		26	35	42.62	57.38
5	22	9	6	15	61	11.01	173		36	25	59.02	40.98

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
5	26	9	3	11	61	11.01	174		35	26	57.38	42.62
6	12	9	6	17	61	11.01	175		32	29	52.46	47.54
7	2	9	5	11	61	11.01	176		33	28	54.1	45.9
7	3	9	6	13	61	11.01	177		37	24	60.66	39.34
7	10	9	6	13	61	11.01	178		31	30	50.82	49.18
7	12	9	1	13	61	11.01	179		15	46	24.59	75.41
7	12	9	1	17	61	11.01	180		27	34	44.26	55.74
7	31	9	6	13	61	11.01	181	554	20	41	32.79	67.21
8	8	9	7	13	61	11.01	182		31	30	50.82	49.18
8	12	9	4	12	61	11.01	183		26	35	42.62	57.38
8	13	9	5	16	61	11.01	184		32	29	52.46	47.54
8	16	9	1	16	61	11.01	185		23	38	37.7	62.3
8	22	9	7	17	61	11.01	186		40	21	65.57	34.43
9	4	9	6	14	61	11.01	187		23	38	37.7	62.3
9	13	9	1	16	61	11.01	188		29	32	47.54	52.46
9	20	9	1	13	61	11.01	189		30	31	49.18	50.82
9	30	9	4	17	61	11.01	190		21	40	34.43	65.57
10	15	9	5	14	61	11.01	191		21	40	34.43	65.57
10	15	9	5	15	61	11.01	192		33	28	54.1	45.9
10	19	9	2	14	61	11.01	193		22	39	36.07	63.93
10	21	9	4	13	61	11.01	194		25	36	40.98	59.02
10	25	9	1	14	61	11.01	195		19	42	31.15	68.85
10	28	9	4	13	61	11.01	196		21	40	34.43	65.57
10	29	9	5	11	61	11.01	197		25	36	40.98	59.02
10	30	9	6	12	61	11.01	198		20	41	32.79	67.21
11	25	9	4	15	61	11.01	199		23	38	37.7	62.3
4	7	9	3	10	60	10.83	200		42	18	70	30

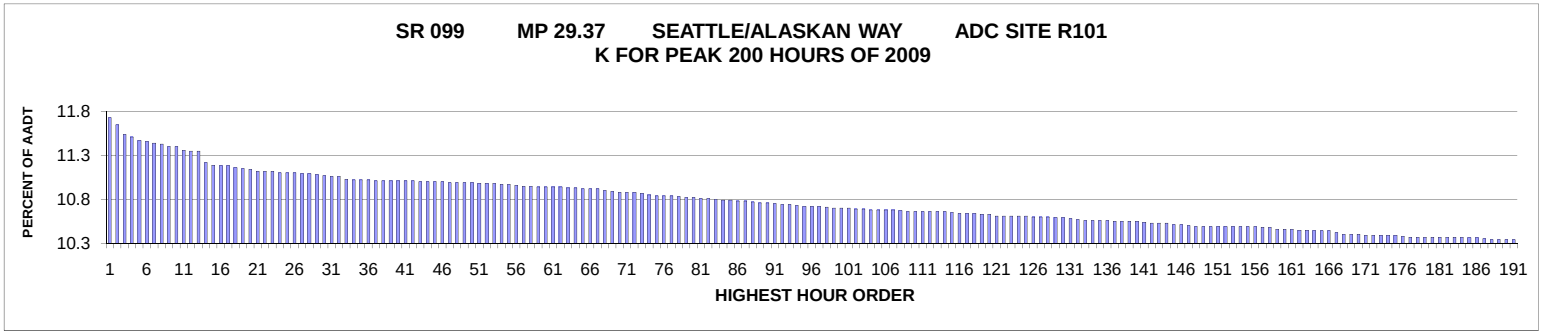

AADT= 73176 **K 30 FACTOR=** 11.07 **K 100 FACTOR=** 10.75 **K 200 FACTOR=** 10.34 **D FACTOR=** 53.84

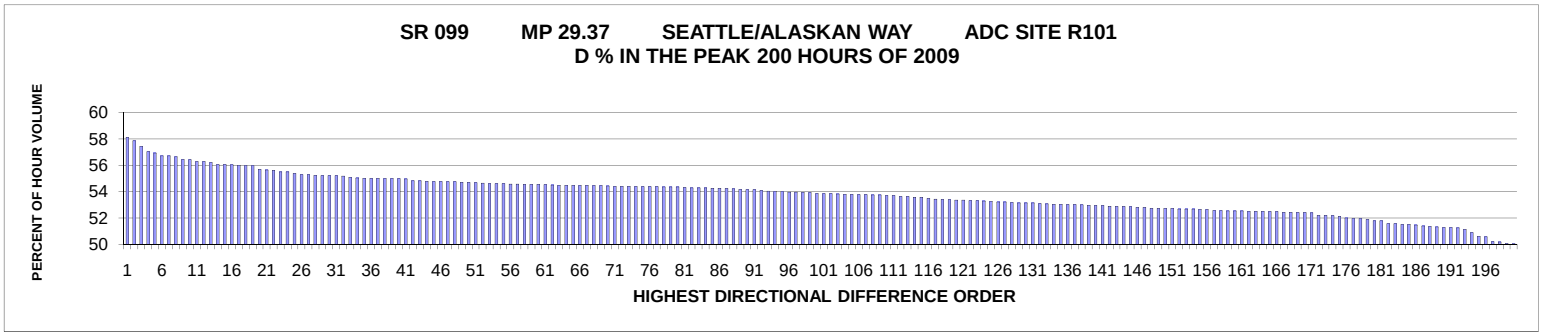

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	14	9	3	18	8585	11.73	1	73176	4018	4567	46.8	53.2
6	11	9	5	17	8527	11.65	2		4146	4381	48.62	51.38
7	16	9	5	18	8447	11.54	3		3847	4600	45.54	54.46
5	21	9	5	18	8424	11.51	4		3974	4450	47.17	52.83
6	4	9	5	18	8390	11.47	5		3980	4410	47.44	52.56
6	18	9	5	18	8387	11.46	6		3872	4515	46.17	53.83
12	16	9	4	18	8374	11.44	7		4057	4317	48.45	51.55
6	16	9	3	18	8366	11.43	8		4087	4279	48.85	51.15
9	10	9	5	18	8344	11.4	9		3789	4555	45.41	54.59
7	9	9	5	18	8342	11.4	10		3945	4397	47.29	52.71
5	15	9	6	17	8315	11.36	11		3843	4472	46.22	53.78
7	30	9	5	17	8306	11.35	12		4139	4167	49.83	50.17
5	14	9	5	18	8305	11.35	13		3722	4583	44.82	55.18
4	23	9	5	18	8208	11.22	14		3796	4412	46.25	53.75
6	10	9	4	18	8186	11.19	15		3685	4501	45.02	54.98
9	15	9	3	18	8178	11.18	16		3962	4216	48.45	51.55
12	1	9	3	18	8178	11.18	17		3740	4438	45.73	54.27

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
6	4	9	5	17	8166	11.16	18		3727	4439	45.64	54.36
5	20	9	4	18	8157	11.15	19		3778	4379	46.32	53.68
7	9	9	5	17	8153	11.14	20		3822	4331	46.88	53.12
6	10	9	4	17	8135	11.12	21	73176	3816	4319	46.91	53.09
7	15	9	4	18	8135	11.12	22		3832	4303	47.11	52.89
9	22	9	3	18	8134	11.12	23		3910	4224	48.07	51.93
7	23	9	5	18	8124	11.1	24		3772	4352	46.43	53.57
7	31	9	6	17	8122	11.1	25		3757	4365	46.26	53.74
5	1	9	6	17	8121	11.1	26		3821	4300	47.05	52.95
8	6	9	5	18	8115	11.09	27		3819	4296	47.06	52.94
5	21	9	5	17	8112	11.09	28		3696	4416	45.56	54.44
9	24	9	5	18	8108	11.08	29		3728	4380	45.98	54.02
12	15	9	3	18	8104	11.07	30		3951	4153	48.75	51.25
5	28	9	5	17	8094	11.06	31		3681	4413	45.48	54.52
6	24	9	4	17	8092	11.06	32		3677	4415	45.44	54.56
12	17	9	5	18	8068	11.03	33		4078	3990	50.55	49.45
5	26	9	3	18	8064	11.02	34		3491	4573	43.29	56.71
6	11	9	5	18	8063	11.02	35		3631	4432	45.03	54.97
7	22	9	4	17	8062	11.02	36		3818	4244	47.36	52.64
5	7	9	5	17	8059	11.01	37		3670	4389	45.54	54.46
5	6	9	4	18	8058	11.01	38		3648	4410	45.27	54.73
11	18	9	4	18	8057	11.01	39		3908	4149	48.5	51.5
7	10	9	6	17	8056	11.01	40		3777	4279	46.88	53.12
8	27	9	5	18	8055	11.01	41	73176	3705	4350	46	54
5	28	9	5	18	8054	11.01	42		3609	4445	44.81	55.19
9	11	9	6	17	8052	11	43		3812	4240	47.34	52.66
6	24	9	4	18	8050	11	44		3675	4375	45.65	54.35
7	22	9	4	18	8047	11	45		3737	4310	46.44	53.56
4	23	9	5	17	8046	11	46		3543	4503	44.03	55.97
12	10	9	5	17	8043	10.99	47		3846	4197	47.82	52.18
7	17	9	6	17	8040	10.99	48		3817	4223	47.48	52.52
7	23	9	5	17	8039	10.99	49		3701	4338	46.04	53.96
9	24	9	5	17	8039	10.99	50		3683	4356	45.81	54.19
5	8	9	6	17	8038	10.98	51		3850	4188	47.9	52.1
6	5	9	6	17	8037	10.98	52		3666	4371	45.61	54.39
6	17	9	4	17	8034	10.98	53		3875	4159	48.23	51.77
8	13	9	5	17	8031	10.97	54		3823	4208	47.6	52.4
8	11	9	3	18	8028	10.97	55		3712	4316	46.24	53.76
8	5	9	4	18	8021	10.96	56		4011	4010	50.01	49.99
8	19	9	4	17	8015	10.95	57		3718	4297	46.39	53.61
12	4	9	6	18	8012	10.95	58		3788	4224	47.28	52.72
6	17	9	4	18	8009	10.94	59		3689	4320	46.06	53.94
5	29	9	6	17	8007	10.94	60		3552	4455	44.36	55.64
12	4	9	6	17	8005	10.94	61	73176	3933	4072	49.13	50.87
12	2	9	4	18	8003	10.94	62		3799	4204	47.47	52.53
7	15	9	4	17	7997	10.93	63		3798	4199	47.49	52.51
7	21	9	3	18	7996	10.93	64		3621	4375	45.29	54.71
5	19	9	3	18	7993	10.92	65		3581	4412	44.8	55.2
6	30	9	3	18	7992	10.92	66		3691	4301	46.18	53.82
7	14	9	3	17	7989	10.92	67		3630	4359	45.44	54.56
6	23	9	3	17	7975	10.9	68		3645	4330	45.71	54.29
7	16	9	5	17	7971	10.89	69		3763	4208	47.21	52.79

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
5	14	9	5	17	7963	10.88	70		3562	4401	44.73	55.27
8	12	9	4	18	7963	10.88	71		3785	4178	47.53	52.47
8	20	9	5	17	7963	10.88	72		3739	4224	46.95	53.05
10	15	9	5	18	7952	10.87	73		3767	4185	47.37	52.63
11	12	9	5	18	7943	10.85	74		3617	4326	45.54	54.46
5	20	9	4	17	7933	10.84	75		3696	4237	46.59	53.41
3	12	9	5	18	7931	10.84	76		3493	4438	44.04	55.96
4	30	9	5	17	7929	10.84	77		3618	4311	45.63	54.37
4	21	9	3	18	7924	10.83	78		3484	4440	43.97	56.03
5	27	9	4	18	7921	10.82	79		3583	4338	45.23	54.77
6	12	9	6	18	7914	10.82	80		3450	4464	43.59	56.41
8	19	9	4	18	7913	10.81	81	73176	3609	4304	45.61	54.39
5	15	9	6	18	7907	10.81	82		3761	4146	47.57	52.43
12	3	9	5	17	7902	10.8	83		3811	4091	48.23	51.77
4	1	9	4	18	7894	10.79	84		3574	4320	45.27	54.73
12	17	9	5	17	7893	10.79	85		3995	3898	50.61	49.39
5	12	9	3	18	7886	10.78	86		3598	4288	45.63	54.37
8	20	9	5	18	7886	10.78	87		3677	4209	46.63	53.37
7	1	9	4	17	7880	10.77	88		3705	4175	47.02	52.98
9	16	9	4	18	7875	10.76	89		3601	4274	45.73	54.27
11	12	9	5	17	7874	10.76	90		3568	4306	45.31	54.69
9	23	9	4	18	7865	10.75	91		3718	4147	47.27	52.73
12	9	9	4	18	7862	10.74	92		3827	4035	48.68	51.32
6	23	9	3	18	7859	10.74	93		3619	4240	46.05	53.95
8	18	9	3	18	7851	10.73	94		3585	4266	45.66	54.34
9	18	9	6	17	7843	10.72	95		3632	4211	46.31	53.69
4	16	9	5	18	7842	10.72	96		3580	4262	45.65	54.35
9	1	9	3	18	7842	10.72	97		3685	4157	46.99	53.01
8	25	9	3	18	7838	10.71	98		3772	4066	48.12	51.88
7	2	9	5	17	7831	10.7	99		3524	4307	45	55
8	5	9	4	17	7831	10.7	100		3810	4021	48.65	51.35
8	27	9	5	17	7830	10.7	101	73176	3657	4173	46.7	53.3
9	17	9	5	18	7821	10.69	102		3604	4217	46.08	53.92
10	8	9	5	17	7821	10.69	103		3711	4110	47.45	52.55
10	23	9	6	17	7816	10.68	104		3699	4117	47.33	52.67
11	19	9	5	17	7816	10.68	105		3790	4026	48.49	51.51
6	19	9	6	17	7814	10.68	106		3678	4136	47.07	52.93
11	5	9	5	17	7813	10.68	107		3710	4103	47.48	52.52
9	1	9	3	17	7807	10.67	108		3749	4058	48.02	51.98
4	9	9	5	18	7803	10.66	109		3321	4482	42.56	57.44
12	3	9	5	18	7803	10.66	110		3684	4119	47.21	52.79
5	7	9	5	18	7802	10.66	111		3360	4442	43.07	56.93
9	30	9	4	18	7800	10.66	112		3524	4276	45.18	54.82
6	26	9	6	17	7798	10.66	113		3513	4285	45.05	54.95
9	15	9	3	17	7798	10.66	114		3786	4012	48.55	51.45
3	13	9	6	17	7790	10.65	115		3507	4283	45.02	54.98
6	3	9	4	17	7788	10.64	116		3637	4151	46.7	53.3
10	15	9	5	17	7784	10.64	117		3698	4086	47.51	52.49
12	9	9	4	17	7783	10.64	118		3648	4135	46.87	53.13
6	30	9	3	17	7780	10.63	119		3447	4333	44.31	55.69
10	7	9	4	18	7775	10.63	120		3652	4123	46.97	53.03
9	16	9	4	17	7766	10.61	121	73176	3624	4142	46.66	53.34

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	8	9	4	18	7762	10.61	122		3896	3866	50.19	49.81
3	11	9	4	18	7761	10.61	123		3463	4298	44.62	55.38
4	21	9	3	17	7761	10.61	124		3366	4395	43.37	56.63
9	2	9	4	18	7761	10.61	125		3538	4223	45.59	54.41
3	18	9	4	18	7759	10.6	126		3558	4201	45.86	54.14
10	8	9	5	18	7759	10.6	127		3685	4074	47.49	52.51
10	9	9	6	17	7755	10.6	128		3547	4208	45.74	54.26
10	21	9	4	18	7751	10.59	129		3688	4063	47.58	52.42
10	22	9	5	18	7749	10.59	130		3577	4172	46.16	53.84
7	7	9	3	18	7740	10.58	131		3263	4477	42.16	57.84
4	30	9	5	18	7736	10.57	132		3717	4019	48.05	51.95
5	19	9	3	17	7728	10.56	133		3518	4210	45.52	54.48
10	1	9	5	17	7727	10.56	134		3616	4111	46.8	53.2
4	16	9	5	17	7726	10.56	135		3460	4266	44.78	55.22
5	18	9	2	18	7725	10.56	136		3429	4296	44.39	55.61
6	2	9	3	18	7723	10.55	137		3523	4200	45.62	54.38
6	2	9	3	17	7722	10.55	138		3692	4030	47.81	52.19
11	4	9	4	18	7722	10.55	139		3610	4112	46.75	53.25
9	9	9	4	18	7721	10.55	140		3530	4191	45.72	54.28
9	25	9	6	17	7711	10.54	141	73176	3536	4175	45.86	54.14
8	6	9	5	17	7707	10.53	142		3686	4021	47.83	52.17
8	12	9	4	17	7707	10.53	143		3622	4085	47	53
11	20	9	6	17	7705	10.53	144		3669	4036	47.62	52.38
9	2	9	4	17	7693	10.51	145		3460	4233	44.98	55.02
12	8	9	3	18	7688	10.51	146		3530	4158	45.92	54.08
9	8	9	3	18	7682	10.5	147		3483	4199	45.34	54.66
12	10	9	5	18	7679	10.49	148		3520	4159	45.84	54.16
8	18	9	3	17	7677	10.49	149		3495	4182	45.53	54.47
5	5	9	3	18	7676	10.49	150		3471	4205	45.22	54.78
8	11	9	3	17	7676	10.49	151		3630	4046	47.29	52.71
11	5	9	5	18	7676	10.49	152		3741	3935	48.74	51.26
10	28	9	4	18	7675	10.49	153		3488	4187	45.45	54.55
4	17	9	6	17	7674	10.49	154		3548	4126	46.23	53.77
10	14	9	4	18	7674	10.49	155		3439	4235	44.81	55.19
6	12	9	6	17	7673	10.49	156		3616	4057	47.13	52.87
11	30	9	2	18	7671	10.48	157		3431	4240	44.73	55.27
12	2	9	4	17	7669	10.48	158		3601	4068	46.96	53.04
6	16	9	3	17	7656	10.46	159		3552	4104	46.39	53.61
7	28	9	3	17	7653	10.46	160		3444	4209	45	55
7	1	9	4	18	7651	10.46	161	73176	3532	4119	46.16	53.84
4	15	9	4	17	7646	10.45	162		3476	4170	45.46	54.54
4	28	9	3	18	7645	10.45	163		3402	4243	44.5	55.5
3	4	9	4	18	7643	10.44	164		3498	4145	45.77	54.23
5	13	9	4	17	7642	10.44	165		3726	3916	48.76	51.24
4	22	9	4	18	7638	10.44	166		3432	4206	44.93	55.07
9	22	9	3	17	7627	10.42	167		3573	4054	46.85	53.15
5	13	9	4	18	7612	10.4	168		3271	4341	42.97	57.03
11	18	9	4	17	7610	10.4	169		3602	4008	47.33	52.67
5	26	9	3	17	7609	10.4	170		3456	4153	45.42	54.58
3	6	9	6	17	7605	10.39	171		3346	4259	44	56
4	24	9	6	17	7603	10.39	172		3546	4057	46.64	53.36
6	15	9	2	17	7602	10.39	173		3342	4260	43.96	56.04

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	21	9	3	17	7600	10.39	174		3582	4018	47.13	52.87
12	11	9	6	17	7600	10.39	175		3797	3803	49.96	50.04
12	22	9	3	17	7599	10.38	176		3461	4138	45.55	54.45
8	14	9	6	17	7592	10.37	177		3546	4046	46.71	53.29
3	26	9	5	18	7591	10.37	178		3472	4119	45.74	54.26
10	7	9	4	17	7590	10.37	179		3461	4129	45.6	54.4
11	3	9	3	18	7589	10.37	180		3443	4146	45.37	54.63
3	12	9	5	17	7586	10.37	181	73176	3333	4253	43.94	56.06
4	24	9	6	18	7586	10.37	182		3177	4409	41.88	58.12
9	30	9	4	17	7586	10.37	183		3506	4080	46.22	53.78
10	13	9	3	18	7586	10.37	184		3533	4053	46.57	53.43
3	5	9	5	18	7580	10.36	185		3429	4151	45.24	54.76
10	5	9	2	18	7578	10.36	186		3441	4137	45.41	54.59
9	3	9	5	17	7571	10.35	187		3603	3968	47.59	52.41
6	19	9	6	18	7570	10.34	188		3441	4129	45.46	54.54
10	2	9	6	17	7569	10.34	189		3444	4125	45.5	54.5
6	3	9	4	18	7568	10.34	190		3276	4292	43.29	56.71
11	13	9	6	17	7566	10.34	191		3596	3970	47.53	52.47
7	7	9	3	17	7562	10.33	192		3293	4269	43.55	56.45
4	29	9	4	18	7560	10.33	193		3307	4253	43.74	56.26

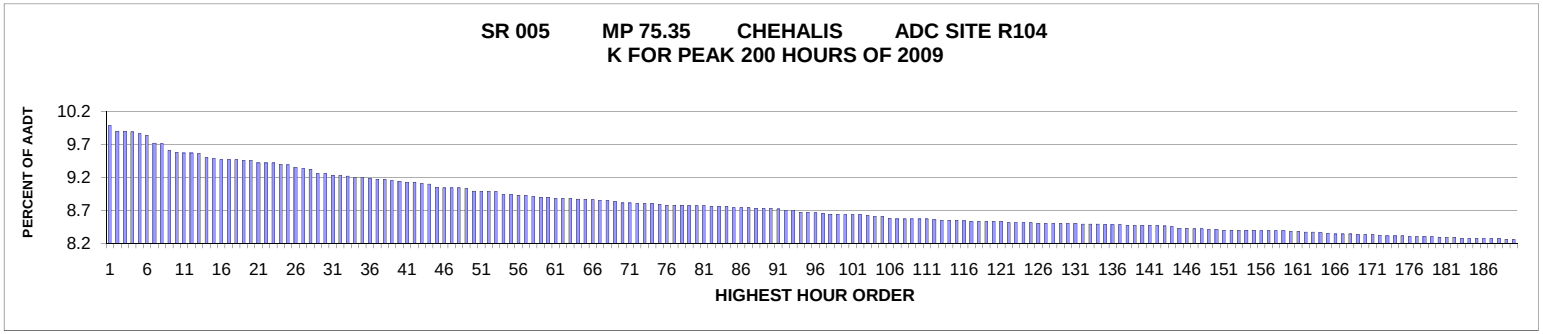

AADT= 59548 **K 30 FACTOR=** 9.46 **K 100 FACTOR=** 8.73 **K 200 FACTOR=** 8.26 **D FACTOR=** 52.87

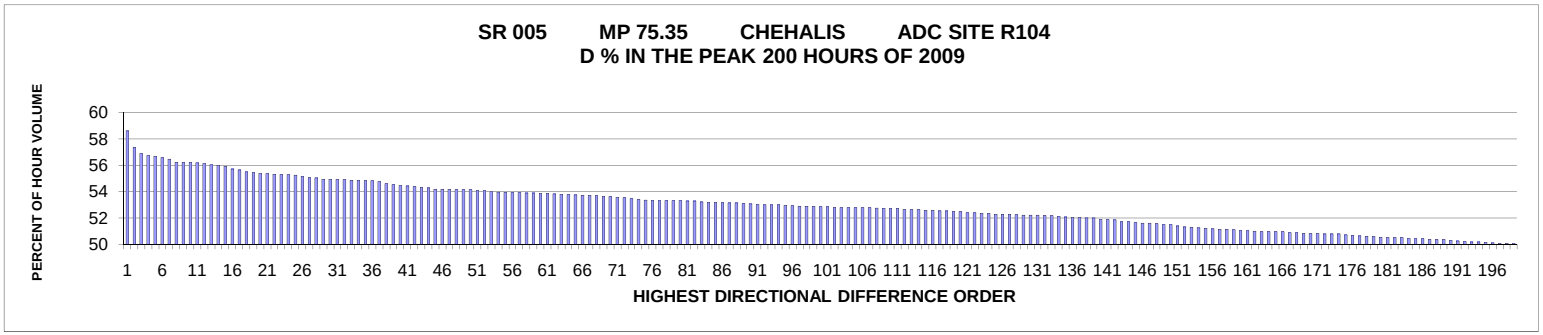

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
7	5	9	1	14	5986	10.05	1	59548	3103	2883	51.84	48.16
7	5	9	1	15	5948	9.99	2		3004	2944	50.5	49.5
7	3	9	6	12	5897	9.9	3		3083	2814	52.28	47.72
7	10	9	6	15	5896	9.9	4		2876	3020	48.78	51.22
7	5	9	1	16	5891	9.89	5		3007	2884	51.04	48.96
7	5	9	1	13	5872	9.86	6		3089	2783	52.61	47.39
7	3	9	6	15	5860	9.84	7		3098	2762	52.87	47.13
9	4	9	6	15	5788	9.72	8		2655	3133	45.87	54.13
7	3	9	6	14	5784	9.71	9		2951	2833	51.02	48.98
7	10	9	6	14	5720	9.61	10		2743	2977	47.95	52.05
12	26	9	7	14	5706	9.58	11		2892	2814	50.68	49.32
9	4	9	6	14	5699	9.57	12		2715	2984	47.64	52.36
6	26	9	6	14	5698	9.57	13		2612	3086	45.84	54.16
9	4	9	6	16	5691	9.56	14		2670	3021	46.92	53.08
9	18	9	6	16	5658	9.5	15		2668	2990	47.15	52.85
6	12	9	6	16	5650	9.49	16		2791	2859	49.4	50.6
9	5	9	7	12	5642	9.47	17		2825	2817	50.07	49.93

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
6	28	9	1	16	5640	9.47	18		3171	2469	56.22	43.78
6	26	9	6	15	5638	9.47	19		2696	2942	47.82	52.18
7	3	9	6	11	5632	9.46	20		2869	2763	50.94	49.06
6	19	9	6	17	5631	9.46	21	59548	2482	3149	44.08	55.92
9	18	9	6	15	5610	9.42	22		2694	2916	48.02	51.98
7	5	9	1	17	5609	9.42	23		2869	2740	51.15	48.85
6	12	9	6	15	5608	9.42	24		2649	2959	47.24	52.76
12	26	9	7	13	5599	9.4	25		2933	2666	52.38	47.62
7	10	9	6	13	5594	9.39	26		2674	2920	47.8	52.2
6	19	9	6	15	5569	9.35	27		2552	3017	45.83	54.17
6	26	9	6	16	5555	9.33	28		2683	2872	48.3	51.7
6	28	9	1	15	5549	9.32	29		2995	2554	53.97	46.03
7	10	9	6	16	5514	9.26	30		2767	2747	50.18	49.82
10	2	9	6	16	5514	9.26	31		2550	2964	46.25	53.75
9	7	9	2	16	5497	9.23	32		3043	2454	55.36	44.64
9	4	9	6	13	5494	9.23	33		2595	2899	47.23	52.77
12	26	9	7	12	5490	9.22	34		2894	2596	52.71	47.29
12	26	9	7	15	5480	9.2	35		2764	2716	50.44	49.56
12	27	9	1	15	5478	9.2	36		2991	2487	54.6	45.4
6	19	9	6	14	5466	9.18	37		2785	2681	50.95	49.05
6	28	9	1	18	5463	9.17	38		3061	2402	56.03	43.97
9	4	9	6	17	5463	9.17	39		2520	2943	46.13	53.87
7	3	9	6	16	5450	9.15	40		2753	2697	50.51	49.49
9	11	9	6	16	5441	9.14	41	59548	2457	2984	45.16	54.84
6	28	9	1	17	5435	9.13	42		2985	2450	54.92	45.08
12	27	9	1	16	5434	9.13	43		2974	2460	54.73	45.27
7	10	9	6	12	5423	9.11	44		2542	2881	46.87	53.13
12	27	9	1	14	5418	9.1	45		2997	2421	55.32	44.68
6	21	9	1	15	5387	9.05	46		2883	2504	53.52	46.48
12	24	9	5	13	5385	9.04	47		2746	2639	50.99	49.01
6	21	9	1	17	5384	9.04	48		2892	2492	53.71	46.29
9	18	9	6	17	5382	9.04	49		2552	2830	47.42	52.58
6	12	9	6	14	5377	9.03	50		2555	2822	47.52	52.48
9	11	9	6	15	5353	8.99	51		2610	2743	48.76	51.24
9	25	9	6	16	5353	8.99	52		2517	2836	47.02	52.98
7	10	9	6	17	5351	8.99	53		2482	2869	46.38	53.62
6	19	9	6	16	5345	8.98	54		2315	3030	43.31	56.69
10	30	9	6	16	5325	8.94	55		2389	2936	44.86	55.14
12	27	9	1	13	5321	8.94	56		2941	2380	55.27	44.73
4	17	9	6	16	5316	8.93	57		2439	2877	45.88	54.12
6	5	9	6	16	5315	8.93	58		2487	2828	46.79	53.21
10	9	9	6	15	5304	8.91	59		2484	2820	46.83	53.17
7	2	9	5	15	5302	8.9	60		2430	2872	45.83	54.17
6	28	9	1	14	5300	8.9	61	59548	2931	2369	55.3	44.7
9	13	9	1	18	5289	8.88	62		2761	2528	52.2	47.8
10	9	9	6	16	5288	8.88	63		2385	2903	45.1	54.9
9	4	9	6	12	5286	8.88	64		2529	2757	47.84	52.16
6	26	9	6	12	5282	8.87	65		2557	2725	48.41	51.59
7	2	9	5	13	5281	8.87	66		2635	2646	49.9	50.1
10	23	9	6	15	5273	8.86	67		2551	2722	48.38	51.62
9	5	9	7	13	5272	8.85	68		2586	2686	49.05	50.95
9	20	9	1	17	5269	8.85	69		2681	2588	50.88	49.12

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
10	9	9	6	14	5260	8.83	70		2484	2776	47.22	52.78
9	4	9	6	18	5246	8.81	71		2337	2909	44.55	55.45
6	26	9	6	13	5244	8.81	72		2398	2846	45.73	54.27
6	21	9	1	14	5241	8.8	73		2774	2467	52.93	47.07
9	18	9	6	14	5241	8.8	74		2564	2677	48.92	51.08
6	20	9	7	12	5238	8.8	75		2647	2591	50.53	49.47
12	23	9	4	15	5234	8.79	76		2660	2574	50.82	49.18
5	8	9	6	15	5229	8.78	77		2352	2877	44.98	55.02
6	5	9	6	15	5229	8.78	78		2382	2847	45.55	54.45
7	11	9	7	12	5227	8.78	79		2491	2736	47.66	52.34
9	25	9	6	17	5224	8.77	80		2439	2785	46.69	53.31
9	25	9	6	15	5222	8.77	81	59548	2360	2862	45.19	54.81
10	2	9	6	15	5221	8.77	82		2354	2867	45.09	54.91
7	11	9	7	13	5216	8.76	83		2464	2752	47.24	52.76
4	3	9	6	15	5215	8.76	84		2604	2611	49.93	50.07
12	24	9	5	15	5215	8.76	85		2540	2675	48.71	51.29
4	10	9	6	16	5207	8.74	86		2401	2806	46.11	53.89
7	2	9	5	14	5204	8.74	87		2431	2773	46.71	53.29
10	23	9	6	16	5202	8.74	88		2579	2623	49.58	50.42
6	21	9	1	16	5198	8.73	89		2755	2443	53	47
6	14	9	1	17	5197	8.73	90		2823	2374	54.32	45.68
6	28	9	1	13	5197	8.73	91		2773	2424	53.36	46.64
6	14	9	1	16	5191	8.72	92		2806	2385	54.06	45.94
6	12	9	6	13	5181	8.7	93		2488	2693	48.02	51.98
4	12	9	1	19	5180	8.7	94		2842	2338	54.86	45.14
10	2	9	6	17	5165	8.67	95		2291	2874	44.36	55.64
12	24	9	5	14	5164	8.67	96		2595	2569	50.25	49.75
9	18	9	6	13	5158	8.66	97		2597	2561	50.35	49.65
4	12	9	1	18	5149	8.65	98		2825	2324	54.87	45.13
6	20	9	7	15	5145	8.64	99		2423	2722	47.09	52.91
6	19	9	6	18	5144	8.64	100		2107	3037	40.96	59.04
9	5	9	7	11	5139	8.63	101	59548	2498	2641	48.61	51.39
9	11	9	6	14	5137	8.63	102		2415	2722	47.01	52.99
9	25	9	6	18	5137	8.63	103		2381	2756	46.35	53.65
7	2	9	5	16	5136	8.62	104		2372	2764	46.18	53.82
6	12	9	6	18	5128	8.61	105		2382	2746	46.45	53.55
6	26	9	6	17	5125	8.61	106		2421	2704	47.24	52.76
7	3	9	6	13	5110	8.58	107		2344	2766	45.87	54.13
6	7	9	1	17	5106	8.57	108		2761	2345	54.07	45.93
9	13	9	1	17	5105	8.57	109		2628	2477	51.48	48.52
4	5	9	1	16	5103	8.57	110		2902	2201	56.87	43.13
5	8	9	6	16	5102	8.57	111		2271	2831	44.51	55.49
9	7	9	2	17	5101	8.57	112		2862	2239	56.11	43.89
10	16	9	6	15	5098	8.56	113		2360	2738	46.29	53.71
12	24	9	5	12	5090	8.55	114		2564	2526	50.37	49.63
6	5	9	6	14	5089	8.55	115		2406	2683	47.28	52.72
9	20	9	1	18	5089	8.55	116		2585	2504	50.8	49.2
6	14	9	1	15	5084	8.54	117		2772	2312	54.52	45.48
4	17	9	6	15	5079	8.53	118		2458	2621	48.4	51.6
9	11	9	6	17	5079	8.53	119		2388	2691	47.02	52.98
9	7	9	2	14	5078	8.53	120		2643	2435	52.05	47.95
4	3	9	6	16	5077	8.53	121	59548	2405	2672	47.37	52.63

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
5	1	9	6	15	5077	8.53	122		2370	2707	46.68	53.32
10	16	9	6	17	5070	8.51	123		2397	2673	47.28	52.72
4	3	9	6	14	5069	8.51	124		2439	2630	48.12	51.88
6	12	9	6	12	5068	8.51	125		2564	2504	50.59	49.41
4	10	9	6	15	5067	8.51	126		2343	2724	46.24	53.76
9	11	9	6	18	5064	8.5	127		2404	2660	47.47	52.53
6	5	9	6	17	5063	8.5	128		2437	2626	48.13	51.87
9	7	9	2	13	5062	8.5	129		2692	2370	53.18	46.82
6	19	9	6	13	5061	8.5	130		2616	2445	51.69	48.31
9	20	9	1	16	5061	8.5	131		2651	2410	52.38	47.62
9	25	9	6	14	5061	8.5	132		2363	2698	46.69	53.31
5	1	9	6	16	5056	8.49	133		2469	2587	48.83	51.17
6	27	9	7	12	5056	8.49	134		2368	2688	46.84	53.16
6	14	9	1	14	5055	8.49	135		2725	2330	53.91	46.09
4	5	9	1	17	5052	8.48	136		2857	2195	56.55	43.45
6	21	9	1	13	5052	8.48	137		2669	2383	52.83	47.17
10	2	9	6	18	5051	8.48	138		2185	2866	43.26	56.74
10	2	9	6	14	5044	8.47	139		2328	2716	46.15	53.85
6	25	9	5	16	5043	8.47	140		2336	2707	46.32	53.68
6	26	9	6	18	5042	8.47	141	59548	2408	2634	47.76	52.24
9	7	9	2	15	5041	8.47	142		2560	2481	50.78	49.22
10	9	9	6	13	5041	8.47	143		2393	2648	47.47	52.53
7	6	9	2	15	5035	8.46	144		2452	2583	48.7	51.3
7	2	9	5	17	5031	8.45	145		2376	2655	47.23	52.77
5	10	9	1	18	5022	8.43	146		2836	2186	56.47	43.53
9	11	9	6	13	5018	8.43	147		2380	2638	47.43	52.57
10	9	9	6	18	5012	8.42	148		2205	2807	43.99	56.01
12	23	9	4	13	5012	8.42	149		2621	2391	52.29	47.71
9	5	9	7	14	5010	8.41	150		2520	2490	50.3	49.7
7	3	9	6	17	5007	8.41	151		2338	2669	46.69	53.31
4	10	9	6	17	5004	8.4	152		2281	2723	45.58	54.42
9	3	9	5	15	5003	8.4	153		2463	2540	49.23	50.77
9	20	9	1	15	5003	8.4	154		2691	2312	53.79	46.21
4	24	9	6	16	5001	8.4	155		2480	2521	49.59	50.41
6	7	9	1	18	5001	8.4	156		2666	2335	53.31	46.69
10	11	9	1	16	4999	8.39	157		2718	2281	54.37	45.63
10	11	9	1	17	4999	8.39	158		2637	2362	52.75	47.25
6	12	9	6	17	4996	8.39	159		2212	2784	44.28	55.72
7	6	9	2	13	4996	8.39	160		2523	2473	50.5	49.5
4	10	9	6	14	4991	8.38	161	59548	2300	2691	46.08	53.92
9	19	9	7	12	4989	8.38	162		2618	2371	52.48	47.52
10	30	9	6	17	4986	8.37	163		2226	2760	44.65	55.35
5	10	9	1	17	4983	8.37	164		2622	2361	52.62	47.38
10	11	9	1	18	4979	8.36	165		2599	2380	52.2	47.8
10	9	9	6	17	4971	8.35	166		2176	2795	43.77	56.23
10	23	9	6	17	4967	8.34	167		2445	2522	49.22	50.78
7	10	9	6	18	4966	8.34	168		2117	2849	42.63	57.37
10	30	9	6	15	4964	8.34	169		2173	2791	43.78	56.22
12	31	9	5	15	4960	8.33	170		2488	2472	50.16	49.84
7	9	9	5	15	4959	8.33	171		2336	2623	47.11	52.89
7	2	9	5	18	4958	8.33	172		2310	2648	46.59	53.41
4	17	9	6	17	4957	8.32	173		2376	2581	47.93	52.07

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
9	12	9	7	11	4951	8.31	174		2532	2419	51.14	48.86
5	29	9	6	15	4949	8.31	175		2215	2734	44.76	55.24
9	13	9	1	16	4947	8.31	176		2471	2476	49.95	50.05
6	14	9	1	18	4945	8.3	177		2670	2275	53.99	46.01
9	26	9	7	12	4944	8.3	178		2465	2479	49.86	50.14
12	23	9	4	16	4944	8.3	179		2432	2512	49.19	50.81
9	20	9	1	14	4941	8.3	180		2479	2462	50.17	49.83
5	1	9	6	14	4938	8.29	181	59548	2422	2516	49.05	50.95
7	11	9	7	11	4938	8.29	182		2277	2661	46.11	53.89
7	9	9	5	16	4935	8.29	183		2305	2630	46.71	53.29
6	28	9	1	19	4926	8.27	184		2886	2040	58.59	41.41
9	27	9	1	17	4925	8.27	185		2605	2320	52.89	47.11
4	24	9	6	15	4923	8.27	186		2357	2566	47.88	52.12
7	5	9	1	12	4923	8.27	187		2493	2430	50.64	49.36
9	13	9	1	19	4923	8.27	188		2444	2479	49.64	50.36
12	27	9	1	17	4923	8.27	189		2765	2158	56.16	43.84
9	27	9	1	18	4920	8.26	190		2610	2310	53.05	46.95
6	5	9	6	18	4917	8.26	191		2265	2652	46.06	53.94
5	3	9	1	17	4916	8.26	192		2628	2288	53.46	46.54
10	4	9	1	17	4909	8.24	193		2703	2206	55.06	44.94
10	25	9	1	15	4909	8.24	194		2531	2378	51.56	48.44
10	25	9	1	16	4909	8.24	195		2608	2301	53.13	46.87
4	10	9	6	18	4908	8.24	196		2212	2696	45.07	54.93
5	8	9	6	14	4904	8.24	197		2409	2495	49.12	50.88
10	25	9	1	17	4903	8.23	198		2563	2340	52.27	47.73
5	3	9	1	18	4902	8.23	199		2524	2378	51.49	48.51
7	5	9	1	18	4902	8.23	200		2416	2486	49.29	50.71

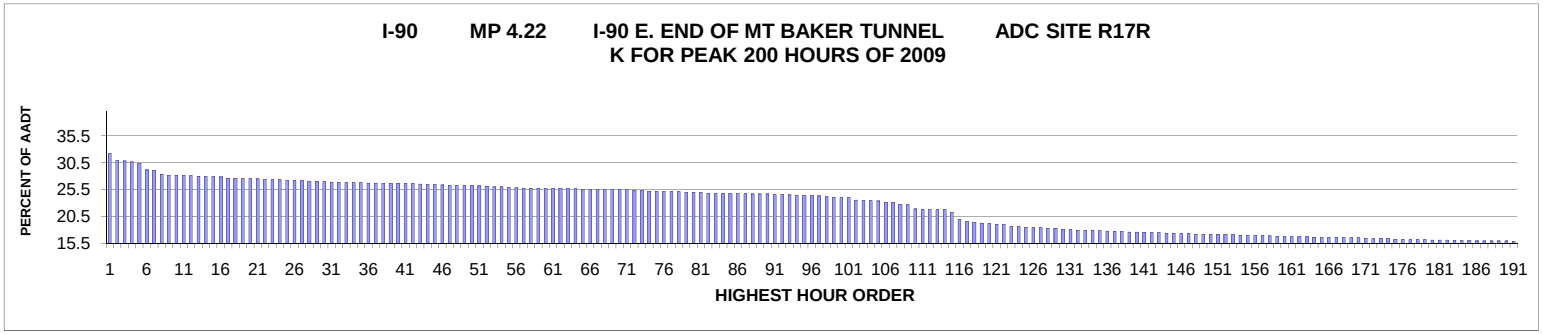

AADT= 11530 **K 30 FACTOR=** 27.48 **K 100 FACTOR=** 24.56 **K 200 FACTOR=** 15.87 **D FACTOR=** 50

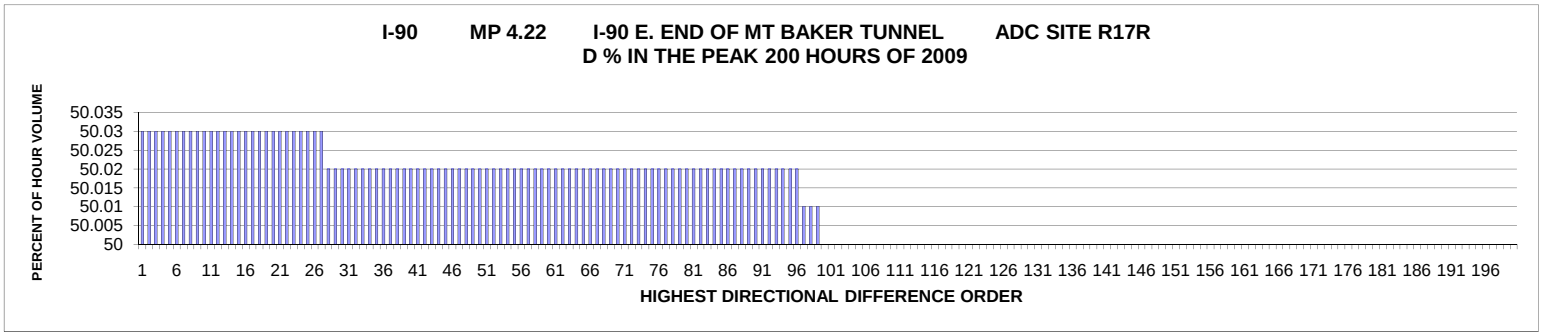

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	15	9	4	7	3706	32.14	1	11530	1853	1853	50	50
7	17	9	6	7	3560	30.88	2		1780	1780	50	50
7	16	9	5	7	3551	30.8	3		1776	1775	50.01	49.99
7	9	9	5	7	3527	30.59	4		1764	1763	50.01	49.99
7	15	9	4	8	3496	30.32	5		1748	1748	50	50
7	16	9	5	8	3360	29.14	6		1680	1680	50	50
7	9	9	5	8	3347	29.03	7		1674	1673	50.01	49.99
7	9	9	5	9	3270	28.36	8		1635	1635	50	50
7	13	9	2	19	3251	28.2	9		1626	1625	50.02	49.98
7	14	9	3	8	3251	28.2	10		1626	1625	50.02	49.98
7	13	9	2	8	3242	28.12	11		1621	1621	50	50
7	14	9	3	9	3234	28.05	12		1617	1617	50	50
7	13	9	2	18	3224	27.96	13		1612	1612	50	50
7	10	9	6	7	3216	27.89	14		1608	1608	50	50
7	17	9	6	9	3213	27.87	15		1607	1606	50.02	49.98
7	13	9	2	15	3207	27.81	16		1604	1603	50.02	49.98
7	13	9	2	10	3179	27.57	17		1590	1589	50.02	49.98

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	14	9	3	16	3179	27.57	18		1590	1589	50.02	49.98
7	13	9	2	9	3175	27.54	19		1588	1587	50.02	49.98
7	13	9	2	16	3171	27.5	20		1586	1585	50.02	49.98
7	17	9	6	16	3168	27.48	21	11530	1584	1584	50	50
7	16	9	5	9	3163	27.43	22		1582	1581	50.02	49.98
7	14	9	3	10	3149	27.31	23		1575	1574	50.02	49.98
7	15	9	4	16	3147	27.29	24		1574	1573	50.02	49.98
7	14	9	3	7	3133	27.17	25		1567	1566	50.02	49.98
7	15	9	4	9	3132	27.16	26		1566	1566	50	50
7	9	9	5	10	3123	27.09	27		1562	1561	50.02	49.98
7	17	9	6	19	3113	27	28		1557	1556	50.02	49.98
7	10	9	6	8	3112	26.99	29		1556	1556	50	50
7	16	9	5	16	3106	26.94	30		1553	1553	50	50
7	10	9	6	9	3094	26.83	31		1547	1547	50	50
7	13	9	2	7	3094	26.83	32		1547	1547	50	50
7	15	9	4	20	3087	26.77	33		1544	1543	50.02	49.98
7	15	9	4	19	3085	26.76	34		1543	1542	50.02	49.98
7	17	9	6	10	3082	26.73	35		1541	1541	50	50
7	16	9	5	18	3076	26.68	36		1538	1538	50	50
7	16	9	5	19	3076	26.68	37		1538	1538	50	50
7	16	9	5	17	3073	26.65	38		1537	1536	50.02	49.98
7	13	9	2	17	3072	26.64	39		1536	1536	50	50
7	17	9	6	17	3071	26.63	40		1536	1535	50.02	49.98
7	15	9	4	18	3070	26.63	41	11530	1535	1535	50	50
7	17	9	6	18	3068	26.61	42		1534	1534	50	50
7	15	9	4	15	3053	26.48	43		1527	1526	50.02	49.98
7	15	9	4	10	3044	26.4	44		1522	1522	50	50
7	15	9	4	17	3039	26.36	45		1520	1519	50.02	49.98
7	16	9	5	15	3038	26.35	46		1519	1519	50	50
7	14	9	3	11	3032	26.3	47		1516	1516	50	50
7	9	9	5	16	3025	26.24	48		1513	1512	50.02	49.98
7	11	9	7	12	3022	26.21	49		1511	1511	50	50
7	14	9	3	18	3022	26.21	50		1511	1511	50	50
7	16	9	5	10	3016	26.16	51		1508	1508	50	50
7	9	9	5	17	3006	26.07	52		1503	1503	50	50
7	10	9	6	16	2996	25.98	53		1498	1498	50	50
7	10	9	6	17	2993	25.96	54		1497	1496	50.02	49.98
7	16	9	5	11	2978	25.83	55		1489	1489	50	50
7	10	9	6	10	2973	25.78	56		1487	1486	50.02	49.98
7	9	9	5	12	2968	25.74	57		1484	1484	50	50
7	9	9	5	14	2965	25.72	58		1483	1482	50.02	49.98
7	9	9	5	11	2964	25.71	59		1482	1482	50	50
7	13	9	2	11	2960	25.67	60		1480	1480	50	50
7	14	9	3	17	2959	25.66	61	11530	1480	1479	50.02	49.98
7	16	9	5	20	2957	25.65	62		1479	1478	50.02	49.98
7	9	9	5	19	2953	25.61	63		1477	1476	50.02	49.98
7	11	9	7	18	2953	25.61	64		1477	1476	50.02	49.98
7	14	9	3	20	2948	25.57	65		1474	1474	50	50
7	10	9	6	15	2943	25.52	66		1472	1471	50.02	49.98
7	10	9	6	18	2943	25.52	67		1472	1471	50.02	49.98
7	17	9	6	11	2935	25.46	68		1468	1467	50.02	49.98
7	17	9	6	15	2935	25.46	69		1468	1467	50.02	49.98

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	10	9	6	20	2933	25.44	70		1467	1466	50.02	49.98
7	14	9	3	19	2931	25.42	71		1466	1465	50.02	49.98
7	9	9	5	13	2928	25.39	72		1464	1464	50	50
7	14	9	3	12	2912	25.26	73		1456	1456	50	50
7	9	9	5	20	2900	25.15	74		1450	1450	50	50
7	9	9	5	15	2897	25.13	75		1449	1448	50.02	49.98
7	14	9	3	15	2894	25.1	76		1447	1447	50	50
7	16	9	5	12	2894	25.1	77		1447	1447	50	50
7	16	9	5	14	2889	25.06	78		1445	1444	50.02	49.98
7	17	9	6	20	2879	24.97	79		1440	1439	50.02	49.98
7	11	9	7	13	2877	24.95	80		1439	1438	50.02	49.98
7	17	9	6	12	2876	24.94	81	11530	1438	1438	50	50
7	14	9	3	14	2855	24.76	82		1428	1427	50.02	49.98
7	9	9	5	18	2854	24.75	83		1427	1427	50	50
7	16	9	5	13	2854	24.75	84		1427	1427	50	50
7	10	9	6	11	2853	24.74	85		1427	1426	50.02	49.98
7	11	9	7	14	2849	24.71	86		1425	1424	50.02	49.98
7	15	9	4	14	2848	24.7	87		1424	1424	50	50
7	15	9	4	13	2847	24.69	88		1424	1423	50.02	49.98
7	12	9	1	13	2845	24.67	89		1423	1422	50.02	49.98
7	10	9	6	12	2842	24.65	90		1421	1421	50	50
7	15	9	4	11	2832	24.56	91		1416	1416	50	50
7	14	9	3	13	2831	24.55	92		1416	1415	50.02	49.98
7	12	9	1	14	2823	24.48	93		1412	1411	50.02	49.98
7	13	9	2	14	2809	24.36	94		1405	1404	50.02	49.98
7	10	9	6	19	2806	24.34	95		1403	1403	50	50
7	15	9	4	12	2803	24.31	96		1402	1401	50.02	49.98
7	10	9	6	14	2799	24.28	97		1400	1399	50.02	49.98
7	11	9	7	19	2782	24.13	98		1391	1391	50	50
7	13	9	2	13	2769	24.02	99		1385	1384	50.02	49.98
7	10	9	6	13	2761	23.95	100		1381	1380	50.02	49.98
7	13	9	2	12	2761	23.95	101	11530	1381	1380	50.02	49.98
7	12	9	1	12	2717	23.56	102		1359	1358	50.02	49.98
7	11	9	7	11	2698	23.4	103		1349	1349	50	50
7	17	9	6	14	2697	23.39	104		1349	1348	50.02	49.98
7	9	9	5	21	2696	23.38	105		1348	1348	50	50
7	11	9	7	17	2666	23.12	106		1333	1333	50	50
7	17	9	6	13	2660	23.07	107		1330	1330	50	50
7	11	9	7	15	2618	22.71	108		1309	1309	50	50
7	12	9	1	15	2613	22.66	109		1307	1306	50.02	49.98
7	17	9	6	8	2520	21.86	110		1260	1260	50	50
7	12	9	1	17	2517	21.83	111		1259	1258	50.02	49.98
7	12	9	1	11	2508	21.75	112		1254	1254	50	50
7	12	9	1	16	2505	21.73	113		1253	1252	50.02	49.98
7	12	9	1	18	2504	21.72	114		1252	1252	50	50
7	11	9	7	16	2453	21.27	115		1227	1226	50.02	49.98
3	20	9	6	18	2291	19.87	116		1146	1145	50.02	49.98
7	16	9	5	21	2248	19.5	117		1124	1124	50	50
7	11	9	7	10	2230	19.34	118		1115	1115	50	50
7	10	9	6	22	2222	19.27	119		1111	1111	50	50
6	3	9	4	18	2210	19.17	120		1105	1105	50	50
7	12	9	1	19	2194	19.03	121	11530	1097	1097	50	50

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	13	9	2	20	2194	19.03	122		1097	1097	50	50
7	17	9	6	21	2148	18.63	123		1074	1074	50	50
9	10	9	5	18	2141	18.57	124		1071	1070	50.02	49.98
1	8	9	5	18	2126	18.44	125		1063	1063	50	50
3	17	9	3	18	2124	18.42	126		1062	1062	50	50
3	20	9	6	17	2124	18.42	127		1062	1062	50	50
7	10	9	6	21	2111	18.31	128		1056	1055	50.02	49.98
7	15	9	4	21	2106	18.27	129		1053	1053	50	50
4	8	9	4	18	2087	18.1	130		1044	1043	50.02	49.98
10	8	9	5	18	2083	18.07	131		1042	1041	50.02	49.98
12	17	9	5	18	2070	17.95	132		1035	1035	50	50
1	6	9	3	18	2063	17.89	133		1032	1031	50.02	49.98
1	6	9	3	19	2063	17.89	134		1032	1031	50.02	49.98
12	16	9	4	18	2056	17.83	135		1028	1028	50	50
7	29	9	4	18	2046	17.75	136		1023	1023	50	50
12	1	9	3	18	2043	17.72	137		1022	1021	50.02	49.98
5	28	9	5	18	2039	17.68	138		1020	1019	50.02	49.98
4	21	9	3	18	2028	17.59	139		1014	1014	50	50
6	2	9	3	18	2025	17.56	140		1013	1012	50.02	49.98
6	11	9	5	18	2017	17.49	141	11530	1009	1008	50.02	49.98
3	16	9	2	18	2016	17.48	142		1008	1008	50	50
7	16	9	5	22	2012	17.45	143		1006	1006	50	50
6	15	9	2	18	2001	17.35	144		1001	1000	50.02	49.98
4	23	9	5	18	1996	17.31	145		998	998	50	50
6	9	9	3	18	1995	17.3	146		998	997	50.03	49.97
7	15	9	4	22	1994	17.29	147		997	997	50	50
1	12	9	2	18	1979	17.16	148		990	989	50.03	49.97
6	10	9	4	18	1977	17.15	149		989	988	50.03	49.97
7	14	9	3	21	1977	17.15	150		989	988	50.03	49.97
7	11	9	7	20	1976	17.14	151		988	988	50	50
1	26	9	2	18	1975	17.13	152		988	987	50.03	49.97
7	30	9	5	18	1972	17.1	153		986	986	50	50
1	7	9	4	18	1956	16.96	154		978	978	50	50
9	17	9	5	18	1954	16.95	155		977	977	50	50
6	18	9	5	18	1951	16.92	156		976	975	50.03	49.97
7	12	9	1	10	1950	16.91	157		975	975	50	50
4	30	9	5	18	1944	16.86	158		972	972	50	50
7	31	9	6	18	1936	16.79	159		968	968	50	50
11	6	9	6	18	1925	16.7	160		963	962	50.03	49.97
2	11	9	4	18	1924	16.69	161	11530	962	962	50	50
12	14	9	2	18	1922	16.67	162		961	961	50	50
8	4	9	3	18	1921	16.66	163		961	960	50.03	49.97
7	22	9	4	18	1919	16.64	164		960	959	50.03	49.97
2	23	9	2	18	1911	16.57	165		956	955	50.03	49.97
11	16	9	2	18	1911	16.57	166		956	955	50.03	49.97
6	30	9	3	18	1909	16.56	167		955	954	50.03	49.97
6	25	9	5	18	1906	16.53	168		953	953	50	50
9	13	9	1	17	1905	16.52	169		953	952	50.03	49.97
5	27	9	4	18	1900	16.48	170		950	950	50	50
9	24	9	5	18	1893	16.42	171		947	946	50.03	49.97
1	5	9	2	18	1884	16.34	172		942	942	50	50
7	14	9	3	22	1883	16.33	173		942	941	50.03	49.97

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
10	1	9	5	18	1883	16.33	174		942	941	50.03	49.97
6	4	9	5	18	1871	16.23	175		936	935	50.03	49.97
12	9	9	4	18	1870	16.22	176		935	935	50	50
11	24	9	3	18	1862	16.15	177		931	931	50	50
1	30	9	6	18	1860	16.13	178		930	930	50	50
9	14	9	2	18	1859	16.12	179		930	929	50.03	49.97
2	10	9	3	18	1858	16.11	180		929	929	50	50
11	10	9	3	18	1857	16.11	181	11530	929	928	50.03	49.97
11	12	9	5	18	1855	16.09	182		928	927	50.03	49.97
8	18	9	3	18	1846	16.01	183		923	923	50	50
8	19	9	4	18	1841	15.97	184		921	920	50.03	49.97

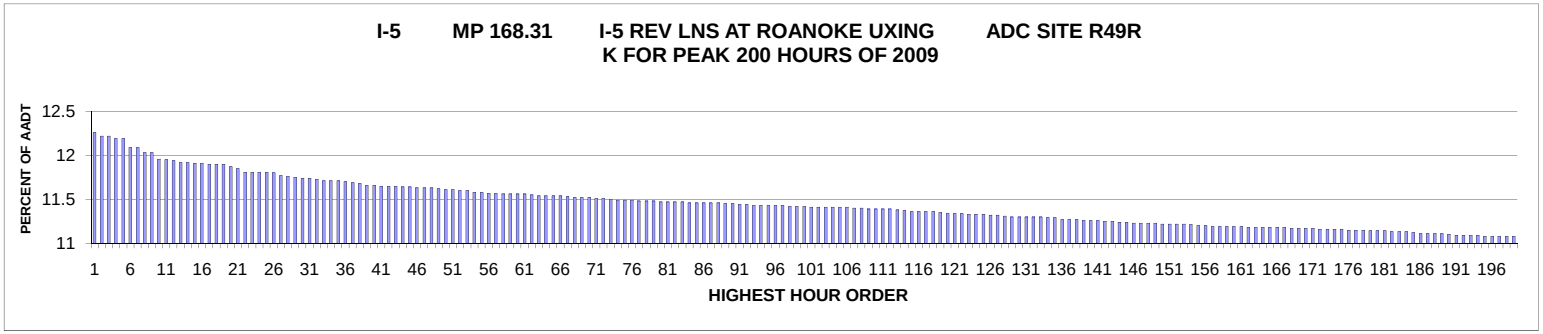

AADT= 44707 **K 30 FACTOR=** 11.75 **K 100 FACTOR=** 11.42 **K 200 FACTOR=** 11.08 **D FACTOR=** 50.01

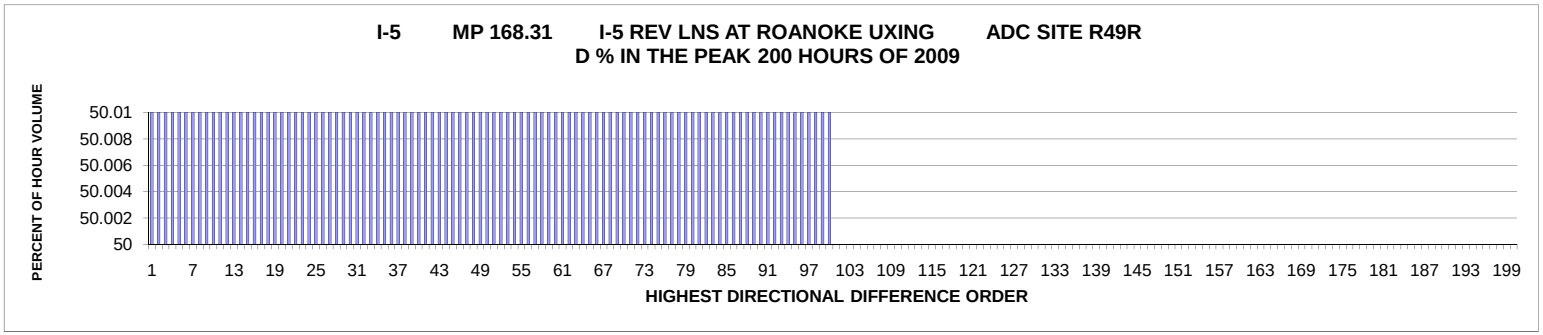

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
2	25	9	4	8	5694	12.74	1	44707	2847	2847	50	50
3	18	9	4	8	5479	12.26	2		2740	2739	50.01	49.99
2	5	9	5	8	5464	12.22	3		2732	2732	50	50
3	26	9	5	8	5462	12.22	4		2731	2731	50	50
2	4	9	4	8	5449	12.19	5		2725	2724	50.01	49.99
3	11	9	4	8	5449	12.19	6		2725	2724	50.01	49.99
4	15	9	4	8	5407	12.09	7		2704	2703	50.01	49.99
2	12	9	5	8	5403	12.09	8		2702	2701	50.01	49.99
3	17	9	3	8	5380	12.03	9		2690	2690	50	50
3	24	9	3	8	5378	12.03	10		2689	2689	50	50
5	13	9	4	8	5346	11.96	11		2673	2673	50	50
2	10	9	3	9	5343	11.95	12		2672	2671	50.01	49.99
4	21	9	3	8	5340	11.94	13		2670	2670	50	50
4	14	9	3	8	5328	11.92	14		2664	2664	50	50
11	4	9	4	8	5327	11.92	15		2664	2663	50.01	49.99
11	3	9	3	8	5326	11.91	16		2663	2663	50	50
1	14	9	4	9	5323	11.91	17		2662	2661	50.01	49.99

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
2	2	9	2	8	5322	11.9	18		2661	2661	50	50
2	27	9	6	8	5321	11.9	19		2661	2660	50.01	49.99
6	9	9	3	8	5318	11.9	20		2659	2659	50	50
4	16	9	5	8	5306	11.87	21	44707	2653	2653	50	50
1	28	9	4	8	5296	11.85	22		2648	2648	50	50
2	3	9	3	8	5281	11.81	23		2641	2640	50.01	49.99
4	30	9	5	8	5280	11.81	24		2640	2640	50	50
6	11	9	5	8	5280	11.81	25		2640	2640	50	50
11	18	9	4	8	5280	11.81	26		2640	2640	50	50
1	29	9	5	8	5276	11.8	27		2638	2638	50	50
1	22	9	5	8	5260	11.77	28		2630	2630	50	50
4	7	9	3	8	5256	11.76	29		2628	2628	50	50
6	10	9	4	8	5251	11.75	30		2626	2625	50.01	49.99
3	5	9	5	8	5248	11.74	31		2624	2624	50	50
3	31	9	3	8	5247	11.74	32		2624	2623	50.01	49.99
5	12	9	3	8	5245	11.73	33		2623	2622	50.01	49.99
7	14	9	3	8	5236	11.71	34		2618	2618	50	50
4	6	9	2	8	5235	11.71	35		2618	2617	50.01	49.99
2	18	9	4	8	5233	11.71	36		2617	2616	50.01	49.99
10	7	9	4	8	5230	11.7	37		2615	2615	50	50
4	29	9	4	8	5227	11.69	38		2614	2613	50.01	49.99
12	3	9	5	9	5222	11.68	39		2611	2611	50	50
11	17	9	3	8	5215	11.66	40		2608	2607	50.01	49.99
3	12	9	5	8	5213	11.66	41	44707	2607	2606	50.01	49.99
2	19	9	5	8	5210	11.65	42		2605	2605	50	50
1	15	9	5	8	5209	11.65	43		2605	2604	50.01	49.99
2	3	9	3	9	5209	11.65	44		2605	2604	50.01	49.99
3	16	9	2	8	5205	11.64	45		2603	2602	50.01	49.99
11	12	9	5	9	5202	11.64	46		2601	2601	50	50
2	17	9	3	8	5201	11.63	47		2601	2600	50.01	49.99
3	10	9	3	8	5201	11.63	48		2601	2600	50.01	49.99
9	30	9	4	8	5199	11.63	49		2600	2599	50.01	49.99
6	3	9	4	8	5197	11.62	50		2599	2598	50.01	49.99
6	4	9	5	8	5192	11.61	51		2596	2596	50	50
4	23	9	5	8	5190	11.61	52		2595	2595	50	50
9	30	9	4	9	5188	11.6	53		2594	2594	50	50
9	29	9	3	8	5184	11.6	54		2592	2592	50	50
5	11	9	2	8	5179	11.58	55		2590	2589	50.01	49.99
1	21	9	4	9	5178	11.58	56		2589	2589	50	50
1	6	9	3	9	5172	11.57	57		2586	2586	50	50
3	12	9	5	9	5171	11.57	58		2586	2585	50.01	49.99
3	19	9	5	8	5169	11.56	59		2585	2584	50.01	49.99
3	25	9	4	8	5169	11.56	60		2585	2584	50.01	49.99
2	12	9	5	9	5168	11.56	61	44707	2584	2584	50	50
5	4	9	2	8	5168	11.56	62		2584	2584	50	50
1	29	9	5	9	5162	11.55	63		2581	2581	50	50
4	27	9	2	8	5158	11.54	64		2579	2579	50	50
1	20	9	3	8	5157	11.54	65		2579	2578	50.01	49.99
3	23	9	2	8	5157	11.54	66		2579	2578	50.01	49.99
11	12	9	5	8	5157	11.54	67		2579	2578	50.01	49.99
11	5	9	5	8	5153	11.53	68		2577	2576	50.01	49.99
4	22	9	4	8	5151	11.52	69		2576	2575	50.01	49.99

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
9	17	9	5	9	5151	11.52	70		2576	2575	50.01	49.99
10	15	9	5	8	5150	11.52	71		2575	2575	50	50
10	8	9	5	9	5148	11.51	72		2574	2574	50	50
1	21	9	4	8	5145	11.51	73		2573	2572	50.01	49.99
9	16	9	4	9	5142	11.5	74		2571	2571	50	50
6	3	9	4	9	5139	11.49	75		2570	2569	50.01	49.99
9	22	9	3	8	5138	11.49	76		2569	2569	50	50
10	13	9	3	8	5135	11.49	77		2568	2567	50.01	49.99
1	26	9	2	9	5133	11.48	78		2567	2566	50.01	49.99
3	13	9	6	8	5132	11.48	79		2566	2566	50	50
10	6	9	3	8	5132	11.48	80		2566	2566	50	50
12	2	9	4	8	5130	11.47	81	44707	2565	2565	50	50
12	3	9	5	8	5129	11.47	82		2565	2564	50.01	49.99
10	15	9	5	9	5128	11.47	83		2564	2564	50	50
10	8	9	5	8	5126	11.47	84		2563	2563	50	50
5	21	9	5	8	5125	11.46	85		2563	2562	50.01	49.99
6	16	9	3	8	5125	11.46	86		2563	2562	50.01	49.99
5	6	9	4	8	5123	11.46	87		2562	2561	50.01	49.99
9	22	9	3	9	5123	11.46	88		2562	2561	50.01	49.99
10	6	9	3	9	5123	11.46	89		2562	2561	50.01	49.99
4	20	9	2	8	5117	11.45	90		2559	2558	50.01	49.99
6	17	9	4	8	5117	11.45	91		2559	2558	50.01	49.99
5	5	9	3	9	5116	11.44	92		2558	2558	50	50
3	5	9	5	9	5113	11.44	93		2557	2556	50.01	49.99
9	16	9	4	8	5112	11.43	94		2556	2556	50	50
1	30	9	6	8	5111	11.43	95		2556	2555	50.01	49.99
3	25	9	4	9	5111	11.43	96		2556	2555	50.01	49.99
1	9	9	6	8	5109	11.43	97		2555	2554	50.01	49.99
9	29	9	3	9	5109	11.43	98		2555	2554	50.01	49.99
6	3	9	4	18	5105	11.42	99		2553	2552	50.01	49.99
4	9	9	5	8	5104	11.42	100		2552	2552	50	50
5	26	9	3	18	5104	11.42	101	44707	2552	2552	50	50
5	18	9	2	8	5103	11.41	102		2552	2551	50.01	49.99
5	20	9	4	8	5103	11.41	103		2552	2551	50.01	49.99
5	26	9	3	8	5103	11.41	104		2552	2551	50.01	49.99
9	23	9	4	8	5101	11.41	105		2551	2550	50.01	49.99
5	28	9	5	8	5100	11.41	106		2550	2550	50	50
12	1	9	3	8	5100	11.41	107		2550	2550	50	50
8	19	9	4	9	5098	11.4	108		2549	2549	50	50
4	2	9	5	8	5097	11.4	109		2549	2548	50.01	49.99
9	15	9	3	9	5094	11.39	110		2547	2547	50	50
11	24	9	3	8	5094	11.39	111		2547	2547	50	50
3	19	9	5	9	5093	11.39	112		2547	2546	50.01	49.99
1	8	9	5	8	5091	11.39	113		2546	2545	50.01	49.99
3	27	9	6	8	5086	11.38	114		2543	2543	50	50
2	4	9	4	9	5085	11.37	115		2543	2542	50.01	49.99
5	28	9	5	9	5079	11.36	116		2540	2539	50.01	49.99
6	18	9	5	8	5079	11.36	117		2540	2539	50.01	49.99
6	23	9	3	8	5079	11.36	118		2540	2539	50.01	49.99
9	15	9	3	8	5079	11.36	119		2540	2539	50.01	49.99
12	10	9	5	9	5074	11.35	120		2537	2537	50	50
12	8	9	3	9	5071	11.34	121	44707	2536	2535	50.01	49.99

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
5	14	9	5	8	5070	11.34	122		2535	2535	50	50
12	1	9	3	9	5068	11.34	123		2534	2534	50	50
10	27	9	3	8	5066	11.33	124		2533	2533	50	50
4	20	9	2	18	5065	11.33	125		2533	2532	50.01	49.99
12	9	9	4	8	5064	11.33	126		2532	2532	50	50
1	27	9	3	9	5062	11.32	127		2531	2531	50	50
3	24	9	3	9	5062	11.32	128		2531	2531	50	50
11	13	9	6	9	5057	11.31	129		2529	2528	50.01	49.99
10	7	9	4	9	5053	11.3	130		2527	2526	50.01	49.99
2	13	9	6	8	5051	11.3	131		2526	2525	50.01	49.99
9	21	9	2	9	5051	11.3	132		2526	2525	50.01	49.99
1	23	9	6	8	5050	11.3	133		2525	2525	50	50
12	9	9	4	9	5050	11.3	134		2525	2525	50	50
10	22	9	5	8	5049	11.29	135		2525	2524	50.01	49.99
9	24	9	5	8	5046	11.29	136		2523	2523	50	50
11	9	9	2	8	5040	11.27	137		2520	2520	50	50
6	2	9	3	18	5038	11.27	138		2519	2519	50	50
6	24	9	4	8	5037	11.27	139		2519	2518	50.01	49.99
1	14	9	4	8	5036	11.26	140		2518	2518	50	50
5	7	9	5	8	5034	11.26	141	44707	2517	2517	50	50
5	5	9	3	8	5033	11.26	142		2517	2516	50.01	49.99
1	7	9	4	8	5031	11.25	143		2516	2515	50.01	49.99
6	25	9	5	8	5030	11.25	144		2515	2515	50	50
4	24	9	6	8	5027	11.24	145		2514	2513	50.01	49.99
6	8	9	2	8	5026	11.24	146		2513	2513	50	50
10	5	9	2	9	5021	11.23	147		2511	2510	50.01	49.99
12	16	9	4	9	5021	11.23	148		2511	2510	50.01	49.99
6	4	9	5	9	5020	11.23	149		2510	2510	50	50
9	17	9	5	8	5020	11.23	150		2510	2510	50	50
5	28	9	5	18	5017	11.22	151		2509	2508	50.01	49.99
9	28	9	2	8	5017	11.22	152		2509	2508	50.01	49.99
1	12	9	2	8	5016	11.22	153		2508	2508	50	50
5	11	9	2	18	5014	11.22	154		2507	2507	50	50
1	26	9	2	8	5013	11.21	155		2507	2506	50.01	49.99
9	23	9	4	9	5008	11.2	156		2504	2504	50	50
3	31	9	3	18	5007	11.2	157		2504	2503	50.01	49.99
9	10	9	5	8	5004	11.19	158		2502	2502	50	50
11	18	9	4	9	5004	11.19	159		2502	2502	50	50
10	22	9	5	9	5003	11.19	160		2502	2501	50.01	49.99
12	15	9	3	9	5003	11.19	161	44707	2502	2501	50.01	49.99
9	2	9	4	8	5002	11.19	162		2501	2501	50	50
1	16	9	6	8	5000	11.18	163		2500	2500	50	50
4	30	9	5	18	5000	11.18	164		2500	2500	50	50
3	17	9	3	9	4999	11.18	165		2500	2499	50.01	49.99
10	5	9	2	8	4999	11.18	166		2500	2499	50.01	49.99
1	13	9	3	9	4998	11.18	167		2499	2499	50	50
2	6	9	6	8	4998	11.18	168		2499	2499	50	50
10	20	9	3	8	4996	11.17	169		2498	2498	50	50
2	9	9	2	9	4995	11.17	170		2498	2497	50.01	49.99
9	14	9	2	8	4994	11.17	171		2497	2497	50	50
5	27	9	4	8	4992	11.17	172		2496	2496	50	50
1	15	9	5	9	4991	11.16	173		2496	2495	50.01	49.99

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
9	9	9	4	8	4991	11.16	174		2496	2495	50.01	49.99
10	28	9	4	8	4990	11.16	175		2495	2495	50	50
10	1	9	5	9	4989	11.16	176		2495	2494	50.01	49.99
5	27	9	4	18	4986	11.15	177		2493	2493	50	50
6	15	9	2	8	4983	11.15	178		2492	2491	50.01	49.99
9	21	9	2	8	4983	11.15	179		2492	2491	50.01	49.99
3	11	9	4	9	4980	11.14	180		2490	2490	50	50
3	6	9	6	8	4979	11.14	181	44707	2490	2489	50.01	49.99
11	2	9	2	8	4979	11.14	182		2490	2489	50.01	49.99
5	19	9	3	8	4978	11.13	183		2489	2489	50	50
10	27	9	3	9	4976	11.13	184		2488	2488	50	50
7	15	9	4	8	4974	11.13	185		2487	2487	50	50
2	20	9	6	8	4970	11.12	186		2485	2485	50	50
6	9	9	3	18	4969	11.11	187		2485	2484	50.01	49.99
8	4	9	3	8	4969	11.11	188		2485	2484	50.01	49.99
2	23	9	2	8	4967	11.11	189		2484	2483	50.01	49.99
1	28	9	4	9	4966	11.11	190		2483	2483	50	50
9	8	9	3	8	4962	11.1	191		2481	2481	50	50
11	5	9	5	9	4959	11.09	192		2480	2479	50.01	49.99
8	26	9	4	9	4958	11.09	193		2479	2479	50	50
12	16	9	4	8	4958	11.09	194		2479	2479	50	50
1	22	9	5	9	4956	11.09	195		2478	2478	50	50
1	26	9	2	18	4955	11.08	196		2478	2477	50.01	49.99
11	17	9	3	9	4955	11.08	197		2478	2477	50.01	49.99
6	9	9	3	9	4954	11.08	198		2477	2477	50	50
4	7	9	3	18	4952	11.08	199		2476	2476	50	50
9	24	9	5	9	4952	11.08	200		2476	2476	50	50

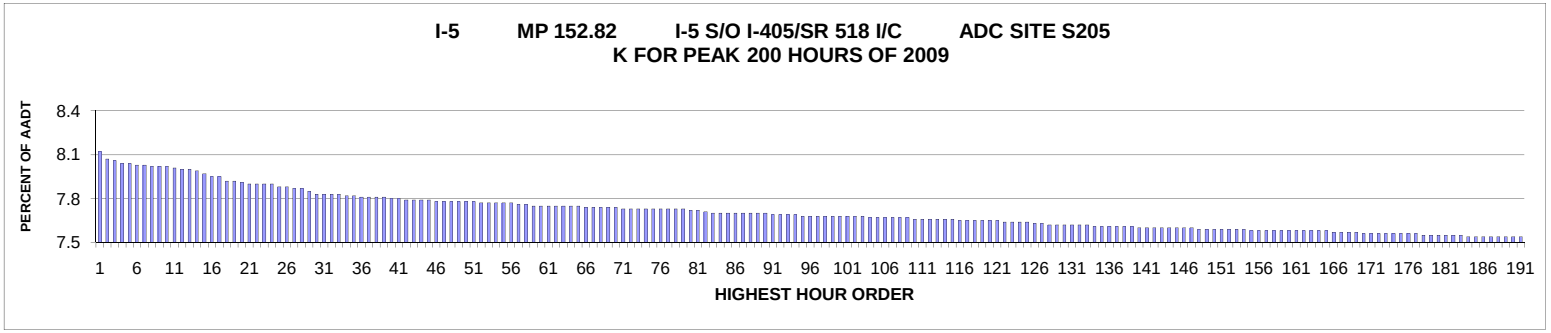

AADT= 207015 **K 30 FACTOR=** 7.83 **K 100 FACTOR=** 7.68 **K 200 FACTOR=** 7.54 **D FACTOR=** 58.02

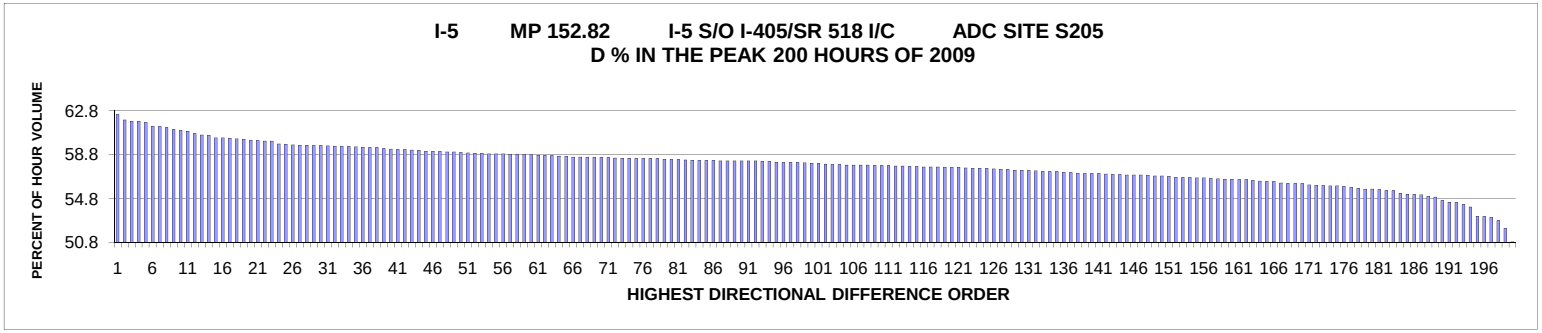

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
2	13	9	6	15	16800	8.12	1	207015	7007	9793	41.71	58.29
3	27	9	6	15	16700	8.07	2		7011	9689	41.98	58.02
5	15	9	6	17	16692	8.06	3		7352	9340	44.05	55.95
8	5	9	4	17	16647	8.04	4		7203	9444	43.27	56.73
4	10	9	6	15	16639	8.04	5		6813	9826	40.95	59.05
8	21	9	6	15	16626	8.03	6		7209	9417	43.36	56.64
8	7	9	6	15	16623	8.03	7		7090	9533	42.65	57.35
6	19	9	6	15	16606	8.02	8		7165	9441	43.15	56.85
4	3	9	6	15	16597	8.02	9		6897	9700	41.56	58.44
5	1	9	6	15	16594	8.02	10		7128	9466	42.96	57.04
5	22	9	6	15	16588	8.01	11		7105	9483	42.83	57.17
6	5	9	6	17	16557	8	12		7293	9264	44.05	55.95
4	17	9	6	17	16552	8	13		7258	9294	43.85	56.15
10	9	9	6	15	16544	7.99	14		6875	9669	41.56	58.44
8	14	9	6	15	16493	7.97	15		7116	9377	43.15	56.85
2	13	9	6	16	16466	7.95	16		6857	9609	41.64	58.36
3	13	9	6	15	16452	7.95	17		6819	9633	41.45	58.55

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
9	3	9	5	18	16400	7.92	18		8337	8063	50.84	49.16
8	28	9	6	16	16388	7.92	19		6975	9413	42.56	57.44
8	14	9	6	16	16368	7.91	20		7014	9354	42.85	57.15
3	27	9	6	16	16361	7.9	21	207015	6739	9622	41.19	58.81
7	17	9	6	15	16355	7.9	22		7133	9222	43.61	56.39
9	18	9	6	15	16353	7.9	23		6922	9431	42.33	57.67
4	17	9	6	16	16351	7.9	24		6829	9522	41.77	58.23
6	19	9	6	17	16319	7.88	25		7156	9163	43.85	56.15
12	18	9	6	15	16312	7.88	26		6903	9409	42.32	57.68
11	25	9	4	15	16301	7.87	27		6691	9610	41.05	58.95
3	20	9	6	15	16287	7.87	28		6749	9538	41.44	58.56
8	5	9	4	18	16245	7.85	29		7671	8574	47.22	52.78
8	12	9	4	18	16217	7.83	30		7179	9038	44.27	55.73
9	18	9	6	16	16206	7.83	31		6854	9352	42.29	57.71
7	10	9	6	15	16204	7.83	32		6930	9274	42.77	57.23
4	7	9	3	17	16199	7.83	33		6446	9753	39.79	60.21
8	6	9	5	18	16197	7.82	34		7045	9152	43.5	56.5
4	10	9	6	16	16183	7.82	35		6758	9425	41.76	58.24
8	14	9	6	17	16170	7.81	36		7228	8942	44.7	55.3
5	22	9	6	16	16169	7.81	37		7252	8917	44.85	55.15
7	17	9	6	16	16167	7.81	38		6959	9208	43.04	56.96
11	25	9	4	14	16166	7.81	39		7249	8917	44.84	55.16
8	28	9	6	15	16151	7.8	40		6752	9399	41.81	58.19
4	17	9	6	15	16139	7.8	41	207015	6815	9324	42.23	57.77
3	27	9	6	17	16136	7.79	42		6546	9590	40.57	59.43
8	13	9	5	15	16130	7.79	43		6892	9238	42.73	57.27
9	3	9	5	16	16123	7.79	44		6872	9251	42.62	57.38
6	25	9	5	18	16119	7.79	45		7037	9082	43.66	56.34
8	11	9	3	17	16114	7.78	46		6565	9549	40.74	59.26
4	16	9	5	17	16109	7.78	47		6563	9546	40.74	59.26
4	15	9	4	17	16106	7.78	48		6752	9354	41.92	58.08
4	22	9	4	17	16101	7.78	49		6613	9488	41.07	58.93
5	29	9	6	15	16099	7.78	50		6725	9374	41.77	58.23
7	24	9	6	15	16096	7.78	51		6808	9288	42.3	57.7
6	3	9	4	17	16083	7.77	52		6612	9471	41.11	58.89
3	13	9	6	16	16077	7.77	53		6752	9325	42	58
3	6	9	6	15	16075	7.77	54		6578	9497	40.92	59.08
5	21	9	5	18	16075	7.77	55		7232	8843	44.99	55.01
8	10	9	2	16	16075	7.77	56		6631	9444	41.25	58.75
10	2	9	6	15	16067	7.76	57		6733	9334	41.91	58.09
7	31	9	6	15	16055	7.76	58		6770	9285	42.17	57.83
8	11	9	3	16	16054	7.75	59		6584	9470	41.01	58.99
5	1	9	6	17	16051	7.75	60		6891	9160	42.93	57.07
10	2	9	6	16	16046	7.75	61	207015	6721	9325	41.89	58.11
10	9	9	6	16	16046	7.75	62		6793	9253	42.33	57.67
8	13	9	5	17	16039	7.75	63		6896	9143	43	57
6	19	9	6	16	16038	7.75	64		6945	9093	43.3	56.7
9	3	9	5	15	16036	7.75	65		6885	9151	42.93	57.07
5	21	9	5	15	16033	7.74	66		6834	9199	42.62	57.38
11	13	9	6	16	16028	7.74	67		6629	9399	41.36	58.64
9	16	9	4	17	16026	7.74	68		6250	9776	39	61
5	1	9	6	16	16019	7.74	69		6692	9327	41.78	58.22

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
5	29	9	6	16	16016	7.74	70		6783	9233	42.35	57.65
3	6	9	6	16	16011	7.73	71		6456	9555	40.32	59.68
6	24	9	4	17	16010	7.73	72		6610	9400	41.29	58.71
6	12	9	6	15	15999	7.73	73		6909	9090	43.18	56.82
7	31	9	6	16	15999	7.73	74		6679	9320	41.75	58.25
7	10	9	6	16	15997	7.73	75		6930	9067	43.32	56.68
9	11	9	6	15	15997	7.73	76		6676	9321	41.73	58.27
9	25	9	6	15	15997	7.73	77		6791	9206	42.45	57.55
8	7	9	6	16	15994	7.73	78		7256	8738	45.37	54.63
6	10	9	4	16	15993	7.73	79		6501	9492	40.65	59.35
5	15	9	6	15	15991	7.72	80		7111	8880	44.47	55.53
6	5	9	6	16	15974	7.72	81	207015	7032	8942	44.02	55.98
2	13	9	6	17	15960	7.71	82		6667	9293	41.77	58.23
3	13	9	6	17	15949	7.7	83		6647	9302	41.68	58.32
5	15	9	6	16	15948	7.7	84		6926	9022	43.43	56.57
3	26	9	5	16	15944	7.7	85		6081	9863	38.14	61.86
4	21	9	3	17	15944	7.7	86		6447	9497	40.44	59.56
4	3	9	6	16	15943	7.7	87		6529	9414	40.95	59.05
8	12	9	4	17	15943	7.7	88		6870	9073	43.09	56.91
5	29	9	6	17	15937	7.7	89		6709	9228	42.1	57.9
7	8	9	4	18	15937	7.7	90		6452	9485	40.48	59.52
7	9	9	5	18	15921	7.69	91		7065	8856	44.38	55.62
6	16	9	3	17	15917	7.69	92		6405	9512	40.24	59.76
3	18	9	4	17	15915	7.69	93		6343	9572	39.86	60.14
8	21	9	6	17	15913	7.69	94		6758	9155	42.47	57.53
6	10	9	4	17	15908	7.68	95		6543	9365	41.13	58.87
6	23	9	3	18	15907	7.68	96		6976	8931	43.85	56.15
10	28	9	4	17	15905	7.68	97		6575	9330	41.34	58.66
8	4	9	3	18	15901	7.68	98		6663	9238	41.9	58.1
9	17	9	5	15	15900	7.68	99		6823	9077	42.91	57.09
7	24	9	6	16	15898	7.68	100		7047	8851	44.33	55.67
6	5	9	6	15	15896	7.68	101	207015	6923	8973	43.55	56.45
1	23	9	6	17	15892	7.68	102		6541	9351	41.16	58.84
8	13	9	5	16	15889	7.68	103		6937	8952	43.66	56.34
8	21	9	6	16	15888	7.67	104		6588	9300	41.47	58.53
4	16	9	5	16	15886	7.67	105		6391	9495	40.23	59.77
4	16	9	5	18	15886	7.67	106		7018	8868	44.18	55.82
10	23	9	6	15	15884	7.67	107		7235	8649	45.55	54.45
2	5	9	5	16	15881	7.67	108		5964	9917	37.55	62.45
6	24	9	4	18	15870	7.67	109		6974	8896	43.94	56.06
11	13	9	6	15	15866	7.66	110		6656	9210	41.95	58.05
7	9	9	5	17	15863	7.66	111		6808	9055	42.92	57.08
4	29	9	4	17	15858	7.66	112		6255	9603	39.44	60.56
8	5	9	4	15	15856	7.66	113		6861	8995	43.27	56.73
10	9	9	6	17	15855	7.66	114		6764	9091	42.66	57.34
6	2	9	3	17	15853	7.66	115		6334	9519	39.95	60.05
8	5	9	4	16	15845	7.65	116		7025	8820	44.34	55.66
3	25	9	4	17	15836	7.65	117		6239	9597	39.4	60.6
7	16	9	5	17	15831	7.65	118		6578	9253	41.55	58.45
12	4	9	6	15	15829	7.65	119		6669	9160	42.13	57.87
8	6	9	5	16	15828	7.65	120		6508	9320	41.12	58.88
6	17	9	4	17	15827	7.65	121	207015	6673	9154	42.16	57.84

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	18	9	3	16	15825	7.64	122		6422	9403	40.58	59.42
12	23	9	4	15	15816	7.64	123		6957	8859	43.99	56.01
7	9	9	5	15	15811	7.64	124		6808	9003	43.06	56.94
3	26	9	5	15	15808	7.64	125		6383	9425	40.38	59.62
6	17	9	4	18	15801	7.63	126		7077	8724	44.79	55.21
8	6	9	5	17	15790	7.63	127		6642	9148	42.06	57.94
4	10	9	6	17	15781	7.62	128		6538	9243	41.43	58.57
9	16	9	4	18	15778	7.62	129		6745	9033	42.75	57.25
7	13	9	2	16	15777	7.62	130		6273	9504	39.76	60.24
6	24	9	4	15	15772	7.62	131		6588	9184	41.77	58.23
10	22	9	5	17	15769	7.62	132		6564	9205	41.63	58.37
4	22	9	4	16	15765	7.62	133		6132	9633	38.9	61.1
7	21	9	3	17	15759	7.61	134		6547	9212	41.54	58.46
9	3	9	5	17	15759	7.61	135		7393	8366	46.91	53.09
4	3	9	6	17	15758	7.61	136		6442	9316	40.88	59.12
2	6	9	6	16	15755	7.61	137		6355	9400	40.34	59.66
2	16	9	2	16	15755	7.61	138		6536	9219	41.49	58.51
9	24	9	5	18	15751	7.61	139		6648	9103	42.21	57.79
7	14	9	3	17	15733	7.6	140		6414	9319	40.77	59.23
8	6	9	5	15	15732	7.6	141	207015	6663	9069	42.35	57.65
9	11	9	6	16	15731	7.6	142		6532	9199	41.52	58.48
5	21	9	5	17	15729	7.6	143		6628	9101	42.14	57.86
8	7	9	6	18	15727	7.6	144		7199	8528	45.77	54.23
10	29	9	5	18	15726	7.6	145		7088	8638	45.07	54.93
3	18	9	4	16	15725	7.6	146		6076	9649	38.64	61.36
8	17	9	2	16	15723	7.6	147		6177	9546	39.29	60.71
9	1	9	3	17	15722	7.59	148		6275	9447	39.91	60.09
8	11	9	3	15	15721	7.59	149		6667	9054	42.41	57.59
7	10	9	6	17	15717	7.59	150		7227	8490	45.98	54.02
3	31	9	3	16	15715	7.59	151		6015	9700	38.28	61.72
6	5	9	6	18	15711	7.59	152		7528	8183	47.92	52.08
11	13	9	6	17	15710	7.59	153		6877	8833	43.77	56.23
6	25	9	5	15	15705	7.59	154		6619	9086	42.15	57.85
8	14	9	6	18	15699	7.58	155		7349	8350	46.81	53.19
8	18	9	3	18	15697	7.58	156		6790	8907	43.26	56.74
1	30	9	6	17	15693	7.58	157		6626	9067	42.22	57.78
12	22	9	3	16	15693	7.58	158		6524	9169	41.57	58.43
3	26	9	5	17	15692	7.58	159		6551	9141	41.75	58.25
9	1	9	3	18	15692	7.58	160		6811	8881	43.4	56.6
7	24	9	6	17	15688	7.58	161	207015	6980	8708	44.49	55.51
7	10	9	6	18	15685	7.58	162		7348	8337	46.85	53.15
5	14	9	5	17	15684	7.58	163		6076	9608	38.74	61.26
9	10	9	5	16	15683	7.58	164		6337	9346	40.41	59.59
7	16	9	5	15	15682	7.58	165		6526	9156	41.61	58.39
9	17	9	5	17	15681	7.57	166		6454	9227	41.16	58.84
10	30	9	6	15	15676	7.57	167		6440	9236	41.08	58.92
8	10	9	2	15	15671	7.57	168		6651	9020	42.44	57.56
3	26	9	5	18	15668	7.57	169		6612	9056	42.2	57.8
6	17	9	4	15	15658	7.56	170		6491	9167	41.45	58.55
9	17	9	5	16	15657	7.56	171		6632	9025	42.36	57.64
5	27	9	4	16	15655	7.56	172		6046	9609	38.62	61.38
8	24	9	2	16	15653	7.56	173		6333	9320	40.46	59.54

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	19	9	4	17	15651	7.56	174		6368	9283	40.69	59.31
11	5	9	5	17	15649	7.56	175		6805	8844	43.49	56.51
9	15	9	3	18	15644	7.56	176		7121	8523	45.52	54.48
7	28	9	3	17	15640	7.56	177		6380	9260	40.79	59.21
9	23	9	4	17	15636	7.55	178		6311	9325	40.36	59.64
2	6	9	6	17	15632	7.55	179		6331	9301	40.5	59.5
7	8	9	4	17	15631	7.55	180		6539	9092	41.83	58.17
3	24	9	3	17	15627	7.55	181	207015	6244	9383	39.96	60.04
11	11	9	4	17	15623	7.55	182		6201	9422	39.69	60.31
4	15	9	4	16	15622	7.55	183		6199	9423	39.68	60.32
11	20	9	6	16	15619	7.54	184		6725	8894	43.06	56.94

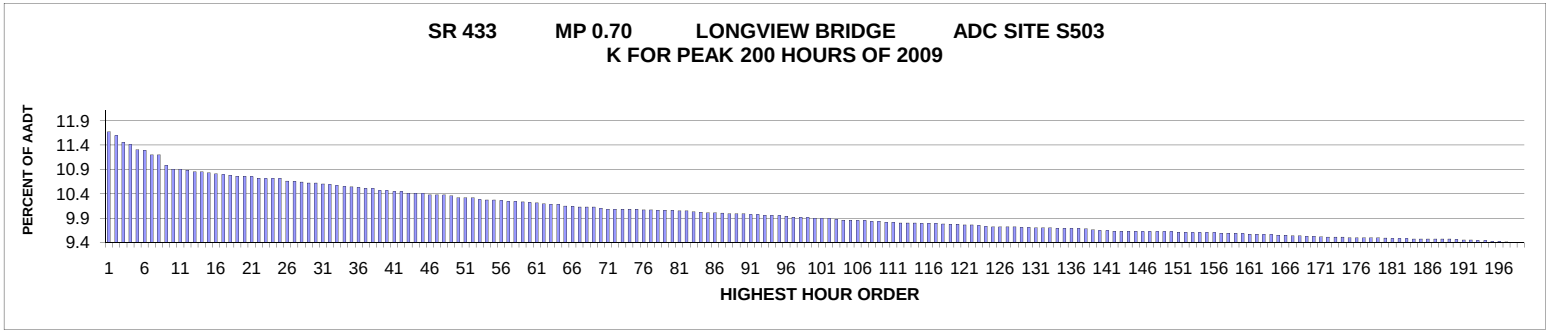

AADT= 19542 **K 30 FACTOR=** 10.62 **K 100 FACTOR=** 9.91 **K 200 FACTOR=** 9.4 **D FACTOR=** 52.17

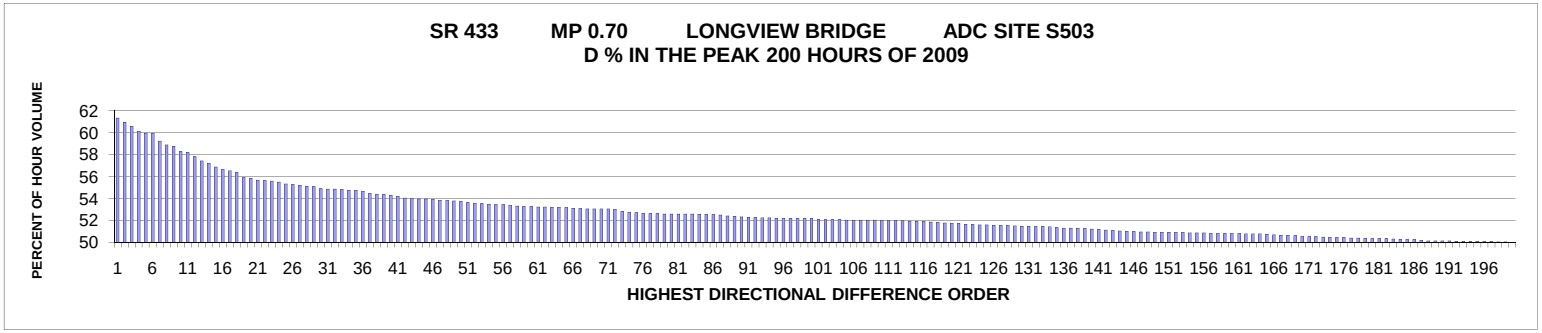

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
9	25	9	6	17	2281	11.67	1	19542	1144	1137	50.15	49.85
8	21	9	6	16	2280	11.67	2		1119	1161	49.08	50.92
7	24	9	6	16	2265	11.59	3		1152	1113	50.86	49.14
8	28	9	6	17	2238	11.45	4		1168	1070	52.19	47.81
8	28	9	6	16	2229	11.41	5		1143	1086	51.28	48.72
8	7	9	6	16	2209	11.3	6		1102	1107	49.89	50.11
8	14	9	6	17	2207	11.29	7		1059	1148	47.98	52.02
8	14	9	6	16	2188	11.2	8		1096	1092	50.09	49.91
8	21	9	6	17	2188	11.2	9		1063	1125	48.58	51.42
8	7	9	6	17	2146	10.98	10		1045	1101	48.7	51.3
7	3	9	6	14	2130	10.9	11		890	1240	41.78	58.22
8	21	9	6	15	2130	10.9	12		1053	1077	49.44	50.56
7	10	9	6	17	2126	10.88	13		1029	1097	48.4	51.6
8	7	9	6	14	2121	10.85	14		1068	1053	50.35	49.65
6	12	9	6	17	2120	10.85	15		1017	1103	47.97	52.03
7	31	9	6	16	2117	10.83	16		1016	1101	47.99	52.01
4	24	9	6	17	2113	10.81	17		922	1191	43.63	56.37

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
9	18	9	6	17	2108	10.79	18		1019	1089	48.34	51.66
7	2	9	5	17	2107	10.78	19		934	1173	44.33	55.67
7	31	9	6	13	2103	10.76	20		1050	1053	49.93	50.07
5	22	9	6	16	2102	10.76	21	19542	957	1145	45.53	54.47
7	10	9	6	16	2100	10.75	22		999	1101	47.57	52.43
5	22	9	6	17	2094	10.72	23		962	1132	45.94	54.06
6	5	9	6	16	2093	10.71	24		1016	1077	48.54	51.46
7	31	9	6	17	2093	10.71	25		1039	1054	49.64	50.36
8	14	9	6	15	2093	10.71	26		993	1100	47.44	52.56
7	3	9	6	12	2084	10.66	27		887	1197	42.56	57.44
8	28	9	6	14	2082	10.65	28		1041	1041	50	50
4	24	9	6	16	2079	10.64	29		941	1138	45.26	54.74
6	19	9	6	16	2076	10.62	30		992	1084	47.78	52.22
7	2	9	5	18	2076	10.62	31		888	1188	42.77	57.23
5	22	9	6	18	2072	10.6	32		898	1174	43.34	56.66
6	19	9	6	17	2069	10.59	33		998	1071	48.24	51.76
7	31	9	6	15	2065	10.57	34		1013	1052	49.06	50.94
8	21	9	6	14	2062	10.55	35		1083	979	52.52	47.48
5	1	9	6	17	2059	10.54	36		1038	1021	50.41	49.59
10	9	9	6	17	2057	10.53	37		1018	1039	49.49	50.51
7	3	9	6	15	2053	10.51	38		837	1216	40.77	59.23
7	24	9	6	17	2053	10.51	39		964	1089	46.96	53.04
10	2	9	6	17	2045	10.46	40		1010	1035	49.39	50.61
7	3	9	6	16	2044	10.46	41	19542	798	1246	39.04	60.96
7	2	9	5	16	2041	10.44	42		905	1136	44.34	55.66
8	21	9	6	13	2041	10.44	43		1027	1014	50.32	49.68
7	10	9	6	18	2035	10.41	44		976	1059	47.96	52.04
9	18	9	6	16	2035	10.41	45		982	1053	48.26	51.74
8	21	9	6	18	2033	10.4	46		951	1082	46.78	53.22
8	20	9	5	17	2028	10.38	47		1056	972	52.07	47.93
8	28	9	6	15	2028	10.38	48		952	1076	46.94	53.06
12	4	9	6	17	2028	10.38	49		1009	1019	49.75	50.25
10	9	9	6	16	2024	10.36	50		957	1067	47.28	52.72
5	22	9	6	15	2017	10.32	51		877	1140	43.48	56.52
8	14	9	6	18	2017	10.32	52		935	1082	46.36	53.64
3	27	9	6	17	2016	10.32	53		807	1209	40.03	59.97
7	5	9	1	14	2008	10.28	54		1232	776	61.35	38.65
6	12	9	6	16	2007	10.27	55		901	1106	44.89	55.11
8	14	9	6	14	2006	10.27	56		981	1025	48.9	51.1
7	3	9	6	13	2005	10.26	57		914	1091	45.59	54.41
8	20	9	5	16	2002	10.24	58		1096	906	54.75	45.25
7	5	9	1	15	2001	10.24	59		1212	789	60.57	39.43
7	17	9	6	17	2000	10.23	60		963	1037	48.15	51.85
8	17	9	2	17	1998	10.22	61	19542	994	1004	49.75	50.25
11	25	9	4	17	1995	10.21	62		943	1052	47.27	52.73
7	17	9	6	16	1991	10.19	63		956	1035	48.02	51.98
4	24	9	6	15	1990	10.18	64		858	1132	43.12	56.88
5	8	9	6	17	1990	10.18	65		957	1033	48.09	51.91
6	5	9	6	17	1983	10.15	66		984	999	49.62	50.38
8	7	9	6	15	1982	10.14	67		1000	982	50.45	49.55
5	22	9	6	14	1979	10.13	68		884	1095	44.67	55.33
7	10	9	6	15	1979	10.13	69		948	1031	47.9	52.1

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	23	9	1	15	1979	10.13	70		1186	793	59.93	40.07
7	10	9	6	14	1974	10.1	71		946	1028	47.92	52.08
6	5	9	6	18	1970	10.08	72		954	1016	48.43	51.57
7	6	9	2	16	1970	10.08	73		1070	900	54.31	45.69
8	5	9	4	17	1970	10.08	74		1011	959	51.32	48.68
4	17	9	6	17	1969	10.08	75		966	1003	49.06	50.94
7	24	9	6	15	1969	10.08	76		995	974	50.53	49.47
7	31	9	6	14	1968	10.07	77		933	1035	47.41	52.59
8	24	9	2	16	1968	10.07	78		1015	953	51.58	48.42
7	2	9	5	15	1966	10.06	79		908	1058	46.19	53.81
10	2	9	6	16	1966	10.06	80		967	999	49.19	50.81
6	26	9	6	17	1965	10.06	81	19542	915	1050	46.56	53.44
10	26	9	2	16	1964	10.05	82		1006	958	51.22	48.78
8	28	9	6	13	1963	10.05	83		1011	952	51.5	48.5
7	24	9	6	13	1961	10.03	84		983	978	50.13	49.87
7	24	9	6	14	1959	10.02	85		978	981	49.92	50.08
4	10	9	6	16	1956	10.01	86		918	1038	46.93	53.07
7	31	9	6	18	1956	10.01	87		909	1047	46.47	53.53
7	6	9	2	15	1955	10	88		1072	883	54.83	45.17
7	3	9	6	11	1953	9.99	89		815	1138	41.73	58.27
7	6	9	2	14	1952	9.99	90		1071	881	54.87	45.13
10	23	9	6	17	1952	9.99	91		914	1038	46.82	53.18
6	26	9	6	15	1949	9.97	92		912	1037	46.79	53.21
7	24	9	6	18	1948	9.97	93		889	1059	45.64	54.36
8	7	9	6	18	1946	9.96	94		896	1050	46.04	53.96
9	25	9	6	18	1946	9.96	95		866	1080	44.5	55.5
6	26	9	6	16	1945	9.95	96		957	988	49.2	50.8
3	6	9	6	17	1943	9.94	97		932	1011	47.97	52.03
4	3	9	6	17	1938	9.92	98		984	954	50.77	49.23
12	23	9	4	17	1938	9.92	99		919	1019	47.42	52.58
12	4	9	6	16	1937	9.91	100		894	1043	46.15	53.85
8	26	9	4	16	1935	9.9	101	19542	1016	919	52.51	47.49
8	28	9	6	18	1933	9.89	102		923	1010	47.75	52.25
6	19	9	6	18	1932	9.89	103		853	1079	44.15	55.85
8	31	9	2	17	1929	9.87	104		983	946	50.96	49.04
8	5	9	4	16	1927	9.86	105		934	993	48.47	51.53
7	17	9	6	15	1926	9.86	106		904	1022	46.94	53.06
8	17	9	2	16	1925	9.85	107		960	965	49.87	50.13
8	24	9	2	17	1925	9.85	108		988	937	51.32	48.68
8	26	9	4	17	1921	9.83	109		977	944	50.86	49.14
12	23	9	4	16	1921	9.83	110		939	982	48.88	51.12
4	3	9	6	16	1918	9.81	111		922	996	48.07	51.93
3	27	9	6	18	1917	9.81	112		809	1108	42.2	57.8
8	19	9	4	16	1916	9.8	113		973	943	50.78	49.22
7	6	9	2	13	1915	9.8	114		1030	885	53.79	46.21
8	3	9	2	16	1915	9.8	115		976	939	50.97	49.03
8	19	9	4	17	1914	9.79	116		999	915	52.19	47.81
7	17	9	6	13	1913	9.79	117		918	995	47.99	52.01
10	16	9	6	17	1913	9.79	118		907	1006	47.41	52.59
2	13	9	6	17	1911	9.78	119		856	1055	44.79	55.21
8	6	9	5	15	1910	9.77	120		974	936	50.99	49.01
7	9	9	5	17	1909	9.77	121	19542	924	985	48.4	51.6

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
3	13	9	6	17	1907	9.76	122		895	1012	46.93	53.07
10	2	9	6	18	1907	9.76	123		889	1018	46.62	53.38
4	17	9	6	16	1905	9.75	124		956	949	50.18	49.82
8	1	9	7	12	1901	9.73	125		901	1000	47.4	52.6
8	29	9	7	13	1900	9.72	126		913	987	48.05	51.95
10	30	9	6	17	1900	9.72	127		888	1012	46.74	53.26
2	27	9	6	17	1899	9.72	128		911	988	47.97	52.03
10	30	9	6	16	1899	9.72	129		932	967	49.08	50.92
8	1	9	7	13	1898	9.71	130		886	1012	46.68	53.32
10	16	9	6	16	1898	9.71	131		873	1025	46	54
1	30	9	6	17	1895	9.7	132		905	990	47.76	52.24
7	23	9	5	17	1895	9.7	133		962	933	50.77	49.23
8	13	9	5	17	1895	9.7	134		932	963	49.18	50.82
11	6	9	6	16	1894	9.69	135		847	1047	44.72	55.28
2	6	9	6	17	1893	9.69	136		854	1039	45.11	54.89
2	27	9	6	16	1893	9.69	137		913	980	48.23	51.77
8	14	9	6	13	1893	9.69	138		966	927	51.03	48.97
11	25	9	4	15	1891	9.68	139		902	989	47.7	52.3
4	10	9	6	17	1887	9.66	140		928	959	49.18	50.82
8	17	9	2	15	1884	9.64	141	19542	940	944	49.89	50.11
7	10	9	6	13	1883	9.64	142		951	932	50.5	49.5
7	2	9	5	13	1882	9.63	143		897	985	47.66	52.34
8	3	9	2	17	1882	9.63	144		888	994	47.18	52.82
8	25	9	3	17	1881	9.63	145		966	915	51.36	48.64
9	18	9	6	18	1881	9.63	146		874	1007	46.46	53.54
2	13	9	6	16	1880	9.62	147		861	1019	45.8	54.2
2	20	9	6	17	1880	9.62	148		967	913	51.44	48.56
1	23	9	6	17	1879	9.62	149		924	955	49.18	50.82
4	3	9	6	18	1879	9.62	150		874	1005	46.51	53.49
5	8	9	6	16	1879	9.62	151		869	1010	46.25	53.75
7	1	9	4	17	1878	9.61	152		940	938	50.05	49.95
7	17	9	6	14	1878	9.61	153		919	959	48.94	51.06
7	22	9	4	17	1877	9.6	154		946	931	50.4	49.6
8	20	9	5	15	1877	9.6	155		955	922	50.88	49.12
9	1	9	3	16	1877	9.6	156		977	900	52.05	47.95
8	6	9	5	16	1876	9.6	157		946	930	50.43	49.57
7	3	9	6	17	1875	9.59	158		747	1128	39.84	60.16
12	18	9	6	17	1875	9.59	159		903	972	48.16	51.84
10	9	9	6	18	1874	9.59	160		896	978	47.81	52.19
7	16	9	5	17	1873	9.58	161	19542	924	949	49.33	50.67
8	3	9	2	15	1870	9.57	162		887	983	47.43	52.57
8	17	9	2	13	1870	9.57	163		934	936	49.95	50.05
8	13	9	5	15	1869	9.56	164		904	965	48.37	51.63
8	16	9	1	15	1868	9.56	165		1030	838	55.14	44.86
1	16	9	6	17	1867	9.55	166		895	972	47.94	52.06
11	25	9	4	14	1867	9.55	167		893	974	47.83	52.17
8	3	9	2	14	1865	9.54	168		960	905	51.47	48.53
9	2	9	4	16	1865	9.54	169		938	927	50.29	49.71
5	1	9	6	16	1863	9.53	170		914	949	49.06	50.94
8	20	9	5	14	1863	9.53	171		930	933	49.92	50.08
7	6	9	2	17	1860	9.52	172		979	881	52.63	47.37
6	26	9	6	14	1859	9.51	173		927	932	49.87	50.13

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	20	9	5	18	1859	9.51	174		923	936	49.65	50.35
4	24	9	6	18	1858	9.51	175		766	1092	41.23	58.77
3	13	9	6	16	1857	9.5	176		880	977	47.39	52.61
11	25	9	4	16	1857	9.5	177		855	1002	46.04	53.96
7	30	9	5	17	1856	9.5	178		915	941	49.3	50.7
9	18	9	6	15	1856	9.5	179		870	986	46.88	53.13
10	9	9	6	15	1856	9.5	180		855	1001	46.07	53.93
7	20	9	2	17	1854	9.49	181	19542	919	935	49.57	50.43
11	20	9	6	16	1853	9.48	182		867	986	46.79	53.21
12	11	9	6	17	1853	9.48	183		869	984	46.9	53.1
8	22	9	7	14	1852	9.48	184		940	912	50.76	49.24
1	16	9	6	16	1851	9.47	185		913	938	49.32	50.68
8	6	9	5	17	1851	9.47	186		885	966	47.81	52.19
8	23	9	1	16	1851	9.47	187		1090	761	58.89	41.11
10	16	9	6	15	1851	9.47	188		822	1029	44.41	55.59
8	4	9	3	17	1850	9.47	189		881	969	47.62	52.38
8	20	9	5	13	1850	9.47	190		974	876	52.65	47.35
7	1	9	4	16	1848	9.46	191		882	966	47.73	52.27
6	12	9	6	18	1847	9.45	192		814	1033	44.07	55.93
8	3	9	2	13	1846	9.45	193		984	862	53.3	46.7
7	21	9	3	17	1844	9.44	194		944	900	51.19	48.81
8	6	9	5	18	1844	9.44	195		874	970	47.4	52.6
8	16	9	1	17	1840	9.42	196		1006	834	54.67	45.33
8	22	9	7	13	1840	9.42	197		893	947	48.53	51.47
3	20	9	6	17	1838	9.41	198		856	982	46.57	53.43
5	8	9	6	18	1837	9.4	199		859	978	46.76	53.24
7	2	9	5	14	1837	9.4	200		829	1008	45.13	54.87

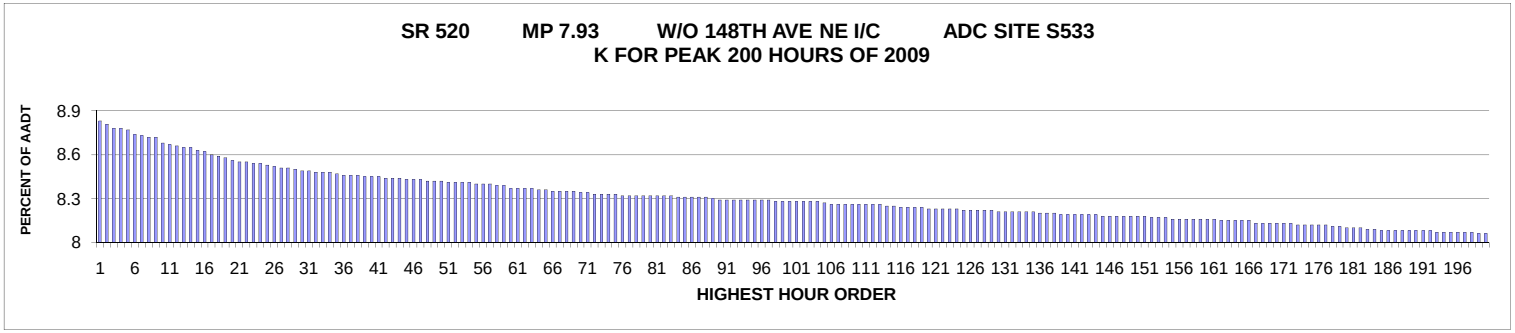

AADT= 97510 **K 30 FACTOR=** 8.49 **K 100 FACTOR=** 8.28 **K 200 FACTOR=** 8.06 **D FACTOR=** 55.58

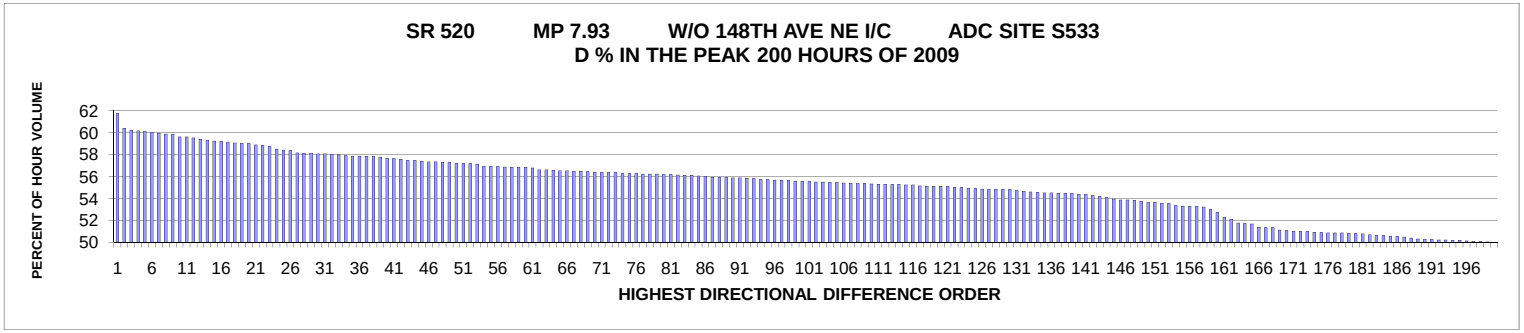

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
10	15	9	5	9	8614	8.83	1	97510	4611	4003	53.53	46.47
10	2	9	6	9	8593	8.81	2		4858	3735	56.53	43.47
10	1	9	5	9	8562	8.78	3		4698	3864	54.87	45.13
8	26	9	4	10	8560	8.78	4		4963	3597	57.98	42.02
10	27	9	3	9	8554	8.77	5		4692	3862	54.85	45.15
4	28	9	3	9	8525	8.74	6		4795	3730	56.25	43.75
8	20	9	5	10	8513	8.73	7		4870	3643	57.21	42.79
9	29	9	3	9	8500	8.72	8		4645	3855	54.65	45.35
9	15	9	3	9	8498	8.72	9		4770	3728	56.13	43.87
10	13	9	3	9	8468	8.68	10		4591	3877	54.22	45.78
4	29	9	4	9	8451	8.67	11		4660	3791	55.14	44.86
9	14	9	2	9	8440	8.66	12		4691	3749	55.58	44.42
5	12	9	3	9	8439	8.65	13		4664	3775	55.27	44.73
5	13	9	4	9	8430	8.65	14		4793	3637	56.86	43.14
9	1	9	3	9	8416	8.63	15		4785	3631	56.86	43.14
9	9	9	4	9	8409	8.62	16		4681	3728	55.67	44.33
5	26	9	3	9	8387	8.6	17		4701	3686	56.05	43.95

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
10	22	9	5	9	8376	8.59	18		4627	3749	55.24	44.76
9	21	9	2	9	8368	8.58	19		4679	3689	55.92	44.08
10	15	9	5	10	8349	8.56	20		4784	3565	57.3	42.7
10	28	9	4	9	8337	8.55	21	97510	4613	3724	55.33	44.67
9	14	9	2	10	8333	8.55	22		5017	3316	60.21	39.79
9	30	9	4	9	8332	8.54	23		4594	3738	55.14	44.86
10	1	9	5	10	8324	8.54	24		4713	3611	56.62	43.38
4	15	9	4	9	8318	8.53	25		4644	3674	55.83	44.17
10	30	9	6	16	8305	8.52	26		4300	4005	51.78	48.22
4	23	9	5	9	8299	8.51	27		4559	3740	54.93	45.07
9	29	9	3	10	8297	8.51	28		4819	3478	58.08	41.92
5	20	9	4	9	8285	8.5	29		4633	3652	55.92	44.08
10	22	9	5	8	8283	8.49	30		4060	4223	49.02	50.98
10	27	9	3	10	8278	8.49	31		4709	3569	56.89	43.11
5	12	9	3	8	8271	8.48	32		4183	4088	50.57	49.43
9	22	9	3	9	8271	8.48	33		4571	3700	55.27	44.73
10	13	9	3	10	8270	8.48	34		4751	3519	57.45	42.55
8	26	9	4	9	8261	8.47	35		4491	3770	54.36	45.64
10	14	9	4	9	8253	8.46	36		4397	3856	53.28	46.72
4	16	9	5	9	8252	8.46	37		4637	3615	56.19	43.81
10	14	9	4	10	8248	8.46	38		4638	3610	56.23	43.77
9	15	9	3	10	8242	8.45	39		4866	3376	59.04	40.96
9	17	9	5	10	8241	8.45	40		4692	3549	56.93	43.07
4	27	9	2	9	8237	8.45	41	97510	4552	3685	55.26	44.74
9	16	9	4	9	8234	8.44	42		4526	3708	54.97	45.03
6	9	9	3	9	8233	8.44	43		4504	3729	54.71	45.29
9	30	9	4	8	8231	8.44	44		3976	4255	48.31	51.69
5	19	9	3	9	8221	8.43	45		4560	3661	55.47	44.53
4	28	9	3	8	8218	8.43	46		4158	4060	50.6	49.4
5	7	9	5	9	8218	8.43	47		4594	3624	55.9	44.1
4	29	9	4	8	8212	8.42	48		4124	4088	50.22	49.78
10	12	9	2	9	8207	8.42	49		4588	3619	55.9	44.1
6	10	9	4	9	8206	8.42	50		4468	3738	54.45	45.55
9	16	9	4	8	8204	8.41	51		4096	4108	49.93	50.07
9	18	9	6	9	8201	8.41	52		4470	3731	54.51	45.49
9	8	9	3	9	8198	8.41	53		4619	3579	56.34	43.66
6	22	9	2	9	8196	8.41	54		4634	3562	56.54	43.46
9	24	9	5	9	8194	8.4	55		4406	3788	53.77	46.23
10	22	9	5	10	8191	8.4	56		4680	3511	57.14	42.86
1	29	9	5	9	8186	8.4	57		4625	3561	56.5	43.5
5	4	9	2	9	8184	8.39	58		4559	3625	55.71	44.29
9	8	9	3	10	8181	8.39	59		4731	3450	57.83	42.17
2	5	9	5	9	8164	8.37	60		4533	3631	55.52	44.48
10	1	9	5	8	8162	8.37	61	97510	3972	4190	48.66	51.34
5	7	9	5	10	8161	8.37	62		4558	3603	55.85	44.15
9	3	9	5	9	8161	8.37	63		4513	3648	55.3	44.7
2	12	9	5	9	8155	8.36	64		4543	3612	55.71	44.29
9	30	9	4	10	8150	8.36	65		4738	3412	58.13	41.87
2	4	9	4	9	8143	8.35	66		4443	3700	54.56	45.44
4	28	9	3	10	8140	8.35	67		4820	3320	59.21	40.79
10	20	9	3	9	8139	8.35	68		4384	3755	53.86	46.14
4	3	9	6	9	8138	8.35	69		4529	3609	55.65	44.35

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
4	8	9	4	9	8135	8.34	70		4588	3547	56.4	43.6
5	13	9	4	8	8131	8.34	71		3983	4148	48.99	51.01
4	14	9	3	9	8125	8.33	72		4358	3767	53.64	46.36
4	30	9	5	9	8125	8.33	73		4500	3625	55.38	44.62
1	23	9	6	9	8121	8.33	74		4613	3508	56.8	43.2
9	15	9	3	8	8120	8.33	75		3978	4142	48.99	51.01
6	5	9	6	9	8116	8.32	76		4452	3664	54.85	45.15
9	9	9	4	8	8116	8.32	77		4046	4070	49.85	50.15
4	30	9	5	8	8115	8.32	78		4048	4067	49.88	50.12
8	25	9	3	10	8114	8.32	79		4789	3325	59.02	40.98
1	28	9	4	9	8111	8.32	80		4485	3626	55.3	44.7
10	13	9	3	8	8110	8.32	81	97510	3983	4127	49.11	50.89
9	28	9	2	9	8109	8.32	82		4493	3616	55.41	44.59
10	28	9	4	10	8109	8.32	83		4691	3418	57.85	42.15
5	20	9	4	8	8107	8.31	84		4087	4020	50.41	49.59
5	13	9	4	10	8106	8.31	85		4867	3239	60.04	39.96
10	28	9	4	8	8106	8.31	86		3867	4239	47.71	52.29
5	11	9	2	9	8103	8.31	87		4560	3543	56.28	43.72
9	2	9	4	10	8101	8.31	88		4650	3451	57.4	42.6
9	22	9	3	10	8097	8.3	89		4653	3444	57.47	42.53
6	16	9	3	9	8088	8.29	90		4436	3652	54.85	45.15
10	12	9	2	10	8088	8.29	91		4814	3274	59.52	40.48
2	2	9	2	9	8087	8.29	92		4538	3549	56.11	43.89
9	16	9	4	10	8087	8.29	93		4698	3389	58.09	41.91
5	21	9	5	9	8086	8.29	94		4307	3779	53.26	46.74
9	17	9	5	9	8085	8.29	95		4439	3646	54.9	45.1
8	25	9	3	9	8083	8.29	96		4384	3699	54.24	45.76
6	30	9	3	9	8081	8.29	97		4369	3712	54.07	45.93
2	3	9	3	9	8075	8.28	98		4400	3675	54.49	45.51
6	24	9	4	9	8075	8.28	99		4478	3597	55.46	44.54
9	24	9	5	8	8074	8.28	100		4057	4017	50.25	49.75
9	9	9	4	10	8073	8.28	101	97510	4716	3357	58.42	41.58
9	24	9	5	10	8070	8.28	102		4588	3482	56.85	43.15
4	15	9	4	8	8069	8.28	103		4121	3948	51.07	48.93
8	4	9	3	10	8069	8.28	104		4682	3387	58.02	41.98
1	22	9	5	9	8060	8.27	105		4515	3545	56.02	43.98
4	14	9	3	10	8059	8.26	106		4716	3343	58.52	41.48
6	15	9	2	10	8056	8.26	107		4779	3277	59.32	40.68
9	18	9	6	10	8055	8.26	108		4653	3402	57.77	42.23
10	14	9	4	8	8054	8.26	109		3935	4119	48.86	51.14
8	24	9	2	9	8053	8.26	110		4583	3470	56.91	43.09
6	11	9	5	9	8050	8.26	111		4312	3738	53.57	46.43
9	14	9	2	8	8050	8.26	112		4025	4025	50	50
10	15	9	5	8	8050	8.26	113		3917	4133	48.66	51.34
2	23	9	2	9	8047	8.25	114		4521	3526	56.18	43.82
2	4	9	4	10	8046	8.25	115		4782	3264	59.43	40.57
6	29	9	2	9	8038	8.24	116		4389	3649	54.6	45.4
6	30	9	3	10	8035	8.24	117		4597	3438	57.21	42.79
5	19	9	3	10	8034	8.24	118		4732	3302	58.9	41.1
10	16	9	6	9	8034	8.24	119		4259	3775	53.01	46.99
9	29	9	3	8	8029	8.23	120		3952	4077	49.22	50.78
2	25	9	4	9	8025	8.23	121	97510	4522	3503	56.35	43.65

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
6	8	9	2	9	8022	8.23	122		4441	3581	55.36	44.64
5	20	9	4	10	8021	8.23	123		4644	3377	57.9	42.1
10	20	9	3	10	8021	8.23	124		4522	3499	56.38	43.62
1	28	9	4	10	8018	8.22	125		4808	3210	59.97	40.03
2	5	9	5	8	8015	8.22	126		4047	3968	50.49	49.51
9	10	9	5	9	8014	8.22	127		4146	3868	51.73	48.27
5	28	9	5	9	8013	8.22	128		4367	3646	54.5	45.5
1	15	9	5	9	8012	8.22	129		4397	3615	54.88	45.12
9	17	9	5	8	8009	8.21	130		4001	4008	49.96	50.04
9	25	9	6	9	8006	8.21	131		4355	3651	54.4	45.6
10	19	9	2	9	8006	8.21	132		4295	3711	53.65	46.35
1	30	9	6	9	8005	8.21	133		4404	3601	55.02	44.98
10	21	9	4	9	8005	8.21	134		4262	3743	53.24	46.76
6	25	9	5	9	8002	8.21	135		4270	3732	53.36	46.64
1	29	9	5	10	7999	8.2	136		4768	3231	59.61	40.39
6	17	9	4	9	7993	8.2	137		4406	3587	55.12	44.88
4	13	9	2	9	7991	8.2	138		4514	3477	56.49	43.51
9	21	9	2	10	7990	8.19	139		4693	3297	58.74	41.26
6	24	9	4	10	7989	8.19	140		4646	3343	58.15	41.85
8	20	9	5	9	7989	8.19	141	97510	4487	3502	56.16	43.84
6	10	9	4	8	7988	8.19	142		3775	4213	47.26	52.74
5	7	9	5	8	7987	8.19	143		3928	4059	49.18	50.82
8	12	9	4	10	7985	8.19	144		4724	3261	59.16	40.84
1	15	9	5	8	7979	8.18	145		3920	4059	49.13	50.87
2	18	9	4	9	7975	8.18	146		4516	3459	56.63	43.37
8	21	9	6	9	7975	8.18	147		4414	3561	55.35	44.65
4	15	9	4	10	7974	8.18	148		4723	3251	59.23	40.77
9	28	9	2	10	7974	8.18	149		4615	3359	57.88	42.12
6	25	9	5	10	7973	8.18	150		4635	3338	58.13	41.87
10	13	9	3	17	7973	8.18	151		4055	3918	50.86	49.14
5	8	9	6	9	7965	8.17	152		4567	3398	57.34	42.66
7	9	9	5	10	7964	8.17	153		4608	3356	57.86	42.14
8	18	9	3	10	7962	8.17	154		4551	3411	57.16	42.84
4	16	9	5	8	7961	8.16	155		3999	3962	50.23	49.77
5	4	9	2	8	7959	8.16	156		3963	3996	49.79	50.21
9	1	9	3	8	7958	8.16	157		4003	3955	50.3	49.7
6	16	9	3	10	7955	8.16	158		4580	3375	57.57	42.43
6	23	9	3	9	7955	8.16	159		4286	3669	53.88	46.12
10	20	9	3	8	7955	8.16	160		3809	4146	47.88	52.12
4	22	9	4	9	7953	8.16	161	97510	4381	3572	55.09	44.91
5	12	9	3	10	7950	8.15	162		4739	3211	59.61	40.39
5	21	9	5	8	7949	8.15	163		4017	3932	50.53	49.47
2	27	9	6	9	7947	8.15	164		4425	3522	55.68	44.32
4	16	9	5	10	7945	8.15	165		4637	3308	58.36	41.64
5	26	9	3	8	7945	8.15	166		4037	3908	50.81	49.19
8	27	9	5	9	7930	8.13	167		4402	3528	55.51	44.49
7	22	9	4	9	7928	8.13	168		4271	3657	53.87	46.13
7	30	9	5	10	7926	8.13	169		4321	3605	54.52	45.48
8	31	9	2	10	7926	8.13	170		4766	3160	60.13	39.87
2	19	9	5	9	7925	8.13	171		4459	3466	56.26	43.74
4	21	9	3	9	7923	8.13	172		4222	3701	53.29	46.71
6	8	9	2	8	7919	8.12	173		3849	4070	48.6	51.4

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
6	12	9	6	9	7918	8.12	174		4403	3515	55.61	44.39
6	23	9	3	10	7917	8.12	175		4564	3353	57.65	42.35
6	1	9	2	9	7915	8.12	176		4451	3464	56.23	43.77
4	29	9	4	10	7914	8.12	177		4674	3240	59.06	40.94
9	23	9	4	8	7907	8.11	178		3897	4010	49.29	50.71
5	11	9	2	10	7906	8.11	179		4776	3130	60.41	39.59
2	3	9	3	10	7903	8.1	180		4732	3171	59.88	40.12
4	21	9	3	8	7899	8.1	181	97510	3901	3998	49.39	50.61
2	12	9	5	10	7894	8.1	182		4723	3171	59.83	40.17
2	23	9	2	8	7888	8.09	183		3870	4018	49.06	50.94
9	1	9	3	10	7888	8.09	184		4640	3248	58.82	41.18
6	11	9	5	10	7883	8.08	185		4460	3423	56.58	43.42
7	13	9	2	10	7883	8.08	186		4744	3139	60.18	39.82
5	29	9	6	10	7881	8.08	187		4438	3443	56.31	43.69
6	16	9	3	8	7880	8.08	188		3871	4009	49.12	50.88
10	30	9	6	9	7880	8.08	189		4251	3629	53.95	46.05
5	8	9	6	10	7877	8.08	190		4543	3334	57.67	42.33
10	20	9	3	17	7877	8.08	191		3955	3922	50.21	49.79
8	13	9	5	9	7875	8.08	192		4343	3532	55.15	44.85
9	21	9	2	8	7873	8.07	193		3912	3961	49.69	50.31
2	13	9	6	9	7870	8.07	194		4404	3466	55.96	44.04
6	9	9	3	10	7870	8.07	195		4442	3428	56.44	43.56
4	13	9	2	10	7869	8.07	196		4858	3011	61.74	38.26
6	18	9	5	9	7868	8.07	197		4372	3496	55.57	44.43
8	5	9	4	10	7865	8.07	198		4509	3356	57.33	42.67
2	17	9	3	9	7864	8.06	199		4475	3389	56.9	43.1
8	27	9	5	10	7864	8.06	200		4510	3354	57.35	42.65

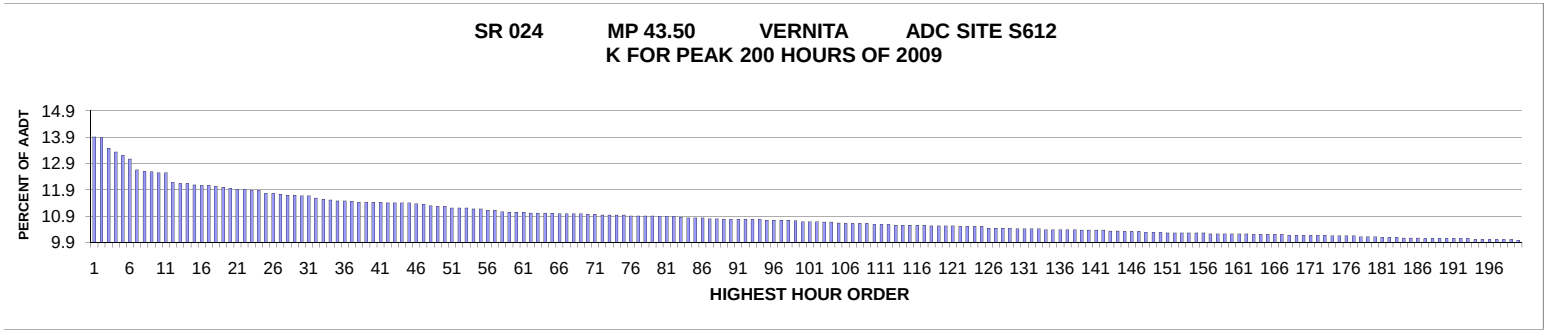

AADT= 3666 **K 30 FACTOR=** 11.67 **K 100 FACTOR=** 10.69 **K 200 FACTOR=** 9.98 **D FACTOR=** 54.71

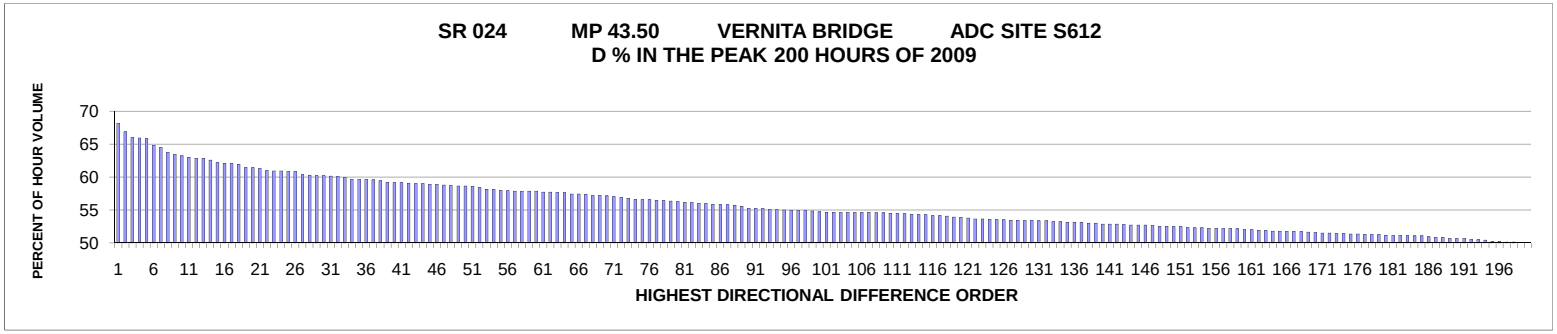

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
9	25	9	6	16	510	13.91	1	3666	222	288	43.53	56.47
9	11	9	6	17	509	13.88	2		226	283	44.4	55.6
10	2	9	6	17	494	13.48	3		208	286	42.11	57.89
9	4	9	6	17	489	13.34	4		226	263	46.22	53.78
8	29	9	7	16	484	13.2	5		295	189	60.95	39.05
6	26	9	6	16	479	13.07	6		208	271	43.42	56.58
9	25	9	6	18	464	12.66	7		228	236	49.14	50.86
9	25	9	6	17	462	12.6	8		190	272	41.13	58.87
10	9	9	6	16	461	12.58	9		218	243	47.29	52.71
9	4	9	6	18	460	12.55	10		238	222	51.74	48.26
10	9	9	6	18	460	12.55	11		234	226	50.87	49.13
10	9	9	6	17	446	12.17	12		202	244	45.29	54.71
6	28	9	1	15	445	12.14	13		184	261	41.35	58.65
9	18	9	6	17	445	12.14	14		201	244	45.17	54.83
9	27	9	1	15	443	12.08	15		196	247	44.24	55.76
10	2	9	6	18	442	12.06	16		198	244	44.8	55.2
10	23	9	6	16	442	12.06	17		229	213	51.81	48.19

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	28	9	6	16	441	12.03	18		226	215	51.25	48.75
8	29	9	7	17	440	12	19		258	182	58.64	41.36
8	29	9	7	15	438	11.95	20		278	160	63.47	36.53
10	2	9	6	16	437	11.92	21	3666	193	244	44.16	55.84
10	11	9	1	16	437	11.92	22		187	250	42.79	57.21
8	14	9	6	16	435	11.87	23		203	232	46.67	53.33
10	8	9	5	17	435	11.87	24		208	227	47.82	52.18
5	8	9	6	16	431	11.76	25		223	208	51.74	48.26
10	4	9	1	16	431	11.76	26		194	237	45.01	54.99
6	19	9	6	16	430	11.73	27		217	213	50.47	49.53
6	26	9	6	17	429	11.7	28		168	261	39.16	60.84
9	4	9	6	16	429	11.7	29		215	214	50.12	49.88
5	8	9	6	18	428	11.67	30		173	255	40.42	59.58
7	5	9	1	16	428	11.67	31		185	243	43.22	56.78
10	4	9	1	18	425	11.59	32		199	226	46.82	53.18
10	11	9	1	17	423	11.54	33		194	229	45.86	54.14
9	7	9	2	16	422	11.51	34		174	248	41.23	58.77
7	5	9	1	14	421	11.48	35		170	251	40.38	59.62
9	27	9	1	18	421	11.48	36		225	196	53.44	46.56
9	6	9	1	15	420	11.46	37		202	218	48.1	51.9
6	19	9	6	17	419	11.43	38		169	250	40.33	59.67
7	5	9	1	15	419	11.43	39		182	237	43.44	56.56
9	24	9	5	17	419	11.43	40		169	250	40.33	59.67
10	16	9	6	17	419	11.43	41	3666	199	220	47.49	52.51
4	4	9	7	18	418	11.4	42		147	271	35.17	64.83
4	5	9	1	17	418	11.4	43		210	208	50.24	49.76
6	21	9	1	17	418	11.4	44		228	190	54.55	45.45
7	3	9	6	15	418	11.4	45		176	242	42.11	57.89
5	22	9	6	17	417	11.37	46		229	188	54.92	45.08
10	15	9	5	17	416	11.35	47		195	221	46.88	53.13
10	1	9	5	17	414	11.29	48		192	222	46.38	53.62
8	28	9	6	17	413	11.27	49		173	240	41.89	58.11
10	11	9	1	15	413	11.27	50		164	249	39.71	60.29
9	6	9	1	12	411	11.21	51		146	265	35.52	64.48
9	27	9	1	16	411	11.21	52		210	201	51.09	48.91
10	3	9	7	17	411	11.21	53		175	236	42.58	57.42
6	21	9	1	14	410	11.18	54		189	221	46.1	53.9
9	26	9	7	16	410	11.18	55		155	255	37.8	62.2
4	4	9	7	17	408	11.13	56		139	269	34.07	65.93
9	11	9	6	18	408	11.13	57		188	220	46.08	53.92
7	5	9	1	18	406	11.07	58		212	194	52.22	47.78
7	2	9	5	17	405	11.05	59		220	185	54.32	45.68
9	5	9	7	13	405	11.05	60		182	223	44.94	55.06
10	10	9	7	17	405	11.05	61	3666	156	249	38.52	61.48
6	21	9	1	16	404	11.02	62		213	191	52.72	47.28
6	26	9	6	18	404	11.02	63		192	212	47.52	52.48
7	5	9	1	17	404	11.02	64		197	207	48.76	51.24
8	9	9	1	14	404	11.02	65		166	238	41.09	58.91
3	27	9	6	17	403	10.99	66		183	220	45.41	54.59
7	10	9	6	16	403	10.99	67		183	220	45.41	54.59
9	11	9	6	16	403	10.99	68		197	206	48.88	51.12
10	16	9	6	18	403	10.99	69		181	222	44.91	55.09

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
10	16	9	6	16	402	10.97	70		180	222	44.78	55.22
10	18	9	1	18	402	10.97	71		213	189	52.99	47.01
5	8	9	6	17	401	10.94	72		169	232	42.14	57.86
6	26	9	6	15	401	10.94	73		171	230	42.64	57.36
9	13	9	1	15	401	10.94	74		187	214	46.63	53.37
9	27	9	1	17	401	10.94	75		212	189	52.87	47.13
8	7	9	6	17	400	10.91	76		193	207	48.25	51.75
9	5	9	7	15	400	10.91	77		189	211	47.25	52.75
10	4	9	1	17	400	10.91	78		201	199	50.25	49.75
10	11	9	1	14	400	10.91	79		148	252	37	63
5	15	9	6	17	399	10.88	80		204	195	51.13	48.87
7	10	9	6	17	399	10.88	81	3666	171	228	42.86	57.14
9	4	9	6	15	399	10.88	82		218	181	54.64	45.36
5	3	9	1	17	398	10.86	83		227	171	57.04	42.96
9	17	9	5	17	397	10.83	84		198	199	49.87	50.13
9	20	9	1	16	397	10.83	85		193	204	48.61	51.39
10	18	9	1	16	397	10.83	86		186	211	46.85	53.15
9	6	9	1	13	396	10.8	87		150	246	37.88	62.12
9	20	9	1	15	396	10.8	88		175	221	44.19	55.81
5	22	9	6	16	395	10.77	89		189	206	47.85	52.15
6	19	9	6	15	395	10.77	90		167	228	42.28	57.72
8	7	9	6	16	395	10.77	91		184	211	46.58	53.42
9	23	9	4	17	395	10.77	92		153	242	38.73	61.27
10	2	9	6	15	395	10.77	93		202	193	51.14	48.86
11	25	9	4	17	395	10.77	94		179	216	45.32	54.68
6	25	9	5	17	394	10.75	95		161	233	40.86	59.14
9	3	9	5	17	394	10.75	96		203	191	51.52	48.48
9	7	9	2	15	394	10.75	97		145	249	36.8	63.2
9	20	9	1	17	394	10.75	98		204	190	51.78	48.22
9	6	9	1	16	393	10.72	99		210	183	53.44	46.56
7	2	9	5	18	392	10.69	100		233	159	59.44	40.56
9	6	9	1	14	392	10.69	101	3666	180	212	45.92	54.08
10	10	9	7	16	392	10.69	102		156	236	39.8	60.2
10	9	9	6	19	391	10.67	103		192	199	49.1	50.9
10	11	9	1	18	391	10.67	104		202	189	51.66	48.34
8	9	9	1	13	390	10.64	105		167	223	42.82	57.18
4	17	9	6	18	389	10.61	106		141	248	36.25	63.75
9	18	9	6	16	389	10.61	107		155	234	39.85	60.15
9	26	9	7	15	389	10.61	108		152	237	39.07	60.93
11	25	9	4	15	389	10.61	109		186	203	47.81	52.19
8	16	9	1	17	388	10.58	110		213	175	54.9	45.1
9	5	9	7	16	388	10.58	111		200	188	51.55	48.45
10	11	9	1	13	388	10.58	112		132	256	34.02	65.98
4	5	9	1	18	387	10.56	113		207	180	53.49	46.51
6	14	9	1	14	387	10.56	114		186	201	48.06	51.94
7	17	9	6	16	387	10.56	115		191	196	49.35	50.65
9	5	9	7	17	387	10.56	116		199	188	51.42	48.58
9	27	9	1	14	387	10.56	117		155	232	40.05	59.95
5	24	9	1	12	386	10.53	118		170	216	44.04	55.96
9	18	9	6	18	386	10.53	119		158	228	40.93	59.07
10	3	9	7	16	386	10.53	120		149	237	38.6	61.4
10	22	9	5	17	386	10.53	121	3666	193	193	50	50

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
6	21	9	1	18	385	10.5	122		223	162	57.92	42.08
7	5	9	1	13	385	10.5	123		144	241	37.4	62.6
8	15	9	7	11	385	10.5	124		219	166	56.88	43.12
9	6	9	1	17	385	10.5	125		216	169	56.1	43.9
9	20	9	1	13	383	10.45	126		127	256	33.16	66.84
10	4	9	1	15	383	10.45	127		162	221	42.3	57.7
10	23	9	6	17	383	10.45	128		194	189	50.65	49.35
11	29	9	1	17	383	10.45	129		203	180	53	47
4	3	9	6	17	382	10.42	130		178	204	46.6	53.4
7	3	9	6	14	382	10.42	131		180	202	47.12	52.88
9	13	9	1	14	382	10.42	132		172	210	45.03	54.97
9	21	9	2	17	382	10.42	133		171	211	44.76	55.24
2	28	9	7	17	381	10.39	134		151	230	39.63	60.37
5	1	9	6	17	381	10.39	135		181	200	47.51	52.49
5	25	9	2	15	381	10.39	136		152	229	39.9	60.1
8	2	9	1	18	381	10.39	137		214	167	56.17	43.83
10	8	9	5	16	381	10.39	138		145	236	38.06	61.94
5	22	9	6	18	380	10.37	139		221	159	58.16	41.84
8	9	9	1	16	380	10.37	140		195	185	51.32	48.68
9	30	9	4	17	380	10.37	141	3666	161	219	42.37	57.63
11	29	9	1	15	380	10.37	142		207	173	54.47	45.53
5	15	9	6	18	379	10.34	143		192	187	50.66	49.34
7	24	9	6	17	379	10.34	144		176	203	46.44	53.56
5	10	9	1	14	378	10.31	145		172	206	45.5	54.5
6	14	9	1	16	378	10.31	146		179	199	47.35	52.65
10	3	9	7	15	378	10.31	147		155	223	41.01	58.99
5	17	9	1	11	377	10.28	148		120	257	31.83	68.17
10	4	9	1	14	377	10.28	149		143	234	37.93	62.07
11	25	9	4	16	377	10.28	150		175	202	46.42	53.58
7	12	9	1	15	376	10.26	151		193	183	51.33	48.67
8	30	9	1	16	376	10.26	152		192	184	51.06	48.94
9	7	9	2	17	376	10.26	153		172	204	45.74	54.26
9	22	9	3	17	376	10.26	154		160	216	42.55	57.45
10	5	9	2	17	376	10.26	155		186	190	49.47	50.53
10	21	9	4	17	376	10.26	156		200	176	53.19	46.81
4	17	9	6	17	375	10.23	157		165	210	44	56
6	14	9	1	15	375	10.23	158		166	209	44.27	55.73
7	3	9	6	16	375	10.23	159		178	197	47.47	52.53
9	15	9	3	17	375	10.23	160		180	195	48	52
9	29	9	3	17	375	10.23	161	3666	164	211	43.73	56.27
10	2	9	6	19	375	10.23	162		172	203	45.87	54.13
6	21	9	1	15	374	10.2	163		170	204	45.45	54.55
6	28	9	1	16	374	10.2	164		171	203	45.72	54.28
9	20	9	1	19	374	10.2	165		235	139	62.83	37.17
10	1	9	5	18	374	10.2	166		183	191	48.93	51.07
10	12	9	2	17	374	10.2	167		163	211	43.58	56.42
4	24	9	6	17	373	10.17	168		175	198	46.92	53.08
5	29	9	6	17	373	10.17	169		178	195	47.72	52.28
7	9	9	5	17	373	10.17	170		173	200	46.38	53.62
7	12	9	1	17	373	10.17	171		215	158	57.64	42.36
8	29	9	7	14	373	10.17	172		219	154	58.71	41.29
10	25	9	1	17	373	10.17	173		203	170	54.42	45.58

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
5	17	9	1	15	372	10.15	174		181	191	48.66	51.34
7	5	9	1	12	372	10.15	175		127	245	34.14	65.86
9	20	9	1	18	372	10.15	176		220	152	59.14	40.86
10	1	9	5	16	372	10.15	177		154	218	41.4	58.6
5	10	9	1	17	371	10.12	178		215	156	57.95	42.05
6	19	9	6	18	371	10.12	179		177	194	47.71	52.29
9	5	9	7	14	371	10.12	180		161	210	43.4	56.6
8	9	9	1	12	370	10.09	181	3666	145	225	39.19	60.81
9	4	9	6	14	370	10.09	182		202	168	54.59	45.41
9	26	9	7	18	370	10.09	183		151	219	40.81	59.19
8	16	9	1	12	369	10.07	184		144	225	39.02	60.98
8	30	9	1	12	369	10.07	185		137	232	37.13	62.87
9	11	9	6	15	369	10.07	186		161	208	43.63	56.37
4	19	9	1	18	368	10.04	187		213	155	57.88	42.12
5	10	9	1	16	368	10.04	188		201	167	54.62	45.38
5	22	9	6	19	368	10.04	189		194	174	52.72	47.28
5	23	9	7	13	368	10.04	190		201	167	54.62	45.38
6	14	9	1	18	368	10.04	191		184	184	50	50
9	26	9	7	17	368	10.04	192		153	215	41.58	58.42
10	23	9	6	18	368	10.04	193		217	151	58.97	41.03
8	9	9	1	18	367	10.01	194		175	192	47.68	52.32
9	13	9	1	16	367	10.01	195		189	178	51.5	48.5
9	25	9	6	14	367	10.01	196		176	191	47.96	52.04
10	3	9	7	14	367	10.01	197		146	221	39.78	60.22
10	25	9	1	16	367	10.01	198		185	182	50.41	49.59
11	20	9	6	16	367	10.01	199		173	194	47.14	52.86
5	10	9	1	15	366	9.98	200		191	175	52.19	47.81

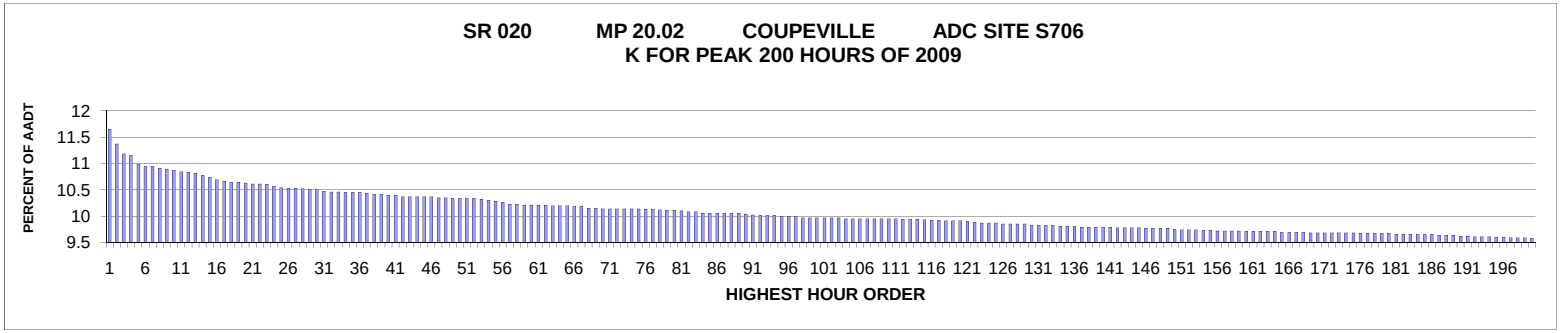

AADT= 8479 **K 30 FACTOR=** 10.5 **K 100 FACTOR=** 9.97 **K 200 FACTOR=** 9.58 **D FACTOR=** 57.16

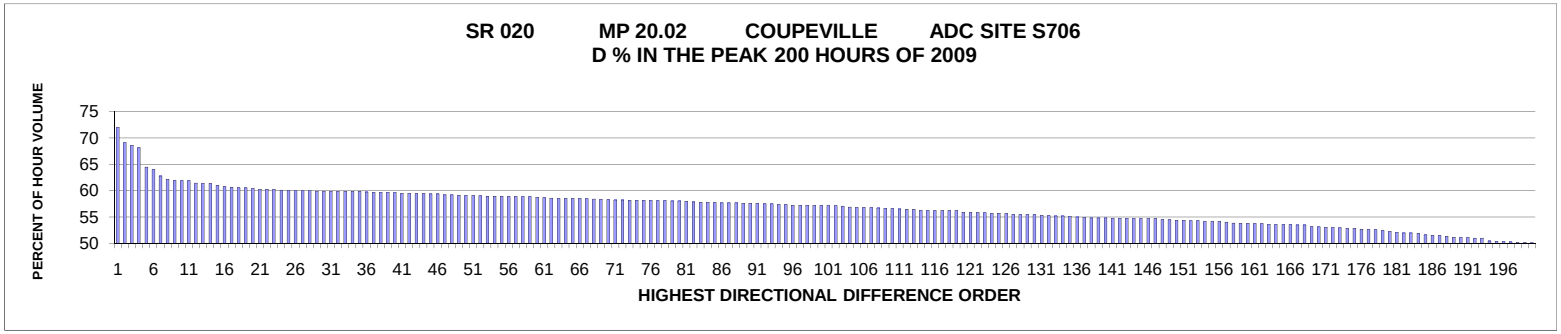

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	21	9	6	17	988	11.65	1	8479	409	579	41.4	58.6
8	1	9	7	16	964	11.37	2		404	560	41.91	58.09
8	1	9	7	15	948	11.18	3		384	564	40.51	59.49
7	25	9	7	13	945	11.15	4		440	505	46.56	53.44
8	1	9	7	14	931	10.98	5		453	478	48.66	51.34
7	10	9	6	17	928	10.94	6		358	570	38.58	61.42
8	20	9	5	17	928	10.94	7		388	540	41.81	58.19
7	5	9	1	13	925	10.91	8		547	378	59.14	40.86
7	2	9	5	17	923	10.89	9		378	545	40.95	59.05
7	3	9	6	17	922	10.87	10		332	590	36.01	63.99
8	21	9	6	16	919	10.84	11		428	491	46.57	53.43
8	1	9	7	13	918	10.83	12		497	421	54.14	45.86
8	15	9	7	15	917	10.81	13		373	544	40.68	59.32
7	23	9	5	17	913	10.77	14		381	532	41.73	58.27
8	14	9	6	17	911	10.74	15		368	543	40.4	59.6
8	1	9	7	12	906	10.69	16		501	405	55.3	44.7
8	8	9	7	16	904	10.66	17		382	522	42.26	57.74

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	12	9	4	17	902	10.64	18		385	517	42.68	57.32
9	27	9	1	16	902	10.64	19		288	614	31.93	68.07
8	7	9	6	16	901	10.63	20		395	506	43.84	56.16
4	30	9	5	17	900	10.61	21	8479	363	537	40.33	59.67
5	1	9	6	17	900	10.61	22		358	542	39.78	60.22
7	31	9	6	17	899	10.6	23		369	530	41.05	58.95
7	3	9	6	16	896	10.57	24		346	550	38.62	61.38
8	7	9	6	17	894	10.54	25		333	561	37.25	62.75
7	1	9	4	17	893	10.53	26		383	510	42.89	57.11
7	24	9	6	16	893	10.53	27		378	515	42.33	57.67
7	31	9	6	15	892	10.52	28		402	490	45.07	54.93
7	25	9	7	14	891	10.51	29		410	481	46.02	53.98
8	3	9	2	17	890	10.5	30		377	513	42.36	57.64
6	5	9	6	17	888	10.47	31		377	511	42.45	57.55
7	17	9	6	16	887	10.46	32		402	485	45.32	54.68
8	8	9	7	15	887	10.46	33		356	531	40.14	59.86
8	15	9	7	14	886	10.45	34		383	503	43.23	56.77
9	4	9	6	17	886	10.45	35		354	532	39.95	60.05
9	26	9	7	13	886	10.45	36		485	401	54.74	45.26
8	26	9	4	17	884	10.43	37		347	537	39.25	60.75
8	5	9	4	17	883	10.41	38		383	500	43.37	56.63
8	8	9	7	13	883	10.41	39		450	433	50.96	49.04
7	31	9	6	16	882	10.4	40		399	483	45.24	54.76
7	3	9	6	15	881	10.39	41	8479	360	521	40.86	59.14
7	3	9	6	14	879	10.37	42		361	518	41.07	58.93
7	9	9	5	17	879	10.37	43		396	483	45.05	54.95
7	10	9	6	14	879	10.37	44		456	423	51.88	48.12
8	2	9	1	13	879	10.37	45		494	385	56.2	43.8
9	27	9	1	17	879	10.37	46		276	603	31.4	68.6
7	13	9	2	17	878	10.35	47		376	502	42.82	57.18
7	17	9	6	17	878	10.35	48		388	490	44.19	55.81
4	29	9	4	17	876	10.33	49		367	509	41.89	58.11
7	22	9	4	17	876	10.33	50		361	515	41.21	58.79
8	8	9	7	17	876	10.33	51		334	542	38.13	61.87
8	29	9	7	14	876	10.33	52		388	488	44.29	55.71
6	3	9	4	17	875	10.32	53		359	516	41.03	58.97
6	25	9	5	17	873	10.3	54		350	523	40.09	59.91
7	25	9	7	16	872	10.28	55		391	481	44.84	55.16
8	6	9	5	17	870	10.26	56		398	472	45.75	54.25
5	23	9	7	14	867	10.23	57		372	495	42.91	57.09
7	15	9	4	17	867	10.23	58		364	503	41.98	58.02
4	24	9	6	17	866	10.21	59		371	495	42.84	57.16
6	15	9	2	17	866	10.21	60		348	518	40.18	59.82
7	3	9	6	12	866	10.21	61	8479	450	416	51.96	48.04
8	22	9	7	15	866	10.21	62		343	523	39.61	60.39
7	14	9	3	17	865	10.2	63		360	505	41.62	58.38
8	6	9	5	16	865	10.2	64		400	465	46.24	53.76
8	16	9	1	13	865	10.2	65		442	423	51.1	48.9
4	28	9	3	17	863	10.18	66		343	520	39.75	60.25
8	18	9	3	17	863	10.18	67		369	494	42.76	57.24
5	23	9	7	13	861	10.15	68		339	522	39.37	60.63
7	24	9	6	17	861	10.15	69		340	521	39.49	60.51

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
5	15	9	6	17	860	10.14	70		367	493	42.67	57.33
7	7	9	3	17	860	10.14	71		352	508	40.93	59.07
8	21	9	6	13	860	10.14	72		390	470	45.35	54.65
9	11	9	6	16	860	10.14	73		383	477	44.53	55.47
9	27	9	1	13	860	10.14	74		511	349	59.42	40.58
9	30	9	4	17	860	10.14	75		354	506	41.16	58.84
7	2	9	5	16	859	10.13	76		383	476	44.59	55.41
8	5	9	4	16	859	10.13	77		392	467	45.63	54.37
9	9	9	4	16	858	10.12	78		359	499	41.84	58.16
7	1	9	4	16	857	10.11	79		402	455	46.91	53.09
8	4	9	3	17	857	10.11	80		359	498	41.89	58.11
6	22	9	2	17	856	10.1	81	8479	344	512	40.19	59.81
6	23	9	3	17	855	10.08	82		374	481	43.74	56.26
7	21	9	3	16	855	10.08	83		405	450	47.37	52.63
8	14	9	6	12	853	10.06	84		427	426	50.06	49.94
6	9	9	3	17	852	10.05	85		351	501	41.2	58.8
7	6	9	2	13	852	10.05	86		466	386	54.69	45.31
8	8	9	7	12	852	10.05	87		453	399	53.17	46.83
8	15	9	7	13	852	10.05	88		407	445	47.77	52.23
9	9	9	4	17	852	10.05	89		350	502	41.08	58.92
8	2	9	1	14	851	10.04	90		458	393	53.82	46.18
8	15	9	7	16	850	10.02	91		375	475	44.12	55.88
7	5	9	1	14	849	10.01	92		502	347	59.13	40.87
9	11	9	6	17	849	10.01	93		363	486	42.76	57.24
9	18	9	6	17	849	10.01	94		361	488	42.52	57.48
7	8	9	4	17	848	10	95		321	527	37.85	62.15
8	15	9	7	12	848	10	96		387	461	45.64	54.36
10	2	9	6	17	847	9.99	97		339	508	40.02	59.98
7	11	9	7	16	845	9.97	98		393	452	46.51	53.49
7	30	9	5	17	845	9.97	99		357	488	42.25	57.75
8	14	9	6	16	845	9.97	100		393	452	46.51	53.49
8	19	9	4	16	845	9.97	101	8479	374	471	44.26	55.74
8	21	9	6	14	845	9.97	102		409	436	48.4	51.6
8	28	9	6	13	845	9.97	103		420	425	49.7	50.3
4	10	9	6	17	844	9.95	104		322	522	38.15	61.85
6	26	9	6	17	844	9.95	105		343	501	40.64	59.36
7	3	9	6	13	844	9.95	106		379	465	44.91	55.09
7	6	9	2	17	844	9.95	107		339	505	40.17	59.83
7	9	9	5	16	844	9.95	108		387	457	45.85	54.15
8	28	9	6	17	844	9.95	109		361	483	42.77	57.23
9	25	9	6	17	844	9.95	110		353	491	41.82	58.18
9	27	9	1	12	844	9.95	111		583	261	69.08	30.92
5	7	9	5	17	843	9.94	112		348	495	41.28	58.72
5	21	9	5	17	843	9.94	113		340	503	40.33	59.67
5	27	9	4	17	843	9.94	114		333	510	39.5	60.5
5	12	9	3	17	842	9.93	115		338	504	40.14	59.86
8	8	9	7	14	841	9.92	116		404	437	48.04	51.96
8	27	9	5	17	841	9.92	117		349	492	41.5	58.5
6	11	9	5	17	840	9.91	118		366	474	43.57	56.43
8	11	9	3	17	840	9.91	119		353	487	42.02	57.98
8	13	9	5	17	840	9.91	120		364	476	43.33	56.67
6	2	9	3	17	839	9.9	121	8479	336	503	40.05	59.95

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	1	9	7	17	838	9.88	122		335	503	39.98	60.02
6	26	9	6	16	837	9.87	123		364	473	43.49	56.51
7	25	9	7	15	837	9.87	124		394	443	47.07	52.93
8	4	9	3	16	837	9.87	125		375	462	44.8	55.2
7	17	9	6	13	835	9.85	126		427	408	51.14	48.86
7	23	9	5	14	835	9.85	127		440	395	52.69	47.31
9	26	9	7	14	835	9.85	128		447	388	53.53	46.47
11	6	9	6	17	835	9.85	129		348	487	41.68	58.32
7	8	9	4	16	833	9.82	130		393	440	47.18	52.82
7	11	9	7	14	833	9.82	131		413	420	49.58	50.42
7	29	9	4	16	833	9.82	132		349	484	41.9	58.1
8	2	9	1	15	833	9.82	133		381	452	45.74	54.26
6	29	9	2	17	832	9.81	134		354	478	42.55	57.45
9	26	9	7	12	832	9.81	135		447	385	53.73	46.27
8	10	9	2	16	831	9.8	136		364	467	43.8	56.2
5	27	9	4	16	830	9.79	137		376	454	45.3	54.7
7	24	9	6	14	830	9.79	138		412	418	49.64	50.36
8	5	9	4	15	830	9.79	139		398	432	47.95	52.05
8	29	9	7	12	830	9.79	140		452	378	54.46	45.54
9	26	9	7	15	830	9.79	141	8479	423	407	50.96	49.04
5	13	9	4	16	829	9.78	142		363	466	43.79	56.21
7	26	9	1	14	829	9.78	143		406	423	48.97	51.03
9	3	9	5	17	829	9.78	144		351	478	42.34	57.66
9	23	9	4	16	829	9.78	145		384	445	46.32	53.68
6	11	9	5	16	828	9.77	146		351	477	42.39	57.61
8	14	9	6	18	828	9.77	147		323	505	39.01	60.99
9	15	9	3	16	828	9.77	148		394	434	47.58	52.42
10	6	9	3	17	828	9.77	149		334	494	40.34	59.66
7	23	9	5	12	827	9.75	150		460	367	55.62	44.38
6	16	9	3	17	826	9.74	151		343	483	41.53	58.47
7	11	9	7	15	826	9.74	152		365	461	44.19	55.81
8	17	9	2	17	826	9.74	153		328	498	39.71	60.29
5	8	9	6	17	825	9.73	154		348	477	42.18	57.82
7	5	9	1	12	825	9.73	155		532	293	64.48	35.52
6	19	9	6	17	824	9.72	156		339	485	41.14	58.86
7	30	9	5	16	824	9.72	157		365	459	44.3	55.7
8	25	9	3	17	824	9.72	158		332	492	40.29	59.71
12	2	9	4	16	824	9.72	159		373	451	45.27	54.73
5	9	9	7	16	823	9.71	160		369	454	44.84	55.16
5	29	9	6	16	823	9.71	161	8479	387	436	47.02	52.98
7	22	9	4	16	823	9.71	162		382	441	46.42	53.58
9	4	9	6	16	823	9.71	163		367	456	44.59	55.41
9	5	9	7	14	823	9.71	164		424	399	51.52	48.48
5	18	9	2	17	822	9.69	165		313	509	38.08	61.92
5	29	9	6	17	822	9.69	166		360	462	43.8	56.2
5	30	9	7	13	822	9.69	167		445	377	54.14	45.86
8	14	9	6	15	822	9.69	168		386	436	46.96	53.04
5	26	9	3	17	821	9.68	169		333	488	40.56	59.44
7	10	9	6	16	821	9.68	170		371	450	45.19	54.81
7	16	9	5	17	821	9.68	171		341	480	41.53	58.47
7	20	9	2	17	821	9.68	172		329	492	40.07	59.93
8	20	9	5	16	821	9.68	173		371	450	45.19	54.81

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	28	9	6	15	821	9.68	174		387	434	47.14	52.86
9	27	9	1	11	821	9.68	175		591	230	71.99	28.01
5	22	9	6	17	820	9.67	176		317	503	38.66	61.34
7	20	9	2	16	820	9.67	177		408	412	49.76	50.24
8	26	9	4	16	820	9.67	178		366	454	44.63	55.37
8	29	9	7	13	820	9.67	179		409	411	49.88	50.12
9	26	9	7	16	820	9.67	180		422	398	51.46	48.54
6	30	9	3	17	819	9.66	181	8479	343	476	41.88	58.12
8	19	9	4	17	819	9.66	182		332	487	40.54	59.46
10	15	9	5	17	819	9.66	183		357	462	43.59	56.41
6	12	9	6	17	818	9.65	184		346	472	42.3	57.7
7	6	9	2	16	818	9.65	185		354	464	43.28	56.72
8	3	9	2	16	818	9.65	186		379	439	46.33	53.67
7	29	9	4	17	817	9.64	187		353	464	43.21	56.79
8	18	9	3	16	817	9.64	188		339	478	41.49	58.51
9	22	9	3	17	817	9.64	189		355	462	43.45	56.55
4	14	9	3	17	816	9.62	190		369	447	45.22	54.78
7	26	9	1	13	816	9.62	191		409	407	50.12	49.88
6	24	9	4	17	815	9.61	192		338	477	41.47	58.53
6	26	9	6	15	815	9.61	193		387	428	47.48	52.52
8	25	9	3	16	815	9.61	194		342	473	41.96	58.04
7	17	9	6	15	814	9.6	195		371	443	45.58	54.42
9	23	9	4	17	814	9.6	196		327	487	40.17	59.83
4	27	9	2	17	813	9.59	197		338	475	41.57	58.43
6	12	9	6	16	813	9.59	198		345	468	42.44	57.56
9	15	9	3	17	813	9.59	199		351	462	43.17	56.83
5	28	9	5	17	812	9.58	200		349	463	42.98	57.02

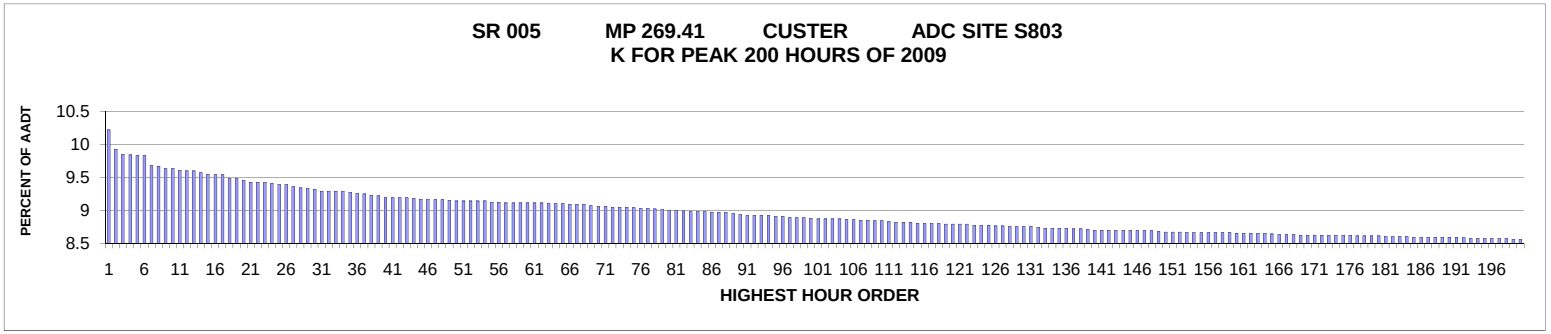

AADT= 27032 **K 30 FACTOR=** 9.32 **K 100 FACTOR=** 8.88 **K 200 FACTOR=** 8.56 **D FACTOR=** 55.03

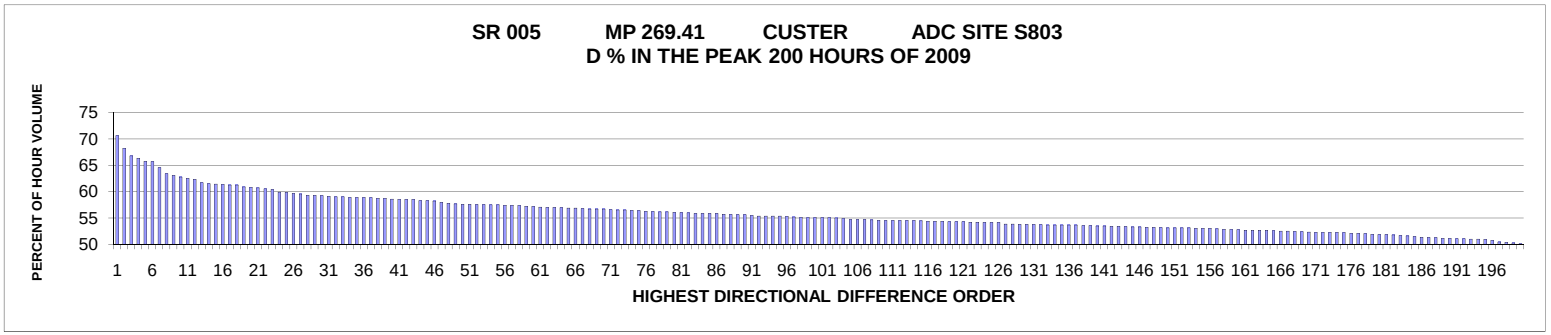

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
9	4	9	6	17	2762	10.22	1	27032	1528	1234	55.32	44.68
7	24	9	6	17	2683	9.93	2		1335	1348	49.76	50.24
10	12	9	2	17	2664	9.85	3		1779	885	66.78	33.22
8	28	9	6	16	2659	9.84	4		1395	1264	52.46	47.54
8	3	9	2	17	2658	9.83	5		1676	982	63.05	36.95
8	14	9	6	17	2657	9.83	6		1438	1219	54.12	45.88
8	14	9	6	16	2617	9.68	7		1388	1229	53.04	46.96
10	23	9	6	16	2613	9.67	8		1334	1279	51.05	48.95
11	20	9	6	17	2604	9.63	9		1454	1150	55.84	44.16
8	28	9	6	17	2602	9.63	10		1447	1155	55.61	44.39
10	9	9	6	17	2598	9.61	11		1378	1220	53.04	46.96
12	29	9	3	17	2596	9.6	12		1458	1138	56.16	43.84
7	24	9	6	18	2595	9.6	13		1378	1217	53.1	46.9
12	28	9	2	17	2588	9.57	14		1486	1102	57.42	42.58
8	28	9	6	18	2581	9.55	15		1411	1170	54.67	45.33
8	3	9	2	16	2580	9.54	16		1487	1093	57.64	42.36
11	12	9	5	17	2578	9.54	17		1618	960	62.76	37.24

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	21	9	6	18	2562	9.48	18		1406	1156	54.88	45.12
9	4	9	6	16	2562	9.48	19		1469	1093	57.34	42.66
9	3	9	5	17	2555	9.45	20		1343	1212	52.56	47.44
8	7	9	6	18	2550	9.43	21	27032	1450	1100	56.86	43.14
8	14	9	6	18	2549	9.43	22		1445	1104	56.69	43.31
11	27	9	6	17	2548	9.43	23		1547	1001	60.71	39.29
10	2	9	6	17	2543	9.41	24		1334	1209	52.46	47.54
7	10	9	6	17	2539	9.39	25		1327	1212	52.26	47.74
10	23	9	6	17	2538	9.39	26		1432	1106	56.42	43.58
12	30	9	4	16	2529	9.36	27		1420	1109	56.15	43.85
12	30	9	4	17	2524	9.34	28		1536	988	60.86	39.14
9	4	9	6	15	2521	9.33	29		1339	1182	53.11	46.89
7	17	9	6	18	2520	9.32	30		1342	1178	53.25	46.75
7	17	9	6	17	2511	9.29	31		1389	1122	55.32	44.68
7	24	9	6	16	2511	9.29	32		1313	1198	52.29	47.71
8	3	9	2	15	2511	9.29	33		1342	1169	53.44	46.56
9	3	9	5	16	2511	9.29	34		1339	1172	53.33	46.67
11	29	9	1	16	2507	9.27	35		1476	1031	58.88	41.12
8	13	9	5	18	2504	9.26	36		1427	1077	56.99	43.01
8	13	9	5	17	2500	9.25	37		1377	1123	55.08	44.92
9	25	9	6	18	2494	9.23	38		1419	1075	56.9	43.1
6	19	9	6	17	2493	9.22	39		1279	1214	51.3	48.7
7	2	9	5	17	2485	9.19	40		1312	1173	52.8	47.2
8	6	9	5	17	2485	9.19	41	27032	1309	1176	52.68	47.32
4	24	9	6	17	2484	9.19	42		1403	1081	56.48	43.52
10	2	9	6	16	2483	9.19	43		1353	1130	54.49	45.51
8	20	9	5	17	2482	9.18	44		1326	1156	53.42	46.58
12	4	9	6	17	2480	9.17	45		1324	1156	53.39	46.61
9	25	9	6	17	2479	9.17	46		1401	1078	56.51	43.49
6	5	9	6	17	2475	9.16	47		1278	1197	51.64	48.36
8	3	9	2	18	2475	9.16	48		1642	833	66.34	33.66
8	7	9	6	16	2473	9.15	49		1329	1144	53.74	46.26
10	9	9	6	18	2472	9.14	50		1388	1084	56.15	43.85
2	13	9	6	17	2471	9.14	51		1445	1026	58.48	41.52
8	21	9	6	17	2471	9.14	52		1366	1105	55.28	44.72
11	27	9	6	16	2470	9.14	53		1519	951	61.5	38.5
11	29	9	1	17	2470	9.14	54		1465	1005	59.31	40.69
6	26	9	6	17	2466	9.12	55		1298	1168	52.64	47.36
12	18	9	6	17	2465	9.12	56		1406	1059	57.04	42.96
8	21	9	6	16	2463	9.11	57		1311	1152	53.23	46.77
9	5	9	7	12	2463	9.11	58		1014	1449	41.17	58.83
10	9	9	6	16	2463	9.11	59		1325	1138	53.8	46.2
10	12	9	2	18	2463	9.11	60		1739	724	70.6	29.4
8	5	9	4	17	2462	9.11	61	27032	1339	1123	54.39	45.61
9	18	9	6	17	2462	9.11	62		1286	1176	52.23	47.77
8	31	9	2	18	2461	9.1	63		1395	1066	56.68	43.32
11	13	9	6	16	2460	9.1	64		1296	1164	52.68	47.32
8	4	9	3	17	2459	9.1	65		1398	1061	56.85	43.15
8	17	9	2	17	2458	9.09	66		1372	1086	55.82	44.18
7	10	9	6	18	2457	9.09	67		1299	1158	52.87	47.13
10	10	9	7	12	2457	9.09	68		963	1494	39.19	60.81
8	27	9	5	18	2452	9.07	69		1421	1031	57.95	42.05

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	12	9	4	18	2449	9.06	70		1373	1076	56.06	43.94
8	19	9	4	17	2448	9.06	71		1328	1120	54.25	45.75
10	12	9	2	16	2447	9.05	72		1607	840	65.67	34.33
7	24	9	6	15	2446	9.05	73		1184	1262	48.41	51.59
8	31	9	2	17	2446	9.05	74		1324	1122	54.13	45.87
10	30	9	6	17	2445	9.04	75		1332	1113	54.48	45.52
6	26	9	6	18	2442	9.03	76		1312	1130	53.73	46.27
12	28	9	2	16	2441	9.03	77		1296	1145	53.09	46.91
12	22	9	3	17	2438	9.02	78		1400	1038	57.42	42.58
11	13	9	6	17	2435	9.01	79		1393	1042	57.21	42.79
9	2	9	4	17	2434	9	80		1303	1131	53.53	46.47
8	20	9	5	16	2433	9	81	27032	1245	1188	51.17	48.83
12	29	9	3	16	2429	8.99	82		1269	1160	52.24	47.76
9	3	9	5	18	2428	8.98	83		1414	1014	58.24	41.76
8	15	9	7	13	2427	8.98	84		1044	1383	43.02	56.98
9	7	9	2	16	2427	8.98	85		1465	962	60.36	39.64
8	6	9	5	18	2426	8.97	86		1367	1059	56.35	43.65
8	26	9	4	17	2426	8.97	87		1338	1088	55.15	44.85
12	31	9	5	16	2425	8.97	88		1436	989	59.22	40.78
7	3	9	6	16	2420	8.95	89		1298	1122	53.64	46.36
11	6	9	6	18	2413	8.93	90		1367	1046	56.65	43.35
9	11	9	6	17	2412	8.92	91		1318	1094	54.64	45.36
3	20	9	6	17	2411	8.92	92		1341	1070	55.62	44.38
7	23	9	5	17	2411	8.92	93		1241	1170	51.47	48.53
9	4	9	6	18	2411	8.92	94		1403	1008	58.19	41.81
8	3	9	2	14	2408	8.91	95		1227	1181	50.96	49.04
11	6	9	6	17	2408	8.91	96		1291	1117	53.61	46.39
7	19	9	1	15	2404	8.89	97		1289	1115	53.62	46.38
9	7	9	2	17	2404	8.89	98		1477	927	61.44	38.56
8	27	9	5	17	2403	8.89	99		1303	1100	54.22	45.78
4	10	9	6	17	2401	8.88	100		1321	1080	55.02	44.98
12	11	9	6	17	2399	8.87	101	27032	1304	1095	54.36	45.64
8	28	9	6	15	2398	8.87	102		1288	1110	53.71	46.29
8	7	9	6	17	2397	8.87	103		1333	1064	55.61	44.39
12	30	9	4	15	2397	8.87	104		1198	1199	49.98	50.02
8	5	9	4	16	2396	8.86	105		1219	1177	50.88	49.12
10	2	9	6	18	2395	8.86	106		1376	1019	57.45	42.55
9	1	9	3	17	2392	8.85	107		1269	1123	53.05	46.95
9	5	9	7	14	2391	8.85	108		1105	1286	46.21	53.79
7	17	9	6	16	2389	8.84	109		1244	1145	52.07	47.93
7	27	9	2	17	2389	8.84	110		1281	1108	53.62	46.38
8	14	9	6	14	2388	8.83	111		1185	1203	49.62	50.38
8	8	9	7	12	2384	8.82	112		1014	1370	42.53	57.47
11	11	9	4	17	2383	8.82	113		1537	846	64.5	35.5
12	4	9	6	18	2383	8.82	114		1362	1021	57.15	42.85
4	24	9	6	18	2379	8.8	115		1368	1011	57.5	42.5
8	25	9	3	17	2379	8.8	116		1397	982	58.72	41.28
10	10	9	7	13	2379	8.8	117		922	1457	38.76	61.24
8	18	9	3	17	2378	8.8	118		1293	1085	54.37	45.63
10	23	9	6	15	2377	8.79	119		1219	1158	51.28	48.72
1	16	9	6	17	2376	8.79	120		1308	1068	55.05	44.95
4	10	9	6	18	2375	8.79	121	27032	1422	953	59.87	40.13

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	29	9	7	12	2375	8.79	122		991	1384	41.73	58.27
9	7	9	2	15	2372	8.77	123		1305	1067	55.02	44.98
2	13	9	6	18	2371	8.77	124		1401	970	59.09	40.91
9	25	9	6	16	2371	8.77	125		1323	1048	55.8	44.2
9	4	9	6	14	2369	8.76	126		1098	1271	46.35	53.65
12	4	9	6	16	2368	8.76	127		1290	1078	54.48	45.52
4	10	9	6	16	2366	8.75	128		1256	1110	53.09	46.91
7	25	9	7	15	2364	8.75	129		1206	1158	51.02	48.98
10	23	9	6	18	2364	8.75	130		1430	934	60.49	39.51
12	31	9	5	15	2364	8.75	131		1264	1100	53.47	46.53
7	2	9	5	16	2362	8.74	132		1287	1075	54.49	45.51
3	13	9	6	17	2360	8.73	133		1249	1111	52.92	47.08
7	10	9	6	16	2360	8.73	134		1222	1138	51.78	48.22
10	8	9	5	17	2360	8.73	135		1321	1039	55.97	44.03
10	16	9	6	18	2360	8.73	136		1318	1042	55.85	44.15
9	6	9	1	17	2358	8.72	137		1444	914	61.24	38.76
4	24	9	6	16	2356	8.72	138		1277	1079	54.2	45.8
4	3	9	6	18	2354	8.71	139		1388	966	58.96	41.04
8	14	9	6	15	2353	8.7	140		1239	1114	52.66	47.34
8	30	9	1	15	2353	8.7	141	27032	1252	1101	53.21	46.79
2	13	9	6	16	2352	8.7	142		1384	968	58.84	41.16
3	13	9	6	18	2352	8.7	143		1302	1050	55.36	44.64
6	26	9	6	16	2352	8.7	144		1218	1134	51.79	48.21
8	4	9	3	16	2351	8.7	145		1232	1119	52.4	47.6
8	22	9	7	13	2350	8.69	146		1145	1205	48.72	51.28
6	19	9	6	16	2349	8.69	147		1292	1057	55	45
12	30	9	4	18	2348	8.69	148		1543	805	65.72	34.28
8	2	9	1	16	2347	8.68	149		1251	1096	53.3	46.7
2	20	9	6	18	2343	8.67	150		1371	972	58.51	41.49
10	12	9	2	15	2343	8.67	151		1398	945	59.67	40.33
12	21	9	2	17	2343	8.67	152		1382	961	58.98	41.02
10	10	9	7	14	2342	8.66	153		1025	1317	43.77	56.23
12	28	9	2	13	2342	8.66	154		878	1464	37.49	62.51
7	24	9	6	14	2341	8.66	155		1062	1279	45.37	54.63
1	30	9	6	17	2340	8.66	156		1279	1061	54.66	45.34
4	17	9	6	16	2340	8.66	157		1274	1066	54.44	45.56
8	1	9	7	13	2340	8.66	158		1070	1270	45.73	54.27
8	7	9	6	15	2340	8.66	159		1218	1122	52.05	47.95
8	10	9	2	17	2339	8.65	160		1221	1118	52.2	47.8
8	30	9	1	17	2337	8.65	161	27032	1386	951	59.31	40.69
9	5	9	7	13	2337	8.65	162		1044	1293	44.67	55.33
12	23	9	4	17	2337	8.65	163		1367	970	58.49	41.51
12	29	9	3	18	2337	8.65	164		1456	881	62.3	37.7
7	16	9	5	17	2335	8.64	165		1211	1124	51.86	48.14
7	24	9	6	19	2334	8.63	166		1231	1103	52.74	47.26
7	26	9	1	16	2334	8.63	167		1320	1014	56.56	43.44
8	28	9	6	13	2334	8.63	168		1027	1307	44	56
4	17	9	6	18	2331	8.62	169		1343	988	57.61	42.39
6	19	9	6	18	2331	8.62	170		1298	1033	55.68	44.32
7	25	9	7	14	2331	8.62	171		1110	1221	47.62	52.38
8	20	9	5	18	2331	8.62	172		1347	984	57.79	42.21
11	13	9	6	18	2331	8.62	173		1370	961	58.77	41.23

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
12	21	9	2	18	2331	8.62	174		1430	901	61.35	38.65
6	25	9	5	17	2330	8.62	175		1271	1059	54.55	45.45
6	12	9	6	16	2329	8.62	176		1247	1082	53.54	46.46
7	25	9	7	16	2328	8.61	177		1211	1117	52.02	47.98
11	28	9	7	17	2328	8.61	178		1436	892	61.68	38.32
12	23	9	4	16	2328	8.61	179		1251	1077	53.74	46.26
7	25	9	7	12	2327	8.61	180		1007	1320	43.27	56.73
8	25	9	3	18	2326	8.6	181	27032	1385	941	59.54	40.46
2	20	9	6	17	2324	8.6	182		1259	1065	54.17	45.83
4	13	9	2	18	2324	8.6	183		1585	739	68.2	31.8
8	28	9	6	14	2324	8.6	184		1089	1235	46.86	53.14
3	6	9	6	17	2323	8.59	185		1265	1058	54.46	45.54
8	1	9	7	14	2323	8.59	186		1145	1178	49.29	50.71
3	27	9	6	18	2322	8.59	187		1367	955	58.87	41.13
8	24	9	2	17	2322	8.59	188		1257	1065	54.13	45.87
8	26	9	4	18	2322	8.59	189		1359	963	58.53	41.47
6	12	9	6	17	2321	8.59	190		1202	1119	51.79	48.21
8	3	9	2	13	2321	8.59	191		1134	1187	48.86	51.14
12	18	9	6	18	2318	8.58	192		1333	985	57.51	42.49
7	3	9	6	17	2317	8.57	193		1210	1107	52.22	47.78
7	23	9	5	18	2317	8.57	194		1275	1042	55.03	44.97
7	2	9	5	18	2316	8.57	195		1334	982	57.6	42.4
8	17	9	2	18	2316	8.57	196		1284	1032	55.44	44.56
8	21	9	6	14	2316	8.57	197		1148	1168	49.57	50.43
9	5	9	7	11	2316	8.57	198		849	1467	36.66	63.34
6	19	9	6	15	2314	8.56	199		1180	1134	50.99	49.01
9	1	9	3	18	2314	8.56	200		1384	930	59.81	40.19

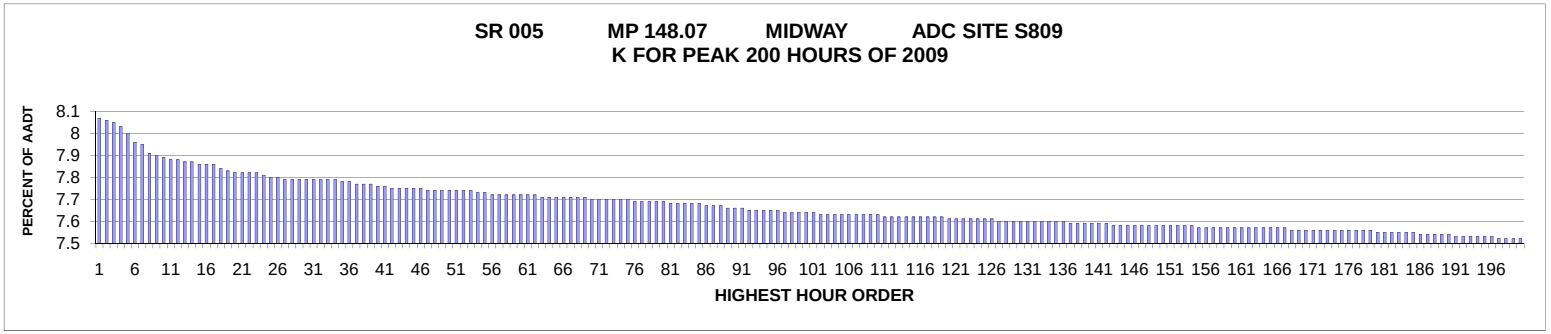

AADT= 191400 **K 30 FACTOR=** 7.79 **K 100 FACTOR=** 7.64 **K 200 FACTOR=** 7.52 **D FACTOR=** 61.85

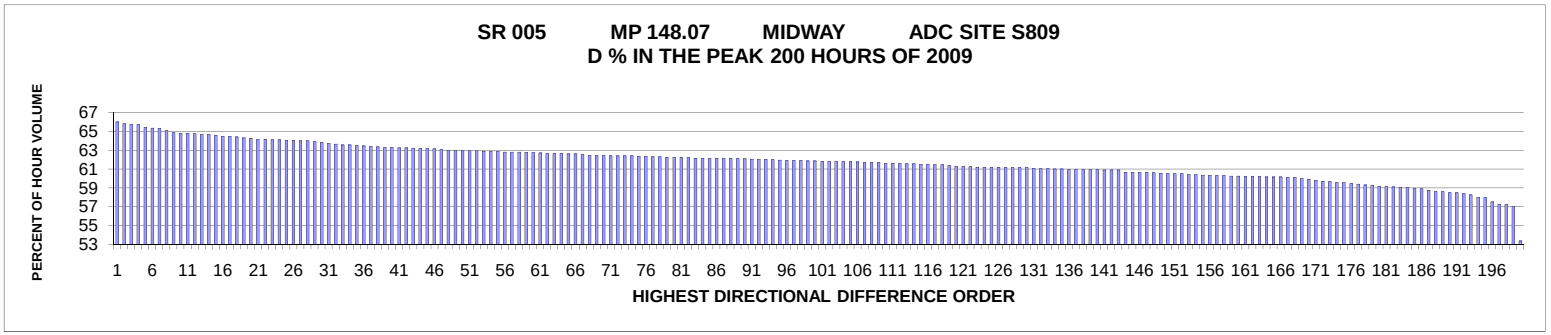

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
4	10	9	6	15	15450	8.07	1	191400	6082	9368	39.37	60.63
3	27	9	6	16	15424	8.06	2		5726	9698	37.12	62.88
2	13	9	6	16	15408	8.05	3		5802	9606	37.66	62.34
6	19	9	6	15	15378	8.03	4		6265	9113	40.74	59.26
4	10	9	6	16	15309	8	5		5774	9535	37.72	62.28
3	27	9	6	15	15233	7.96	6		6202	9031	40.71	59.29
2	13	9	6	15	15216	7.95	7		6045	9171	39.73	60.27
6	25	9	5	18	15145	7.91	8		6063	9082	40.03	59.97
1	30	9	6	16	15122	7.9	9		5629	9493	37.22	62.78
10	9	9	6	15	15097	7.89	10		5947	9150	39.39	60.61
4	15	9	4	17	15089	7.88	11		5680	9409	37.64	62.36
5	15	9	6	17	15087	7.88	12		6250	8837	41.43	58.57
5	8	9	6	15	15065	7.87	13		5889	9176	39.09	60.91
4	3	9	6	15	15054	7.87	14		5873	9181	39.01	60.99
8	21	9	6	15	15053	7.86	15		6182	8871	41.07	58.93
9	3	9	5	16	15053	7.86	16		5986	9067	39.77	60.23
9	18	9	6	16	15049	7.86	17		5845	9204	38.84	61.16

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	26	9	4	17	15013	7.84	18		5860	9153	39.03	60.97
3	13	9	6	16	14988	7.83	19		5672	9316	37.84	62.16
6	18	9	5	16	14975	7.82	20		5688	9287	37.98	62.02
6	5	9	6	17	14970	7.82	21	191400	6132	8838	40.96	59.04
7	17	9	6	15	14967	7.82	22		6055	8912	40.46	59.54
4	16	9	5	17	14959	7.82	23		5534	9425	36.99	63.01
6	23	9	3	18	14943	7.81	24		5845	9098	39.12	60.88
6	26	9	6	15	14924	7.8	25		5920	9004	39.67	60.33
7	9	9	5	17	14923	7.8	26		5780	9143	38.73	61.27
6	17	9	4	17	14919	7.79	27		5784	9135	38.77	61.23
4	16	9	5	16	14917	7.79	28		5501	9416	36.88	63.12
8	20	9	5	17	14916	7.79	29		5808	9108	38.94	61.06
5	8	9	6	16	14910	7.79	30		5535	9375	37.12	62.88
10	22	9	5	17	14910	7.79	31		5657	9253	37.94	62.06
4	17	9	6	16	14908	7.79	32		5683	9225	38.12	61.88
6	19	9	6	17	14907	7.79	33		6259	8648	41.99	58.01
5	22	9	6	15	14905	7.79	34		5930	8975	39.79	60.21
10	9	9	6	16	14898	7.78	35		5781	9117	38.8	61.2
9	25	9	6	15	14894	7.78	36		5919	8975	39.74	60.26
6	10	9	4	16	14875	7.77	37		5446	9429	36.61	63.39
9	16	9	4	17	14869	7.77	38		5292	9577	35.59	64.41
8	20	9	5	18	14867	7.77	39		6394	8473	43.01	56.99
3	13	9	6	15	14851	7.76	40		5885	8966	39.63	60.37
9	18	9	6	15	14849	7.76	41	191400	5920	8929	39.87	60.13
4	3	9	6	16	14837	7.75	42		5661	9176	38.15	61.85
7	10	9	6	15	14833	7.75	43		5978	8855	40.3	59.7
3	18	9	4	17	14831	7.75	44		5328	9503	35.92	64.08
2	5	9	5	17	14829	7.75	45		5313	9516	35.83	64.17
3	25	9	4	17	14829	7.75	46		5317	9512	35.86	64.14
3	20	9	6	15	14823	7.74	47		5896	8927	39.78	60.22
9	3	9	5	15	14823	7.74	48		6018	8805	40.6	59.4
2	20	9	6	15	14822	7.74	49		5799	9023	39.12	60.88
8	27	9	5	17	14816	7.74	50		5678	9138	38.32	61.68
9	3	9	5	18	14813	7.74	51		6915	7898	46.68	53.32
6	5	9	6	16	14809	7.74	52		5880	8929	39.71	60.29
6	16	9	3	17	14807	7.74	53		5370	9437	36.27	63.73
7	23	9	5	17	14800	7.73	54		5680	9120	38.38	61.62
4	17	9	6	17	14799	7.73	55		5902	8897	39.88	60.12
8	20	9	5	16	14785	7.72	56		5699	9086	38.55	61.45
6	10	9	4	17	14779	7.72	57		5480	9299	37.08	62.92
8	26	9	4	16	14778	7.72	58		5524	9254	37.38	62.62
5	29	9	6	16	14774	7.72	59		5642	9132	38.19	61.81
3	13	9	6	17	14773	7.72	60		5650	9123	38.25	61.75
3	6	9	6	16	14771	7.72	61	191400	5435	9336	36.8	63.2
2	27	9	6	17	14767	7.72	62		5742	9025	38.88	61.12
2	17	9	3	16	14764	7.71	63		5119	9645	34.67	65.33
10	2	9	6	15	14761	7.71	64		5737	9024	38.87	61.13
4	24	9	6	15	14760	7.71	65		5672	9088	38.43	61.57
2	20	9	6	17	14758	7.71	66		5774	8984	39.12	60.88
5	1	9	6	16	14758	7.71	67		5586	9172	37.85	62.15
5	21	9	5	17	14758	7.71	68		5637	9121	38.2	61.8
4	8	9	4	16	14752	7.71	69		5150	9602	34.91	65.09

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
2	13	9	6	17	14743	7.7	70		5881	8862	39.89	60.11
2	5	9	5	16	14739	7.7	71		5053	9686	34.28	65.72
9	3	9	5	17	14736	7.7	72		6300	8436	42.75	57.25
3	25	9	4	16	14735	7.7	73		5220	9515	35.43	64.57
4	17	9	6	15	14732	7.7	74		5869	8863	39.84	60.16
7	23	9	5	18	14731	7.7	75		5680	9051	38.56	61.44
4	22	9	4	17	14722	7.69	76		5383	9339	36.56	63.44
9	4	9	6	16	14717	7.69	77		5835	8882	39.65	60.35
5	18	9	2	17	14715	7.69	78		5394	9321	36.66	63.34
8	28	9	6	15	14715	7.69	79		5933	8782	40.32	59.68
5	1	9	6	15	14713	7.69	80		5814	8899	39.52	60.48
6	25	9	5	17	14705	7.68	81	191400	5660	9045	38.49	61.51
7	23	9	5	16	14705	7.68	82		5577	9128	37.93	62.07
3	31	9	3	16	14703	7.68	83		5035	9668	34.24	65.76
2	19	9	5	17	14702	7.68	84		5452	9250	37.08	62.92
5	1	9	6	17	14692	7.68	85		5803	8889	39.5	60.5
6	24	9	4	17	14682	7.67	86		5646	9036	38.46	61.54
5	21	9	5	18	14674	7.67	87		6128	8546	41.76	58.24
8	21	9	6	16	14671	7.67	88		5734	8937	39.08	60.92
6	18	9	5	17	14668	7.66	89		5539	9129	37.76	62.24
3	6	9	6	15	14659	7.66	90		5667	8992	38.66	61.34
9	17	9	5	17	14657	7.66	91		5539	9118	37.79	62.21
3	27	9	6	17	14649	7.65	92		5683	8966	38.79	61.21
5	14	9	5	16	14649	7.65	93		5205	9444	35.53	64.47
7	9	9	5	15	14645	7.65	94		6020	8625	41.11	58.89
2	17	9	3	17	14644	7.65	95		5205	9439	35.54	64.46
10	15	9	5	17	14642	7.65	96		5506	9136	37.6	62.4
5	7	9	5	17	14627	7.64	97		5499	9128	37.59	62.41
7	1	9	4	16	14627	7.64	98		5413	9214	37.01	62.99
3	4	9	4	17	14624	7.64	99		5155	9469	35.25	64.75
7	24	9	6	15	14620	7.64	100		5863	8757	40.1	59.9
9	16	9	4	16	14618	7.64	101	191400	5267	9351	36.03	63.97
4	15	9	4	16	14613	7.63	102		5254	9359	35.95	64.05
10	9	9	6	17	14611	7.63	103		5910	8701	40.45	59.55
6	11	9	5	17	14610	7.63	104		5477	9133	37.49	62.51
8	20	9	5	15	14608	7.63	105		6067	8541	41.53	58.47
1	23	9	6	17	14605	7.63	106		5535	9070	37.9	62.1
2	20	9	6	16	14604	7.63	107		5492	9112	37.61	62.39
8	27	9	5	16	14601	7.63	108		5674	8927	38.86	61.14
2	19	9	5	16	14597	7.63	109		5140	9457	35.21	64.79
10	28	9	4	17	14597	7.63	110		5582	9015	38.24	61.76
2	16	9	2	17	14591	7.62	111		5578	9013	38.23	61.77
8	26	9	4	18	14589	7.62	112		6139	8450	42.08	57.92
6	19	9	6	16	14588	7.62	113		6017	8571	41.25	58.75
4	30	9	5	16	14581	7.62	114		5238	9343	35.92	64.08
9	11	9	6	15	14580	7.62	115		5760	8820	39.51	60.49
5	15	9	6	16	14578	7.62	116		5595	8983	38.38	61.62
6	11	9	5	16	14578	7.62	117		5528	9050	37.92	62.08
9	1	9	3	17	14578	7.62	118		5401	9177	37.05	62.95
10	8	9	5	17	14576	7.62	119		5547	9029	38.06	61.94
2	27	9	6	15	14574	7.61	120		5689	8885	39.04	60.96
3	24	9	3	17	14568	7.61	121	191400	5263	9305	36.13	63.87

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
4	8	9	4	17	14565	7.61	122		5308	9257	36.44	63.56
4	23	9	5	17	14564	7.61	123		5478	9086	37.61	62.39
5	20	9	4	17	14564	7.61	124		5474	9090	37.59	62.41
5	5	9	3	17	14563	7.61	125		5047	9516	34.66	65.34
6	25	9	5	16	14562	7.61	126		5538	9024	38.03	61.97
6	11	9	5	15	14555	7.6	127		5802	8753	39.86	60.14
9	23	9	4	17	14555	7.6	128		5442	9113	37.39	62.61
6	18	9	5	15	14552	7.6	129		5737	8815	39.42	60.58
8	31	9	2	17	14552	7.6	130		5242	9310	36.02	63.98
7	15	9	4	17	14547	7.6	131		5598	8949	38.48	61.52
7	15	9	4	16	14542	7.6	132		5441	9101	37.42	62.58
6	30	9	3	17	14541	7.6	133		5422	9119	37.29	62.71
9	17	9	5	15	14540	7.6	134		6051	8489	41.62	58.38
5	20	9	4	16	14538	7.6	135		5353	9185	36.82	63.18
10	30	9	6	16	14537	7.6	136		5394	9143	37.11	62.89
4	28	9	3	17	14536	7.59	137		5192	9344	35.72	64.28
8	28	9	6	16	14534	7.59	138		5896	8638	40.57	59.43
4	24	9	6	16	14532	7.59	139		5515	9017	37.95	62.05
6	24	9	4	18	14529	7.59	140		5947	8582	40.93	59.07
2	12	9	5	16	14526	7.59	141	191400	5190	9336	35.73	64.27
10	23	9	6	15	14518	7.59	142		6029	8489	41.53	58.47
7	8	9	4	17	14517	7.58	143		5475	9042	37.71	62.29
7	22	9	4	17	14517	7.58	144		5498	9019	37.87	62.13
10	30	9	6	15	14514	7.58	145		5401	9113	37.21	62.79
6	29	9	2	17	14511	7.58	146		5328	9183	36.72	63.28
9	15	9	3	16	14510	7.58	147		5336	9174	36.77	63.23
7	13	9	2	16	14507	7.58	148		5399	9108	37.22	62.78
6	16	9	3	16	14506	7.58	149		5329	9177	36.74	63.26
10	29	9	5	17	14505	7.58	150		5653	8852	38.97	61.03
4	22	9	4	16	14501	7.58	151		5122	9379	35.32	64.68
2	6	9	6	17	14500	7.58	152		5585	8915	38.52	61.48
10	8	9	5	16	14500	7.58	153		5531	8969	38.14	61.86
3	26	9	5	16	14499	7.58	154		5097	9402	35.15	64.85
6	5	9	6	15	14497	7.57	155		5941	8556	40.98	59.02
3	26	9	5	18	14495	7.57	156		5620	8875	38.77	61.23
3	26	9	5	17	14491	7.57	157		5702	8789	39.35	60.65
6	18	9	5	18	14491	7.57	158		5655	8836	39.02	60.98
6	25	9	5	15	14491	7.57	159		5775	8716	39.85	60.15
9	24	9	5	17	14489	7.57	160		5415	9074	37.37	62.63
5	21	9	5	16	14487	7.57	161	191400	5336	9151	36.83	63.17
7	31	9	6	15	14487	7.57	162		5740	8747	39.62	60.38
4	3	9	6	17	14486	7.57	163		5547	8939	38.29	61.71
5	29	9	6	15	14486	7.57	164		5714	8772	39.44	60.56
7	14	9	3	17	14485	7.57	165		5471	9014	37.77	62.23
2	27	9	6	16	14484	7.57	166		5324	9160	36.76	63.24
7	17	9	6	16	14481	7.57	167		5921	8560	40.89	59.11
5	15	9	6	15	14479	7.56	168		5992	8487	41.38	58.62
9	22	9	3	18	14479	7.56	169		5700	8779	39.37	60.63
7	20	9	2	16	14478	7.56	170		5265	9213	36.37	63.63
4	29	9	4	17	14475	7.56	171		5205	9270	35.96	64.04
4	23	9	5	16	14474	7.56	172		5353	9121	36.98	63.02
6	11	9	5	18	14474	7.56	173		5628	8846	38.88	61.12

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
6	24	9	4	15	14470	7.56	174		5638	8832	38.96	61.04
3	18	9	4	16	14469	7.56	175		5114	9355	35.34	64.66
10	1	9	5	17	14467	7.56	176		5518	8949	38.14	61.86
9	11	9	6	16	14464	7.56	177		5617	8847	38.83	61.17
9	17	9	5	16	14464	7.56	178		5461	9003	37.76	62.24
3	4	9	4	16	14462	7.56	179		4948	9514	34.21	65.79
7	14	9	3	16	14460	7.55	180		5270	9190	36.45	63.55
7	6	9	2	16	14459	7.55	181	191400	5433	9026	37.58	62.42
1	30	9	6	17	14454	7.55	182		5478	8976	37.9	62.1
10	29	9	5	18	14451	7.55	183		5901	8550	40.83	59.17
3	11	9	4	17	14449	7.55	184		5404	9045	37.4	62.6
7	9	9	5	16	14444	7.55	185		5434	9010	37.62	62.38
1	16	9	6	15	14435	7.54	186		5639	8796	39.06	60.94
7	8	9	4	16	14435	7.54	187		5269	9166	36.5	63.5
3	5	9	5	17	14434	7.54	188		5078	9356	35.18	64.82
5	21	9	5	15	14432	7.54	189		5800	8632	40.19	59.81
9	15	9	3	17	14431	7.54	190		5505	8926	38.15	61.85
4	29	9	4	16	14417	7.53	191		4984	9433	34.57	65.43
1	13	9	3	16	14416	7.53	192		4902	9514	34	66
9	24	9	5	16	14416	7.53	193		5506	8910	38.19	61.81
8	21	9	6	18	14414	7.53	194		6127	8287	42.51	57.49
8	19	9	4	16	14413	7.53	195		5368	9045	37.24	62.76
7	10	9	6	17	14410	7.53	196		6163	8247	42.77	57.23
1	23	9	6	16	14399	7.52	197		5516	8883	38.31	61.69
7	7	9	3	16	14399	7.52	198		5366	9033	37.27	62.73
7	16	9	5	16	14399	7.52	199		5458	8941	37.91	62.09
3	11	9	4	16	14397	7.52	200		5207	9190	36.17	63.83

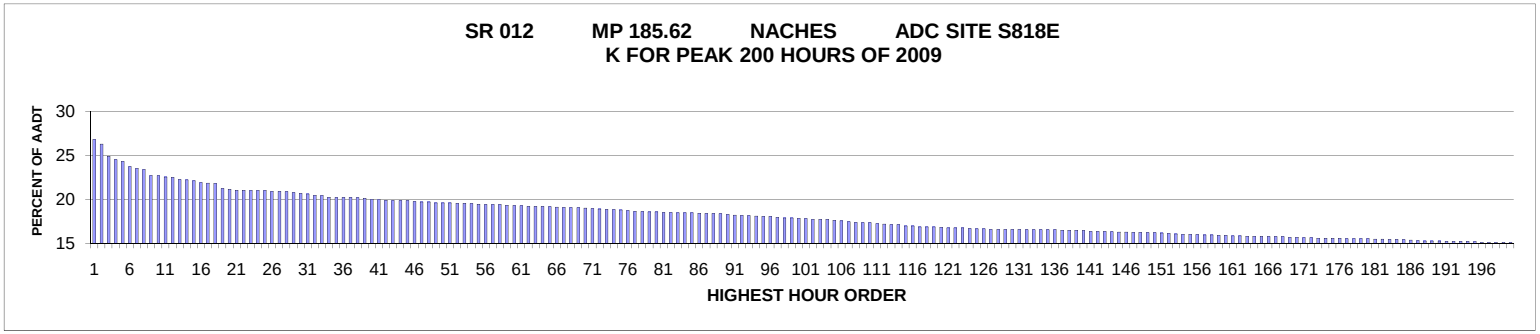

AADT= 4209 **K 30 FACTOR=** 20.67 **K 100 FACTOR=** 17.84 **K 200 FACTOR=** 15.06 **D FACTOR=** 56.92

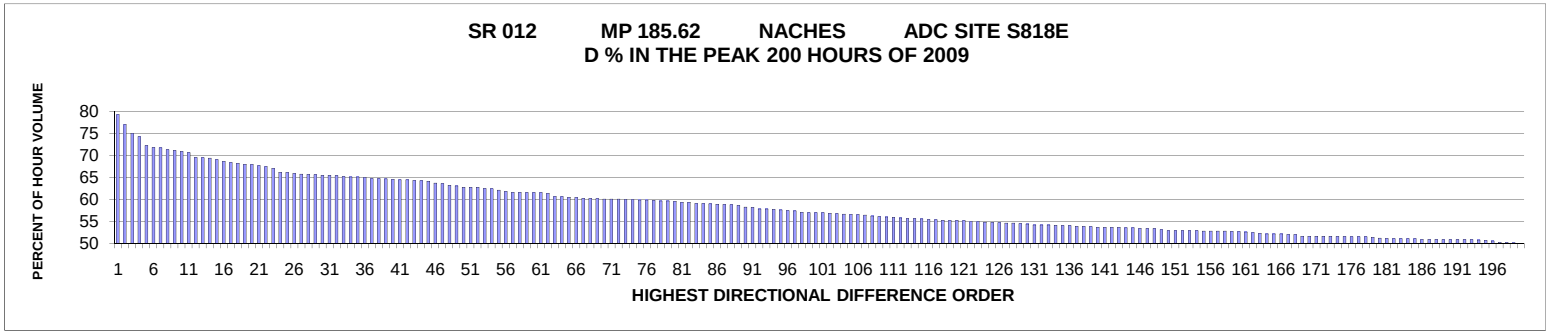

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	2	9	1	18	1128	26.8	1	4209	895	233	79.34	20.66
5	25	9	2	12	1107	26.3	2		625	482	56.46	43.54
7	19	9	1	15	1048	24.9	3		584	464	55.73	44.27
5	25	9	2	14	1031	24.5	4		615	416	59.65	40.35
5	25	9	2	13	1024	24.33	5		630	394	61.52	38.48
7	19	9	1	16	998	23.71	6		636	362	63.73	36.27
5	25	9	2	15	990	23.52	7		587	403	59.29	40.71
5	25	9	2	16	984	23.38	8		590	394	59.96	40.04
7	12	9	1	14	955	22.69	9		468	487	49.01	50.99
7	19	9	1	13	955	22.69	10		463	492	48.48	51.52
7	12	9	1	13	949	22.55	11		474	475	49.95	50.05
5	24	9	1	13	947	22.5	12		408	539	43.08	56.92
7	26	9	1	15	936	22.24	13		454	482	48.5	51.5
7	19	9	1	14	935	22.21	14		506	429	54.12	45.88
5	25	9	2	17	930	22.1	15		609	321	65.48	34.52
7	5	9	1	16	921	21.88	16		600	321	65.15	34.85
7	19	9	1	17	920	21.86	17		622	298	67.61	32.39

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	5	9	1	15	918	21.81	18		500	418	54.47	45.53
9	7	9	2	13	894	21.24	19		449	445	50.22	49.78
8	16	9	1	16	890	21.15	20		546	344	61.35	38.65
7	5	9	1	14	886	21.05	21	4209	480	406	54.18	45.82
5	24	9	1	14	885	21.03	22		393	492	44.41	55.59
7	19	9	1	12	884	21	23		415	469	46.95	53.05
8	9	9	1	16	884	21	24		552	332	62.44	37.56
9	7	9	2	14	884	21	25		456	428	51.58	48.42
7	12	9	1	15	880	20.91	26		440	440	50	50
8	2	9	1	15	880	20.91	27		447	433	50.8	49.2
6	28	9	1	16	878	20.86	28		486	392	55.35	44.65
5	24	9	1	17	874	20.77	29		561	313	64.19	35.81
9	7	9	2	15	870	20.67	30		503	367	57.82	42.18
7	26	9	1	13	868	20.62	31		410	458	47.24	52.76
6	28	9	1	14	861	20.46	32		426	435	49.48	50.52
5	24	9	1	12	859	20.41	33		352	507	40.98	59.02
6	28	9	1	15	852	20.24	34		448	404	52.58	47.42
7	5	9	1	13	851	20.22	35		473	378	55.58	44.42
7	26	9	1	14	851	20.22	36		416	435	48.88	51.12
8	2	9	1	17	851	20.22	37		524	327	61.57	38.43
6	28	9	1	13	850	20.19	38		362	488	42.59	57.41
7	12	9	1	16	848	20.15	39		494	354	58.25	41.75
5	23	9	7	11	841	19.98	40		237	604	28.18	71.82
5	24	9	1	16	840	19.96	41	4209	502	338	59.76	40.24
5	23	9	7	12	837	19.89	42		256	581	30.59	69.41
8	9	9	1	17	836	19.86	43		540	296	64.59	35.41
5	23	9	7	13	835	19.84	44		292	543	34.97	65.03
8	2	9	1	14	835	19.84	45		346	489	41.44	58.56
9	6	9	1	14	831	19.74	46		446	385	53.67	46.33
7	5	9	1	17	829	19.7	47		576	253	69.48	30.52
7	26	9	1	16	829	19.7	48		469	360	56.57	43.43
8	9	9	1	14	825	19.6	49		455	370	55.15	44.85
5	23	9	7	16	824	19.58	50		445	379	54	46
7	12	9	1	12	824	19.58	51		389	435	47.21	52.79
8	9	9	1	15	823	19.55	52		439	384	53.34	46.66
9	20	9	1	15	823	19.55	53		418	405	50.79	49.21
6	21	9	1	13	821	19.51	54		387	434	47.14	52.86
9	7	9	2	16	818	19.43	55		491	327	60.02	39.98
7	12	9	1	17	816	19.39	56		550	266	67.4	32.6
8	23	9	1	13	816	19.39	57		451	365	55.27	44.73
9	20	9	1	16	816	19.39	58		420	396	51.47	48.53
8	2	9	1	16	814	19.34	59		490	324	60.2	39.8
9	6	9	1	12	812	19.29	60		346	466	42.61	57.39
8	9	9	1	13	811	19.27	61	4209	400	411	49.32	50.68
8	16	9	1	14	808	19.2	62		403	405	49.88	50.12
5	24	9	1	18	807	19.17	63		554	253	68.65	31.35
9	6	9	1	15	807	19.17	64		513	294	63.57	36.43
9	6	9	1	13	806	19.15	65		368	438	45.66	54.34
5	24	9	1	15	804	19.1	66		395	409	49.13	50.87
7	26	9	1	17	803	19.08	67		546	257	68	32
5	25	9	2	11	802	19.05	68		430	372	53.62	46.38
6	28	9	1	12	801	19.03	69		359	442	44.82	55.18

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	16	9	1	17	800	19.01	70		514	286	64.25	35.75
8	23	9	1	15	797	18.94	71		448	349	56.21	43.79
8	23	9	1	14	795	18.89	72		385	410	48.43	51.57
7	3	9	6	12	794	18.86	73		319	475	40.18	59.82
7	18	9	7	13	793	18.84	74		344	449	43.38	56.62
9	5	9	7	11	790	18.77	75		272	518	34.43	65.57
5	22	9	6	19	788	18.72	76		219	569	27.79	72.21
8	16	9	1	15	785	18.65	77		419	366	53.38	46.62
8	2	9	1	13	783	18.6	78		299	484	38.19	61.81
7	18	9	7	12	781	18.56	79		308	473	39.44	60.56
9	5	9	7	12	781	18.56	80		322	459	41.23	58.77
5	23	9	7	18	779	18.51	81	4209	502	277	64.44	35.56
5	23	9	7	14	778	18.48	82		334	444	42.93	57.07
8	23	9	1	16	777	18.46	83		478	299	61.52	38.48
9	5	9	7	13	777	18.46	84		299	478	38.48	61.52
9	7	9	2	12	777	18.46	85		405	372	52.12	47.88
7	5	9	1	12	775	18.41	86		417	358	53.81	46.19
8	16	9	1	13	774	18.39	87		415	359	53.62	46.38
7	3	9	6	14	773	18.37	88		340	433	43.98	56.02
8	2	9	1	12	772	18.34	89		349	423	45.21	54.79
5	23	9	7	15	769	18.27	90		363	406	47.2	52.8
8	9	9	1	12	767	18.22	91		362	405	47.2	52.8
6	21	9	1	14	765	18.18	92		404	361	52.81	47.19
5	23	9	7	17	763	18.13	93		458	305	60.03	39.97
6	21	9	1	12	761	18.08	94		410	351	53.88	46.12
9	13	9	1	13	760	18.06	95		401	359	52.76	47.24
9	20	9	1	14	760	18.06	96		386	374	50.79	49.21
5	24	9	1	11	755	17.94	97		239	516	31.66	68.34
5	22	9	6	17	752	17.87	98		239	513	31.78	68.22
9	20	9	1	13	752	17.87	99		364	388	48.4	51.6
9	4	9	6	17	751	17.84	100		280	471	37.28	62.72
6	14	9	1	15	750	17.82	101	4209	451	299	60.13	39.87
6	27	9	7	16	746	17.72	102		379	367	50.8	49.2
7	19	9	1	18	746	17.72	103		535	211	71.72	28.28
7	26	9	1	12	746	17.72	104		361	385	48.39	51.61
7	18	9	7	11	742	17.63	105		253	489	34.1	65.9
6	14	9	1	14	739	17.56	106		385	354	52.1	47.9
5	22	9	6	18	733	17.42	107		227	506	30.97	69.03
8	23	9	1	12	731	17.37	108		383	348	52.39	47.61
9	13	9	1	14	730	17.34	109		385	345	52.74	47.26
9	5	9	7	15	729	17.32	110		400	329	54.87	45.13
7	25	9	7	12	725	17.22	111		267	458	36.83	63.17
9	13	9	1	15	724	17.2	112		402	322	55.52	44.48
8	16	9	1	12	720	17.11	113		326	394	45.28	54.72
8	30	9	1	13	720	17.11	114		355	365	49.31	50.69
5	25	9	2	18	714	16.96	115		467	247	65.41	34.59
8	30	9	1	17	714	16.96	116		395	319	55.32	44.68
6	21	9	1	15	710	16.87	117		380	330	53.52	46.48
5	22	9	6	16	709	16.84	118		250	459	35.26	64.74
7	18	9	7	15	709	16.84	119		344	365	48.52	51.48
7	18	9	7	16	708	16.82	120		373	335	52.68	47.32
6	21	9	1	16	705	16.75	121	4209	410	295	58.16	41.84

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	3	9	6	13	705	16.75	122		279	426	39.57	60.43
7	5	9	1	18	705	16.75	123		490	215	69.5	30.5
8	30	9	1	14	702	16.68	124		361	341	51.42	48.58
7	18	9	7	14	701	16.65	125		283	418	40.37	59.63
9	5	9	7	14	701	16.65	126		327	374	46.65	53.35
7	3	9	6	15	698	16.58	127		296	402	42.41	57.59
8	30	9	1	16	698	16.58	128		419	279	60.03	39.97
9	13	9	1	16	698	16.58	129		423	275	60.6	39.4
9	20	9	1	17	698	16.58	130		411	287	58.88	41.12
8	9	9	1	18	697	16.56	131		492	205	70.59	29.41
6	28	9	1	17	696	16.54	132		439	257	63.07	36.93
7	24	9	6	17	696	16.54	133		279	417	40.09	59.91
9	7	9	2	17	696	16.54	134		396	300	56.9	43.1
5	23	9	7	10	695	16.51	135		179	516	25.76	74.24
6	27	9	7	15	695	16.51	136		332	363	47.77	52.23
5	31	9	1	14	694	16.49	137		375	319	54.03	45.97
7	25	9	7	11	694	16.49	138		240	454	34.58	65.42
8	1	9	7	12	694	16.49	139		249	445	35.88	64.12
8	8	9	7	13	693	16.46	140		311	382	44.88	55.12
6	14	9	1	13	688	16.35	141	4209	337	351	48.98	51.02
8	1	9	7	15	688	16.35	142		312	376	45.35	54.65
9	5	9	7	16	688	16.35	143		397	291	57.7	42.3
8	23	9	1	17	687	16.32	144		447	240	65.07	34.93
8	1	9	7	16	685	16.27	145		357	328	52.12	47.88
9	4	9	6	18	685	16.27	146		242	443	35.33	64.67
8	30	9	1	15	684	16.25	147		318	366	46.49	53.51
9	4	9	6	19	683	16.23	148		241	442	35.29	64.71
7	11	9	7	15	682	16.2	149		366	316	53.67	46.33
8	1	9	7	14	681	16.18	150		271	410	39.79	60.21
9	13	9	1	17	680	16.16	151		407	273	59.85	40.15
7	19	9	1	11	679	16.13	152		296	383	43.59	56.41
9	6	9	1	16	676	16.06	153		424	252	62.72	37.28
6	27	9	7	17	674	16.01	154		344	330	51.04	48.96
8	16	9	1	18	674	16.01	155		452	222	67.06	32.94
9	27	9	1	15	673	15.99	156		331	342	49.18	50.82
7	3	9	6	16	671	15.94	157		275	396	40.98	59.02
9	27	9	1	14	671	15.94	158		325	346	48.44	51.56
6	26	9	6	17	670	15.92	159		252	418	37.61	62.39
8	2	9	1	19	670	15.92	160		516	154	77.01	22.99
7	25	9	7	13	667	15.85	161	4209	303	364	45.43	54.57
9	12	9	7	13	667	15.85	162		303	364	45.43	54.57
8	15	9	7	14	665	15.8	163		338	327	50.83	49.17
6	27	9	7	12	664	15.78	164		305	359	45.93	54.07
9	13	9	1	12	664	15.78	165		319	345	48.04	51.96
6	27	9	7	14	663	15.75	166		286	377	43.14	56.86
8	7	9	6	16	663	15.75	167		287	376	43.29	56.71
9	5	9	7	10	663	15.75	168		193	470	29.11	70.89
9	27	9	1	17	661	15.7	169		356	305	53.86	46.14
8	2	9	1	11	660	15.68	170		250	410	37.88	62.12
7	4	9	7	12	658	15.63	171		270	388	41.03	58.97
7	26	9	1	18	658	15.63	172		468	190	71.12	28.88
8	8	9	7	12	656	15.59	173		301	355	45.88	54.12

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
6	7	9	1	14	655	15.56	174		344	311	52.52	47.48
7	11	9	7	13	655	15.56	175		270	385	41.22	58.78
7	17	9	6	18	655	15.56	176		233	422	35.57	64.43
5	31	9	1	13	653	15.51	177		320	333	49	51
8	8	9	7	11	653	15.51	178		228	425	34.92	65.08
7	12	9	1	18	652	15.49	179		409	243	62.73	37.27
8	8	9	7	14	652	15.49	180		294	358	45.09	54.91
8	1	9	7	11	651	15.47	181	4209	187	464	28.73	71.27
9	27	9	1	16	651	15.47	182		307	344	47.16	52.84
7	3	9	6	17	650	15.44	183		280	370	43.08	56.92
7	11	9	7	12	650	15.44	184		286	364	44	56
8	1	9	7	13	648	15.4	185		222	426	34.26	65.74
9	5	9	7	17	647	15.37	186		329	318	50.85	49.15
9	20	9	1	12	643	15.28	187		309	334	48.06	51.94
8	22	9	7	14	642	15.25	188		283	359	44.08	55.92
8	30	9	1	12	642	15.25	189		328	314	51.09	48.91
8	30	9	1	18	642	15.25	190		381	261	59.35	40.65
5	22	9	6	20	641	15.23	191		217	424	33.85	66.15
7	11	9	7	16	640	15.21	192		329	311	51.41	48.59
7	17	9	6	16	640	15.21	193		270	370	42.19	57.81
7	18	9	7	17	640	15.21	194		394	246	61.56	38.44
7	17	9	6	17	638	15.16	195		252	386	39.5	60.5
8	14	9	6	18	636	15.11	196		204	432	32.08	67.92
7	24	9	6	18	635	15.09	197		218	417	34.33	65.67
9	4	9	6	16	635	15.09	198		257	378	40.47	59.53
9	6	9	1	11	635	15.09	199		215	420	33.86	66.14
5	24	9	1	19	634	15.06	200		476	158	75.08	24.92

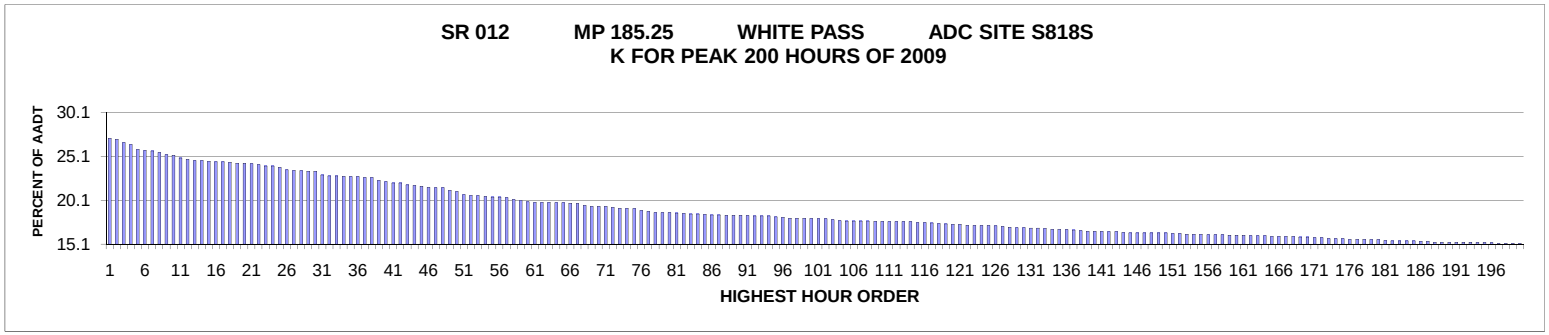

AADT= 2121 **K 30 FACTOR=** 23.39 **K 100 FACTOR=** 18.01 **K 200 FACTOR=** 15.18 **D FACTOR=** 59.29

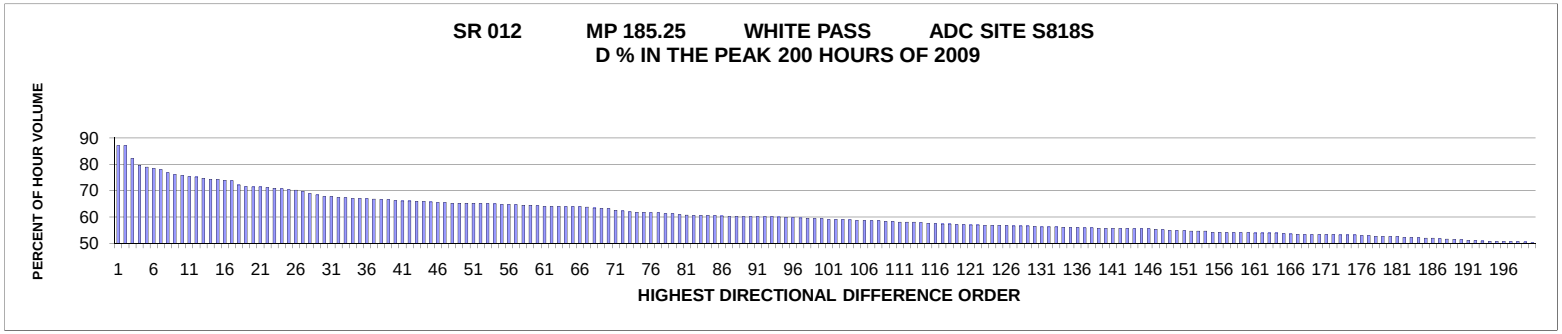

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
5	23	9	7	11	576	27.16	1	2121	143	433	24.83	75.17
7	19	9	1	15	574	27.06	2		310	264	54.01	45.99
7	5	9	1	16	565	26.64	3		397	168	70.27	29.73
7	5	9	1	15	561	26.45	4		313	248	55.79	44.21
7	19	9	1	17	549	25.88	5		389	160	70.86	29.14
7	19	9	1	16	547	25.79	6		365	182	66.73	33.27
5	23	9	7	12	545	25.7	7		140	405	25.69	74.31
9	7	9	2	13	541	25.51	8		297	244	54.9	45.1
9	5	9	7	11	536	25.27	9		138	398	25.75	74.25
7	5	9	1	14	535	25.22	10		305	230	57.01	42.99
5	23	9	7	10	528	24.89	11		114	414	21.59	78.41
9	6	9	1	15	525	24.75	12		359	166	68.38	31.62
4	5	9	1	18	522	24.61	13		172	350	32.95	67.05
7	19	9	1	14	522	24.61	14		321	201	61.49	38.51
9	6	9	1	14	520	24.52	15		295	225	56.73	43.27
7	19	9	1	13	519	24.47	16		277	242	53.37	46.63
9	6	9	1	12	519	24.47	17		205	314	39.5	60.5

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	5	9	1	17	518	24.42	18		387	131	74.71	25.29
5	23	9	7	18	516	24.33	19		355	161	68.8	31.2
7	5	9	1	13	516	24.33	20		310	206	60.08	39.92
5	23	9	7	16	514	24.23	21	2121	290	224	56.42	43.58
5	23	9	7	13	512	24.14	22		185	327	36.13	63.87
5	22	9	6	17	509	24	23		178	331	34.97	65.03
5	22	9	6	19	509	24	24		146	363	28.68	71.32
9	7	9	2	14	506	23.86	25		291	215	57.51	42.49
9	5	9	7	12	500	23.57	26		174	326	34.8	65.2
5	23	9	7	17	498	23.48	27		337	161	67.67	32.33
9	5	9	7	13	497	23.43	28		168	329	33.8	66.2
9	6	9	1	13	496	23.39	29		221	275	44.56	55.44
9	7	9	2	15	496	23.39	30		322	174	64.92	35.08
9	7	9	2	16	487	22.96	31		315	172	64.68	35.32
6	28	9	1	15	485	22.87	32		246	239	50.72	49.28
8	9	9	1	14	485	22.87	33		274	211	56.49	43.51
5	23	9	7	14	484	22.82	34		197	287	40.7	59.3
6	28	9	1	16	483	22.77	35		270	213	55.9	44.1
8	9	9	1	17	483	22.77	36		327	156	67.7	32.3
7	3	9	6	12	481	22.68	37		190	291	39.5	60.5
8	9	9	1	15	481	22.68	38		256	225	53.22	46.78
9	5	9	7	10	474	22.35	39		100	374	21.1	78.9
6	14	9	1	15	471	22.21	40		298	173	63.27	36.73
7	5	9	1	12	468	22.07	41	2121	266	202	56.84	43.16
8	9	9	1	13	468	22.07	42		243	225	51.92	48.08
7	3	9	6	14	463	21.83	43		209	254	45.14	54.86
5	23	9	7	15	462	21.78	44		237	225	51.3	48.7
4	5	9	1	17	460	21.69	45		199	261	43.26	56.74
6	28	9	1	13	457	21.55	46		200	257	43.76	56.24
6	28	9	1	14	456	21.5	47		241	215	52.85	47.15
8	9	9	1	16	456	21.5	48		275	181	60.31	39.69
6	21	9	1	13	450	21.22	49		243	207	54	46
5	22	9	6	16	447	21.07	50		159	288	35.57	64.43
9	7	9	2	12	439	20.7	51		229	210	52.16	47.84
9	5	9	7	16	438	20.65	52		262	176	59.82	40.18
5	22	9	6	18	437	20.6	53		152	285	34.78	65.22
7	5	9	1	18	435	20.51	54		334	101	76.78	23.22
7	19	9	1	12	434	20.46	55		214	220	49.31	50.69
9	4	9	6	18	434	20.46	56		160	274	36.87	63.13
9	4	9	6	17	432	20.37	57		177	255	40.97	59.03
9	5	9	7	15	428	20.18	58		251	177	58.64	41.36
10	11	9	1	15	425	20.04	59		199	226	46.82	53.18
9	5	9	7	14	422	19.9	60		194	228	45.97	54.03
5	22	9	6	20	421	19.85	61	2121	147	274	34.92	65.08
7	19	9	1	18	421	19.85	62		317	104	75.3	24.7
9	13	9	1	14	421	19.85	63		241	180	57.24	42.76
6	14	9	1	14	420	19.8	64		223	197	53.1	46.9
9	20	9	1	15	420	19.8	65		234	186	55.71	44.29
10	11	9	1	16	419	19.75	66		195	224	46.54	53.46
6	21	9	1	12	418	19.71	67		235	183	56.22	43.78
6	28	9	1	12	414	19.52	68		196	218	47.34	52.66
4	5	9	1	19	411	19.38	69		108	303	26.28	73.72

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
9	6	9	1	16	411	19.38	70		271	140	65.94	34.06
9	13	9	1	15	411	19.38	71		231	180	56.2	43.8
5	23	9	7	19	409	19.28	72		274	135	66.99	33.01
6	21	9	1	15	407	19.19	73		220	187	54.05	45.95
9	20	9	1	16	407	19.19	74		237	170	58.23	41.77
9	13	9	1	16	406	19.14	75		270	136	66.5	33.5
9	6	9	1	18	401	18.91	76		305	96	76.06	23.94
7	25	9	7	12	399	18.81	77		152	247	38.1	61.9
7	3	9	6	13	396	18.67	78		140	256	35.35	64.65
9	4	9	6	16	396	18.67	79		154	242	38.89	61.11
9	7	9	2	17	396	18.67	80		253	143	63.89	36.11
9	6	9	1	11	395	18.62	81	2121	129	266	32.66	67.34
9	20	9	1	14	394	18.58	82		210	184	53.3	46.7
6	27	9	7	16	393	18.53	83		215	178	54.71	45.29
12	26	9	7	14	393	18.53	84		207	186	52.67	47.33
6	21	9	1	14	392	18.48	85		211	181	53.83	46.17
7	19	9	1	11	391	18.43	86		168	223	42.97	57.03
10	11	9	1	14	391	18.43	87		173	218	44.25	55.75
7	25	9	7	11	390	18.39	88		129	261	33.08	66.92
8	9	9	1	12	390	18.39	89		191	199	48.97	51.03
10	11	9	1	17	390	18.39	90		209	181	53.59	46.41
8	9	9	1	18	389	18.34	91		275	114	70.69	29.31
7	3	9	6	15	388	18.29	92		153	235	39.43	60.57
7	24	9	6	14	388	18.29	93		166	222	42.78	57.22
9	13	9	1	13	388	18.29	94		216	172	55.67	44.33
8	30	9	1	15	386	18.2	95		199	187	51.55	48.45
9	20	9	1	13	385	18.15	96		214	171	55.58	44.42
7	17	9	6	17	383	18.06	97		165	218	43.08	56.92
10	11	9	1	13	383	18.06	98		199	184	51.96	48.04
12	27	9	1	15	383	18.06	99		222	161	57.96	42.04
2	8	9	1	15	382	18.01	100		268	114	70.16	29.84
5	22	9	6	14	381	17.96	101	2121	152	229	39.9	60.1
8	30	9	1	17	381	17.96	102		246	135	64.57	35.43
7	24	9	6	17	379	17.87	103		167	212	44.06	55.94
7	5	9	1	19	377	17.77	104		300	77	79.58	20.42
5	23	9	7	9	376	17.73	105		67	309	17.82	82.18
6	27	9	7	15	376	17.73	106		191	185	50.8	49.2
6	28	9	1	17	376	17.73	107		224	152	59.57	40.43
9	4	9	6	19	376	17.73	108		148	228	39.36	60.64
8	30	9	1	16	375	17.68	109		240	135	64	36
9	5	9	7	17	375	17.68	110		252	123	67.2	32.8
5	22	9	6	13	374	17.63	111		135	239	36.1	63.9
5	22	9	6	15	374	17.63	112		150	224	40.11	59.89
6	21	9	1	16	374	17.63	113		217	157	58.02	41.98
7	3	9	6	16	374	17.63	114		154	220	41.18	58.82
6	26	9	6	13	372	17.54	115		169	203	45.43	54.57
8	30	9	1	13	372	17.54	116		174	198	46.77	53.23
9	13	9	1	17	371	17.49	117		238	133	64.15	35.85
6	27	9	7	12	370	17.44	118		173	197	46.76	53.24
8	30	9	1	14	369	17.4	119		194	175	52.57	47.43
7	3	9	6	17	368	17.35	120		149	219	40.49	59.51
7	31	9	6	16	368	17.35	121	2121	169	199	45.92	54.08

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
9	6	9	1	17	366	17.26	122		241	125	65.85	34.15
4	5	9	1	16	365	17.21	123		194	171	53.15	46.85
6	7	9	1	13	365	17.21	124		214	151	58.63	41.37
8	7	9	6	13	365	17.21	125		180	185	49.32	50.68
6	26	9	6	16	364	17.16	126		160	204	43.96	56.04
7	17	9	6	18	363	17.11	127		141	222	38.84	61.16
1	3	9	7	15	361	17.02	128		257	104	71.19	28.81
6	14	9	1	13	360	16.97	129		199	161	55.28	44.72
8	22	9	7	14	360	16.97	130		156	204	43.33	56.67
6	26	9	6	14	359	16.93	131		163	196	45.4	54.6
8	30	9	1	12	359	16.93	132		187	172	52.09	47.91
7	10	9	6	16	358	16.88	133		159	199	44.41	55.59
9	4	9	6	20	356	16.78	134		146	210	41.01	58.99
9	7	9	2	11	356	16.78	135		169	187	47.47	52.53
9	5	9	7	9	355	16.74	136		46	309	12.96	87.04
9	13	9	1	12	354	16.69	137		154	200	43.5	56.5
6	28	9	1	11	353	16.64	138		163	190	46.18	53.82
6	21	9	1	11	351	16.55	139		172	179	49	51
6	26	9	6	17	351	16.55	140		140	211	39.89	60.11
7	17	9	6	12	351	16.55	141	2121	140	211	39.89	60.11
6	7	9	1	14	350	16.5	142		177	173	50.57	49.43
6	26	9	6	18	350	16.5	143		141	209	40.29	59.71
9	20	9	1	17	348	16.41	144		232	116	66.67	33.33
6	14	9	1	16	347	16.36	145		209	138	60.23	39.77
6	19	9	6	15	347	16.36	146		160	187	46.11	53.89
7	17	9	6	14	347	16.36	147		136	211	39.19	60.81
7	31	9	6	18	347	16.36	148		121	226	34.87	65.13
8	7	9	6	15	347	16.36	149		162	185	46.69	53.31
9	18	9	6	15	347	16.36	150		181	166	52.16	47.84
1	3	9	7	14	346	16.31	151		179	167	51.73	48.27
6	27	9	7	14	346	16.31	152		153	193	44.22	55.78
7	17	9	6	15	344	16.22	153		120	224	34.88	65.12
8	14	9	6	18	344	16.22	154		119	225	34.59	65.41
9	4	9	6	15	344	16.22	155		143	201	41.57	58.43
7	3	9	6	11	343	16.17	156		98	245	28.57	71.43
8	7	9	6	16	343	16.17	157		144	199	41.98	58.02
12	26	9	7	13	343	16.17	158		118	225	34.4	65.6
7	17	9	6	16	342	16.12	159		143	199	41.81	58.19
9	13	9	1	18	342	16.12	160		253	89	73.98	26.02
9	27	9	1	15	342	16.12	161	2121	176	166	51.46	48.54
2	8	9	1	16	340	16.03	162		243	97	71.47	28.53
7	24	9	6	18	340	16.03	163		121	219	35.59	64.41
8	7	9	6	18	340	16.03	164		131	209	38.53	61.47
5	23	9	7	20	339	15.98	165		224	115	66.08	33.92
8	14	9	6	17	339	15.98	166		138	201	40.71	59.29
9	4	9	6	14	339	15.98	167		151	188	44.54	55.46
9	11	9	6	18	339	15.98	168		170	169	50.15	49.85
6	27	9	7	17	337	15.89	169		187	150	55.49	44.51
9	5	9	7	18	337	15.89	170		243	94	72.11	27.89
7	10	9	6	15	336	15.84	171		142	194	42.26	57.74
8	30	9	1	18	336	15.84	172		234	102	69.64	30.36
6	28	9	1	18	333	15.7	173		218	115	65.47	34.53

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	14	9	6	16	333	15.7	174		157	176	47.15	52.85
12	27	9	1	16	333	15.7	175		220	113	66.07	33.93
1	3	9	7	17	332	15.65	176		289	43	87.05	12.95
6	20	9	7	13	332	15.65	177		168	164	50.6	49.4
7	2	9	5	15	332	15.65	178		120	212	36.14	63.86
6	20	9	7	16	331	15.61	179		190	141	57.4	42.6
6	27	9	7	18	331	15.61	180		187	144	56.5	43.5
8	14	9	6	14	329	15.51	181	2121	130	199	39.51	60.49
1	4	9	1	14	328	15.46	182		204	124	62.2	37.8
5	22	9	6	12	328	15.46	183		120	208	36.59	63.41
7	17	9	6	13	328	15.46	184		123	205	37.5	62.5
12	27	9	1	14	328	15.46	185		136	192	41.46	58.54
6	14	9	1	12	327	15.42	186		147	180	44.95	55.05
6	20	9	7	15	327	15.42	187		165	162	50.46	49.54
6	26	9	6	15	325	15.32	188		150	175	46.15	53.85
7	3	9	6	18	325	15.32	189		149	176	45.85	54.15
7	24	9	6	19	325	15.32	190		117	208	36	64
8	21	9	6	15	325	15.32	191		118	207	36.31	63.69
8	22	9	7	13	325	15.32	192		140	185	43.08	56.92
9	5	9	7	19	325	15.32	193		246	79	75.69	24.31
7	10	9	6	17	324	15.28	194		124	200	38.27	61.73
7	25	9	7	15	324	15.28	195		147	177	45.37	54.63
8	22	9	7	17	323	15.23	196		194	129	60.06	39.94
6	7	9	1	15	322	15.18	197		194	128	60.25	39.75
7	19	9	1	19	322	15.18	198		251	71	77.95	22.05
10	11	9	1	18	322	15.18	199		199	123	61.8	38.2
12	27	9	1	13	322	15.18	200		132	190	40.99	59.01

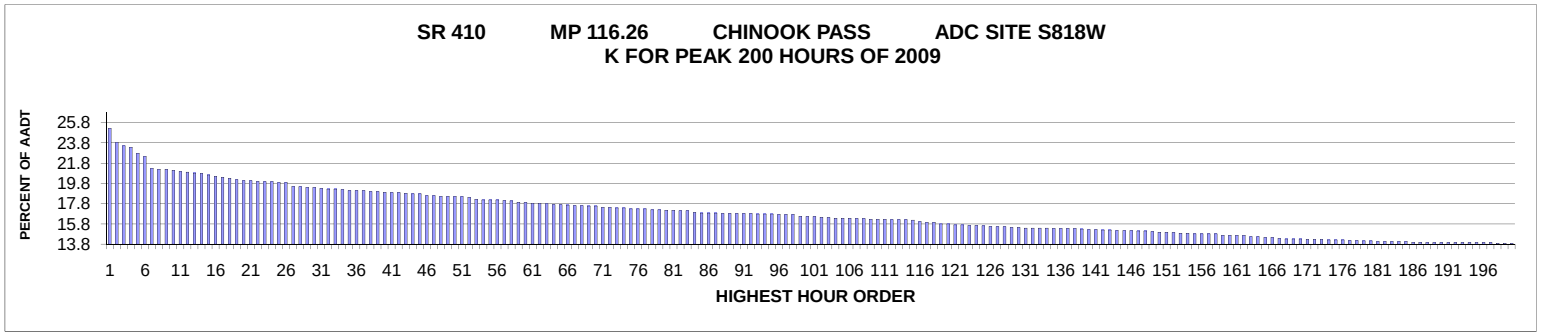

AADT= 1950 **K 30 FACTOR=** 19.38 **K 100 FACTOR=** 16.51 **K 200 FACTOR=** 13.85 **D FACTOR=** 54.76

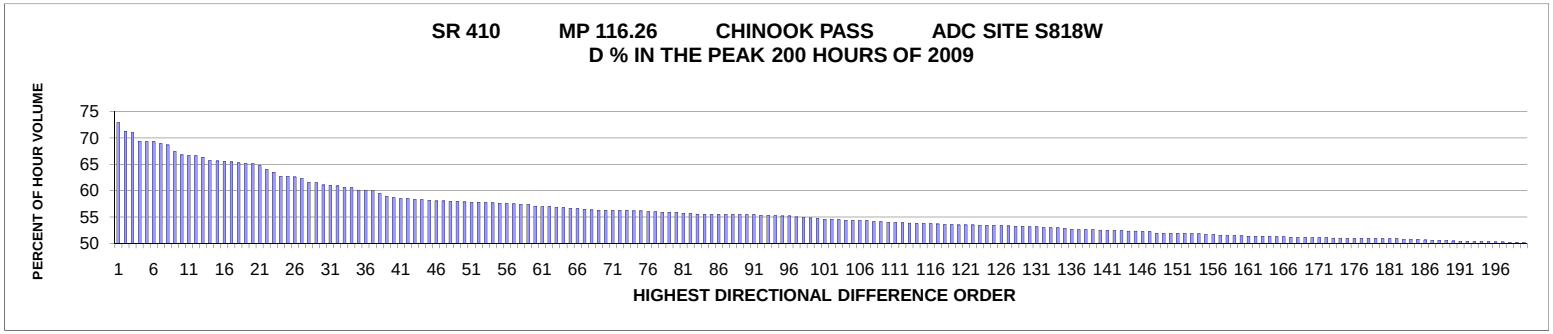

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	9	9	1	16	492	25.23	1	1950	323	169	65.65	34.35
5	25	9	2	16	465	23.85	2		261	204	56.13	43.87
5	25	9	2	12	458	23.49	3		228	230	49.78	50.22
5	25	9	2	15	456	23.38	4		262	194	57.46	42.54
9	20	9	1	16	444	22.77	5		207	237	46.62	53.38
8	16	9	1	16	438	22.46	6		243	195	55.48	44.52
5	25	9	2	13	415	21.28	7		211	204	50.84	49.16
5	24	9	1	13	413	21.18	8		192	221	46.49	53.51
5	24	9	1	16	413	21.18	9		233	180	56.42	43.58
5	25	9	2	14	411	21.08	10		202	209	49.15	50.85
9	20	9	1	15	409	20.97	11		179	230	43.77	56.23
9	20	9	1	14	408	20.92	12		203	205	49.75	50.25
9	20	9	1	13	406	20.82	13		171	235	42.12	57.88
5	24	9	1	17	405	20.77	14		245	160	60.49	39.51
9	7	9	2	14	402	20.62	15		177	225	44.03	55.97
8	30	9	1	17	400	20.51	16		186	214	46.5	53.5
8	23	9	1	14	398	20.41	17		184	214	46.23	53.77

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	9	9	1	12	396	20.31	18		177	219	44.7	55.3
8	8	9	7	14	393	20.15	19		175	218	44.53	55.47
5	24	9	1	14	391	20.05	20		178	213	45.52	54.48
9	13	9	1	13	391	20.05	21	1950	199	192	50.9	49.1
8	16	9	1	13	390	20	22		216	174	55.38	44.62
8	23	9	1	13	389	19.95	23		194	195	49.87	50.13
9	7	9	2	15	389	19.95	24		193	196	49.61	50.39
5	24	9	1	15	387	19.85	25		197	190	50.9	49.1
8	9	9	1	17	387	19.85	26		236	151	60.98	39.02
9	27	9	1	15	380	19.49	27		181	199	47.63	52.37
8	23	9	1	15	379	19.44	28		194	185	51.19	48.81
5	25	9	2	17	378	19.38	29		211	167	55.82	44.18
8	23	9	1	12	378	19.38	30		185	193	48.94	51.06
9	12	9	7	15	376	19.28	31		181	195	48.14	51.86
8	16	9	1	15	375	19.23	32		184	191	49.07	50.93
9	7	9	2	13	375	19.23	33		163	212	43.47	56.53
5	23	9	7	15	374	19.18	34		174	200	46.52	53.48
5	25	9	2	11	372	19.08	35		203	169	54.57	45.43
5	31	9	1	14	372	19.08	36		195	177	52.42	47.58
9	7	9	2	12	372	19.08	37		196	176	52.69	47.31
5	24	9	1	12	370	18.97	38		157	213	42.43	57.57
9	6	9	1	13	370	18.97	39		176	194	47.57	52.43
8	9	9	1	14	369	18.92	40		188	181	50.95	49.05
6	14	9	1	13	368	18.87	41	1950	163	205	44.29	55.71
9	20	9	1	17	368	18.87	42		185	183	50.27	49.73
8	23	9	1	16	367	18.82	43		212	155	57.77	42.23
8	9	9	1	13	366	18.77	44		177	189	48.36	51.64
9	27	9	1	16	366	18.77	45		160	206	43.72	56.28
9	13	9	1	15	362	18.56	46		201	161	55.52	44.48
9	27	9	1	17	362	18.56	47		183	179	50.55	49.45
8	9	9	1	15	361	18.51	48		185	176	51.25	48.75
9	27	9	1	13	361	18.51	49		177	184	49.03	50.97
9	27	9	1	14	361	18.51	50		161	200	44.6	55.4
6	14	9	1	14	360	18.46	51		182	178	50.56	49.44
9	7	9	2	16	359	18.41	52		186	173	51.81	48.19
9	20	9	1	12	355	18.21	53		159	196	44.79	55.21
8	9	9	1	18	354	18.15	54		236	118	66.67	33.33
8	15	9	7	17	354	18.15	55		183	171	51.69	48.31
8	16	9	1	17	354	18.15	56		222	132	62.71	37.29
8	16	9	1	14	353	18.1	57		166	187	47.03	52.97
9	6	9	1	14	352	18.05	58		167	185	47.44	52.56
6	13	9	7	15	350	17.95	59		176	174	50.29	49.71
5	23	9	7	14	349	17.9	60		168	181	48.14	51.86
5	31	9	1	17	348	17.85	61	1950	221	127	63.51	36.49
9	12	9	7	16	348	17.85	62		170	178	48.85	51.15
5	23	9	7	16	347	17.79	63		167	180	48.13	51.87
8	15	9	7	16	345	17.69	64		189	156	54.78	45.22
9	12	9	7	13	345	17.69	65		169	176	48.99	51.01
8	8	9	7	15	344	17.64	66		187	157	54.36	45.64
8	16	9	1	12	343	17.59	67		169	174	49.27	50.73
8	30	9	1	13	343	17.59	68		176	167	51.31	48.69
8	15	9	7	14	342	17.54	69		147	195	42.98	57.02

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
9	13	9	1	17	342	17.54	70		182	160	53.22	46.78
5	23	9	7	12	340	17.44	71		145	195	42.65	57.35
8	8	9	7	13	340	17.44	72		131	209	38.53	61.47
5	23	9	7	13	339	17.38	73		127	212	37.46	62.54
8	30	9	1	15	339	17.38	74		147	192	43.36	56.64
8	15	9	7	12	337	17.28	75		140	197	41.54	58.46
9	13	9	1	14	337	17.28	76		160	177	47.48	52.52
9	26	9	7	13	337	17.28	77		180	157	53.41	46.59
8	8	9	7	16	335	17.18	78		170	165	50.75	49.25
8	30	9	1	14	335	17.18	79		168	167	50.15	49.85
8	16	9	1	18	334	17.13	80		225	109	67.37	32.63
9	27	9	1	12	334	17.13	81	1950	146	188	43.71	56.29
5	31	9	1	13	333	17.08	82		162	171	48.65	51.35
9	6	9	1	15	333	17.08	83		180	153	54.05	45.95
6	7	9	1	14	330	16.92	84		180	150	54.55	45.45
8	22	9	7	16	329	16.87	85		155	174	47.11	52.89
8	30	9	1	16	329	16.87	86		175	154	53.19	46.81
9	13	9	1	16	329	16.87	87		184	145	55.93	44.07
5	24	9	1	11	328	16.82	88		114	214	34.76	65.24
6	13	9	7	16	328	16.82	89		165	163	50.3	49.7
6	14	9	1	15	328	16.82	90		177	151	53.96	46.04
8	30	9	1	12	328	16.82	91		161	167	49.09	50.91
9	5	9	7	15	328	16.82	92		162	166	49.39	50.61
5	30	9	7	15	327	16.77	93		128	199	39.14	60.86
8	23	9	1	17	327	16.77	94		198	129	60.55	39.45
9	5	9	7	14	327	16.77	95		156	171	47.71	52.29
8	21	9	6	18	326	16.72	96		138	188	42.33	57.67
9	13	9	1	12	326	16.72	97		173	153	53.07	46.93
9	20	9	1	18	326	16.72	98		174	152	53.37	46.63
5	23	9	7	17	323	16.56	99		169	154	52.32	47.68
9	5	9	7	12	322	16.51	100		171	151	53.11	46.89
9	12	9	7	17	322	16.51	101	1950	167	155	51.86	48.14
8	8	9	7	18	321	16.46	102		178	143	55.45	44.55
9	5	9	7	13	320	16.41	103		149	171	46.56	53.44
5	31	9	1	15	319	16.36	104		149	170	46.71	53.29
8	22	9	7	14	319	16.36	105		143	176	44.83	55.17
9	26	9	7	15	319	16.36	106		134	185	42.01	57.99
8	7	9	6	17	318	16.31	107		135	183	42.45	57.55
8	8	9	7	17	318	16.31	108		165	153	51.89	48.11
5	22	9	6	17	317	16.26	109		92	225	29.02	70.98
8	15	9	7	13	317	16.26	110		135	182	42.59	57.41
8	15	9	7	15	317	16.26	111		147	170	46.37	53.63
5	31	9	1	16	316	16.21	112		167	149	52.85	47.15
9	4	9	6	19	316	16.21	113		99	217	31.33	68.67
9	12	9	7	12	316	16.21	114		133	183	42.09	57.91
9	6	9	1	16	315	16.15	115		176	139	55.87	44.13
8	9	9	1	11	312	16	116		135	177	43.27	56.73
9	4	9	6	17	311	15.95	117		104	207	33.44	66.56
9	6	9	1	12	311	15.95	118		151	160	48.55	51.45
5	24	9	1	18	308	15.79	119		202	106	65.58	34.42
9	7	9	2	17	308	15.79	120		150	158	48.7	51.3
5	22	9	6	18	306	15.69	121	1950	83	223	27.12	72.88

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	15	9	7	18	306	15.69	122		152	154	49.67	50.33
8	30	9	1	18	305	15.64	123		148	157	48.52	51.48
9	4	9	6	18	305	15.64	124		105	200	34.43	65.57
8	22	9	7	12	304	15.59	125		133	171	43.75	56.25
5	23	9	7	18	303	15.54	126		172	131	56.77	43.23
5	25	9	2	18	302	15.49	127		164	138	54.3	45.7
9	13	9	1	11	302	15.49	128		139	163	46.03	53.97
8	8	9	7	12	301	15.44	129		132	169	43.85	56.15
8	28	9	6	18	301	15.44	130		105	196	34.88	65.12
8	7	9	6	15	300	15.38	131		135	165	45	55
8	22	9	7	13	300	15.38	132		126	174	42	58
9	11	9	6	17	300	15.38	133		112	188	37.33	62.67
10	25	9	1	15	300	15.38	134		163	137	54.33	45.67
5	22	9	6	19	299	15.33	135		86	213	28.76	71.24
8	7	9	6	16	299	15.33	136		126	173	42.14	57.86
8	22	9	7	17	299	15.33	137		157	142	52.51	47.49
9	7	9	2	18	299	15.33	138		165	134	55.18	44.82
11	1	9	1	15	298	15.28	139		146	152	48.99	51.01
9	5	9	7	17	297	15.23	140		91	206	30.64	69.36
9	26	9	7	14	297	15.23	141	1950	124	173	41.75	58.25
8	8	9	7	11	296	15.18	142		124	172	41.89	58.11
8	14	9	6	18	296	15.18	143		91	205	30.74	69.26
6	12	9	6	17	295	15.13	144		132	163	44.75	55.25
9	12	9	7	18	295	15.13	145		172	123	58.31	41.69
9	19	9	7	15	295	15.13	146		142	153	48.14	51.86
5	23	9	7	11	294	15.08	147		111	183	37.76	62.24
5	30	9	7	16	294	15.08	148		161	133	54.76	45.24
9	20	9	1	11	293	15.03	149		134	159	45.73	54.27
10	4	9	1	16	292	14.97	150		135	157	46.23	53.77
10	10	9	7	16	292	14.97	151		130	162	44.52	55.48
8	21	9	6	15	291	14.92	152		143	148	49.14	50.86
8	14	9	6	16	290	14.87	153		113	177	38.97	61.03
8	29	9	7	12	290	14.87	154		131	159	45.17	54.83
5	22	9	6	16	289	14.82	155		100	189	34.6	65.4
5	30	9	7	14	289	14.82	156		141	148	48.79	51.21
9	18	9	6	18	289	14.82	157		90	199	31.14	68.86
11	1	9	1	14	289	14.82	158		147	142	50.87	49.13
5	31	9	1	12	286	14.67	159		132	154	46.15	53.85
9	5	9	7	11	286	14.67	160		147	139	51.4	48.6
9	18	9	6	17	286	14.67	161	1950	110	176	38.46	61.54
9	19	9	7	17	286	14.67	162		146	140	51.05	48.95
9	4	9	6	15	283	14.51	163		153	130	54.06	45.94
9	12	9	7	14	283	14.51	164		122	161	43.11	56.89
6	13	9	7	13	282	14.46	165		139	143	49.29	50.71
8	22	9	7	18	282	14.46	166		166	116	58.87	41.13
8	22	9	7	11	280	14.36	167		112	168	40	60
8	29	9	7	17	279	14.31	168		123	156	44.09	55.91
9	11	9	6	16	279	14.31	169		118	161	42.29	57.71
9	25	9	6	18	279	14.31	170		94	185	33.69	66.31
8	28	9	6	17	278	14.26	171		115	163	41.37	58.63
9	27	9	1	18	278	14.26	172		154	124	55.4	44.6
10	4	9	1	13	278	14.26	173		133	145	47.84	52.16

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
6	13	9	7	14	277	14.21	174		117	160	42.24	57.76
9	5	9	7	16	277	14.21	175		148	129	53.43	46.57
9	19	9	7	14	277	14.21	176		139	138	50.18	49.82
6	14	9	1	16	276	14.15	177		146	130	52.9	47.1
8	22	9	7	15	276	14.15	178		144	132	52.17	47.83
8	23	9	1	11	275	14.1	179		127	148	46.18	53.82
9	26	9	7	18	275	14.1	180		153	122	55.64	44.36
8	14	9	6	15	274	14.05	181	1950	136	138	49.64	50.36
8	29	9	7	15	274	14.05	182		120	154	43.8	56.2
9	7	9	2	11	274	14.05	183		130	144	47.45	52.55
9	11	9	6	18	274	14.05	184		91	183	33.21	66.79
9	26	9	7	12	274	14.05	185		118	156	43.07	56.93
8	21	9	6	17	273	14	186		109	164	39.93	60.07
10	4	9	1	14	273	14	187		109	164	39.93	60.07
6	6	9	7	16	272	13.95	188		126	146	46.32	53.68
6	7	9	1	12	272	13.95	189		151	121	55.51	44.49
8	7	9	6	18	272	13.95	190		96	176	35.29	64.71
8	8	9	7	19	272	13.95	191		140	132	51.47	48.53
8	15	9	7	11	272	13.95	192		127	145	46.69	53.31
8	23	9	1	18	272	13.95	193		177	95	65.07	34.93
9	11	9	6	19	272	13.95	194		98	174	36.03	63.97
9	18	9	6	16	272	13.95	195		113	159	41.54	58.46
9	19	9	7	13	272	13.95	196		119	153	43.75	56.25
9	26	9	7	17	272	13.95	197		139	133	51.1	48.9
9	6	9	1	17	271	13.9	198		137	134	50.55	49.45
9	27	9	1	11	271	13.9	199		110	161	40.59	59.41
9	25	9	6	17	270	13.85	200		83	187	30.74	69.26

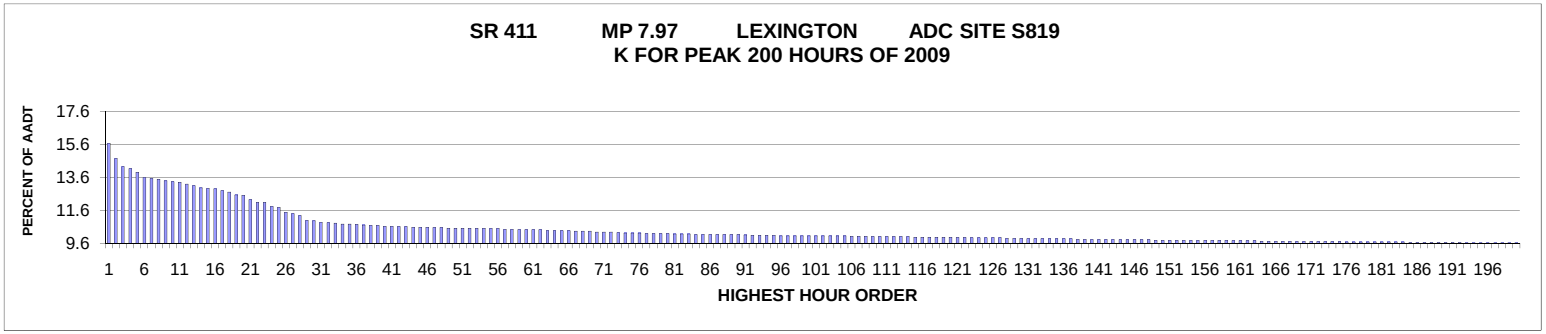

AADT= 3651 **K 30 FACTOR=** 10.96 **K 100 FACTOR=** 10.05 **K 200 FACTOR=** 9.61 **D FACTOR=** 62.86

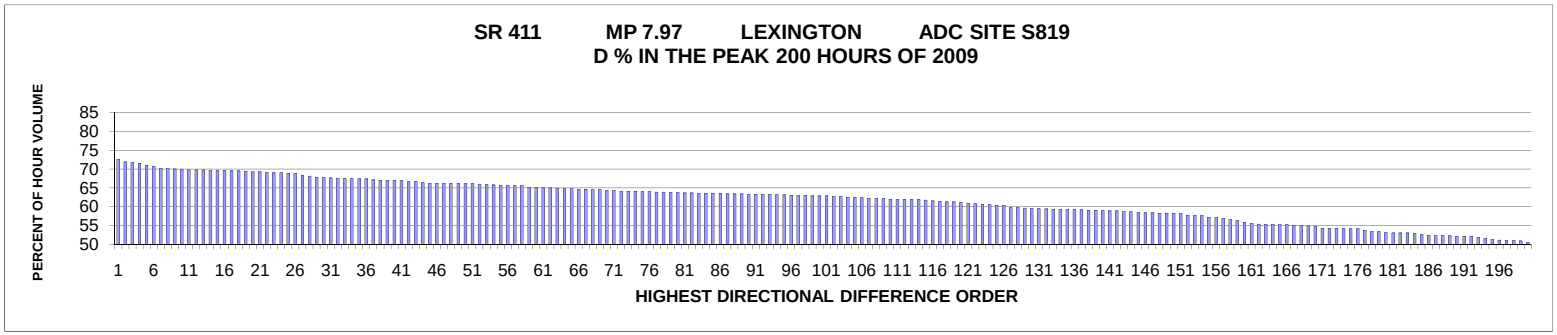

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	7	9	6	16	572	15.67	1	3651	415	157	72.55	27.45
2	28	9	7	11	539	14.76	2		212	327	39.33	60.67
2	28	9	7	14	520	14.24	3		255	265	49.04	50.96
2	28	9	7	12	516	14.13	4		232	284	44.96	55.04
2	28	9	7	10	508	13.91	5		202	306	39.76	60.24
8	7	9	6	15	496	13.59	6		342	154	68.95	31.05
2	28	9	7	17	494	13.53	7		271	223	54.86	45.14
2	21	9	7	16	492	13.48	8		266	226	54.07	45.93
2	28	9	7	15	489	13.39	9		270	219	55.21	44.79
2	28	9	7	9	487	13.34	10		233	254	47.84	52.16
2	28	9	7	18	486	13.31	11		289	197	59.47	40.53
2	21	9	7	18	482	13.2	12		264	218	54.77	45.23
2	21	9	7	13	478	13.09	13		214	264	44.77	55.23
7	24	9	6	17	473	12.96	14		332	141	70.19	29.81
2	21	9	7	17	472	12.93	15		246	226	52.12	47.88
2	28	9	7	19	471	12.9	16		253	218	53.72	46.28
2	28	9	7	13	467	12.79	17		218	249	46.68	53.32

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
2	28	9	7	8	464	12.71	18		251	213	54.09	45.91
2	28	9	7	16	458	12.54	19		234	224	51.09	48.91
2	28	9	7	20	457	12.52	20		240	217	52.52	47.48
2	21	9	7	15	447	12.24	21	3651	248	199	55.48	44.52
2	21	9	7	12	441	12.08	22		202	239	45.8	54.2
2	21	9	7	14	441	12.08	23		239	202	54.2	45.8
8	7	9	6	17	432	11.83	24		309	123	71.53	28.47
2	21	9	7	11	430	11.78	25		188	242	43.72	56.28
10	15	9	5	17	419	11.48	26		271	148	64.68	35.32
7	24	9	6	16	416	11.39	27		288	128	69.23	30.77
2	21	9	7	19	411	11.26	28		223	188	54.26	45.74
6	12	9	6	17	401	10.98	29		255	146	63.59	36.41
2	21	9	7	10	400	10.96	30		202	198	50.5	49.5
10	28	9	4	17	397	10.87	31		245	152	61.71	38.29
8	14	9	6	13	396	10.85	32		233	163	58.84	41.16
8	14	9	6	16	395	10.82	33		233	162	58.99	41.01
5	15	9	6	17	393	10.76	34		252	141	64.12	35.88
11	4	9	4	17	393	10.76	35		260	133	66.16	33.84
10	2	9	6	17	392	10.74	36		265	127	67.6	32.4
10	5	9	2	17	391	10.71	37		250	141	63.94	36.06
3	7	9	7	13	390	10.68	38		202	188	51.79	48.21
7	31	9	6	16	390	10.68	39		227	163	58.21	41.79
10	1	9	5	18	388	10.63	40		256	132	65.98	34.02
10	9	9	6	18	388	10.63	41	3651	247	141	63.66	36.34
10	9	9	6	16	387	10.6	42		226	161	58.4	41.6
10	27	9	3	17	387	10.6	43		266	121	68.73	31.27
7	24	9	6	18	386	10.57	44		258	128	66.84	33.16
9	11	9	6	17	386	10.57	45		236	150	61.14	38.86
9	18	9	6	17	386	10.57	46		234	152	60.62	39.38
9	2	9	4	17	385	10.55	47		267	118	69.35	30.65
9	18	9	6	18	385	10.55	48		245	140	63.64	36.36
6	5	9	6	17	384	10.52	49		238	146	61.98	38.02
8	11	9	3	17	384	10.52	50		244	140	63.54	36.46
8	14	9	6	15	384	10.52	51		219	165	57.03	42.97
8	26	9	4	17	384	10.52	52		252	132	65.63	34.38
9	21	9	2	18	384	10.52	53		267	117	69.53	30.47
10	6	9	3	18	384	10.52	54		276	108	71.88	28.13
4	6	9	2	17	383	10.49	55		223	160	58.22	41.78
10	8	9	5	17	383	10.49	56		253	130	66.06	33.94
9	22	9	3	18	381	10.44	57		252	129	66.14	33.86
10	7	9	4	17	381	10.44	58		240	141	62.99	37.01
4	30	9	5	18	380	10.41	59		252	128	66.32	33.68
5	21	9	5	18	380	10.41	60		249	131	65.53	34.47
6	26	9	6	17	380	10.41	61	3651	253	127	66.58	33.42
8	17	9	2	18	380	10.41	62		251	129	66.05	33.95
8	19	9	4	18	378	10.35	63		240	138	63.49	36.51
8	21	9	6	16	378	10.35	64		253	125	66.93	33.07
10	6	9	3	17	378	10.35	65		234	144	61.9	38.1
10	20	9	3	17	378	10.35	66		234	144	61.9	38.1
7	16	9	5	17	377	10.33	67		237	140	62.86	37.14
9	4	9	6	17	377	10.33	68		222	155	58.89	41.11
9	14	9	2	17	377	10.33	69		237	140	62.86	37.14

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
4	10	9	6	17	375	10.27	70		237	138	63.2	36.8
5	1	9	6	17	375	10.27	71		222	153	59.2	40.8
9	1	9	3	17	375	10.27	72		253	122	67.47	32.53
5	29	9	6	17	374	10.24	73		216	158	57.75	42.25
4	21	9	3	17	373	10.22	74		237	136	63.54	36.46
5	28	9	5	17	373	10.22	75		221	152	59.25	40.75
9	19	9	7	14	373	10.22	76		174	199	46.65	53.35
4	29	9	4	17	372	10.19	77		206	166	55.38	44.62
5	1	9	6	18	372	10.19	78		251	121	67.47	32.53
8	14	9	6	17	372	10.19	79		238	134	63.98	36.02
10	29	9	5	17	372	10.19	80		231	141	62.1	37.9
4	22	9	4	18	371	10.16	81	3651	249	122	67.12	32.88
4	23	9	5	18	371	10.16	82		227	144	61.19	38.81
6	19	9	6	17	371	10.16	83		235	136	63.34	36.66
6	11	9	5	18	370	10.13	84		259	111	70	30
8	5	9	4	18	370	10.13	85		257	113	69.46	30.54
8	14	9	6	18	370	10.13	86		232	138	62.7	37.3
8	31	9	2	17	370	10.13	87		252	118	68.11	31.89
9	21	9	2	17	370	10.13	88		238	132	64.32	35.68
10	1	9	5	17	370	10.13	89		230	140	62.16	37.84
11	6	9	6	17	370	10.13	90		234	136	63.24	36.76
9	22	9	3	17	369	10.11	91		226	143	61.25	38.75
4	17	9	6	18	368	10.08	92		245	123	66.58	33.42
7	22	9	4	18	368	10.08	93		254	114	69.02	30.98
9	10	9	5	17	368	10.08	94		236	132	64.13	35.87
9	29	9	3	17	368	10.08	95		239	129	64.95	35.05
2	28	9	7	21	367	10.05	96		188	179	51.23	48.77
5	18	9	2	17	367	10.05	97		225	142	61.31	38.69
6	12	9	6	18	367	10.05	98		232	135	63.22	36.78
8	4	9	3	17	367	10.05	99		238	129	64.85	35.15
9	4	9	6	16	367	10.05	100		214	153	58.31	41.69
9	24	9	5	16	367	10.05	101	3651	217	150	59.13	40.87
9	24	9	5	18	367	10.05	102		254	113	69.21	30.79
10	2	9	6	15	367	10.05	103		191	176	52.04	47.96
10	7	9	4	16	367	10.05	104		192	175	52.32	47.68
10	13	9	3	16	367	10.05	105		227	140	61.85	38.15
5	18	9	2	18	366	10.02	106		218	148	59.56	40.44
5	22	9	6	16	366	10.02	107		217	149	59.29	40.71
10	12	9	2	18	366	10.02	108		250	116	68.31	31.69
2	20	9	6	17	365	10	109		220	145	60.27	39.73
5	27	9	4	17	365	10	110		217	148	59.45	40.55
6	4	9	5	17	365	10	111		228	137	62.47	37.53
8	3	9	2	17	365	10	112		240	125	65.75	34.25
8	7	9	6	18	365	10	113		254	111	69.59	30.41
8	28	9	6	16	365	10	114		213	152	58.36	41.64
1	30	9	6	16	364	9.97	115		207	157	56.87	43.13
6	5	9	6	16	364	9.97	116		232	132	63.74	36.26
8	27	9	5	18	364	9.97	117		261	103	71.7	28.3
9	23	9	4	17	364	9.97	118		234	130	64.29	35.71
10	16	9	6	17	364	9.97	119		229	135	62.91	37.09
12	4	9	6	16	364	9.97	120		227	137	62.36	37.64
4	17	9	6	17	363	9.94	121	3651	234	129	64.46	35.54

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
5	7	9	5	18	363	9.94	122		253	110	69.7	30.3
3	6	9	6	17	362	9.92	123		212	150	58.56	41.44
5	22	9	6	17	362	9.92	124		209	153	57.73	42.27
7	16	9	5	16	362	9.92	125		191	171	52.76	47.24
9	16	9	4	16	362	9.92	126		219	143	60.5	39.5
9	26	9	7	13	362	9.92	127		178	184	49.17	50.83
4	16	9	5	18	361	9.89	128		243	118	67.31	32.69
4	27	9	2	18	361	9.89	129		256	105	70.91	29.09
9	15	9	3	18	361	9.89	130		251	110	69.53	30.47
5	29	9	6	16	360	9.86	131		198	162	55	45
7	10	9	6	17	360	9.86	132		215	145	59.72	40.28
7	16	9	5	18	360	9.86	133		241	119	66.94	33.06
8	10	9	2	17	360	9.86	134		238	122	66.11	33.89
10	9	9	6	17	360	9.86	135		230	130	63.89	36.11
10	10	9	7	12	360	9.86	136		161	199	44.72	55.28
12	3	9	5	17	360	9.86	137		244	116	67.78	32.22
4	20	9	2	18	359	9.83	138		243	116	67.69	32.31
6	9	9	3	18	359	9.83	139		242	117	67.41	32.59
3	7	9	7	14	358	9.81	140		168	190	46.93	53.07
3	13	9	6	18	358	9.81	141	3651	225	133	62.85	37.15
4	7	9	3	17	358	9.81	142		220	138	61.45	38.55
6	15	9	2	16	358	9.81	143		218	140	60.89	39.11
6	16	9	3	17	358	9.81	144		240	118	67.04	32.96
9	26	9	7	14	358	9.81	145		148	210	41.34	58.66
10	8	9	5	16	358	9.81	146		208	150	58.1	41.9
10	15	9	5	18	358	9.81	147		250	108	69.83	30.17
11	3	9	3	17	358	9.81	148		241	117	67.32	32.68
3	13	9	6	17	357	9.78	149		236	121	66.11	33.89
5	16	9	7	15	357	9.78	150		189	168	52.94	47.06
5	27	9	4	18	357	9.78	151		235	122	65.83	34.17
8	1	9	7	14	357	9.78	152		175	182	49.02	50.98
8	21	9	6	17	357	9.78	153		213	144	59.66	40.34
8	25	9	3	18	357	9.78	154		249	108	69.75	30.25
9	9	9	4	17	357	9.78	155		226	131	63.31	36.69
9	15	9	3	17	357	9.78	156		210	147	58.82	41.18
9	28	9	2	16	357	9.78	157		199	158	55.74	44.26
10	7	9	4	18	357	9.78	158		248	109	69.47	30.53
10	21	9	4	17	357	9.78	159		230	127	64.43	35.57
4	10	9	6	16	356	9.75	160		210	146	58.99	41.01
4	20	9	2	17	356	9.75	161	3651	232	124	65.17	34.83
6	9	9	3	17	356	9.75	162		230	126	64.61	35.39
8	26	9	4	15	356	9.75	163		186	170	52.25	47.75
4	24	9	6	17	355	9.72	164		196	159	55.21	44.79
7	17	9	6	18	355	9.72	165		210	145	59.15	40.85
8	28	9	6	15	355	9.72	166		186	169	52.39	47.61
10	23	9	6	17	355	9.72	167		224	131	63.1	36.9
12	15	9	3	17	355	9.72	168		225	130	63.38	36.62
4	27	9	2	17	354	9.7	169		230	124	64.97	35.03
6	5	9	6	18	354	9.7	170		226	128	63.84	36.16
6	30	9	3	17	354	9.7	171		220	134	62.15	37.85
7	31	9	6	17	354	9.7	172		224	130	63.28	36.72
9	3	9	5	17	354	9.7	173		227	127	64.12	35.88

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
9	17	9	5	17	354	9.7	174		229	125	64.69	35.31
10	30	9	6	16	354	9.7	175		210	144	59.32	40.68
4	21	9	3	16	353	9.67	176		187	166	52.97	47.03
5	20	9	4	17	353	9.67	177		228	125	64.59	35.41
6	11	9	5	17	353	9.67	178		246	107	69.69	30.31
7	24	9	6	15	353	9.67	179		182	171	51.56	48.44
8	13	9	5	17	353	9.67	180		223	130	63.17	36.83
8	20	9	5	15	353	9.67	181	3651	191	162	54.11	45.89
9	2	9	4	18	353	9.67	182		243	110	68.84	31.16
10	9	9	6	15	353	9.67	183		184	169	52.12	47.88
10	30	9	6	17	353	9.67	184		222	131	62.89	37.11
5	15	9	6	16	352	9.64	185		205	147	58.24	41.76
6	9	9	3	16	352	9.64	186		201	151	57.1	42.9
8	17	9	2	17	352	9.64	187		233	119	66.19	33.81
8	24	9	2	18	352	9.64	188		231	121	65.63	34.38
9	16	9	4	17	352	9.64	189		218	134	61.93	38.07
10	16	9	6	16	352	9.64	190		199	153	56.53	43.47
11	2	9	2	17	352	9.64	191		229	123	65.06	34.94
12	2	9	4	17	352	9.64	192		221	131	62.78	37.22
2	27	9	6	17	351	9.61	193		219	132	62.39	37.61
4	15	9	4	17	351	9.61	194		223	128	63.53	36.47
6	18	9	5	18	351	9.61	195		246	105	70.09	29.91
7	25	9	7	16	351	9.61	196		165	186	47.01	52.99
8	10	9	2	18	351	9.61	197		248	103	70.66	29.34
8	21	9	6	18	351	9.61	198		230	121	65.53	34.47
9	1	9	3	18	351	9.61	199		242	109	68.95	31.05
9	18	9	6	16	351	9.61	200		202	149	57.55	42.45

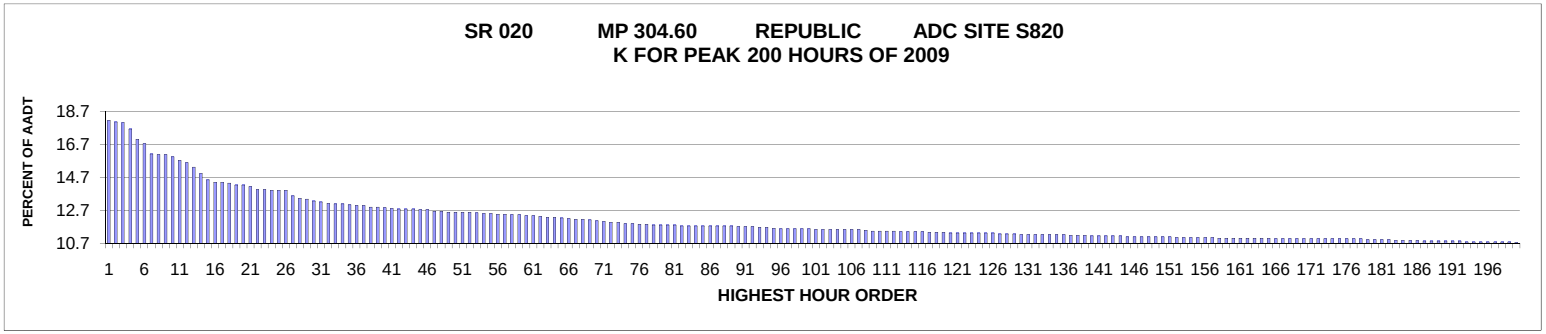

AADT= 2263 **K 30 FACTOR=** 13.26 **K 100 FACTOR=** 11.58 **K 200 FACTOR=** 10.74 **D FACTOR=** 53.94

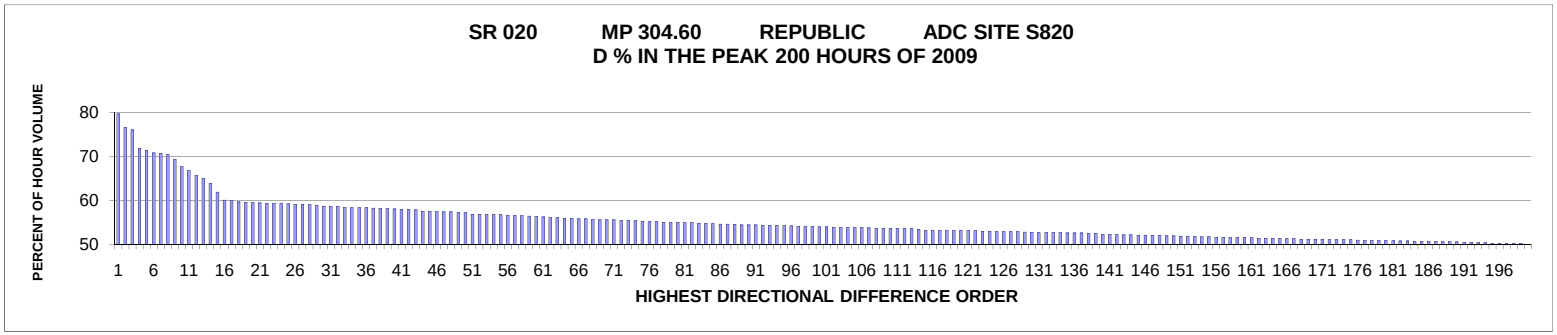

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
9	5	9	7	13	411	18.16	1	2263	224	187	54.5	45.5
9	5	9	7	18	409	18.07	2		140	269	34.23	65.77
9	5	9	7	12	408	18.03	3		242	166	59.31	40.69
9	4	9	6	15	399	17.63	4		197	202	49.37	50.63
9	4	9	6	17	385	17.01	5		207	178	53.77	46.23
9	4	9	6	14	379	16.75	6		193	186	50.92	49.08
9	4	9	6	13	365	16.13	7		194	171	53.15	46.85
9	4	9	6	12	364	16.08	8		205	159	56.32	43.68
9	5	9	7	11	364	16.08	9		199	165	54.67	45.33
9	5	9	7	17	361	15.95	10		151	210	41.83	58.17
9	2	9	4	17	356	15.73	11		189	167	53.09	46.91
9	4	9	6	16	353	15.6	12		203	150	57.51	42.49
9	5	9	7	15	347	15.33	13		208	139	59.94	40.06
9	6	9	1	18	338	14.94	14		100	238	29.59	70.41
9	6	9	1	13	329	14.54	15		186	143	56.53	43.47
6	13	9	7	15	326	14.41	16		218	108	66.87	33.13
9	4	9	6	11	326	14.41	17		190	136	58.28	41.72

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
9	4	9	6	19	325	14.36	18		133	192	40.92	59.08
9	2	9	4	13	322	14.23	19		175	147	54.35	45.65
9	4	9	6	18	322	14.23	20		180	142	55.9	44.1
9	6	9	1	19	320	14.14	21	2263	90	230	28.13	71.88
9	5	9	7	16	316	13.96	22		187	129	59.18	40.82
10	16	9	6	17	316	13.96	23		188	128	59.49	40.51
9	2	9	4	18	315	13.92	24		175	140	55.56	44.44
9	3	9	5	17	315	13.92	25		168	147	53.33	46.67
10	16	9	6	13	315	13.92	26		173	142	54.92	45.08
9	5	9	7	14	307	13.57	27		159	148	51.79	48.21
5	22	9	6	17	304	13.43	28		165	139	54.28	45.72
9	2	9	4	15	303	13.39	29		171	132	56.44	43.56
9	2	9	4	12	300	13.26	30		153	147	51	49
7	14	9	3	13	299	13.21	31		164	135	54.85	45.15
9	6	9	1	14	297	13.12	32		163	134	54.88	45.12
9	3	9	5	14	296	13.08	33		146	150	49.32	50.68
10	9	9	6	15	296	13.08	34		131	165	44.26	55.74
9	4	9	6	10	295	13.04	35		161	134	54.58	45.42
6	13	9	7	11	294	12.99	36		86	208	29.25	70.75
6	13	9	7	14	294	12.99	37		210	84	71.43	28.57
6	13	9	7	16	292	12.9	38		174	118	59.59	40.41
9	6	9	1	12	292	12.9	39		170	122	58.22	41.78
10	9	9	6	14	291	12.86	40		102	189	35.05	64.95
9	3	9	5	16	290	12.81	41	2263	170	120	58.62	41.38
5	22	9	6	15	289	12.77	42		133	156	46.02	53.98
9	5	9	7	19	289	12.77	43		130	159	44.98	55.02
10	9	9	6	16	289	12.77	44		129	160	44.64	55.36
9	2	9	4	14	288	12.73	45		142	146	49.31	50.69
9	3	9	5	13	288	12.73	46		163	125	56.6	43.4
9	1	9	3	17	286	12.64	47		148	138	51.75	48.25
9	3	9	5	11	286	12.64	48		145	141	50.7	49.3
9	1	9	3	15	285	12.59	49		163	122	57.19	42.81
9	3	9	5	12	285	12.59	50		145	140	50.88	49.12
9	3	9	5	15	285	12.59	51		162	123	56.84	43.16
10	15	9	5	16	285	12.59	52		145	140	50.88	49.12
8	31	9	2	15	284	12.55	53		157	127	55.28	44.72
6	13	9	7	12	283	12.51	54		83	200	29.33	70.67
8	22	9	7	13	283	12.51	55		124	159	43.82	56.18
7	27	9	2	17	282	12.46	56		152	130	53.9	46.1
10	16	9	6	14	282	12.46	57		153	129	54.26	45.74
5	27	9	4	17	281	12.42	58		149	132	53.02	46.98
9	6	9	1	11	281	12.42	59		139	142	49.47	50.53
8	7	9	6	13	280	12.37	60		131	149	46.79	53.21
10	16	9	6	16	280	12.37	61	2263	159	121	56.79	43.21
10	9	9	6	17	279	12.33	62		129	150	46.24	53.76
6	12	9	6	17	278	12.28	63		143	135	51.44	48.56
9	11	9	6	17	278	12.28	64		146	132	52.52	47.48
6	12	9	6	13	277	12.24	65		138	139	49.82	50.18
10	9	9	6	13	276	12.2	66		125	151	45.29	54.71
9	3	9	5	18	275	12.15	67		143	132	52	48
9	11	9	6	16	275	12.15	68		163	112	59.27	40.73
6	13	9	7	17	274	12.11	69		175	99	63.87	36.13

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
10	16	9	6	15	273	12.06	70		162	111	59.34	40.66
8	3	9	2	13	272	12.02	71		151	121	55.51	44.49
9	11	9	6	15	271	11.98	72		157	114	57.93	42.07
10	15	9	5	17	271	11.98	73		146	125	53.87	46.13
10	8	9	5	17	269	11.89	74		143	126	53.16	46.84
10	19	9	2	12	269	11.89	75		120	149	44.61	55.39
7	9	9	5	16	268	11.84	76		140	128	52.24	47.76
8	28	9	6	13	268	11.84	77		142	126	52.99	47.01
7	23	9	5	17	267	11.8	78		138	129	51.69	48.31
9	2	9	4	16	267	11.8	79		147	120	55.06	44.94
9	17	9	5	17	267	11.8	80		143	124	53.56	46.44
9	18	9	6	15	267	11.8	81	2263	139	128	52.06	47.94
5	22	9	6	16	266	11.75	82		128	138	48.12	51.88
5	24	9	1	13	266	11.75	83		155	111	58.27	41.73
7	17	9	6	13	266	11.75	84		117	149	43.98	56.02
7	20	9	2	13	266	11.75	85		129	137	48.5	51.5
7	31	9	6	13	266	11.75	86		136	130	51.13	48.87
8	7	9	6	17	266	11.75	87		130	136	48.87	51.13
8	31	9	2	13	266	11.75	88		151	115	56.77	43.23
9	8	9	3	13	266	11.75	89		139	127	52.26	47.74
6	8	9	2	17	265	11.71	90		142	123	53.58	46.42
6	13	9	7	10	265	11.71	91		101	164	38.11	61.89
7	14	9	3	17	265	11.71	92		138	127	52.08	47.92
6	12	9	6	12	264	11.67	93		127	137	48.11	51.89
9	6	9	1	17	264	11.67	94		108	156	40.91	59.09
10	19	9	2	11	263	11.62	95		127	136	48.29	51.71
6	11	9	5	17	262	11.58	96		148	114	56.49	43.51
8	13	9	5	14	262	11.58	97		132	130	50.38	49.62
9	25	9	6	13	262	11.58	98		141	121	53.82	46.18
9	25	9	6	16	262	11.58	99		143	119	54.58	45.42
10	19	9	2	14	262	11.58	100		124	138	47.33	52.67
6	13	9	7	18	261	11.53	101	2263	181	80	69.35	30.65
6	14	9	1	12	261	11.53	102		143	118	54.79	45.21
8	6	9	5	17	261	11.53	103		137	124	52.49	47.51
8	17	9	2	18	261	11.53	104		138	123	52.87	47.13
9	11	9	6	13	261	11.53	105		129	132	49.43	50.57
9	25	9	6	15	261	11.53	106		154	107	59	41
10	11	9	1	14	261	11.53	107		208	53	79.69	20.31
8	19	9	4	17	260	11.49	108		141	119	54.23	45.77
6	2	9	3	17	259	11.44	109		133	126	51.35	48.65
8	4	9	3	13	259	11.44	110		123	136	47.49	52.51
8	7	9	6	14	259	11.44	111		140	119	54.05	45.95
9	7	9	2	12	259	11.44	112		123	136	47.49	52.51
5	1	9	6	17	258	11.4	113		138	120	53.49	46.51
5	8	9	6	17	258	11.4	114		134	124	51.94	48.06
6	12	9	6	14	258	11.4	115		133	125	51.55	48.45
7	9	9	5	13	258	11.4	116		125	133	48.45	51.55
5	23	9	7	14	257	11.36	117		142	115	55.25	44.75
6	5	9	6	17	257	11.36	118		134	123	52.14	47.86
8	12	9	4	13	257	11.36	119		111	146	43.19	56.81
7	10	9	6	16	256	11.31	120		148	108	57.81	42.19
7	10	9	6	17	256	11.31	121	2263	152	104	59.38	40.63

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	20	9	5	16	256	11.31	122		143	113	55.86	44.14
8	27	9	5	17	256	11.31	123		141	115	55.08	44.92
9	1	9	3	14	256	11.31	124		131	125	51.17	48.83
9	1	9	3	18	256	11.31	125		139	117	54.3	45.7
10	20	9	3	16	256	11.31	126		135	121	52.73	47.27
8	25	9	3	13	255	11.27	127		142	113	55.69	44.31
8	31	9	2	17	255	11.27	128		148	107	58.04	41.96
9	12	9	7	14	255	11.27	129		117	138	45.88	54.12
6	11	9	5	18	254	11.22	130		106	148	41.73	58.27
8	3	9	2	14	254	11.22	131		137	117	53.94	46.06
8	5	9	4	17	254	11.22	132		135	119	53.15	46.85
10	7	9	4	17	254	11.22	133		123	131	48.43	51.57
10	9	9	6	18	254	11.22	134		108	146	42.52	57.48
10	16	9	6	18	254	11.22	135		144	110	56.69	43.31
10	18	9	1	13	254	11.22	136		124	130	48.82	51.18
5	22	9	6	18	253	11.18	137		134	119	52.96	47.04
6	14	9	1	11	253	11.18	138		141	112	55.73	44.27
7	27	9	2	13	253	11.18	139		136	117	53.75	46.25
5	24	9	1	15	252	11.14	140		135	117	53.57	46.43
5	29	9	6	15	252	11.14	141	2263	146	106	57.94	42.06
8	22	9	7	11	252	11.14	142		102	150	40.48	59.52
8	28	9	6	15	252	11.14	143		137	115	54.37	45.63
10	11	9	1	15	252	11.14	144		193	59	76.59	23.41
5	26	9	3	15	251	11.09	145		147	104	58.57	41.43
7	10	9	6	13	251	11.09	146		138	113	54.98	45.02
8	7	9	6	12	251	11.09	147		126	125	50.2	49.8
8	10	9	2	12	251	11.09	148		128	123	51	49
8	12	9	4	14	251	11.09	149		144	107	57.37	42.63
10	2	9	6	15	251	11.09	150		127	124	50.6	49.4
10	21	9	4	13	251	11.09	151		131	120	52.19	47.81
6	6	9	7	13	250	11.05	152		81	169	32.4	67.6
7	23	9	5	15	250	11.05	153		128	122	51.2	48.8
8	14	9	6	17	250	11.05	154		146	104	58.4	41.6
9	1	9	3	12	250	11.05	155		123	127	49.2	50.8
9	9	9	4	17	250	11.05	156		136	114	54.4	45.6
9	18	9	6	14	250	11.05	157		118	132	47.2	52.8
5	22	9	6	14	249	11	158		118	131	47.39	52.61
7	13	9	2	14	249	11	159		128	121	51.41	48.59
7	22	9	4	17	249	11	160		131	118	52.61	47.39
7	23	9	5	18	249	11	161	2263	121	128	48.59	51.41
8	10	9	2	14	249	11	162		122	127	49	51
9	25	9	6	12	249	11	163		122	127	49	51
10	6	9	3	17	249	11	164		143	106	57.43	42.57
10	20	9	3	13	249	11	165		118	131	47.39	52.61
5	21	9	5	17	248	10.96	166		133	115	53.63	46.37
5	28	9	5	17	248	10.96	167		149	99	60.08	39.92
7	21	9	3	13	248	10.96	168		133	115	53.63	46.37
7	31	9	6	15	248	10.96	169		120	128	48.39	51.61
8	1	9	7	11	248	10.96	170		126	122	50.81	49.19
8	19	9	4	14	248	10.96	171		125	123	50.4	49.6
8	19	9	4	16	248	10.96	172		139	109	56.05	43.95
8	21	9	6	13	248	10.96	173		114	134	45.97	54.03

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
9	2	9	4	11	248	10.96	174		144	104	58.06	41.94
9	3	9	5	10	248	10.96	175		131	117	52.82	47.18
9	6	9	1	15	248	10.96	176		129	119	52.02	47.98
9	8	9	3	15	248	10.96	177		132	116	53.23	46.77
10	2	9	6	16	248	10.96	178		121	127	48.79	51.21
6	5	9	6	15	247	10.91	179		145	102	58.7	41.3
7	31	9	6	12	247	10.91	180		125	122	50.61	49.39
9	17	9	5	16	247	10.91	181	2263	130	117	52.63	47.37
9	18	9	6	17	247	10.91	182		124	123	50.2	49.8
8	5	9	4	13	246	10.87	183		127	119	51.63	48.37
8	6	9	5	16	246	10.87	184		130	116	52.85	47.15
10	11	9	1	13	246	10.87	185		187	59	76.02	23.98
10	16	9	6	12	246	10.87	186		141	105	57.32	42.68
7	31	9	6	16	245	10.83	187		123	122	50.2	49.8
8	4	9	3	17	245	10.83	188		124	121	50.61	49.39
9	10	9	5	16	245	10.83	189		144	101	58.78	41.22
9	11	9	6	14	245	10.83	190		136	109	55.51	44.49
10	1	9	5	15	245	10.83	191		140	105	57.14	42.86
10	21	9	4	11	245	10.83	192		115	130	46.94	53.06
5	1	9	6	15	244	10.78	193		131	113	53.69	46.31
5	23	9	7	15	244	10.78	194		122	122	50	50
6	9	9	3	16	244	10.78	195		119	125	48.77	51.23
6	12	9	6	15	244	10.78	196		121	123	49.59	50.41
7	20	9	2	17	244	10.78	197		128	116	52.46	47.54
8	3	9	2	12	244	10.78	198		123	121	50.41	49.59
10	19	9	2	13	244	10.78	199		124	120	50.82	49.18
5	29	9	6	17	243	10.74	200		121	122	49.79	50.21

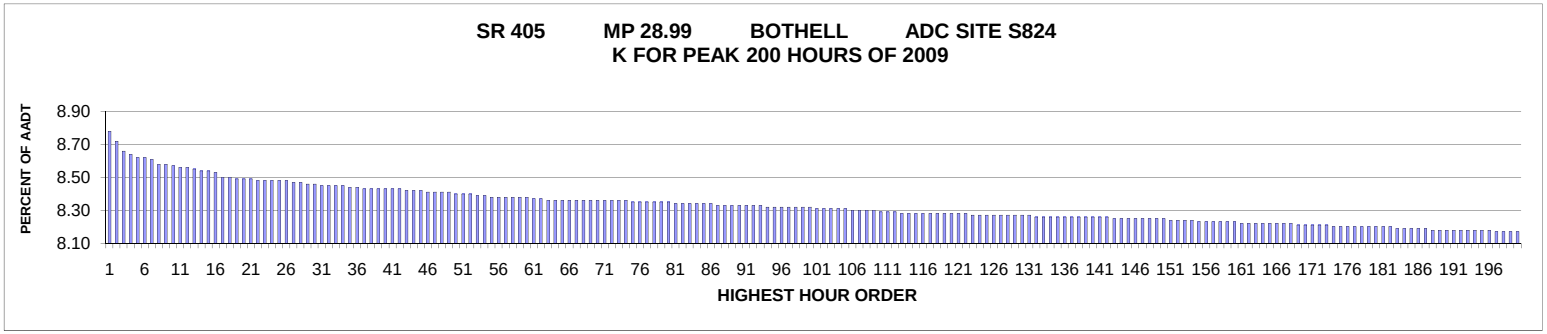

AADT= 111033 **K 30 FACTOR=** 8.46 **K 100 FACTOR=** 8.32 **K 200 FACTOR=** 8.17 **D FACTOR=** 52.09

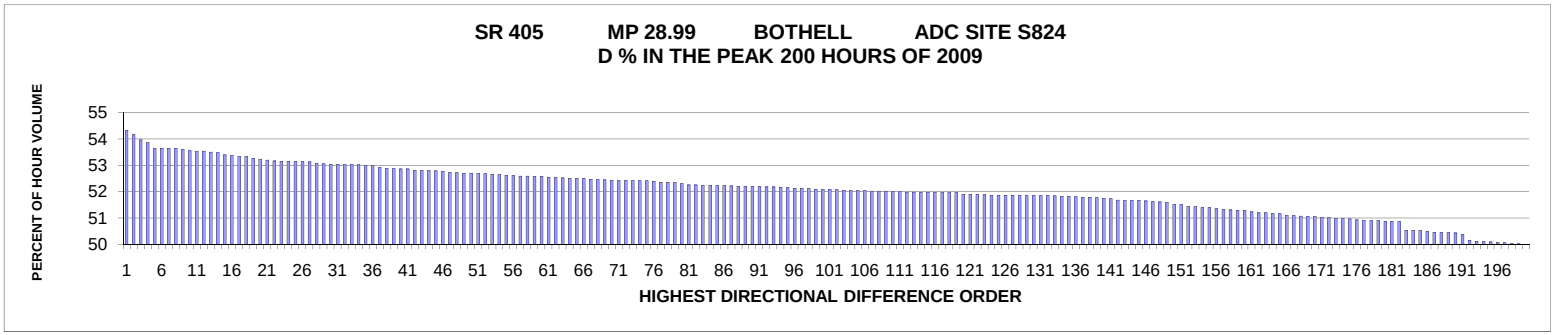

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
5	8	9	6	17	9748	8.78	1	111033	5065	4683	51.96	48.04
8	20	9	5	17	9682	8.72	2		5021	4661	51.86	48.14
7	16	9	5	17	9612	8.66	3		4985	4627	51.86	48.14
7	23	9	5	17	9591	8.64	4		4996	4595	52.09	47.91
6	5	9	6	17	9572	8.62	5		5045	4527	52.71	47.29
7	16	9	5	18	9569	8.62	6		5019	4550	52.45	47.55
10	23	9	6	16	9562	8.61	7		4938	4624	51.64	48.36
6	12	9	6	17	9527	8.58	8		5065	4462	53.16	46.84
5	14	9	5	17	9525	8.58	9		4930	4595	51.76	48.24
12	18	9	6	17	9510	8.57	10		4866	4644	51.17	48.83
7	9	9	5	17	9507	8.56	11		4992	4515	52.51	47.49
9	3	9	5	17	9506	8.56	12		4746	4760	49.93	50.07
5	15	9	6	17	9495	8.55	13		4871	4624	51.30	48.70
2	13	9	6	17	9484	8.54	14		5087	4397	53.64	46.36
8	12	9	4	17	9479	8.54	15		4949	4530	52.21	47.79
6	24	9	4	18	9468	8.53	16		4893	4575	51.68	48.32
7	15	9	4	17	9442	8.50	17		4984	4458	52.79	47.21

			DAY OF		HR	PERCENT OF	HOUR		NORTH	SOUTH	PERCENT NORTH IS OF TOTAL	PERCENT SOUTH IS OF TOTAL
8	24	9	2	17	9439	8.50	18		4896	4543	51.87	48.13
4	16	9	5	17	9431	8.49	19		4967	4464	52.67	47.33
7	14	9	3	18	9430	8.49	20		4819	4611	51.10	48.90
8	6	9	5	17	9429	8.49	21	111033	4888	4541	51.84	48.16
7	15	9	4	18	9420	8.48	22		4992	4428	52.99	47.01
7	17	9	6	18	9419	8.48	23		4829	4590	51.27	48.73
8	11	9	3	17	9418	8.48	24		4921	4497	52.25	47.75
7	10	9	6	17	9413	8.48	25		4830	4583	51.31	48.69
7	9	9	5	18	9412	8.48	26		4981	4431	52.92	47.08
7	7	9	3	17	9401	8.47	27		4988	4413	53.06	46.94
7	30	9	5	17	9399	8.47	28		4841	4558	51.51	48.49
8	13	9	5	18	9393	8.46	29		4698	4695	50.02	49.98
8	27	9	5	17	9392	8.46	30		4894	4498	52.11	47.89
6	12	9	6	16	9387	8.45	31		4914	4473	52.35	47.65
9	10	9	5	17	9387	8.45	32		4805	4582	51.19	48.81
10	8	9	5	17	9380	8.45	33		4858	4522	51.79	48.21
7	28	9	3	17	9378	8.45	34		4862	4516	51.84	48.16
5	21	9	5	18	9376	8.44	35		4897	4479	52.23	47.77
12	10	9	5	17	9370	8.44	36		4685	4685	50.00	50.00
11	20	9	6	17	9362	8.43	37		4870	4492	52.02	47.98
7	21	9	3	17	9360	8.43	38		4869	4491	52.02	47.98
6	9	9	3	17	9358	8.43	39		4946	4412	52.85	47.15
6	11	9	5	17	9358	8.43	40		4875	4483	52.09	47.91
4	10	9	6	17	9356	8.43	41	111033	4902	4454	52.39	47.61
12	23	9	4	16	9356	8.43	42		4775	4581	51.04	48.96
9	30	9	4	18	9352	8.42	43		4715	4637	50.42	49.58
7	7	9	3	18	9349	8.42	44		4859	4490	51.97	48.03
6	11	9	5	18	9348	8.42	45		4902	4446	52.44	47.56
9	1	9	3	17	9338	8.41	46		4876	4462	52.22	47.78
5	8	9	6	18	9337	8.41	47		4852	4485	51.97	48.03
7	13	9	2	18	9337	8.41	48		4963	4374	53.15	46.85
8	6	9	5	18	9337	8.41	49		4837	4500	51.80	48.20
4	17	9	6	17	9326	8.40	50		4833	4493	51.82	48.18
8	4	9	3	17	9324	8.40	51		4894	4430	52.49	47.51
8	21	9	6	16	9323	8.40	52		4835	4488	51.86	48.14
11	6	9	6	16	9316	8.39	53		4753	4563	51.02	48.98
6	17	9	4	18	9312	8.39	54		4972	4340	53.39	46.61
5	15	9	6	16	9306	8.38	55		4779	4527	51.35	48.65
6	23	9	3	17	9305	8.38	56		4836	4469	51.97	48.03
1	30	9	6	17	9302	8.38	57		4891	4411	52.58	47.42
9	18	9	6	16	9302	8.38	58		4658	4644	50.08	49.92
8	7	9	6	17	9301	8.38	59		4985	4316	53.60	46.40
12	23	9	4	15	9301	8.38	60		4761	4540	51.19	48.81
6	22	9	2	17	9294	8.37	61	111033	4904	4390	52.77	47.23
12	22	9	3	17	9294	8.37	62		4736	4558	50.96	49.04
6	17	9	4	17	9287	8.36	63		4827	4460	51.98	48.02
10	9	9	6	17	9287	8.36	64		4693	4594	50.53	49.47
5	12	9	3	17	9286	8.36	65		4982	4304	53.65	46.35
5	21	9	5	17	9285	8.36	66		4830	4455	52.02	47.98
6	24	9	4	17	9285	8.36	67		4893	4392	52.70	47.30
8	21	9	6	17	9285	8.36	68		4819	4466	51.90	48.10
9	17	9	5	17	9284	8.36	69		4774	4510	51.42	48.58
6	23	9	3	18	9282	8.36	70		4882	4400	52.60	47.40

			DAY OF		HR	PERCENT OF	HOUR		NORTH	SOUTH	PERCENT NORTH IS OF TOTAL	PERCENT SOUTH IS OF TOTAL
6	18	9	5	17	9281	8.36	71		4978	4303	53.64	46.36
6	15	9	2	17	9279	8.36	72		4864	4415	52.42	47.58
7	22	9	4	18	9279	8.36	73		4787	4492	51.59	48.41
3	26	9	5	17	9278	8.36	74		4916	4362	52.99	47.01
4	24	9	6	17	9276	8.35	75		4880	4396	52.61	47.39
5	27	9	4	17	9275	8.35	76		4881	4394	52.63	47.37
6	30	9	3	18	9275	8.35	77		4846	4429	52.25	47.75
7	23	9	5	18	9269	8.35	78		4828	4441	52.09	47.91
7	6	9	2	17	9268	8.35	79		4858	4410	52.42	47.58
7	24	9	6	17	9268	8.35	80		4803	4465	51.82	48.18
6	25	9	5	18	9265	8.34	81	111033	4718	4547	50.92	49.08
1	16	9	6	17	9263	8.34	82		4856	4407	52.42	47.58
8	14	9	6	16	9262	8.34	83		4819	4443	52.03	47.97
9	11	9	6	17	9262	8.34	84		4821	4441	52.05	47.95
3	6	9	6	17	9261	8.34	85		4870	4391	52.59	47.41
6	18	9	5	18	9257	8.34	86		4777	4480	51.60	48.40
8	14	9	6	17	9251	8.33	87		4832	4419	52.23	47.77
8	28	9	6	17	9247	8.33	88		4717	4530	51.01	48.99
6	16	9	3	18	9245	8.33	89		4826	4419	52.20	47.80
6	30	9	3	17	9245	8.33	90		4930	4315	53.33	46.67
8	18	9	3	17	9245	8.33	91		4793	4452	51.84	48.16
7	22	9	4	17	9244	8.33	92		4811	4433	52.04	47.96
8	11	9	3	18	9244	8.33	93		4793	4451	51.85	48.15
9	11	9	6	16	9243	8.32	94		4720	4523	51.07	48.93
8	5	9	4	17	9239	8.32	95		4802	4437	51.98	48.02
9	3	9	5	18	9239	8.32	96		4698	4541	50.85	49.15
7	8	9	4	18	9238	8.32	97		4899	4339	53.03	46.97
6	19	9	6	16	9236	8.32	98		4573	4663	49.51	50.49
10	30	9	6	17	9234	8.32	99		4868	4366	52.72	47.28
8	5	9	4	18	9233	8.32	100		4875	4358	52.80	47.20
6	10	9	4	17	9232	8.31	101	111033	4840	4392	52.43	47.57
4	21	9	3	17	9230	8.31	102		4849	4381	52.54	47.46
8	19	9	4	17	9229	8.31	103		4785	4444	51.85	48.15
9	25	9	6	17	9225	8.31	104		4813	4412	52.17	47.83
6	9	9	3	18	9224	8.31	105		4849	4375	52.57	47.43
2	6	9	6	17	9221	8.30	106		4995	4226	54.17	45.83
12	11	9	6	17	9219	8.30	107		4529	4690	49.13	50.87
10	15	9	5	17	9217	8.30	108		4736	4481	51.38	48.62
7	13	9	2	17	9216	8.30	109		4819	4397	52.29	47.71
12	18	9	6	16	9209	8.29	110		4695	4514	50.98	49.02
9	22	9	3	17	9205	8.29	111		4800	4405	52.15	47.85
4	9	9	5	17	9200	8.29	112		4822	4378	52.41	47.59
3	13	9	6	17	9199	8.28	113		4920	4279	53.48	46.52
5	22	9	6	17	9199	8.28	114		4772	4427	51.88	48.12
8	31	9	2	17	9196	8.28	115		4681	4515	50.90	49.10
7	24	9	6	16	9194	8.28	116		4874	4320	53.01	46.99
3	20	9	6	17	9192	8.28	117		4853	4339	52.80	47.20
11	12	9	5	17	9191	8.28	118		4748	4443	51.66	48.34
2	13	9	6	16	9190	8.28	119		4882	4308	53.12	46.88
9	18	9	6	17	9190	8.28	120		4679	4511	50.91	49.09
7	28	9	3	18	9188	8.28	121	111033	4725	4463	51.43	48.57
10	23	9	6	17	9188	8.28	122		4811	4377	52.36	47.64
2	27	9	6	18	9187	8.27	123		4918	4269	53.53	46.47

			DAY OF		HR	PERCENT OF	HOUR		NORTH	SOUTH	PERCENT NORTH IS OF TOTAL	PERCENT SOUTH IS OF TOTAL
8	12	9	4	18	9187	8.27	124		4773	4414	51.95	48.05
9	2	9	4	17	9186	8.27	125		4793	4393	52.18	47.82
9	4	9	6	17	9183	8.27	126		4729	4454	51.50	48.50
12	2	9	4	17	9183	8.27	127		4718	4465	51.38	48.62
7	8	9	4	17	9182	8.27	128		4869	4313	53.03	46.97
10	7	9	4	17	9180	8.27	129		4896	4284	53.33	46.67
7	1	9	4	17	9179	8.27	130		4823	4356	52.54	47.46
8	4	9	3	18	9179	8.27	131		4753	4426	51.78	48.22
9	16	9	4	17	9176	8.26	132		4783	4393	52.13	47.87
9	25	9	6	16	9174	8.26	133		4597	4577	50.11	49.89
9	24	9	5	17	9173	8.26	134		4744	4429	51.72	48.28
4	15	9	4	17	9172	8.26	135		4875	4297	53.15	46.85
5	20	9	4	18	9172	8.26	136		4834	4338	52.70	47.30
6	12	9	6	18	9172	8.26	137		4912	4260	53.55	46.45
3	12	9	5	17	9168	8.26	138		4908	4260	53.53	46.47
7	30	9	5	18	9168	8.26	139		4774	4394	52.07	47.93
10	2	9	6	18	9168	8.26	140		4585	4583	50.01	49.99
8	25	9	3	18	9167	8.26	141	111033	4754	4413	51.86	48.14
11	11	9	4	17	9167	8.26	142		4798	4369	52.34	47.66
4	23	9	5	17	9165	8.25	143		4826	4339	52.66	47.34
5	22	9	6	16	9165	8.25	144		4678	4487	51.04	48.96
9	9	9	4	17	9165	8.25	145		4809	4356	52.47	47.53
5	8	9	6	16	9162	8.25	146		4779	4383	52.16	47.84
8	7	9	6	16	9158	8.25	147		4932	4226	53.85	46.15
10	30	9	6	16	9158	8.25	148		4808	4350	52.50	47.50
10	22	9	5	17	9156	8.25	149		4761	4395	52.00	48.00
5	26	9	3	17	9155	8.25	150		4815	4340	52.59	47.41
1	23	9	6	17	9153	8.24	151		4884	4269	53.36	46.64
7	29	9	4	17	9148	8.24	152		4775	4373	52.20	47.80
7	27	9	2	17	9147	8.24	153		4851	4296	53.03	46.97
8	20	9	5	18	9146	8.24	154		4776	4370	52.22	47.78
8	25	9	3	17	9143	8.23	155		4677	4466	51.15	48.85
10	28	9	4	17	9142	8.23	156		4869	4273	53.26	46.74
12	17	9	5	17	9141	8.23	157		4619	4522	50.53	49.47
4	24	9	6	18	9139	8.23	158		4743	4396	51.90	48.10
11	25	9	4	15	9137	8.23	159		4409	4728	48.25	51.75
5	14	9	5	18	9136	8.23	160		4829	4307	52.86	47.14
3	13	9	6	18	9132	8.22	161	111033	4928	4204	53.96	46.04
9	18	9	6	18	9132	8.22	162		4607	4525	50.45	49.55
4	16	9	5	18	9129	8.22	163		4841	4288	53.03	46.97
12	1	9	3	17	9128	8.22	164		4597	4531	50.36	49.64
8	27	9	5	18	9127	8.22	165		4750	4377	52.04	47.96
3	18	9	4	18	9126	8.22	166		4741	4385	51.95	48.05
8	7	9	6	18	9125	8.22	167		4882	4243	53.50	46.50
8	28	9	6	16	9122	8.22	168		4639	4483	50.86	49.14
4	28	9	3	17	9120	8.21	169		4838	4282	53.05	46.95
5	20	9	4	17	9116	8.21	170		4843	4273	53.13	46.87
5	22	9	6	15	9115	8.21	171		4598	4517	50.44	49.56
4	24	9	6	16	9112	8.21	172		4723	4389	51.83	48.17
11	6	9	6	17	9112	8.21	173		4551	4561	49.95	50.05
5	27	9	4	18	9109	8.20	174		4816	4293	52.87	47.13
8	10	9	2	17	9109	8.20	175		4808	4301	52.78	47.22
5	15	9	6	18	9108	8.20	176		4705	4403	51.66	48.34

			DAY OF		HR	PERCENT OF	HOUR		NORTH	SOUTH	PERCENT NORTH IS OF TOTAL	PERCENT SOUTH IS OF TOTAL
5	28	9	5	18	9106	8.20	177		4747	4359	52.13	47.87
6	19	9	6	17	9106	8.20	178		4593	4513	50.44	49.56
8	26	9	4	17	9106	8.20	179		4600	4506	50.52	49.48
6	10	9	4	18	9104	8.20	180		4884	4220	53.65	46.35
9	2	9	4	18	9102	8.20	181	111033	4668	4434	51.29	48.71
9	4	9	6	15	9102	8.20	182		4538	4564	49.86	50.14
8	21	9	6	18	9097	8.19	183		4630	4467	50.90	49.10
12	4	9	6	17	9097	8.19	184		4557	4540	50.09	49.91
12	18	9	6	18	9095	8.19	185		4636	4459	50.97	49.03
8	6	9	5	16	9094	8.19	186		4745	4349	52.18	47.82
2	12	9	5	17	9090	8.19	187		4764	4326	52.41	47.59
10	8	9	5	18	9088	8.18	188		4771	4317	52.50	47.50
7	31	9	6	15	9087	8.18	189		4694	4393	51.66	48.34
5	1	9	6	17	9085	8.18	190		4804	4281	52.88	47.12
3	20	9	6	18	9082	8.18	191		4722	4360	51.99	48.01
6	16	9	3	17	9080	8.18	192		4638	4442	51.08	48.92
9	1	9	3	18	9080	8.18	193		4830	4250	53.19	46.81
11	13	9	6	16	9079	8.18	194		4783	4296	52.68	47.32
3	19	9	5	18	9078	8.18	195		4825	4253	53.15	46.85
12	9	9	4	17	9078	8.18	196		4650	4428	51.22	48.78
7	2	9	5	16	9075	8.17	197		4831	4244	53.23	46.77
6	8	9	2	17	9072	8.17	198		4929	4143	54.33	45.67
4	21	9	3	18	9071	8.17	199		4682	4389	51.62	48.38
11	4	9	4	17	9070	8.17	200		4732	4338	52.17	47.83

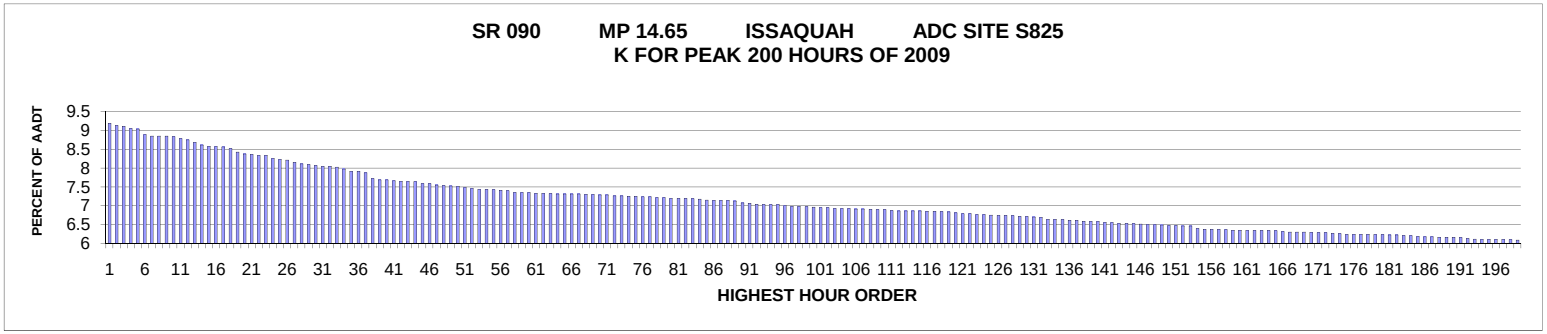

AADT= 119100 K 30 FACTOR= 8.09 K 100 FACTOR= 6.97 K 200 FACTOR= 6.08 D FACTOR= 62.22

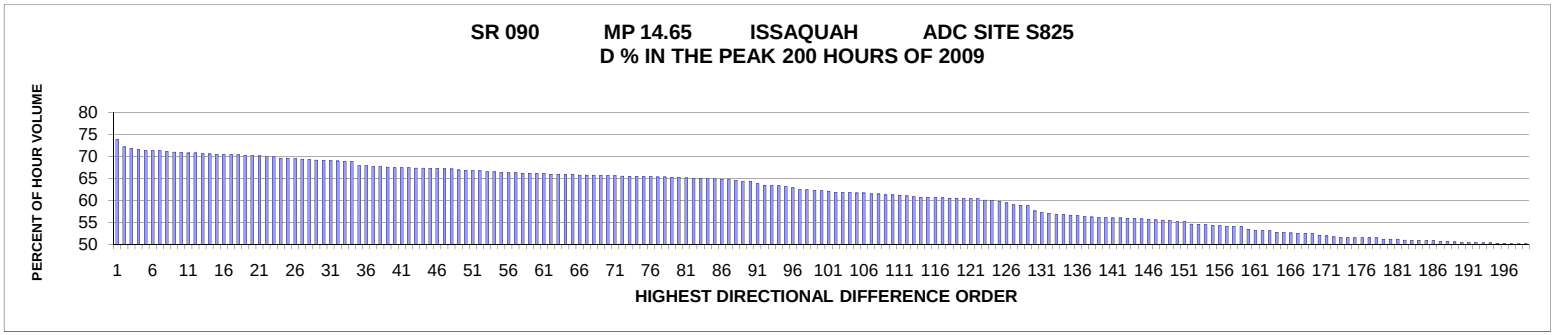

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
1	30	9	6	18	10949	9.19	1	119100	7274	3675	66.44	33.56
1	30	9	6	17	10946	9.19	2		7181	3765	65.6	34.4
1	16	9	6	18	10877	9.13	3		7121	3756	65.47	34.53
1	16	9	6	17	10847	9.11	4		7084	3763	65.31	34.69
1	23	9	6	17	10775	9.05	5		7087	3688	65.77	34.23
1	23	9	6	18	10768	9.04	6		7055	3713	65.52	34.48
1	22	9	5	18	10575	8.88	7		6955	3620	65.77	34.23
1	14	9	4	18	10542	8.85	8		7027	3515	66.66	33.34
1	9	9	6	18	10540	8.85	9		6775	3765	64.28	35.72
1	9	9	6	17	10536	8.85	10		6850	3686	65.02	34.98
1	29	9	5	18	10521	8.83	11		6962	3559	66.17	33.83
1	15	9	5	18	10459	8.78	12		6945	3514	66.4	33.6
1	28	9	4	18	10424	8.75	13		6998	3426	67.13	32.87
1	21	9	4	18	10353	8.69	14		6798	3555	65.66	34.34
1	14	9	4	17	10260	8.61	15		6640	3620	64.72	35.28
1	13	9	3	18	10219	8.58	16		6772	3447	66.27	33.73
1	26	9	2	18	10208	8.57	17		6873	3335	67.33	32.67

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
1	15	9	5	17	10193	8.56	18		6551	3642	64.27	35.73
1	29	9	5	17	10149	8.52	19		6631	3518	65.34	34.66
1	16	9	6	16	10027	8.42	20		6051	3976	60.35	39.65
1	22	9	5	17	9971	8.37	21	119100	6513	3458	65.32	34.68
1	20	9	3	18	9952	8.36	22		6695	3257	67.27	32.73
1	21	9	4	17	9937	8.34	23		6457	3480	64.98	35.02
1	13	9	3	17	9932	8.34	24		6573	3359	66.18	33.82
1	19	9	2	17	9827	8.25	25		5797	4030	58.99	41.01
1	19	9	2	18	9797	8.23	26		6057	3740	61.83	38.17
1	28	9	4	17	9773	8.21	27		6345	3428	64.92	35.08
1	30	9	6	16	9701	8.15	28		5960	3741	61.44	38.56
1	26	9	2	17	9661	8.11	29		6321	3340	65.43	34.57
1	9	9	6	16	9638	8.09	30		5825	3813	60.44	39.56
1	20	9	3	17	9615	8.07	31		6332	3283	65.86	34.14
1	23	9	6	16	9587	8.05	32		5954	3633	62.1	37.9
1	2	9	6	17	9586	8.05	33		5436	4150	56.71	43.29
1	5	9	2	18	9551	8.02	34		6737	2814	70.54	29.46
1	27	9	3	18	9498	7.97	35		6399	3099	67.37	32.63
1	27	9	3	17	9425	7.91	36		6158	3267	65.34	34.66
1	12	9	2	18	9423	7.91	37		6296	3127	66.82	33.18
1	12	9	2	17	9372	7.87	38		6102	3270	65.11	34.89
1	5	9	2	17	9199	7.72	39		6214	2985	67.55	32.45
1	8	9	5	17	9145	7.68	40		5801	3344	63.43	36.57
1	13	9	3	8	9142	7.68	41	119100	2596	6546	28.4	71.6
1	29	9	5	8	9122	7.66	42		2647	6475	29.02	70.98
1	19	9	2	16	9106	7.65	43		5068	4038	55.66	44.34
1	8	9	5	18	9097	7.64	44		6045	3052	66.45	33.55
1	28	9	4	8	9093	7.63	45		2606	6487	28.66	71.34
1	17	9	7	17	9029	7.58	46		4109	4920	45.51	54.49
1	6	9	3	17	9024	7.58	47		5825	3199	64.55	35.45
1	14	9	4	16	8994	7.55	48		5446	3548	60.55	39.45
1	23	9	6	8	8966	7.53	49		2725	6241	30.39	69.61
1	15	9	5	16	8951	7.52	50		5459	3492	60.99	39.01
1	22	9	5	16	8948	7.51	51		5531	3417	61.81	38.19
1	14	9	4	8	8907	7.48	52		2477	6430	27.81	72.19
1	2	9	6	16	8877	7.45	53		4818	4059	54.28	45.72
1	22	9	5	8	8855	7.43	54		2590	6265	29.25	70.75
1	6	9	3	18	8845	7.43	55		5809	3036	65.68	34.32
1	16	9	6	8	8839	7.42	56		2618	6221	29.62	70.38
1	13	9	3	16	8821	7.41	57		5331	3490	60.44	39.56
1	26	9	2	8	8802	7.39	58		2483	6319	28.21	71.79
1	21	9	4	16	8756	7.35	59		5286	3470	60.37	39.63
1	9	9	6	15	8745	7.34	60		4534	4211	51.85	48.15
1	28	9	4	9	8738	7.34	61	119100	2960	5778	33.88	66.12
1	9	9	6	19	8727	7.33	62		5444	3283	62.38	37.62
1	30	9	6	8	8726	7.33	63		2623	6103	30.06	69.94
1	29	9	5	9	8718	7.32	64		2800	5918	32.12	67.88
1	28	9	4	16	8712	7.31	65		5334	3378	61.23	38.77
1	29	9	5	16	8706	7.31	66		5414	3292	62.19	37.81
1	22	9	5	9	8705	7.31	67		2798	5907	32.14	67.86
1	12	9	2	8	8704	7.31	68		2542	6162	29.2	70.8
1	7	9	4	17	8700	7.3	69		5639	3061	64.82	35.18

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
1	30	9	6	19	8683	7.29	70		5503	3180	63.38	36.62
1	15	9	5	8	8672	7.28	71		2501	6171	28.84	71.16
1	26	9	2	16	8666	7.28	72		5347	3319	61.7	38.3
1	15	9	5	9	8650	7.26	73		2800	5850	32.37	67.63
1	9	9	6	8	8644	7.26	74		2537	6107	29.35	70.65
1	7	9	4	18	8637	7.25	75		5806	2831	67.22	32.78
1	14	9	4	9	8634	7.25	76		2670	5964	30.92	69.08
1	12	9	2	9	8616	7.23	77		2555	6061	29.65	70.35
1	13	9	3	9	8612	7.23	78		2683	5929	31.15	68.85
1	20	9	3	16	8589	7.21	79		5196	3393	60.5	39.5
1	30	9	6	15	8589	7.21	80		4863	3726	56.62	43.38
1	21	9	4	8	8569	7.19	81	119100	2463	6106	28.74	71.26
1	16	9	6	19	8565	7.19	82		5383	3182	62.85	37.15
1	17	9	7	16	8559	7.19	83		4077	4482	47.63	52.37
1	23	9	6	19	8550	7.18	84		5270	3280	61.64	38.36
1	20	9	3	8	8538	7.17	85		2529	6009	29.62	70.38
1	31	9	7	17	8513	7.15	86		3963	4550	46.55	53.45
1	30	9	6	9	8504	7.14	87		2773	5731	32.61	67.39
1	2	9	6	18	8503	7.14	88		4740	3763	55.75	44.25
1	26	9	2	9	8502	7.14	89		2641	5861	31.06	68.94
1	15	9	5	19	8482	7.12	90		5669	2813	66.84	33.16
1	29	9	5	19	8423	7.07	91		5535	2888	65.71	34.29
1	16	9	6	15	8405	7.06	92		4630	3775	55.09	44.91
1	12	9	2	16	8385	7.04	93		5133	3252	61.22	38.78
1	6	9	3	16	8370	7.03	94		5083	3287	60.73	39.27
1	8	9	5	8	8368	7.03	95		2398	5970	28.66	71.34
1	9	9	6	9	8368	7.03	96		2570	5798	30.71	69.29
1	31	9	7	16	8324	6.99	97		4040	4284	48.53	51.47
1	16	9	6	9	8316	6.98	98		2830	5486	34.03	65.97
1	23	9	6	9	8312	6.98	99		2707	5605	32.57	67.43
1	27	9	3	16	8297	6.97	100		5162	3135	62.22	37.78
1	28	9	4	19	8292	6.96	101	119100	5411	2881	65.26	34.74
1	17	9	7	15	8267	6.94	102		4139	4128	50.07	49.93
1	12	9	2	19	8266	6.94	103		5804	2462	70.22	29.78
1	6	9	3	8	8258	6.93	104		2407	5851	29.15	70.85
1	31	9	7	15	8242	6.92	105		4130	4112	50.11	49.89
1	24	9	7	17	8241	6.92	106		3863	4378	46.88	53.12
1	14	9	4	19	8234	6.91	107		5447	2787	66.15	33.85
1	24	9	7	16	8227	6.91	108		4077	4150	49.56	50.44
1	7	9	4	8	8214	6.9	109		2146	6068	26.13	73.87
1	23	9	6	15	8206	6.89	110		4617	3589	56.26	43.74
1	21	9	4	9	8201	6.89	111		2791	5410	34.03	65.97
1	22	9	5	19	8187	6.87	112		5310	2877	64.86	35.14
1	26	9	2	19	8174	6.86	113		5654	2520	69.17	30.83
1	8	9	5	16	8173	6.86	114		4901	3272	59.97	40.03
1	2	9	6	15	8171	6.86	115		4183	3988	51.19	48.81
1	20	9	3	9	8167	6.86	116		2541	5626	31.11	68.89
1	10	9	7	16	8160	6.85	117		3957	4203	48.49	51.51
1	10	9	7	14	8156	6.85	118		3944	4212	48.36	51.64
1	13	9	3	19	8144	6.84	119		5368	2776	65.91	34.09
1	31	9	7	13	8132	6.83	120		4029	4103	49.55	50.45
1	27	9	3	8	8116	6.81	121	119100	2441	5675	30.08	69.92

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
1	8	9	5	9	8075	6.78	122		2630	5445	32.57	67.43
1	21	9	4	19	8072	6.78	123		5349	2723	66.27	33.73
1	17	9	7	14	8051	6.76	124		4001	4050	49.7	50.3
1	15	9	5	10	8046	6.76	125		2947	5099	36.63	63.37
1	24	9	7	13	8036	6.75	126		3900	4136	48.53	51.47
1	10	9	7	17	8033	6.74	127		3819	4214	47.54	52.46
1	18	9	1	16	8027	6.74	128		3447	4580	42.94	57.06
1	6	9	3	19	8011	6.73	129		5558	2453	69.38	30.62
1	27	9	3	9	7992	6.71	130		2644	5348	33.08	66.92
1	31	9	7	18	7987	6.71	131		3675	4312	46.01	53.99
1	19	9	2	15	7978	6.7	132		4205	3773	52.71	47.29
1	6	9	3	9	7970	6.69	133		2468	5502	30.97	69.03
1	17	9	7	18	7912	6.64	134		3496	4416	44.19	55.81
1	5	9	2	16	7904	6.64	135		4988	2916	63.11	36.89
1	31	9	7	14	7899	6.63	136		3889	4010	49.23	50.77
1	8	9	5	19	7868	6.61	137		5547	2321	70.5	29.5
1	17	9	7	13	7868	6.61	138		3884	3984	49.36	50.64
1	18	9	1	17	7854	6.59	139		3335	4519	42.46	57.54
1	3	9	7	17	7846	6.59	140		3496	4350	44.56	55.44
1	27	9	3	19	7842	6.58	141	119100	5306	2536	67.66	32.34
1	24	9	7	14	7807	6.55	142		3828	3979	49.03	50.97
1	10	9	7	13	7786	6.54	143		3957	3829	50.82	49.18
1	20	9	3	19	7781	6.53	144		5234	2547	67.27	32.73
1	7	9	4	9	7775	6.53	145		2316	5459	29.79	70.21
1	10	9	7	15	7761	6.52	146		3844	3917	49.53	50.47
1	7	9	4	16	7754	6.51	147		4780	2974	61.65	38.35
1	2	9	6	14	7729	6.49	148		3842	3887	49.71	50.29
1	24	9	7	15	7726	6.49	149		3897	3829	50.44	49.56
1	31	9	7	12	7718	6.48	150		3842	3876	49.78	50.22
1	4	9	1	16	7710	6.47	151		3336	4374	43.27	56.73
1	3	9	7	16	7702	6.47	152		3615	4087	46.94	53.06
1	21	9	4	10	7696	6.46	153		2965	4731	38.53	61.47
1	14	9	4	10	7689	6.46	154		3016	4673	39.22	60.78
1	16	9	6	10	7612	6.39	155		3063	4549	40.24	59.76
1	24	9	7	18	7587	6.37	156		3474	4113	45.79	54.21
1	16	9	6	14	7586	6.37	157		4104	3482	54.1	45.9
1	25	9	1	16	7582	6.37	158		3483	4099	45.94	54.06
1	3	9	7	15	7571	6.36	159		3633	3938	47.99	52.01
1	30	9	6	10	7559	6.35	160		3019	4540	39.94	60.06
1	6	9	3	10	7557	6.35	161	119100	2628	4929	34.78	65.22
1	4	9	1	15	7555	6.34	162		3431	4124	45.41	54.59
1	13	9	3	10	7554	6.34	163		2735	4819	36.21	63.79
1	17	9	7	12	7551	6.34	164		3883	3668	51.42	48.58
1	29	9	5	10	7545	6.34	165		2972	4573	39.39	60.61
1	2	9	6	13	7540	6.33	166		3773	3767	50.04	49.96
1	24	9	7	12	7516	6.31	167		3754	3762	49.95	50.05
1	22	9	5	15	7508	6.3	168		4204	3304	55.99	44.01
1	14	9	4	15	7504	6.3	169		4201	3303	55.98	44.02
1	15	9	5	15	7498	6.3	170		4162	3336	55.51	44.49
1	25	9	1	17	7486	6.29	171		3203	4283	42.79	57.21
1	18	9	1	14	7480	6.28	172		3677	3803	49.16	50.84
1	5	9	2	8	7479	6.28	173		1847	5632	24.7	75.3

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
1	25	9	1	14	7459	6.26	174		3837	3622	51.44	48.56
1	29	9	5	15	7440	6.25	175		4178	3262	56.16	43.84
1	9	9	6	10	7436	6.24	176		3066	4370	41.23	58.77
1	18	9	1	13	7436	6.24	177		3905	3531	52.51	47.49
1	22	9	5	10	7435	6.24	178		2921	4514	39.29	60.71
1	23	9	6	10	7429	6.24	179		3054	4375	41.11	58.89
1	28	9	4	10	7422	6.23	180		3015	4407	40.62	59.38
1	19	9	2	14	7417	6.23	181	119100	3797	3620	51.19	48.81
1	18	9	1	15	7412	6.22	182		3507	3905	47.32	52.68
1	7	9	4	19	7403	6.22	183		5150	2253	69.57	30.43
1	26	9	2	15	7389	6.2	184		4100	3289	55.49	44.51
1	28	9	4	15	7380	6.2	185		4065	3315	55.08	44.92
1	9	9	6	14	7357	6.18	186		3903	3454	53.05	46.95
1	3	9	7	14	7345	6.17	187		3589	3756	48.86	51.14
1	21	9	4	15	7345	6.17	188		4120	3225	56.09	43.91
1	30	9	6	14	7341	6.16	189		4145	3196	56.46	43.54
1	5	9	2	9	7338	6.16	190		2236	5102	30.47	69.53
1	13	9	3	15	7336	6.16	191		4110	3226	56.03	43.97
1	12	9	2	10	7319	6.15	192		2754	4565	37.63	62.37
1	23	9	6	14	7303	6.13	193		3977	3326	54.46	45.54
1	5	9	2	19	7275	6.11	194		5100	2175	70.1	29.9
1	10	9	7	12	7265	6.1	195		3585	3680	49.35	50.65
1	25	9	1	15	7265	6.1	196		3529	3736	48.58	51.42
1	20	9	3	15	7263	6.1	197		4058	3205	55.87	44.13
1	26	9	2	10	7260	6.1	198		2822	4438	38.87	61.13
1	2	9	6	12	7249	6.09	199		3561	3688	49.12	50.88
1	25	9	1	13	7241	6.08	200		3798	3443	52.45	47.55

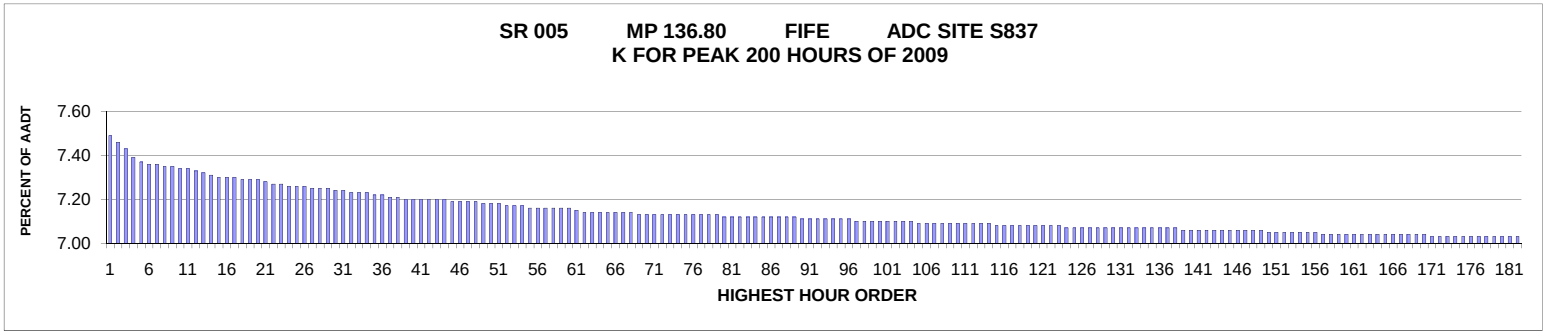

AADT= 182204 **K 30 FACTOR=** 7.24 **K 100 FACTOR=** 7.1 **K 200 FACTOR=** 7.02 **D FACTOR=** 53.64

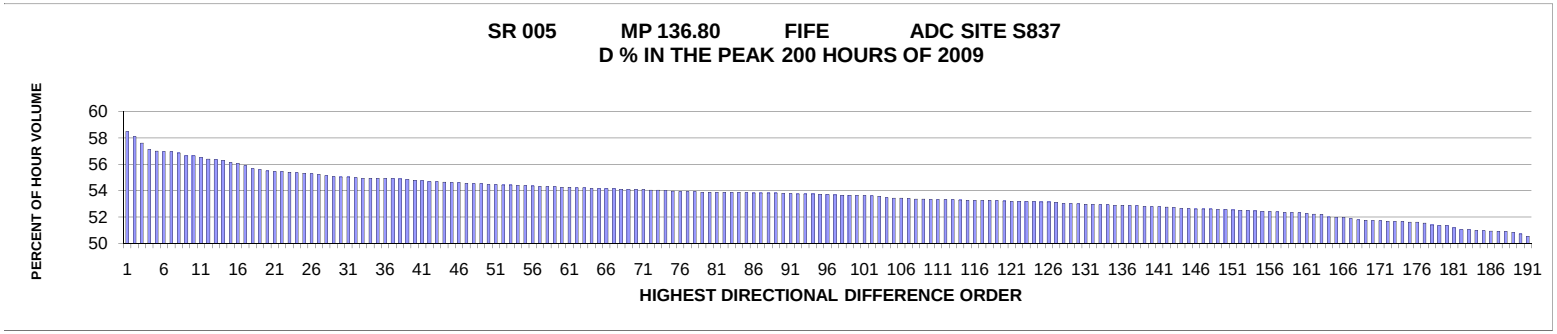

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
2	16	9	2	16	13647	7.49	1	182204	6235	7412	45.69	54.31
3	27	9	6	15	13587	7.46	2		6237	7350	45.90	54.10
2	13	9	6	15	13541	7.43	3		6189	7352	45.71	54.29
2	20	9	6	15	13462	7.39	4		6011	7451	44.65	55.35
5	8	9	6	15	13435	7.37	5		6158	7277	45.84	54.16
2	5	9	5	16	13414	7.36	6		5687	7727	42.40	57.60
3	6	9	6	15	13413	7.36	7		6044	7369	45.06	54.94
3	13	9	6	15	13396	7.35	8		6043	7353	45.11	54.89
3	4	9	4	16	13387	7.35	9		5804	7583	43.36	56.64
3	18	9	4	17	13373	7.34	10		6083	7290	45.49	54.51
5	1	9	6	15	13373	7.34	11		6198	7175	46.35	53.65
2	17	9	3	16	13362	7.33	12		5754	7608	43.06	56.94
8	12	9	4	17	13331	7.32	13		6277	7054	47.09	52.91
2	12	9	5	16	13321	7.31	14		5876	7445	44.11	55.89
8	13	9	5	15	13303	7.30	15		6031	7272	45.34	54.66
8	13	9	5	17	13299	7.30	16		6341	6958	47.68	52.32
8	14	9	6	14	13292	7.30	17		6279	7013	47.24	52.76

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
11	25	9	4	13	13285	7.29	18		6431	6854	48.41	51.59
2	13	9	6	16	13279	7.29	19		6204	7075	46.72	53.28
4	30	9	5	17	13274	7.29	20		6157	7117	46.38	53.62
4	29	9	4	17	13267	7.28	21	182204	6076	7191	45.80	54.20
4	16	9	5	16	13244	7.27	22		6039	7205	45.60	54.40
11	25	9	4	14	13243	7.27	23		6497	6746	49.06	50.94
4	3	9	6	15	13233	7.26	24		6162	7071	46.57	53.43
4	15	9	4	17	13232	7.26	25		6185	7047	46.74	53.26
4	29	9	4	16	13227	7.26	26		5776	7451	43.67	56.33
8	4	9	3	16	13217	7.25	27		6092	7125	46.09	53.91
6	18	9	5	15	13216	7.25	28		6123	7093	46.33	53.67
4	22	9	4	17	13214	7.25	29		6099	7115	46.16	53.84
7	9	9	5	15	13192	7.24	30		6081	7111	46.10	53.90
5	20	9	4	16	13185	7.24	31		6026	7159	45.70	54.30
8	5	9	4	17	13176	7.23	32		6357	6819	48.25	51.75
3	30	9	2	17	13169	7.23	33		6042	7127	45.88	54.12
3	26	9	5	17	13168	7.23	34		6465	6703	49.10	50.90
8	11	9	3	17	13160	7.22	35		6077	7083	46.18	53.82
8	12	9	4	16	13159	7.22	36		5965	7194	45.33	54.67
4	23	9	5	17	13143	7.21	37		6138	7005	46.70	53.30
7	15	9	4	17	13137	7.21	38		6191	6946	47.13	52.87
5	7	9	5	17	13126	7.20	39		6128	6998	46.69	53.31
8	13	9	5	16	13123	7.20	40		6201	6922	47.25	52.75
8	5	9	4	16	13117	7.20	41	182204	6253	6864	47.67	52.33
2	5	9	5	17	13115	7.20	42		6000	7115	45.75	54.25
8	21	9	6	14	13112	7.20	43		6211	6901	47.37	52.63
4	28	9	3	17	13110	7.20	44		5913	7197	45.10	54.90
8	10	9	2	17	13107	7.19	45		6085	7022	46.43	53.57
3	25	9	4	17	13102	7.19	46		6174	6928	47.12	52.88
2	19	9	5	16	13100	7.19	47		5892	7208	44.98	55.02
8	5	9	4	15	13098	7.19	48		6123	6975	46.75	53.25
8	18	9	3	16	13091	7.18	49		5988	7103	45.74	54.26
4	15	9	4	16	13088	7.18	50		5967	7121	45.59	54.41
7	22	9	4	16	13086	7.18	51		6045	7041	46.19	53.81
8	22	9	7	13	13072	7.17	52		6240	6832	47.74	52.26
7	21	9	3	17	13058	7.17	53		6079	6979	46.55	53.45
5	15	9	6	18	13057	7.17	54		6459	6598	49.47	50.53
8	11	9	3	16	13051	7.16	55		5934	7117	45.47	54.53
4	17	9	6	16	13050	7.16	56		6156	6894	47.17	52.83
5	22	9	6	13	13050	7.16	57		6023	7027	46.15	53.85
3	4	9	4	17	13049	7.16	58		6040	7009	46.29	53.71
8	22	9	7	12	13049	7.16	59		6197	6852	47.49	52.51
3	18	9	4	16	13040	7.16	60		5607	7433	43.00	57.00
2	27	9	6	15	13033	7.15	61	182204	5875	7158	45.08	54.92
3	24	9	3	17	13018	7.14	62		6007	7011	46.14	53.86
4	30	9	5	16	13015	7.14	63		5985	7030	45.99	54.01
8	20	9	5	18	13015	7.14	64		6415	6600	49.29	50.71
3	31	9	3	16	13007	7.14	65		5707	7300	43.88	56.12
3	11	9	4	17	13006	7.14	66		6095	6911	46.86	53.14
7	14	9	3	17	13006	7.14	67		6035	6971	46.40	53.60
4	10	9	6	15	13002	7.14	68		6184	6818	47.56	52.44
5	15	9	6	15	13000	7.13	69		5970	7030	45.92	54.08

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
4	16	9	5	17	12999	7.13	70		6025	6974	46.35	53.65
8	20	9	5	15	12998	7.13	71		6082	6916	46.79	53.21
6	5	9	6	15	12996	7.13	72		5995	7001	46.13	53.87
6	7	9	1	18	12996	7.13	73		6381	6615	49.10	50.90
8	17	9	2	16	12996	7.13	74		5814	7182	44.74	55.26
8	24	9	2	16	12989	7.13	75		5964	7025	45.92	54.08
6	11	9	5	15	12988	7.13	76		5787	7201	44.56	55.44
8	7	9	6	14	12986	7.13	77		6181	6805	47.60	52.40
5	12	9	3	17	12985	7.13	78		6047	6938	46.57	53.43
7	27	9	2	16	12983	7.13	79		5893	7090	45.39	54.61
4	1	9	4	16	12978	7.12	80		5798	7180	44.68	55.32
5	21	9	5	17	12978	7.12	81	182204	6266	6712	48.28	51.72
6	19	9	6	15	12974	7.12	82		6232	6742	48.03	51.97
6	22	9	2	16	12974	7.12	83		5821	7153	44.87	55.13
5	21	9	5	15	12972	7.12	84		5750	7222	44.33	55.67
5	7	9	5	16	12971	7.12	85		5832	7139	44.96	55.04
8	12	9	4	18	12970	7.12	86		6098	6872	47.02	52.98
2	17	9	3	17	12969	7.12	87		5996	6973	46.23	53.77
8	10	9	2	16	12969	7.12	88		5889	7080	45.41	54.59
8	12	9	4	15	12967	7.12	89		5897	7070	45.48	54.52
5	27	9	4	16	12959	7.11	90		5666	7293	43.72	56.28
5	18	9	2	17	12958	7.11	91		6038	6920	46.60	53.40
5	10	9	1	14	12957	7.11	92		6354	6603	49.04	50.96
4	21	9	3	16	12956	7.11	93		5690	7266	43.92	56.08
8	4	9	3	17	12956	7.11	94		6050	6906	46.70	53.30
3	25	9	4	16	12949	7.11	95		5775	7174	44.60	55.40
7	8	9	4	17	12946	7.11	96		6152	6794	47.52	52.48
2	16	9	2	15	12945	7.10	97		5979	6966	46.19	53.81
5	14	9	5	18	12939	7.10	98		5969	6970	46.13	53.87
5	15	9	6	16	12936	7.10	99		6038	6898	46.68	53.32
7	23	9	5	15	12936	7.10	100		5942	6994	45.93	54.07
2	13	9	6	14	12935	7.10	101	182204	6132	6803	47.41	52.59
5	20	9	4	17	12930	7.10	102		6131	6799	47.42	52.58
2	13	9	6	17	12928	7.10	103		6292	6636	48.67	51.33
3	31	9	3	17	12928	7.10	104		5979	6949	46.25	53.75
8	19	9	4	16	12924	7.09	105		5849	7075	45.26	54.74
8	21	9	6	15	12924	7.09	106		6131	6793	47.44	52.56
4	27	9	2	17	12923	7.09	107		5899	7024	45.65	54.35
5	21	9	5	16	12922	7.09	108		5785	7137	44.77	55.23
4	17	9	6	15	12920	7.09	109		6176	6744	47.80	52.20
5	5	9	3	17	12920	7.09	110		5985	6935	46.32	53.68
7	13	9	2	16	12920	7.09	111		5950	6970	46.05	53.95
8	7	9	6	17	12919	7.09	112		6519	6400	50.46	49.54
4	21	9	3	17	12915	7.09	113		5883	7032	45.55	54.45
2	9	9	2	16	12912	7.09	114		5413	7499	41.92	58.08
7	23	9	5	16	12908	7.08	115		6034	6874	46.75	53.25
6	29	9	2	17	12907	7.08	116		5961	6946	46.18	53.82
8	21	9	6	13	12905	7.08	117		6049	6856	46.87	53.13
3	27	9	6	16	12901	7.08	118		6079	6822	47.12	52.88
4	22	9	4	16	12896	7.08	119		5729	7167	44.42	55.58
6	23	9	3	16	12896	7.08	120		5928	6968	45.97	54.03
8	20	9	5	17	12896	7.08	121	182204	6230	6666	48.31	51.69

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
4	14	9	3	16	12893	7.08	122		5354	7539	41.53	58.47
7	14	9	3	16	12891	7.08	123		5743	7148	44.55	55.45
6	18	9	5	16	12889	7.07	124		6033	6856	46.81	53.19
5	14	9	5	16	12886	7.07	125		5735	7151	44.51	55.49
7	22	9	4	15	12886	7.07	126		5901	6985	45.79	54.21
8	14	9	6	18	12886	7.07	127		6549	6337	50.82	49.18
8	17	9	2	17	12885	7.07	128		6012	6873	46.66	53.34
2	18	9	4	16	12884	7.07	129		5561	7323	43.16	56.84
5	12	9	3	16	12884	7.07	130		5605	7279	43.50	56.50
3	19	9	5	18	12882	7.07	131		6245	6637	48.48	51.52
5	1	9	6	18	12881	7.07	132		6291	6590	48.84	51.16
8	20	9	5	16	12880	7.07	133		5944	6936	46.15	53.85
8	3	9	2	15	12879	7.07	134		5818	7061	45.17	54.83
4	30	9	5	18	12878	7.07	135		5959	6919	46.27	53.73
2	27	9	6	16	12877	7.07	136		5936	6941	46.10	53.90
6	25	9	5	16	12876	7.07	137		5949	6927	46.20	53.80
7	6	9	2	18	12875	7.07	138		6104	6771	47.41	52.59
6	21	9	1	18	12869	7.06	139		6230	6639	48.41	51.59
3	11	9	4	16	12867	7.06	140		5782	7085	44.94	55.06
6	21	9	1	13	12866	7.06	141	182204	6177	6689	48.01	51.99
6	8	9	2	16	12865	7.06	142		5792	7073	45.02	54.98
8	11	9	3	18	12865	7.06	143		6034	6831	46.90	53.10
4	22	9	4	18	12864	7.06	144		6058	6806	47.09	52.91
3	20	9	6	14	12862	7.06	145		6015	6847	46.77	53.23
4	1	9	4	17	12862	7.06	146		5999	6863	46.64	53.36
8	1	9	7	12	12857	7.06	147		6078	6779	47.27	52.73
8	22	9	7	15	12857	7.06	148		6385	6472	49.66	50.34
5	7	9	5	18	12856	7.06	149		6117	6739	47.58	52.42
2	16	9	2	17	12848	7.05	150		6018	6830	46.84	53.16
5	18	9	2	16	12847	7.05	151		5854	6993	45.57	54.43
8	16	9	1	14	12845	7.05	152		6382	6463	49.68	50.32
8	16	9	1	13	12842	7.05	153		6381	6461	49.69	50.31
4	23	9	5	18	12841	7.05	154		6066	6775	47.24	52.76
4	3	9	6	14	12840	7.05	155		6095	6745	47.47	52.53
8	18	9	3	15	12838	7.05	156		5787	7051	45.08	54.92
8	21	9	6	16	12835	7.04	157		6060	6775	47.21	52.79
6	29	9	2	16	12833	7.04	158		5888	6945	45.88	54.12
5	21	9	5	18	12830	7.04	159		6202	6628	48.34	51.66
6	25	9	5	17	12830	7.04	160		6201	6629	48.33	51.67
8	18	9	3	17	12830	7.04	161	182204	6083	6747	47.41	52.59
8	19	9	4	17	12827	7.04	162		6074	6753	47.35	52.65
8	7	9	6	15	12825	7.04	163		6282	6543	48.98	51.02
11	12	9	5	16	12825	7.04	164		6007	6818	46.84	53.16
8	21	9	6	17	12824	7.04	165		6283	6541	48.99	51.01
3	27	9	6	17	12823	7.04	166		6371	6452	49.68	50.32
4	10	9	6	18	12823	7.04	167		6160	6663	48.04	51.96
5	11	9	2	17	12820	7.04	168		5915	6905	46.14	53.86
8	8	9	7	13	12820	7.04	169		6029	6791	47.03	52.97
8	8	9	7	14	12820	7.04	170		6291	6529	49.07	50.93
2	20	9	6	16	12818	7.03	171		6024	6794	47.00	53.00
7	21	9	3	16	12818	7.03	172		5893	6925	45.97	54.03
7	15	9	4	15	12817	7.03	173		5839	6978	45.56	54.44

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
5	15	9	6	17	12814	7.03	174		6363	6451	49.66	50.34
6	19	9	6	16	12811	7.03	175		6109	6702	47.69	52.31
5	10	9	1	16	12809	7.03	176		6178	6631	48.23	51.77
11	13	9	6	15	12809	7.03	177		5998	6811	46.83	53.17
8	10	9	2	15	12808	7.03	178		5938	6870	46.36	53.64
8	14	9	6	13	12807	7.03	179		6192	6615	48.35	51.65
4	27	9	2	16	12806	7.03	180		5493	7313	42.89	57.11
6	23	9	3	18	12806	7.03	181	182204	6164	6642	48.13	51.87
3	3	9	3	16	12805	7.03	182		5553	7252	43.37	56.63
7	8	9	4	18	12805	7.03	183		5986	6819	46.75	53.25
7	25	9	7	12	12805	7.03	184		6344	6461	49.54	50.46
8	17	9	2	15	12805	7.03	185		5844	6961	45.64	54.36
4	4	9	7	13	12799	7.02	186		6379	6420	49.84	50.16
4	3	9	6	16	12796	7.02	187		6011	6785	46.98	53.02
4	28	9	3	16	12796	7.02	188		5582	7214	43.62	56.38
7	14	9	3	18	12795	7.02	189		6020	6775	47.05	52.95
6	26	9	6	18	12792	7.02	190		6434	6358	50.30	49.70
6	30	9	3	16	12789	7.02	191		5782	7007	45.21	54.79
6	25	9	5	15	12787	7.02	192		5799	6988	45.35	54.65
11	13	9	6	16	12785	7.02	193		6114	6671	47.82	52.18

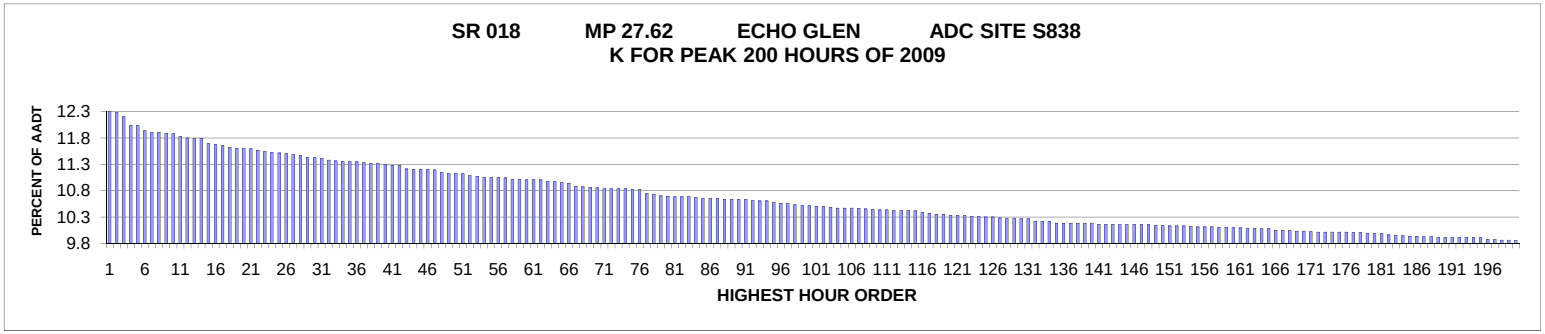

AADT= 21277 **K 30 FACTOR=** 11.42 **K 100 FACTOR=** 10.51 **K 200 FACTOR=** 9.85 **D FACTOR=** 57

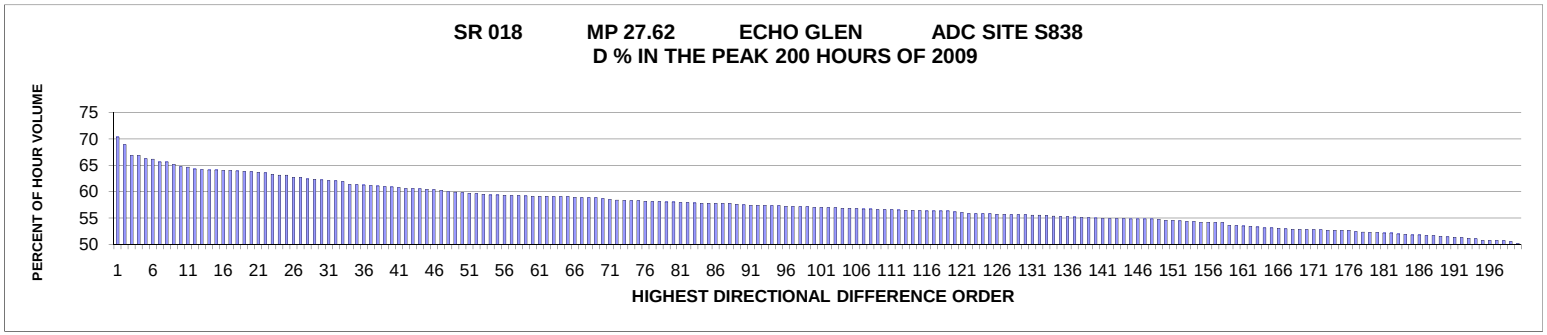

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
5	22	9	6	17	2618	12.3	1	21277	1378	1240	52.64	47.36
6	12	9	6	17	2612	12.28	2		1181	1431	45.21	54.79
7	24	9	6	16	2595	12.2	3		1191	1404	45.9	54.1
5	22	9	6	15	2562	12.04	4		1405	1157	54.84	45.16
8	7	9	6	17	2559	12.03	5		1148	1411	44.86	55.14
5	22	9	6	16	2538	11.93	6		1302	1236	51.3	48.7
7	2	9	5	17	2533	11.9	7		1075	1458	42.44	57.56
7	2	9	5	16	2531	11.9	8		1091	1440	43.11	56.89
7	24	9	6	17	2529	11.89	9		1031	1498	40.77	59.23
7	17	9	6	16	2527	11.88	10		1083	1444	42.86	57.14
5	15	9	6	17	2516	11.82	11		1044	1472	41.49	58.51
7	17	9	6	17	2510	11.8	12		1027	1483	40.92	59.08
7	31	9	6	17	2508	11.79	13		1090	1418	43.46	56.54
11	25	9	4	16	2508	11.79	14		1096	1412	43.7	56.3
9	4	9	6	17	2487	11.69	15		1226	1261	49.3	50.7
11	25	9	4	15	2482	11.67	16		1201	1281	48.39	51.61
6	26	9	6	17	2480	11.66	17		1047	1433	42.22	57.78

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
5	15	9	6	18	2473	11.62	18		1119	1354	45.25	54.75
7	10	9	6	17	2469	11.6	19		1030	1439	41.72	58.28
8	16	9	1	15	2469	11.6	20		1176	1293	47.63	52.37
6	26	9	6	16	2465	11.59	21	21277	1115	1350	45.23	54.77
9	4	9	6	16	2461	11.57	22		1249	1212	50.75	49.25
10	16	9	6	17	2456	11.54	23		1086	1370	44.22	55.78
11	29	9	1	15	2451	11.52	24		1242	1209	50.67	49.33
8	14	9	6	16	2450	11.51	25		1124	1326	45.88	54.12
8	14	9	6	17	2446	11.5	26		1076	1370	43.99	56.01
8	7	9	6	16	2442	11.48	27		1067	1375	43.69	56.31
6	19	9	6	17	2441	11.47	28		1145	1296	46.91	53.09
8	21	9	6	17	2431	11.43	29		1035	1396	42.58	57.42
11	25	9	4	17	2430	11.42	30		1051	1379	43.25	56.75
7	17	9	6	18	2428	11.41	31		1066	1362	43.9	56.1
8	16	9	1	17	2421	11.38	32		1041	1380	43	57
7	31	9	6	16	2417	11.36	33		1056	1361	43.69	56.31
7	10	9	6	16	2415	11.35	34		1008	1407	41.74	58.26
11	29	9	1	14	2414	11.35	35		1316	1098	54.52	45.48
11	29	9	1	16	2412	11.34	36		1105	1307	45.81	54.19
8	21	9	6	16	2410	11.33	37		1131	1279	46.93	53.07
6	5	9	6	17	2409	11.32	38		1089	1320	45.21	54.79
8	28	9	6	17	2406	11.31	39		1016	1390	42.23	57.77
8	28	9	6	16	2404	11.3	40		1123	1281	46.71	53.29
10	9	9	6	17	2401	11.28	41	21277	1038	1363	43.23	56.77
7	10	9	6	18	2400	11.28	42		1030	1370	42.92	57.08
6	19	9	6	16	2385	11.21	43		1142	1243	47.88	52.12
8	23	9	1	16	2383	11.2	44		942	1441	39.53	60.47
5	15	9	6	16	2382	11.2	45		999	1383	41.94	58.06
6	12	9	6	16	2382	11.2	46		1055	1327	44.29	55.71
8	16	9	1	14	2380	11.19	47		1255	1125	52.73	47.27
2	13	9	6	17	2373	11.15	48		974	1399	41.05	58.95
8	7	9	6	15	2369	11.13	49		1148	1221	48.46	51.54
8	14	9	6	18	2368	11.13	50		1047	1321	44.21	55.79
5	8	9	6	17	2366	11.12	51		1031	1335	43.58	56.42
8	7	9	6	18	2357	11.08	52		1025	1332	43.49	56.51
9	25	9	6	18	2356	11.07	53		1046	1310	44.4	55.6
8	14	9	6	15	2352	11.05	54		1109	1243	47.15	52.85
7	24	9	6	18	2351	11.05	55		1057	1294	44.96	55.04
9	4	9	6	18	2351	11.05	56		1221	1130	51.94	48.06
4	24	9	6	17	2348	11.04	57		1017	1331	43.31	56.69
10	9	9	6	16	2343	11.01	58		1056	1287	45.07	54.93
5	22	9	6	18	2342	11.01	59		1373	969	58.63	41.37
5	1	9	6	17	2341	11	60		1008	1333	43.06	56.94
8	16	9	1	18	2341	11	61	21277	953	1388	40.71	59.29
9	18	9	6	17	2340	11	62		1004	1336	42.91	57.09
8	16	9	1	13	2336	10.98	63		1212	1124	51.88	48.12
9	11	9	6	17	2334	10.97	64		913	1421	39.12	60.88
6	12	9	6	18	2329	10.95	65		1059	1270	45.47	54.53
7	31	9	6	15	2328	10.94	66		1099	1229	47.21	52.79
8	23	9	1	15	2316	10.88	67		1006	1310	43.44	56.56
9	4	9	6	15	2313	10.87	68		1272	1041	54.99	45.01
6	18	9	5	17	2311	10.86	69		765	1546	33.1	66.9

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	16	9	1	16	2309	10.85	70		1093	1216	47.34	52.66
9	25	9	6	17	2305	10.83	71		909	1396	39.44	60.56
5	21	9	5	17	2304	10.83	72		868	1436	37.67	62.33
7	2	9	5	18	2304	10.83	73		1085	1219	47.09	52.91
7	17	9	6	15	2304	10.83	74		1053	1251	45.7	54.3
1	16	9	6	17	2303	10.82	75		873	1430	37.91	62.09
7	10	9	6	15	2302	10.82	76		972	1330	42.22	57.78
7	5	9	1	14	2287	10.75	77		998	1289	43.64	56.36
7	2	9	5	15	2282	10.73	78		1063	1219	46.58	53.42
6	26	9	6	15	2276	10.7	79		1135	1141	49.87	50.13
6	19	9	6	18	2274	10.69	80		1074	1200	47.23	52.77
7	31	9	6	18	2273	10.68	81	21277	1018	1255	44.79	55.21
3	13	9	6	17	2272	10.68	82		848	1424	37.32	62.68
8	9	9	1	16	2272	10.68	83		892	1380	39.26	60.74
10	2	9	6	17	2271	10.67	84		990	1281	43.59	56.41
2	13	9	6	16	2267	10.65	85		957	1310	42.21	57.79
11	6	9	6	17	2266	10.65	86		845	1421	37.29	62.71
10	23	9	6	17	2265	10.65	87		933	1332	41.19	58.81
9	11	9	6	16	2263	10.64	88		927	1336	40.96	59.04
7	19	9	1	14	2262	10.63	89		1063	1199	46.99	53.01
9	17	9	5	17	2262	10.63	90		764	1498	33.78	66.22
6	26	9	6	18	2261	10.63	91		1021	1240	45.16	54.84
7	16	9	5	17	2257	10.61	92		810	1447	35.89	64.11
5	22	9	6	14	2255	10.6	93		1334	921	59.16	40.84
8	2	9	1	15	2255	10.6	94		970	1285	43.02	56.98
8	28	9	6	18	2248	10.57	95		1044	1204	46.44	53.56
2	20	9	6	17	2246	10.56	96		813	1433	36.2	63.8
3	27	9	6	17	2244	10.55	97		936	1308	41.71	58.29
8	2	9	1	14	2241	10.53	98		1089	1152	48.59	51.41
3	20	9	6	17	2237	10.51	99		907	1330	40.55	59.45
3	6	9	6	17	2236	10.51	100		825	1411	36.9	63.1
5	29	9	6	17	2234	10.5	101	21277	941	1293	42.12	57.88
9	18	9	6	16	2233	10.49	102		976	1257	43.71	56.29
8	2	9	1	16	2229	10.48	103		896	1333	40.2	59.8
5	25	9	2	13	2228	10.47	104		990	1238	44.43	55.57
7	3	9	6	13	2228	10.47	105		1350	878	60.59	39.41
5	8	9	6	16	2227	10.47	106		1035	1192	46.48	53.52
8	16	9	1	12	2225	10.46	107		1236	989	55.55	44.45
7	26	9	1	17	2223	10.45	108		861	1362	38.73	61.27
6	5	9	6	18	2221	10.44	109		1015	1206	45.7	54.3
10	16	9	6	18	2220	10.43	110		1002	1218	45.14	54.86
8	6	9	5	17	2219	10.43	111		772	1447	34.79	65.21
4	17	9	6	17	2218	10.42	112		902	1316	40.67	59.33
8	9	9	1	15	2218	10.42	113		907	1311	40.89	59.11
8	23	9	1	14	2216	10.42	114		995	1221	44.9	55.1
9	25	9	6	16	2215	10.41	115		962	1253	43.43	56.57
9	11	9	6	18	2209	10.38	116		931	1278	42.15	57.85
5	1	9	6	16	2206	10.37	117		885	1321	40.12	59.88
7	24	9	6	15	2203	10.35	118		980	1223	44.48	55.52
11	25	9	4	14	2202	10.35	119		1052	1150	47.77	52.23
7	19	9	1	17	2198	10.33	120		900	1298	40.95	59.05
6	28	9	1	16	2197	10.33	121	21277	811	1386	36.91	63.09

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
8	2	9	1	17	2196	10.32	122		900	1296	40.98	59.02
4	3	9	6	17	2194	10.31	123		904	1290	41.2	58.8
6	5	9	6	16	2193	10.31	124		913	1280	41.63	58.37
6	25	9	5	17	2192	10.3	125		754	1438	34.4	65.6
6	12	9	6	15	2191	10.3	126		976	1215	44.55	55.45
5	10	9	1	17	2188	10.28	127		846	1342	38.67	61.33
5	22	9	6	19	2186	10.27	128		1338	848	61.21	38.79
7	26	9	1	16	2185	10.27	129		883	1302	40.41	59.59
8	30	9	1	14	2184	10.26	130		1056	1128	48.35	51.65
9	3	9	5	17	2184	10.26	131		826	1358	37.82	62.18
5	29	9	6	16	2174	10.22	132		911	1263	41.9	58.1
9	4	9	6	14	2174	10.22	133		1297	877	59.66	40.34
8	28	9	6	15	2173	10.21	134		1029	1144	47.35	52.65
8	16	9	1	19	2167	10.18	135		860	1307	39.69	60.31
4	24	9	6	16	2166	10.18	136		915	1251	42.24	57.76
5	8	9	6	18	2166	10.18	137		1035	1131	47.78	52.22
7	26	9	1	15	2166	10.18	138		1033	1133	47.69	52.31
4	3	9	6	16	2165	10.18	139		961	1204	44.39	55.61
6	21	9	1	16	2165	10.18	140		892	1273	41.2	58.8
8	13	9	5	17	2161	10.16	141	21277	793	1368	36.7	63.3
8	20	9	5	17	2161	10.16	142		763	1398	35.31	64.69
11	29	9	1	17	2161	10.16	143		841	1320	38.92	61.08
10	8	9	5	17	2160	10.15	144		764	1396	35.37	64.63
1	30	9	6	17	2159	10.15	145		787	1372	36.45	63.55
6	28	9	1	15	2159	10.15	146		919	1240	42.57	57.43
7	5	9	1	15	2159	10.15	147		933	1226	43.21	56.79
9	7	9	2	13	2159	10.15	148		880	1279	40.76	59.24
7	3	9	6	12	2158	10.14	149		1384	774	64.13	35.87
7	23	9	5	17	2158	10.14	150		776	1382	35.96	64.04
5	25	9	2	12	2156	10.13	151		917	1239	42.53	57.47
7	26	9	1	14	2155	10.13	152		1020	1135	47.33	52.67
10	16	9	6	16	2155	10.13	153		1050	1105	48.72	51.28
4	17	9	6	16	2153	10.12	154		901	1252	41.85	58.15
6	28	9	1	17	2152	10.11	155		740	1412	34.39	65.61
5	10	9	1	18	2151	10.11	156		840	1311	39.05	60.95
7	12	9	1	17	2151	10.11	157		781	1370	36.31	63.69
3	27	9	6	16	2150	10.1	158		903	1247	42	58
8	21	9	6	15	2149	10.1	159		1085	1064	50.49	49.51
7	29	9	4	17	2147	10.09	160		668	1479	31.11	68.89
9	18	9	6	18	2147	10.09	161	21277	962	1185	44.81	55.19
7	19	9	1	15	2144	10.08	162		916	1228	42.72	57.28
7	30	9	5	17	2144	10.08	163		806	1338	37.59	62.41
3	6	9	6	16	2143	10.07	164		877	1266	40.92	59.08
8	23	9	1	13	2142	10.07	165		1047	1095	48.88	51.12
8	21	9	6	18	2138	10.05	166		995	1143	46.54	53.46
11	29	9	1	13	2138	10.05	167		1224	914	57.25	42.75
8	9	9	1	14	2137	10.04	168		966	1171	45.2	54.8
1	23	9	6	17	2135	10.03	169		772	1363	36.16	63.84
6	21	9	1	14	2134	10.03	170		925	1209	43.35	56.65
5	10	9	1	16	2132	10.02	171		943	1189	44.23	55.77
6	14	9	1	16	2130	10.01	172		853	1277	40.05	59.95
6	28	9	1	14	2130	10.01	173		951	1179	44.65	55.35

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	17	9	6	14	2130	10.01	174		1027	1103	48.22	51.78
2	16	9	2	17	2129	10.01	175		720	1409	33.82	66.18
5	17	9	1	16	2129	10.01	176		841	1288	39.5	60.5
7	19	9	1	16	2128	10	177		942	1186	44.27	55.73
8	2	9	1	13	2128	10	178		1049	1079	49.3	50.7
8	15	9	7	12	2124	9.98	179		1357	767	63.89	36.11
10	2	9	6	18	2124	9.98	180		1002	1122	47.18	52.82
6	11	9	5	17	2123	9.98	181	21277	629	1494	29.63	70.37
5	25	9	2	14	2119	9.96	182		890	1229	42	58
6	21	9	1	15	2116	9.95	183		935	1181	44.19	55.81
7	12	9	1	15	2115	9.94	184		841	1274	39.76	60.24
5	22	9	6	13	2112	9.93	185		1308	804	61.93	38.07
9	24	9	5	17	2112	9.93	186		699	1413	33.1	66.9
4	24	9	6	18	2111	9.92	187		967	1144	45.81	54.19
6	14	9	1	15	2111	9.92	188		889	1222	42.11	57.89
5	1	9	6	18	2109	9.91	189		1010	1099	47.89	52.11
5	17	9	1	17	2109	9.91	190		898	1211	42.58	57.42
6	19	9	6	15	2109	9.91	191		1018	1091	48.27	51.73
10	9	9	6	18	2109	9.91	192		961	1148	45.57	54.43
8	9	9	1	17	2108	9.91	193		800	1308	37.95	62.05
11	20	9	6	17	2108	9.91	194		758	1350	35.96	64.04
9	7	9	2	14	2106	9.9	195		856	1250	40.65	59.35
2	13	9	6	18	2101	9.87	196		898	1203	42.74	57.26
8	14	9	6	14	2100	9.87	197		1071	1029	51	49
7	16	9	5	16	2097	9.86	198		814	1283	38.82	61.18
7	16	9	5	18	2097	9.86	199		753	1344	35.91	64.09
8	27	9	5	17	2096	9.85	200		749	1347	35.73	64.27

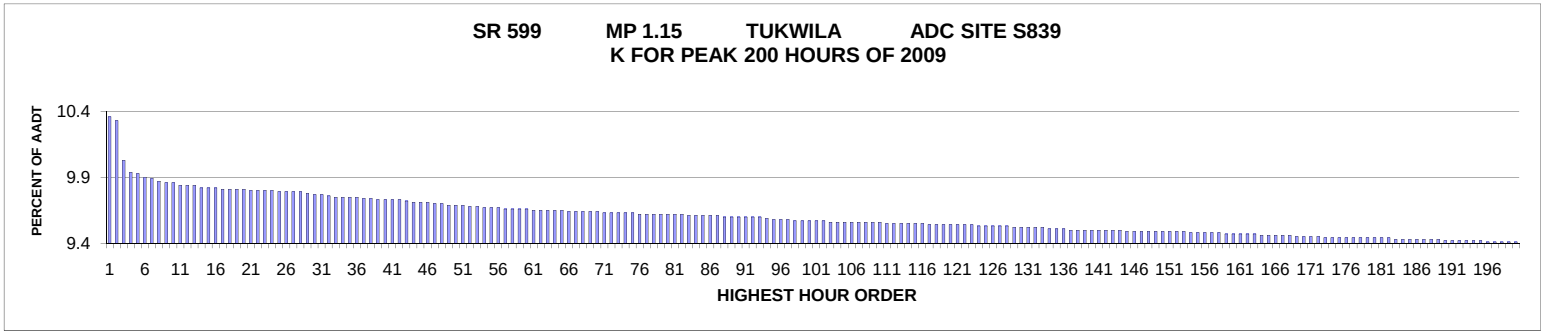

AADT= 39926 **K 30 FACTOR=** 9.77 **K 100 FACTOR=** 9.57 **K 200 FACTOR=** 9.41 **D FACTOR=** 64.11

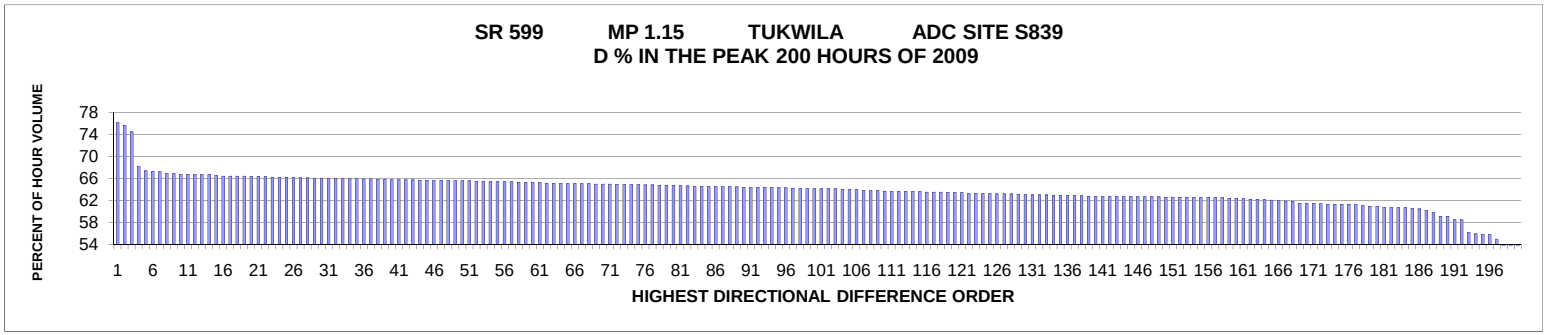

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
10	6	9	3	8	4135	10.36	1	39926	2816	1319	68.1	31.9
6	16	9	3	17	4125	10.33	2		1689	2436	40.95	59.05
6	24	9	4	17	4003	10.03	3		1461	2542	36.5	63.5
11	4	9	4	17	3970	9.94	4		1396	2574	35.16	64.84
8	5	9	4	17	3963	9.93	5		1564	2399	39.47	60.53
8	20	9	5	17	3951	9.9	6		1477	2474	37.38	62.62
12	17	9	5	17	3948	9.89	7		1484	2464	37.59	62.41
3	26	9	5	8	3942	9.87	8		2629	1313	66.69	33.31
9	30	9	4	17	3938	9.86	9		1505	2433	38.22	61.78
10	6	9	3	17	3938	9.86	10		1476	2462	37.48	62.52
7	15	9	4	17	3929	9.84	11		1519	2410	38.66	61.34
7	14	9	3	17	3928	9.84	12		1460	2468	37.17	62.83
9	2	9	4	17	3927	9.84	13		1454	2473	37.03	62.97
5	12	9	3	17	3921	9.82	14		1378	2543	35.14	64.86
6	3	9	4	17	3919	9.82	15		1493	2426	38.1	61.9
10	27	9	3	17	3919	9.82	16		1404	2515	35.83	64.17
12	10	9	5	17	3917	9.81	17		1465	2452	37.4	62.6

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
8	12	9	4	17	3916	9.81	18		1484	2432	37.9	62.1
9	3	9	5	17	3916	9.81	19		1604	2312	40.96	59.04
12	15	9	3	17	3915	9.81	20		1540	2375	39.34	60.66
10	13	9	3	17	3912	9.8	21	39926	1418	2494	36.25	63.75
10	28	9	4	17	3912	9.8	22		1485	2427	37.96	62.04
10	29	9	5	17	3912	9.8	23		1507	2405	38.52	61.48
11	3	9	3	8	3912	9.8	24		2563	1349	65.52	34.48
9	29	9	3	17	3909	9.79	25		1426	2483	36.48	63.52
10	7	9	4	17	3909	9.79	26		1389	2520	35.53	64.47
3	2	9	2	7	3908	9.79	27		2974	934	76.1	23.9
12	3	9	5	17	3907	9.79	28		1466	2441	37.52	62.48
12	10	9	5	16	3904	9.78	29		1427	2477	36.55	63.45
11	10	9	3	17	3902	9.77	30		1457	2445	37.34	62.66
4	16	9	5	8	3901	9.77	31		2582	1319	66.19	33.81
10	1	9	5	8	3895	9.76	32		2572	1323	66.03	33.97
9	16	9	4	17	3894	9.75	33		1409	2485	36.18	63.82
12	14	9	2	16	3894	9.75	34		1417	2477	36.39	63.61
12	1	9	3	17	3893	9.75	35		1441	2452	37.02	62.98
11	19	9	5	17	3892	9.75	36		1397	2495	35.89	64.11
9	15	9	3	17	3889	9.74	37		1505	2384	38.7	61.3
11	4	9	4	8	3889	9.74	38		2495	1394	64.16	35.84
6	17	9	4	17	3886	9.73	39		1427	2459	36.72	63.28
10	7	9	4	8	3886	9.73	40		2594	1292	66.75	33.25
5	20	9	4	17	3884	9.73	41	39926	1449	2435	37.31	62.69
10	8	9	5	17	3883	9.73	42		1503	2380	38.71	61.29
6	16	9	3	18	3882	9.72	43		1801	2081	46.39	53.61
11	5	9	5	17	3878	9.71	44		1545	2333	39.84	60.16
8	27	9	5	17	3876	9.71	45		1444	2432	37.25	62.75
5	13	9	4	17	3875	9.71	46		1522	2353	39.28	60.72
1	15	9	5	8	3874	9.7	47		2602	1272	67.17	32.83
7	8	9	4	17	3871	9.7	48		1437	2434	37.12	62.88
5	13	9	4	8	3870	9.69	49		2581	1289	66.69	33.31
10	1	9	5	17	3870	9.69	50		1491	2379	38.53	61.47
9	22	9	3	17	3868	9.69	51		1449	2419	37.46	62.54
7	16	9	5	17	3865	9.68	52		1521	2344	39.35	60.65
5	14	9	5	17	3864	9.68	53		1297	2567	33.57	66.43
1	15	9	5	17	3862	9.67	54		1375	2487	35.6	64.4
8	19	9	4	17	3862	9.67	55		1413	2449	36.59	63.41
10	5	9	2	17	3862	9.67	56		1443	2419	37.36	62.64
9	30	9	4	8	3858	9.66	57		2559	1299	66.33	33.67
11	2	9	2	8	3857	9.66	58		2544	1313	65.96	34.04
5	6	9	4	17	3856	9.66	59		1295	2561	33.58	66.42
6	10	9	4	8	3856	9.66	60		2504	1352	64.94	35.06
3	5	9	5	17	3854	9.65	61	39926	1348	2506	34.98	65.02
6	23	9	3	17	3852	9.65	62		1443	2409	37.46	62.54
8	25	9	3	17	3852	9.65	63		1453	2399	37.72	62.28
5	7	9	5	17	3851	9.65	64		1388	2463	36.04	63.96
7	22	9	4	17	3851	9.65	65		1503	2348	39.03	60.97
7	30	9	5	16	3849	9.64	66		1436	2413	37.31	62.69
12	9	9	4	17	3848	9.64	67		1414	2434	36.75	63.25
2	24	9	3	8	3847	9.64	68		2504	1343	65.09	34.91
9	9	9	4	17	3847	9.64	69		1402	2445	36.44	63.56

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
12	2	9	4	17	3847	9.64	70		1447	2400	37.61	62.39
1	13	9	3	17	3846	9.63	71		1408	2438	36.61	63.39
6	10	9	4	17	3846	9.63	72		1438	2408	37.39	62.61
3	11	9	4	17	3845	9.63	73		1367	2478	35.55	64.45
5	12	9	3	8	3844	9.63	74		2512	1332	65.35	34.65
6	9	9	3	8	3844	9.63	75		2519	1325	65.53	34.47
5	27	9	4	8	3842	9.62	76		2498	1344	65.02	34.98
6	25	9	5	17	3842	9.62	77		1396	2446	36.34	63.66
9	3	9	5	18	3842	9.62	78		1832	2010	47.68	52.32
10	20	9	3	17	3841	9.62	79		1376	2465	35.82	64.18
7	14	9	3	8	3840	9.62	80		2562	1278	66.72	33.28
7	30	9	5	17	3840	9.62	81	39926	1520	2320	39.58	60.42
10	27	9	3	8	3839	9.62	82		2549	1290	66.4	33.6
8	11	9	3	17	3837	9.61	83		1432	2405	37.32	62.68
12	14	9	2	15	3837	9.61	84		1507	2330	39.28	60.72
4	23	9	5	8	3836	9.61	85		2533	1303	66.03	33.97
1	14	9	4	17	3835	9.61	86		1367	2468	35.65	64.35
8	4	9	3	17	3835	9.61	87		1427	2408	37.21	62.79
6	2	9	3	8	3834	9.6	88		2482	1352	64.74	35.26
12	16	9	4	17	3834	9.6	89		1452	2382	37.87	62.13
6	16	9	3	8	3833	9.6	90		2530	1303	66.01	33.99
9	15	9	3	16	3832	9.6	91		1376	2456	35.91	64.09
9	8	9	3	17	3831	9.6	92		1499	2332	39.13	60.87
10	8	9	5	8	3831	9.6	93		2527	1304	65.96	34.04
11	18	9	4	17	3827	9.59	94		1407	2420	36.77	63.23
7	23	9	5	17	3825	9.58	95		1357	2468	35.48	64.52
8	10	9	2	17	3824	9.58	96		1473	2351	38.52	61.48
4	23	9	5	17	3823	9.58	97		1364	2459	35.68	64.32
11	5	9	5	8	3822	9.57	98		2530	1292	66.2	33.8
12	9	9	4	8	3822	9.57	99		2512	1310	65.72	34.28
5	7	9	5	8	3821	9.57	100		2510	1311	65.69	34.31
6	11	9	5	17	3819	9.57	101	39926	1492	2327	39.07	60.93
12	14	9	2	17	3819	9.57	102		1479	2340	38.73	61.27
7	9	9	5	17	3818	9.56	103		1479	2339	38.74	61.26
7	31	9	6	15	3817	9.56	104		1429	2388	37.44	62.56
8	13	9	5	17	3817	9.56	105		1479	2338	38.75	61.25
10	15	9	5	8	3817	9.56	106		2495	1322	65.37	34.63
5	4	9	2	8	3816	9.56	107		2502	1314	65.57	34.43
11	3	9	3	17	3815	9.56	108		1360	2455	35.65	64.35
11	12	9	5	8	3815	9.56	109		2502	1313	65.58	34.42
11	12	9	5	17	3815	9.56	110		1424	2391	37.33	62.67
12	3	9	5	8	3814	9.55	111		2506	1308	65.71	34.29
12	17	9	5	16	3814	9.55	112		1350	2464	35.4	64.6
4	15	9	4	17	3813	9.55	113		1383	2430	36.27	63.73
2	10	9	3	8	3812	9.55	114		2487	1325	65.24	34.76
5	19	9	3	17	3811	9.55	115		1342	2469	35.21	64.79
10	29	9	5	16	3811	9.55	116		1301	2510	34.14	65.86
7	7	9	3	17	3810	9.54	117		1452	2358	38.11	61.89
9	1	9	3	17	3810	9.54	118		1440	2370	37.8	62.2
10	22	9	5	8	3810	9.54	119		2511	1299	65.91	34.09
6	17	9	4	18	3809	9.54	120		1684	2125	44.21	55.79
4	21	9	3	17	3808	9.54	121	39926	1410	2398	37.03	62.97

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
6	4	9	5	18	3808	9.54	122		1682	2126	44.17	55.83
8	5	9	4	18	3808	9.54	123		1796	2012	47.16	52.84
2	12	9	5	17	3806	9.53	124		1368	2438	35.94	64.06
4	28	9	3	8	3805	9.53	125		2499	1306	65.68	34.32
6	2	9	3	17	3805	9.53	126		1385	2420	36.4	63.6
1	22	9	5	17	3804	9.53	127		1343	2461	35.3	64.7
2	11	9	4	17	3803	9.53	128		1351	2452	35.52	64.48
6	15	9	2	17	3802	9.52	129		1383	2419	36.38	63.62
7	30	9	5	15	3801	9.52	130		1425	2376	37.49	62.51
2	3	9	3	8	3799	9.52	131		2483	1316	65.36	34.64
3	4	9	4	17	3799	9.52	132		1354	2445	35.64	64.36
9	17	9	5	15	3799	9.52	133		1402	2397	36.9	63.1
1	28	9	4	8	3798	9.51	134		2537	1261	66.8	33.2
6	17	9	4	8	3797	9.51	135		2517	1280	66.29	33.71
9	24	9	5	16	3795	9.51	136		1345	2450	35.44	64.56
3	5	9	5	8	3794	9.5	137		2512	1282	66.21	33.79
5	28	9	5	17	3794	9.5	138		1399	2395	36.87	63.13
5	5	9	3	8	3793	9.5	139		2467	1326	65.04	34.96
11	10	9	3	8	3793	9.5	140		2500	1293	65.91	34.09
2	5	9	5	17	3792	9.5	141	39926	1366	2426	36.02	63.98
9	22	9	3	16	3792	9.5	142		1303	2489	34.36	65.64
1	13	9	3	8	3791	9.5	143		2481	1310	65.44	34.56
4	28	9	3	17	3791	9.5	144		1331	2460	35.11	64.89
2	25	9	4	8	3789	9.49	145		2476	1313	65.35	34.65
9	24	9	5	17	3789	9.49	146		1418	2371	37.42	62.58
10	19	9	2	17	3789	9.49	147		1407	2382	37.13	62.87
10	28	9	4	8	3789	9.49	148		2491	1298	65.74	34.26
10	20	9	3	8	3788	9.49	149		2502	1286	66.05	33.95
3	4	9	4	8	3787	9.49	150		2459	1328	64.93	35.07
4	29	9	4	17	3787	9.49	151		1343	2444	35.46	64.54
9	30	9	4	16	3787	9.49	152		1280	2507	33.8	66.2
10	22	9	5	17	3787	9.49	153		1395	2392	36.84	63.16
4	21	9	3	8	3786	9.48	154		2483	1303	65.58	34.42
5	20	9	4	8	3786	9.48	155		2484	1302	65.61	34.39
6	30	9	3	17	3785	9.48	156		1333	2452	35.22	64.78
8	26	9	4	17	3784	9.48	157		1416	2368	37.42	62.58
3	5	9	5	7	3783	9.48	158		2861	922	75.63	24.37
11	2	9	2	17	3782	9.47	159		1350	2432	35.7	64.3
11	4	9	4	7	3782	9.47	160		2817	965	74.48	25.52
8	11	9	3	16	3781	9.47	161	39926	1337	2444	35.36	64.64
11	17	9	3	16	3781	9.47	162		1281	2500	33.88	66.12
12	1	9	3	18	3779	9.47	163		1571	2208	41.57	58.43
8	24	9	2	17	3777	9.46	164		1416	2361	37.49	62.51
9	1	9	3	16	3777	9.46	165		1287	2490	34.07	65.93
9	15	9	3	8	3777	9.46	166		2486	1291	65.82	34.18
7	9	9	5	16	3776	9.46	167		1313	2463	34.77	65.23
8	26	9	4	16	3776	9.46	168		1333	2443	35.3	64.7
11	13	9	6	17	3775	9.45	169		1521	2254	40.29	59.71
8	18	9	3	17	3773	9.45	170		1400	2373	37.11	62.89
1	21	9	4	17	3772	9.45	171		1349	2423	35.76	64.24
9	22	9	3	18	3772	9.45	172		1704	2068	45.17	54.83
7	14	9	3	16	3771	9.44	173		1232	2539	32.67	67.33

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	NORTH VOLUME	SOUTH VOLUME	PERCENT NORTH IS OF TOTAL VOLUME	PERCENT SOUTH IS OF TOTAL VOLUME
9	3	9	5	16	3771	9.44	174		1355	2416	35.93	64.07
6	17	9	4	16	3770	9.44	175		1322	2448	35.07	64.93
9	23	9	4	17	3770	9.44	176		1393	2377	36.95	63.05
10	21	9	4	17	3770	9.44	177		1389	2381	36.84	63.16
2	12	9	5	8	3769	9.44	178		2517	1252	66.78	33.22
3	3	9	3	8	3768	9.44	179		2449	1319	64.99	35.01
6	3	9	4	8	3768	9.44	180		2382	1386	63.22	36.78
11	17	9	3	17	3768	9.44	181	39926	1407	2361	37.34	62.66
12	10	9	5	15	3768	9.44	182		1375	2393	36.49	63.51
3	24	9	3	8	3767	9.43	183		2499	1268	66.34	33.66
6	10	9	4	16	3767	9.43	184		1316	2451	34.93	65.07
12	2	9	4	8	3767	9.43	185		2408	1359	63.92	36.08
9	22	9	3	8	3766	9.43	186		2443	1323	64.87	35.13
10	20	9	3	16	3766	9.43	187		1300	2466	34.52	65.48
9	29	9	3	8	3765	9.43	188		2504	1261	66.51	33.49
6	3	9	4	16	3764	9.43	189		1334	2430	35.44	64.56
1	22	9	5	8	3763	9.42	190		2518	1245	66.91	33.09
2	5	9	5	8	3762	9.42	191		2499	1263	66.43	33.57
5	19	9	3	8	3762	9.42	192		2449	1313	65.1	34.9
8	20	9	5	8	3762	9.42	193		2532	1230	67.3	32.7
6	4	9	5	17	3761	9.42	194		1369	2392	36.4	63.6
12	11	9	6	17	3761	9.42	195		1564	2197	41.58	58.42
1	29	9	5	8	3759	9.41	196		2482	1277	66.03	33.97
12	2	9	4	18	3759	9.41	197		1664	2095	44.27	55.73
7	22	9	4	16	3758	9.41	198		1306	2452	34.75	65.25
12	1	9	3	8	3758	9.41	199		2455	1303	65.33	34.67
12	17	9	5	18	3758	9.41	200		1651	2107	43.93	56.07

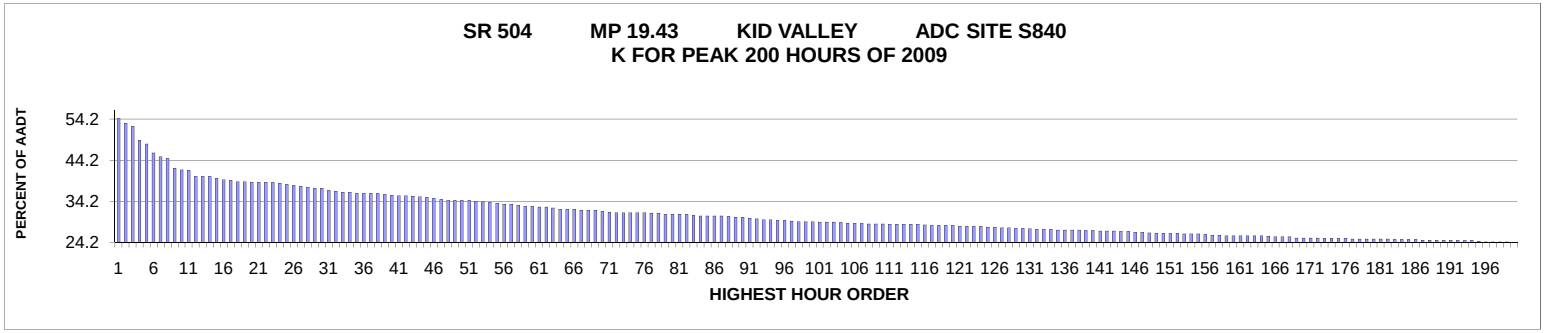

AADT= 731 **K 30 FACTOR=** 37.35 **K 100 FACTOR=** 29.27 **K 200 FACTOR=** 24.21 **D FACTOR=** 71.43

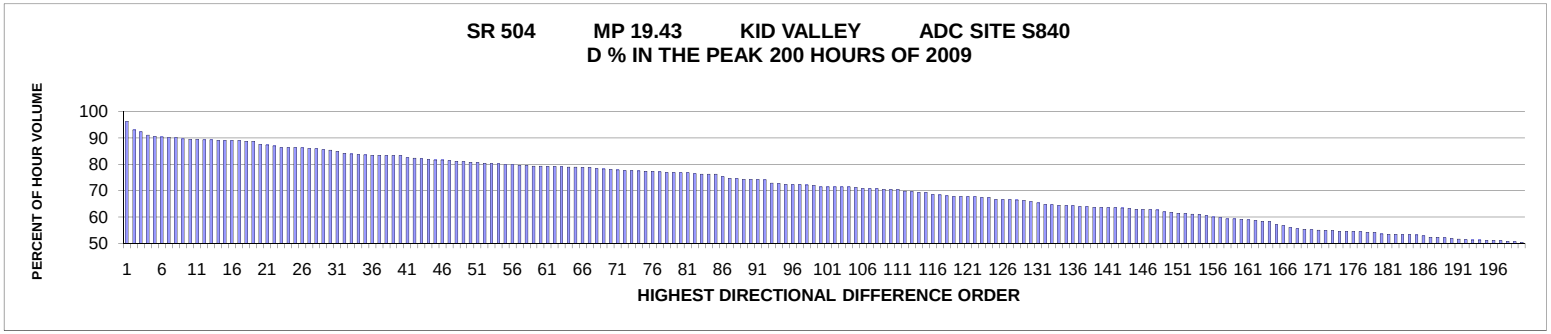

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
5	24	9	1	16	397	54.31	1	731	146	251	36.78	63.22
5	24	9	1	17	389	53.21	2		65	324	16.71	83.29
5	24	9	1	15	383	52.39	3		211	172	55.09	44.91
7	25	9	7	14	358	48.97	4		250	108	69.83	30.17
5	24	9	1	14	352	48.15	5		241	111	68.47	31.53
5	24	9	1	13	336	45.96	6		281	55	83.63	16.37
5	23	9	7	17	329	45.01	7		68	261	20.67	79.33
9	12	9	7	14	326	44.6	8		211	115	64.72	35.28
5	23	9	7	15	309	42.27	9		183	126	59.22	40.78
9	12	9	7	16	306	41.86	10		135	171	44.12	55.88
7	3	9	6	15	305	41.72	11		166	139	54.43	45.57
5	17	9	1	15	294	40.22	12		141	153	47.96	52.04
7	11	9	7	15	294	40.22	13		155	139	52.72	47.28
9	12	9	7	17	294	40.22	14		93	201	31.63	68.37
7	18	9	7	16	291	39.81	15		106	185	36.43	63.57
8	22	9	7	15	288	39.4	16		168	120	58.33	41.67
6	27	9	7	14	287	39.26	17		194	93	67.6	32.4

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
6	27	9	7	16	285	38.99	18		109	176	38.25	61.75
7	25	9	7	15	285	38.99	19		167	118	58.6	41.4
5	23	9	7	16	284	38.85	20		133	151	46.83	53.17
5	24	9	1	12	284	38.85	21	731	252	32	88.73	11.27
5	25	9	2	15	284	38.85	22		123	161	43.31	56.69
5	23	9	7	14	283	38.71	23		200	83	70.67	29.33
5	25	9	2	17	282	38.58	24		52	230	18.44	81.56
7	25	9	7	16	280	38.3	25		83	197	29.64	70.36
7	11	9	7	14	278	38.03	26		176	102	63.31	36.69
8	16	9	1	15	277	37.89	27		135	142	48.74	51.26
7	26	9	1	14	275	37.62	28		163	112	59.27	40.73
5	24	9	1	18	273	37.35	29		44	229	16.12	83.88
7	11	9	7	17	273	37.35	30		56	217	20.51	79.49
8	1	9	7	16	269	36.8	31		59	210	21.93	78.07
9	12	9	7	15	268	36.66	32		147	121	54.85	45.15
7	18	9	7	14	266	36.39	33		169	97	63.53	36.47
7	18	9	7	15	266	36.39	34		130	136	48.87	51.13
6	27	9	7	15	264	36.11	35		134	130	50.76	49.24
7	19	9	1	14	264	36.11	36		168	96	63.64	36.36
7	26	9	1	15	264	36.11	37		121	143	45.83	54.17
8	2	9	1	15	264	36.11	38		135	129	51.14	48.86
6	28	9	1	15	262	35.84	39		132	130	50.38	49.62
8	16	9	1	16	261	35.7	40		71	190	27.2	72.8
5	25	9	2	13	260	35.57	41	731	209	51	80.38	19.62
7	11	9	7	16	260	35.57	42		93	167	35.77	64.23
5	25	9	2	16	259	35.43	43		72	187	27.8	72.2
7	19	9	1	16	258	35.29	44		74	184	28.68	71.32
7	3	9	6	16	257	35.16	45		86	171	33.46	66.54
8	1	9	7	14	255	34.88	46		169	86	66.27	33.73
7	18	9	7	17	253	34.61	47		57	196	22.53	77.47
5	25	9	2	14	251	34.34	48		167	84	66.53	33.47
6	27	9	7	17	251	34.34	49		42	209	16.73	83.27
6	28	9	1	16	251	34.34	50		82	169	32.67	67.33
8	16	9	1	17	251	34.34	51		58	193	23.11	76.89
8	16	9	1	14	250	34.2	52		176	74	70.4	29.6
7	19	9	1	15	249	34.06	53		133	116	53.41	46.59
5	23	9	7	18	248	33.93	54		35	213	14.11	85.89
8	15	9	7	17	247	33.79	55		47	200	19.03	80.97
7	19	9	1	17	245	33.52	56		52	193	21.22	78.78
9	12	9	7	13	245	33.52	57		187	58	76.33	23.67
7	3	9	6	17	243	33.24	58		63	180	25.93	74.07
5	16	9	7	17	241	32.97	59		35	206	14.52	85.48
8	2	9	1	16	241	32.97	60		74	167	30.71	69.29
5	16	9	7	15	240	32.83	61	731	147	93	61.25	38.75
7	25	9	7	17	240	32.83	62		43	197	17.92	82.08
7	11	9	7	12	238	32.56	63		215	23	90.34	9.66
5	18	9	2	15	236	32.28	64		88	148	37.29	62.71
7	5	9	1	15	236	32.28	65		131	105	55.51	44.49
7	11	9	7	13	236	32.28	66		187	49	79.24	20.76
5	17	9	1	16	234	32.01	67		78	156	33.33	66.67
7	18	9	7	13	234	32.01	68		189	45	80.77	19.23
8	1	9	7	17	234	32.01	69		41	193	17.52	82.48

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
5	25	9	2	12	232	31.74	70		210	22	90.52	9.48
8	1	9	7	15	231	31.6	71		104	127	45.02	54.98
6	27	9	7	12	230	31.46	72		206	24	89.57	10.43
6	28	9	1	17	230	31.46	73		47	183	20.43	79.57
7	26	9	1	13	230	31.46	74		179	51	77.83	22.17
8	15	9	7	16	230	31.46	75		86	144	37.39	62.61
8	22	9	7	14	230	31.46	76		148	82	64.35	35.65
8	22	9	7	17	229	31.33	77		50	179	21.83	78.17
8	23	9	1	16	229	31.33	78		67	162	29.26	70.74
5	23	9	7	13	227	31.05	79		189	38	83.26	16.74
7	26	9	1	16	227	31.05	80		65	162	28.63	71.37
9	20	9	1	15	227	31.05	81	731	121	106	53.3	46.7
8	22	9	7	16	226	30.92	82		91	135	40.27	59.73
8	23	9	1	17	225	30.78	83		47	178	20.89	79.11
5	18	9	2	16	224	30.64	84		58	166	25.89	74.11
8	16	9	1	13	224	30.64	85		187	37	83.48	16.52
8	23	9	1	14	224	30.64	86		143	81	63.84	36.16
9	20	9	1	14	224	30.64	87		143	81	63.84	36.16
9	20	9	1	16	223	30.51	88		64	159	28.7	71.3
7	3	9	6	13	222	30.37	89		171	51	77.03	22.97
7	19	9	1	13	222	30.37	90		177	45	79.73	20.27
7	3	9	6	12	220	30.1	91		196	24	89.09	10.91
5	17	9	1	13	219	29.96	92		167	52	76.26	23.74
7	3	9	6	18	217	29.69	93		40	177	18.43	81.57
7	25	9	7	13	217	29.69	94		162	55	74.65	25.35
5	23	9	7	12	216	29.55	95		201	15	93.06	6.94
8	23	9	1	15	216	29.55	96		104	112	48.15	51.85
5	17	9	1	14	215	29.41	97		132	83	61.4	38.6
5	24	9	1	19	214	29.27	98		8	206	3.74	96.26
7	3	9	6	14	214	29.27	99		142	72	66.36	33.64
8	2	9	1	13	214	29.27	100		159	55	74.3	25.7
6	27	9	7	18	213	29.14	101	731	23	190	10.8	89.2
7	4	9	7	14	213	29.14	102		116	97	54.46	45.54
7	5	9	1	16	213	29.14	103		74	139	34.74	65.26
5	17	9	1	17	212	29	104		46	166	21.7	78.3
7	25	9	7	12	211	28.86	105		182	29	86.26	13.74
7	26	9	1	17	211	28.86	106		49	162	23.22	76.78
8	30	9	1	13	211	28.86	107		170	41	80.57	19.43
5	18	9	2	13	210	28.73	108		163	47	77.62	22.38
5	31	9	1	16	210	28.73	109		54	156	25.71	74.29
8	2	9	1	14	210	28.73	110		142	68	67.62	32.38
5	18	9	2	14	209	28.59	111		113	96	54.07	45.93
6	28	9	1	14	209	28.59	112		142	67	67.94	32.06
8	1	9	7	12	209	28.59	113		187	22	89.47	10.53
8	30	9	1	14	209	28.59	114		135	74	64.59	35.41
8	30	9	1	17	209	28.59	115		38	171	18.18	81.82
6	28	9	1	12	208	28.45	116		185	23	88.94	11.06
6	28	9	1	13	207	28.32	117		166	41	80.19	19.81
8	1	9	7	13	207	28.32	118		160	47	77.29	22.71
8	9	9	1	16	207	28.32	119		82	125	39.61	60.39
8	30	9	1	16	207	28.32	120		81	126	39.13	60.87
8	15	9	7	12	206	28.18	121	731	165	41	80.1	19.9

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
5	31	9	1	15	205	28.04	122		117	88	57.07	42.93
8	22	9	7	13	205	28.04	123		177	28	86.34	13.66
9	12	9	7	12	205	28.04	124		171	34	83.41	16.59
7	25	9	7	18	204	27.91	125		30	174	14.71	85.29
8	8	9	7	15	204	27.91	126		104	100	50.98	49.02
8	8	9	7	18	203	27.77	127		79	124	38.92	61.08
9	20	9	1	17	203	27.77	128		38	165	18.72	81.28
6	27	9	7	13	202	27.63	129		161	41	79.7	20.3
9	13	9	1	13	202	27.63	130		147	55	72.77	27.23
8	30	9	1	15	201	27.5	131		103	98	51.24	48.76
7	4	9	7	16	200	27.36	132		71	129	35.5	64.5
7	19	9	1	12	200	27.36	133		179	21	89.5	10.5
9	12	9	7	18	200	27.36	134		42	158	21	79
5	30	9	7	15	199	27.22	135		95	104	47.74	52.26
6	23	9	3	16	199	27.22	136		57	142	28.64	71.36
7	18	9	7	18	199	27.22	137		42	157	21.11	78.89
9	20	9	1	13	199	27.22	138		157	42	78.89	21.11
5	16	9	7	16	198	27.09	139		81	117	40.91	59.09
8	2	9	1	17	198	27.09	140		45	153	22.73	77.27
7	14	9	3	16	197	26.95	141	731	58	139	29.44	70.56
8	9	9	1	15	197	26.95	142		105	92	53.3	46.7
9	13	9	1	16	197	26.95	143		55	142	27.92	72.08
7	5	9	1	14	196	26.81	144		140	56	71.43	28.57
8	17	9	2	14	196	26.81	145		101	95	51.53	48.47
5	24	9	1	11	195	26.68	146		176	19	90.26	9.74
7	15	9	4	14	195	26.68	147		117	78	60	40
8	15	9	7	13	194	26.54	148		137	57	70.62	29.38
5	23	9	7	19	193	26.4	149		15	178	7.77	92.23
5	30	9	7	14	193	26.4	150		130	63	67.36	32.64
7	10	9	6	14	193	26.4	151		127	66	65.8	34.2
8	8	9	7	16	193	26.4	152		54	139	27.98	72.02
7	24	9	6	16	192	26.27	153		55	137	28.65	71.35
8	9	9	1	17	192	26.27	154		53	139	27.6	72.4
8	17	9	2	16	192	26.27	155		59	133	30.73	69.27
7	10	9	6	15	191	26.13	156		87	104	45.55	54.45
7	18	9	7	12	190	25.99	157		164	26	86.32	13.68
9	12	9	7	19	190	25.99	158		21	169	11.05	88.95
7	4	9	7	15	189	25.85	159		88	101	46.56	53.44
7	5	9	1	17	189	25.85	160		40	149	21.16	78.84
7	11	9	7	18	189	25.85	161	731	30	159	15.87	84.13
7	17	9	6	16	189	25.85	162		61	128	32.28	67.72
8	3	9	2	15	189	25.85	163		72	117	38.1	61.9
8	8	9	7	17	189	25.85	164		45	144	23.81	76.19
9	11	9	6	15	188	25.72	165		92	96	48.94	51.06
5	25	9	2	18	187	25.58	166		33	154	17.65	82.35
7	4	9	7	17	187	25.58	167		52	135	27.81	72.19
7	18	9	7	19	187	25.58	168		21	166	11.23	88.77
7	15	9	4	16	185	25.31	169		56	129	30.27	69.73
7	24	9	6	17	185	25.31	170		43	142	23.24	76.76
8	16	9	1	11	185	25.31	171		159	26	85.95	14.05
8	23	9	1	12	185	25.31	172		165	20	89.19	10.81
7	17	9	6	14	184	25.17	173		100	84	54.35	45.65

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	20	9	2	15	184	25.17	174		83	101	45.11	54.89
7	24	9	6	15	184	25.17	175		93	91	50.54	49.46
8	16	9	1	18	184	25.17	176		23	161	12.5	87.5
5	31	9	1	14	183	25.03	177		98	85	53.55	46.45
7	5	9	1	13	183	25.03	178		158	25	86.34	13.66
7	24	9	6	14	183	25.03	179		115	68	62.84	37.16
8	8	9	7	14	183	25.03	180		124	59	67.76	32.24
8	22	9	7	18	183	25.03	181	731	24	159	13.11	86.89
9	26	9	7	16	183	25.03	182		68	115	37.16	62.84
5	18	9	2	12	182	24.9	183		162	20	89.01	10.99
5	31	9	1	13	182	24.9	184		144	38	79.12	20.88
8	5	9	4	15	182	24.9	185		76	106	41.76	58.24
8	17	9	2	13	182	24.9	186		137	45	75.27	24.73
7	4	9	7	13	181	24.76	187		139	42	76.8	23.2
7	16	9	5	16	181	24.76	188		46	135	25.41	74.59
7	25	9	7	11	181	24.76	189		163	18	90.06	9.94
8	23	9	1	13	181	24.76	190		158	23	87.29	12.71
9	26	9	7	17	181	24.76	191		30	151	16.57	83.43
5	16	9	7	12	180	24.62	192		164	16	91.11	8.89
7	2	9	5	15	180	24.62	193		74	106	41.11	58.89
9	26	9	7	13	180	24.62	194		146	34	81.11	18.89
9	13	9	1	15	179	24.49	195		80	99	44.69	55.31
5	16	9	7	14	178	24.35	196		113	65	63.48	36.52
6	28	9	1	18	178	24.35	197		27	151	15.17	84.83
7	10	9	6	13	178	24.35	198		138	40	77.53	22.47
8	24	9	2	15	178	24.35	199		85	93	47.75	52.25
5	30	9	7	17	177	24.21	200		42	135	23.73	76.27

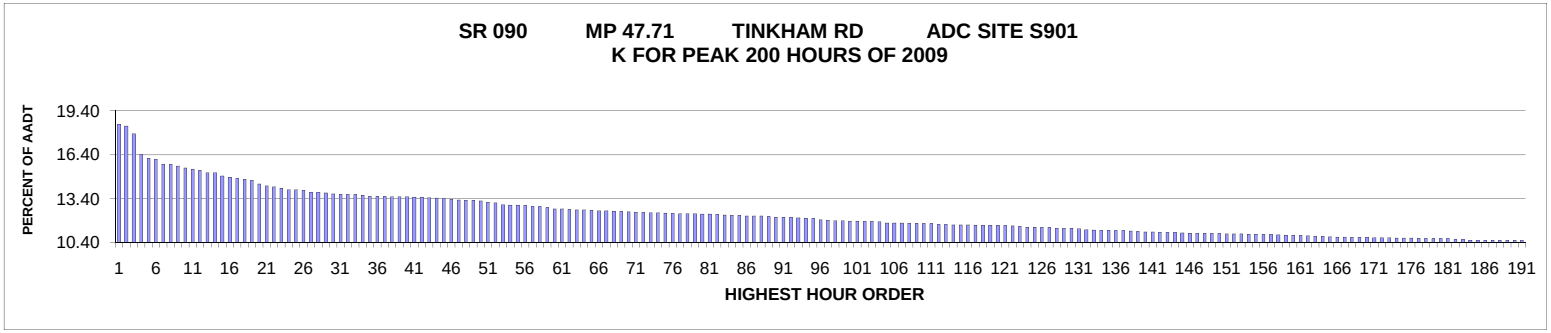

AADT= 30170 **K 30 FACTOR=** 13.72 **K 100 FACTOR=** 12.12 **K 200 FACTOR=** 10.54 **D FACTOR=** 61.78

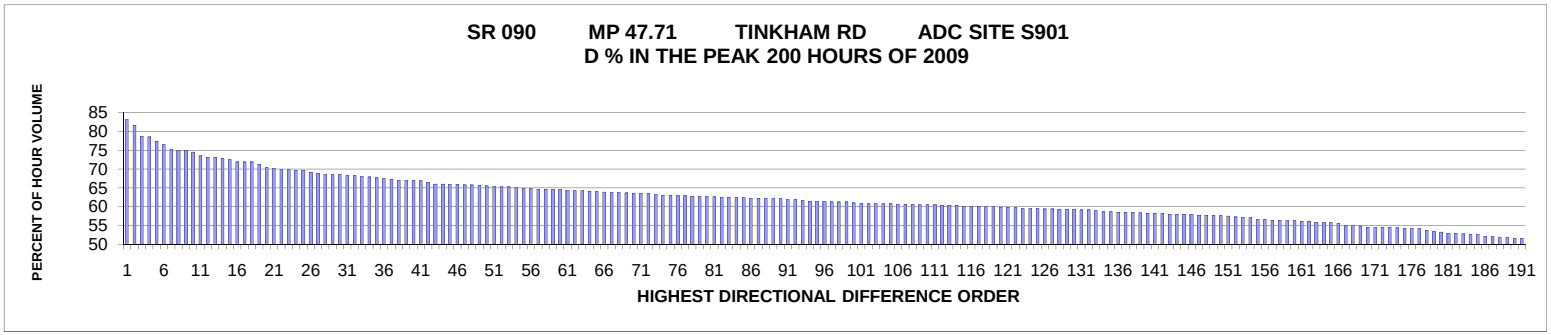

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
11	29	9	1	15	5580	18.50	1	30170	2639	2941	47.29	52.71
11	29	9	1	16	5535	18.35	2		2340	3195	42.28	57.72
11	29	9	1	14	5379	17.83	3		2805	2574	52.15	47.85
8	9	9	1	14	4951	16.41	4		1851	3100	37.39	62.61
11	25	9	4	16	4876	16.16	5		2641	2235	54.16	45.84
12	27	9	1	16	4852	16.08	6		1472	3380	30.34	69.66
11	29	9	1	17	4752	15.75	7		1689	3063	35.54	64.46
11	25	9	4	15	4749	15.74	8		2686	2063	56.56	43.44
11	29	9	1	13	4714	15.62	9		2647	2067	56.15	43.85
8	9	9	1	15	4677	15.50	10		1745	2932	37.31	62.69
8	23	9	1	15	4648	15.41	11		1757	2891	37.80	62.20
8	23	9	1	16	4621	15.32	12		1816	2805	39.30	60.70
12	27	9	1	15	4578	15.17	13		1736	2842	37.92	62.08
8	9	9	1	16	4576	15.17	14		1621	2955	35.42	64.58
8	23	9	1	14	4509	14.95	15		1907	2602	42.29	57.71
8	9	9	1	13	4482	14.86	16		1789	2693	39.92	60.08
8	9	9	1	17	4455	14.77	17		1617	2838	36.30	63.70

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
11	25	9	4	14	4444	14.73	18		2418	2026	54.41	45.59
12	27	9	1	14	4416	14.64	19		1989	2427	45.04	54.96
11	25	9	4	17	4341	14.39	20		2447	1894	56.37	43.63
10	11	9	1	18	4303	14.26	21	30170	1662	2641	38.62	61.38
8	7	9	6	15	4287	14.21	22		2508	1779	58.50	41.50
8	7	9	6	14	4259	14.12	23		2479	1780	58.21	41.79
8	23	9	1	19	4226	14.01	24		1151	3075	27.24	72.76
11	29	9	1	12	4223	14.00	25		2631	1592	62.30	37.70
8	2	9	1	16	4216	13.97	26		1520	2696	36.05	63.95
8	9	9	1	12	4173	13.83	27		2004	2169	48.02	51.98
12	27	9	1	17	4165	13.81	28		1146	3019	27.52	72.48
8	9	9	1	18	4158	13.78	29		1560	2598	37.52	62.48
4	3	9	6	15	4140	13.72	30		2733	1407	66.01	33.99
4	26	9	1	17	4136	13.71	31		1234	2902	29.84	70.16
3	29	9	1	16	4127	13.68	32		1600	2527	38.77	61.23
8	21	9	6	16	4126	13.68	33		2332	1794	56.52	43.48
8	7	9	6	16	4114	13.64	34		2484	1630	60.38	39.62
4	19	9	1	17	4089	13.55	35		1446	2643	35.36	64.64
8	2	9	1	15	4086	13.54	36		1492	2594	36.51	63.49
8	23	9	1	13	4086	13.54	37		1907	2179	46.67	53.33
1	4	9	1	15	4082	13.53	38		1173	2909	28.74	71.26
8	2	9	1	17	4082	13.53	39		1523	2559	37.31	62.69
8	7	9	6	17	4080	13.52	40		2410	1670	59.07	40.93
12	27	9	1	13	4074	13.50	41	30170	2291	1783	56.23	43.77
3	1	9	1	16	4073	13.50	42		1310	2763	32.16	67.84
3	29	9	1	15	4060	13.46	43		1693	2367	41.70	58.30
12	26	9	7	13	4051	13.43	44		2533	1518	62.53	37.47
12	26	9	7	15	4041	13.39	45		1771	2270	43.83	56.17
8	23	9	1	18	4030	13.36	46		1403	2627	34.81	65.19
2	8	9	1	16	4015	13.31	47		1191	2824	29.66	70.34
3	29	9	1	17	4009	13.29	48		1379	2630	34.40	65.60
12	26	9	7	14	4008	13.28	49		2177	1831	54.32	45.68
8	7	9	6	13	3998	13.25	50		2375	1623	59.40	40.60
4	4	9	7	19	3967	13.15	51		671	3296	16.91	83.09
2	16	9	2	16	3954	13.11	52		1578	2376	39.91	60.09
4	26	9	1	16	3917	12.98	53		1334	2583	34.06	65.94
8	2	9	1	14	3911	12.96	54		1594	2317	40.76	59.24
3	22	9	1	16	3908	12.95	55		1544	2364	39.51	60.49
12	26	9	7	16	3905	12.94	56		1307	2598	33.47	66.53
10	11	9	1	16	3877	12.85	57		1438	2439	37.09	62.91
10	25	9	1	16	3873	12.84	58		1388	2485	35.84	64.16
3	22	9	1	15	3860	12.79	59		1770	2090	45.85	54.15
8	21	9	6	18	3833	12.70	60		2431	1402	63.42	36.58
11	15	9	1	16	3829	12.69	61	30170	1268	2561	33.12	66.88
3	29	9	1	14	3816	12.65	62		1807	2009	47.35	52.65
4	5	9	1	19	3809	12.63	63		1149	2660	30.17	69.83
10	25	9	1	17	3806	12.62	64		1333	2473	35.02	64.98
3	1	9	1	17	3800	12.60	65		1255	2545	33.03	66.97
11	28	9	7	14	3791	12.57	66		1597	2194	42.13	57.87
4	19	9	1	16	3788	12.56	67		1407	2381	37.14	62.86
10	11	9	1	19	3779	12.53	68		1314	2465	34.77	65.23
3	22	9	1	17	3776	12.52	69		1293	2483	34.24	65.76

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
4	5	9	1	18	3767	12.49	70		1387	2380	36.82	63.18
8	7	9	6	18	3764	12.48	71		2257	1507	59.96	40.04
11	28	9	7	15	3756	12.45	72		1406	2350	37.43	62.57
2	16	9	2	15	3754	12.44	73		1670	2084	44.49	55.51
2	8	9	1	17	3752	12.44	74		1055	2697	28.12	71.88
8	21	9	6	15	3743	12.41	75		2223	1520	59.39	40.61
8	8	9	7	12	3734	12.38	76		2307	1427	61.78	38.22
1	25	9	1	16	3733	12.37	77		1052	2681	28.18	71.82
8	23	9	1	12	3732	12.37	78		1915	1817	51.31	48.69
8	2	9	1	18	3728	12.36	79		1312	2416	35.19	64.81
4	19	9	1	18	3724	12.34	80		1333	2391	35.79	64.21
8	7	9	6	12	3723	12.34	81	30170	2284	1439	61.35	38.65
12	26	9	7	12	3716	12.32	82		2534	1182	68.19	31.81
4	26	9	1	18	3702	12.27	83		1119	2583	30.23	69.77
8	2	9	1	13	3700	12.26	84		1712	1988	46.27	53.73
8	23	9	1	20	3698	12.26	85		992	2706	26.83	73.17
1	4	9	1	16	3688	12.22	86		941	2747	25.52	74.48
8	28	9	6	17	3688	12.22	87		2192	1496	59.44	40.56
10	11	9	1	15	3688	12.22	88		1448	2240	39.26	60.74
1	18	9	1	16	3670	12.16	89		910	2760	24.80	75.20
8	9	9	1	11	3657	12.12	90		1990	1667	54.42	45.58
2	16	9	2	14	3656	12.12	91		1781	1875	48.71	51.29
10	25	9	1	15	3655	12.11	92		1385	2270	37.89	62.11
8	28	9	6	16	3647	12.09	93		2177	1470	59.69	40.31
2	16	9	2	17	3637	12.06	94		1457	2180	40.06	59.94
4	12	9	1	18	3631	12.04	95		1395	2236	38.42	61.58
8	21	9	6	14	3609	11.96	96		2181	1428	60.43	39.57
8	9	9	1	20	3596	11.92	97		1011	2585	28.11	71.89
8	23	9	1	17	3588	11.89	98		1734	1854	48.33	51.67
12	27	9	1	12	3587	11.89	99		2301	1286	64.15	35.85
11	28	9	7	16	3580	11.87	100		1159	2421	32.37	67.63
8	8	9	7	11	3579	11.86	101	30170	2472	1107	69.07	30.93
2	15	9	1	16	3572	11.84	102		1169	2403	32.73	67.27
4	26	9	1	15	3569	11.83	103		1364	2205	38.22	61.78
2	13	9	6	17	3567	11.82	104		2074	1493	58.14	41.86
3	29	9	1	13	3543	11.74	105		1887	1656	53.26	46.74
8	1	9	7	12	3541	11.74	106		2054	1487	58.01	41.99
8	2	9	1	12	3540	11.73	107		1791	1749	50.59	49.41
4	3	9	6	13	3537	11.72	108		2332	1205	65.93	34.07
11	8	9	1	16	3530	11.70	109		1437	2093	40.71	59.29
3	29	9	1	18	3524	11.68	110		1148	2376	32.58	67.42
8	9	9	1	19	3523	11.68	111		1274	2249	36.16	63.84
8	28	9	6	15	3507	11.62	112		2003	1504	57.11	42.89
8	8	9	7	13	3505	11.62	113		1951	1554	55.66	44.34
8	22	9	7	12	3501	11.60	114		2133	1368	60.93	39.07
10	11	9	1	17	3498	11.59	115		1488	2010	42.54	57.46
8	21	9	6	17	3496	11.59	116		2047	1449	58.55	41.45
4	19	9	1	15	3494	11.58	117		1402	2092	40.13	59.87
4	12	9	1	17	3490	11.57	118		1371	2119	39.28	60.72
11	28	9	7	13	3490	11.57	119		1804	1686	51.69	48.31
3	22	9	1	14	3487	11.56	120		1718	1769	49.27	50.73
8	28	9	6	18	3484	11.55	121	30170	2083	1401	59.79	40.21

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
4	3	9	6	16	3482	11.54	122		2052	1430	58.93	41.07
10	4	9	1	16	3469	11.50	123		1367	2102	39.41	60.59
4	5	9	1	20	3451	11.44	124		863	2588	25.01	74.99
11	8	9	1	15	3451	11.44	125		1481	1970	42.92	57.08
11	25	9	4	13	3445	11.42	126		1930	1515	56.02	43.98
10	4	9	1	17	3444	11.42	127		1361	2083	39.52	60.48
1	4	9	1	14	3436	11.39	128		1300	2136	37.83	62.17
4	12	9	1	19	3434	11.38	129		1297	2137	37.77	62.23
10	25	9	1	18	3433	11.38	130		1176	2257	34.26	65.74
3	1	9	1	15	3417	11.33	131		1346	2071	39.39	60.61
11	28	9	7	12	3403	11.28	132		1981	1422	58.21	41.79
8	9	9	1	21	3394	11.25	133		800	2594	23.57	76.43
11	29	9	1	18	3388	11.23	134		1203	2185	35.51	64.49
8	22	9	7	11	3384	11.22	135		2192	1192	64.78	35.22
2	13	9	6	18	3380	11.20	136		1979	1401	58.55	41.45
3	13	9	6	17	3379	11.20	137		1690	1689	50.01	49.99
8	1	9	7	11	3375	11.19	138		2065	1310	61.19	38.81
1	25	9	1	17	3358	11.13	139		901	2457	26.83	73.17
3	8	9	1	15	3356	11.12	140		1160	2196	34.56	65.44
8	21	9	6	12	3354	11.12	141	30170	2112	1242	62.97	37.03
12	30	9	4	16	3349	11.10	142		1319	2030	39.38	60.62
1	18	9	1	17	3344	11.08	143		836	2508	25.00	75.00
8	2	9	1	19	3340	11.07	144		1140	2200	34.13	65.87
4	24	9	6	17	3337	11.06	145		2046	1291	61.31	38.69
2	8	9	1	15	3329	11.03	146		1214	2115	36.47	63.53
11	22	9	1	16	3328	11.03	147		1050	2278	31.55	68.45
3	8	9	1	18	3327	11.03	148		611	2716	18.36	81.64
10	4	9	1	18	3321	11.01	149		1304	2017	39.27	60.73
11	8	9	1	17	3318	11.00	150		1319	1999	39.75	60.25
8	21	9	6	13	3316	10.99	151		2015	1301	60.77	39.23
2	21	9	7	18	3315	10.99	152		750	2565	22.62	77.38
10	4	9	1	15	3314	10.98	153		1347	1967	40.65	59.35
2	15	9	1	17	3310	10.97	154		1006	2304	30.39	69.61
2	13	9	6	16	3306	10.96	155		1739	1567	52.60	47.40
3	22	9	1	18	3304	10.95	156		1097	2207	33.20	66.80
11	25	9	4	18	3302	10.94	157		1788	1514	54.15	45.85
8	23	9	1	21	3294	10.92	158		708	2586	21.49	78.51
1	3	9	7	17	3291	10.91	159		874	2417	26.56	73.44
12	26	9	7	17	3291	10.91	160		1027	2264	31.21	68.79
8	28	9	6	14	3283	10.88	161	30170	1889	1394	57.54	42.46
10	11	9	1	14	3275	10.86	162		1332	1943	40.67	59.33
1	2	9	6	12	3269	10.84	163		2078	1191	63.57	36.43
8	7	9	6	19	3268	10.83	164		1974	1294	60.40	39.60
8	29	9	7	12	3251	10.78	165		2070	1181	63.67	36.33
8	7	9	6	11	3250	10.77	166		2123	1127	65.32	34.68
4	3	9	6	12	3249	10.77	167		2216	1033	68.21	31.79
11	27	9	6	12	3243	10.75	168		2170	1073	66.91	33.09
3	8	9	1	14	3240	10.74	169		1325	1915	40.90	59.10
11	15	9	1	17	3239	10.74	170		1020	2219	31.49	68.51
8	8	9	7	14	3238	10.73	171		1629	1609	50.31	49.69
8	1	9	7	13	3235	10.72	172		1712	1523	52.92	47.08
12	24	9	5	14	3235	10.72	173		1777	1458	54.93	45.07

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
2	27	9	6	17	3231	10.71	174		1805	1426	55.87	44.13
3	13	9	6	18	3229	10.70	175		1654	1575	51.22	48.78
4	3	9	6	17	3229	10.70	176		1942	1287	60.14	39.86
4	12	9	1	16	3225	10.69	177		1361	1864	42.20	57.80
11	27	9	6	14	3220	10.67	178		1659	1561	51.52	48.48
11	27	9	6	13	3216	10.66	179		1864	1352	57.96	42.04
8	22	9	7	13	3215	10.66	180		1840	1375	57.23	42.77
1	25	9	1	15	3214	10.65	181	30170	1152	2062	35.84	64.16
4	24	9	6	18	3196	10.59	182		1956	1240	61.20	38.80
1	18	9	1	15	3195	10.59	183		1007	2188	31.52	68.48
4	10	9	6	17	3187	10.56	184		1684	1503	52.84	47.16
4	17	9	6	17	3186	10.56	185		1864	1322	58.51	41.49
11	27	9	6	15	3184	10.55	186		1448	1736	45.48	54.52
3	6	9	6	17	3183	10.55	187		1793	1390	56.33	43.67
4	19	9	1	14	3183	10.55	188		1452	1731	45.62	54.38
2	15	9	1	15	3181	10.54	189		1196	1985	37.60	62.40
3	13	9	6	16	3181	10.54	190		1590	1591	49.98	50.02
12	23	9	4	15	3181	10.54	191		1543	1638	48.51	51.49
8	21	9	6	19	3174	10.52	192		1856	1318	58.48	41.52

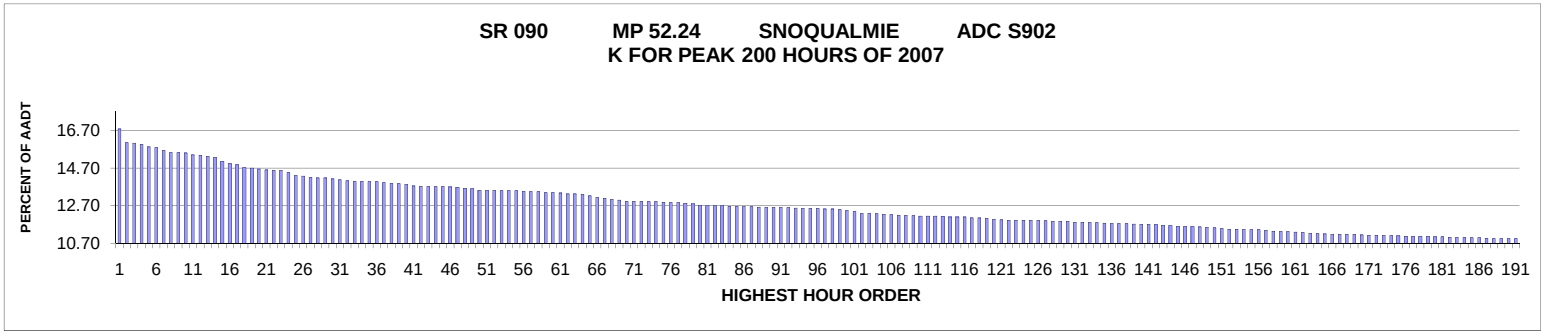

AADT= 27535 **K 30 FACTOR=** 14.12 **K 100 FACTOR=** 12.61 **K 200 FACTOR=** 10.93 **D FACTOR=** 62.16

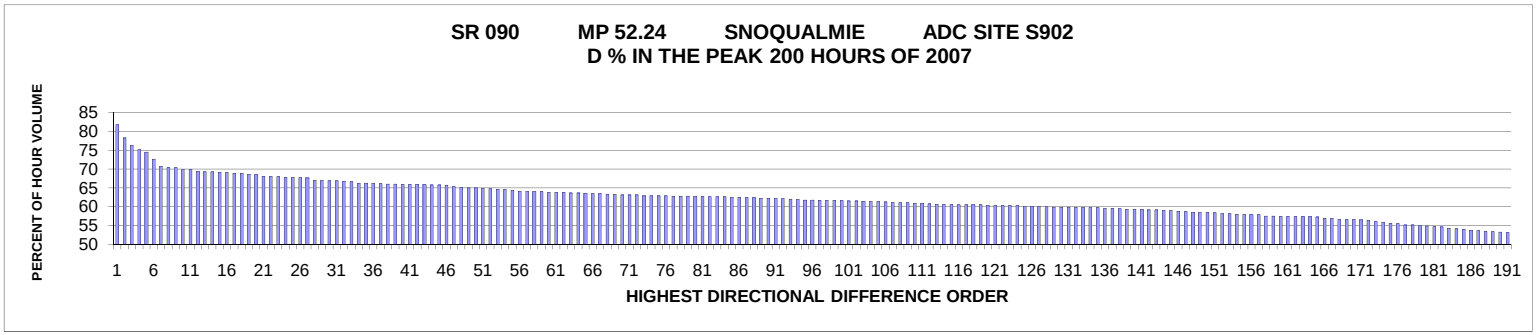

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	5	9	1	14	4621	16.78	1	27535	1718	2903	37.18	62.82
6	21	9	1	16	4417	16.04	2		1545	2872	34.98	65.02
7	12	9	1	15	4413	16.03	3		1510	2903	34.22	65.78
7	26	9	1	16	4391	15.95	4		1633	2758	37.19	62.81
7	12	9	1	17	4355	15.82	5		1438	2917	33.02	66.98
6	28	9	1	16	4349	15.79	6		1364	2985	31.36	68.64
7	12	9	1	16	4303	15.63	7		1426	2877	33.14	66.86
7	12	9	1	14	4273	15.52	8		1588	2685	37.16	62.84
7	26	9	1	15	4270	15.51	9		1648	2622	38.59	61.41
6	21	9	1	17	4268	15.50	10		1454	2814	34.07	65.93
7	26	9	1	17	4240	15.40	11		1430	2810	33.73	66.27
7	5	9	1	15	4232	15.37	12		1539	2693	36.37	63.63
7	5	9	1	16	4217	15.32	13		1574	2643	37.33	62.67
7	5	9	1	13	4202	15.26	14		1571	2631	37.39	62.61
7	5	9	1	17	4143	15.05	15		1477	2666	35.65	64.35
7	26	9	1	18	4112	14.93	16		1360	2752	33.07	66.93
6	28	9	1	15	4091	14.86	17		1388	2703	33.93	66.07

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	26	9	1	14	4053	14.72	18		1640	2413	40.46	59.54
6	28	9	1	17	4044	14.69	19		1252	2792	30.96	69.04
6	21	9	1	15	4030	14.64	20		1382	2648	34.29	65.71
7	3	9	6	12	4020	14.60	21	27535	2734	1286	68.01	31.99
6	21	9	1	18	4013	14.57	22		1354	2659	33.74	66.26
7	5	9	1	18	4013	14.57	23		1234	2779	30.75	69.25
6	14	9	1	17	3980	14.45	24		1331	2649	33.44	66.56
6	21	9	1	14	3940	14.31	25		1491	2449	37.84	62.16
7	12	9	1	18	3930	14.27	26		1484	2446	37.76	62.24
7	19	9	1	19	3913	14.21	27		1180	2733	30.16	69.84
6	14	9	1	18	3903	14.17	28		1178	2725	30.18	69.82
7	26	9	1	19	3901	14.17	29		1247	2654	31.97	68.03
7	19	9	1	14	3889	14.12	30		1536	2353	39.50	60.50
7	19	9	1	15	3872	14.06	31		1620	2252	41.84	58.16
6	28	9	1	14	3858	14.01	32		1397	2461	36.21	63.79
7	12	9	1	13	3849	13.98	33		1437	2412	37.33	62.67
7	17	9	6	16	3849	13.98	34		2151	1698	55.88	44.12
6	26	9	6	16	3846	13.97	35		2416	1430	62.82	37.18
7	3	9	6	14	3843	13.96	36		2293	1550	59.67	40.33
7	19	9	1	16	3833	13.92	37		1594	2239	41.59	58.41
6	26	9	6	15	3821	13.88	38		2377	1444	62.21	37.79
7	24	9	6	15	3818	13.87	39		2159	1659	56.55	43.45
7	26	9	1	13	3805	13.82	40		1727	2078	45.39	54.61
6	26	9	6	14	3787	13.75	41	27535	2360	1427	62.32	37.68
7	12	9	1	12	3781	13.73	42		1530	2251	40.47	59.53
7	19	9	1	13	3776	13.71	43		1540	2236	40.78	59.22
6	28	9	1	18	3774	13.71	44		1160	2614	30.74	69.26
7	24	9	6	16	3774	13.71	45		2146	1628	56.86	43.14
6	14	9	1	16	3773	13.70	46		1394	2379	36.95	63.05
6	7	9	1	17	3767	13.68	47		1188	2579	31.54	68.46
7	19	9	1	18	3749	13.62	48		1276	2473	34.04	65.96
7	17	9	6	15	3743	13.59	49		2076	1667	55.46	44.54
6	26	9	6	17	3718	13.50	50		2253	1465	60.60	39.40
6	21	9	1	19	3717	13.50	51		1353	2364	36.40	63.60
7	12	9	1	19	3717	13.50	52		1267	2450	34.09	65.91
6	19	9	6	15	3714	13.49	53		2244	1470	60.42	39.58
6	14	9	1	15	3712	13.48	54		1300	2412	35.02	64.98
7	24	9	6	17	3711	13.48	55		2222	1489	59.88	40.12
7	19	9	1	17	3704	13.45	56		1368	2336	36.93	63.07
7	10	9	6	15	3702	13.44	57		2001	1701	54.05	45.95
7	5	9	1	12	3700	13.44	58		1420	2280	38.38	61.62
4	26	9	1	16	3688	13.39	59		1245	2443	33.76	66.24
4	19	9	1	17	3684	13.38	60		1335	2349	36.24	63.76
6	19	9	6	16	3681	13.37	61	27535	2310	1371	62.75	37.25
4	26	9	1	17	3665	13.31	62		1183	2482	32.28	67.72
3	29	9	1	16	3664	13.31	63		1463	2201	39.93	60.07
6	19	9	6	17	3662	13.30	64		2379	1283	64.96	35.04
6	7	9	1	16	3641	13.22	65		1134	2507	31.15	68.85
7	17	9	6	17	3615	13.13	66		2208	1407	61.08	38.92
6	28	9	1	13	3607	13.10	67		1539	2068	42.67	57.33
6	26	9	6	13	3589	13.03	68		2290	1299	63.81	36.19
7	31	9	6	16	3576	12.99	69		2067	1509	57.80	42.20

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
3	29	9	1	15	3561	12.93	70		1473	2088	41.36	58.64
7	2	9	5	15	3561	12.93	71		2188	1373	61.44	38.56
7	17	9	6	14	3560	12.93	72		1953	1607	54.86	45.14
7	3	9	6	13	3556	12.91	73		2142	1414	60.24	39.76
6	19	9	6	18	3555	12.91	74		2225	1330	62.59	37.41
6	12	9	6	16	3543	12.87	75		2031	1512	57.32	42.68
7	31	9	6	17	3541	12.86	76		2126	1415	60.04	39.96
6	28	9	1	19	3540	12.86	77		1051	2489	29.69	70.31
4	12	9	1	18	3533	12.83	78		1353	2180	38.30	61.70
6	12	9	6	17	3523	12.79	79		2172	1351	61.65	38.35
7	24	9	6	14	3502	12.72	80		1867	1635	53.31	46.69
6	12	9	6	15	3501	12.71	81	27535	1963	1538	56.07	43.93
7	2	9	5	17	3498	12.70	82		2263	1235	64.69	35.31
7	2	9	5	16	3497	12.70	83		2164	1333	61.88	38.12
6	21	9	1	13	3484	12.65	84		1448	2036	41.56	58.44
7	19	9	1	12	3483	12.65	85		1514	1969	43.47	56.53
3	22	9	1	16	3477	12.63	86		1424	2053	40.95	59.05
6	14	9	1	14	3477	12.63	87		1380	2097	39.69	60.31
4	26	9	1	18	3476	12.62	88		1073	2403	30.87	69.13
4	19	9	1	16	3473	12.61	89		1318	2155	37.95	62.05
6	7	9	1	18	3472	12.61	90		1182	2290	34.04	65.96
7	10	9	6	16	3471	12.61	91		1926	1545	55.49	44.51
6	7	9	1	15	3468	12.59	92		1154	2314	33.28	66.72
7	26	9	1	12	3462	12.57	93		1688	1774	48.76	51.24
3	29	9	1	17	3459	12.56	94		1181	2278	34.14	65.86
4	19	9	1	18	3456	12.55	95		1246	2210	36.05	63.95
7	2	9	5	18	3456	12.55	96		2193	1263	63.45	36.55
7	10	9	6	17	3447	12.52	97		2036	1411	59.07	40.93
2	16	9	2	16	3445	12.51	98		1454	1991	42.21	57.79
7	10	9	6	14	3440	12.49	99		1832	1608	53.26	46.74
7	3	9	6	11	3423	12.43	100		2368	1055	69.18	30.82
6	19	9	6	14	3408	12.38	101	27535	2063	1345	60.53	39.47
6	26	9	6	12	3381	12.28	102		2296	1085	67.91	32.09
4	12	9	1	19	3380	12.28	103		1303	2077	38.55	61.45
6	26	9	6	18	3378	12.27	104		2119	1259	62.73	37.27
3	22	9	1	15	3369	12.24	105		1609	1760	47.76	52.24
6	14	9	1	13	3361	12.21	106		1449	1912	43.11	56.89
4	4	9	7	19	3358	12.20	107		613	2745	18.25	81.75
2	16	9	2	15	3355	12.18	108		1513	1842	45.10	54.90
7	17	9	6	18	3347	12.16	109		2042	1305	61.01	38.99
3	22	9	1	17	3344	12.14	110		1202	2142	35.94	64.06
7	24	9	6	18	3343	12.14	111		2016	1327	60.31	39.69
4	12	9	1	17	3342	12.14	112		1321	2021	39.53	60.47
6	28	9	1	12	3341	12.13	113		1603	1738	47.98	52.02
7	19	9	1	20	3332	12.10	114		976	2356	29.29	70.71
6	12	9	6	18	3331	12.10	115		2040	1291	61.24	38.76
6	12	9	6	14	3330	12.09	116		1785	1545	53.60	46.40
4	3	9	6	16	3319	12.05	117		2073	1246	62.46	37.54
7	5	9	1	19	3319	12.05	118		1140	2179	34.35	65.65
7	2	9	5	19	3313	12.03	119		2100	1213	63.39	36.61
7	24	9	6	13	3299	11.98	120		1816	1483	55.05	44.95
7	31	9	6	15	3289	11.94	121	27535	1767	1522	53.72	46.28

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
7	11	9	7	15	3286	11.93	122		1883	1403	57.30	42.70
7	31	9	6	18	3284	11.93	123		2005	1279	61.05	38.95
7	2	9	5	14	3282	11.92	124		1982	1300	60.39	39.61
7	17	9	6	19	3281	11.92	125		1928	1353	58.76	41.24
7	10	9	6	18	3279	11.91	126		1956	1323	59.65	40.35
6	28	9	1	20	3273	11.89	127		835	2438	25.51	74.49
1	4	9	1	15	3272	11.88	128		970	2302	29.65	70.35
7	11	9	7	12	3270	11.88	129		2076	1194	63.49	36.51
7	3	9	6	15	3268	11.87	130		1799	1469	55.05	44.95
6	21	9	1	12	3255	11.82	131		1527	1728	46.91	53.09
7	17	9	6	13	3254	11.82	132		1888	1366	58.02	41.98
3	1	9	1	16	3250	11.80	133		1216	2034	37.42	62.58
2	13	9	6	17	3245	11.79	134		1832	1413	56.46	43.54
4	26	9	1	15	3242	11.77	135		1232	2010	38.00	62.00
6	5	9	6	17	3235	11.75	136		1964	1271	60.71	39.29
6	5	9	6	16	3233	11.74	137		1920	1313	59.39	40.61
7	25	9	7	12	3229	11.73	138		1854	1375	57.42	42.58
7	11	9	7	14	3226	11.72	139		1912	1314	59.27	40.73
2	16	9	2	14	3221	11.70	140		1571	1650	48.77	51.23
3	29	9	1	14	3221	11.70	141	27535	1502	1719	46.63	53.37
7	19	9	1	21	3218	11.69	142		803	2415	24.95	75.05
7	31	9	6	14	3208	11.65	143		1741	1467	54.27	45.73
7	25	9	7	11	3204	11.64	144		1976	1228	61.67	38.33
7	11	9	7	16	3195	11.60	145		1833	1362	57.37	42.63
3	1	9	1	17	3190	11.59	146		1196	1994	37.49	62.51
6	7	9	1	19	3190	11.59	147		1145	2045	35.89	64.11
4	3	9	6	15	3184	11.56	148		1905	1279	59.83	40.17
6	14	9	1	19	3177	11.54	149		1147	2030	36.10	63.90
7	24	9	6	12	3171	11.52	150		1837	1334	57.93	42.07
7	24	9	6	19	3162	11.48	151		1864	1298	58.95	41.05
6	7	9	1	14	3154	11.45	152		1116	2038	35.38	64.62
7	31	9	6	19	3150	11.44	153		1841	1309	58.44	41.56
4	19	9	1	15	3146	11.43	154		1262	1884	40.11	59.89
2	22	9	1	16	3142	11.41	155		1289	1853	41.02	58.98
4	5	9	1	19	3142	11.41	156		978	2164	31.13	68.87
4	3	9	6	13	3140	11.40	157		2051	1089	65.32	34.68
6	5	9	6	18	3124	11.35	158		1961	1163	62.77	37.23
7	18	9	7	12	3121	11.33	159		1901	1220	60.91	39.09
7	11	9	7	11	3115	11.31	160		2018	1097	64.78	35.22
6	5	9	6	15	3109	11.29	161	27535	1758	1351	56.55	43.45
4	24	9	6	17	3107	11.28	162		1854	1253	59.67	40.33
6	19	9	6	19	3092	11.23	163		1852	1240	59.90	40.10
6	19	9	6	13	3083	11.20	164		1844	1239	59.81	40.19
1	4	9	1	16	3080	11.19	165		842	2238	27.34	72.66
7	2	9	5	13	3078	11.18	166		1824	1254	59.26	40.74
7	17	9	6	12	3078	11.18	167		1795	1283	58.32	41.68
7	11	9	7	13	3077	11.17	168		1860	1217	60.45	39.55
7	10	9	6	13	3075	11.17	169		1787	1288	58.11	41.89
7	31	9	6	13	3067	11.14	170		1676	1391	54.65	45.35
2	8	9	1	16	3063	11.12	171		1086	1977	35.46	64.54
3	29	9	1	18	3062	11.12	172		1017	2045	33.21	66.79
7	6	9	2	15	3062	11.12	173		1130	1932	36.90	63.10

MO	DY	YR	DAY OF WK	HR	HR VOL	PERCENT OF AADT	HOUR NUMBER	AADT	EAST VOLUME	WEST VOLUME	PERCENT EAST IS OF TOTAL VOLUME	PERCENT WEST IS OF TOTAL VOLUME
4	12	9	1	16	3060	11.11	174		1302	1758	42.55	57.45
4	24	9	6	18	3055	11.09	175		1860	1195	60.88	39.12
2	8	9	1	17	3050	11.08	176		984	2066	32.26	67.74
3	13	9	6	17	3046	11.06	177		1519	1527	49.87	50.13
7	31	9	6	12	3043	11.05	178		1828	1215	60.07	39.93
7	26	9	1	11	3042	11.05	179		1521	1521	50.00	50.00
7	10	9	6	12	3041	11.04	180		1834	1207	60.31	39.69
6	20	9	7	12	3038	11.03	181	27535	1862	1176	61.29	38.71
7	12	9	1	11	3035	11.02	182		1299	1736	42.80	57.20
4	17	9	6	17	3032	11.01	183		1743	1289	57.49	42.51
6	21	9	1	20	3032	11.01	184		982	2050	32.39	67.61
2	16	9	2	17	3027	10.99	185		1322	1705	43.67	56.33
7	10	9	6	19	3026	10.99	186		1867	1159	61.70	38.30
6	12	9	6	13	3019	10.96	187		1629	1390	53.96	46.04
3	29	9	1	13	3013	10.94	188		1521	1492	50.48	49.52
2	22	9	1	17	3012	10.94	189		1133	1879	37.62	62.38
7	18	9	7	11	3011	10.94	190		1821	1190	60.48	39.52
6	28	9	1	21	3009	10.93	191		656	2353	21.80	78.20
6	12	9	6	19	3007	10.92	192		1847	1160	61.42	38.58
3	22	9	1	14	3004	10.91	193		1480	1524	49.27	50.73

GLOSSARY

ADC…….**Automated Data Collection**

ADT……..…**Average Daily Traffic**
(An average 24-hours of traffic volumes at a given location for some period of time less than a year. An ADT may be measured for six months, a season, a month, a week, or as little as two days. An ADT is a valid number for only the period over which it was measured.)

AADT……..**Annual Average Daily Traffic**
(The average 24-hour traffic volume at a given location over a full 365-day year—that is, the total number of vehicles passing the site in a year divided by 365.)

PEAK HOUR……...Highest recorded volume hours for the year

K FACTOR……..…The proportion of daily traffic occurring during the peak hour
(Expressed as a decimal)

K 30 FACTOR……..The proportion of daily traffic occurring during the 30th peak hour
(Expressed as decimal)

K 50 FACTOR……..…The proportion of daily traffic occurring during the 50th peak hour
(Expressed as a decimal)

K 100 FACTOR……...The proportion of daily traffic occurring during the 100th peak hour
(Expressed as a decimal)

K 200 FACTOR……...The proportion of daily traffic occurring during the 200th peak hour
(Expressed as a decimal)

D FACTOR……The proportion of peak-hour traffic traveling in the peak direction
(Expressed as a decimal)

DDHV……....Directional design hour volume
