


Resource:

Wilder-Paving

1-08.5 SS “Time for Completion”
 2006-”An unworkable day is defined as.....
that prevents satisfactory and timely performance of the work, and such performance, if not hindered, would have otherwise progressed toward physical completion of the work.”

2008-”An unworkable day is defined as....
that prevents satisfactory and timely performance of the Work shown on the critical path of the Contractor’s approved progress schedule.”

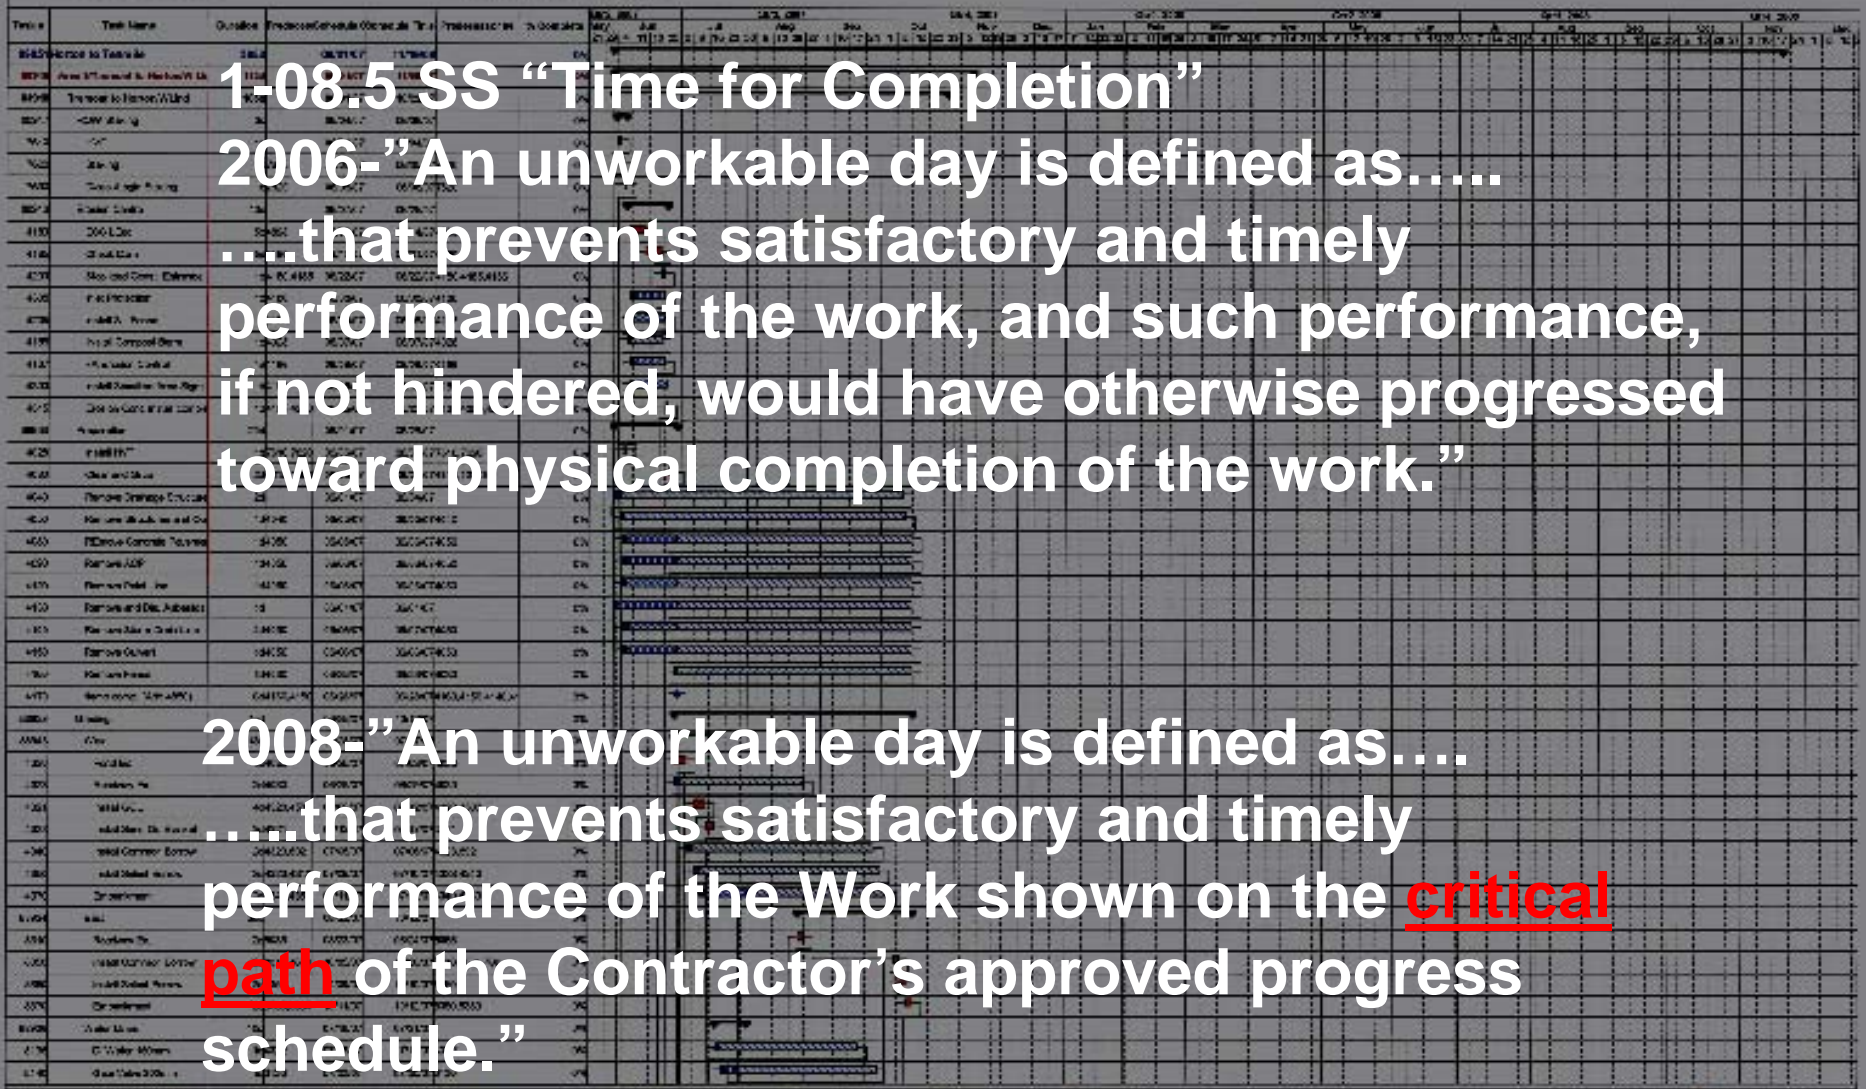

Default	Complete	Complete Milestone	Remaining	Remaining Milestone	Free Float	Total Float (L)	Total Float (R)	Delay	Non-Resource	Exclude 1	Required Date
Critical	Remaining	Remaining Milestone	Remaining	Remaining Milestone							
Parent	Complete	Complete Milestone	Remaining	Remaining Milestone							


Resource:

Wilder-Paving

1-08.5 SS "Time for Completion"

2006-"The days between December 25 and January 1 will be classified as nonworking days, provided that, the Contractor actually suspends work on the project."

2008-"The days between December 25 and January 1 will be classified as non working days."

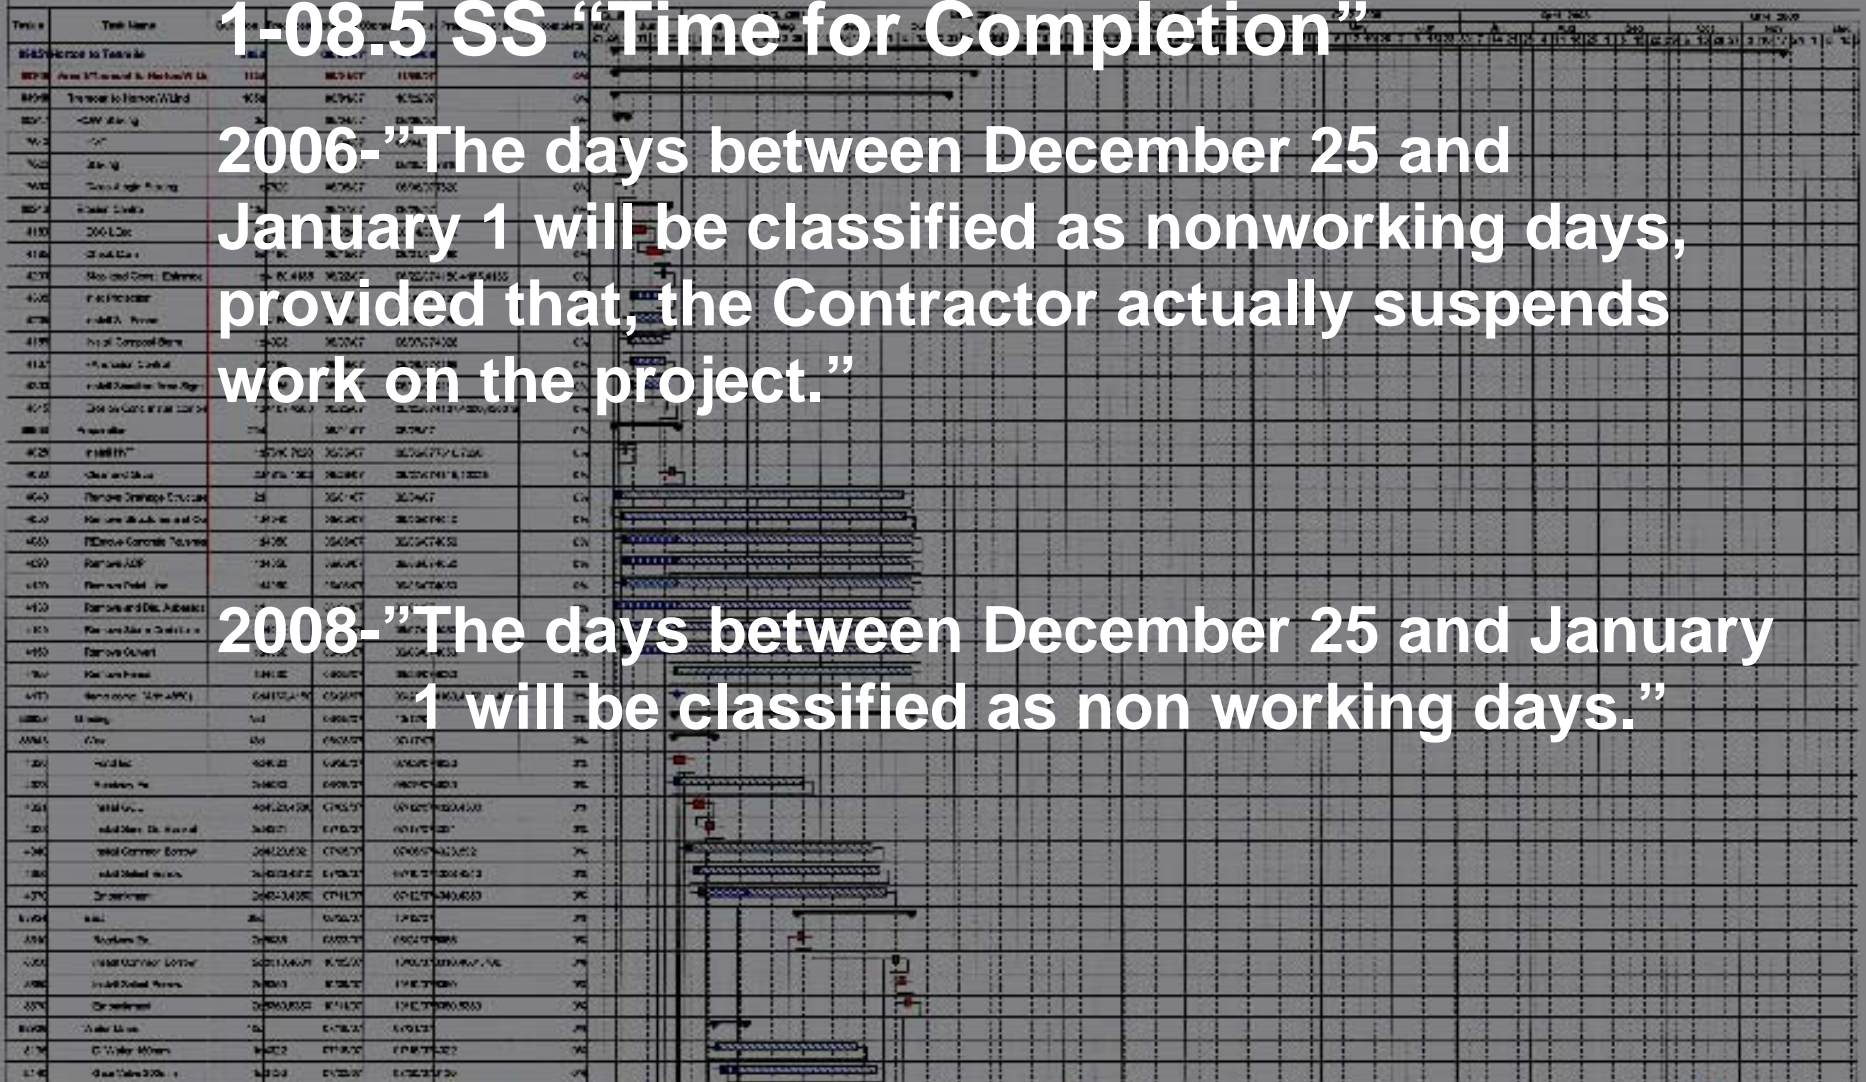

Resource:

Wilder-Paving

8-02.3(8) Planting

All planting shall be accomplished during the following periods:

1. Non-irrigated Plant Material October 1 to March 1

8-02.3(12) Completion of Initial Planting

Completion of the initial planting within a designated area includes the following: ... A minimum of 95% shall be in a healthy and vigorous growing condition, as described in Section 8-02, on May 31st.

Task	Task Name	Duration	Start	Finish	Resources	Progress
8000	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8010	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8020	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8030	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8040	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8050	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8060	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8070	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8080	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8090	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8100	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8110	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8120	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8130	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8140	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8150	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8160	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8170	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8180	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8190	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8200	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8210	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8220	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8230	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8240	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8250	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8260	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8270	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8280	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8290	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8300	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8310	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8320	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8330	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8340	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8350	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8360	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8370	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8380	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8390	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8400	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8410	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8420	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8430	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8440	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8450	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8460	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8470	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8480	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8490	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%
8500	Work to Task 80	1 day	08/21/07	08/21/07	CA	100%

Legend for task status and resources:

- Complete: Green square
- Complete Milestone: Green diamond
- Remaining: Blue square
- Remaining Milestone: Blue diamond
- Free Float: Yellow square
- Total Float (F): Red square
- Total Float (I): Red square
- Delay: Black triangle
- Non Resource: Dashed line
- Essential: Blue square
- Required Date: Blue square

Resource:

Wilder-Paving

1-08.9 SS “Liquidated Damages”

2006- (Substantial Completion) “When the Contract Work has progressed to the extent that the Contracting Agency has full use and benefit of the facilities, both from the operational and safety standpoint, and only minor and incidental work remain....”

2008- (Substantial Completion) “When the Contract Work has progressed to the extent that the Contracting Agency has full use and benefit of the facilities, both from the operational and safety standpoint, all the initial plantings are completed....”

Legend for Gantt chart symbols:

- Default: Complete (Green), Remaining Milestone (Red), Remaining Milestone (Blue)
- Critical: Remaining (Red)
- Parent: Complete (Green), Complete Milestone (Green), Remaining (Blue), Remaining Milestone (Blue)

Other symbols: Resource (Blue), Milestone (Green), Milestone (Red), Milestone (Blue), Milestone (Green), Milestone (Red), Milestone (Blue), Milestone (Green), Milestone (Red), Milestone (Blue)
