



Washington State
Department of Transportation

SR 520 Bridge Replacement and HOV Program



Medina to SR 202: Eastside Transit and HOV Project

Julie Meredith, P.E.

Director

SR 520 Bridge Replacement
and HOV Program

Mike Cotten, P.E.

Design-Build Manager

SR 520 Bridge Replacement
and HOV Program

Daniel Babuca, P.E.

Engineering Manager

Medina to SR 202: Eastside
Transit and HOV Project

Dave Edwards, P.E.

Project Engineer

Medina to SR 202: Eastside
Transit and HOV Project

Voluntary Submitters' Meeting

**Seattle Central Library
Seattle, WA**

**April 21, 2010
2 – 4 p.m.**


Presentation Outline

- **Project overview**
- **Design and environmental details**
- **Contract elements and procurement**
- **Questions and answers**
- **Open house**



SR 520 legislative highlights



- **ESSB 6392—**
Clarifying the use of revenue generated from tolling the state route number 520 corridor.
 - Toll revenues can be used in the entire SR 520 corridor.
 - Enables the Eastside Project to move forward.

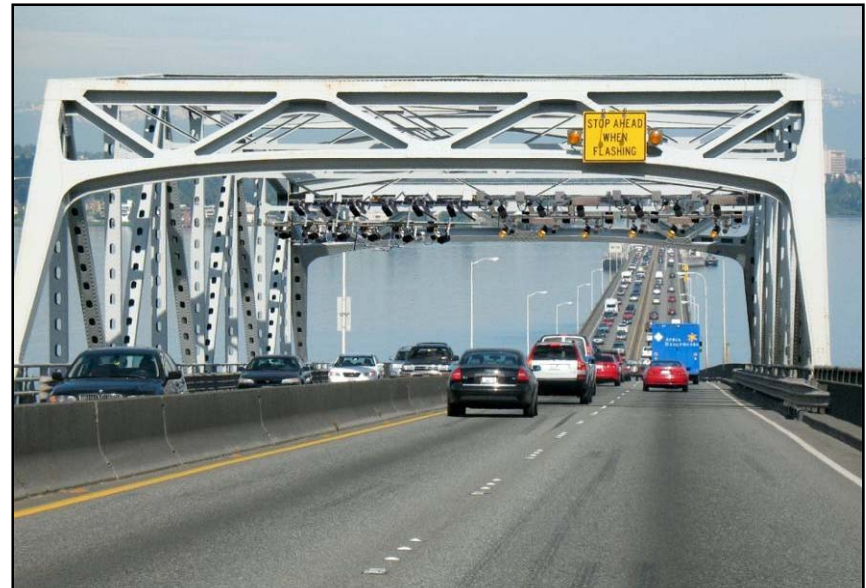

Eastside Project schedule



Eastside Project features

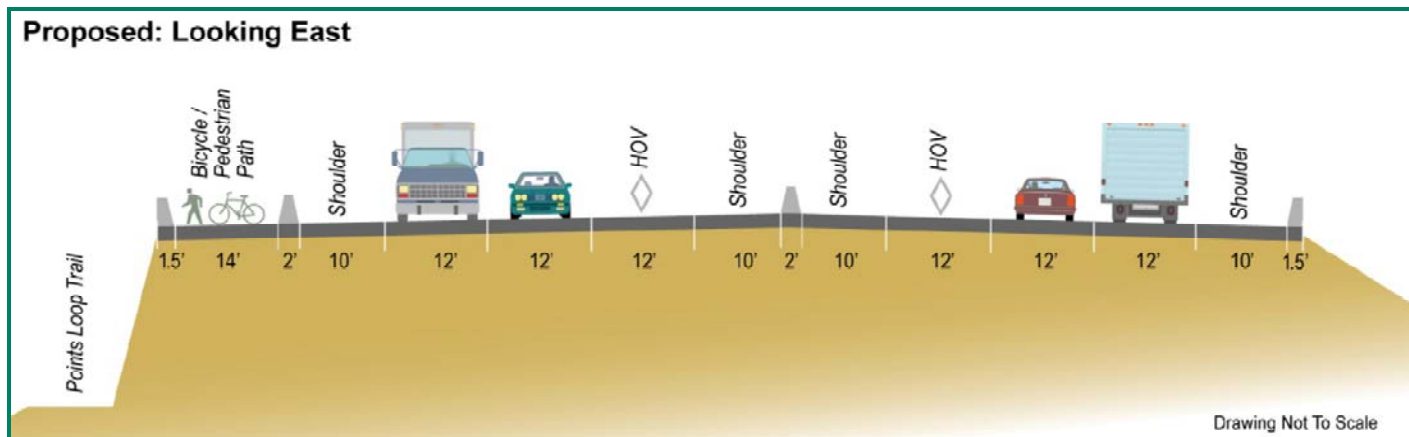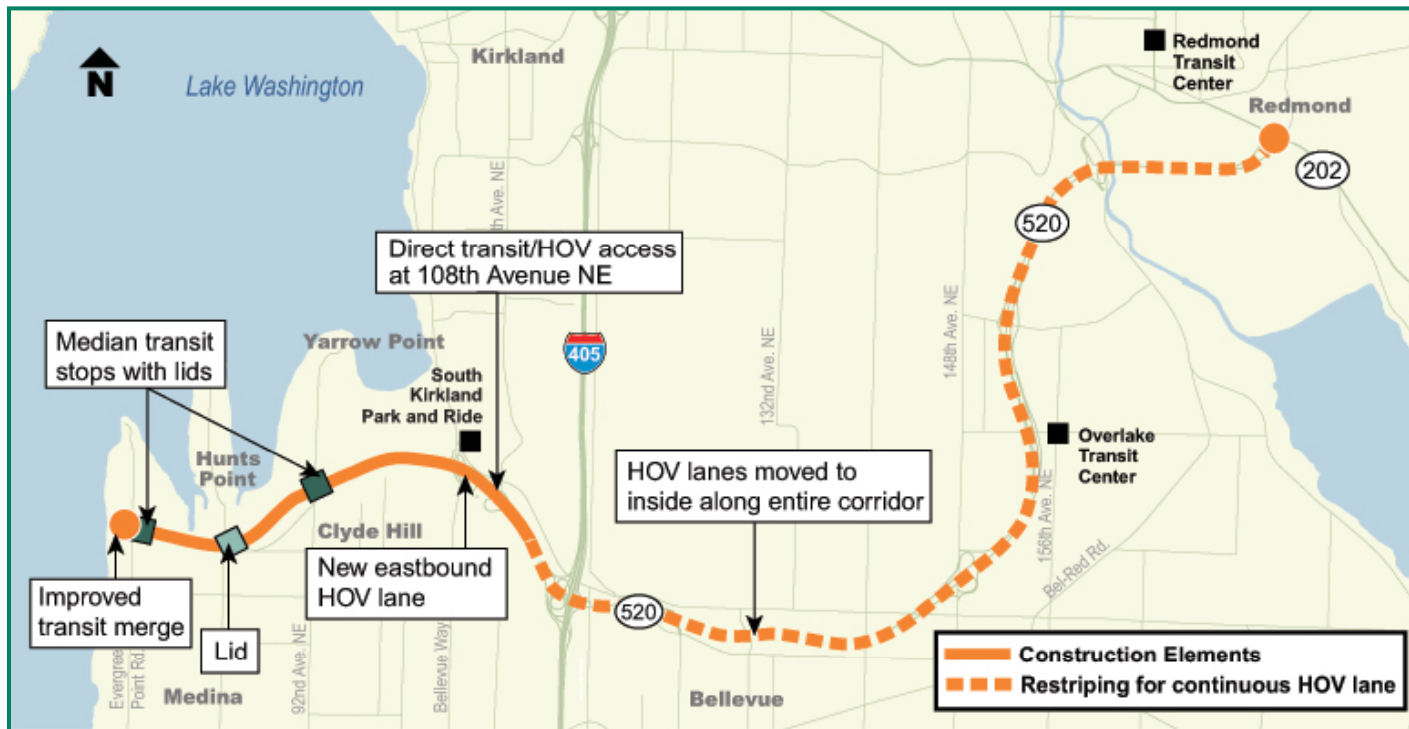

Key elements and commitments

- Three lids and two transit stops
- Interchange configurations
- Local trail and regional path
- Lid features
- Corridor look and feel
- Noise walls
- Fish passable structures and increased stream channel habitat
- Restoration of Yarrow Creek system
- Stormwater treatment



Level of Completion, June 2010

Right of way plans	100%
Acquisitions	In progress
Design –Fish culvert	Conceptual plans
Design –Corridor design	Conceptual plans
Permits –Federal and state	Complete
Geotechnical reports	Complete
Utilities and other local agreements	Partial completion

Permit Strategy: What permits will WSDOT receive?

Permit	Approving Agency	When Submitted	Anticipated Issuance
<ul style="list-style-type: none"> Endangered Species Act <ul style="list-style-type: none"> USFWS Informal Consultation NMFS Formal Consultation 	Federal Services	May 2009	Consultation completed: October 2009
<ul style="list-style-type: none"> Clean Water Act (CWA) Section 404 CWA Section 401 Certification CZMA Certification Hydraulic Project Approval 	U.S. Army Corps Ecology Ecology WDFW	June 2009	May 2010
<ul style="list-style-type: none"> Shoreline Substantial Development Permit Critical Areas Compliance 	Local Jurisdictions Local Jurisdictions	April 2010	May-June 2010

Permit Strategy: What permits will the Design-Builder obtain?

Permit	Approving Agency	When Submitted	When Re-submitted
<ul style="list-style-type: none">• NPDES Construction General Permit• Street Use Permit• Building Permit• Noise Variances	Local Jurisdictions Local Jurisdictions Local Jurisdictions Local Jurisdictions	As needed	As needed

Design-Build procurement schedule

Action	Dates
Step 1 – SOQ Phase	
RFQ issued	April 12, 2010
Voluntary meeting for Submitters	April 21, 2010
Deadline for submitting RFQ questions	May 6, 2010
Deadline for WSDOT response to RFQ questions	May 13, 2010
SOQ due	May 20, 2010
Short-listed Submitters teams notified	June 11, 2010
Step 2 – Proposal Phase	
Draft RFP issued	May 21, 2010**
RFP issued*	June 14, 2010**
Voluntary RFP meeting*	June 23, 2010**
Deadline for submitting Proposers' questions*	Aug. 25, 2010**
Deadline for submitting Proposers' ATC's*	Aug.25, 2010**
Deadline for WSDOT response to Proposers' questions*	Sept. 8, 2010**
Proposals Due*	Sept. 16, 2010**
Best Value Proposer announced *	Oct. 13, 2010**
Contract awarded	Oct. 25, 2010**

*Short-listed teams only


**Dates may change

Federal funding

- DBE goal for participation and training.
 - <http://www.omwbe.wa.gov>
- Training hours.
- Buy America.
- State and Federal prevailing wage requirements.



Conflict of interest policy

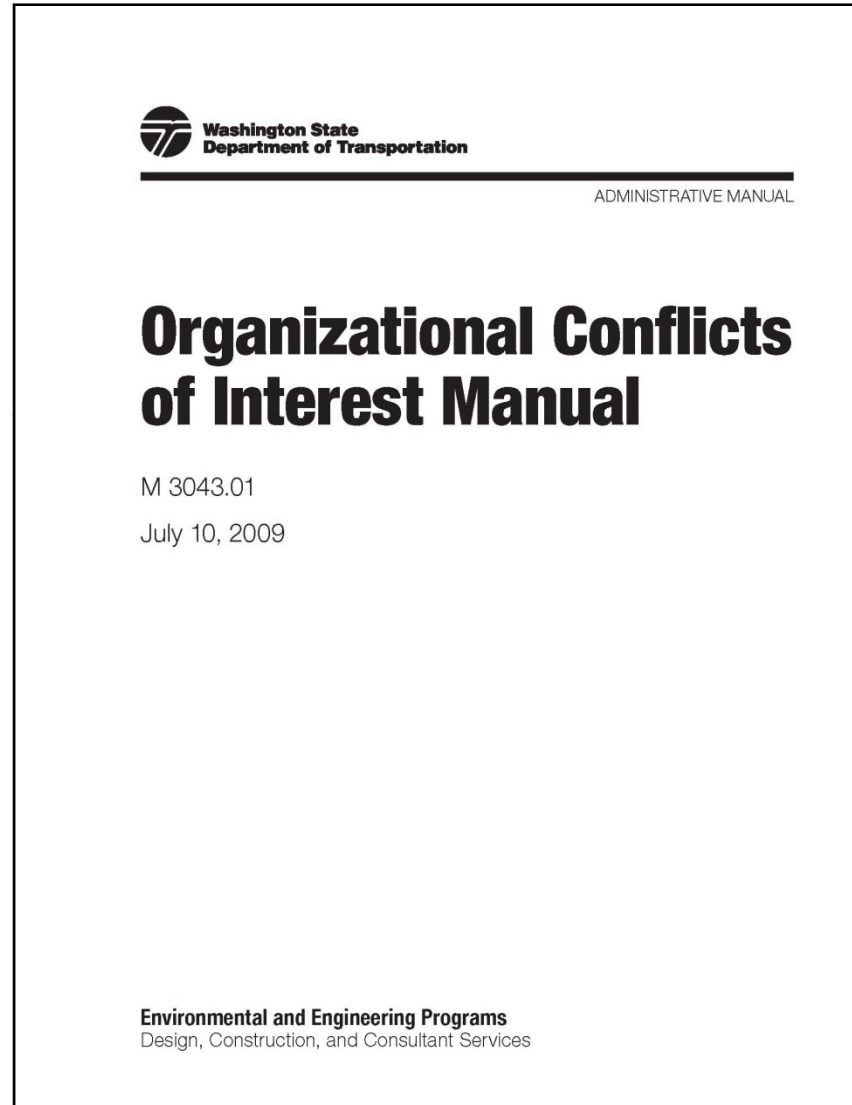

For further inquiries

Submittal information

Dave Mariman

WSDOT Contract Ad and Award Office

E-mail: MarimaD@wsdot.wa.gov

Phone: 360-705-7017

Technical questions

Dave Edwards, P.E.

Project Engineer

SR 520 Eastside Transit and HOV Project

E-mail: EdwardD@wsdot.wa.gov

Phone: 206-770-3530

Conflict of interest inquiries

Daniel Babuca

Engineering Manager

SR 520 Eastside Transit and HOV Project

E-mail: BabucaD@wsdot.wa.gov

Phone: 206-770-3545

WSDOT Contract Ad and Award Web page

www.wsdot.wa.gov/biz/contaa/

- Download today's presentation, displays and questions and answers.
- Locate additional materials and information, as they become available.

Questions?

For more information visit the program Web site at:

www.wsdot.wa.gov/projects/SR520Bridge

